



ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड
(भारत सरकार का उद्यम)
GRID CONTROLLER OF INDIA LIMITED
(A Government of India Enterprise)



[formerly Power System Operation Corporation Limited (POSOCO)]
राष्ट्रीय भार प्रेषण केन्द्र / **National Load Despatch Centre**

कार्यालय : बी-9, प्रथम एवं द्वितीय तल, कुतुब इंस्टीट्यूशनल एरिया, कटवारिया सराय, नई दिल्ली - 110016
Office : 1st and 2nd Floor, B-9, Qutab Institutional Area, Katwaria Sarai, New Delhi -110016
CIN : U40105DL2009GOI188682, Website : www.grid-india.in, E-mail : gridindiacc@grid-india.in, Tel.: 011- 42785855

संदर्भ संख्या : - GRID-INDIA/NLDC/MR/

दिनांक : 25.07.2023

सेवा में,

वितरण सूची के अनुसार

विषय:- निष्पादन रिपोर्ट – जून 2023

महोदय,

आई०ई०जी०सी०-2010 के प्रावधान के अनुसार, जून 2023 माह की अखिल भारतीय प्रणाली की निष्पादन रिपोर्ट संलग्न है।

धन्यवाद

भवदीय

(सुरजीत बनर्जी)

मुख्य महाप्रबन्धक (प्रणाली प्रचालन)

(रा०भा०प्रे०के०)

संलग्नक : मासिक प्रणाली रिपोर्ट

वितरण सूची Distribution List

- 1 सचिव, के.वि.नि.आ. तीसरा एवं चौथा तल, चंद्रलोक भवन, 36, जनपथ, नई दिल्ली-110001
Secretary, CERC, 3rd & 4th Floor, Chanderlok Building, 36, Janpath, New Delhi-110001
- 2 मुख्य अभियंता (जी एम), के.वि.प्रा., सेवा भवन, आर. के. पुरम, नई दिल्ली-110066
Chief Engineer (GM), CEA, Sewa Bhavan, R.K.Puram, New Delhi-110066
- 3 सदस्य सचिव, उ. क्षेत्र. वि. स., 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली - 110016
Member Secretary, NRPC, 18/A, SJSS Marg, Katwaria Sarai, New Delhi-110016
- 4 सदस्य सचिव, प. क्षेत्र. वि. स., एफ-3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई - 400093
Member Secretary, WRPC, F-3, MIDC Area, Andheri (East), Mumbai-400093
- 5 सदस्य सचिव, द. क्षेत्र. वि. स., 29, रेस कोर्स क्रॉस रोड, बंगलूरु - 560009
Member Secretary, SRPC, 29, Race Course Cross Road, Bangalore-560009
- 6 सदस्य सचिव, पू. क्षेत्र. वि. स., 14, गोल्फ क्लब रोड, कोलकाता - 700033
Member Secretary, ERPC, 14, Golf Club Road, Kolkata-700033
- 7 सदस्य सचिव, उ. पू. क्षेत्र. वि. स., मेघालय राज्य आवासीय वित्त सहकारी समिति लिमिटेड भवन, नॉग्रिम हिल्स, शिलोंग - 793003
Member Secretary, NERPC, Meghalaya State Housing Finance Cooperative Society Ltd. Building, Nongrim Hills, Shillong -793003
- 8 मुख्य अभियंता, राष्ट्रीय विद्युत समिति, एनआरपीसी भवन, तृतीय तल, 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली - 110016
Chief Engineer, National Power Committee, NRPC Building, 3rd floor, 18/A, SJSS Marg, Katwaria Sarai, New Delhi-110016
- 9 कार्यपालक निदेशक, पू. क्षेत्र. भा. प्रे. के., 14, गोल्फ क्लब रोड, कोलकाता - 700033
Executive Director, ERLDC, 14, Golf Club Road, Kolkata-700033
- 10 कार्यपालक निदेशक, प. क्षेत्र. भा. प्रे. के., एफ-3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई - 400093
Executive Director, WRLDC, F-3, MIDC Area, Andheri (East), Mumbai-400093
- 11 कार्यपालक निदेशक, उ. क्षेत्र. भा. प्रे. के., 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली - 110016
Executive Director, NRLDC, 18/A, SJSS Marg, Katwaria Sarai, New Delhi-110016
- 12 कार्यपालक निदेशक, द. क्षेत्र. भा. प्रे. के., 29, रेस कोर्स क्रॉस रोड, बंगलूरु - 560009
Executive Director, SRLDC, 29, Race Course Cross Road, Bangalore-560009
- 13 मुख्य महाप्रबंधक, पू. क्षेत्र. भा. प्रे. के., डोंगतिह, लोअर नॉग्रह, लापलंग, शिलोंग- 793006
Chief General Manager, NERLDC, Dongtiah, Lower Nongrah, Laplang, Shillong-793006



ग्रिड-इंडिया
GRID-INDIA

GRID CONTROLLER OF INDIA LIMITED

Formerly Power System Operation Corporation Limited

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड

NATIONAL LOAD DESPATCH CENTRE –राष्ट्रीय भार प्रेषण केन्द्र

मासिक ऑपरेशन रिपोर्ट

Monthly
Operation Report



जून 2023

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड
राष्ट्रीय भार प्रेषण केंद्र, नई दिल्ली

GRID CONTROLLER OF INDIA LIMITED

Formerly Power System Operation Corporation Limited

NATIONAL LOAD DESPATCH CENTRE, NEW DELHI



ग्रिड-इंडिया
GRID-INDIA

माह जून 2023 के लिए प्रचालन निष्पादन रिपोर्ट

OPERATIONAL PERFORMANCE REPORT FOR THE

MONTH OF JUNE-2023


पृष्ठसूची CONTENTS

1	माह जून 2023 की सारांश रिपोर्ट Summary of report for the month of JUNE 2023	1-5
2	क्षेत्रवार स्थापित विद्युत क्षमता Region wise Installed Capacity	6
3	राष्ट्रीय स्तर पर सांध्यकालीन शिखर मांगपूर्ति Peak demand met at National level	7-8
4	राष्ट्रीय स्तर पर विद्युत ऊर्जा खपत Energy consumption at National level	9-10
5	फ्रिक्वेंसी रूपरेखा Frequency profile	11-12
6	राष्ट्रीय स्तर पर जल विद्युत ऊर्जा उत्पादन Hydro generation at National level	13-14
7	राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन Wind generation at National level	15
8	राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन Solar generation at National level	16
9	राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग पूर्ति Daily maximum demand met at National level	17
10	09 जून के माँग एवं उत्पादन प्लॉट (अधिकतम मांग पूर्ति) व माँग का डाटा (15 मिनट अंतराल) Demand and generation plots for 09-JUNE (Max Demand Met) and Demand data (15-minute interval)	18-22
11	ऊर्जा आपूर्ति की वास्तविक स्थिति Actual power supply position	23
12	ऊर्जा आवश्यकता एवं आपूर्ति की पिछले वर्ष माह जून 2022 से तुलना Energy requirement and met comparison with JUNE 2022	24
13	शिखर मांग आवश्यकता एवं आपूर्ति की पिछले वर्ष माह जून 2022 से तुलना Peak demand requirement and met comparison with JUNE 2022	25


14	क्षेत्रीय स्तर पर शिड्यूल एवं ड्रावल Schedule & drawal at regional level	26
15	अंतर क्षेत्रीय विनिमय Inter-regional exchanges	27-36
16	अंतर राष्ट्रीय विद्युत विनिमय Inter-national exchanges	37-39
17	एसटीओए (द्विपक्षीय एवं सामूहिक) एवं यू आइ का ब्यौरा Bilateral and collective short-term open access & UI details	40
18	पावर मार्केट की सूचना Power market information	41-44
19	अक्षय ऊर्जा प्रमाण पत्र प्रक्रिया Renewable energy certificate mechanism	45-47
20	मुख्य घटनाएँ एवं डिस्टर्बेंस Important events/disturbances	48-63
21	नए कमीशंड पारेषण तत्व New elements commissioned	64
22	विभव रूपरेखा Voltage profile	65
23	जून 2023 के दौरान रा.भा.प्रे.के. द्वारा निगरानी में तत्वों के आउटेज की सूची List of outage of elements monitored by NLDC for the month of JUNE 2023	66-80
24	अब तक उच्चतम (मांग व ऊर्जा) आँकड़े : माह जून 2023 तक All Time Highest (Demand & Energy) figures: Till JUNE 2023	81
25	जून 2023 के लिए सिस्टम रिलाइबिलिटी सूचकांक System Reliability Indices for JUNE 2023	82

1. SUMMARY OF REPORT FOR THE MONTH OF JUN-2023

EVENING PEAK HOUR (at 2000hrs) DEMAND MET AT NATIONAL LEVEL (MW)

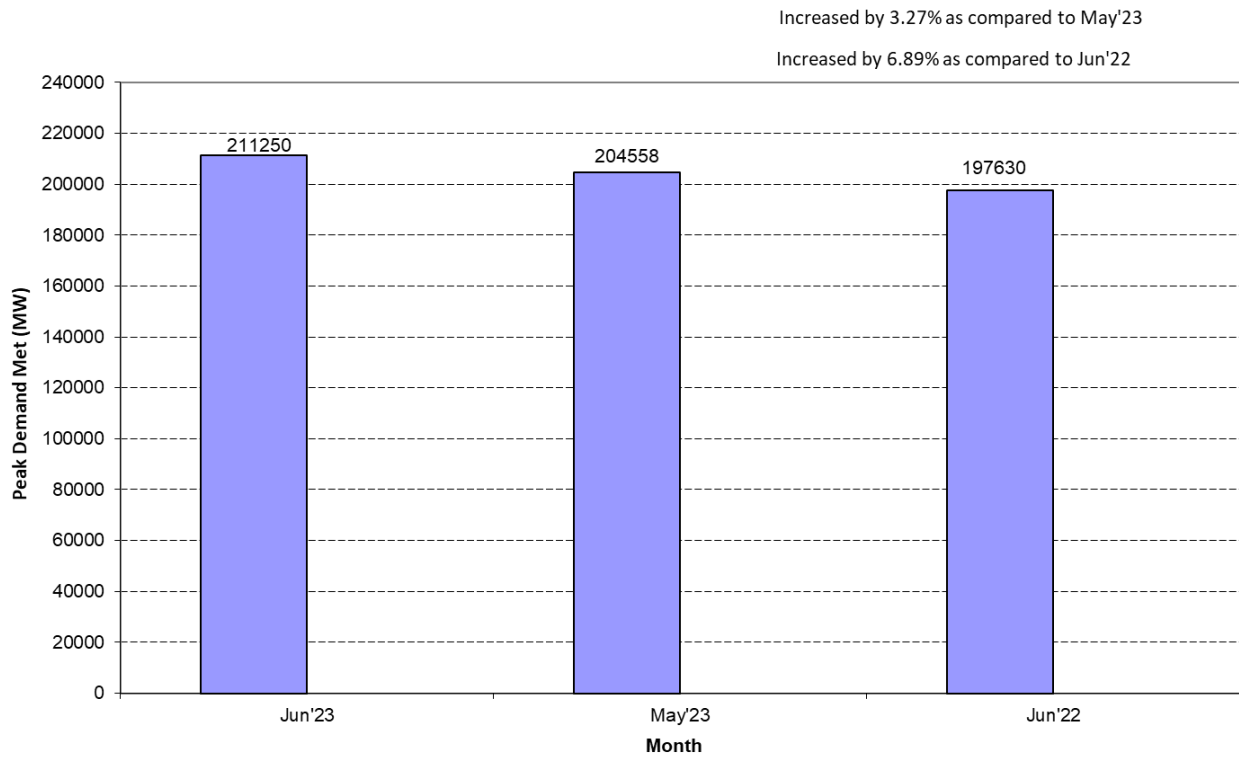


Frequency within IEGC Band

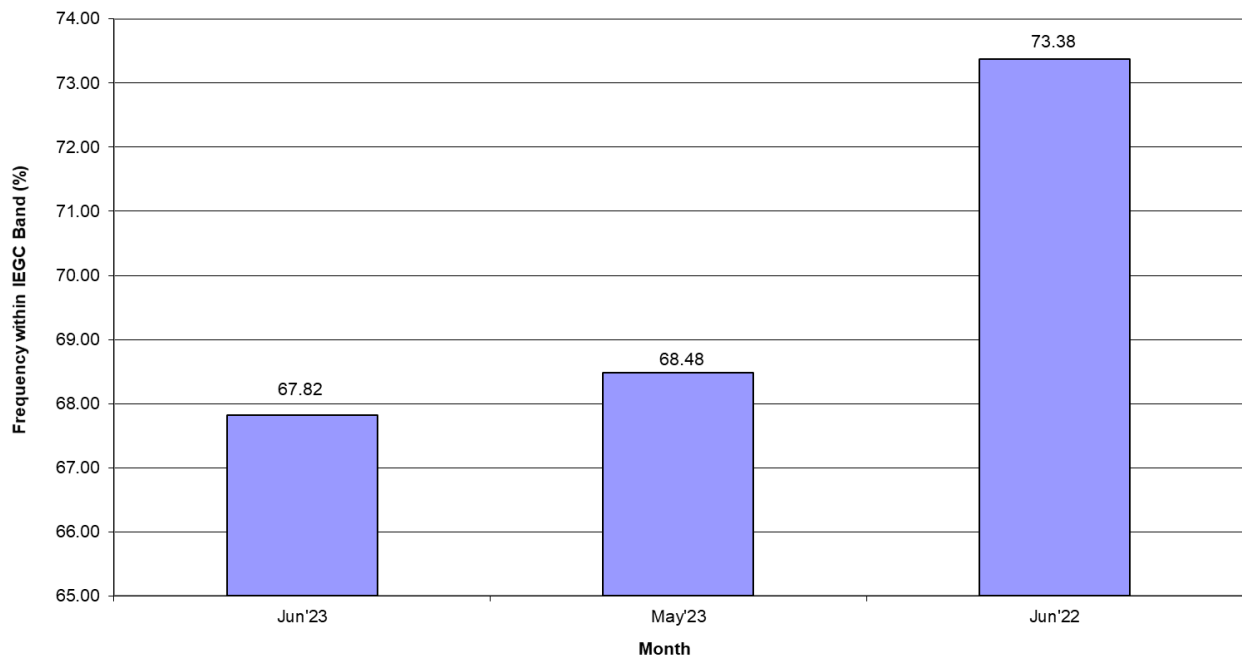

ENERGY MET AT NATIONAL LEVEL (MU)


Increased by 3.22% as compared to May'23

Increased by 4.32% as compared to Jun'22

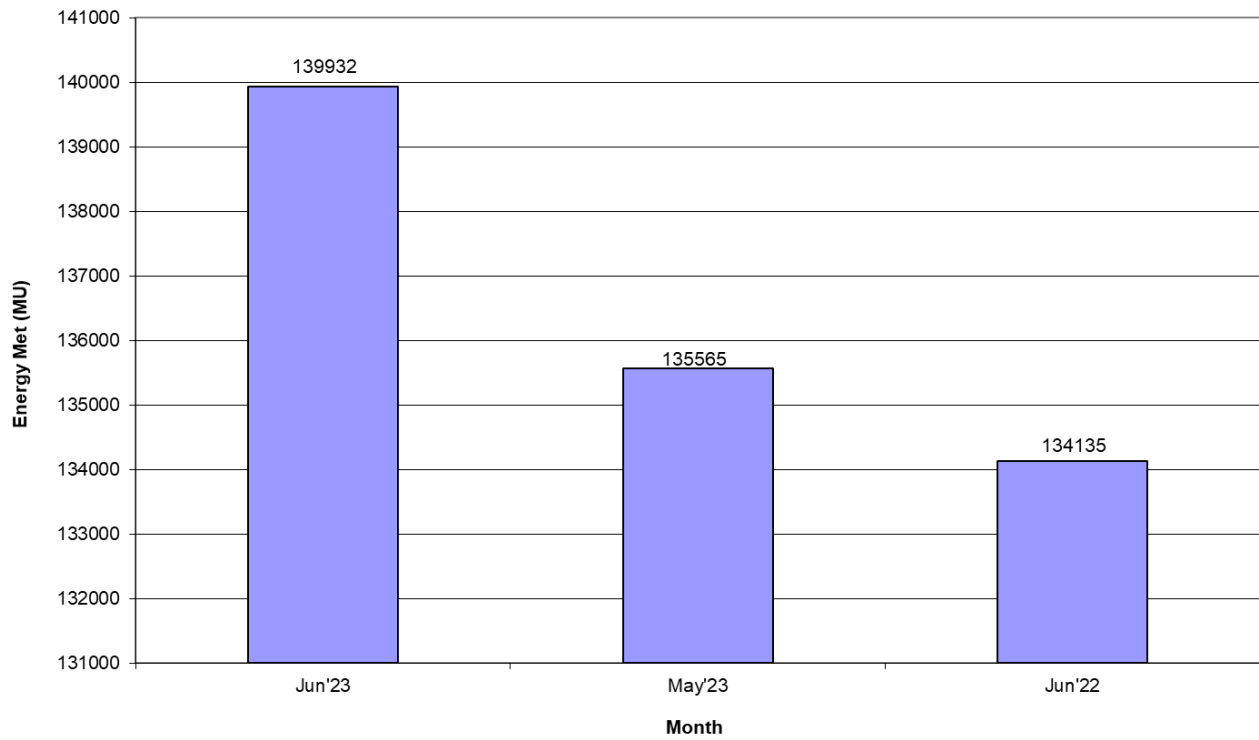


AVERAGE ENERGY MET AT NATIONAL LEVEL (MU/Day)

Increased by 4.32% as compared to Jun'22

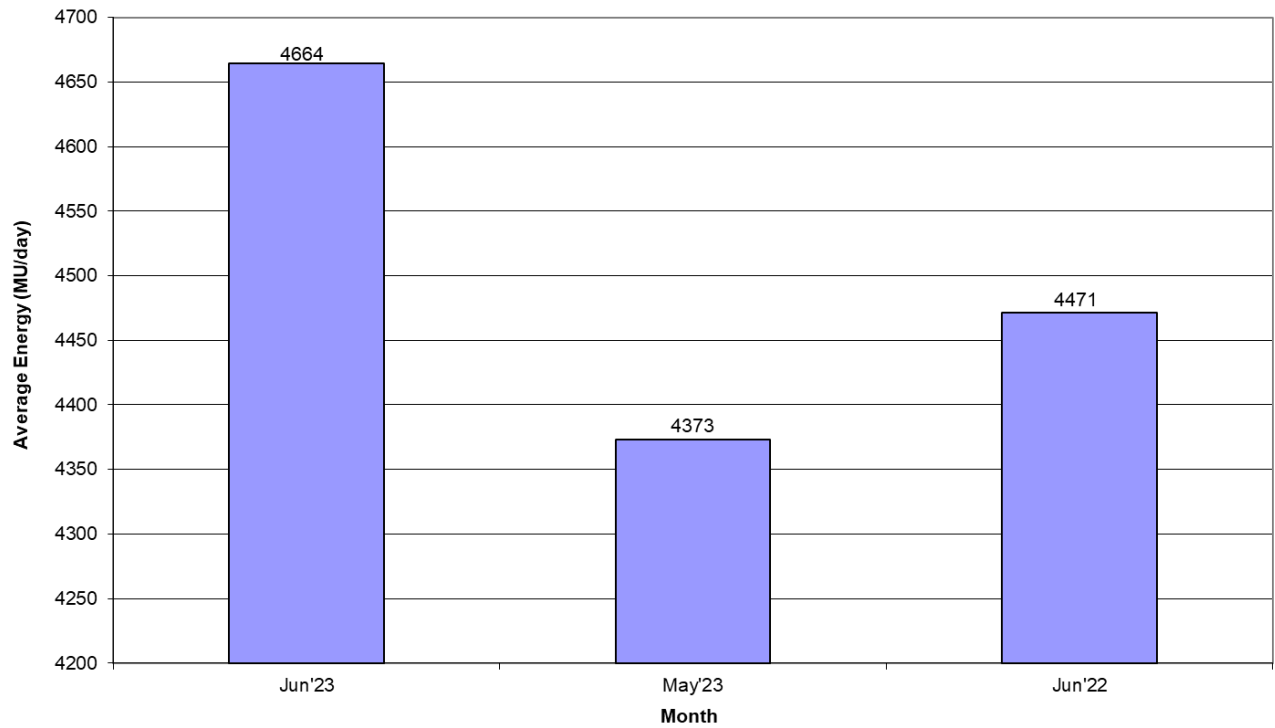


HYDRO GENERATION AT NATIONAL LEVEL (MU)

Increased by 26.17% as compared to May'23
Decreased by 0.58% as compared to Jun'22

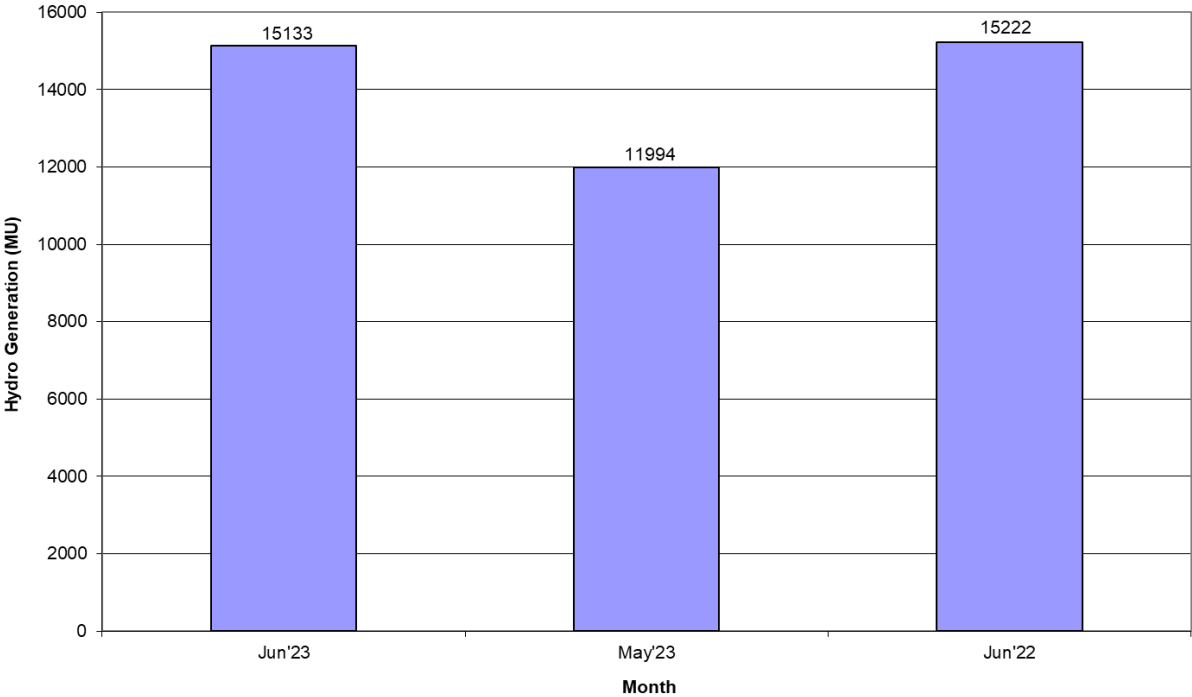

AVERAGE HYDRO GENERATION AT NATIONAL LEVEL (MU/Day)


Decreased by 0.58% as compared to Jun'22

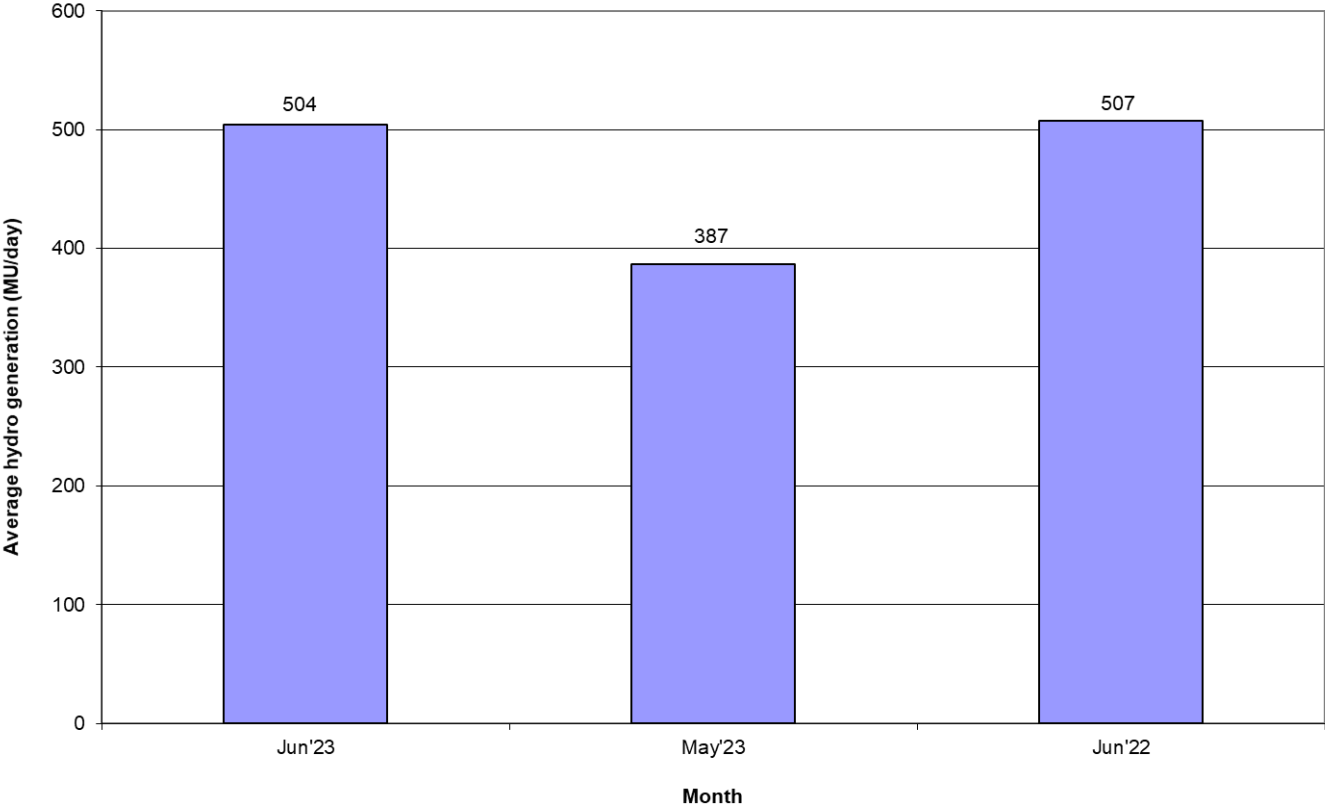

WIND GENERATION AT NATIONAL LEVEL (MU)


Increased by 56.98% as compared to May'23

Increased by 15.70% as compared to Jun'22

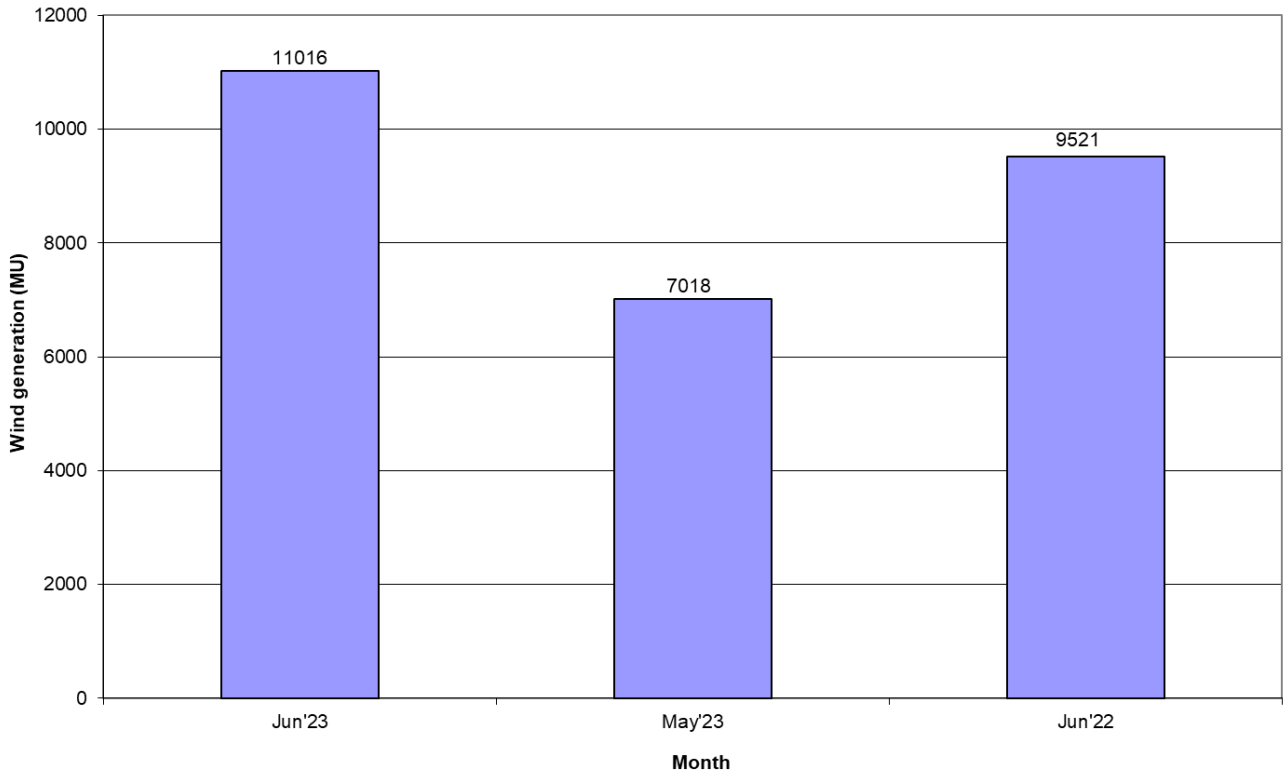

AVERAGE WIND GENERATION AT NATIONAL LEVEL (MU/Day)


Increased by 15.70% as compared to Jun'22

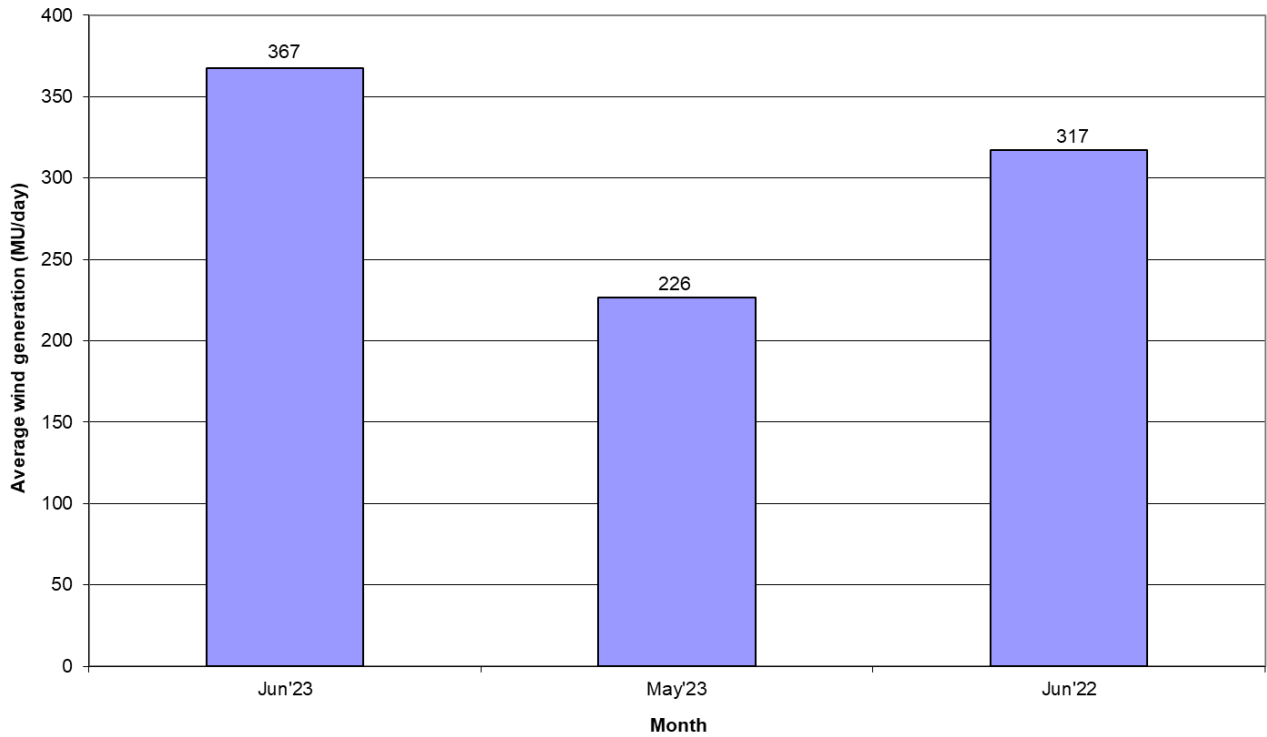

SOLAR GENERATION AT NATIONAL LEVEL (MU)


Decreased by 10.32% as compared to May'23

Increased by 13.78% as compared to Jun'22

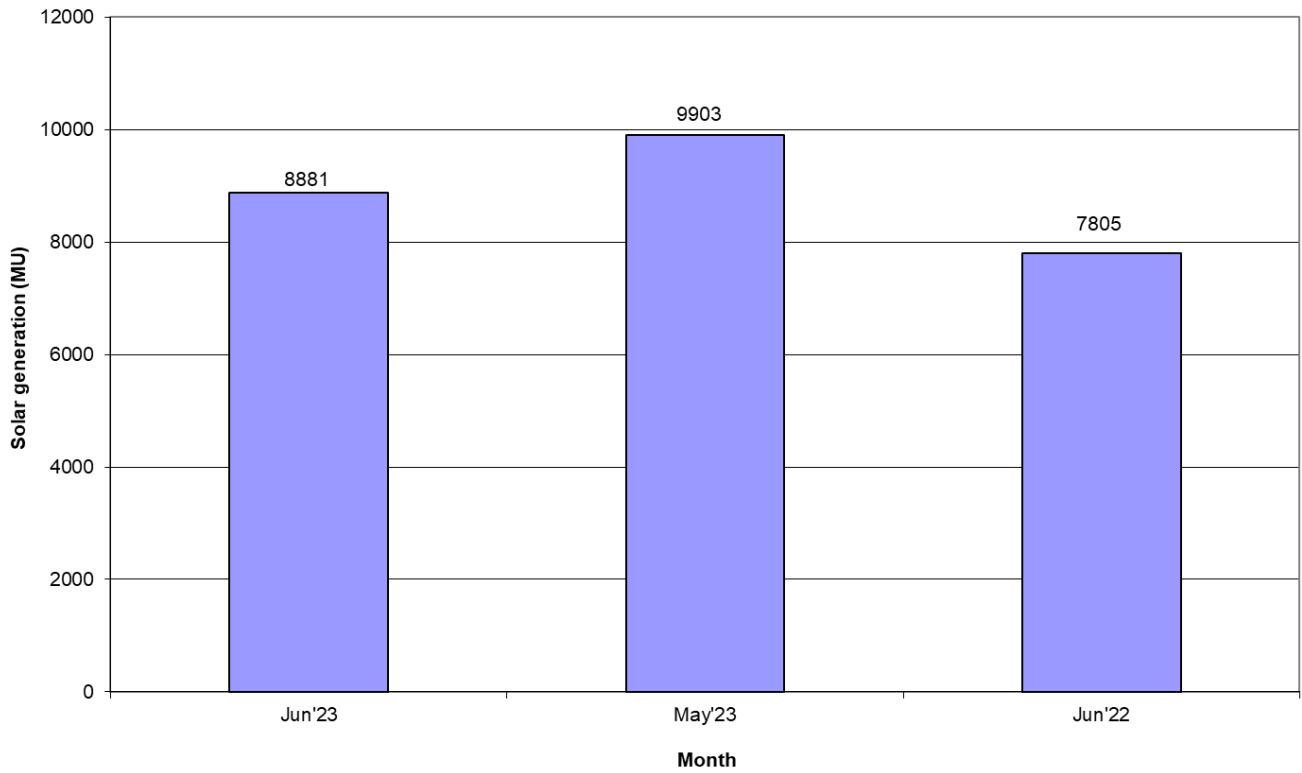

AVERAGE SOLAR GENERATION AT NATIONAL LEVEL (MU/Day)

Increased by 13.78% as compared to Jun'22

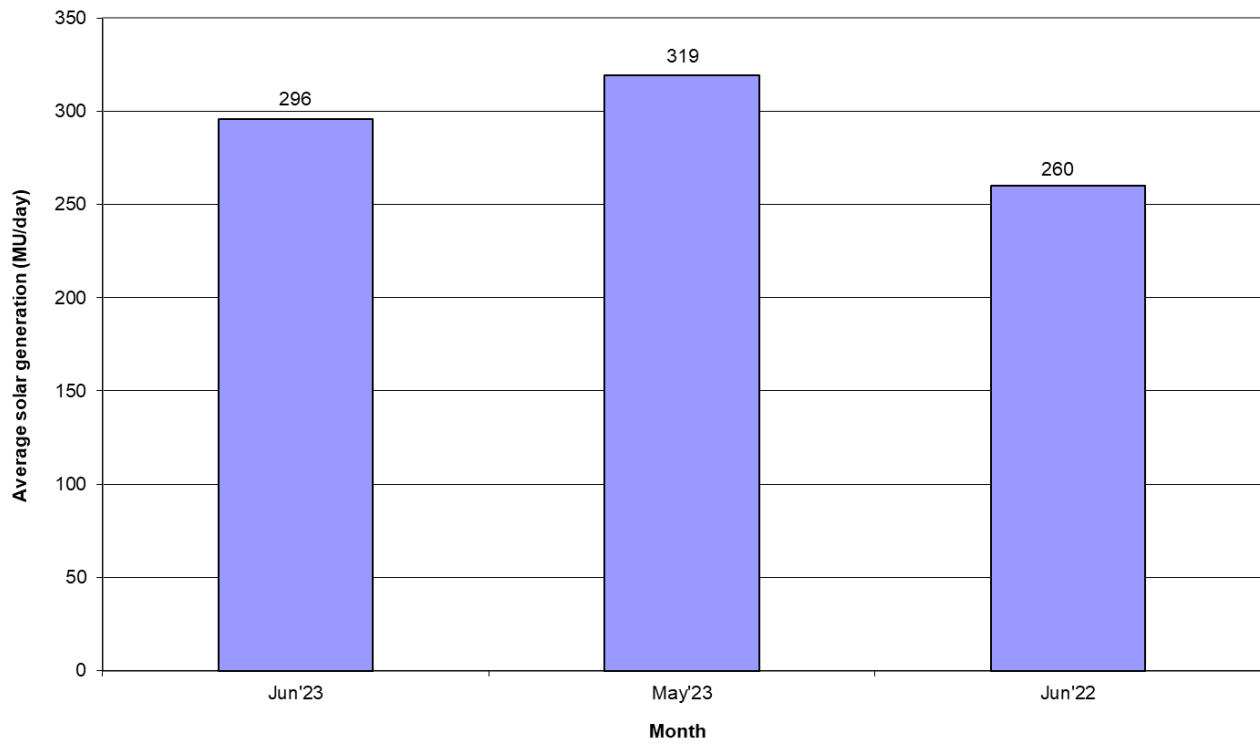

2. ALL INDIA REGIONWISE INSTALLED CAPACITY

As on 30.06.2023
(All figures are in MW)

S No	Region	THERMAL					NUCLEAR	HYDRO	RES @ MNRE	GRAND TOTAL
		COAL	LIGNITE	GAS	DIESEL	TOTAL				
1	NR	55437	1580	5781	0	62798	1620	20752	33966	119135
2	WR	74602	1400	10806	0	86808	2540	7563	41730	138641
3	SR	46997	3640	6492	434	57563	3320	11827	51501	124211
4	ER	28229	0	80	0	28309	0	4764	1857	34930
5	NER	631	0	1665	36	2332	0	1944	551	4827
6	ISLANDS	0	0	0	120	120	0	0	38	158
	ALL INDIA	205895	6620	24824	589	237929	7480	46850	129643	421902

Remarks: Data from CEA website

3. राष्ट्रीय स्तर पर संध्याकालीन शिखर विद्युत मांग पूर्ति
EVENING PEAK HOUR DEMAND MET AT NATIONAL LEVEL

माह: जून 2023 MONTH:- JUN 2023


सभी आंकड़े मेगावाट में All figures in MW

दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
1-Jun-23	56004	60964	48237	26609	3307	195121
2-Jun-23	58492	61911	49101	26162	3326	198992
3-Jun-23	58946	60818	49518	26252	3416	198950
4-Jun-23	56141	54626	42722	25633	3214	182336
5-Jun-23	61147	61419	48358	26969	3393	201286
6-Jun-23	58524	63198	47664	27445	3458	200289
7-Jun-23	63139	62684	47184	26700	3358	203065
8-Jun-23	65135	62905	48610	27105	3404	207159
9-Jun-23	67027	63465	47588	25154	3133	206367
10-Jun-23	63674	61067	46829	25305	3017	199892
11-Jun-23	64682	59282	42604	23853	2864	193285
12-Jun-23	69843	62024	46951	24446	3179	206443
13-Jun-23	68031	59347	48237	26110	3042	204767
14-Jun-23	65956	58750	48995	27320	2829	203850
15-Jun-23	66734	57386	50524	27348	2491	204483
16-Jun-23	68603	56049	50105	27243	2407	204407
17-Jun-23	67548	57629	49388	26720	2413	203698
18-Jun-23	64715	56512	44002	25016	2328	192573
19-Jun-23	66642	60411	48527	24959	2653	203192
20-Jun-23	68263	60684	47012	25113	2659	203731
21-Jun-23	72481	61116	45252	24561	2805	206215
22-Jun-23	75577	60318	46910	25526	2919	211250
23-Jun-23	76072	58647	45785	26333	2984	209821
24-Jun-23	65934	55187	44838	25702	3239	194900
25-Jun-23	60815	52460	42527	24889	3104	183795
26-Jun-23	66648	53484	46348	23492	3200	193172
27-Jun-23	66828	52258	45836	22798	3046	190766
28-Jun-23	67195	51963	46574	23674	3117	192523
29-Jun-23	64990	51080	44854	24564	3104	188592
30-Jun-23	65241	51919	47057	24794	3031	192042
उच्चतम MAXIMUM	76072	63465	50524	27445	3458	211250
निम्नतम MINIMUM	56004	51080	42527	22798	2328	182336
औसत AVERAGE	65368	58319	46938	25593	3015	199232
अब तक का उच्चतम All Time Max.	76072	63593	52366	28579	3510	211250
दिनांक Date	23.06.23	18.04.23	18.04.23	18.04.23	12.08.22	22.06.23

नोट : सभी आंकड़े 2000 बजे की मांगपूर्ति पर आधारित है ।

Note: The above figures correspond to value at 2000 Hrs

EVENING PEAK HOUR DEMAND (2000hrs) MET DURING THE MONTH OF JUNE 2023

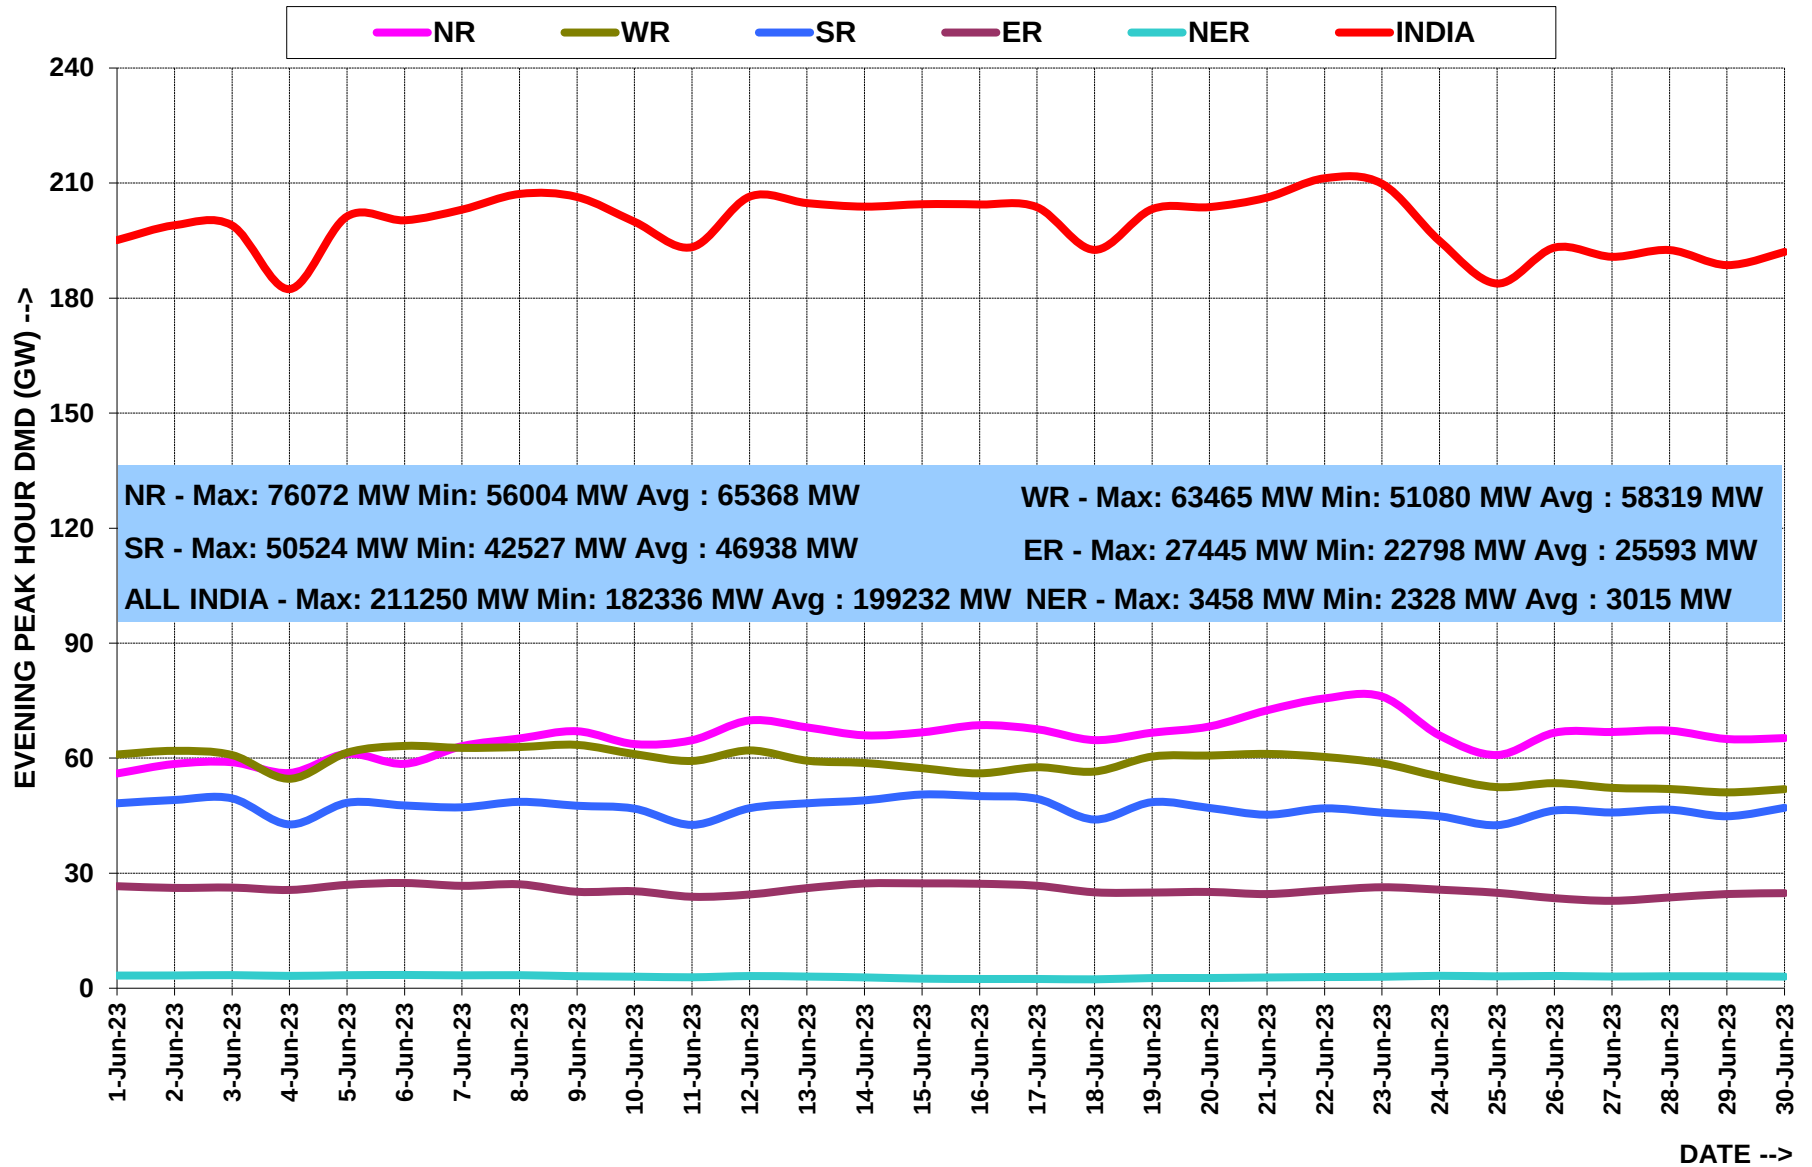


4. राष्ट्रीय स्तर पर विद्युत ऊर्जा आपूर्ति ENERGY MET AT NATIONAL LEVEL

माह: जून 2023 MONTH:- JUN 2023

सभी आंकड़े मिलियन यूनिट में All figures in MU

दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Jun-23	1170	1455	1160	607	66	4458
02-Jun-23	1231	1476	1178	610	64	4560
03-Jun-23	1295	1486	1203	613	66	4664
04-Jun-23	1223	1340	1111	600	61	4335
05-Jun-23	1352	1423	1167	616	65	4622
06-Jun-23	1364	1475	1182	626	68	4715
07-Jun-23	1398	1491	1165	634	69	4757
08-Jun-23	1467	1502	1184	639	68	4861
09-Jun-23	1520	1527	1191	615	61	4913
10-Jun-23	1526	1513	1152	600	58	4848
11-Jun-23	1448	1438	1087	590	52	4615
12-Jun-23	1587	1432	1166	576	56	4817
13-Jun-23	1621	1462	1181	590	59	4914
14-Jun-23	1581	1422	1202	591	56	4851
15-Jun-23	1525	1383	1236	601	44	4789
16-Jun-23	1567	1340	1266	627	44	4843
17-Jun-23	1578	1362	1236	631	43	4850
18-Jun-23	1466	1349	1150	600	42	4607
19-Jun-23	1511	1428	1166	572	45	4722
20-Jun-23	1546	1459	1157	579	49	4790
21-Jun-23	1615	1462	1127	582	49	4835
22-Jun-23	1668	1466	1105	577	51	4866
23-Jun-23	1719	1436	1101	577	57	4888
24-Jun-23	1690	1368	1062	575	62	4757
25-Jun-23	1402	1261	992	553	64	4272
26-Jun-23	1419	1262	1049	527	63	4320
27-Jun-23	1497	1239	1089	517	61	4403
28-Jun-23	1505	1226	1105	497	61	4393
29-Jun-23	1480	1204	1107	504	61	4356
30-Jun-23	1441	1198	1112	500	60	4311
कुल TOTAL	44413	41883	34386	17524	1726	139932
उच्चतम MAXIMUM	1719	1527	1266	639	69	4914
निम्नतम MINIMUM	1170	1198	992	497	42	4272
औसत AVERAGE	1480	1396	1146	584	58	4664
संचयी 2023-24 Cumulative 2023-24	116921	128318	105507	50481	4827	406053
अब तक का उच्चतम All Time Max.	1737	1539	1329	639	69	4914
दिनांक Date	28.06.22	18.04.23	19.04.23	08.06.23	15.07.22	13.06.23

ENERGY MET DURING THE MONTH OF JUNE' 2023

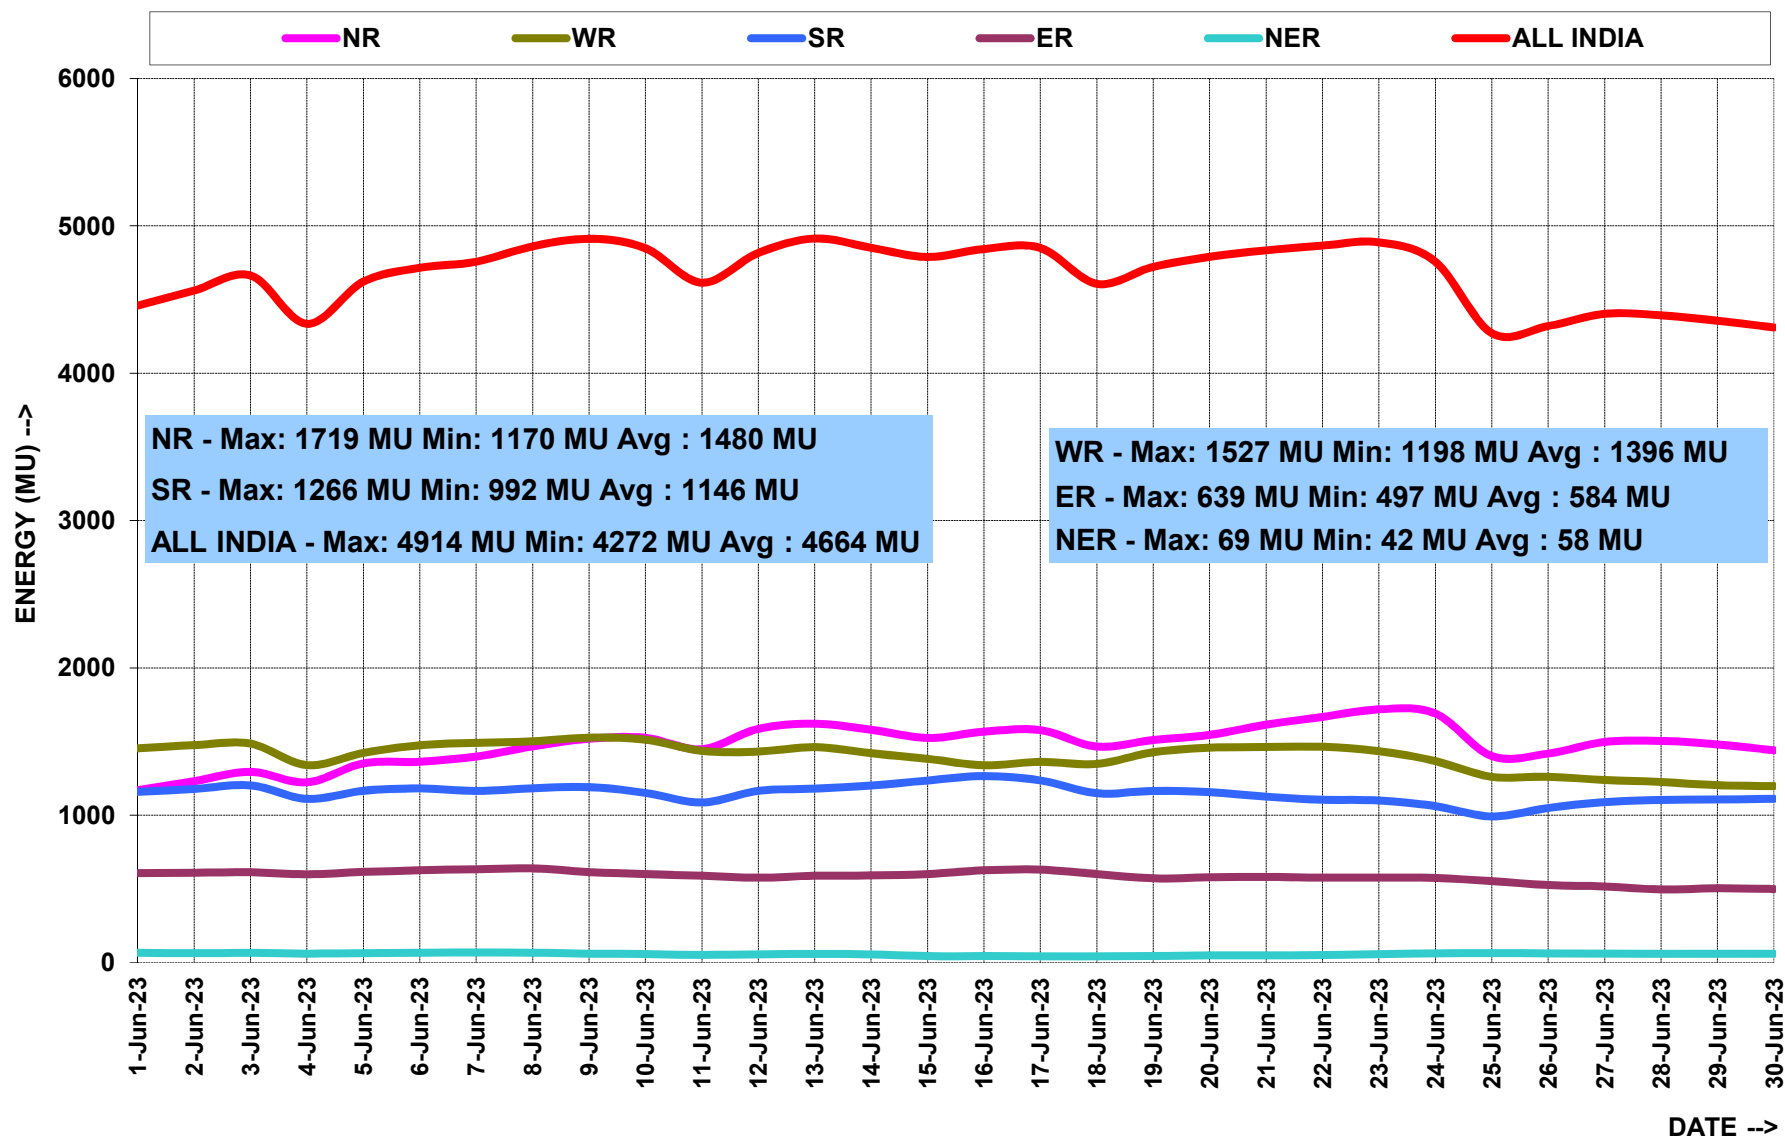

5. वर्ष 2023-24 के लिए आवृत्ति रूपरेखा FREQUENCY PROFILE FOR YEAR 2023-24

राष्ट्रीय ग्रीड NATIONAL GRID								
फ्रिक्वेंसी रूपरेखा (Hz)			<49.9	49.9-50.05	>50.05	उच्चतम फ्रिक्वेंसी	निम्नतम फ्रिक्वेंसी	औसत फ्रिक्वेंसी
% समय	Apr-23	All India Grid	10.54	67.90	21.56	50.33	49.49	49.99
	May-23	All India Grid	9.83	68.48	21.69	50.43	49.48	49.99
	Jun-23	All India Grid	6.47	67.82	25.71	50.41	49.51	50.01
	2023-24 (upto Jun)	All India Grid	8.96	68.07	22.97	50.43	49.48	50.00

5.1 जून 2023 के लिए आवृत्ति रूपरेखा FREQUENCY PROFILE FOR JUNE 2023

फ्रिक्वेंसी रूपरेखा (Hz)		<49.9	49.9-50.05	>50.05	उच्चतम फ्रिक्वेंसी	निम्नतम फ्रिक्वेंसी	औसत फ्रिक्वेंसी	एफ़.वी.आई.
% समय	01-Jun-23	3.04	62.96	33.99	50.25	49.78	50.02	0.05
	02-Jun-23	11.06	71.60	17.34	50.30	49.72	49.99	0.06
	03-Jun-23	10.73	65.68	23.59	50.21	49.75	49.99	0.05
	04-Jun-23	14.02	65.19	20.80	50.27	49.59	49.98	0.08
	05-Jun-23	3.63	61.05	35.31	50.26	49.79	50.02	0.05
	06-Jun-23	5.24	63.58	31.18	50.29	49.74	50.02	0.05
	07-Jun-23	1.96	68.66	29.39	50.36	49.82	50.02	0.06
	08-Jun-23	3.74	66.38	29.88	50.29	49.84	50.02	0.05
	09-Jun-23	1.91	69.36	28.73	50.27	49.84	50.02	0.04
	10-Jun-23	4.26	73.51	22.23	50.30	49.82	50.00	0.04
	11-Jun-23	12.47	71.41	16.12	50.21	49.74	49.98	0.05
	12-Jun-23	1.24	65.34	33.43	50.30	49.83	50.03	0.06
	13-Jun-23	4.88	58.85	36.26	50.32	49.72	50.03	0.08
	14-Jun-23	14.81	61.71	23.47	50.41	49.51	49.99	0.12
	15-Jun-23	18.78	60.30	20.91	50.31	49.60	49.97	0.12
	16-Jun-23	8.38	69.04	22.58	50.24	49.68	50.00	0.06
	17-Jun-23	8.97	65.71	25.32	50.25	49.76	50.00	0.05
	18-Jun-23	2.35	69.71	27.94	50.30	49.82	50.02	0.05
	19-Jun-23	3.58	72.94	23.48	50.31	49.77	50.01	0.05
	20-Jun-23	3.48	74.02	22.50	50.21	49.80	50.01	0.03
	21-Jun-23	8.53	76.09	15.38	50.17	49.76	49.99	0.04
	22-Jun-23	3.44	71.12	25.44	50.25	49.82	50.01	0.04
	23-Jun-23	7.75	70.10	22.14	50.25	49.81	50.00	0.05
	24-Jun-23	3.28	77.57	19.16	50.17	49.81	50.00	0.03
	25-Jun-23	0.91	69.22	29.86	50.22	49.82	50.02	0.04
	26-Jun-23	7.35	69.87	22.78	50.25	49.67	50.00	0.05
	27-Jun-23	7.05	58.76	34.19	50.34	49.69	50.02	0.08
	28-Jun-23	2.71	75.38	21.91	50.25	49.78	50.01	0.04
	29-Jun-23	6.38	66.49	27.13	50.33	49.78	50.01	0.07
	30-Jun-23	8.22	63.02	28.76	50.24	49.70	50.01	0.06


6.राष्ट्रीय स्तर पर जल विद्युत उत्पादन
HYDRO GENERATION AT NATIONAL LEVEL

माह: जून 2023 MONTH:- JUN 2023

सभी आंकड़े मिलियन यूनिट में All figures in MU

दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Jun-23	251	41	56	70	9	427
02-Jun-23	252	43	64	75	10	443
03-Jun-23	242	49	66	72	9	439
04-Jun-23	225	28	61	59	9	380
05-Jun-23	224	31	61	63	8	387
06-Jun-23	223	41	64	69	8	406
07-Jun-23	228	25	61	65	9	389
08-Jun-23	228	17	56	70	9	379
09-Jun-23	235	17	58	69	9	388
10-Jun-23	261	15	61	66	13	416
11-Jun-23	276	14	61	75	23	450
12-Jun-23	296	19	56	77	26	474
13-Jun-23	322	18	57	76	28	502
14-Jun-23	343	19	61	84	25	532
15-Jun-23	345	20	37	100	27	529
16-Jun-23	327	21	57	102	29	536
17-Jun-23	327	19	50	125	30	550
18-Jun-23	352	17	45	101	29	544
19-Jun-23	359	19	49	105	27	559
20-Jun-23	374	19	46	115	29	583
21-Jun-23	383	19	47	115	29	592
22-Jun-23	384	23	47	115	30	599
23-Jun-23	392	23	41	103	30	589
24-Jun-23	391	22	40	98	27	576
25-Jun-23	387	19	37	85	19	546
26-Jun-23	380	21	32	102	26	561
27-Jun-23	389	21	35	103	26	574
28-Jun-23	397	21	39	100	23	579
29-Jun-23	397	20	35	125	24	600
30-Jun-23	393	20	38	130	23	604
कुल TOTAL	9580	701	1517	2714	621	15133
उच्चतम MAXIMUM	397	49	66	130	30	604
निम्नतम MINIMUM	223	14	32	59	8	379
औसत AVERAGE	319	23	51	90	21	504
संचयी 2023-24 Cumulative 2023-24	20928	2796	5708	5664	1278	36374
अब तक का उच्चतम All Time Max.	409	167	208	157	41	877
दिनांक Date	22.08.22	18.12.14	31.08.18	14.09.22	01.08.22	30.08.22

HYDRO ENERGY DURING THE MONTH OF JUNE' 2023

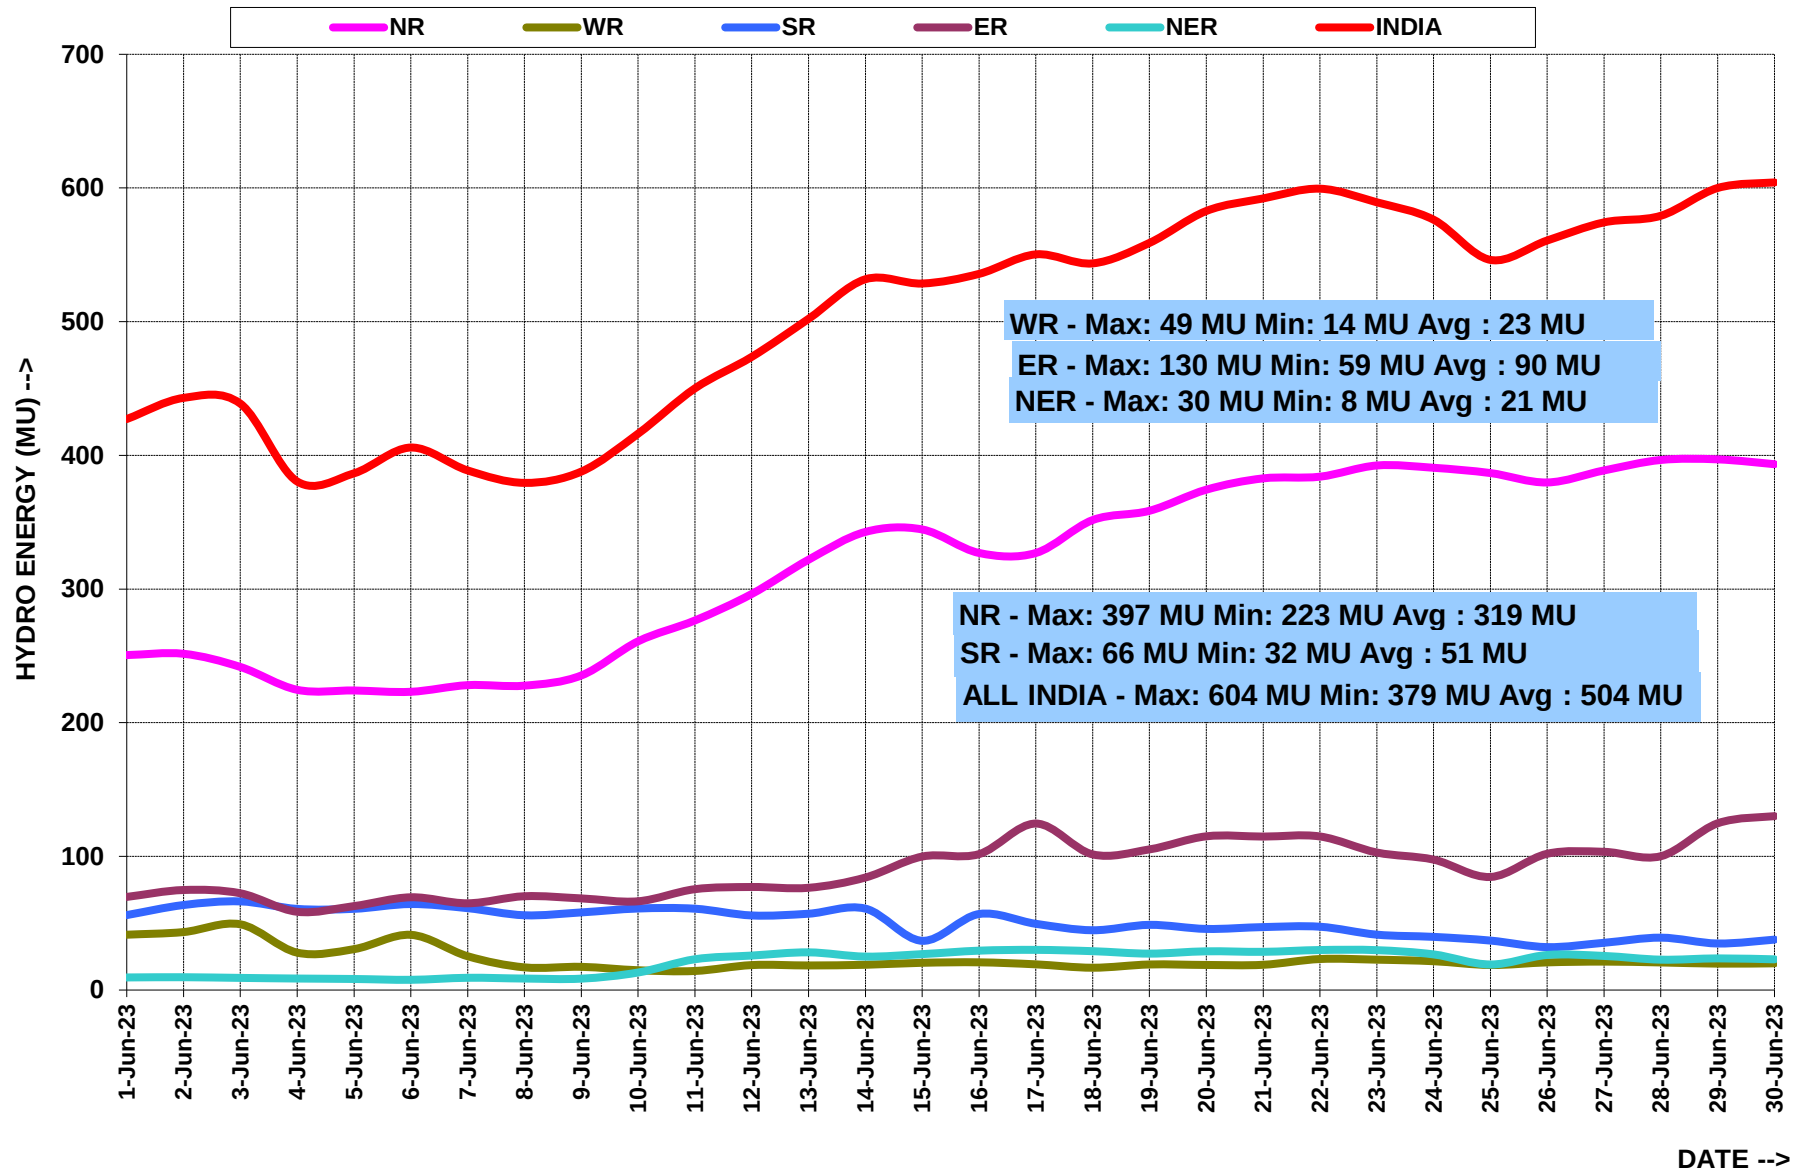

7. राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन
WIND GENERATION AT NATIONAL LEVEL

माह: जून 2023 MONTH:- JUN 2023

सभी आंकड़े मिलियन यूनिट में All figures in MU

दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Jun-23	18	173	123	-----	-----	313
02-Jun-23	11	175	132	-----	-----	318
03-Jun-23	16	135	130	-----	-----	281
04-Jun-23	25	139	155	-----	-----	318
05-Jun-23	11	140	172	-----	-----	324
06-Jun-23	31	150	168	-----	-----	349
07-Jun-23	18	141	180	-----	-----	340
08-Jun-23	31	154	196	-----	-----	381
09-Jun-23	48	147	215	-----	-----	410
10-Jun-23	60	157	222	-----	-----	439
11-Jun-23	41	158	209	-----	-----	407
12-Jun-23	43	214	193	-----	-----	450
13-Jun-23	46	237	220	-----	-----	503
14-Jun-23	61	249	222	-----	-----	533
15-Jun-23	49	190	176	-----	-----	416
16-Jun-23	52	107	239	-----	-----	399
17-Jun-23	69	131	223	-----	-----	424
18-Jun-23	25	160	198	-----	-----	383
19-Jun-23	45	135	124	-----	-----	304
20-Jun-23	63	130	118	-----	-----	311
21-Jun-23	58	112	122	-----	-----	291
22-Jun-23	49	126	129	-----	-----	304
23-Jun-23	46	118	178	-----	-----	342
24-Jun-23	42	105	206	-----	-----	352
25-Jun-23	31	88	152	-----	-----	272
26-Jun-23	21	115	224	-----	-----	360
27-Jun-23	15	108	204	-----	-----	326
28-Jun-23	15	121	218	-----	-----	354
29-Jun-23	20	156	218	-----	-----	395
30-Jun-23	29	176	214	-----	-----	419
कुल TOTAL	1088	4448	5481	-----	-----	11016
उच्चतम MAXIMUM	69	249	239	-----	-----	533
निम्नतम MINIMUM	11	88	118	-----	-----	272
औसत AVERAGE	36	148	183	-----	-----	367
संचयी 2023-24 Cumulative 2023-24	2686	10833	8803	-----	-----	22322
अब तक का उच्चतम All Time Max.	78	272	297	-----	-----	555
दिनांक Date	09.06.22	22.05.22	12.07.22	-----	-----	22.05.22

*Source: As reported by SLDCs. Limited visibility of embedded wind generator data.

8. राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन
SOLAR GENERATION AT NATIONAL LEVEL

माह: जून 2023 MONTH:- JUN 2023

सभी आंकड़े मिलियन यूनिट में All figures in MU

दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Jun-23	114	56	120	2.9	1.2	294
02-Jun-23	129	62	120	5.6	1.2	317
03-Jun-23	129	62	125	5.7	1.3	323
04-Jun-23	138	59	84	3.1	1.2	286
05-Jun-23	130	67	128	2.9	1.3	329
06-Jun-23	120	66	123	2.9	1.1	313
07-Jun-23	132	66	118	3.1	1.0	320
08-Jun-23	134	67	123	2.8	1.1	329
09-Jun-23	135	68	125	3.0	0.9	332
10-Jun-23	132	67	125	3.0	0.8	327
11-Jun-23	132	65	119	5.5	0.6	321
12-Jun-23	138	60	125	2.9	0.7	326
13-Jun-23	132	59	129	2.2	1.0	323
14-Jun-23	134	60	128	2.6	0.5	324
15-Jun-23	120	56	133	2.9	0.5	312
16-Jun-23	93	41	135	2.8	0.5	272
17-Jun-23	71	42	112	2.8	0.4	228
18-Jun-23	107	48	99	5.6	0.4	260
19-Jun-23	135	51	108	5.2	0.4	299
20-Jun-23	134	57	105	3.1	0.6	300
21-Jun-23	136	56	99	2.2	0.6	295
22-Jun-23	136	54	103	2.6	0.7	297
23-Jun-23	140	47	95	2.3	1.0	286
24-Jun-23	139	42	88	2.3	1.3	272
25-Jun-23	125	40	94	1.7	1.1	262
26-Jun-23	120	33	97	4.4	1.2	256
27-Jun-23	121	33	106	4.1	1.0	265
28-Jun-23	122	36	106	1.8	0.9	266
29-Jun-23	122	35	107	2.1	0.8	266
30-Jun-23	126	37	116	2.4	0.9	283
कुल TOTAL	3773	1593	3393	97	26	8881
उच्चतम MAXIMUM	140	68	135	6	1	332
निम्नतम MINIMUM	71	33	84	2	0	228
औसत AVERAGE	126	53	113	3	1	296
संचयी 2023-24 Cumulative 2023-24	11812	5447	10697	336	89.3	28381
अब तक का उच्चतम All Time Max.	147	71	143	7	2.4	351
दिनांक Date	10.05.23	12.05.23	21.03.23	23.03.23	22.06.22	10.05.23

*Source: RLDCs for solar connected to ISTS; SLDCs for embedded solar. Limited visibility of embedded solar data.

9. राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग पूर्ति
DAILY MAXIMUM DEMAND MET AT NATIONAL LEVEL

माह: जून 2023 MONTH:- JUN 2023

सभी आंकड़े मेगावाट में All figures in MW


दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL	विभिन्नता फैक्टर Diversity Factor*
01-Jun-23	55724	67044	54171	28345	3399	199477	1.046
02-Jun-23	58321	68043	55616	28146	3401	206375	1.035
03-Jun-23	59470	68736	56532	28224	3474	211608	1.023
04-Jun-23	58812	63987	50553	28132	3276	199064	1.029
05-Jun-23	62895	67041	56144	28776	3488	213982	1.020
06-Jun-23	63638	67777	56642	29020	3504	217259	1.015
07-Jun-23	66257	68483	56684	29277	3437	217843	1.029
08-Jun-23	68134	69491	56452	29137	3400	222920	1.017
09-Jun-23	70740	69562	56676	29325	3130	223235	1.028
10-Jun-23	68793	68872	53217	27001	3014	219301	1.007
11-Jun-23	69767	63651	48324	27587	2871	206667	1.027
12-Jun-23	73064	65173	54744	27520	3220	218673	1.023
13-Jun-23	72058	63863	54416	27903	3099	215352	1.028
14-Jun-23	71761	62164	55214	28172	2982	214583	1.027
15-Jun-23	70190	61415	57788	28671	2517	210901	1.046
16-Jun-23	70461	58221	58198	28995	2544	211962	1.030
17-Jun-23	69834	58936	56420	28797	2524	211781	1.022
18-Jun-23	67953	60095	52585	28317	2368	204565	1.033
19-Jun-23	68934	63352	55852	26704	2692	213661	1.018
20-Jun-23	71327	64709	53769	27625	2689	214640	1.026
21-Jun-23	74979	65748	53179	27358	2942	217678	1.030
22-Jun-23	76809	65868	52006	26644	2968	215225	1.042
23-Jun-23	77341	63432	51560	27647	3131	215938	1.033
24-Jun-23	75869	60548	49437	27329	3287	209620	1.033
25-Jun-23	72171	56194	45788	26436	3131	198675	1.025
26-Jun-23	68581	55874	49116	24970	3305	193289	1.044
27-Jun-23	69215	54881	51037	23402	3085	194244	1.038
28-Jun-23	69616	54070	51206	23765	3145	194218	1.039
29-Jun-23	67566	53231	52510	24990	3128	190460	1.058
30-Jun-23	66660	53665	51760	25168	3066	193125	1.037
उच्चतम MAXIMUM	77341	69562	58198	29325	3504	223235	1.058
निम्नतम MINIMUM	55724	53231	45788	23402	2368	190460	1.007
औसत AVERAGE	68565	62804	53587	27446	3074	209211	1.030
अब तक का उच्चतम All Time Max.	77341	71321	64314	29325	3596	223235	
दिनांक Date	23.06.23	27.12.22	15.03.23	09.06.23	17.08.22	09.06.23	

* Diversity factor = (Sum of regional max demands) / All India max demand


नोट : यह आंकड़े एनएलडीसी स्काडा प्रणाली में दर्ज दैनिक अधिकतम मांगपूर्ति दर्शाते हैं।

Note: The above figures denote daily maximum demand met recorded in NLDC SCADA.


10. DEMAND AND GENERATION PLOTS FOR 09 JUNE (MAXIMUM DEMAND MET)

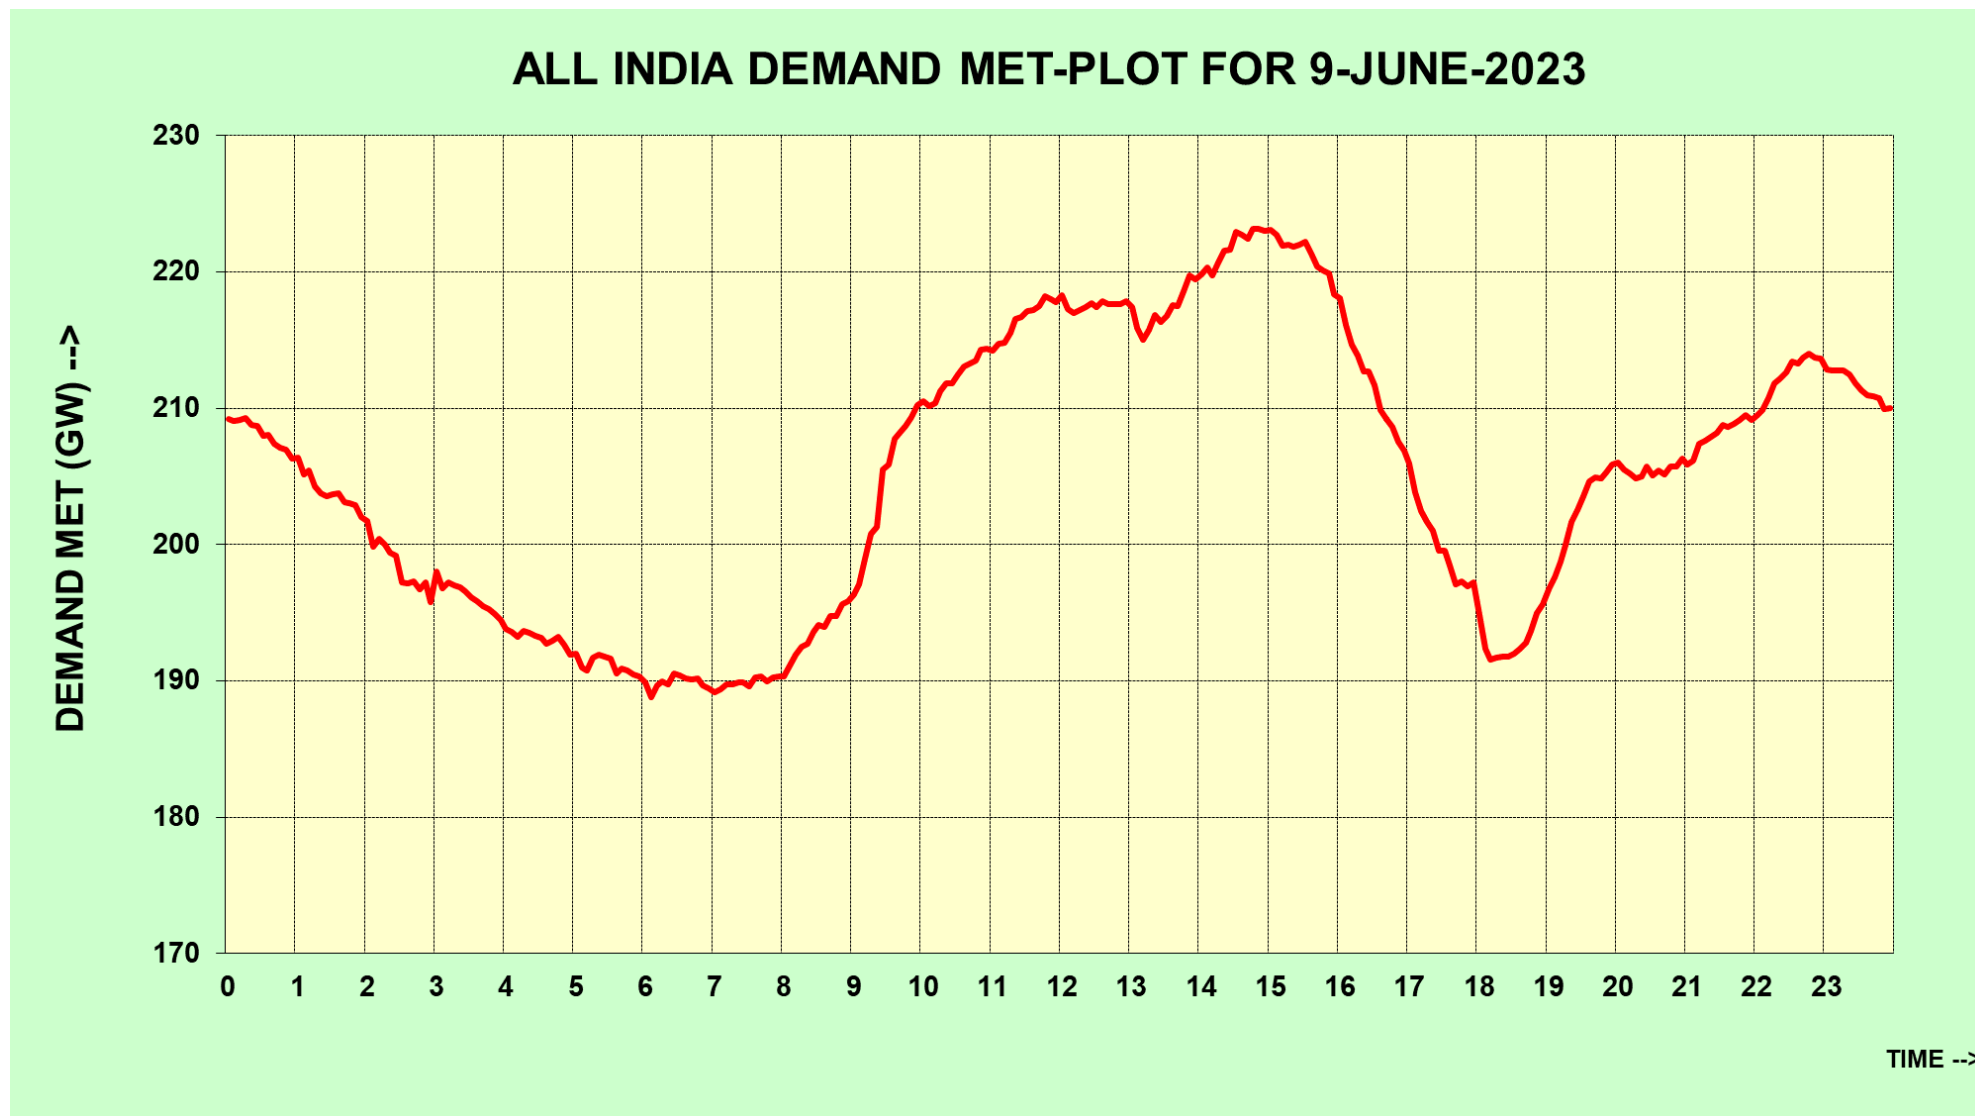


REGIONAL DEMAND MET PLOT FOR 9-JUNE-2023

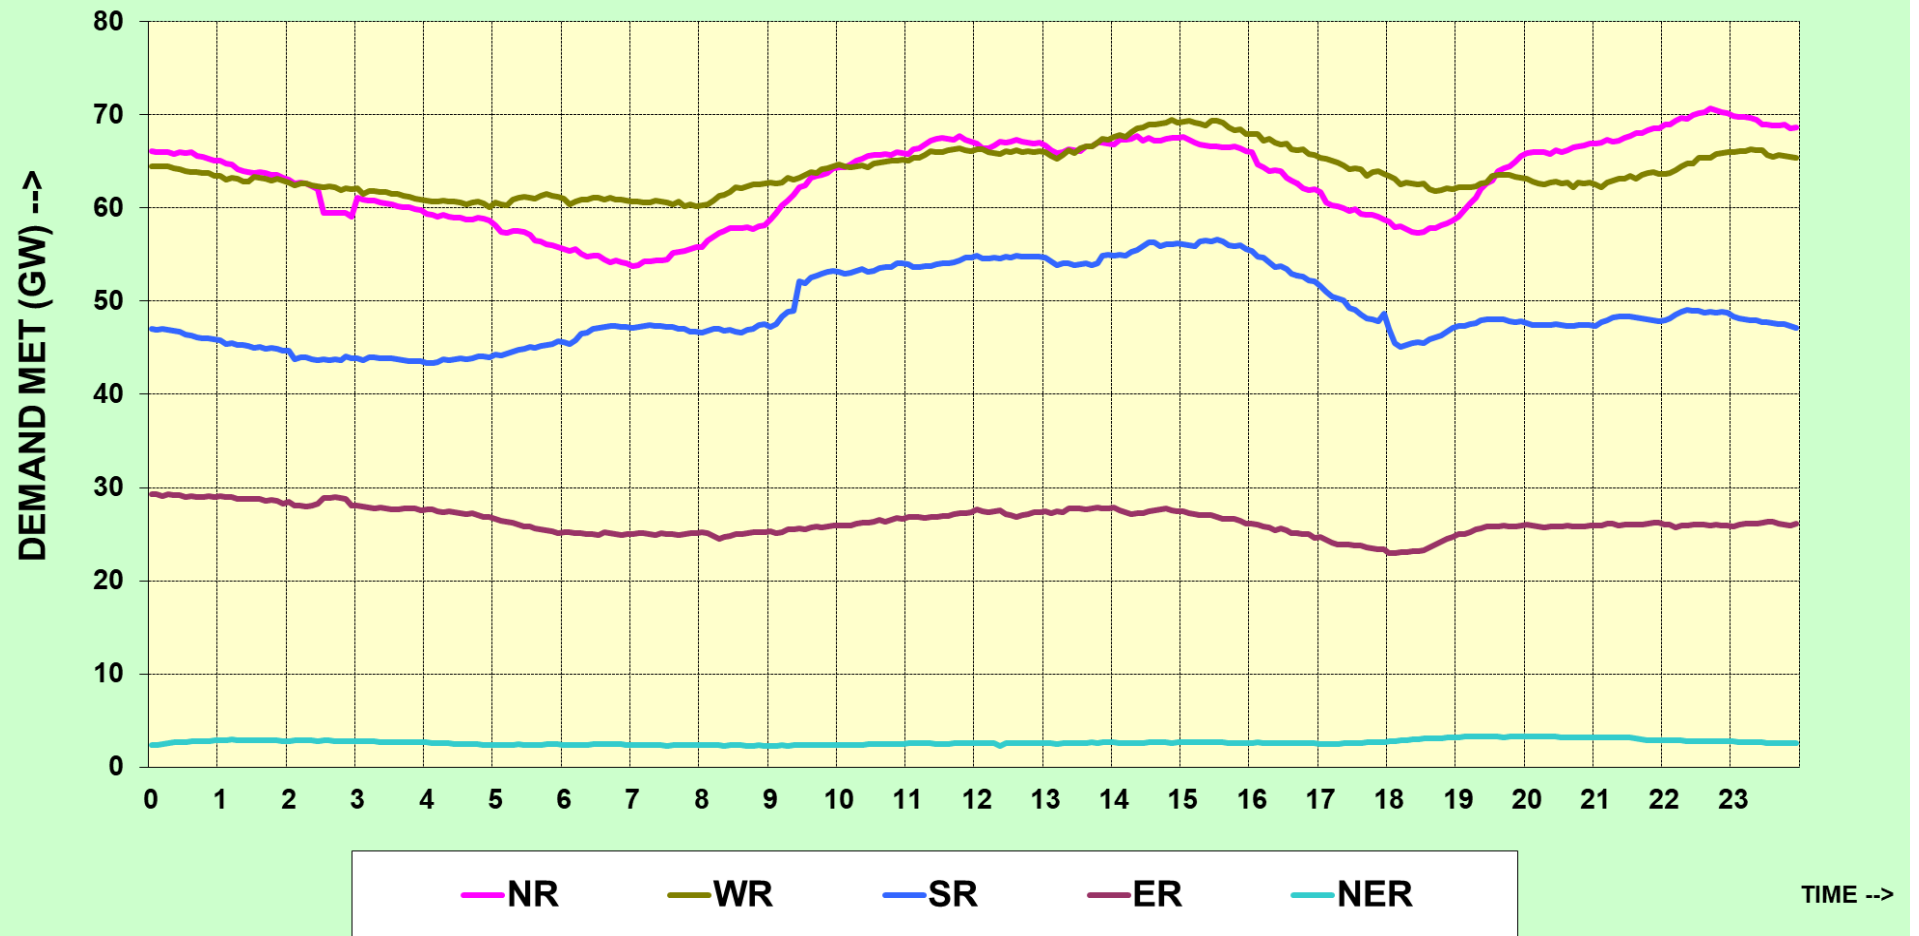

ALL INDIA GENERATION PLOT FOR 9-JUNE-2023

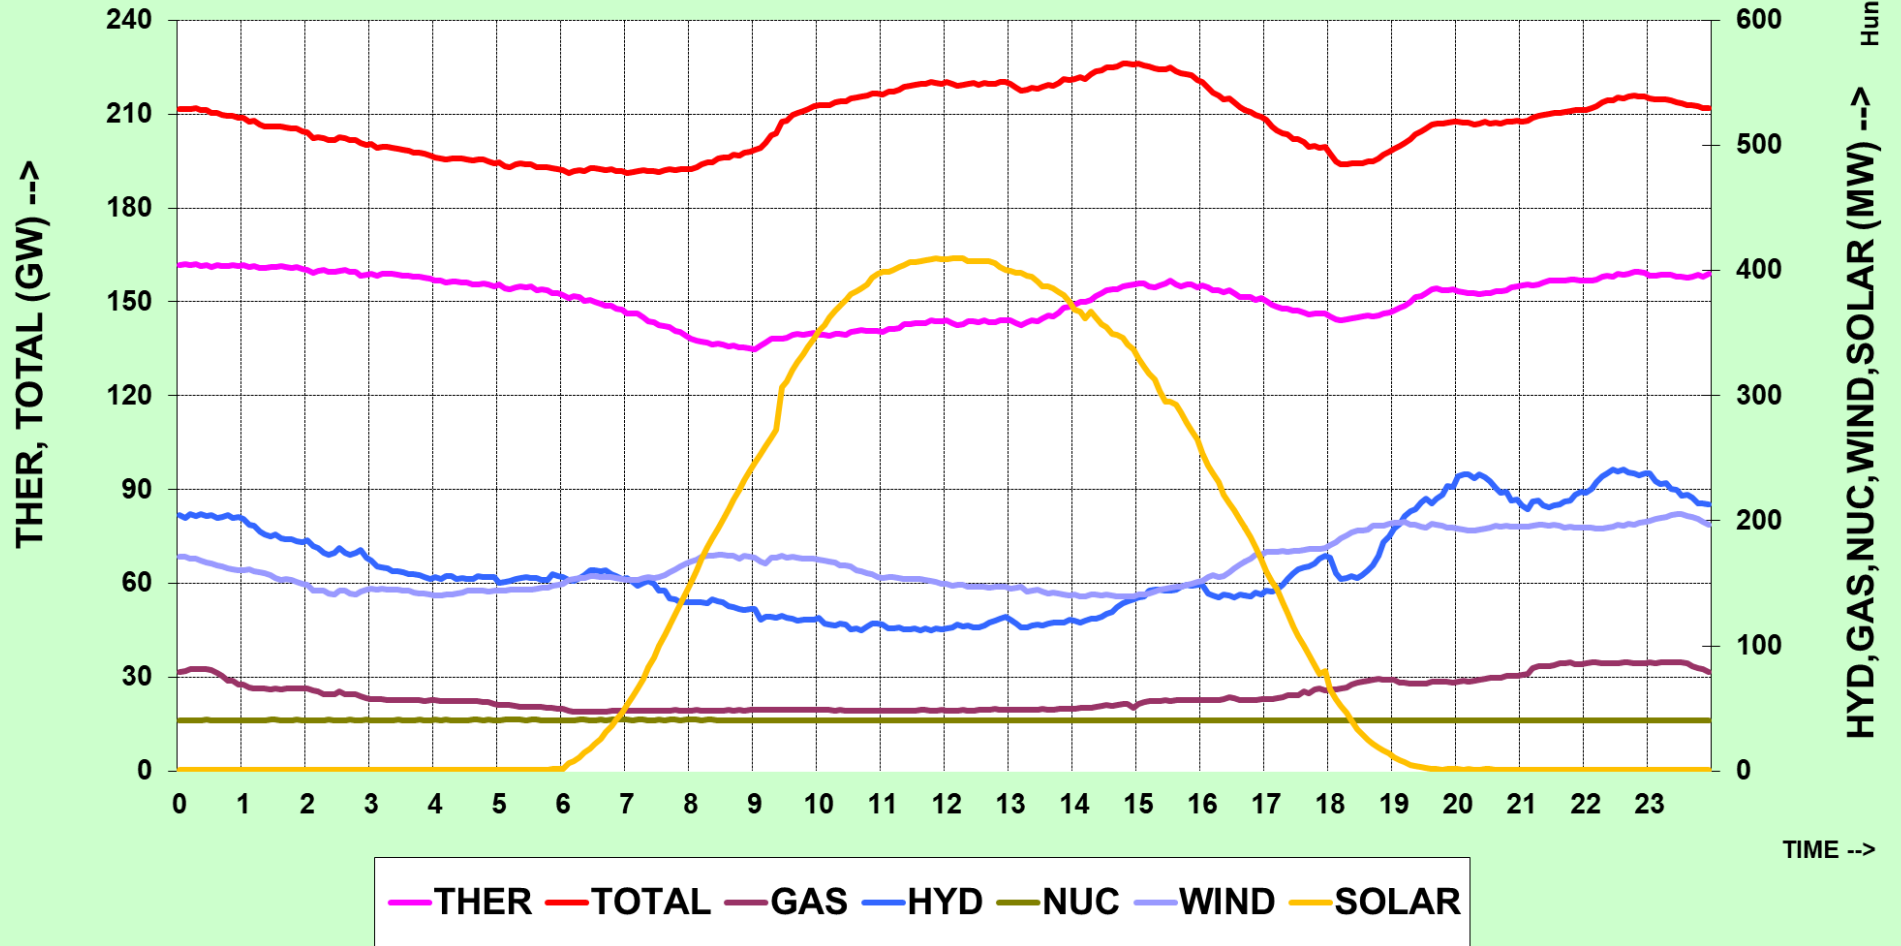

All India Fuel-wise Generation Patterns for 9-JUNE-2023

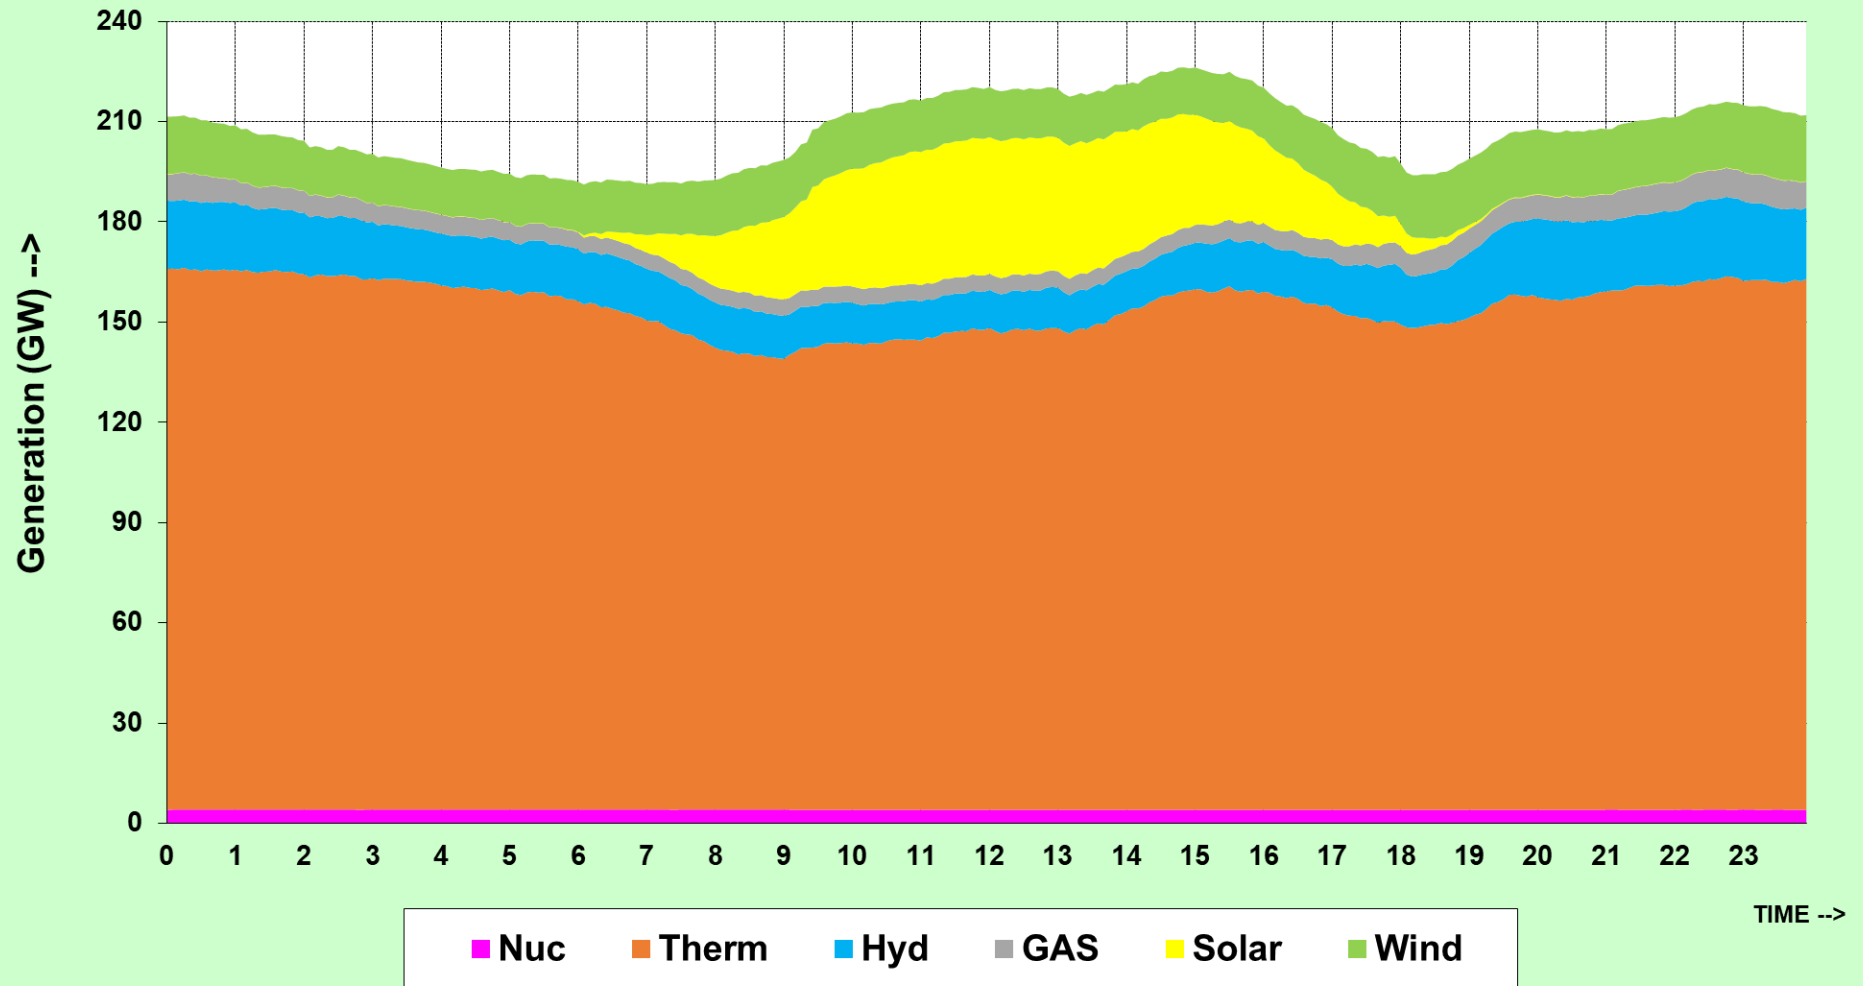

09 जून 2023 (अधिकतम माँग) की आल इंडिया माँग आपूर्ति
ALL INDIA DEMAND MET FOR 09 JUN 2023 (MAXIMUM DEMAND*)

Time (hrs)	All India Demand (MW)		Time (hrs)	All India Demand (MW)
00:05	209044		12:05	217290
00:20	208794		12:20	217397
00:35	208034		12:35	217847
00:50	206957		12:50	217605
01:05	205154		13:05	215882
01:20	203747		13:20	216848
01:35	203754		13:35	217572
01:50	202901		13:50	219725
02:05	199832		14:05	220312
02:20	199380		14:20	221538
02:35	197149		14:35	222705
02:50	197242		14:50	223169
03:05	196802		15:05	222697
03:20	196824		15:20	221835
03:35	195807		15:35	221367
03:50	194874		15:50	219903
04:05	193585		16:05	216108
04:20	193507		16:20	212715
04:35	192696		16:35	209877
04:50	192637		16:50	207530
05:05	190938		17:05	203803
05:20	191928		17:20	201025
05:35	190565		17:35	198487
05:50	190452		17:50	196906
06:05	188768		18:05	192381
06:20	189706		18:20	191777
06:35	190169		18:35	192321
06:50	189690		18:50	194980
07:05	189342		19:05	197559
07:20	189852		19:20	201632
07:35	190220		19:35	204652
07:50	190217		19:50	205258
08:05	191146		20:05	205492
08:20	192738		20:20	205028
08:35	193934		20:35	205418
08:50	195644		20:50	205751
09:05	197084		21:05	206148
09:20	201278		21:20	207926
09:35	207786		21:35	208625
09:50	209336		21:50	209474
10:05	210155		22:05	209840
10:20	211847		22:20	212215
10:35	213080		22:35	213269
10:50	214282		22:50	213726
11:05	214739		23:05	212758
11:20	216536		23:20	212446
11:35	217235		23:35	210951
11:50	217993		23:50	209956
Maximum Demand of 223235 MW met@14:52 hrs (from 1 min. interval SCADA DATA)				

* 15 minute interval SCADA DATA of instantaneous demand

11. ACTUAL POWER SUPPLY POSITION - JUNE 2023

REGION	STATE	Requirement/Availability in MU/DAY			Requirement/Availability in MU				Peak Demand/Peak Met in MW			
		Requirement	Energy met	Surplus(+)/ Deficit(-)	Requirem ent	Energy met	Surplus(+)/ Deficit(-)	% Shortage	Requirement	Peak Demand Met	Surplus(+)/ Deficit(-)	% Shortage
NR	Chandigarh	6	6	0.0	182	182	0	0.0	377	377	0	0.0
	Delhi	122	122	0.0	3667	3666	0	0.0	6916	7226	310	4.5
	Haryana	205	205	-0.7	6159	6137	-22	-0.4	10020	11634	1614	16.1
	Himachal Pradesh	31	31	-0.1	935	933	-2	-0.2	1753	1753	0	0.0
	J&K(UT) and Ladakh(UT)	53	52	-0.9	1586	1560	-26	-1.6	2847	2847	0	0.0
	Punjab	236	236	0.0	7077	7077	0	0.0	11940	15293	3353	28.1
	Rajasthan	271	271	-0.1	8136	8133	-3	0.0	15840	15840	0	0.0
	Uttar Pradesh	504	504	-0.2	15123	15116	-7	0.0	27611	27611	0	0.0
	Uttarakhand	50	50	-0.1	1495	1491	-4	-0.3	2415	2436	21	0.9
	Railway	3	3	0.0	103	103	0	0.0	189	189	0	0.0
	NFL	0	0	0.0	2	2	0	0.0	4	4	0	0.0
	TOTAL	1482	1480	-2.1	44466	44402	-64	-0.1	78048	77898	-150	-0.2
WR	Gujarat	392	392	0.0	11759	11759	0	0.0	22225	22225	0	0.0
	Madhya Pradesh	241	241	0.0	7234	7234	0	0.0	11837	11837	0	0.0
	Chhattisgarh	107	106	0.0	3196	3195	-1	0.0	5289	5289	0	0.0
	Maharashtra	585	584	-0.8	17535	17512	-23	-0.1	28546	28546	0	0.0
	Goa	15	15	0.0	440	440	0	-0.1	776	776	0	0.0
	DNHDDPDCL	29	29	0.0	879	879	0	0.0	1311	1311	0	0.0
	AMNSIL	18	18	0.0	537	537	0	0.0	863	863	0	0.0
	BALCO*	12	12	0.0	372	372	0	0.0	525	525	0	0.0
	TOTAL	1398	1398	-0.8	41952	41927	-25	-0.1	69366	69022	-344	-0.5
SR	Andhra Pradesh	237	237	0.0	7113	7113	0	0.0	12903	12900	-3	0.0
	Telangana	200	202	2.5	6000	6075	75	1.2	11436	11417	-19	-0.2
	Karnataka	244	246	2.5	7309	7383	75	1.0	14198	14198	0	0.0
	Kerala	80	81	0.8	2415	2439	24	1.0	4644	4616	-28	-0.6
	Tamil Nadu	366	369	3.3	10967	11065	98	0.9	18527	18522	-5	0.0
	Puducherry	10	10	0.1	309	311	3	0.9	505	505	0	0.0
	TOTAL	1137	1146	9.1	34112	34386	274	0.8	58217	58217	0	0.0
ER	Bihar	137	135	-2.2	4112	4047	-65	-1.6	7071	7071	0	0.0
	Jharkhand	37	37	-0.5	1111	1096	-15	-1.4	1923	1923	0	0.0
	DVC	77	77	0.0	2300	2300	0	0.0	3594	3594	0	0.0
	Odisha	121	121	0.0	3632	3631	-1	0.0	6854	6854	0	0.0
	West Bengal	213	213	0.0	6402	6402	0	0.0	11806	11806	0	0.0
	Sikkim	1	1	0.0	42	42	0	0.0	101	101	0	0.0
	Railways_ER ISTS*	0	0	0.0	3	3	0	0.0	41	41	0	0.0
	TOTAL	587	584	-2.7	17603	17522	-81	-0.5	29669	29326	-343	-1.2
NER	Arunachal Pradesh	3	3	0.0	79	79	0	0.0	155	155	0	0.0
	Assam	38	38	-0.1	1141	1139	-3	-0.2	2307	2307	0	0.0
	Manipur	2	2	0.0	71	71	0	0.0	185	185	0	0.0
	Meghalaya	6	5	-1.1	177	143	-34	-19.4	333	333	0	0.0
	Mizoram	2	2	0.0	51	51	0	0.0	125	125	0	0.0
	Nagaland	3	3	0.0	81	81	0	0.0	167	167	0	0.0
	Tripura	5	5	0.0	150	150	0	0.0	362	362	0	0.0
	TOTAL	58	57	-1.2	1751	1714	-37	-2.1	3560	3541	-19	-0.5
ALL INDIA		4663	4665	2.3	139883	139951	68	0.0				

* BALCO has been added as new entity wef 20.12.2022

NOTE: BASED ON THE DATA FURNISHED BY ENTITIES ON DAILY BASIS

12. ENERGY COMPARISON OF JUNE 2023 vs JUNE 2022

REGION	STATE	Energy Requirement (MU)					Energy Met (MU)				
		Jun-22	Jun-23	Difference	% Change	Average MU/day for Jun-23	Jun-22	Jun-23	Difference	% Change	Average MU/day for Jun-23
NR	Chandigarh	198	182	-15	-8	6	198	182	-15	-8	6
	Delhi	3904	3667	-237	-6	122	3903	3666	-237	-6	122
	Haryana	6371	6159	-212	-3	205	6351	6137	-214	-3	205
	Himachal Pradesh	1040	935	-104	-10	31	1034	933	-101	-10	31
	J&K(UT) and Ladakh(UT)	1569	1586	17	1	53	1525	1560	34	2	52
	Punjab	7533	7077	-455	-6	236	7533	7077	-455	-6	236
	Rajasthan	8886	8136	-750	-8	271	8723	8133	-590	-7	271
	Uttar Pradesh	15130	15123	-7	0	504	14857	15116	259	2	504
	Uttarakhand	1512	1495	-17	-1	50	1479	1491	12	1	50
	Railway/NFL	93	105	12	13	4	93	105	12	13	4
	TOTAL	46235	44466	-1769	-4	1482	45696	44402	-1294	-3	1480
WR	Gujarat	12599	11759	-840	-7	392	12599	11759	-840	-7	392
	Madhya Pradesh	7023	7234	210	3	241	7023	7234	210	3	241
	Chhattisgarh	3041	3196	155	5	107	3040	3195	154	5	106
	Maharashtra	16003	17535	1532	10	585	16003	17512	1508	9	584
	Goa	384	440	56	15	15	384	440	56	15	15
	DNHDDPDCL	840	879	39	5	29	840	879	39	5	29
	AMNSIL	529	537	8	1	18	529	537	8	1	18
	BALCO*		372	-	-	12		372	-	-	12
	TOTAL	40420	41952	1532	4	1398	40419	41927	1508	4	1398
SR	Andhra Pradesh	6062	7113	1051	17	237	6062	7113	1051	17	237
	Telangana	5748	6000	251	4	200	5748	6075	327	6	202
	Karnataka	6220	7309	1089	18	244	6219	7383	1165	19	246
	Kerala	2359	2415	56	2	80	2359	2439	80	3	81
	Tamil Nadu	10459	10967	508	5	366	10458	11065	607	6	369
	Puducherry	280	309	29	10	10	280	311	31	11	10
	TOTAL	31128	34112	2984	10	1137	31125	34386	3261	10	1146
ER	Bihar	3712	4112	400	11	137	3658	4047	389	11	135
	Jharkhand	1044	1111	67	6	37	963	1096	133	14	37
	DVC	2463	2300	-163	-7	77	2463	2300	-162	-7	77
	Odisha	3872	3632	-240	-6	121	3872	3631	-241	-6	121
	West Bengal	5551	6402	851	15	213	5545	6402	857	15	213
	Sikkim	44	42	-2	-4	1	44	42	-2	-4	1
	Railways_ER ISTS*		3	-	-	0		3	-	-	0
	TOTAL	16685	17603	917	5	587	16544	17522	978	6	584
NER	Arunachal Pradesh	79	79	0	0	3	79	79	0	0	3
	Assam	991	1141	150	15	38	991	1139	148	15	38
	Manipur	77	71	-6	-7	2	76	71	-6	-7	2
	Meghalaya	164	177	14	8	6	156	143	-13	-8	5
	Mizoram	51	51	0	0	2	51	51	0	0	2
	Nagaland	78	81	3	4	3	78	81	3	4	3
	Tripura	220	150	-70	-32	5	220	150	-70	-32	5
	TOTAL	1659	1751	91	6	58	1651	1714	63	4	57
ALL INDIA		136127	139883	3756	3	4663	135435	139951	4516	3	4665

* BALCO has been added as new entity wef 20.12.2022

13. DEMAND COMPARISON OF JUNE 2023 vs JUNE 2022

REGION	STATE	Peak Requirement (MW)				Peak Met (MW)			
		Jun-22	Jun-23	Difference	% Change	Jun-22	Jun-23	Difference	% Change
NR	Chandigarh	411	377	-34	-8.3	411	377	-34	-8.3
	Delhi	7695	6916	-779	-10.1	7695	7226	-469	-6.1
	Haryana	12768	10020	-2748	-21.5	12768	11634	-1134	-8.9
	Himachal Pradesh	1739	1753	14	0.8	1739	1753	14	0.8
	J&K(UT) and Ladakh(UT)	2723	2847	124	4.6	2723	2847	124	4.6
	Punjab	14207	11940	-2267	-16.0	14207	15293	1086	7.6
	Rajasthan	16012	15840	-172	-1.1	16012	15840	-172	-1.1
	Uttar Pradesh	26165	27611	1446	5.5	25755	27611	1856	7.2
	Uttarakhand	2594	2415	-179	-6.9	2594	2436	-158	-6.1
	Railway/NFL	173	193	20	11.4	173	193	20	11.4
WR	Gujarat	21236	22225	989	5	21236	22225	989	4.7
	Madhya Pradesh	11520	11837	317	3	11480	11837	357	3.1
	Chhattisgarh	4685	5289	604	13	4685	5289	604	12.9
	Maharashtra	26972	28546	1575	6	26972	28546	1575	5.8
	Goa	663	776	113	17	661	776	116	17.5
	DNHDDPDCL	1243	1311	68	5.5	1243	1311	68	5.5
	AMNSIL	919	863	-55	-6.0	919	863	-55	-6.0
	BALCO*		525	-	-		525	-	-
SR	Andhra Pradesh	11218	12903	1685	15.0	11218	12900	1682	15.0
	Telangana	10519	11436	917	8.7	10519	11417	898	8.5
	Karnataka	12260	14198	1938	15.8	12260	14198	1938	15.8
	Kerala	4190	4644	454	10.8	4182	4616	434	10.4
	Tamil Nadu	16906	18527	1621	9.6	16906	18522	1616	9.6
	Puducherry	482	505	23	4.8	482	505	23	4.8
ER	Bihar	7045	7071	26	0.4	6294	7071	777	12.3
	Jharkhand	2190	1923	-267	-12.2	1661	1923	262	15.8
	DVC	3526	3594	68	1.9	3526	3594	68	1.9
	Odisha	6367	6854	487	7.7	6367	6854	487	7.7
	West Bengal	9743	11806	2063	21.2	9713	11806	2093	21.5
	Sikkim	116	101	-15	-12.9	116	101	-15	-12.9
	Railways_ER ISTS*		41	41	-		41	41	-
NER	Arunachal Pradesh	158	155	-3	-1.8	137	155	18	13.2
	Assam	2140	2307	167	7.8	2059	2307	247	12.0
	Manipur	201	185	-16	-8.2	198	185	-13	-6.8
	Meghalaya	342	333	-9	-2.7	342	333	-9	-2.7
	Mizoram	118	125	7	6.2	118	125	7	6.2
	Nagaland	150	167	17	11.1	150	167	17	11.1
	Tripura	306	362	56	18.2	306	362	56	18.2

* BALCO has been added as new entity wef 20.12.2022

14. SCHEDULE AND DRAWAL OF CONSTITUENTS - JUNE 2023

REGION	STATE	SCHEDULE (MU)	ACTUAL DRAWAL (MU)	Over drawal(+)/ Under Drawal(-) (MU)	% OD/UD	SCHEDULE (MU/DAY)	ACTUAL DRAWAL (MU/DAY)	Over drawal(+)/ Under Drawal(-) (MU/DAY)
NR	Chandigarh	185.47	185.52	0.05	0.03	6.18	6.18	0.00
	Delhi	3389.83	3392.06	2.23	0.07	112.99	113.07	0.07
	Haryana	4421.26	4421.31	0.05	0.00	147.38	147.38	0.00
	Himachal Pradesh	-59.94	-59.93	0.01	-0.01	-2.00	-2.00	0.00
	J&K(UT) and Ladakh(UT)	770.06	763.60	-6.46	-0.84	25.67	25.45	-0.22
	Punjab	3800.59	3718.51	-82.08	-2.16	126.69	123.95	-2.74
	Rajasthan	1922.87	1813.01	-109.86	-5.71	64.10	60.43	-3.66
	Uttar Pradesh	7298.55	7242.77	-55.78	-0.76	243.29	241.43	-1.86
	Uttarakhand	711.38	687.19	-24.19	-3.40	23.71	22.91	-0.81
	Railway	99.45	102.68	3.23	3.24	3.32	3.42	0.11
	NFL	2.34	2.33	-0.01	-0.60	0.08	0.08	0.00
	Total	22541.88	22269.05	-272.83	-1.21	751.40	742.30	-9.09
WR	Gujarat	5302.31	5279.29	-23.02	-0.43	176.74	175.98	-0.77
	Madhya Pradesh	3777.81	3662.60	-115.21	-3.05	125.93	122.09	-3.84
	Chhattisgarh	1591.21	1565.41	-25.80	-1.62	53.04	52.18	-0.86
	Maharashtra	6195.23	6205.71	10.47	0.17	206.51	206.86	0.35
	Goa	428.33	427.53	-0.80	-0.19	14.28	14.25	-0.03
	DNHDDPDCL	886.62	879.48	-7.14	-0.81	29.55	29.32	-0.24
	AMNSIL	277.41	276.17	-1.24	-0.45	9.25	9.21	-0.04
	BALCO*	372.50	372.02	-0.48	-0.13	12.42	12.40	-0.02
	Total	18831.42	18668.20	-163.22	-0.87	627.71	622.27	-5.44
SR	Andhra Pradesh	2037.76	2033.11	-4.65	-0.23	67.93	67.77	-0.16
	Telangana	2605.38	2611.45	6.07	0.23	86.85	87.05	0.20
	Karnataka	2172.52	2184.09	11.57	0.53	72.42	72.80	0.39
	Kerala	1858.95	1898.49	39.54	2.13	61.97	63.28	1.32
	Tamil Nadu	4872.23	4752.73	-119.50	-2.45	162.41	158.42	-3.98
	Puducherry	299.75	289.95	-9.80	-3.27	9.99	9.67	-0.33
	Goa (SR)	67.77	68.47	0.70	1.03	2.26	2.28	0.02
	Total	13914.36	13838.29	-76.07	-0.55	463.81	461.28	-2.54
ER	Bihar	3801.16	3774.50	-26.66	-0.70	126.71	125.82	-0.89
	Jharkhand	943.30	928.74	-14.56	-1.54	31.44	30.96	-0.49
	DVC	-1275.86	-1264.65	11.22	-0.88	-42.53	-42.15	0.37
	Odisha	1563.71	1571.73	8.02	0.51	52.12	52.39	0.27
	West Bengal	2731.78	2658.98	-72.80	-2.66	91.06	88.63	-2.43
	Sikkim	40.35	39.98	-0.37	-0.92	1.35	1.33	-0.01
	Railways_ER ISTS*	7.29	3.39	-3.90	-53.51	0.24	0.11	-0.13
	Total	7811.73	7712.68	-99.05	-1.27	260.39	257.09	-3.30
NER	Arunachal Pradesh	80.25	76.82	-3.42	-4.26	2.67	2.56	-0.11
	Assam	930.69	941.31	10.62	1.14	31.02	31.38	0.35
	Manipur	75.39	70.88	-4.51	-5.98	2.51	2.36	-0.15
	Meghalaya	63.64	60.02	-3.62	-5.69	2.12	2.00	-0.12
	Mizoram	50.30	44.29	-6.01	-11.94	1.68	1.48	-0.20
	Nagaland	75.34	72.22	-3.12	-4.14	2.51	2.41	-0.10
	Tripura	161.40	167.19	5.78	3.58	5.38	5.57	0.19
	Total	1437.00	1432.73	-4.28	-0.30	47.90	47.76	-0.14
All India Total		64536.39	63920.95	-615.44	-0.95	2151.21	2130.70	-20.51
* BALCO has been added as new entity wef 20.12.2022								

15. INTER REGIONAL EXCHANGES 2023-24

(All figures in MU)

	Apr'23	May'23	Jun'23	Fin. Year 2023-24
Name of Line				
Import of NR from WR (WR-NR)				
WR - NR 765 kV Gwalior - Agra 2xS/C	635.95	996.71	863.68	2496.34
WR-NR 765 kV Gwalior - Phagi 2xS/C	553.05	453.93	342.56	1349.54
WR-NR 765 kV Jabalpur-Orai D/C	430.29	804.53	778.33	2013.15
WR-NR 765 kV Satna-Orai	505.37	598.85	574.83	1679.05
WR-NR 765 kV Gwalior-Orai	0.00	0.00	0.00	0.00
WR - NR HVDC Champa - Kurukshetra	804.26	1126.68	2069.11	4000.05
WR - NR HVDC Vindhyachal	0.49	3.23	3.13	6.85
WR - NR 400 kV Zerda Kankroli	0.00	0.00	1.48	1.48
WR - NR 400 kV Zerda Bhinmal	0.00	0.00	0.00	0.00
WR - NR 400 kV RAPP C - Shujalpur D/C	2.28	31.04	16.05	49.37
WR - NR 220 kV Bhanpura - Ranpur	9.67	65.53	68.13	143.33
WR - NR 220 kV Bhanpura - Modak	0.00	0.00	0.00	0.00
WR - NR 220 kV Auraiya - Malanpur/Mehgaon	0.00	0.15	0.00	0.15
WR - NR 400 kV Vindhyachal-Rihand D/C	0.00	0.00	0.00	0.00
WR - NR HVDC Mundra - Mohindergarh	132.55	340.75	234.27	707.57
WR-NR 765 kV Banaskata-Chittorgarh D/C	0.00	3.26	16.02	19.28
WR-NR 765 kV Varanasi-Vindhyachal	1030.05	1663.34	1854.30	4547.69
Total WR - NR	4103.96	6088.00	6821.89	17013.85
Export of NR to WR (NR-WR)				
NR - WR 765 kV Gwalior - Agra 2xS/C	0.00	0.00	0.00	0.00
NR - WR 765 kV Gwalior - Phagi 2xS/C	0.00	5.41	0.00	5.41
NR - WR 765 kV Jabalpur-Orai D/C	0.00	0.00	0.00	0.00
NR - WR 765 kV Satna-Orai	0.00	0.00	0.00	0.00
NR - WR 765 kV Gwalior-Orai	440.87	385.11	301.32	1127.30
NR - WR HVDC Champa- Kurukshetra	0.00	0.00	0.00	0.00
NR - WR HVDC Vindhyachal	289.83	273.88	267.04	830.75
NR - WR 400 kV Zerda Kankroli	185.75	94.43	108.34	388.52
NR - WR 400 kV Zerda Bhinmal	282.42	181.64	200.56	664.62
NR - WR 400 kV RAPP C - Shujalpur D/C	85.74	45.64	45.64	177.02
NR - WR 220 kV Bhanpura - Ranpur	0.00	0.00	0.00	0.00
NR - WR 220 kV Bhanpura - Modak	0.00	0.00	0.00	0.00
NR - WR 220 kV Auraiya - Malanpur/Mehgaon	56.56	28.58	50.82	135.96
NR-WR 400 kV Rihand-Vindhyachal D/C	644.30	672.49	642.32	1959.11
NR - WR HVDC Mundra - Mohindergarh	243.86	54.36	36.25	334.47
NR - WR 765 kV Banaskata-Chittorgarh D/C	976.83	428.19	421.52	1826.54
NR-WR 765 kV Varanasi-Vindhyachal	0.00	0.00	0.00	0.00
Total NR - WR	3206.16	2169.73	2073.81	7449.70

	Apr'23	May'23	Jun'23	Fin. Year 2023-24
Name of Line				
Import of NR from ER (ER-NR)				
ER - NR 765 kV Sasaram - Fatehpur	166.02	114.36	82.57	362.95
ER - NR 765 kV Gaya - Varanasi 2*S/C	224.56	107.46	28.46	360.48
ER - NR 765 kV Gaya - Balia	246.38	335.46	321.28	903.12
ER - NR HVDC Alipurduar - Agra	0.00	0.00	375.05	375.05
ER-NR 400 kV Patna - Balia D/C	219.16	246.32	242.35	707.83
ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	127.03	223.63	277.35	628.01
ER - NR 400 kV Biharshariff - Balia D/C	22.11	72.32	102.97	197.40
ER - NR 400 kV Motihari - Gorakhpur D/C	156.88	188.70	180.09	525.67
ER - NR 400 kV Biharshariff - Varanasi D/C	67.56	47.21	34.66	149.43
ER - NR 400 kV Sasaram -Varanasi	74.99	38.68	46.09	159.76
ER - NR 400 kV Sasaram -Allahabad	51.91	33.39	21.29	106.59
ER - NR 220 kV Sahupuri-Karnamasa	78.64	82.22	82.32	243.18
ER - NR 132 kV Sahupuri - Karnamasa	1.92	0.00	0.96	2.88
ER - NR 132 kV 132 kV Rihand - Nagar Untari	0.00	0.00	0.00	0.00
ER - NR 132 kV Rihand - Garhwa	0.46	0.00	0.00	0.46
ER-NR 400 kV Naubatpur - Balia D/C	211.13	243.59	239.56	694.28
Total ER-NR	1648.75	1733.34	2035.00	5417.09
Import of NR from NER (NER-NR)				
NER-NR HVDC Biswanath Chariali - Agra	0.00	0.00	153.62	153.62
Total NER - NR	0.00	0.00	153.62	153.62
Export of NR to ER (NR-ER)				
NR - ER 765 kV Sasaram - Fatehpur	0.00	2.65	7.74	10.39
NR - ER 765 kV Gaya - Varanasi 2*S/C	0.30	38.74	102.98	142.02
NR - ER 765 kV Gaya - Balia	0.00	0.00	0.00	0.00
NR - ER HVDC Alipurduar - Agra	0.00	0.00	0.00	0.00
NR - ER 400 kV Patna - Balia 2xD/C	0.00	0.00	0.00	0.00
NR - ER 400 kV Muzaffarpur - Gorakhpur D/C	3.47	0.00	0.00	3.47
NR - ER 400 kV Biharshariff - Balia D/C	17.15	4.18	13.06	34.39
ER - NR 400 kV Motihari - Gorakhpur D/C	0.00	0.00	0.00	0.00
NR - ER 400 kV Biharshariff - Varanasi D/C	2.90	7.31	20.53	30.74
NR - ER 400 kV Sasaram -Varanasi	0.00	0.00	0.00	0.00
NR - ER 400 kV Sasaram -Allahabad	2.25	0.00	0.00	2.25
NR - ER 220 kV Sahupuri-Karnamasa	0.00	0.00	0.00	0.00
NR - ER 132 kV Sahupuri - Karnamasa	0.01	0.96	0.48	1.45
NR - ER 132 kV 132 kV Rihand - Nagar Untari	1.74	2.20	1.08	5.02
ER - NR 132 kV Rihand - Garhwa	10.23	8.48	19.67	38.38
NR-ER 400 kV Balia- Naubatpur D/C	0.00	0.00	0.00	0.00
Total NR - ER	38.05	64.52	165.54	268.11
Export of NR to NER (NER-NR)				
NR-NER HVDC Biswanath Chariali - Agra	261.93	291.71	104.47	658.11
Total NR - NER	261.93	291.71	104.47	658.11

	Apr'23	May'23	Jun'23	Fin. Year 2023-24
Name of Line				
Export of WR to ER (WR-ER)				
WR - ER 765 kV Ranchi - Dharamjaygarh 2xS/C	139.81	504.96	673.15	1317.92
WR - ER 765 kV Dharamjaygarh - Jharsuguda 2xD/C	652.31	469.82	490.99	1613.12
WR - ER 765 kV Durg - Jharsuguda D/C	0.00	0.64	1.75	2.39
WR - ER 400 kV Sipat - Ranchi D/C	15.97	93.84	118.29	228.10
WR - ER 400 kV Raigarh - Jharsuguda 2xD/C	0.44	6.23	8.79	15.46
WR - ER 220 kV Korba - Budhipadar D/C	36.08	80.04	73.19	189.32
WR - ER 220 kV Raigarh - Budhipadar	0.15	0.57	1.17	1.89
Total WR - ER	844.75	1156.11	1367.33	3368.19
Import of WR from ER (ER - WR)				
ER - WR 765 kV Ranchi - Dharamjaygarh 2xS/C	144.10	11.95	15.57	171.63
ER - WR 765 kV Dharamjaygarh - Jharsuguda 2xD/C	25.46	58.29	33.08	116.84
ER - WR 765 kV Durg - Jharsuguda D/C	394.08	204.42	148.02	746.51
ER - WR 400 kV Sipat - Ranchi D/C	55.56	5.71	9.07	70.34
ER - WR 400 kV Raigarh - Jharsuguda 2xD/C	248.78	148.94	125.69	523.40
ER - WR 220 kV Korba - Budhipadar D/C	1.45	0.00	0.14	1.59
ER - WR 220 kV Raigarh - Budhipadar	55.98	38.46	41.41	135.84
Total ER - WR	925.41	467.76	372.98	1766.15
Export of ER to NER (ER - NER)				
ER - NER 400 kV Binaguri - Bongaigaon D/C	6.99	16.15	105.81	128.95
ER - NER 400 kV Alipurduar - Bongaigaon D/C	4.62	34.31	135.94	174.87
ER - NER 220 kV Birpara - Salakati D/C	0.54	3.12	31.19	34.84
Total ER - NER	12.16	53.58	272.93	338.66
Import of ER from NER (NER - ER)				
NER - ER 400 kV Binaguri - Bongaigaon D/C	52.83	40.19	37.75	130.77
NER - ER 400 kV Alipurduar - Bongaigaon D/C	182.37	135.22	72.81	390.39
NER - ER 220 kV Birpara - Salakati D/C	34.59	31.32	10.78	76.68
Total NER - ER	269.78	206.73	121.33	597.84
Export of ER to SR (ER - SR)				
ER - SR HVDC Gazuwaka	375.93	395.23	208.61	979.77
ER - SR HVDC Talchar - Kolar	1233.20	1204.28	984.75	3422.23
ER - SR 765 kV Angul- Srikakulam D/C	1683.42	1561.33	1412.42	4657.17
Total ER - SR	3292.55	3160.85	2605.77	9059.17
Import of ER from SR (SR - ER)				
SR - ER HVDC Gazuwaka	0.00	0.00	55.34	55.34
SR - ER HVDC Talchar - Kolar	0.00	0.00	0.00	0.01
SR - ER 765 kV Angul- Srikakulam D/C	0.00	0.00	0.00	0.00
Total SR - ER	0.00	0.00	55.34	55.35

	Apr'23	May'23	Jun'23	Fin. Year 2023-24
Name of Line				
Export of WR to SR (WR-SR)				
WR - SR HVDC Bhadrawati	544.41	411.52	171.68	1127.62
WR - SR 765 kV Sholapur - Raichur 2xS/C	417.69	222.76	146.07	786.52
WR - SR 765 kV Wardha - Nizamabad D/C	1323.51	873.44	1018.25	3215.21
WR - SR 400KV Kolhapur-Kudgi D/C	0.00	0.00	0.00	0.00
WR-SR HVDC Raigarh-Pugalur	3004.35	1791.86	1182.91	5979.12
WR-SR 220kV Xeldem - Ambewadi S/C	77.16	70.18	68.17	215.51
WR-SR 220kV Ponda - Ambewadi S/C	0.29	1.54	0.28	2.10
Total WR - SR	5367.41	3371.30	2587.37	11326.08
Import of WR from SR (SR - WR)				
SR - WR HVDC Bhadrawati	4.11	25.09	178.09	207.30
SR - WR 765 kV Raichur - Sholapur 2xS/C	29.13	205.27	344.82	579.23
SR - WR 765 kV Wardha - Nizamabad D/C	0.00	3.90	0.32	4.22
SR - WR 400KV Kolhapur-Kudgi D/C	623.59	719.30	784.98	2127.87
SR-WR HVDC Pugalur-Raigarh	0.00	3.73	14.87	18.59
WR-SR 220kV Ambewadi - Xeldem S/C	0.00	0.00	0.00	0.00
WR-SR 220kV Ambewadi-Ponda S/C	0.00	0.00	0.01	0.01
Total SR - WR	656.84	957.30	1323.09	2937.23
TOTAL ALL INDIA	20628	19721	20060	60409

*In case of mutiple ckt / DC pole year corres. to the commissioning of final element

Date	15.1 Import-Export of NR with WR during June 2023																	
	Import of NR from WR (WR-NR)																	
	WR - NR 765 kV Gwalior - Agra 2xS/C	WR-NR 765 kV Gwalior-Phagi 2xS/C	WR-NR 765 kV Jabalpur- Orai D/C	WR-NR 765 kV Satna- Orai	WR-NR 765 kV Gwalior-Orai	WR - NR HVDC Champa- Kurukshetra	WR - NR HVDC Vindhyachal	WR - NR 400 kV Zerda- Kankroli	WR - NR 400 kV Zerda- Bhinmal	WR-NR 400 kV RAPP C - Shujalpur D/C	WR - NR 220 kV Bhanpura - Ranpur	WR - NR 220 kV Bhanpura - Modak	WR - NR 220 kV Auraiya - Malanpur / Mehgaon	WR-NR 400 KV Rihand Vindhyachal D/C	WR - NR HVDC Mundra - M'garh	WR -NR 765 kV Banaskata - Chittorgarh D/C	WR-NR 765 kV Varanasi- Vindhyachal	Total WR - NR
1-Jun-23	21.65	3.30	12.16	16.49	0.00	39.74	0.00	0.00	0.00	0.00	1.93		0.00	0.00	10.77	0.00	59.35	165.39
2-Jun-23	26.89	6.47	17.47	17.74	0.00	34.89	0.00	0.00	0.00	0.00	2.03		0.00	0.00	7.35	0.00	62.64	175.48
3-Jun-23	30.93	10.56	25.16	19.58	0.00	34.90	0.00	0.00	0.00	0.00	2.02		0.00	0.00	7.35	0.00	59.61	190.11
4-Jun-23	33.17	2.93	28.71	7.57	0.00	50.38	0.00	0.00	0.00	0.00	1.95		0.00	0.00	7.35	0.00	65.59	197.65
5-Jun-23	39.34	15.59	34.36	22.80	0.00	58.32	0.00	0.00	0.00	0.88	2.15		0.00	0.00	7.35	0.00	61.22	242.01
6-Jun-23	34.07	11.03	29.50	20.78	0.00	57.84	0.00	0.00	0.00	0.00	2.17		0.00	0.00	7.35	0.00	64.50	227.24
7-Jun-23	32.64	10.98	29.25	19.89	0.00	82.30	0.00	0.00	0.00	0.00	2.11		0.00	0.00	8.46	0.00	68.90	254.53
8-Jun-23	35.98	11.36	31.70	20.65	0.00	93.01	0.00	0.00	0.00	0.00	2.26		0.00	0.00	21.18	0.00	71.18	287.32
9-Jun-23	36.19	11.88	32.29	20.06	0.00	85.88	0.00	0.00	0.00	0.32	2.41		0.00	0.00	9.58	0.00	66.30	264.91
10-Jun-23	33.98	10.08	31.40	19.10	0.00	86.28	0.00	0.00	0.00	0.00	2.61		0.00	0.00	12.90	0.00	68.56	264.91
11-Jun-23	29.39	7.52	27.79	17.81	0.00	79.25	0.00	0.00	0.00	0.00	2.52		0.00	0.00	9.24	0.00	71.40	244.92
12-Jun-23	39.94	12.87	37.82	21.80	0.00	68.66	0.00	0.70	0.00	2.19	3.63		0.00	0.00	7.34	7.11	66.72	268.78
13-Jun-23	33.71	7.34	30.68	20.18	0.00	105.90	0.00	0.78	0.00	0.27	2.71		0.00	0.00	11.74	8.52	69.25	291.08
14-Jun-23	27.61	3.39	23.36	18.66	0.00	88.72	0.00	0.00	0.00	0.00	2.61		0.00	0.00	27.66	0.39	61.90	254.30
15-Jun-23	21.18	10.16	21.85	19.03	0.00	61.80	0.00	0.00	0.00	0.00	2.66		0.00	0.00	31.01	0.00	55.20	222.89
16-Jun-23	27.32	22.56	31.16	20.79	0.00	50.80	0.00	0.00	0.00	2.39	2.59		0.00	0.00	7.01	0.00	58.12	222.74
17-Jun-23	25.29	16.07	30.53	21.08	0.00	65.09	0.00	0.00	0.00	0.29	2.17		0.00	0.00	7.78	0.00	64.36	232.66
18-Jun-23	18.10	3.24	17.18	18.21	0.00	82.30	0.00	0.00	0.00	0.00	1.77		0.00	0.00	13.27	0.00	63.74	217.81
19-Jun-23	17.77	4.55	14.12	18.79	0.00	52.59	0.00	0.00	0.00	0.00	1.97		0.00	0.00	12.86	0.00	55.42	178.07
20-Jun-23	17.90	6.65	15.05	18.68	0.00	45.21	0.54	0.00	0.00	0.00	1.90		0.00	0.00	6.72	0.00	46.80	159.45
21-Jun-23	24.39	13.21	25.34	20.48	0.00	41.08	0.00	0.00	0.00	0.00	2.10		0.00	0.00	0.00	0.00	53.79	180.39
22-Jun-23	27.62	12.08	27.73	21.24	0.00	64.30	0.00	0.00	0.00	0.00	2.34		0.00	0.00	0.00	0.00	59.13	214.44
23-Jun-23	32.26	15.33	31.97	21.16	0.00	81.53	0.00	0.00	0.00	0.14	2.41		0.00	0.00	0.00	0.00	64.86	249.66
24-Jun-23	29.50	17.64	32.30	20.76	0.00	90.82	0.10	0.00	0.00	0.89	2.33		0.00	0.00	0.00	0.00	69.50	263.84
25-Jun-23	21.34	9.83	18.27	15.16	0.00	61.11	2.49	0.00	0.00	0.00	2.03		0.00	0.00	0.00	0.00	63.55	193.78
26-Jun-23	27.46	16.63	21.00	17.03	0.00	80.28	0.00	0.00	0.00	0.27	1.89		0.00	0.00	0.00	0.00	62.60	227.16
27-Jun-23	26.47	21.97	21.85	19.01	0.00	100.29	0.00	0.00	0.00	2.60	2.08		0.00	0.00	0.00	0.00	56.29	250.56
28-Jun-23	31.03	19.48	30.20	21.08	0.00	71.00	0.00	0.00	0.00	3.31	2.27		0.00	0.00	0.00	0.00	57.00	235.37
29-Jun-23	31.63	15.60	30.88	20.71	0.00	70.57	0.00	0.00	0.00	2.39	2.25		0.00	0.00	0.00	0.00	52.03	226.06
30-Jun-23	28.93	12.26	17.25	18.51	0.00	84.27	0.00	0.00	0.00	0.11	2.26		0.00	0.00	0.00	0.00	54.79	218.38
Total	863.68	342.56	778.33	574.83	0.00	2069.11	3.13	1.48	0.00	16.05	68.13	0.00	0.00	0.00	234.27	16.02	1854.30	6821.89
Disclaimer:- Blank entry if the line under outage/shutdown on corrsponding day																		

Date	15.1 Import-Export of NR with WR during June 2023																	
	Export of NR to WR (NR- WR)																	
	NR - WR 765 kV Gwalior - Agra 2xS/C	NR-WR 765 kV Gwalior-Phagi 2xS/C	NR-WR 765 kV Jabalpur- Orai D/C	NR-WR 765 kV Satna- Orai	NR-WR 765 kV Gwalior-Orai	NR - WR HVDC Champa- Kurukshetra	NR - WR HVDC Vindhyachal	NR - WR 400 kV Zerda- Kankroli	NR - WR 400 kV Zerda- Bhinmal	NR-WR 400 kV RAPP C - Shujalpur D/C	WR - NR 220 kV Bhanpura - Ranpur	WR - NR 220 kV Bhanpura - Modak	NR - WR 220 kV Auraiya - Malanpur / Mehgaon	NR-WR 400 kV Rihand- Vindhyachal D/C	NR - WR HVDC Mundra - M'garh	NR - WR 765 kV Banaskata - Chittorgarh D/C	NR-WR 765 kV Varanasi- Vindhyachal	Total NR - WR
1-Jun-23	0.00	0.00	0.00	0.00	11.75	0.00	12.16	4.63	7.39	5.79	0.00		1.14	22.15	0.00	19.12	0.00	84.13
2-Jun-23	0.00	0.00	0.00	0.00	12.85	0.00	12.12	4.45	6.30	3.11	0.00		1.00	22.11	0.00	19.09	0.00	81.03
3-Jun-23	0.00	0.00	0.00	0.00	12.92	0.00	12.20	6.65	4.84	2.14	0.00		1.05	22.42	0.00	22.52	0.00	84.74
4-Jun-23	0.00	0.00	0.00	0.00	3.58	0.00	10.57	4.54	9.50	4.23	0.00		0.28	21.73	0.00	17.50	0.00	71.93
5-Jun-23	0.00	0.00	0.00	0.00	10.86	0.00	12.19	2.89	4.82	0.00	0.00		0.59	22.35	0.00	13.57	0.00	67.27
6-Jun-23	0.00	0.00	0.00	0.00	10.06	0.00	12.16	3.34	7.38	1.50	0.00		2.53	21.68	0.00	11.23	0.00	69.88
7-Jun-23	0.00	0.00	0.00	0.00	10.44	0.00	12.16	3.05	6.09	1.23	0.00		2.33	21.93	0.00	13.48	0.00	70.71
8-Jun-23	0.00	0.00	0.00	0.00	10.01	0.00	12.16	3.39	6.80	0.07	0.00		1.88	21.67	0.00	14.71	0.00	70.69
9-Jun-23	0.00	0.00	0.00	0.00	10.14	0.00	9.54	3.13	7.58	0.00	0.00		1.69	21.79	0.00	11.24	0.00	65.11
10-Jun-23	0.00	0.00	0.00	0.00	10.39	0.00	7.26	3.35	9.33	0.22	0.00		1.77	22.00	0.00	17.60	0.00	71.92
11-Jun-23	0.00	0.00	0.00	0.00	10.04	0.00	4.54	2.50	6.13	0.32	0.00		1.19	20.65	0.00	12.03	0.00	57.40
12-Jun-23	0.00	0.00	0.00	0.00	10.37	0.00	1.23	0.00	1.52	0.00	0.00		1.27	21.75	0.00	0.00	0.00	36.14
13-Jun-23	0.00	0.00	0.00	0.00	9.07	0.00	7.72	0.00	1.37	0.00	0.00		2.17	21.33	0.00	0.00	0.00	41.66
14-Jun-23	0.00	0.00	0.00	0.00	8.45	0.00	6.20	1.13	5.13	1.88	0.00		1.72	19.91	0.00	0.00	0.00	44.42
15-Jun-23	0.00	0.00	0.00	0.00	10.25	0.00	7.48	2.10	6.07	0.99	0.00		2.00	21.03	0.00	7.69	0.00	57.61
16-Jun-23	0.00	0.00	0.00	0.00	13.12	0.00	10.72	3.75	10.15	0.00	0.00		2.87	21.76	0.00	18.69	0.00	81.06
17-Jun-23	0.00	0.00	0.00	0.00	11.98	0.00	11.63	12.22	3.52	0.00	0.00		2.86	21.94	0.00	20.60	0.00	84.75
18-Jun-23	0.00	0.00	0.00	0.00	7.36	0.00	12.18	2.62	10.47	3.89	0.00		2.93	21.72	0.00	20.94	0.00	82.11
19-Jun-23	0.00	0.00	0.00	0.00	6.25	0.00	12.19	6.28	12.95	5.91	0.00		2.15	21.88	0.00	26.16	0.00	93.77
20-Jun-23	0.00	0.00	0.00	0.00	6.49	0.00	6.04	8.02	7.90	6.45	0.00		1.88	20.18	0.00	30.01	0.00	86.97
21-Jun-23	0.00	0.00	0.00	0.00	8.82	0.00	7.28	4.69	6.59	2.98	0.00		2.23	22.08	5.21	15.97	0.00	75.85
22-Jun-23	0.00	0.00	0.00	0.00	9.04	0.00	7.14	2.85	8.11	2.04	0.00		2.13	21.95	3.53	10.74	0.00	67.53
23-Jun-23	0.00	0.00	0.00	0.00	9.66	0.00	1.23	2.60	6.40	0.00	0.00		1.90	22.09	5.86	9.56	0.00	59.30
24-Jun-23	0.00	0.00	0.00	0.00	9.18	0.00	1.20	3.20	7.51	0.00	0.00		2.13	21.87	1.06	13.81	0.00	59.96
25-Jun-23	0.00	0.00	0.00	0.00	10.87	0.00	1.03	4.08	7.85	2.89	0.00		1.75	19.19	2.11	21.03	0.00	70.80
26-Jun-23	0.00	0.00	0.00	0.00	13.24	0.00	8.54	3.19	6.11	0.00	0.00		1.11	20.73	2.94	17.94	0.00	73.80
27-Jun-23	0.00	0.00	0.00	0.00	13.05	0.00	11.72	3.38	6.61	0.00	0.00		0.93	20.81	3.27	17.73	0.00	77.50
28-Jun-23	0.00	0.00	0.00	0.00	10.59	0.00	12.15	2.74	5.69	0.00	0.00		1.13	21.17	2.16	10.73	0.00	66.36
29-Jun-23	0.00	0.00	0.00	0.00	9.62	0.00	12.15	1.80	4.84	0.00	0.00		1.04	20.24	4.11	5.24	0.00	59.04
30-Jun-23	0.00	0.00	0.00	0.00	10.87	0.00	12.15	1.77	5.61	0.00	0.00		1.17	20.21	6.00	2.59	0.00	60.37
Total	0.00	0.00	0.00	0.00	301.32	0.00	267.04	108.34	200.56	45.64	0.00	0.00	50.82	642.32	36.25	421.52	0.00	2073.81
	Disclaimer:- Blank entry if the line under outage/shutdown on corrsponding day																	

Date	15.2 Import-Export of NR with ER & NER during June 2023																		
	Import of NR from ER (ER-NR)																	Import of NR from NER (NER-NR)	
	ER - NR 765 kV Sasaram - Fatehpur	ER - NR 765 kV Gaya - Varanasi 2*s/C	ER - NR 765 kV Gaya Balia	ER - NR HVDC Alipurduar - Agra	ER-NR 400 kV Patna - Balia D/C	ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	ER - NR 400 kV Biharshariff - Balia D/C	ER - NR 400 kV Motihari - Gorakhpur D/C	ER - NR 400 kV Biharshariff - Varanasi D/C	ER-NR 400 kV Sasaram - Varanasi	ER-NR 400 kV Sasaram - Allahabad	ER - NR 220 kV Sahupuri-Karamnasa	ER - NR 132 kV Sahupuri - Karamnasa	ER - NR 132 kV Rihand - Nagar Untari	NR - ER 132 kV Rihand - Garhwa	ER-NR 400 kV Naubatpur - Balia D/C	Total ER -NR	NER-NR HVDC Biswanath Chariali - Agra	Total NER-NR
1-Jun-23	1.54	0.00	9.56		3.77	0.14	0.00	1.14	0.00	1.64	0.67	2.50			0.00	3.21	24.17	0.00	0.00
2-Jun-23	0.00	0.00	9.43		2.52	2.52	0.00	2.02	0.00	1.57	0.72	2.83			0.00	1.84	23.45	0.00	0.00
3-Jun-23	0.00	0.00	10.80		4.82	2.10	0.00	2.53	0.00	1.58	0.72	2.73	0.00		0.00	4.30	29.58	0.00	0.00
4-Jun-23	0.00	0.00	10.50		4.39	0.36	0.00	2.70	0.00	1.70	0.63	2.58	0.00		0.00	3.82	26.68	0.00	0.00
5-Jun-23	2.45	0.00	12.53		7.56	3.24	-1.03	3.40	0.00	1.08	1.26	3.03	0.48		0.00	7.65	41.65	0.00	0.00
6-Jun-23	1.95	0.00	11.63		6.89	1.47	0.00	3.51	0.00	1.72	0.65	2.83			0.00	6.67	37.32	0.00	0.00
7-Jun-23	1.78	0.00	11.23	0.00	6.74	1.67	0.00	3.90	0.00	1.50	0.54	2.85	0.48		0.00	6.63	37.32	0.00	0.00
8-Jun-23	2.56	0.00	11.40	0.00	6.48	1.71	0.00	3.78	0.00	1.70	0.58	2.96	0.00		0.00	6.14	37.31	0.00	0.00
9-Jun-23	2.80	0.00	12.28		6.28	5.01	0.49	5.13	0.73	1.64	0.69	3.41		0.00	0.00	7.87	46.33	0.00	0.00
10-Jun-23	0.02	0.00	13.43		9.53	7.49	3.29	5.70	0.48	1.82	0.57	3.36	0.00	0.00	0.00	8.06	53.75	0.00	0.00
11-Jun-23	0.12	0.00	11.93		8.77	8.82	3.57	4.99	0.24	1.98	0.45	3.44		0.00	0.00	7.39	51.70	0.00	0.00
12-Jun-23	5.12	3.84	13.80		8.99	15.23	6.76	8.79	3.52	1.24	1.09	3.85			0.00	9.37	81.60	0.00	0.00
13-Jun-23	2.21	0.00	10.34		6.67	12.53	4.19	5.07	0.28	1.61	0.70	3.70			0.00	6.21	53.51	0.00	0.00
14-Jun-23	2.82	0.00	8.76		6.44	11.44	4.51	4.31	0.08	1.77	0.59	3.33			0.00	6.20	50.25	0.00	0.00
15-Jun-23	5.04	0.00	7.11		8.52	12.51	6.73	6.81	0.72	1.67	0.75	3.44	0.00		0.00	8.49	61.79	1.84	1.84
16-Jun-23	6.37	0.17	8.72	4.00	10.73	15.48	7.67	8.56	2.61	1.50	0.81	3.70			0.00	10.64	80.96	5.80	5.80
17-Jun-23	4.06	0.00	10.34	21.84	10.23	13.77	6.21	7.38	1.53	1.78	0.56	3.95	0.00		0.00	10.25	91.90	6.07	6.07
18-Jun-23	0.00	0.00	8.03	23.74	7.27	10.32	3.16	5.32	0.00	2.12	0.23	3.36	0.00		0.00	7.18	70.73	6.04	6.04
19-Jun-23	2.79	0.00	9.90	24.19	10.15	14.91	5.92	8.27	1.69	1.67	0.42	3.57	0.00		0.00	10.41	93.89	8.42	8.42
20-Jun-23	5.05	3.02	10.87	23.60	12.29	15.79	7.10	10.08	3.45	1.49	0.79	3.87			0.00	12.60	110.00	12.18	12.18
21-Jun-23	6.19	3.61	12.37	23.16	12.08	15.01	7.62	10.42	4.31	1.28	1.02	3.79		0.00		13.40	114.26	11.58	11.58
22-Jun-23	5.76	2.96	14.17	23.23	10.27	16.99	8.68	9.40	3.85	1.52	0.84	2.46	0.00	0.00		13.18	113.31	11.62	11.62
23-Jun-23	4.50	1.78	14.31	18.15	11.44	14.81	7.69	8.62	2.95	1.33	0.71	2.14		0.00	0.00	11.80	100.23	13.06	13.06
24-Jun-23	2.22	0.00	12.36	24.10	7.44	8.20	3.24	5.01	0.38	1.56	0.71	1.30			0.00	7.28	73.80	16.75	16.75
25-Jun-23	0.00	0.00	6.51	32.36	1.47	2.79	0.00	1.67	0.00	1.90	0.45	1.16			0.00	0.56	48.87	14.94	14.94
26-Jun-23	1.16	0.00	8.02	25.32	6.06	9.18	0.45	5.62	0.00	1.69	0.69	1.59			0.00	5.91	65.69	12.01	12.01
27-Jun-23	4.42	3.23	11.54	26.61	10.99	13.43	3.42	8.97	2.70	1.32	1.04		0.00		0.00	9.34	97.01	12.02	12.02
28-Jun-23	2.96	2.59	12.12	35.00	11.31	13.41	3.93	8.64	2.34	1.18	1.12	1.94			0.00	11.06	107.60	7.34	7.34
29-Jun-23	4.10	3.73	11.20	34.94	12.77	15.20	5.91	10.73	2.35	1.20	0.93	1.48	0.00	0.00	0.00	12.20	116.74	6.99	6.99
30-Jun-23	4.58	3.53	6.09	34.81	9.48	11.82	3.46	7.62	0.45	0.33	0.36	1.17			0.00	9.90	93.60	6.96	6.96
Total	82.57	28.46	321.28	375.05	242.35	277.35	102.97	180.09	34.66	46.09	21.29	82.32	0.96	0.00	0.00	239.56	2035.00	153.62	153.62
Disclaimer:- Blank entry if the line under outage/shutdown on corrsponding day																			

Date	15.2 Import-Export of NR with ER & NER during June 2023																		
	Export of NR to ER (NR- ER)																	Export of NR to NER (NR-NER)	
	NR - ER 765 kV Sasaram - Fatehpur	NR - ER 765 kV Gaya - Varanasi 2*S/C	NR - ER 765 kV Gaya Balia	NR - ER HVDC Alipurduar - Agra	NR-ER 400 kV Patna - Balia D/C	NR - ER 400 kV Muzaffarpur - Gorakhpur D/C	NR - ER 400 kV Biharshariff - Balia D/C	NR - ER 400 kV Motihari - Gorakhpur D/C	NR - ER 400 kV Biharshariff - Varanasi D/C	NR-ER 400 kV Sasaram - Varanasi	NR-ER 400 kV Sasaram - Allahabad	NR - ER 220 kV Sahupuri-Karamnasa	NR - ER 132 kV Sahupuri - Karamnasa	NR - ER 132 kV Rihand - Nagar Untari	NR - ER 132 kV Rihand - Garhwa	NR-ER 400 kV Balia-Naubatpur D/C	Total NR - ER	NR-NER HVDC Biswanath Chariali - Agra	Total NR-NER
1-Jun-23	0.00	12.86	0.00		0.00	0.00	1.27	0.00	3.48	0.00	0.00	0.00			0.67	0.00	18.28	5.56	5.56
2-Jun-23	1.92	13.08	0.00		0.00	0.00	0.57	0.00	3.24	0.00	0.00	0.00			0.66	0.00	19.47	7.63	7.63
3-Jun-23	1.28	9.31	0.00		0.00	0.00	0.91	0.00	2.72	0.00	0.00	0.00	0.00		0.70	0.00	14.92	7.29	7.29
4-Jun-23	3.05	12.35	0.00		0.00	0.00	3.22	0.00	4.13	0.00	0.00	0.00	0.00		0.67	0.00	23.42	8.82	8.82
5-Jun-23	0.00	6.26	0.00		0.00	0.00	0.00	0.00	1.00	0.00	0.00	0.00	0.00		0.69	0.00	7.95	9.22	9.22
6-Jun-23	0.00	5.95	0.00		0.00	0.00	1.05	0.00	1.04	0.00	0.00	0.00			0.67	0.00	8.71	9.50	9.50
7-Jun-23	0.00	4.12	0.00	0.00	0.00	0.00	0.91	0.00	0.67	0.00	0.00	0.00	0.00		0.63	0.00	6.33	9.51	9.51
8-Jun-23	0.00	2.98	0.00	0.00	0.00	0.00	1.89	0.00	0.52	0.00	0.00	0.00	0.00		0.68	0.00	6.07	7.20	7.20
9-Jun-23	0.00	0.62	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.11	0.71	0.00	1.44	9.79	9.79
10-Jun-23	0.00	0.86	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.72	0.00	1.58	8.02	8.02
11-Jun-23	0.00	3.15	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.09	0.72	0.00	3.96	4.60	4.60
12-Jun-23	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.70	0.00	0.70	3.86	3.86
13-Jun-23	0.00	3.97	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.72	0.00	4.69	4.63	4.63
14-Jun-23	0.00	4.45	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.68	0.00	5.13	5.51	5.51
15-Jun-23	0.00	2.73	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.72	0.00	3.45	3.33	3.33
16-Jun-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.80	0.00	0.80	0.00	0.00
17-Jun-23	0.00	1.91	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.84	0.00	2.75	0.00	0.00
18-Jun-23	0.65	7.53	0.00	0.00	0.00	0.00	0.00	0.00	0.70	0.00	0.00	0.00	0.00		0.87	0.00	9.75	0.00	0.00
19-Jun-23	0.00	2.02	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.86	0.00	2.88	0.00	0.00
20-Jun-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.88	0.00	0.88	0.00	0.00
21-Jun-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.83		0.00	0.83	0.00	0.00
22-Jun-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.48	0.05		0.00	0.53	0.00	0.00
23-Jun-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.48	0.00	0.48	0.00	0.00
24-Jun-23	0.00	1.55	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.74	0.00	2.29	0.00	0.00
25-Jun-23	0.84	4.53	0.00	0.00	0.00	0.00	3.24	0.00	2.55	0.00	0.00	0.00			0.70	0.00	11.86	0.00	0.00
26-Jun-23	0.00	2.75	0.00	0.00	0.00	0.00	0.00	0.00	0.48	0.00	0.00	0.00			0.67	0.00	3.90	0.00	0.00
27-Jun-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00		0.66	0.00	0.66	0.00	0.00
28-Jun-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.65	0.00	0.65	0.00	0.00
29-Jun-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.47	0.00	0.47	0.00	0.00
30-Jun-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.71	0.00	0.71	0.00	0.00
Total	7.74	102.98	0.00	0.00	0.00	0.00	13.06	0.00	20.53	0.00	0.00	0.00	0.48	1.08	19.67	0.00	165.54	104.47	104.47
Disclaimer:- Blank entry if the line under outage/shutdown on corrsponding day																			

Date	15.3 Import and Export of ER with WR & NER during June 2023																							
	Export of WR to ER (WR-ER)								Import of WR from ER (ER - WR)								Export of ER to NER (ER-NER)				Import of ER from NER (NER-ER)			
	WR - ER 765 kV Dharamjaygarh - Ranchi 2xS/C	WR - ER 765 kV Dharamjaygarh - Jharsuguda Q/C	WR - ER 765 kV Durg - Jharsuguda D/C	WR - ER 400 kV Sipat - Ranchi D/C	WR - ER 400 kV Raigarh - Jharsuguda-2xD/C	WR - ER 220 kV Korba - Budhipadar D/C	WR - ER 220 kV Raigarh - Budhipadar	Total WR - ER	ER - WR 765 kV Dharamjaygarh - Ranchi 2xS/C	ER-WR 765 kV Dharamjaygarh - Jharsuguda D/C	ER-WR 765 kV Durg - Jharsuguda D/C	ER - WR 400 kV Sipat - Ranchi D/C	ER - WR 400 kV Raigarh - Jharsuguda-2xD/C	ER - WR 220 kV Korba - Budhipadar D/C	ER - WR 220 kV Raigarh - Budhipadar	Total ER - WR	ER - NER 400 kV Binaguri - Bongaigaon D/C	ER - NER 400 kV Alipurduar - Bongaigaon D/C	ER - NER 220 kV Birpara - Salakati D/C	Total ER - NER	NER - ER 400 kV Binaguri - Bongaigaon D/C	NER - ER 400 kV Alipurduar - Bongaigaon 2xD/C	NER - ER 220 kV Birpara - Salakati D/C	Total NER - ER
1-Jun-23	27.2	16.0	0.0	4.9	0.1	3.3	0.0	51.48	0.0	1.0	6.8	0.0	4.8	0.0	1.8	14.49	3.29	10.13	1.90	15.32	0.00	0.00	0.00	0.00
2-Jun-23	31.1	18.2	0.0	5.4	0.0	3.3	0.0	57.97	0.0	1.4	6.2	0.0	5.0	0.0	2.0	14.56	2.86	8.97	1.40	13.24	0.00	0.00	0.00	0.00
3-Jun-23	33.2	22.4	0.0	5.0	0.0	2.3	0.0	62.86	0.0	0.2	5.4	0.0	8.4	0.0	1.4	15.33	3.12	9.23	1.65	13.99	0.00	0.00	0.00	0.00
4-Jun-23	33.8	26.8	0.3	6.2	1.1	3.7	0.0	71.90	0.0	0.8	4.0	0.0	3.7	0.0	1.1	9.60	2.86	8.20	1.18	12.23	0.00	0.00	0.00	0.00
5-Jun-23	33.7	15.2	0.0	5.7	0.1	3.0	0.0	57.71	0.0	1.8	4.5	0.0	4.4	0.0	1.2	11.87	3.02	8.59	1.57	13.18	0.00	0.00	0.00	0.00
6-Jun-23	31.8	17.3	0.0	5.6	0.0	2.9	0.1	57.78	0.0	2.2	5.4	0.0	4.7	0.0	1.1	13.51	3.95	11.16	2.11	17.22	0.00	0.00	0.00	0.00
7-Jun-23	31.5	13.3	0.0	6.1	0.4	3.1	0.0	54.51	0.0	2.7	6.3	0.0	2.6	0.0	1.7	13.29	3.58	9.65	2.06	15.29	0.00	0.00	0.00	0.00
8-Jun-23	33.3	15.5	0.0	6.4	1.0	3.5	0.0	59.74	0.0	0.9	4.5	0.0	1.1	0.0	1.2	7.75	4.62	10.22	2.14	16.97	0.00	0.00	0.00	0.00
9-Jun-23	30.3	14.0	0.1	5.6	1.0	2.8	0.0	53.88	0.0	1.1	4.2	0.0	1.8	0.0	1.3	8.34	2.95	3.86	0.89	7.69	0.01	0.08	0.00	0.08
10-Jun-23	29.4	17.4	0.0	5.3	0.3	3.4	0.0	55.87	0.0	0.0	5.0	0.0	2.8	0.0	0.6	8.51	1.23	1.49	0.31	3.04	0.16	0.41	0.18	0.75
11-Jun-23	29.0	17.9	0.1	5.7	0.2	2.7	0.0	55.61	0.0	0.1	5.8	0.1	3.8	0.0	1.2	10.97	0.24	0.24	0.07	0.55	1.53	2.73	0.80	5.06
12-Jun-23	22.9	14.9	0.0	3.8	0.0	2.1	0.0	43.82	0.1	0.1	8.7	0.1	7.4	0.0	2.0	18.51	0.30	0.40	0.28	0.98	2.34	3.15	0.60	6.10
13-Jun-23	22.1	7.2	0.0	4.8	0.0	2.9	0.0	36.99	0.0	1.7	8.7	0.1	5.3	0.0	1.7	17.48	0.26	0.30	0.09	0.65	2.30	3.69	0.56	6.54
14-Jun-23	20.9	10.7	0.0	4.1	0.0	2.8	0.0	38.51	0.3	1.3	6.4	0.3	5.2	0.0	1.7	15.19	0.01	0.00	0.00	0.01	2.64	3.29	0.74	6.67
15-Jun-23	19.6	9.7	0.0	3.1	0.0	2.6	0.0	35.02	0.6	2.7	5.6	0.3	4.7	0.0	2.0	15.81	0.00	0.00	0.00	0.00	6.79	8.76	1.87	17.43
16-Jun-23	23.5	6.8	0.0	3.4	0.0	2.1	0.0	35.73	0.1	3.0	4.4	0.1	7.1	0.0	2.1	16.84	0.00	0.00	0.00	0.00	7.27	8.99	1.53	17.79
17-Jun-23	22.6	14.5	0.0	3.5	0.0	1.9	0.0	42.46	0.0	0.1	2.8	0.2	5.5	0.0	1.8	10.43	0.01	0.00	0.00	0.01	4.79	10.73	1.41	16.93
18-Jun-23	18.9	18.2	0.2	3.6	0.3	2.2	0.0	43.39	0.2	0.2	2.4	0.2	4.2	0.0	1.6	8.73	0.01	0.00	0.00	0.01	4.29	10.38	1.33	16.01
19-Jun-23	7.8	22.6	0.0	1.1	0.0	1.6	0.0	33.12	2.0	0.0	4.5	0.8	6.3	0.0	1.9	15.57	0.32	0.01	0.11	0.44	1.82	6.96	0.74	9.52
20-Jun-23	5.5	27.8	0.0	0.4	0.0	1.3	0.0	34.93	2.6	0.5	8.1	2.0	7.7	0.0	1.7	22.68	0.99	0.39	0.48	1.85	1.04	3.90	0.23	5.16
21-Jun-23	11.0	25.9	0.0	1.4	0.0	2.4	0.2	40.87	2.1	0.1	7.0	1.4	6.1	0.0	0.7	17.40	1.26	0.41	0.37	2.05	1.18	3.90	0.28	5.36
22-Jun-23	13.3	19.4	0.0	1.7	0.0	2.8	0.2	37.50	1.5	0.0	4.7	1.1	5.5	0.0	0.3	13.06	1.79	0.51	0.48	2.78	1.07	3.58	0.32	4.98
23-Jun-23	18.5	15.5	0.0	2.6	0.0	2.1	0.1	38.76	1.3	0.7	4.4	0.7	5.3	0.0	0.7	13.15	3.19	2.81	0.77	6.77	0.50	2.27	0.18	2.95
24-Jun-23	23.7	11.7	0.0	3.9	0.0	1.4	0.1	40.81	0.2	1.7	3.3	0.3	4.4	0.0	1.2	11.11	9.20	8.59	1.90	19.69	0.00	0.01	0.00	0.01
25-Jun-23	24.2	22.9	0.6	4.5	0.2	2.0	0.3	54.80	0.0	0.7	1.8	0.1	2.5	0.0	0.9	5.97	13.00	11.63	2.62	27.25	0.00	0.00	0.00	0.00
26-Jun-23	20.5	17.3	0.0	4.3	0.8	1.8	0.0	44.74	0.0	0.0	2.0	0.0	0.7	0.0	0.9	3.61	9.12	7.94	1.93	18.99	0.00	0.00	0.00	0.00
27-Jun-23	11.8	11.5	0.0	2.7	1.5	2.1	0.0	29.55	1.6	2.6	4.5	0.4	0.5	0.0	1.2	10.74	8.73	6.47	1.59	16.79	0.00	0.00	0.00	0.00
28-Jun-23	17.0	15.8	0.0	3.2	0.8	2.0	0.0	38.81	1.7	3.2	4.2	0.4	1.5	0.0	1.3	12.25	9.24	5.14	1.68	16.05	0.00	0.00	0.00	0.00
29-Jun-23	11.5	12.0	0.0	2.1	0.4	1.8	0.0	27.92	0.3	1.2	3.7	0.1	1.4	0.0	1.7	8.42	8.44	4.66	1.77	14.87	0.00	0.00	0.00	0.00
30-Jun-23	13.4	12.5	0.3	2.2	0.7	1.2	0.0	30.28	1.1	1.1	2.4	0.4	1.5	0.1	1.3	7.82	8.22	4.95	1.83	15.00	0.00	0.00	0.00	0.00
Total	673.15	490.99	1.75	118.29	8.79	73.19	1.17	1367.33	15.57	33.08	148.02	9.07	125.69	0.14	41.41	372.98	105.81	135.94	31.19	272.93	37.75	72.81	10.78	121.33

Date	15.4 Import and Export of SR with ER & WR during June 2023																							
	Export of ER to SR (ER - SR)				Import of ER from SR (SR - ER)				Export of WR to SR (WR-SR)								Import of WR from SR (SR - WR)							
	ER - SR HVDC Gazuwaka	ER - SR HVDC Talchar -Kolar	ER-SR 765 kV Angul-Srikakulam D/C	Total ER - SR	SR - ER HVDC Gazuwaka	SR - ER HVDC Talchar -	SR-ER 765 kV Angul-Srikakulam D/C	Total SR - ER	WR - SR HVDC Bhadrawati	WR - SR 765 kV Sholapur - Raichur 2xS/C	WR-SR 765 kV Wardha - Nizamabad D/C	WR-SR 400KV Kolhapur-Kudgi D/C	WR-SR HVDC Raigarh-Puglur	WR-SR 220kV Xeldem - Ambewadi S/C	WR-SR 220kV Ponda - Ambewadi S/C	Total WR - SR	SR - WR HVDC Bhadrawati	SR - WR 765 kV Raichur - Sholapur 2xS/C	SR-WR 765 kV Wardha - Nizamabad D/C	SR-WR 400KV Kolhapur-Kudgi D/C	SR-WR HVDC Raigarh-Puglur	WR-SR 220kV Xeldem - Ambewadi S/C	WR-SR 220kV Ponda - Ambewadi S/C	Total SR - WR
1-Jun-23	12.39	41.00	38.41	91.80	0.00	0.00	0.00	0.00	23.90	0.19	21.13	0.00	76.32	1.96	0.00	123.51	0.00	18.11	0.00	28.08	0.00	0.00	0.00	46.20
2-Jun-23	12.39	39.69	46.75	98.83	0.00	0.00	0.00	0.00	15.38	3.12	28.71	0.00	61.03	2.35	0.00	110.59	0.00	15.13	0.00	28.76	0.00	0.00	0.00	43.89
3-Jun-23	12.40	42.50	51.96	106.85	0.00	0.00	0.00	0.00	7.29	3.49	34.89	0.00	39.80	2.61	0.00	88.09	0.00	6.14	0.00	25.59	0.00	0.00	0.00	31.73
4-Jun-23	12.41	40.90	49.15	102.46	0.00	0.00	0.00	0.00	7.24	6.99	35.12	0.00	28.67	2.49	0.00	80.50	0.00	6.10	0.00	24.55	0.00	0.00	0.00	30.65
5-Jun-23	12.41	36.07	41.25	89.73	0.00	0.00	0.00	0.00	7.30	0.97	25.79	0.00	37.15	2.54	0.00	73.75	0.00	14.79	0.00	28.48	0.00	0.00	0.00	43.27
6-Jun-23	12.41	24.93	46.39	83.74	0.00	0.00	0.00	0.00	5.20	3.64	34.08	0.00	44.72	2.58	0.00	90.22	1.90	9.64	0.00	24.93	0.00	0.00	0.00	36.47
7-Jun-23	12.42	17.26	40.42	70.11	0.00	0.00	0.00	0.00	9.27	2.66	27.66	0.00	36.63	2.73	0.00	78.96	1.77	15.69	0.00	28.53	0.00	0.00	0.00	45.99
8-Jun-23	13.66	24.10	42.09	79.86	0.00	0.00	0.00	0.00	5.11	5.15	34.02	0.00	20.96	2.69	0.00	67.93	9.25	11.37	0.00	29.01	0.00	0.00	0.00	49.64
9-Jun-23	14.96	24.12	40.56	79.64	0.00	0.00	0.00	0.00	0.00	3.11	30.92	0.00	29.42	2.18	0.00	65.63	11.90	15.37	0.00	30.06	0.00	0.00	0.00	57.34
10-Jun-23	13.25	24.36	44.63	82.24	0.00	0.00	0.00	0.00	0.00	3.59	32.45	0.00	19.85	1.42	0.00	57.30	14.20	16.55	0.00	28.51	6.49	0.00	0.00	65.75
11-Jun-23	9.17	23.68	46.32	79.17	0.20	0.00	0.00	0.20	0.00	2.88	33.42	0.00	15.45	2.56	0.00	54.31	16.67	11.03	0.00	28.21	5.99	0.00	0.00	61.91
12-Jun-23	0.00	22.05	58.21	80.26	8.24	0.00	0.00	8.24	5.20	9.85	41.09	0.00	31.94	2.36	0.00	90.44	5.97	4.67	0.00	22.74	0.00	0.00	0.00	33.38
13-Jun-23	0.00	24.15	52.84	76.99	7.71	0.00	0.00	7.71	9.80	6.35	34.50	0.00	36.51	1.98	0.00	89.14	0.00	10.28	0.00	22.30	0.00	0.00	0.00	32.58
14-Jun-23	0.00	24.17	55.17	79.34	7.55	0.00	0.00	7.55	5.24	5.86	43.93	0.00	43.54	2.43	0.00	101.00	11.98	7.17	0.00	24.60	0.00	0.00	0.00	43.75
15-Jun-23	0.00	24.17	59.80	83.97	7.55	0.00	0.00	7.55	0.00	10.85	48.88	0.00	75.09	2.44	0.00	137.26	10.38	1.66	0.00	24.93	0.00	0.00	0.00	36.97
16-Jun-23	0.36	23.60	55.74	79.70	6.23	0.00	0.00	6.23	1.36	9.03	39.11	0.00	39.23	2.37	0.00	91.09	8.05	7.46	0.00	27.86	0.00	0.00	0.00	43.36
17-Jun-23	0.00	41.04	53.05	94.08	6.06	0.00	0.00	6.06	1.75	9.12	40.50	0.00	42.62	2.24	0.00	96.23	8.20	8.84	0.00	26.35	0.00	0.00	0.00	43.39
18-Jun-23	0.00	48.00	46.89	94.89	6.07	0.00	0.00	6.07	7.26	2.73	34.17	0.00	57.21	2.27	0.00	103.64	0.00	14.00	0.00	26.53	0.00	0.00	0.00	40.53
19-Jun-23	0.23	45.47	53.95	99.64	5.72	0.00	0.00	5.72	9.04	5.83	42.13	0.00	82.78	2.21	0.00	141.98	0.00	6.65	0.00	25.02	0.00	0.00	0.00	31.66
20-Jun-23	4.95	45.60	53.51	104.06	0.00	0.00	0.00	0.00	17.46	6.22	39.67	0.00	70.90	2.39	0.00	136.63	0.00	6.94	0.00	25.63	0.00	0.00	0.00	32.57
21-Jun-23	6.84	47.96	47.50	102.30	0.00	0.00	0.00	0.00	13.75	3.99	34.23	0.00	57.45	2.47	0.00	111.89	0.00	9.51	0.00	27.38	0.00	0.00	0.00	36.89
22-Jun-23	9.95	33.28	46.35	89.58	0.00	0.00	0.00	0.00	7.28	5.98	34.39	0.00	39.00	2.43	0.00	89.07	0.00	9.90	0.00	25.75	0.00	0.00	0.00	35.65
23-Jun-23	7.40	33.20	41.81	82.40	0.00	0.00	0.00	0.00	7.27	3.69	25.89	0.00	26.78	1.02	0.00	64.65	0.00	16.77	0.04	28.71	0.00	0.00	0.00	45.52
24-Jun-23	5.11	30.00	40.72	75.83	0.00	0.00	0.00	0.00	3.78	1.93	25.16	0.00	14.62	2.36	0.00	47.85	8.71	17.72	0.29	26.91	0.00	0.00	0.01	53.64
25-Jun-23	5.11	30.14	38.82	74.07	0.00	0.00	0.00	0.00	0.00	3.54	26.20	0.00	20.96	1.80	0.23	52.74	7.20	15.00	0.00	24.45	0.00	0.00	0.00	46.64
26-Jun-23	5.13	31.32	38.33	74.79	0.00	0.00	0.00	0.00	0.00	3.17	30.64	0.00	25.00	2.29	0.00	61.09	10.96	20.75	0.00	27.17	2.38	0.00	0.00	61.27
27-Jun-23	5.09	37.53	45.55	88.17	0.00	0.00	0.00	0.00	0.00	4.89	35.19	0.00	29.45	2.26	0.00	71.79	15.35	10.73	0.00	24.35	0.00	0.00	0.00	50.43
28-Jun-23	5.10	33.71	47.67	86.48	0.00	0.00	0.00	0.00	1.81	5.86	34.76	0.00	23.33	2.33	0.00	68.09	12.91	11.94	0.00	24.39	0.00	0.00	0.00	49.25
29-Jun-23	5.09	33.41	45.91	84.40	0.00	0.00	0.00	0.00	0.00	5.91	34.28	0.00	30.69	2.20	0.00	73.09	11.88	13.98	0.00	23.79	0.00	0.00	0.00	49.65
30-Jun-23	10.37	37.34	42.67	90.38	0.00	0.00	0.00	0.00	0.00	5.50	35.36	0.00	25.85	2.20	0.00	68.91	10.81	10.93	0.00	21.41	0.00	0.00	0.00	43.14
TOTAL	208.61	984.75	1412.42	2605.77	55.34	0.00	0.00	55.34	171.68	146.07	1018.25	0.00	1182.91	68.17	0.28	2587.37	178.09	344.82	0.32	784.98	14.87	0.00	0.01	1323.09

16. भूटान , नेपाल, बांग्लादेश एवं म्यान्मार के साथ अंतरराष्ट्रीय विद्युत विनिमय								
अप्रैल 2023 से मार्च 2024 April 2023 to March 2024								
अंतरराष्ट्रीय विद्युत विनिमय [भारत 'से निर्यात'/'को आयात']								
Transnational Exchange ('Export from'/'Import to' India)								
माह MONTH	भूटान BHUTAN		नेपाल NEPAL		बांग्लादेश BANGLADESH		म्यान्मार MYANMAR	
	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)
अप्रैल 2023 APR'23	19.40	41.40	357.99	0.00	687.30	0.00	0.73	0.00
मई 2023 MAY'23	2.27	114.78	265.04	0.34	750.12	0.00	0.09	0.00
जून 2023 JUN'23	0.00	626.15	80.00	88.86	743.92	0.00	0.77	0.00
कुल Total	21.67	782.33	703.03	89.20	2181.34	0.00	1.59	0.00
* Based on daily operational data								

Date	16.1 Import from neighbouring countries during June 2023													
	(All figures in MU)													
	Import from Bhutan								Import from Bangladesh		Import from Nepal			Import from Myanmar
	400 kV Tala-Binaguri I,II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurwar D/C*	400 kV Jigmeling-Alipurwar D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-Jun-23	3.82	1.11	0.00	0.00	2.28	3.46	1.11	0.18	0.00	0.00	0.00	0.00	0.00	0.00
2-Jun-23	3.95	0.65	0.00	0.00	2.54	3.86	1.02	0.09	0.00	0.00	0.00	0.00	0.00	0.00
3-Jun-23	3.39	0.45	0.00	0.00	2.03	3.08	1.07	0.14	0.00	0.00	0.00	0.00	0.00	0.00
4-Jun-23	2.96	0.31	0.00	0.00	1.60	2.43	0.83	0.17	0.00	0.00	0.00	0.00	0.00	0.00
5-Jun-23	2.54	0.13	0.00	0.00	1.67	2.58	1.01	0.13	0.00	0.00	0.00	0.00	0.00	0.00
6-Jun-23	3.83	0.00	0.00	0.00	1.63	2.48	1.10	0.30	0.00	0.00	0.00	0.00	0.00	0.00
7-Jun-23	2.40	0.56	0.00	0.00	1.07	1.66	1.04	0.18	0.00	0.00	0.00	0.00	0.00	0.00
8-Jun-23	1.99	0.34	0.00	0.00	1.10	1.69	1.06	0.11	0.00	0.00	0.00	0.00	0.00	0.00
9-Jun-23	2.33	0.58	0.00	0.00	1.06	1.64	1.05	0.05	0.00	0.00	0.00	0.00	0.00	0.00
10-Jun-23	2.36	0.63	0.00	0.00	1.27	1.95	0.86	0.00	0.00	0.00	0.00	0.00	0.00	0.00
11-Jun-23	2.27	0.57	0.00	0.00	2.22	2.47	0.87	0.00	0.00	0.00	0.00	0.00	0.00	0.00
12-Jun-23	2.48	0.69	0.00	0.00	2.38	3.65	0.99	0.03	0.00	0.00	0.00	2.25	0.00	0.00
13-Jun-23	2.48	0.66	0.00	0.00	1.93	2.95	0.92	0.00	0.00	0.00	0.00	5.98	0.00	0.00
14-Jun-23	2.80	0.85	0.00	0.00	2.90	4.40	0.90	0.00	0.00	0.00	0.00	7.86	0.00	0.00
15-Jun-23	8.20	3.52	0.31	0.00	3.38	5.05	0.41	0.05	0.00	0.00	0.00	6.53	0.00	0.00
16-Jun-23	18.18	6.41	2.77	0.23	5.59	8.34	0.37	0.42	0.00	0.00	0.00	4.42	0.00	0.00
17-Jun-23	19.16	5.92	2.96	1.06	5.44	8.14	0.43	0.31	0.00	0.00	0.00	5.03	0.00	0.00
18-Jun-23	19.08	5.93	3.05	1.05	5.85	8.75	0.43	0.38	0.00	0.00	0.00	3.79	0.00	0.00
19-Jun-23	19.43	6.11	3.01	0.62	4.92	7.36	0.43	0.38	0.00	0.00	0.00	5.27	0.00	0.00
20-Jun-23	19.14	5.92	3.32	0.73	5.54	9.58	0.37	0.57	0.00	0.00	0.00	6.87	0.00	0.00
21-Jun-23	18.77	5.68	2.41	0.54	3.70	11.09	0.63	0.24	0.00	0.00	0.00	6.79	0.00	0.00
22-Jun-23	16.13	4.80	2.21	0.31	3.43	10.25	0.76	0.23	0.00	0.00	0.00	6.28	0.00	0.00
23-Jun-23	11.69	3.32	1.25	0.00	2.60	7.82	0.78	0.22	0.00	0.00	0.00	6.65	0.00	0.00
24-Jun-23	9.40	2.48	0.98	0.00	2.45	7.34	0.53	0.49	0.00	0.00	0.00	6.94	0.00	0.00
25-Jun-23	8.95	2.27	0.66	0.00	2.36	5.79	0.21	0.68	0.00	0.00	0.00	6.61	0.00	0.00
26-Jun-23	11.04	3.04	1.67	0.23	3.26	4.92	0.50	0.38	0.00	0.00	0.00	6.03	0.00	0.00
27-Jun-23	8.25	2.11	0.86	0.00	3.73	5.64	0.49	0.38	0.00	0.00	0.00	5.63	0.00	0.00
28-Jun-23	10.03	2.69	1.38	0.00	4.51	6.82	0.54	0.59	0.00	0.00	0.00	6.94	0.00	0.00
29-Jun-23	17.46	5.08	2.46	0.42	5.20	7.90	0.75	0.51	0.00	0.00	0.00	7.91	0.00	0.00
30-Jun-23	18.20	5.34	2.59	0.43	5.78	8.73	0.98	0.56	0.00	0.00	0.00	7.81	0.00	0.00
Total	272.70	78.15	31.89	5.62	93.44	161.81	22.44	7.77	0.00	0.00	0.00	115.58	0.00	0.00

Based on SEM/Energy meter data for links where available (*Mangdechu generation receipt at APD through a bypassed arrangement at 400kV Punatsanchu station)

Date	16.2 Export to neighbouring countries during June 2023													
	(All figures in MU)													
	Export to Bhutan								Export to Bangladesh		Export to Nepal			Export to Myanmar
	400 kV Tala-Binaguri I, II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurwar D/C*	400 kV Jigmeling-Alipurwar D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-Jun-23	0.00	0.00	0.18	0.31	0.00	0.00	0.00	0.00	21.24	3.66	1.34	4.38	0.00	0.02
2-Jun-23	0.00	0.00	0.49	0.89	0.00	0.00	0.00	0.00	21.44	3.67	1.34	4.63	0.00	0.01
3-Jun-23	0.00	0.00	0.68	0.88	0.00	0.00	0.00	0.00	21.43	3.67	1.39	4.57	0.00	0.03
4-Jun-23	0.00	0.00	0.96	1.01	0.00	0.00	0.00	0.00	21.43	3.73	1.44	4.95	0.00	0.04
5-Jun-23	0.00	0.00	1.05	1.05	0.00	0.00	0.00	0.00	21.54	3.65	1.31	4.84	0.00	0.04
6-Jun-23	0.00	0.81	1.03	1.03	0.00	0.00	0.00	0.00	21.60	3.57	1.46	4.32	0.00	0.02
7-Jun-23	0.00	0.00	0.71	0.28	0.00	0.00	0.00	0.00	21.62	3.77	1.58	4.73	0.00	0.03
8-Jun-23	0.00	0.00	0.78	0.30	0.00	0.00	0.00	0.00	21.62	3.71	1.56	4.48	0.00	0.03
9-Jun-23	0.00	0.00	0.88	0.48	0.00	0.00	0.00	0.00	21.56	3.11	1.52	4.57	0.00	0.04
10-Jun-23	0.00	0.00	1.03	0.62	0.00	0.00	0.00	0.04	21.50	3.16	1.48	2.64	0.00	0.03
11-Jun-23	0.00	0.00	1.11	1.18	0.00	0.00	0.00	0.02	22.10	3.46	1.33	0.72	0.00	0.02
12-Jun-23	0.00	0.00	1.01	1.39	0.00	0.00	0.00	0.00	21.42	3.36	1.25	0.00	0.00	0.03
13-Jun-23	0.00	0.00	0.85	1.27	0.00	0.00	0.00	0.01	21.29	3.65	1.29	0.00	0.00	0.03
14-Jun-23	0.00	0.00	0.62	1.31	0.00	0.00	0.00	0.02	21.39	3.97	1.17	0.00	0.00	0.03
15-Jun-23	0.00	0.00	0.00	0.87	0.00	0.00	0.00	0.00	21.42	3.92	1.23	0.00	0.00	0.02
16-Jun-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.52	3.59	1.31	0.00	0.00	0.03
17-Jun-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.32	3.62	1.43	0.00	0.00	0.03
18-Jun-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.53	3.14	1.35	0.00	0.00	0.02
19-Jun-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.48	3.49	1.20	0.00	0.00	0.02
20-Jun-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.46	3.60	1.00	0.00	0.00	0.00
21-Jun-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.48	3.81	1.08	0.00	0.00	0.03
22-Jun-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.45	3.94	1.25	0.00	0.00	0.03
23-Jun-23	0.00	0.00	0.00	0.06	0.00	0.00	0.00	0.00	21.67	3.80	1.15	0.00	0.00	0.03
24-Jun-23	0.00	0.00	0.00	0.03	0.00	0.00	0.00	0.00	21.54	3.80	1.02	0.00	0.00	0.03
25-Jun-23	0.00	0.00	0.00	0.15	0.00	0.00	0.00	0.00	22.39	3.86	0.83	0.00	0.00	0.03
26-Jun-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.75	3.61	0.74	0.00	0.00	0.03
27-Jun-23	0.00	0.00	0.00	0.12	0.00	0.00	0.00	0.00	22.09	3.26	0.77	0.00	0.00	0.02
28-Jun-23	0.00	0.00	0.00	0.05	0.00	0.00	0.00	0.00	22.27	2.91	0.78	0.00	0.00	0.03
29-Jun-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	17.19	2.85	0.92	0.00	0.00	0.03
30-Jun-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	16.69	3.07	0.61	0.00	0.00	0.01
Total	0.00	0.81	11.38	13.28	0.00	0.00	0.00	0.09	638.43	106.41	36.13	44.83	0.03	0.77

Based on SEM/Energy meter data for links where available (*Mangdechu generation receipt at APD through a bypassed arrangement at 400kV Punatsanchu station)

17. एसटीओए (द्विपक्षीय एवं सामूहिक) एवं डी एस एम बिलिंग का ब्योरा – जून 2023

STOA (BILATERAL AND COLLECTIVE) & DSM BILLING DETAILS - JUN 2023

द्विपक्षीय एसटीओए BILATERAL SHORT TERM OPEN ACCESS

जून 2023 Jun 2023			Apr'23- Jun'23	
नोडल क्षे.भा.प्रे.के. का नाम Name of Nodal RLDC	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Energy Approved(MU)	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Energy Approved (MU)
ऊ. क्षे. NR	1194	5434	2955	9553
प.क्षे. WR	951	2275	2901	7619
द.क्षे. SR	881	1631	2420	8580
पू.क्षे. ER	765	1184	2157	2889
पूर्वांचल क्षे. NER	134	59	283	74
कुल TOTAL	3925	10583	10716	28715

एसटीओए SHORT TERM OPEN ACCESS

	सामूहिक एसटीओए Collective STOA		द्विपक्षीय एसटीओए Bilateral STOA	
माह MONTH	क्रेताओं / विक्रेताओं की सं. NO. of Buyers/Sellers	अनुमोदित ऊर्जा (मि.यु.) Approved Energy (MU)	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Approved Energy (MU)
अप्रैल 2023 Apr'23	5580	6941	3322	9714
मई 2023 May'23	5798	6626	3469	8418
जून 2023 Jun'23	5783	6966	3925	10583
कुल TOTAL	17161	20533	10716	28715

* Approved Energy (MU) includes the Real Time Market (RTM) transactions (started from 1st Jun-20) as well, while No. of Buyers/Sellers are excluding RTM transactions.

** Approved Energy (MU) includes the Real Time Market (RTM) transactions (started from 1st Jun-20) as well, while No. of Buyers/Sellers are excluding RTM transactions.

मासिक डी एस एम बिलिंग का ब्योरा* 2021-22
MONTHLY DSM BILLING DETAILS* 2021-22

अनंतिम आँकड़े
Provisional data
subject to change
करोड़ रु. में (RS. IN CRORES)

क्षेत्र REGION →	उत्तरी क्षेत्र NORTH	पश्चिमी क्षेत्र WEST	दक्षिणी क्षेत्र SOUTH	पूर्वी क्षेत्र EAST	पूर्वांचल क्षेत्र NORTH EAST
सप्ताह WEEK ↓					
29.05.23 to 04.06.23	241.34	252.85	195.92	215.36	---
05.06.23 to 11.06.23	235.17	273.15	239.86	187.64	---
12.06.23 to 18.06.23	125.27	246.20	224.23	103.33	---
19.06.23 to 25.06.23	194.27	310.86	171.36	171.48	---
26.06.23 to 02.07.23	145.48	249.27	187.78	182.19	---

* Amount shown is Payable to DSM pool. ^Provisional Data

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL) पावर एक्स्चेंज के माध्यम से विनिमय – माह:- जून 2023 EXCHANGES THROUGH POWER EXCHANGES - JUNE 2023								
क्र. सं. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.घु. मे) Through Power Exchange in MU					
			Integrated Day Ahead Market (I-DAM)		Real Time Market (RTM)		Total (I-DAM+RTM)	
			विक्रय Sale	क्रय Purchase	विक्रय Sale	क्रय Purchase	विक्रय Sale	क्रय Purchase
1	पंजाब Punjab	उत्तरी क्षेत्र NR	198.84	362.09	102.68	188.15	301.52	550.24
2	हरियाणा Haryana		181.57	51.26	78.13	40.79	259.71	92.05
3	राजस्थान Rajasthan		283.06	31.58	314.25	75.53	597.31	107.12
4	दिल्ली Delhi		295.43	2.81	161.17	26.62	456.60	29.43
5	उत्तर प्रदेश Uttar Pradesh		221.39	168.32	36.09	150.00	257.49	318.32
6	उत्तराखंड Uttarakhand		26.94	48.52	49.44	7.34	76.38	55.85
7	हिमाचल प्रदेश Himachal Pradesh		213.39	43.91	127.67	22.56	341.05	66.47
8	जम्मू और कश्मीर J & K		26.61	34.93	116.66	28.96	143.27	63.88
9	केन्द्र शासित चंडीगढ़ UT Chandigarh		30.50	1.98	0.95	0.62	31.44	2.60
10	ए डी हाइड्रो AD Hydro		49.94	0.00	5.00	0.00	54.95	0.00
11	करचम वांगतू Karcham Wangtoo		28.36	0.00	4.70	0.00	33.06	0.00
12	श्री सीमेंट Shree Cement		13.45	0.00	4.20	1.24	17.65	1.24
13	नाथपा झाकरी Nathpa Jhakri		0.00	0.00	0.00	0.00	0.00	0.00
14	लांको बुधिल LANCO Budhil		4.96	0.00	0.34	0.00	5.30	0.00
15	सिंगरौली Singrauli		0.00	0.00	2.67	0.00	2.67	0.00
16	दादरी-I Dadri TPS		0.00	0.00	0.78	0.00	0.78	0.00
17	दादरी-II Dadri stg-II		0.00	0.00	0.34	0.00	0.34	0.00
18	ऊंचाहार-I Unchahar-I TPS		0.00	0.00	0.18	0.00	0.18	0.00
19	ऊंचाहार-II Unchahar-II TPS		0.00	0.00	0.51	0.00	0.51	0.00
20	ऊंचाहार-III Unchahar-III TPS		0.00	0.00	0.09	0.00	0.09	0.00
21	रिहंद-I Rihand STPS-I		0.00	0.00	2.68	0.00	2.68	0.00
22	रिहंद-II Rihand STPS-II		0.00	0.00	2.38	0.00	2.38	0.00
23	रिहंद-III Rihand STPS-III		0.00	0.00	2.79	0.00	2.79	0.00
24	एपीसीपीएल झज्जर APCPL Jhajjar		0.00	0.00	0.00	0.00	0.00	0.00
25	सेज Sainj HEP		21.69	0.00	9.05	0.32	30.74	0.32
26	दादरी गैस Dadri GPP		0.00	0.00	0.00	0.00	0.00	0.00
27	औरैया गैस NTPC Auraiya		0.00	0.00	0.00	0.00	0.00	0.00
28	अंता गैस NTPC Anta		0.00	0.00	0.00	0.00	0.00	0.00
29	रामपुर एचईपी RAMPUR HEP		0.00	0.00	0.00	0.00	0.00	0.00
30	ऊंचाहार-IV UNCHAHAR-IV		0.00	0.00	2.76	0.00	2.76	0.00
31	एनटीपीसी कोलडाम NTPC KOLDAM		0.00	0.00	0.00	0.00	0.00	0.00
32	कोटेश्वर Koteshtar		0.00	0.00	0.00	0.00	0.00	0.00
33	टांडा स्टेज-२ Tanda Stg-2		0.00	0.00	0.37	0.00	0.37	0.00
34	अदानी सौर एनर्जी टू लिमिटेड Adani Solar Energy Jodhpur Two Limited		10.99	0.00	0.00	0.00	10.99	0.00
35	सिंगोली भटवारी हेप Singoli Bhatwari HEP		15.48	0.00	5.87	0.00	21.35	0.00
36	रेलवे Railways		0.00	19.74	0.00	7.36	0.00	27.10
37	टिहरी Tehri		0.00	0.00	0.00	0.00	0.00	0.00
38	Renew Solar Energy (Jharkhand Three) Private Limited (RSEJTPL)		0.00	0.00	0.00	0.00	0.00	0.00
39	सोरांग एच.ई.पी. Sorang HEP, (Himachal Sorang Power Private Ltd)		3.51	0.00	5.11	0.00	8.63	0.00
40	अदानी संकर ऊर्जा जैसलमेर वन लिमिटेड (सौर)Adani Hybrid Energy Jaisalmer One Limited (Solar)		0.00	0.00	0.00	0.00	0.00	0.00
41	अदानी संकर ऊर्जा जैसलमेर टू लिमिटेड (सौर) Adani Hybrid Energy Jaisalmer Two Limited (Solar)		0.00	0.00	0.00	0.00	0.00	0.00
42	अदानी संकर ऊर्जा जैसलमेर थ्री लिमिटेड (सौर) Adani Hybrid Energy Jaisalmer Three Limited (Solar)		0.00	0.00	0.00	0.00	0.00	0.00
43	अयाना रिनूवेबल पावर वन लिमिटेड Ayana Renewable Power One Private Limited		0.00	0.00	0.00	0.00	0.00	0.00
44	Adani Hybrid Energy Jaisalmer Four Limited (Solar)अदानी संकर ऊर्जा जैसलमेर चार लिमिटेड (सौर)		0.00	0.00	0.00	0.00	0.00	0.00
45	रिणीव सोलर ऊर्जा प्राइवेट लिमिटेड Renew Solar Urja private limited		0.00	0.00	0.00	0.00	0.00	0.00
46	NEA-NR एन ई ए-एन आर		0.00	22.25	0.00	0.00	0.00	22.25
47	रेनेव सूर्या रवि प्राइवेट लिमिटेड (सौर) Renew Surya Ravi Private Limited (Solar)		39.73	0.00	0.93	0.00	40.67	0.00
48	अजूर पावर मपल प्राइवेट लिमिटेड (सौर) Azure Power Maple Pvt Ltd (Solar)		0.00	0.00	0.00	0.00	0.00	0.00
49	अदानी ग्रीन हाइब्रिड सौर जैसलमेर Adani Green Hybrid Solar Jaisalmer		0.00	0.00	0.00	0.00	0.00	0.00
50	अदानी ग्रीन हाइब्रिड पवन जैसलमेरAdani Green Hybrid Wind Jaisalmer		0.00	0.00	0.00	0.00	0.00	0.00
51	अदानी ग्रीन सौर जैसलमेर Adani Green Solar Jaisalmer		0.00	0.00	0.00	0.00	0.00	0.00
52	ABC Renewable Energy (RJ-01) Private Limited एबीसी नवीकरणीय ऊर्जा (आर-01) प्राइवेट लिमिटेड		0.00	0.00	0.00	0.00	0.00	0.00
53	SBSR Power Cleantech Eleven Private Limited एसबीएसआर पावर क्लीनटेक लिमिटेड		2.46	0.00	0.00	0.00	2.46	0.00
54	टनकपुर पावर स्टेशन Tanakpur Power Station		0.00	0.00	0.00	0.00	0.00	0.00
55	उरी पावर स्टेशन Uri I Power Station		0.00	0.00	0.00	0.00	0.00	0.00
56	उरी पावर स्टेशन Uri II Power Station		0.00	0.00	0.00	0.00	0.00	0.00
57	चमेरा पावर स्टेशन Chamera I Power Station		0.00	0.00	0.00	0.00	0.00	0.00
58	चमेरा पावर स्टेशन Chamera II Power Station		0.00	0.00	0.00	0.00	0.00	0.00
59	चमेरा पावर स्टेशन Chamera III Power Station		0.00	0.00	0.00	0.00	0.00	0.00
60	धौलीगंगा पावर स्टेशन Dhauliganga Power Station		0.00	0.00	0.00	0.00	0.00	0.00
61	दुलहशती पावर स्टेशन Dulhashti Power Station		0.00	0.00	0.00	0.00	0.00	0.00
62	किसनगंगा पावर स्टेशन Kishanganga Power Station		0.00	0.00	0.00	0.00	0.00	0.00
63	पार्वती पावर स्टेशन Parbati III Power Station		0.00	0.00	0.00	0.00	0.00	0.00
64	सेवा पावर स्टेशन Sewa II Power Station		0.00	0.00	0.00	0.00	0.00	0.00
65	सलाल पावर स्टेशन Salal Power Station		0.00	0.00	0.00	0.00	0.00	0.00
66	ADANI SOLAR ENERGY JAISALMER ONE PRIVATE LIMITED AHS अदानी सौर ऊर्जा जैसलमेर वन प्राइवेट लिमिटेड ए एच अंस		0.00	0.00	0.00	0.00	0.00	0.00
67	पार्वती ह. ई. प्रोजेक्ट Parbati II HE Project		0.00	0.00	0.00	0.00	0.00	0.00
68	एनटीपीसी अंटा जीपीएस NTPC ANT A GPS RLNG		0.00	0.00	0.00	0.00	0.00	0.00
69	एनटीपीसी औरैया जीपीएस NTPC AURAIYA GPS RLNG		0.00	0.00	0.00	0.00	0.00	0.00
70	एनटीपीसी दादरी जीपीएस NTPC DADRI GPS RLNG		0.00	0.00	0.00	0.00	0.00	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL) पावर एक्स्चेंज के माध्यम से विनिमय – माह:- जून 2023 EXCHANGES THROUGH POWER EXCHANGES - JUNE 2023								
क्र. सं. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU					
			Integrated Day Ahead Market (I-DAM)		Real Time Market (RTM)		Total (I-DAM+RTM)	
			विक्रय Sale	क्रय Purchase	विक्रय Sale	क्रय Purchase	विक्रय Sale	क्रय Purchase
71	मध्य प्रदेश Madhya Pradesh	पश्चिमी क्षेत्र WR	91.81	25.10	324.83	27.07	416.64	52.16
72	महाराष्ट्र Maharashtra		60.12	860.37	43.24	380.36	103.36	1240.73
73	गुजरात Gujarat		45.48	331.79	12.58	98.87	58.07	430.66
74	छत्तीसगढ़ Chhattisgarh		289.92	7.37	69.89	23.78	359.81	31.16
75	गोवा डब्लू आर Goa WR		7.46	27.61	0.21	6.73	7.67	34.34
76	जिंदल पावर JINDAL POWER		57.09	0.00	2.51	2.36	59.60	2.36
77	लॉको Lanco		0.00	0.00	0.00	0.00	0.00	0.00
78	ए सी बी आई एल ACBIL		49.51	0.00	4.81	0.26	54.33	0.26
79	जिंदल स्टील JINDAL STEEL		87.00	0.00	3.58	2.81	90.58	2.81
80	बालको 2 BALCO 2		0.00	0.00	1.94	0.00	1.94	0.00
81	जीएमआर वरोरा GMR Warora		10.04	0.00	3.66	0.00	13.71	0.00
82	एस्सार पावर एम पी Essar Power MP Ltd		91.38	0.00	10.03	0.12	101.41	0.12
83	के एस के महानदी KSK Mahanadi		3.57	0.00	0.00	0.00	3.57	0.00
84	जिंदल पावर लिमिटेड Jindal Power Ltd. Stg-II		88.39	0.00	4.91	14.03	93.30	14.03
85	रायगढ़ एनर्जी लिमिटेड Raigarh Energy Ltd.		7.91	0.00	0.24	0.00	8.15	0.00
86	डी बी पावर DB Power		59.35	0.00	1.03	0.00	60.39	0.00
87	धारीवाल Dhariwal		0.00	0.00	0.00	0.00	0.00	0.00
88	जेपी निगरी JAYPEE NIGRIE		106.08	0.00	0.11	0.00	106.18	0.00
89	डीजेन मेगा पावर DGEN Mega power		0.00	0.00	2.28	0.00	2.28	0.00
90	एम बी पावर MB Power		129.72	0.00	12.02	0.00	141.74	0.00
91	अदानी पावर स्टेज 3 Adani Power STG3		0.00	0.00	0.00	0.00	0.00	0.00
92	टॉरेंट पावर Torrent Power		0.00	0.00	0.00	0.00	0.00	0.00
93	मारुति क्लीन कोल पावर Maruti Clean Coal Power		13.46	0.00	2.04	0.00	15.50	0.00
94	झाबुआ पावर Jhabua Power		27.52	0.00	18.90	0.34	46.42	0.34
95	विंध्याचल स्टेज-1 Vindhyachal stg-1		0.00	0.00	0.41	0.00	0.41	0.00
96	विंध्याचल स्टेज-2 Vindhyachal stg-2		0.00	0.00	0.09	0.00	0.09	0.00
97	विंध्याचल स्टेज-3 Vindhyachal stg-3		0.00	0.00	0.32	0.00	0.32	0.00
98	विंध्याचल स्टेज-4 Vindhyachal stg-4		0.00	0.00	0.22	0.00	0.22	0.00
99	विंध्याचल स्टेज-5 Vindhyachal stg-5		0.00	0.00	0.18	0.00	0.18	0.00
100	मौदा स्टेज-1 Mouda Stg-1		0.00	0.00	0.72	0.00	0.72	0.00
101	सिपत स्टेज-1 Sipat Stg-1		0.00	0.00	0.09	0.00	0.09	0.00
102	सिपत स्टेज-2 Sipat Stg-2		0.00	0.00	0.36	0.00	0.36	0.00
103	सासन Sasan UMPP		0.00	0.00	22.25	0.00	22.25	0.00
104	भिलाई एनएसपिसीएल NSPCL Bhilai		0.00	0.00	0.00	0.00	0.00	0.00
105	कोरबा स्टेज-3 Korba Stg 3		0.00	0.00	0.06	0.00	0.06	0.00
106	टीआरएन एनर्जी TRN Energy		5.78	0.00	12.95	0.00	18.74	0.00
107	गंधार Gandhar		0.00	0.00	0.00	0.54	0.00	0.54
108	कोरबा Korba		0.00	0.00	0.23	0.00	0.23	0.00
109	आर के एम पावर RKM Power		35.93	0.00	18.03	0.00	53.96	0.00
110	कावस Kawas		0.00	0.00	0.00	0.26	0.00	0.26
111	मौदा स्टेज-2 Mouda Stg-2		0.00	0.00	0.91	0.00	0.91	0.00
112	एस के एस पावर SKS Power		50.58	0.00	16.64	2.50	67.22	2.50
113	एन टी पि सी सोलापुर NTPC Sholapur		0.00	0.00	0.29	0.00	0.29	0.00
114	एन टी पि सी गदरवारा NTPC Gadawara		0.00	0.00	1.72	0.00	1.72	0.00
115	एन टी पि सी लारा NTPC Lara		0.00	0.00	0.29	0.00	0.29	0.00
116	रायपुर एनर्जी Raipur Energen		116.26	0.00	8.86	0.00	125.13	0.00
117	आर्सेलर मित्तल ArcelorMittal Nippon steel (ESIL)		0.00	26.13	0.00	19.41	0.00	45.53
118	खरगोन Khargone STPP		0.00	0.00	0.58	0.00	0.58	0.00
119	कोस्टल गुजरात पावर लिमिटेड Coastal Gujrat Power Limited		0.00	0.00	0.35	0.00	0.35	0.00
120	कंटीनम पावर ट्रेडिंग Continuum Power Trading (TN) Private Limited		7.78	0.00	0.00	0.00	7.78	0.00
121	ऑस्ट्रो एनर्जी प्राइवेट लिमिटेड Ostro Energy Private Limited (OEPL)		0.00	0.00	0.00	0.00	0.00	0.00
122	दमन डीयू/दादरा और नगर हवेलीDaman & Diu/Dadar and Nagar Haveli		0.00	121.09	1.64	29.22	1.64	150.32
123	अदानी विंड एनर्जी Adani Wind Energy Kutchn Five Limited		0.00	0.00	0.00	0.00	0.00	0.00
124	आर जी पि पि एल RGPPL		0.00	0.00	0.00	0.31	0.00	0.31
125	Kakrapar Atomic Power Station काकरपर अटॉमिक पावर स्टेशन		0.00	0.00	157.27	0.00	157.27	0.00
126	BALCO बालको		0.00	11.76	0.00	20.08	0.00	31.85
127	अदानी विंड एनर्जी कूछ फोर लिमिटेड नखटरना ADANI WIND ENERGY KUTCHH FOUR Ltd. Nakhatrana		14.94	0.00	0.00	0.00	14.94	0.00
128	एनटीपीसी झनोर गंधार जीपीएस NTPC Jhanor Gandhar GPS RLNG		0.00	0.00	0.00	0.00	0.00	0.00
129	एनटीपीसी कावस गपद NTPC Kawas GPS RLNG		0.00	0.00	0.00	0.00	0.00	0.00
130	रत्नागिरी गैस और पावर प्राइवेट लिमिटेड Ratnagiri Gas and Power Private Limited-LTRLNG		0.00	0.00	0.00	0.00	0.00	0.00
131	विंड फाइव एनर्जी लिमिटेड WIND FIVE RENERGY LIMITED		13.45	0.00	0.00	0.00	13.45	0.00
132	एनटीपीसी झनोर गंधार जीपीएस कॉम गैस NTPC Jhanor Gandhar GPS_COMGAS		0.00	0.00	0.00	0.00	0.00	0.00
133	धारीवाल एस टी यू DHARIWAL STU OTH		2.89	0.00	0.00	0.00	2.89	0.00
134	धारीवाल आइ एस टी एस Dhariwal ISTS		4.98	0.00	0.00	0.00	4.98	0.00
135	इनोक्स ग्रीन एनर्जी सर्विसेस लिमिटेड INOX GREEN ENERGY SERVICES LIMITED		1.97	0.00	0.00	0.00	1.97	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL) पावर एक्स्चेंज के माध्यम से विनिमय – माह:- जून 2023 EXCHANGES THROUGH POWER EXCHANGES - JUNE 2023								
क्र. सं. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU					
			Integrated Day Ahead Market (I-DAM)		Real Time Market (RTM)		Total (I-DAM+RTM)	
			विक्रय Sale	क्रय Purchase	विक्रय Sale	क्रय Purchase	विक्रय Sale	क्रय Purchase
136	आंध्र प्रदेश Andhra Pradesh	दक्षिणी क्षेत्र SR	50.63	383.04	42.48	179.88	93.11	562.92
137	कर्नाटक Karnataka		86.69	30.39	51.22	57.19	137.91	87.58
138	केरलKerala		3.00	135.08	4.56	101.61	7.56	236.69
139	तमिलनाडु Tamilnadu		53.90	185.07	25.75	91.23	79.65	276.31
140	पांडिचेरी Pondicherry		20.51	0.04	10.15	0.25	30.67	0.29
141	गोवा एस आर Goa SR		0.00	20.67	0.00	2.87	0.00	23.54
142	तेलंगाना TELANGANA		45.53	188.02	28.89	443.52	74.42	631.54
143	कोस्टल एनरजेन Costal Energen		23.47	0.00	0.14	0.00	23.60	0.00
144	आई एल और एफ एस IL&FS		0.00	0.00	0.32	0.00	0.32	0.00
145	सिंहद्रि स्टेज -2 Simhadri Stg-2		0.00	0.00	0.71	0.00	0.71	0.00
146	एनएलसी इंडिया स्टेशन 1 विस्तार NLC India Station I Expansion		0.00	0.00	0.00	0.00	0.00	0.00
147	एन एल सी स्टेज-1 NLC TPS-II Stg-1		0.00	0.00	0.00	0.00	0.00	0.00
148	एन एल सी स्टेज-2 NLC TPS-II Stg-2		0.00	0.00	0.00	0.00	0.00	0.00
149	रामागुंडम स्टेज-1 Ramagundam Stg-1		0.00	0.00	0.23	0.00	0.23	0.00
150	तलचर स्टेज -2 Talcher Stg-2		0.00	0.00	0.98	0.00	0.98	0.00
151	रामागुंडम स्टेज-3 Ramagundam Stg-3		0.00	0.00	0.03	0.00	0.03	0.00
152	सेमकोर्प गायत्री Sembcorp Gayatri		86.16	0.00	4.13	0.00	90.30	0.00
153	वल्लूर Vallur		0.00	0.00	0.00	0.00	0.00	0.00
154	कुडगी NTPC Kudgi		0.00	0.00	1.04	0.00	1.04	0.00
155	सिंहद्रि स्टेज -1 Simhadri Stg-1		0.00	0.00	0.07	0.00	0.07	0.00
156	एन एल सी टी पी एस -11 एक्सपन NLC TPS-II Expn		0.00	0.00	0.00	0.00	0.00	0.00
157	एनटीपीएल NTPL		0.00	0.00	4.26	0.00	4.26	0.00
158	नयवेली न्यू थर्मल पावर प्रोजेक्ट Neyveli New Thermal Power Project		0.00	0.00	0.00	0.00	0.00	0.00
159	रामगुंडम फ्लोटिंग सोलर पी वी स्टेशन Ramagundam Floating Solar PV Station		8.42	0.00	0.00	0.00	8.42	0.00
160	सिंहद्रि फ्लोटिंग सोलर Simhadri Floating solar		1.72	0.00	0.00	0.00	1.72	0.00
161	सिंहद्रि एफएसपी 15 एमवी प्रोजेक्ट Simhadri FSP 15 MW Project		2.75	0.00	0.00	0.00	2.75	0.00
162	सेमकोर्प एनर्जी इंडिया लिमिटेड Sembcorp energy india limited		15.03	0.00	2.02	0.00	17.05	0.00
163	जे एस डब्ल्यू रिनैव एनर्जी टू लिमिटेड JSW RENEW ENERGY TWO LIMITED		0.00	0.00	0.00	0.00	0.00	0.00
164	Ostro Kannada Power Private Limited ओस्ट्रो कन्नड पावर प्राइवेट लिमिटेड		13.75	0.00	3.45	0.00	17.20	0.00
165	Simhapuri Energy Limited सिमहापुरी एनर्जि लिमिटेड		1.16	0.00	3.85	1.34	5.00	1.34
166	पश्चिम बंगाल West Bengal	पूर्वी क्षेत्र ER	2.90	712.78	61.95	248.18	64.84	960.96
167	ओडिशा Odisha		31.38	33.69	60.59	129.17	91.97	162.86
168	बिहार Bihar		119.44	13.60	177.00	39.43	296.44	53.03
169	झारखंड Jharkhand		10.13	100.10	50.28	39.37	60.41	139.47
170	सिक्किम Sikkim		7.75	0.00	6.42	2.17	14.17	2.17
171	दामोदर घाटी परियोजना DVC		25.46	42.12	8.79	25.66	34.25	67.77
172	मैथन पावर लिमिटेड Maithon P. Ltd		0.00	0.00	0.00	0.00	0.00	0.00
173	आधुनिक पा. लिमिटेड Adhunik P.Ltd		3.41	0.00	1.99	0.00	5.40	0.00
174	चुजाचेन Chuzachen HEP		6.49	0.00	0.35	0.00	6.84	0.00
175	जीएमआर कमलंगा GMR Kamalanga		0.71	0.00	0.05	0.00	0.76	0.00
176	जिंदल आई पी टी एल JIPTL		157.12	0.00	0.26	0.00	157.38	0.00
177	जोरथंग Jorethang		0.00	0.00	2.12	0.00	2.12	0.00
178	फरक्का-III Farakka-III		0.00	0.00	0.36	0.00	0.36	0.00
179	बाढ़-II Barh Stage-II		0.00	0.00	1.28	0.00	1.28	0.00
180	कहलगाँव-II Kahalgaon Stage-II		0.00	0.00	1.55	0.00	1.55	0.00
181	फरक्का Farakka		0.02	0.00	0.56	0.00	0.58	0.00
182	कहलगाँव Kahalgaon		0.00	0.00	1.55	0.00	1.55	0.00
183	तालचर Talcher		0.01	0.00	0.75	0.00	0.75	0.00
184	तीस्ता-III Teesta-III		141.92	0.00	34.96	0.00	176.88	0.00
185	दिक्चु Dikchu HEP		7.24	0.00	3.08	0.00	10.32	0.00
186	ताशिदिंग Tashiding HEP		0.00	0.00	2.55	0.00	2.55	0.00
187	केबीएनएल KBUNL		0.00	0.00	0.07	0.00	0.07	0.00
188	दर्लीपल्ली Darlipalli		0.00	0.00	0.88	0.00	0.88	0.00
189	नवीनगर NPGC Nabinagar		0.00	0.00	2.55	0.00	2.55	0.00
190	नेपाल विद्युत प्राधिकरण Nepal Electricity Authority		118.36	46.16	0.00	0.00	118.36	46.16
191	Barh STPS Stage-I बाढ़ एसटीपीएस स्टेज-1		0.00	0.00	0.13	0.00	0.13	0.00
192	NTPC North Karanpura STPS नॉर्थ करनपुरा		0.00	0.00	0.00	0.00	0.00	0.00
193	Druk Green Power Corporation Limited-Bhutan द्रुक ग्रीन पावर कार्पोरेशन लिमिटेड-भूटान		0.00	0.00	0.00	0.00	0.00	0.00
194	NTPC BARH1 Unit 2 एनटीपीसी बाढ़ 1		0.00	0.00	159.98	0.00	159.98	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL) पावर एक्स्चेंज के माध्यम से विनिमय – माह:- जून 2023 EXCHANGES THROUGH POWER EXCHANGES - JUNE 2023								
क्र. सं. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU					
			Integrated Day Ahead Market (I-DAM)		Real Time Market (RTM)		Total (I-DAM+RTM)	
			विक्रय Sale	क्रय Purchase	विक्रय Sale	क्रय Purchase	विक्रय Sale	क्रय Purchase
195	अरुणाचल प्रदेश Arunachal Pradesh	पूर्वोत्तर क्षेत्र NER	12.05	1.36	6.52	1.24	18.57	2.59
196	असम Assam		60.62	159.74	45.46	69.39	106.07	229.13
197	मणिपुर Manipur		1.55	0.00	15.35	3.17	16.90	3.17
198	मेघालय Meghalaya		9.63	32.02	0.69	25.80	10.32	57.82
199	मिज़ोरम Mizoram		6.37	0.00	0.00	0.00	6.37	0.00
200	नागालैंड Nagaland		2.92	0.85	2.63	3.73	5.55	4.57
201	त्रिपुरा Tripura		0.00	7.93	8.11	31.50	8.11	39.43
202	अगरतला जीटीपीपी Agartala GTPP_AGO		0.00	0.00	0.19	0.00	0.19	0.00
203	असम जीबीपीपी Assam GBPP_KTO		0.00	0.00	0.51	0.00	0.51	0.00
204	पलाताना Palatana		3.08	0.00	9.06	0.00	12.14	0.00
205	Doyang HEP दोयांग हेप		0.00	0.00	0.00	0.00	0.00	0.00
206	बोंगाईगाँव Bongaigaon TPP		1.24	0.00	1.47	0.00	2.71	0.00
207	कामेंग Kameng HEP		0.00	0.00	19.88	0.00	19.88	0.00
			4291	4291	2675	2675	6967	6967

19. INFORMATION ABOUT RENEWABLE ENERGY
CERTIFICATE MECHANISM

MONTH : JUNE 2023

RE Source & Unit wise break up (01.06.2023-30.06.2023)

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	325	6	1	1
2	Urban or Municipal Waste	0	0	0	0
3	Solar Thermal	0	0	0	0
4	Solar PV	3	3	51	2
5	Small Hydro	13	2	14	4
6	Others	0	0	0	0
7	Geothermal	0	0	0	0
8	Biomass	0	0	0	0
9	Bio-fuel cogeneration	0	0	15	3
	Total	341	11	81	10

RECs Issued (01.06.2023-30.06.2023)

Sr.No.	Non Solar	Solar	Total
1	324837	92394	417231

Redemption of REC (01.06.2023-30.06.2023)

Sr.No.	Non Solar	Solar	Total
1	655263	167	655430

19. INFORMATION ABOUT RENEWABLE ENERGY
CERTIFICATE MECHANISM

MONTH : JUNE 2023

RE Source & Unit wise break up (Apr'23-Jun'23)

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	326	7	103	3
2	Urban or Municipal Waste	0	0	0	0
3	Solar Thermal	0	0	0	0
4	Solar PV	54	5	65	3
5	Small Hydro	42	7	36	6
6	Others	0	0	0	0
7	Geothermal	0	0	0	0
8	Biomass	5	1	0	0
9	Bio-fuel cogeneration	4	1	19	4
	Total	431	21	223	16

RECs Issued (Apr'23-Jun'23)

Sr.No.	Non Solar	Solar	Total
1	848334	332890	1181224

Redemption of REC (Apr'23-Jun'23)

Sr.No.	Non Solar	Solar	Total
1	1133886	132387	1266273

19. INFORMATION ABOUT RENEWABLE ENERGY
CERTIFICATE MECHANISM

MONTH : JUNE 2023

RE Source & Unit wise break up Since Inception to Jun'23

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	3051	514	2572	510
2	Urban or Municipal Waste	0	0	0	0
3	Solar Thermal	0	0	0	0
4	Solar PV	1324	497	1250	468
5	Small Hydro	686	40	692	41
6	Others	4	2	3	1
7	Geothermal	0	0	0	0
8	Biomass	402	37	373	34
9	Bio-fuel cogeneration	813	89	379	54
	Total	6280	1179	5269	1108

RECs Issued since Inception to Jun'23

Sr.No.	Non Solar	Solar	Total
1	88728474	12743628	101472102

Redemption of REC since Inception to Jun'23

Sr.No.	Non Solar	Solar	Total
1	68662071	11760775	80422846

REC Closing balance as on 30.06.2023

Sr.No.	Non Solar	Solar	Total
1	20066403	982853	21049256

20.Details of Grid Events during the Month of June 2023
Northern Region



Sl.No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (H:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GI-2	Rajasthan	04-Jun-2023 00:10	04-Jun-2023 01:24	01:14	0	0	0.000	0.000	48075	56181	i) As reported, at 00:10hrs, multiple 765kV lines at Bhadla2(PG) i.e., 765kV Bhadla2-Fatehgarh2 ckt-1 & 2 and 765kV Bhadla2-Ajmer ckt-1 tripped during heavy thunderstorm with lightning, windstorm and rain. Details of the trippings are as follows: a. 765kV Bhadla2-Fatehgarh2 ckt-1 tripped on Y-N phase to earth fault (fault sensed in zone-2 at Fatehgarh2 as per DR) with fault distance of 50.99 mtrs. and fault current of 14kA from Bhadla2(PG). b. 765kV Bhadla2-Fatehgarh2 ckt-2 tripped on R-N phase to earth fault (fault sensed in zone-2 at Fatehgarh2 as per DR) with fault distance of 71.68 mtrs. and fault current of 14kA from Bhadla2(PG). c. 765kV Bhadla2-Ajmer ckt-2 tripped on permanent R-N phase to earth fault with fault distance of 290 mtrs. and fault current of 11kA from Bhadla2(PG). ii) As per PMU, the details of the event is given below: a. At 00:10:13:00hrs, transient Y-N fault occurred on 765kV Bhadla2-Fatehgarh2 ckt-2 and line successfully auto-reclosed. Then at 00:10:16:920hrs, again R-N fault occurred on 765kV Bhadla2-Fatehgarh2 ckt-2 within reclaim time and hence the line tripped (3-phase-tripped). b. At 00:10:15:320hrs, transient R-N fault occurred on 765kV Bhadla2-Fatehgarh2 ckt-1 and line successfully auto-reclosed. Then at 00:10:16:880hrs, again Y-N fault occurred on 765kV Bhadla2-Fatehgarh2 ckt-1 within reclaim time and hence the line tripped (3-phase-tripped). c. At 00:10:20:280hrs, 765kV Bhadla2-Ajmer ckt-1 tripped on permanent R-N fault with unsuccessful auto-reclose. iii) As per SCADA, no generation/load loss is observed in Rajasthan control area.	1) 765kV Bhadla2(PG)-Fatehgarh2(PG) Ckt-1 2) 765kV Bhadla2(PG)-Fatehgarh2(PG) Ckt-2 3) 765kV Bhadla2(PG)-Ajmer(PG) Ckt-1
2	GI-1	Rajasthan	05-Jun-2023 08:37	05-Jun-2023 11:26	02:49	175	0	0.382	0.000	45767	51259	i) Total generation of 220kV TPGEI evacuates through 220 KV TATA Noorsar SL_BKN PG (TPGEL)-Bikaner(PG) (TPGEL) Ckt. As per PMU, during antecedent condition generation of 220kV TPGEI was ~175MW. ii) As reported, 220 KV TATA Noorsar SL_BKN PG (TPGEL)-Bikaner(PG) (TPGEL) Ckt tripped on B-N phase to earth fault with fault current of 15 kA and fault distance of 0.79km from Bikaner(PG) end. iii) As per PMU at Bikaner(PG) and Fatehgarh2(PG), B-N phase to earth fault with fault clearing time of 80ms is observed. As per PMU at Bhadla(PG), Y-N phase to earth fault with fault clearing time of 80ms is observed. (There is Phase sequence configuration issue in PMU at Bhadla(PG) end and same has been communicated to POWERGRID for necessary actions at their end). iv) As per SCADA, generation loss of approx. 175MW is observed in NR Solar generation.	1) 220 KV TATA Noorsar SL_BKN PG (TPGEL)-Bikaner(PG) (TPGEL) Ckt
3	GI-2	Haryana	06-Jun-2023 00:10	06-Jun-2023 08:46	08:36	0	0	0.000	0.000	48645	60550	i) 400/220kV Daulatabad(HV) S/s has one and half breaker bus scheme. 400/220kV 315MVA ICT-1,2,3,384 and 400kV Daulatabad-Ghanonda D/C were connected at 400kV Bus-2 and the rest of the elements i.e., 400kV Daulatabad-Gurgaon(PG) D/C & 400kV Daulatabad-Jhajjar(APCL) D/C were connected at 400kV Bus-1. ii) As per PMU, DR/EL & tripping report received, sequence of the event are as follows: a) At 00:10:35:400hrs, B-N phase to earth fault occurred on 400 KV Gurgaon(PG)-Daulatabad(HV) (HV) Ckt-2. On this fault, A/R started at Daulatabad end, however line tripped from both end on DT received from Gurgaon(PG) end within ~60msec of A/R start. b) Further at 00:10:36:500hrs, B-N phase to earth fault occurred on 400 KV Gurgaon(PG)-Daulatabad(HV) (HV) Ckt-1. On this fault, A/R started at Daulatabad end, however line tripped from both end on DT received from Gurgaon(PG) end within ~50msec of A/R start. c) DT received from Gurgaon(PG) end might be due to PLLC misoperation. POWERGRID has been communicated regarding the same to take necessary corrective actions at their end. d) At the same time, Bus bar protection of 400kV Bus-2 at Daulatabad also mal-operated and all the Main CB connected at 400kV Bus-2 opened. As reported, there was some issue in bay unit of ICT-4. Issue has been already taken up with OEM (Siemens). e) Due to operation of bus bar protection, 400/220kV 315MVA ICT-384 tripped. f) During same time, 400/220kV 315MVA ICT-2 at Daulatabad was also hand tripped. As reported, there was some issue in auxiliary contacts of CB at LV side of ICT-2. Issue w.r.t. ICT-2 has been corrected. g) Further, it is also observed that, on tripping command of Bus bar protection of bus bar-2, Y & B ph pole of CB of ICT-4 tripped instantaneously however, R-ph pole of CB didn't open and it later opened after ~1300msec on O/C E/F protection operation. As reported, issue w.r.t. ICT-4 CB has been taken up. iii) As per SCADA, no change in demand of Haryana control area is observed.	1) 400 KV Gurgaon(PG)-Daulatabad(HV) (HV) Ckt-1 2) 400 KV Gurgaon(PG)-Daulatabad(HV) (HV) Ckt-2 3) 400kV Bus 2 at Daulatabad(HV) 4) 400/220 kV 315 MVA ICT 3 at Daulatabad(HV) 5) 400/220 kV 315 MVA ICT 3 at Daulatabad(HV) 6) 400/220 kV 315 MVA ICT 2 at Daulatabad(HV)
4	GI-2	Uttar Pradesh	06-Jun-2023 23:59	07-Jun-2023 00:35	00:36	0	170	0.000	0.280	49804	60627	i) 400/132kV Mau(UP) has double main transfer bus scheme at both 400kV & 132kV level. During antecedent condition, 400/132 kV 200 MVA ICT 1 & 2 at Mau(UP) were carrying approx. 105MW & 400/132 kV 200 MVA ICT 3 was carrying ~73MW. Bus at 132kV side were running in split mode. ICT-1&2 were connected to one bus and ICT-3 was at another bus. ii) As reported, at 23:59 hrs on 06th Jun23, Y-phase CT at Mau end of 132kV Mau-Semari Jamalpur ckt-2 damaged. On this fault, 400/132 kV 200 MVA ICT 1 & 2 at Mau(UP) both tripped on over current earth fault protection operation. At the same time, 132kV Mau-Semari Jamalpur ckt-2 also tripped. iii) As per PMU & DR, Y-N phase to earth fault which converted into Y-B-N double phase to earth fault with delayed clearance of 440msec is observed. iv) As per DR of 400/132kV ICT-2 at Mau(UP), non-directional E/F protection started, however trip signal is not high. Details of protection operation in ICT-2 need to be reviewed. v) As per SCADA, change in demand of approx. 170MW is observed in UP control area. vi) As reported, damaged Y-ph CT has been replaced on 07th June 2023.	1) 132kV Mau-Semari Jamalpur ckt-2 2) 400/132 kV 200 MVA ICT 1 at Mau(UP) 3) 400/132 kV 200 MVA ICT 2 at Mau(UP)
5	GI-1	Haryana	06-Jun-2023 01:06	06-Jun-2023 04:14	03:08	0	240	0.000	0.418	46363	57451	i) 220/66kV Palwal(HS) S/s has double main bus scheme. ii) As reported, at 01:06hrs, R-phase common jumper of bus isolator of 220/66kV 160MVA ICT-1 got disconnected from suspension insulator string due to breaking of hardware of suspension insulator string during high speed wind and subsequently it touched the B-phase of 220kV bus, which resulted in bus fault. 220 KV Prithala (GPTL)-Palwal(HV) (HVPNL) Ckt-1 & 2 tripped during the event. iii) As per CT at Palwal(HS) end, 220 KV Prithala (GPTL)-Palwal(HV) (HVPNL) Ckt-1 & 2 tripped on R-B-N double phase to ground fault sensed in zone-4 (indicating bus fault) with fault current of approx. 5.2kA in R-phase and 5.5kA in B-phase and fault clearing time of approx. 400ms. iv) As per PMU at Prithala, R-B-N double phase to ground fault with the delayed clearance of 360msec is observed. v) As per SCADA, change in demand of approx. 240MW in Haryana control area is observed.	1) 220 KV Prithala (GPTL)-Palwal(HV) (HVPNL) Ckt-1 2) 220 KV Prithala (GPTL)-Palwal(HV) (HVPNL) Ckt-2
6	GD-1	Himachal Pradesh	09-Jun-2023 16:01	09-Jun-2023 17:11	01:10	60	0	0.104	0.000	57580	65913	i) During antecedent condition, 220kV Budhil-Lahal ckt was already under shutdown in order to avoid reverse power flow. 35 MW Budhil HPS (IPP) - UNIT 1 & 2 were generating approx. 25MW and 35MW respectively and total 60MW of generation was evacuating through 220 KV Chamera_3-Budhil Ckt. ii) As reported, at 16:01 hrs, 220 KV Chamera_3(NH)-Budhil(LB) (LB) Ckt tripped on B-N phase to earth fault during heavy rain and thunderstorm. Due to this, 35 MW Budhil HPS (IPP) - UNIT 1 & 2 tripped due to loss of evacuation path. iii) As per PMU at Jalandhar(PG), B-N phase to earth fault with fault clearing time of 80msec is observed. iv) As per SCADA, no change in demand is observed in HP control area. v) As per SCADA, generation loss of approx. 60MW is observed at Budhil HPS(IPP).	1) 220 KV Chamera_3(NH)-Budhil(LB) (LB) Ckt 2) 35 MW Budhil HPS (IPP) - UNIT 1 3) 35 MW Budhil HPS (IPP) - UNIT 2

20.Details of Grid Events during the Month of June 2023
Northern Region



Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (H:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation Load in the Regional Grid during the Grid Event		Antecedent Generation Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
7	GI-1	Jammu & Kashmir and Ladakh	09-Jun-2023 15:30	09-Jun-2023 19:31	04:01	110	0	0.185	0.000	59332	66437	i) During antecedent condition, 110 MW Kishenganga - UNIT 1 & 3 were generating approx. 110MW each. 110 MW Kishenganga - UNIT 2 was already under shutdown. 110 MW Kishenganga - UNIT 3, 220 KV Kishenganga(NH)-Delina(PDG) (PG) Ckt-1 and 220 KV Kishenganga(NH)-Wagooara(PG) (PG) Ckt-2 were connected to 220KV Bus 2 at Kishenganga(NH) and rest of the elements were connected to 220KV Bus 1 at Kishenganga(NH). ii) As reported, at 15:30hrs, R phase CT failure occurred at 110 MW Kishenganga - UNIT 3. This led to bus bar protection operation of 220KV Bus 2 at Kishenganga(NH) which further led to tripping of all the elements connected to Bus-2. iii) As per PMU at Kishenganga(PG), R-N phase to ground fault is observed in the system with fault clearance time of 80ms. iv) As per SCADA, no change in demand is observed at J&K and Ladakh control area. v) As per SCADA, generation loss of approx. 110MW is observed at Kishenganga(NH).	1) 220KV Bus 2 at Kishenganga(NH) 2) 220 KV Kishenganga(NH)-Delina(PDG) (PG) Ckt-1 3) 110 MW Kishenganga - UNIT 3 4) 220 KV Kishenganga(NH)-Wagooara(PG) (PG) Ckt-2
8	GD-1	Haryana	09-Jun-2023 21:09	09-Jun-2023 22:35	01:26	0	370	0.000	0.551	52604	67125	i) 220/132kV Mohana(Haryana) has double main bus scheme at both 220kV & 132kV level. There are six 220kV lines connected at 220kV level i.e., 220KV Mohana-Sonapat(PG) D/C, 220KV Mohana-Sampla (Haryana) D/C and 220KV Mohana-Samalakhia (Haryana) D/C. Samalakhia is further connected to 220KV Chhajpur(Haryana) which is further connected to 400/220KV Panipat(BBMB). ii) As reported, at 21:09 hrs on 09th Jun23, R-phase CT at Mohana end of 220 KV Mohana(HV)-Sonapat(PG) (HVPNL) Ckt-1, damaged and line tripped. At the same time, two limbs of CB at Mohana end of 220 KV Mohana(HV)-Sonapat(PG) (HVPNL) Ckt-2 also damaged and ckt-2 also tripped. iii) As per telephonic communication with Mohana S/s, fault was in Z-4 from Mohana end having time delay setting of 1sec and bus bar protection operation was also not healthy due to issue in isolator status, hence fault didn't clear. Further, 220KV Mohana-Sampla (Haryana) D/C tripped in Z-2 from Sampla end. 220KV Mohana-Samalakhia (Haryana) D/C also became dead due to tripping of 220KV Panipat-Chhajpur ckt-1&2 due to conductor snapping. With this, 220/132kV Mohana S/s became dead. iv) At 22:35hrs, supply to Mohana S/s was restored through 220KV Mohana-Sampla (Haryana) D/C. v) As per DR received from Sonapat(PG) end, 220 KV Mohana(HV)-Sonapat(PG) (HVPNL) Ckt-1 tripped within 120msec on R-N fault and 220 KV Mohana(HV)-Sonapat(PG) (HVPNL) Ckt-2 tripped with the delay of ~360msec on R-N fault in Z-2. vi) As per PMU, R-N fault which cleared within 120msec followed by R-N fault with delayed clearance of 360 msec is observed. vii) As per SCADA, change in demand of approx. 370MW is observed in Haryana control area.	1) 220 KV Mohana(HV)-Sonapat(PG) (HVPNL) Ckt-1 2) 220 KV Mohana(HV)-Sonapat(PG) (HVPNL) Ckt-2 3) 220KV Mohana-Sampla ckt-1 4) 220KV Mohana-Sampla ckt-2
9	GI-2	Uttar Pradesh	10-Jun-2023 16:15	10-Jun-2023 16:51	00:36	0	130	0.000	0.202	55771	64245	i) 400/132kV Mau(UP) has double main transfer bus scheme at both 400kV & 132kV level. During antecedent condition, 400/132 KV 200 MVA ICT 1 & 2 at Mau(UP) were carrying approx. 70MW & 400/132 KV 200 MVA ICT 3 was carrying ~86MW. Bus at 132kV side were running in split mode. ICT-1&2 were connected to one bus and ICT-3 was at another bus. ii) As reported, at 16:15 hrs on 10th Jun23, R-phase CT at Mau end of 132KV Mau-Semari Jamalpur ckt-2 damaged. On this fault, 400/132 KV 200 MVA ICT 1 & 2 at Mau(UP) both tripped on over current earth fault protection operation. At the same time, PRV protection also operated in ICT-1. iii) As per PMU & DR, Y-N phase to earth fault with delayed clearance of 720msec is observed. iv) As per DR of 400/132KV ICT-2 at Mau(UP), trip signal is not high. SLDC-UP has been communicated regarding the same and to review the protection operation details. v) As per SCADA, Change in demand of approx. 130MW is observed in UP control area. vi) As reported, damaged R-ph CT has been replaced on 11th June 2023 and testing of ICT-1 w.r.t. PRV protection operation has also been done, testing results were found ok and ICT-1 was charged at 18:24hrs on 13th Jun23.	1) 132KV Mau-Semari Jamalpur ckt-2 2) 400/132 KV 200 MVA ICT 1 at Mau(UP) 3) 400/132 KV 200 MVA ICT 2 at Mau(UP)
10	GI-2	Punjab	10-Jun-2023 11:32	10-Jun-2023 12:23	00:51	0	385	0.000	0.563	60081	68344	i) 400/220kV Patiala(PG) has double main transfer bus scheme at 220kV level. During antecedent condition, 400/220 KV 315 MVA ICT 1 & 2 and 400/220 KV 500 MVA ICT 3 at Patiala(PG) were carrying approx. 66MW, 66MW and 103MW respectively. Bus coupler was in closed condition. ii) As reported, 220KV Bus-1 at Patiala(PG) was under planned outage which was reviewed at 11:19 hrs of 10.06.2023. At 11:32 hrs, during switching of load from Bus-1 to Bus-2, due to some breaker issue in 220KV Patiala(PG)-Bahadurgarh(PG) (PSTCL) Ckt, bus bar protection operated at 220KV level of 400/220KV Patiala(PG) leading to tripping of both 220KV Bus-1&2 at Patiala(PG). iii) As per FIR received from SLDC-Punjab, 220 KV Patiala(PG)-Ablowal(PG) (PSTCL) Ckt-1 tripped on B-N phase to earth fault (fault sensed in zone-2 from Ablowal end) with fault distance of 12.61km and fault current of 4.495 kA from Ablowal(PG) end and 220 KV Patiala(PG)-Ablowal(PG) (PSTCL) Ckt-2 tripped on B-N phase to earth fault (fault sensed in zone-2 from Ablowal end) with fault distance of 10.35km and fault current of 4.749 kA from Ablowal(PG) end. iv) As per PMU at Patiala(PG), B-N phase to earth fault converted to Y-N double phase to earth fault with delayed clearance of 360msec is observed. v) As per SCADA, change in demand of approx. 385MW is observed in Punjab control area.	1) 220KV Bus 1 at Patiala(PG) 2) 220KV Bus 2 at Patiala(PG) 3) 220 KV Patiala(PG)-Ablowal(PG) (PSTCL) Ckt-1 4) 220 KV Patiala(PG)-Ablowal(PG) (PSTCL) Ckt-2 5) 220 KV Patiala(PG)-Nabha(PG) (PSTCL) Ckt-1 6) 220 KV Patiala(PG)-Nabha(PG) (PSTCL) Ckt-2 7) 220 KV Patiala(PG)-Bahadurgarh(PG) (PSTCL) Ckt 8) 400/220KV 315MVA ICT-1 at Patiala(PG) 9) 400/220KV 315MVA ICT-2 at Patiala(PG) 10) 400/220KV 500MVA ICT-3 at Patiala(PG)
11	GD-1	Himachal Pradesh, Haryana	13-Jun-2023 18:52	13-Jun-2023 20:37	01:45	0	110	0.000	0.179	49760	61331	i) 220/132kV Pinjore(HP) has double main bus scheme at both 220kV & 132kV level. During antecedent condition, power was coming through 220KV Panchkula(HR) - Pinjore(HR) Ckt 1 & 2 from Panchkula end to Pinjore end and power was going out from Pinjore end to Baddi end through 220KV Baddi(HP) - Pinjore(HR) Ckt 1 & 2. Remaining power was being fed to the 132kV feeders at Pinjore through 220/66kV 100 MVA ICT-1&2 at Pinjore(HR). ii) As reported, at 18:52 hrs, 220KV Panchkula(HR) - Pinjore(HR) Ckt 1 & 2 tripped due to stormy weather (DPR operated). Due to this tripping, power flow through 220KV Baddi(HP) - Pinjore(HR) Ckt 1 & 2 and 220/66kV 100MVA ICT-1 & 3 at Baddi(HP) became zero (lines on no-load condition and lines were radially feeding the ICTs). iii) At 20:10 hrs, 220KV Baddi(HP) - Pinjore(HR) Ckt 1 & 2 manually tripped from Pinjore end for safety purpose. iv) After restoration of 220KV Panchkula(HR) - Pinjore(HR) Ckt 1 & 2, attempt was taken to close both 220KV Baddi(HP) - Pinjore(HR) Ckt 1 & 2. 220KV Baddi(HP) - Pinjore(HR) Ckt 1 held, but 220KV Baddi(HP) - Pinjore(HR) Ckt 2 tripped due to B-phase jumper of wave-strap snap at Pinjore(HR) end. Due to tripping of 220KV Baddi(HP) - Pinjore(HR) Ckt 1, 220KV Baddi(HP) - Pinjore(HR) Ckt 1 again manually tripped to avoid overloading on ckt-1. v) As per PMU, B-N phase to earth fault with delayed clearance of 280msec followed by R-N phase to earth fault with delayed clearance of 800msec is observed. vi) As per SCADA, change in demand of approx. 110MW is observed in HP control area.	1) 220KV Panchkula(HR) - Pinjore(HR) Ckt 1 2) 220KV Panchkula(HR) - Pinjore(HR) Ckt 2 3) 220KV Baddi(HP) - Pinjore(HR) Ckt 1 4) 220KV Baddi(HP) - Pinjore(HR) Ckt 2
12	GD-1	Punjab	14-Jun-2023 20:08	15-Jun-2023 00:39	04:31	0	115	0.000	0.180	52021	63848	i) 220/66kV Khassa(PG) has single bus scheme at both 220kV & 66kV level. During antecedent condition, power was coming through 220 KV Amritsar(PG)-Khassa(PG) (PSTCL) Ckt-1 & 2 from Amritsar end to Khassa end and power was going out from Khassa end to Chogawan and Civil lines Amritsar end through 220 KV Chogawan(PG)-Khassa(PG) (PSTCL) Ckt and 220 KV Khassa(PG)-Civil lines Amritsar (PS) (PSTCL) ckt respectively. Remaining power was being fed to the 66kV feeders at Khassa through 220/66kV ICT-1&2 at Khassa(PG). ii) As reported, at 20:06 hrs, 220 KV Chogawan(PG)-Khassa(PG) (PSTCL) ckt and 220 KV Khassa(PG)-Civil lines Amritsar (PS) (PSTCL) ckt tripped due to tower collapse (stormy weather). iii) Again at 20:08 hrs, 220 KV Amritsar(PG)-Khassa(PG) (PSTCL) Ckt-1 tripped on B-N phase to fault with fault distance of 23 km from Amritsar(PG) end. 220 KV Amritsar(PG)-Khassa(PG) (PSTCL) Ckt-2 also tripped during the same time, but line didn't trip from Powergrid end, as reported. Due to this tripping, 220/66kV Khassa(PG) S/s became dead. iv) As per DR of 220 KV Amritsar(PG) (DR end)-Khassa(PG) (PSTCL) Ckt-1, B-N phase to earth fault is observed (fault sensed in zone-2 at Amritsar(PG) end) with fault current of ~7.06kA from Amritsar(PG) end and fault clearing time of ~520ms. v) As per SCADA, 220 KV Chogawan(PG)-Civil lines Amritsar (PS) (PSTCL) ckt also tripped during the same time (reason yet to be shared). vi) As per PMU at Amritsar(PG), B-N phase to earth fault with fault clearance time of 80msec is observed at 20:06hrs and B-N phase to earth fault with delayed fault clearance time of 520msec is observed at 20:08hrs. vii) As per SCADA, change in demand of approx. 115MW is observed in Punjab control area.	1) 220 KV Chogawan(PG)-Khassa(PG) (PSTCL) ckt 2) 220 KV Khassa(PG)-Civil lines Amritsar (PS) (PSTCL) ckt 3) 220 KV Amritsar(PG)-Khassa(PG) (PSTCL) Ckt-1 4) 220 KV Amritsar(PG)-Khassa(PG) (PSTCL) Ckt-2

20.Details of Grid Events during the Month of June 2023													
Northern Region													
Sl No.	Category of Grid Event (GI 1or 2/ GD-1 to GD-5)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (H:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
13	GI-1	Punjab	18-Jun-2023 00:07	18-Jun-2023 01:30	01:23	0	350	0.000	0.516	52638	67807	i) 220/132/66kV Wadala(PS) and 220/132/66kV Verpal(PS) has double main bus scheme at 220kV level. ii) As reported, at 00:07hrs, 220/132kV ICT 1 & 4 at Wadala(PS) tripped (exact reason of tripping yet to be shared). As per SCADA, during the same time, 220/132kV ICT 3, 4 & 5 at Verpal(PS) along with all the 132kV feeders at Verpal(PS) also tripped and 132kV buses at Verpal(PS) became dead. iii) As per SCADA SOE, 132kV Wadala-Batla ckt-1, 2 & 3, 132kV Wadala-Hargo ckt-1 and 132/11kV ICT 2 at Wadala(PS) also tripped during the same time. iv) As per information received from SLDC Punjab, at 00:14 hrs, R-phase CT of 220 kV Verpal(PS) –Amritsar(PG) ckt-2 blasted at Verpal(PS) end. Further, fire was also observed in the cable of 220 kV Verpal(PS) –Amritsar(PG) ckt-1. As per SCADA, during the same time, 220 kV Verpal(PS) –Wadala(PS) ckt-1 and 220 kV Verpal(PS) –Wadala(PS) ckt-2 also tripped. v) As per information received from CPCC2, 220kV Verpal(PS) –Amritsar(PG) ckt-1 tripped only from Verpal(PS) end and line remained charged from Amritsar(PG) end. vi) As per DR of 220 kV Verpal(PS) –Amritsar(PG) (end) ckt-2, R-N phase to earth fault (fault sensed in zone-2) is observed with fault current of approx. 27.55kA in R-phase and fault clearing time of 145ms. vii) As per PMU at Amritsar(PG), Y-N phase to earth fault with delayed clearance of 440msec is observed at 00:07hrs and R-N phase to earth fault with delayed clearance of 240msec is observed at 00:14hrs. viii) As per SCADA, change in demand of approx. 315MW at 00:07hrs and 350MW at 00:14hrs is observed in Punjab control area.	1) 220/132kV ICT 1 at Wadala(PS) 2) 220/132kV ICT 4 at Wadala(PS) 3) 220/132kV ICT 3 at Verpal(PS) 4) 220/132kV ICT 4 at Verpal(PS) 5) 220/132kV ICT 5 at Verpal(PS) 6) 220 kV Verpal(PS) –Wadala(PS) ckt-1 7) 220 kV Verpal(PS) –Wadala(PS) ckt-2 8) 220 kV Verpal(PS) –Amritsar(PG) ckt-1 9) 220 kV Verpal(PS) –Amritsar(PG) ckt-2
14	GD-1	J&K	19-Jun-2023 08:28	19-Jun-2023 11:44	03:16	0	190	0.000	0.329	12580.51111	57677	i) During antecedent condition, active power loading of 220 kV Kishenpur(PG)-Barn(JK) (POD JK) Ckt-1 & 2 was approx. 98MW each. ii) As reported, at 08:28hrs, 220 kV Kishenpur(PG)-Barn(JK) (POD JK) Ckt-1 & 2 tripped on B-N phase to phase fault from Barn end only. iii) As per DR of 220 kV Barn(JK)-Kishenpur(PG) Ckt-1 & 2 at Kishenpur end, B-N fault in Z-2 is observed which cleared in ~160msec. iv) As per PMU at Kishenpur(PG), B-N fault which cleared in 160msec is observed. v) As per SCADA, load loss of approx. 190MW occurred in J&K control area.	1) 220 kV Kishenpur(PG)-Barn(JK) (POD JK) Ckt-1 2) 220 kV Kishenpur(PG)-Barn(JK) (POD JK) Ckt-2
15	GD-1	Rajasthan	20-Jun-2023 05:21	20-Jun-2023 07:36	02:15	0	280	0.000	0.480	13178.68333	58276	i) 400/220kV Ratangarh(Raj) has double main & transfer bus scheme at 220kV side. ii) During antecedent condition, 400/220 kV 315 MVA ICT 2 at Ratangarh(RS) and 220kV feeders to Badnu, Sikar(PG)-II, Ratangarh-I and Khethi-I connected at 220kV Bus-B. Remaining elements were connected at 220kV Bus-A. iii) As reported at 05:21 hrs, B-ph bus jumper of 220 kV Ratangarh-Badnu (Raj) Ckt broke and created B-N phase to earth bus fault on 220kV bus-B. 220kV Badnu ckt tripped in Z-1 from Ratangarh end (distance relay at Ratangarh end sensed fault in Z-1, forward direction due to issue of improper fault selection by relay in case of near fault). iv) 220kV Bus bar protection was in blocked condition due to some circuitry fault and hence, bus bar protection didn't not operate. v) Continuous pickup and reset of Z-4 is observed in adjacent 220kV lines connected at 220kV Bus-B due to which none of the lines tripped in Z-4 from Ratangarh end (Z-4 time delay setting is kept as 160msec at Ratangarh end). As fault was still persisting 220kV lines connected at 220kV Bus-B tripped from remote end on distance protection operation in Z-2. Rajasthan has been communicated to check the operation of Z-4 distance protection at Ratangarh end. vi) 220kV Ratangarh-Sikar ckt-1 connected at 220kV Bus-A also tripped in Z-4 as bus coupler breaker opened with the time delay more than Z-4 time delay (160msec). vii) After approx. 600msec of the fault, 400/220kV 315MVA ICT-2 at Ratangarh(Raj) tripped on over current E/F protection operation and fault cleared with the tripping of this ICT. viii) 220kV Badnu S/s became dead during the tripping event as it was having feeding from 400/220kV Ratangarh(Raj) only. ix) As per SCADA, change in load of approx. 280MW is observed in Rajasthan control area. x) As informed by Rajasthan, issue w.r.t. bus bar protection at 220kV side of 400/220kV Ratangarh(Raj) has been corrected and bus bar protection is now healthy and in service.	1) 400/220 kV 315 MVA ICT 2 at Ratangarh(RS) 2) 220 kV Ratangarh(RS)-Sikar(PG) (PG) Ckt-1 3) 220 kV Ratangarh(RS)-Sikar(PG) (PG) Ckt-2 4) 220 kV Ratangarh-Badnu (Raj) Ckt 5) 220 kV Ratangarh-Ratangarh220 (Raj) Ckt-1 6) 220 kV Ratangarh-Khethi (Raj) Ckt-1
16	GD-1	J&K	25-Jun-2023 16:36	25-Jun-2023 18:25	01:49	0	230	0.000	0.440	7191.232639	52294	i) During antecedent condition, 220 kV MirBazar(PDD)-NewWanpoh(PG) (POD JK) Ckt-1, 220kV Pampore- Mirbazar D/C were not in service. 220 kV MirBazar(PDD)-NewWanpoh(PG) (POD JK) Ckt-1 was out since 14:55 hrs of the 25th June 2023 for routine maintenance of the line. Active power loading of 220 kV MirBazar(PDD)-NewWanpoh(PG) (POD JK) Ckt-2 was 231MW. ii) As reported, at 16:36hrs, 220 kV MirBazar(PDD)-NewWanpoh(PG) (POD JK) Ckt-2 tripped on R-N fault in line. iii) As per DR at NewWanpoh(PG) end of 220 kV MirBazar(PDD)-NewWanpoh(PG) (POD JK) Ckt-2, zone-1 distance protection operated with fault current of 8.7kA. iv) Due to tripping of 220 kV MirBazar(PDD)-NewWanpoh(PG) (POD JK) Ckt-2, supply to Mirbazar S/s got affected. v) As per PMU at Kishenpur(PG), R-N fault which cleared within 100msec is observed. vi) As per SCADA, load loss of approx. 230MW occurred in J&K control area. vii) Further, at around 17:12hrs, ~80MW load was restored by charging 220kV Pampore- Mirbazar D/C and complete load of Mirbazar restore at 18:25 hrs with the charging of 220 kV MirBazar(PDD)-NewWanpoh(PG) (POD JK) Ckt-2.	1) 220 kV Mir Bazar(PDD)-NewWanpoh(PG) (POD JK) Ckt-2
17	GD-1	J&K	26-Jun-2023 14:56	26-Jun-2023 17:56	03:00	0	225	0.000	0.369	54411	61047	i) During antecedent condition, active power loading of 220 kV Kishenpur(PG)-Barn(JK) (POD JK) Ckt-1 & 2 was approx. 112MW each. Both the circuit are on same tower and line length is 35km. ii) As reported, at 16:56hrs, 220 kV Kishenpur(PG)-Barn(JK) (POD JK) Ckt-2 tripped on R-Y phase to phase fault. Fault currents were Ir~6kA & Iy~3kA and fault distance was ~20km from Kishenpur end. At the same time, 220 kV Kishenpur(PG)-Barn(JK) (POD JK) Ckt-1 also tripped. Fault distance ~32km from Kishenpur end. iii) As per DR of 220 kV Kishenpur(PG)-Barn(JK) (POD JK) Ckt-1 & 2 at Kishenpur end, 220 kV Kishenpur(PG)-Barn(JK) (POD JK) Ckt-1 tripped on R-Y fault in Z-1 from Kishenpur end instantaneously and 220 kV Kishenpur(PG)-Barn(JK) (POD JK) Ckt-2 tripped with delay of ~160msec from Kishenpur end on R-Y fault in Z-2. iv) As per SCADA, load loss of approx. 225MW occurred in J&K control area. v) Further at 17:56hrs, 220 kV Kishenpur(PG)-Barn(JK) (POD JK) Ckt-2 was charged which again tripped at 20:38hrs on phase to earth fault and revived back at 21:49hrs. vi) Later at 00:11hrs on 27th June 2023, 220 kV Kishenpur(PG)-Barn(JK) (POD JK) Ckt-2 was taken under shutdown and both the circuits revived at 04:02 hrs.	1) 220 kV Kishenpur(PG)-Barn(JK) (POD JK) Ckt-1 2) 220 kV Kishenpur(PG)-Barn(JK) (POD JK) Ckt-2
18	GI-2	Uttar Pradesh	26-Jun-2023 06:37	26-Jun-2023 08:37	02:00	0	0	0.000	0.000	44268	49165	i) 400/220kV Shahjahanpur (PG) has double main transfer bus scheme at 220kV level. During antecedent condition, 400/220 kV 500 MVA ICT 1 & 2 at Shahjahanpur (PG) were carrying approx. 40MW and 36MW respectively. Bus coupler was in closed condition. ii) As reported, at 06:37 hrs, bus bar protection of 220kV Bus-2 operated on R-N bus fault and elements connected to bus-2 i.e., 400/220 kV 500 MVA ICT 1 at Shahjahanpur(PG), 220 kV Azipur (UP)-Shahjahanpur(PG) (UP) Ckt-2 and 220 kV Shahjahanpur(PG)-Shahjahanpur(UP) (UP) Ckt-1 tripped. iii) Bus coupler breaker opened instantaneously and 220kV bus-1 at Shahjahanpur (PG) and elements connected to it remained intact. iv) As per PMU at Lucknow(PG), R-N phase to earth fault which cleared within 80msec is observed. v) As per SCADA, no change in demand in Uttar Pradesh control area.	1) 220kV Bus 2 at Shahjahanpur(PG) 2) 400/220 kV 500 MVA ICT 1 at Shahjahanpur(PG) 3) 220 kV Azipur (UP)-Shahjahanpur(PG) (UP) Ckt-2 4) 220 kV Shahjahanpur(PG)-Shahjahanpur(UP) (UP) Ckt-1

20.Details of Grid Events during the Month of June 2023
Northern Region



Sl.No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (H:M:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(G1 for 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
19	GD-1	Punjab	29-Jun-2023 21:07	29-Jun-2023 22:50	01:43	0	995	0.000	1.512	47358	65805	i) As reported, at 21.07hrs, earth wire of 220 KV Moga(PG)-Mehal- Kalan(PS) (PSTCL) Ckt-1 & 2 snapped between Moga S/s Gantry and tower location no. 1. This led to bus bar protection operation of 220kV bus -1 at Moga(PG) due to fault in 220 KV Moga(PG)-Mehal- Kalan(PS) (PSTCL) Ckt-2. Due to this, 220 KV Moga(PG)-Mogan(PS) (PSTCL) Ckt-4, 400/220 kv 500 MVA ICT 1 at Moga(PG) and 400/220 kv 315 MVA ICT 4 at Moga(PG) tripped. ii) 220 KV Moga(PG)-Mehal- Kalan(PS) (PSTCL) Ckt-1 (connected at 220kV Bus-2) tripped due to DT received at Moga(PG) end. During the same time, 220 KV Moga(PG)-Ajitwal(PS) (PSTCL) Ckt-1 (connected at 220kV bus-2) also tripped on R-Y-N double phase to earth fault. iii) As per DR of Moga(PG) end, R-N phase to earth fault (Ir=30.73KA, fault sensed in zone-1) followed by Y-B phase to phase fault (Iy=30.83KA, Ib=30.56KA) are observed in 220 KV Moga(PG)-Mehal-Kalan(PS) (PSTCL) Ckt-2, fault distance was 70m from Moga(PG) end. At the same time, R-Y-N double phase to earth fault (Ir=42.66KA, Iy=44.11KA) with fault clearance time of 90ms is observed in 220 KV Moga(PG) (end)-Ajitwal(PS) (PSTCL) Ckt-1, fault distance was 0.6m from Moga(PG) end. iv) As per SCADA SOE, 220/66 kv ICT 2 at Mehal- Kalan(PS) and 220KV Mogan(PS)-Baghapurana(PS) Ckt-1 also tripped during the same time (Reason yet to be shared). v) As per PMU at Allahabad(PG), multiple faults are observed. vi) Whole event leads to load loss of Baghapurana (feeding through Mogan (Punjab)), Jagraon (feeding through Ajitwal) and load of Mehal-Kalan. As per SCADA, change in demand of approx. 995 MW is observed in Punjab control area. vii) As reported, 220 kv Baghapurana & Jagraon load revived within 5-10 minutes.	1) 220 KV Moga(PG)-Mehal- Kalan(PS) (PSTCL) Ckt-1 2) 220 KV Moga(PG)-Mehal- Kalan(PS) (PSTCL) Ckt-2 3) 220 KV Moga(PG)-Ajitwal(PS) (PSTCL) Ckt-1 4) 220 KV Moga(PG)-Mogan(PS) (PSTCL) Ckt-4 5) 400/220 kv 500 MVA ICT 1 at Moga(PG) 6) 400/220 kv 315 MVA ICT 4 at Moga(PG)

20.Details of Grid Events during the Month of June 2023



Western Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GI-2	WR	04-Jun-23 14:32	04-Jun-23 15:17	00:45	-	81	-	0.002	63854	53546	At 14:32 Hrs/04.06.2023, 400 kV Lonikhand-Pune tripped due to wave trap blast at Lonikhand end and 400 kV Lonikhand-Lonikhand-II 1 tripped due to LA blast at Lonikhand end. At the same time 400 kV Lonikhand-Chakan and 400 kV Karjat-Lonikhand-II 1&2 also tripped due to reverse zone protection and Overvoltage ST1 protection respectively. Load loss of 81 MW occurred due to the event.	Tripping of 1. 400 kV Lonikhand-Pune 2. 400 kV Lonikhand-Lonikhand-II 1&2 3. 400 kV Lonikhand-Chakan 4. 400 kV Karjat-Lonikhand-II 1&2
2	GI-2	WR	04-Jun-23 15:20	04-Jun-23 19:48	04:28	1260	-	0.020	-	64330	52843	At 15:20 hrs/04.06.2023, multiple elements at 765/400kV Kotra PS tripped due to multiple equipment failures on the account of heavy rains and thunderstorm. Total Generation loss of 1260 MW occurred due to tripping of units at SKS (2*300 MW) (due to loss of evacuation path), REGL (1*600 MW) and DB Power (1*600 MW) (due to generator protection). 765/400kV ICT-2,3 & 4 and 765kV BR-2 tripped on differential protection. 765kV Kotra-Champa D/C, 400kV Kotra-SKS D/C, 400kV Kotra-Lara 2 & 400kV Kotra-REGL 2 tripped on distance protection operation.	Tripping of 1. 765 kV Kotra-Champa 1&2 2. 765 kV Kotra-Bus Reactor 2 3. 765/400 kV Kotra-ICT 2,3&4 4. 400 kV Kotra- Lara 2 5. 400 kV Kotra- REGL 2 6. 400 kV Kotra- SKS 1&2 7. SKS Unit 1,2 (300 MW each) 8. REGL unit 1 (600 MW) 9. DB Power Unit 1(600 MW)
3	GI-1	WR	11-Jun-23 14:48	11-Jun-23 15:28	00:40	-	-	-	-	70128	61843	At 14:48 Hrs/11-06-2023, 220 kV Borivali- Tarapur line tripped on R-E fault from Tarapur end. As the fault was not cleared from Borivali end, 220 kV Borivali Bus 1 and all the elements connected to it tripped on LBB protection operation. There was no load loss due to the event.	Tripping of 1. 220kV Borivali-Tarapur 2. 220kV Borivali - Bolar 3. 220kV Borivali -Kharghar 4. 220kV Borivali -Bhandup 5. 220kV Borivali -Tata 4 6. 220kV Borivali - Adani Borivali 1 7. 220kV Borivali- AdaniGorai 2 8. 220kV Borivali- Adani Aarey 2
4	GI-2	WR	13-Jun-23 09:46	13-Jun-23 10:13	00:27	-	-	-	-	70427	60866	At 09:46 Hrs / 13-06-2023, 400kV Padghe Nagothane 1 tripped on Y-B Fault. At the same time R-phase CT (towards Bus side) of 400 kV Dabhol-Nagothane 1 failed & resulted in Bus bar protection operation and tripping of all connected feeders along with Bus coupler at 400 kV Nagothane. Load loss of 160 MW occurred due to LTS operation at Wadhkal region due to the event.	Tripping of 1. 400 kV Nagothane-Padghe 1&2 2. 400 kV Nagothane-Buses 1&2 3. 400 kV Dabhol-Nagothane 1&2 4. 400/220 kV Nagothane-ICTs 1,2&3
5	GI-1	WR	13-Jun-23 13:30	13-Jun-23 16:16	02:46	280	-	0.004	-	71471	61063	At 13:30 Hrs / 13-06-2023, 220 kV Ratadiya-Bhuj 2 conductor snapped from the B-Phase CT side jumper clamp and touched gantry of 220kV Ratadiya Bus 1. This resulted in Bus bar protection operation and tripping of the line along with 220/33 kV Ratadiya-ICTs 2&4. As Bus coupler was kept in open condition, Generation loss of 280 MW occurred at Ratadiya (AGEMPL) wind power station.	Tripping of 1. 220 kV Ratadiya-Bhuj 2 2. 220 kV Ratadiya Bus 1 3. 220/33 kV Ratadiya ICTs 2&4
6	GD-1	WR	13-Jun-23 17:46	13-Jun-23 18:17	00:31	-	170	-	0.003	72782	59196	At 17:46 Hrs / 13-06-2023, 220 kV Kala – New Kharadpada 1 tripped on R-E fault. 220 kV Kala-New Kharadpada 1 was already under planned shutdown. 220 kV Bus Coupler at 220 kV Kharadpada was in open condition and the load on 220 kV Kharadpada Bus 2 was fed radially from Kala s/s through New Kharadpada. With the tripping of 220 kV Kala – New Kharadpada 2, 220 kV New Kharadpada substation went dark. 220 kV New Kharadpada-Kharadpada D/C became dead and H/T later by site. Load loss of around 170 MW is occurred due to the event.	Tripping of 1. 220 kV Kala-New Kharadpada 1 2. 220 kV Kharadpada-New Kharadpada 1&2 3. 220 kV New Kharadpada-Reliance 1&2

20.Details of Grid Events during the Month of June 2023

Western Region



Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
7	GD-1	WR	15-Jun-23 16:36	15-Jun-23 18:03	01:27	-	-	-	-	69518	58686	At 16:36 Hrs / 15-06-2023, 220 kV Bachhau-Bhuvad 1&2 tripped at 16:36 hrs on B phase to earth fault. Prior to the event, WTGs were manually stopped by site due to high wind speed because of Biparjoy cyclone. No generation was present at Bhuvad (ReNew) wind station during the event.	Tripping of 1. 220 kV Bachhau-Bhuvad 1&2 2. 220/33 kV Bhuvad-ICT 1&2
8	GD-1	WR	15-Jun-23 18:49	15-Jun-23 21:15	02:26	5	-	0.000	-	68762	56724	At 18:49 Hrs / 15-06-2023, 220 kV Bhuj-Dayapar 1 tripped on B phase to earth fault. Generation loss of 5 MW occurred at 220 kV Dayapar (INOX) wind station due to loss of evacuation path.	Tripping of 1. 220 kV Bhuj-Dayapar 1
9	GD-1	WR	16-Jun-23 01:23	16-Jun-23 06:19	04:56	-	-	-	-	69469	57709	At 01:23 Hrs / 16-06-2023, 220 kV Bhuj-Naranpar 2 tripped on B phase to earth fault. Prior to the event, WTGs were auto cut out due to high wind speed because of Biparjoy cyclone. No generation was present at 220 kV Naranpar (GIWEL-III) wind power station during the event	Tripping of 1. 220 kV Bhuj-Naranpar 1
10	GD-1	WR	16-Jun-23 06:23	16-Jun-23 17:59	11:36	-	-	-	-	66883	56556	At 06:23 Hrs / 16-06-2023, 220 kV Bhuj-Gadhsisa 1 tripped on Y-B phase to phase fault due to broken wave trap isolator pad clamp. Prior to the event, WTGs were manually stopped by site due to high wind speed because of Biparjoy cyclone. No generation was present at Gadhsisa (ReNew AP2) wind power station during the event	Tripping of 1. 220 kV Bhuj-Gadhsisa 1
11	GD-1	WR	16-Jun-23 08:05	16-Jun-23 09:58	01:53	-	-	-	-	62256	54794	At 08:05 Hrs / 16-06-2023, 220 kV Jamkhambaliya-Khakharda 1 tripped on vector surge protection operation due to Biparjoy cyclone effect. Prior to the event, WTGs were auto cut out due to high wind speed because of Biparjoy cyclone. No generation was present at Khakharda (Apraava) wind power station during the event	Tripping of 1. 220 kV Jamkhambaliya-Khakharda 1
12	GD-1	WR	16-Jun-23 09:22	16-Jun-23 12:07	02:45	-	-	-	-	62005	55432	At 09:22 Hrs / 16-06-2023, 220 kV Bachhau-Ostro 1 tripped on B phase to earth fault. At the same time 220 kV Bachhau-Ostro 1 also tripped. Prior to the event, WTGs were out due to high wind speed because of Biparjoy cyclone. No generation was present at Ostro (ReNew) wind power station during the event	Tripping of 1. 220 kV Bachhau-Ostro 1&2
13	GD-1	WR	16-Jun-23 10:23	16-Jun-23 17:01	06:38	-	-	-	-	60256	56252	At 10:23 Hrs / 16-06-2023, 220 kV Jamkhambaliya-Khakharda 1 tripped on vector surge protection operation due to Biparjoy cyclone effect. Prior to the event, WTGs were auto cut out due to high wind speed because of Biparjoy cyclone. No generation was present at Khakharda (Apraava) wind power station during the event	Tripping of 1. 220 kV Jamkhambaliya-Khakharda 1
14	GD-1	WR	16-Jun-23 11:11	16-Jun-23 11:46	00:35	-	-	-	-	60024	55917	At 11:09 Hrs / 16-06-2023, 765/400 kV Lakadia-ICT 1 tripped on DC earth fault. Prior to the event, 765/400 kV Lakadia-ICT 2 tripped at 06:54 hrs / 16-06-2023 on Buchholz relay operation. With the tripping of these 765/400 kV Lakadia ICTs, 400 kV Jamkhambaliya was radially connected to 400 kV Bachhau through 400 kV Lakadia. At 11:11 hrs, 400 kV Bachhau-Lakadia 1&2 tripped on B phase to earth fault and Y-B phase to phase fault respectively. With these tripping, 400 kV side of Lakadia & 400/220 kV Jamkhambaliya substations became dark. No generation loss was reported during the event.	Tripping of 1. 765/400 kV Lakadia-ICT 1 2. 400 kV Bachhau-Lakadia 1&2 3. 400 kV Jamkhambaliya-Lakadia 1&2 4. 220 kV Jamkhambaliya-Sidhpur 1
15	GD-1	WR	16-Jun-23 11:55	16-Jun-23 13:27	01:32	30.9	-	0.001	-	60768	54982	At 11:55 Hrs / 16-06-2023, 220 kV Bhuj-Nanavalka 1 tripped on R phase to earth fault due to insulation failure at Tower 10/15. Generation loss of 30.9 MW occurred at 220 kV Nanavalka (Alfanar) wind power station due to loss of evacuation path.	Tripping of 1. 220 kV Bhuj-Nanavalka 1

20.Details of Grid Events during the Month of June 2023



Western Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
16	GD-1	WR	16-Jun-23 14:15	16-Jun-23 19:06	04:51	-	-	-	-	61122	55386	At 14:15 Hrs / 16-06-2023, 220 kV Bhuj-Baranda 1 tripped on B phase to earth fault. Prior to the event, all WTGs tripped due to high wind speed because of Biparjoy cyclone. No generation was present at 220 kV Baranda (Avikaran) wind power station during the event	Tripping of 1. 220 kV Bhuj-Baranda 1
17	GD-1	WR	16-Jun-23 14:15	16-Jun-23 15:48	01:33	-	-	-	-	61122	55386	At 14:15 Hrs / 16-06-2023, 220 kV Bhuj-Kotda Madh 1 tripped due to false DT signal recieved at Kotda Madh end. Prior to the event, all WTGs tripped due to high wind speed because of Biparjoy cyclone. No generation was present at 220 kV Kotda Madh (Alfanar) wind station during the event	Tripping of 1. 220 kV Bhuj-Kotda Madh 1
18	GD-1	WR	16-Jun-23 17:20	16-Jun-23 23:08	05:48	20	-	0.000	-	64867	55094	At 17:20 Hrs / 16-06-2023, 220 kV Bhuj-Kotda Madh 1 tripped due to false DT signal recieved at Kotda Madh end. Generation loss of 20 MW occurred at 220 kV Kotda Madh (Alfanar) wind power station due to loss of evacuation path.	Tripping of 1. 220 kV Bhuj-Kotda Madh 1
19	GD-1	WR	30-Jun-23 03:34	30-Jun-23 15:19	11:45	37.3	-	0.001	-	56406	46115	At 03:34 Hrs / 30-06-2023, 220 kV Bhuj-Kotda Madh 1 tripped on R phase to earth fault. Generation loss of 37.3 MW occurred at Kotda Madh (Alfanar) wind power plant due to the event,	Tripping of 1. 220 kV Bhuj-Kotda Madh 1
20	GI-1	WR	30-Jun-23 03:42	30-Jun-23 17:34	13:52	173.4	-	0.003	-	56244	46120	At 03:42 Hrs / 30-06-2023, 220 kV Bhuj-Ratadia 2 tripped on R phase to earth fault due to R phase suspension insulator got punctured at tower number 3. Generation loss of 173.4 MW occurred at Ratadia (AGEMPL) wind power plant due to the event,	Tripping of 1. 220 kV Bhuj-Ratadia 2 2. 220 kV Ratadiya Bus 1 3. 220/33kV Ratadiya ICT-2 & 4

20.Details of Grid Events during the Month of June 2023
Southern Region



Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid		Brief details of the event (pre fault and post fault system conditions)	Name of Elements (Tripped/Manually opened)
	(GI for 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-1	Kerala	03-Jun-23 23:36	03-Jun-23 23:41	5mins	0	377	0.00%	0.77%	46118	49250	Complete Outage of 220kV/110kV Ambalathara SS, 220kV/110kV/11kV Kanhirode SS, 220kV/110kV/11kV Mylatty SS, 220kV/110kV/33kV Taliparamba SS, and 220kV/110kV Thalassery SS of KSEB: 220kV/110kV Ambalathara SS, 220kV/110kV/11kV Kanhirode SS, 220kV/110kV/11kV Mylatty SS, 220kV/110kV/33kV Taliparamba SS, and 220kV/110kV Thalassery SS are being radially fed through 220kV Kanhirode Areakode and 220kV Areakode Orkattery lines. As per the reports submitted, the triggering incident was RYB-N fault in 220kV Kanhirode Areakode and 220kV Kanhirode Orkattery lines. Tripping of both lines resulted in a complete outage of 220kV/110kV Ambalathara SS, 220kV/110kV/11kV Kanhirode SS, 220kV/110kV/11kV Mylatty SS, 220kV/110kV/33kV Taliparamba SS, and 220kV/110kV Thalassery SS.	1. 220kV Kanhirode Areakode 2. 220kV Kanhirode Orkattery
2	GD-1	Tamil Nadu	06-Jun-23 10:59	06-Jun-23 12:03	1 hrs 4 mins	49.8	63	0.09%	0.12%	52462	53706	Complete Outage of 230kV/110kV/22kV Karaikudi_TN of TANTRANSCO: During antecedent conditions, all elements were connected to 230kV Bus-2 at 230kV/110kV/22kV Karaikudi_TN. As per the reports submitted, the triggering incident was an R-phase Bus side jumper cut in 230kV Karaikudi_TN Karaikudi_PG line-2. Immediately, 230kV Bus-2 B8P operated and all the elements connected to the Bus tripped. This resulted in a complete outage of 230kV/110kV/22kV Karaikudi_TN SS.	1. 230kV Karaikudi_TN Karaikudi_PG line-1&2 2. 230kV Karaikudi_TN Kavanur line-1,2,3&4 3. 230kV Karaikudi_TN Valuthur 4. 230kV Karaikudi_TN NT Kudy Line-1 4. 230kV/110kV Karaikudi_TN Transformer-1,2&3
3	GD-1	Karnataka	06-Jun-23 19:25	06-Jun-23 20:31	54mins	0	730	0.00%	1.49%	42379	48923	Tripping of 220kV Bus-2 of 400kV/220kV Hoody SS and Complete Outage of 220kV/66kV Exora SS, 220kV/66kV EDC SS, 220kV/66kV HAL SS, 220kV/66kV Vikas Tech Park SS and 220kV/66kV Sarjapur SS of KPTCL: As per the reports submitted, the triggering incident was B-N fault in 220kV Bus-2 at 400kV/220kV Hoody SS. This resulted in loss of power supply of 220kV Bus-2 of 400kV/220kV Hoody SS which further led to complete loss of supply at 20kV/66kV Exora SS, 220kV/66kV EDC SS, 220kV/66kV HAL SS, 220kV/66kV Vikas Tech Park SS, and 220kV/66kV Sarjapur SS.	1. 400kV/220kV Hoody ICT-2&3 2. All the lines connected to 220kV Hoody Bus-2
4	GD-1	Karnataka	07-Jun-23 09:47	07-Jun-23 10:22	35mins	0	135	0.00%	0.27%	52670	49457	Complete Outage of 220kV/66kV A'Halli SS of KPTCL: During antecedent conditions, 220kV Anthrasanahalli Nelamangala Line was under outage. The triggering incident was R-phase jumper cut in 220kV Anthrasanahally Tumkur Line-1 &2 and the lines tripped. Subsequently, the 220kV Anthrasanahally MRS Shimoga line was hand tripped in order to control over loading. Tripping of all these lines resulted in complete outage of 220kV/66kV A'Halli SS.	1. 220kV Anthrasanahally Tumkur Line-1 &2 2. 220kV Anthrasanahally MRS Shimoga line
5	GD-1	Telangana	08-Jun-23 08:20	08-Jun-23 13:52	5hrs 32mins	0	0	0.00%	0.00%	48318	46256	Complete Outage of 400kV Yadadri TPS generating station of TSGENCO and 400kV/220kV Damarcherla SS of TSTRANSCO: 400kV Yadadri TPS generating station is radially connected to 400kV/220kV Damarcherla SS. As per the reports submitted, the triggering incident was DC supply failure at 400kV/220kV Damarcherla SS causing all the CTDs of lines and transformers to operate and all these elements tripped. Tripping of all these lines and transformers at 400kV/220kV Damarcherla SS resulted in complete outage of 400kV Yadadri TPS generating station and 400kV/220kV Damarcherla SS.	1. 400kV Yadadri TPS Damarcherla line-1&2 2. 400kV/220kV Damarcherla ICT-1&2 3. 220kV Damarcherla Miryalaguda line-1&2
6	GD-1	Tamil Nadu	10-Jun-23 17:22	10-Jun-23 17:36	14mins	0	200	0.00%	0.43%	47635	46037	Complete Outage of 230kV/110kV/11kV Kadaperi SS of TANTRANSCO: 230kV/110kV/11kV Kadaperi SS was operating with single bus at 230kV level. As per the reports submitted, the triggering incident was B-N fault in 110kV Kadaperi SP Koil feeder and the fault was not cleared at Kadaperi end. Subsequently, remote ends of all 230kV lines connected to 230kV/110kV/11kV Kadaperi SS cleared the fault on the operation of DEF protection. Tripping of all 230kV lines resulted in a complete outage of 230kV/110kV/11kV Kadaperi SS.	1. 230kV Kadaperi Kalivendapattu 2. 230kV Kadaperi Sriperumbudur line-1&2 3. 230kV Kadaperi Alandur 4. 230kV Kadaperi Porur 5. 230kV/110kV Kadaeri Auto transformer-1,2&3
7	GD-1	Karnataka	11-Jun-23 11:53	11-Jun-23 19:53	8hrs	830	0	1.65%	0.00%	50232	47451	Complete Outage of 400kV YTPS Generating Station of KPCL: During antecedent conditions, 400kV BPS YTPS line-1 was under LC. As per the reports submitted, the triggering incident was YB fault in 400kV YTPS BPS line-2. Tripping of the only connected line resulted in complete outage of 400kV YTPS generating station.	1. 400kV YTPS BPS line-2

20.Details of Grid Events during the Month of June 2023
Southern Region



Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid		Brief details of the event (pre fault and post fault system conditions)	Name of Elements (Tripped/Manually opened)
	(GI for 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
8	GD-1	Tamil Nadu	11-Jun-23 11:49	11-Jun-23 12:32	43mins	35	47	0.07%	0.10%	50236	47454	Complete Outage of 230kV/110kV/22kV Karaikudi_TN of TANTRANSCO: During antecedent conditions, all elements were connected to 230kV Bus-1 at 230kV/110kV/22kV Karaikudi_TN. As per the reports submitted, the triggering incident was an R-phase Bus side jumper cut between 230kV Karaikudi_TN Kavanur line-2 and 230kV Karaikudi_TN Karaikudi_PG line-2 at 230kV Karaikudi_TN end. Immediately, 230kV Bus-1 BBP operated and all the elements connected to the bus tripped. This resulted in a complete outage of 230kV/110kV/22kV Karaikudi_TN SS.	1. 230kV Karaikudi_TN Karaikudi_PG line-1&2 2. 230kV Karaikudi_TN Kavanur line-1,2,3&4 3. 230kV Karaikudi_TN Valuthur 4. 230kV Karaikudi_TN NT Kudy Line-1 4. 230kV/110kV Karaikudi_TN Transformer-1,2&3
9	GD-1	Karnataka	12-Jun-23 18:20	12-Jun-23 19:26	1hr 6mins	0	163	0.00%	0.35%	41479	46021	Complete Outage of 220kV/66kV Exora SS, 220kV/66kV Sarjapur SS and 220kV/66kV Vikas Tech Park SS of KPTCL : As per the reports submitted, the triggering incident was R-N fault in 220kV Hoody Malur line. Since the line is radially feeding 220kV/66kV Exora SS, 220kV/66kV Sarjapur SS and 220kV/66kV Vikas Tech park SS , tripping of this line resulted in complete outage of 220kV/66kV Exora SS, 220kV/66kV Sarjapur SS and 220kV/66kV Vikas Tech Park SS.	1. 220kV Hoody Malur
10	GD-1	Tamil Nadu	16-Jun-23 14:48	16-Jun-23 15:25	37mins	0	100	0.00%	0.17%	54400	57672	Complete Outage of 230kV/110kV Acharapakkam SS of TANTRANSCO: As per the reports submitted, the triggering incident was B-N fault in 230kV Acharapakkam Villupuram line. Subsequently, 230kV Acharapakkam Maps line tripped on over loading at MAPS end. Tripping of both lines resulted in complete outage of 230kV/110kV Acharapakkam SS.	1. 230kV Acharapakkam Villupuram 2. 230kV Acharapakkam MAPS
11	GI-2	Tamil Nadu	03-Jun-23 15:02	03-Jun-23 16:56	1hr 54mins	0	0	0.00%	0.00%	51769	56162	Tripping of 400kV Bus-1 of 400kV/230kV/110kV SVChatram SS of TANTRANSCO: As per the reports submitted, the triggering incident was LBB maloperation in 400kV Pondy SV Chatram line at SV Chatram end causing all the Main CBs connected to Bus-1 to trip. At the same time, due to non-availability of Tie CB, DT was sent to remote ends of 400kV Alamythy SVChatram Line-2 and 400kV NCTPS SV Chatram Line-2 and both these lines tripped.	1. 400kV Alamythy SV Chatram Line-2 2. 400kV NCTPS SV Chatram Line-2
12	GI-1	Tamil Nadu	05-Jun-23 17:53	05-Jun-23 18:23	30mins	275	0	0.63%	0.00%	43486	48350	Tripping of 230kV Bus of 230kV/110kV Sanganeer SS of TANTARNSCO: 230kV/110kV Sanganeer SS is operating with single bus configuration at 230kV level. As per the reports submitted, the triggering incident was LBB operation at Sanganeer end while hand-tripping 230kV Kayathar Sanganeer. This resulted in tripping of all the elements connected to 230kV Bus. 110kV Bus was intact during the event.	1. 230kV Kayathar Sanganeer 2. 230kV Sanganeer SR Pudur 3. 230kV Sanganeer Udayathur 4. 230kV Sanganeer Abishegapatty 5. 230kV/110kV Sanganeer Transformer-1&2
13	GI-1	Karnataka	10-Jun-23 16:10	10-Jun-23 19:15	3 hrs 5 mins	0	0	0.00%	0.00%	51007	51245	Tripping of 220kV Bus-1 of 400kV/220kV Munirabad SS of PGCIL SR-1: During antecedent conditions, at 400kV/220kV Munirabad SS, main circuit breaker of 220kV Munirabad Lingapur line-2 was bypassed and the line was charged through Bus Coupler by connecting to 220kV Bus-1. At 16:10hrs, 220kV Munirabad Lingapur line-1 was hand tripped, and subsequently, 220kV Munirabad Lingapur line-2 tripped at Munirabad end as the Bus Coupler tripped on over current protection. Since this is the only line connected to Bus-1 at Munirabad, this resulted in the de-energization of 220kV Bus-1 of 400kV/220kV Munirabad SS.	1. 220kV Munirabad Lingapur line-1&2
14	GI-1	Andhra Pradesh	17-Jun-23 13:43	17-Jun-23 14:54	1hr 11mins	0	0	0.00%	0.00%	53795	54721	Tripping of 220kV Bus-2 of 220kV Vizag Switching Station of APTRANSCO: As per the reports submitted, the triggering incident was Y-N fault in 220kV Bus-2 at 220kV Vizag Switching Station. Immediately, 220kV Bus-2 BBP operated and all the elements connected to 220kV Bus-2 tripped.	1. 400kV/220kV Gajuwaka ICT-1&2 2. 220kV VSS MRS line-1&2 3. 220kV VSS Kalpakka line-2

20.Details of Grid Events during the Month of June 2023



Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(G1 or 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-1	Chandil	10.06.2023 17:00	16.06.2023 17:29	00:29	0	170	0.00%	0.71%	28176	23927	At 17:00 Hrs, 220 kV Ramchandrapur-Chandil tripped due to operation of LBB at Chandil S/s leading to total supply failure at Chandil S/s as 220 kV Ranchi-Chandil was under breakdown and 220 kV Santaldin-Chandil was switched off to limit loading of 220 kV Ramchandrapur-Chandil, which remained as the only source for Chandil. Around 170 MW load loss occurred at Chandil.	220 kV Ramchandrapur-Chandil
2	GD-1	Lapanga, OPGC	10.06.2023 17:27	10.06.2023 19:09	01:42	580	0	2.03%	0.00%	28542	24579	At 16:21 Hrs, 400 kV Meramundali-Lapanga-1 tripped due to Y_N fault. Subsequently, at 16:25 Hrs, 400 kV Meramundali-Lapanga-2 tripped due to R_B_N fault. While taking charging attempt of 400 kV Meramundali-Lapanga 1 at 17:27 Hrs, 400 kV Side of Lapanga S/s and 400 kV OPGC S/s became dead. U#4 at OPGC also tripped due to loss of evacuation path. Generation loss of around 585 MW occurred at OPGC.	400 kV Meramundali-Lapanga D/c 400 kV Lapanga-Sterlite D/c 400 kV Jharsuguda-OPGC D/c 400/220 kV ICT-1&2 at Lapanga 660MW U#4 at OPGC
3	GD-1	Atri, Narendrapur	16.06.2023 10:40	16.06.2023 11:11	00:31	0	244	0.00%	0.94%	30517	26051	At 10:02 Hrs, HVDC Talcher-Kolar Pole-1 blocked, leading to high loading of 400 kV TSTPP-Meramundali D/c and 400 kV Meramundali-Mendhasal D/c. To control loading of these lines, load reconfiguration was being done in downstream at Narendrapur and Atri. Load of Aska, New Aska and Purushottampur which were fed from Bhanjanagar was shifted to Narendrapur. Entire load of Narendrapur and Atri was put on single line i.e., 220 kV Therubali-Narendrapur. This line got overloaded and tripped, leading to total supply failure at Narendrapur and Atri S/s. Total 244 MW load loss occurred at Narendrapur and Atri.	220 kV Therubali-Narendrapur 220 kV Narendrapur-Atri D/c 220 kV Atri-Infocity 220/132 kV ATR-1&2 of Narendrapur 220/132 kV AR-1&2 at Atri 132 kV Atri-Samuka 132 kV Atri-Banki
4	GD-1	Teesta-3, Dikchu	28.06.2023 02:28	28.06.2023 02:56	00:28	1410	0	4.96%	0.00%	28420	21099	At 02:28 Hrs, Resistive fault struck 400 kV Rangpo-Teesta 3 and 400 kV Rangpo-Dikchu and both lines tripped. 400 kV Teesta 3-Dikchu also tripped at the same time. All six units at Teesta 3 and two units at Dikchu tripped leading to generation loss of around 1410 MW (Teesta 3: 1304 MW, Dikchu-106 MW)	400 kV Teesta 3-Dikchu 400 kV Rangpo-Dikchu 400 kV Teesta 3-Rangpo

20.Details of Grid Events during the Month of June 2023													
North-Eastern Region													
Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM:SS)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the		Antecedent Generation/Load in the Regional Grid		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(G1 1or 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD 1	Zuangtui, Saitual, Serchip, Vankal and Khawzawl areas of Mizoram Power System	06-Jun-23 00:10	06-Jun-23 00:53	00:43:00	0	21	0.00%	0.75%	1785	2811	Zuangtui, Saitual, Serchip, Vankal and Khawzawl areas of Mizoram Power System were connected with rest of NER grid through 132 kv Melriat(PG) -Zuangtui & 132 kv Zuangtui - Saitual lines. 132 kv Lunglei-Serchip line was under shutdown to avoid overloading of 132 kv Aizawl-Lungmual line. At 00:10 Hrs on 06.06.2023, 132 kv Melriat(PG) -Zuangtui & 132 kv Zuangtui - Saitual lines tripped. Due to tripping of these elements, Zuangtui, Saitual, Serchip, Vankal and Khawzawl areas of Mizoram Power System got separated from rest of NER Grid and subsequently collapsed due to no source available in these areas. Power supply was extended to Zuangtui, Saitual, Serchip, Vankal and Khawzawl areas of Mizoram Power System by charging 132 kv Melriat-Zuangtui line at 00:53 Hrs on 06.06.2023.	132 kv Melriat(PG) -Zuangtui & 132 kv Zuangtui - Saitual lines
2	GD 1	Zuangtui, Saitual, Serchip, Vankal and Khawzawl areas of Mizoram Power System	06-Jun-23 01:58	06-Jun-23 02:21	00:23:00	0	18	0.00%	0.62%	1767	2924	Zuangtui, Saitual, Serchip, Vankal and Khawzawl areas of Mizoram Power System were connected with rest of NER grid through 132 kv Melriat(PG) -Zuangtui line.132 kv Lunglei-Serchip line was under shutdown to avoid overloading of 132 kv Aizawl-Lungmual line. 132 kv Zuangtui - Saitual line was under tripped condition since 00:10 Hrs on 06.06.2023. At 01:58 Hrs on 06.06.2023, 132kv Melriat(PG)-Zuangtui line tripped. Due to tripping of this element, Zuangtui, Saitual, Serchip, Vankal and Khawzawl areas of Mizoram Power System got separated from rest of NER Grid and subsequently collapsed due to no source available in these areas. Power supply was extended to Zuangtui, Saitual, Serchip, Vankal and Khawzawl areas of Mizoram Power System by charging 132 kv Melriat-Zuangtui line at 02:21 Hrs on 06.06.2023	132 kv Melriat(PG) -Zuangtui line
3	GD 1	Zuangtui, Saitual, Serchip, Vankal and Khawzawl areas of Mizoram Power System	06-Jun-23 13:40	06-Jun-23 14:15	00:35:00	0	51	0.00%	1.70%	1707	3008	Zuangtui, Saitual, Serchip, Vankal and Khawzawl areas of Mizoram Power System were connected with rest of NER grid through 132 kv Melriat(PG) -Zuangtui line. 132 kv Lunglei-Serchip line was under shutdown to avoid overloading of 132 kv Aizawl-Lungmual line.132 kv Zuangtui - Saitual line was under tripped condition since 00:10 Hrs on 06.06.2023. At 13:40 Hrs on 06.06.2023, 132 kv Melriat(PG) -Zuangtui line tripped. Due to tripping of this element, Zuangtui, Saitual, Serchip, Vankal and Khawzawl areas of Mizoram Power System got separated from rest of NER Grid and subsequently collapsed due to no source available in these areas Power supply was extended to Zuangtui, Saitual, Serchip, Vankal and Khawzawl areas of Mizoram Power System by charging 132 kv Melriat-Zuangtui line at 14:15 Hrs on 06.06.2023	132 kv Melriat(PG) -Zuangtui line
4	GD 1	Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System	06-Jun-23 17:38	06-Jun-23 18:14	00:36:00	0	25	0.00%	0.82%	2217	3059	Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System were connected with rest of NER grid through 132 kv Balipara-Tenga line. At 17:38 Hrs on 06.06.2023, 132 kv Balipara-Tenga line tripped. Due to tripping of this element, Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System got separated from rest of NER Grid and subsequently collapsed due to no source available in these areas. Power supply was extended to Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System by charging 132 kv Balipara-Tenga line at 18:14 Hrs on 06.06.2023.	132 kv Balipara-Tenga line
5	GD 1	Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System	08-Jun-23 09:39	08-Jun-23 10:40	01:01:00	0	23	0.00%	0.78%	1857	2934	Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System were connected with rest of NER grid through 132 kv Balipara-Tenga line. At 09:39 Hrs on 08.06.2023, 132 kv Balipara-Tenga line tripped. Due to tripping of this element, Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System got separated from rest of NER Grid and subsequently collapsed due to no source available in these areas. 132 kv Balipara-Tenga line was declared faulty at 10:40 Hrs on 08.06.2023. Power supply was extended to Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System by charging 132 kv Balipara-Tenga line at 19:15 Hrs on 08.06.2023.	132 kv Balipara-Tenga line
6	GD 1	Lumshnong area of Meghalaya Power System	08-Jun-23 15:24	08-Jun-23 15:32	00:08	0	13	0%	0%	1850	2929	Lumshnong area of Meghalaya Power System was connected with rest of NER grid through 132 kv Khleihriat-Lumshnong line. 132 kv Lumshnong-Panchgram line was under planned shutdown since 05:12 Hrs on 08.06.2023. At 15:24 Hrs on 08.06.2023, 132 kv Khleihriat-Lumshnong line tripped. Due to tripping of this element, Lumshnong area of Meghalaya Power System got separated from rest of NER Grid and subsequently collapsed due to no source available in this area. Power supply was extended to Lumshnong area of Meghalaya Power System by charging 132 kv Khleihriat-Lumshnong line at 15:32 Hrs on 08.06.2023.	132 kv Khleihriat-Lumshnong line
7	GD 1	Lumshnong area of Meghalaya Power System	08-Jun-23 15:48	08-Jun-23 16:10	00:22	0	10	0%	0%	1826	2898	Lumshnong area of Meghalaya Power System was connected with rest of NER grid through 132 kv Khleihriat-Lumshnong line. 132 kv Lumshnong-Panchgram line was under planned shutdown since 05:12 Hrs on 08.06.2023. At 15:48 Hrs on 08.06.2023, 132 kv Khleihriat-Lumshnong line tripped. Due to tripping of this element, Lumshnong area of Meghalaya Power System got separated from rest of NER Grid and subsequently collapsed due to no source available in this area. Power supply was extended to Lumshnong area of Meghalaya Power System by charging 132 kv Khleihriat-Lumshnong line at 16:10 Hrs on 08.06.2023.	132 kv Khleihriat-Lumshnong line

20.Details of Grid Events during the Month of June 2023													
North-Eastern Region													
Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM:SS)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the		Antecedent Generation/Load in the Regional Grid		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(G1 1or 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
8	GD 1	Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System	08-Jun-23 21:55	08-Jun-23 22:47	00:52:00	0	16	0.00%	0.50%	2135	3169	Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System were connected with rest of NER grid through 132 kV Balipara-Tenga line. At 21:55 Hrs on 08.06.2023, 132 kV Balipara-Tenga line tripped. Due to tripping of this element, Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System got separated from rest of NER Grid and subsequently collapsed due to no source available in these areas. Power supply was extended to Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System by charging 132 kV Balipara-Tenga line at 22:47 Hrs on 08.06.2023.	132 kV Balipara-Tenga line
9	GD 1	Rokhia area of Tripura Power System	09-Jun-23 05:40	09-Jun-23 06:24	00:44:00	19	8	1.12%	0.33%	1701	2392	Rokhia area of Tripura Power System was connected with rest of NER grid through 132 kV Monarchak - Rokhia and 132 kV Rokhia -Agartala D/C lines. At 05:40 Hrs on 09.06.2023, 132 kV Monarchak - Rokhia and 132 kV Rokhia -Agartala D/C lines tripped. Due to tripping of these elements, Rokhia area of Tripura Power System got separated from rest of NER Grid and subsequently collapsed due to load generation mismatch in this area. Power supply was extended to Rokhia area of Tripura Power System by charging 132 kV Rokhia - Agartala 1 line at 06:24 Hrs on 09.06.2023.	132 kV Monarchak - Rokhia and 132 kV Rokhia -Agartala D/C lines
10	GD 1	Daporizo, Basar, Along, Pasighat, Roing, Tezu and Namsai areas of Arunachal Pradesh Power System	10-Jun-23 12:02	10-Jun-23 13:04	01:02:00	0	22	0.00%	0.88%	1748	2503	Daporizo, Basar, Along, Pasighat, Roing, Tezu and Namsai areas of Arunachal Pradesh Power System were connected with the rest of NER Grid through 132 kV Daporijo - Ziro line. At 12:02 Hrs on 10.06.2023, 132 kV Daporijo - Ziro Line tripped. Due to tripping of this element, Daporizo, Basar, Along, Pasighat, Roing, Tezu and Namsai areas of Arunachal Pradesh Power System got separated from the rest of NER Grid and subsequently collapsed due to no source available in these areas. Power supply was extended to the Daporizo, Basar, Along, Pasighat, Roing, Tezu and Namsai areas of Arunachal Pradesh Power System by charging 132 kV Daporijo - Ziro line at 13:04 Hrs on 10.06.23.	132 kV Daporijo - Ziro line
11	GD 1	New Umtru Generating Station of Meghalaya Power System	12-Jun-23 22:00	12-Jun-23 22:23	00:23:00	36	0	1.30%	0.00%	2759	3036	New Umtru Generating Station of Meghalaya Power System was connected with the rest of NER Grid through 132 kV EPIP II - New Umtru and 132 kV Umtru - New Umtru lines. At 22:00 Hrs on 12.06.2023, 132 kV EPIP II - New Umtru and 132 kV Umtru - New Umtru lines tripped. Due to tripping of these elements, New Umtru Generating Station of Meghalaya Power System got separated from rest of NER Grid and subsequently collapsed due to loss of evacuation path. Power supply was extended to New Umtru Generating Station of Meghalaya Power System by charging 132 kV EPIP II - New Umtru line at 22:23 Hrs on 12.06.2023.	132 kV EPIP II - New Umtru and 132 kV Umtru - New Umtru lines
12	GD 1	Leshka Generating Station of Meghalaya Power System	13-Jun-23 23:01	13-Jun-23 23:22	00:21	84	0	3%	0%	2941	2914	Leshka Generating Stations of Meghalaya Power System was connected with rest of NER grid through 132 kV Myntdu Leshka - Khleihriat D/C lines. At 23:01 Hrs on 13.06.2023, 132 kV Myntdu Leshka - Khleihriat D/C lines tripped. Due to tripping of these elements, Leshka Generating Stations of Meghalaya Power System got separated from rest of NER Grid and subsequently collapsed due to loss of evacuation path. Power supply was extended to Leshka Generating Station of Meghalaya Power System by charging 132 kV Myntdu Leshka - Khleihriat D/C lines at 23:22 Hrs on 13.06.2023.	132 kV Myntdu Leshka - Khleihriat D/C lines
13	GD 1	Leshka Generating Station of Meghalaya Power System	14-Jun-23 03:08	14-Jun-23 03:25	00:17	42	0	2%	0%	2623	2311	Leshka Generating Station of Meghalaya Power System was connected with rest of NER grid through 132 kV Myntdu Leshka - Khleihriat D/C lines. At 03:08 Hrs on 14.06.2023, 132 kV Myntdu Leshka - Khleihriat D/C lines tripped. Due to tripping of these elements, Leshka Generating Station of Meghalaya Power System got separated from rest of NER Grid and subsequently collapsed due to loss of evacuation path. Power supply was extended to Leshka Generating Station of Meghalaya Power System by charging 132 kV Myntdu Leshka - Khleihriat 1 line at 03:25 Hrs on 14.06.2023.	132 kV Myntdu Leshka - Khleihriat D/C lines
14	GD 1	Ningthoukhong, Churachandrapur and Thanlon areas of Manipur Power System	15-Jun-23 11:02	15-Jun-23 11:51	00:49	0	19	0%	1%	2281	1753	Ningthoukhong, Churachandrapur and Thanlon areas of Manipur Power System were connected with rest of NER grid through 132 kV Loktak - Ningthoukhong, 132 kV Imphal (PG) - Ningthoukhong and 132 kV Ningthoukhong - Churachandpur D/C lines. 132kV Kakching - Churachandpur and 132kV Elangkangpokpi - Churachandpur were under tripped condition since 12:21 Hrs on 08.06.2023. At 11:02 Hrs on 15.06.2023, 132 kV Loktak - Ningthoukhong, 132 kV Imphal (PG) - Ningthoukhong and 132 kV Ningthoukhong - Churachandpur D/C lines tripped. Due to tripping of these elements, Ningthoukhong, Churachandrapur and Thanlon areas of Manipur Power System got separated from rest of NER Grid and subsequently collapsed due to no source available in these areas. Power supply was extended to Ningthoukhong, Churachandrapur and Thanlon areas of Manipur Power System by charging 132 kV Imphal (PG) - Ningthoukhong line at 11:51 Hrs on 15.06.2023.	132 kV Loktak - Ningthoukhong, 132 kV Imphal (PG) - Ningthoukhong and 132 kV Ningthoukhong - Churachandpur D/C lines

20.Details of Grid Events during the Month of June 2023													
North-Eastern Region													
Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM:SS)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the		Antecedent Generation/Load in the Regional Grid		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(G1 1or 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
15	GD 1	Ningthoukhong, Churachandrapur and Thanlon areas of Manipur Power System	16-Jun-23 13:25	16-Jun-23 14:07	00:42	0	11	0%	1%	2878	1978	Ningthoukhong, Churachandrapur and Thanlon areas of Manipur Power System were connected with rest of NER grid through 132 kV Loktak - Ningthoukhong, 132 kV Imphal (PG) - Ningthoukong and 132 kV Ningthoukhong - Churachandpur 1 lines. 132 kV Kakching - Churachandpur and 132kV Elangkangpokpi - Churachandpur were under tripped condition since 12:21 Hrs on 08.06.2023. Also, 132 kV Ningthoukhong - Churachandpur 2 line was under outage since 11:02 Hrs on 15.06.2023 At 13:25 Hrs on 16.06.2023, 132 kV Loktak - Ningthoukhong, 132 kV Imphal (PG) - Ningthoukong and 132 kV Ningthoukhong - Churachandpur 1 lines tripped. Due to tripping of these elements, Ningthoukhong, Churachandrapur and Thanlon areas of Manipur Power System got separated from rest of NER Grid and subsequently collapsed due to no source available in these areas. Power supply was extended to Ningthoukhong, Churachandrapur and Thanlon areas of Manipur Power System by charging 132 kV Imphal (PG) - Ningthoukong line at 14:07 Hrs on 16.06.2023.	132 kV Loktak - Ningthoukhong, 132 kV Imphal (PG) - Ningthoukong and 132 kV Ningthoukhong - Churachandpur 1 lines
16	GD 1	Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System	17-Jun-23 07:07	17-Jun-23 08:01	00:54	16.7	32.7	1%	2%	2852	1676	Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System were connected with rest of NER grid through 132 kV Balipara-Tenga line. At 07:07 Hrs on 17.06.2023, 132 kV Balipara-Tenga line tripped. Due to tripping of this element, Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System got separated from rest of NER Grid and subsequently collapsed due to load generation mismatch in these areas. Power supply was extended to Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System by charging 132 kV Balipara-Tenga line at 08:01 Hrs on 17.06.2023.	132 kV Balipara-Tenga line
17	GD 1	Monarchak and Rabindranagar areas of Tripura Power System	18-Jun-23 07:02	18-Jun-23 08:02	01:00	60	3	2%	0%	2733	1804	Monarchak and Rabindranagar areas of Tripura Power System were connected with rest of NER grid through 132 kV Monarchak - Rokhia line. 132 kV Monarchak - Udaipur line was under Planned Shutdown from 06:49 Hrs on 18.06.2023. At 07:02 Hrs on 18.06.2023, 132 kV Monarchak - Rokhia line tripped. Due to tripping of this element, Monarchak and Rabindranagar areas of Tripura Power System got separated from rest of NER Grid and subsequently collapsed due to load generation mismatch in these areas. Power supply was extended to Monarchak and Rabindranagar areas of Tripura Power System by charging 132kV Monarchak-Udaipur line at 08:02 Hrs on 18.06.2023.	132 kV Monarchak - Rokhia line
18	GD 1	Panchgram area of Assam Power System	18-Jun-23 08:06	18-Jun-23 08:23	00:17	0	15	0%	1%	2612	1899	Panchgram area of Assam Power System was connected with rest of NER grid through 132 kV Lumshong - Panchgram, 132 kV Hallakandi - Panchgram and 132 kV Badarpur - Panchgram lines. 132 kV Srikona - Panchgram line was under outage due to tower collapse since 14.01.2019. At 08:06 Hrs on 18.06.2023, 132 kV Lumshong - Panchgram, 132 kV Hallakandi - Panchgram and 132 kV Badarpur - Panchgram lines tripped. Due to tripping of these elements, Panchgram area of Assam Power System got separated from rest of NER Grid and subsequently collapsed due to no source available in this area. Power supply was extended to Panchgram area of Assam Power System by charging 132 kV Hallakandi - Panchgram line at 08:23 Hrs on 18.06.2023.	132 kV Lumshong - Panchgram, 132 kV Hallakandi - Panchgram and 132 kV Badarpur - Panchgram lines
19	GD 1	Dhaligaon, Barpeta, Jogighopa, Gosaigaon, IOCL load and part load of Bornagar areas of Assam Power System	18-Jun-23 12:29	18-Jun-23 12:35	00:06	0	55	0%	3%	2600	1867	Dhaligaon, Barpeta, Jogighopa, Gosaigaon, IOCL load and part load of Bornagar areas of Assam Power System were connected with rest of NER grid through 132 kV BTPS - Dhaligaon D/C lines. 132 kV Nalbari-Barpeta line was under shutdown to avoid overloading of 132 kV BTPS-Dhaligaon D/C lines and 132 kV Gosaigaon - Gauripur line was under shutdown to avoid overloading of 132 kV BTPS - Kokrajhar D/C lines. At 12:29 Hrs on 18.06.2023, 132 kV BTPS - Dhaligaon D/C lines tripped. Due to tripping of these elements, Dhaligaon, Barpeta, Jogighopa, Gosaigaon, IOCL load and part load of Bornagar areas of Assam Power System got separated from rest of NER Grid and subsequently collapsed due to no source available in these areas. Power supply was extended to Dhaligaon, Barpeta, Jogighopa, Gosaigaon, IOCL load and part load of Bornagar areas of Assam Power System by charging 132 kV BTPS - Dhaligaon 1 line at 12:35 Hrs on 18.06.2023.	132 kV BTPS - Dhaligaon D/C lines
20	GD 1	Panchgram area of Assam Power System	18-Jun-23 13:00	18-Jun-23 13:23	00:23	0	18	0%	1%	2633	1768	Panchgram area of Assam Power System was connected with rest of NER grid through 132 kV Lumshong - Panchgram and 132 kV Hallakandi - Panchgram lines. 132 kV Badarpur-Panchgram line was under planned shutdown for installation, wiring, testing of distance relay. 132 kV Srikona - Panchgram was under outage due to tower collapse since 14.01.2019. At 13:00 Hrs on 18.06.2023, 132 kV Lumshong - Panchgram and 132 kV Hallakandi - Panchgram lines tripped. Due to tripping of these elements, Panchgram area of Assam Power System got separated from rest of NER Grid and subsequently collapsed due to no source available in this area. Power supply was extended to Panchgram area of Assam Power System by charging 132 kV Hallakandi - Panchgram line at 13:23 Hrs on 18.06.2023.	132 kV Lumshong - Panchgram and 132 kV Hallakandi - Panchgram lines

20.Details of Grid Events during the Month of June 2023

North-Eastern Region



Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM:SS)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the		Antecedent Generation/Load in the Regional Grid		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(G1 for 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
21	GD 1	Dhaligaon, Barpeta, Jogighopa, IOCL load and part load of Bornagar areas of Assam Power System	20-Jun-23 22:37	20-Jun-23 22:42	00:05	0	56	0%	2%	3058	2285	Dhaligaon, Barpeta, Jogighopa, IOCL load and part load of Bornagar areas of Assam Power System were connected with rest of NER grid through 132 kv BTPS - Dhaligaon D/C lines. 132 kv Nalbari-Barpeta line was under shutdown to avoid overloading of 132 kv BTPS - Dhaligaon D/C lines. 132 kv Gosaigaon - Dhaligaon line was under shutdown to avoid overloading of 132 kv BTPS - Kokrajhar D/C lines. At 22:37 Hrs on 20.06.2023, 132 kv BTPS - Dhaligaon D/C lines tripped. Due to tripping of these elements, Dhaligaon, Barpeta, Jogighopa, IOCL load and part load of Bornagar areas of Assam Power System got separated from rest of NER Grid and subsequently collapsed due to no source available in these areas. Power supply was extended to Dhaligaon, Barpeta, Jogighopa, IOCL load and part load of Bornagar areas of Assam Power System by charging 132 kv BTPS - Dhaligaon 1 line at 22:42 Hrs on 20.06.2023.	132 kv BTPS - Dhaligaon D/C lines
22	GD 1	Rangia, Kamalpur, Amingaon, Nalbari, part load of Sishugram, and part load of Bornagar areas of Assam Power System	21-Jun-23 04:59	21-Jun-23 05:29	00:30	0	68	0%	4%	3054	1711	Rangia, Kamalpur, Amingaon, Nalbari, part load of Sishugram, and part load of Bornagar areas of Assam Power System were connected with rest of NER grid through 220 kv Rangia - BTPS 1 & 132 kv Rangia-Motonga lines. 220kv Rangia - BTPS 2 line was declared faulty. 132 kv Rangia - Sipajhar, 132kv Rangia - Tanga and 132kv Amingaon - AIMS lines were under shutdown to avoid overloading of 220kv Rangia - BTPS D/C lines. 132 kv Nalbari - Barpeta was under shutdown to avoid overloading of 132 kv BTPS - Dhaligaon D/C lines. At 04:59 Hrs on 21.06.2023, 220 kv Rangia - BTPS 1 & 132 kv Rangia-Motonga lines tripped. Due to tripping of these elements, Rangia, Kamalpur, Amingaon, Nalbari, part load of Sishugram, and part load of Bornagar areas of Assam Power System got separated from rest of NER Grid and subsequently collapsed due to no source available in these areas. Power supply was extended to Rangia, Kamalpur, Amingaon, Nalbari, part load of Sishugram, and part load of Bornagar areas of Assam Power System by charging 132 kv Rangia-Motonga line at 05:29 Hrs on 21.06.2023.	220 kv Rangia - BTPS 1 & 132 kv Rangia-Motonga lines
23	GD 1	Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System	21-Jun-23 13:46	21-Jun-23 14:33	00:47	17	23	1%	1%	2622	2285	Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System were connected with rest of NER grid through 132 kv Balipara - Tenga line. At 13:46 Hrs on 21.06.2023, 132 kv Balipara - Tenga line tripped. Due to tripping of this element, Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System got separated from rest of NER Grid and subsequently collapsed due to load generation mismatch in these areas. 132 kv Balipara - Tenga line was declared faulty at 14:33 Hrs on 21.06.2023. Power supply was extended to Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System by charging 132 kv Balipara - Tenga line at 21:41 Hrs on 21.06.2023.	132 kv Balipara - Tenga line
24	GD 1	Dhaligaon, Barpeta, Jogighopa,Gossalgaon, IOCL load, Bornagar and Nalbari areas of Assam Power System	21-Jun-23 21:06	21-Jun-23 21:12	00:06	0	135	0%	5%	3165	2833	Dhaligaon, Barpeta, Jogighopa,Gossalgaon, IOCL load, Bornagar and Nalbari areas of Assam Power System were connected with rest of NER grid through 132 kv BTPS - Dhaligaon D/C lines. 220 kv Rangia - BTPS D/C lines were under outage due to tower collapse at loc.no. 452. 132 kv Rangia-Nalbari, 132kv Rangia - Bornagar and 132kv Gossalgaon-Gauripur lines were under shutdown to avoid overloading of 132 kv BTPS-Dhaligaon D/C lines. At 21:06 Hrs on 21.06.2023, 132 kv BTPS - Dhaligaon D/C lines tripped. Due to tripping of these elements, Dhaligaon, Barpeta, Jogighopa,Gossalgaon, IOCL load, Bornagar and Nalbari areas of Assam Power System got separated from rest of NER Grid and subsequently collapsed due to no source available in these areas. Power supply was extended to Dhaligaon, Barpeta, Jogighopa,Gossalgaon, IOCL load, Bornagar and Nalbari areas of Assam Power System by charging 132 kv BTPS-Dhaligaon 1 line at 21:12 Hrs on 21.06.2023.	132 kv BTPS - Dhaligaon D/C lines
25	GD 1	Dhaligaon, Barpeta, Jogighopa,Gossalgaon, IOCL load, Bornagar and Nalbari areas of Assam Power System	21-Jun-23 22:34	21-Jun-23 22:39	00:05	0	111	0%	4%	3150	2520	Dhaligaon, Barpeta, Jogighopa,Gossalgaon, IOCL load, Bornagar and Nalbari areas of Assam Power System were connected with rest of NER grid through 132 kv BTPS - Dhaligaon D/C lines. 220 kv Rangia - BTPS D/C lines were under outage due to tower collapse at loc.no. 452. 132 kv Rangia-Nalbari, 132kv Rangia - Bornagar and 132kv Gossalgaon-Gauripur lines were under shutdown to avoid overloading of 132 kv BTPS-Dhaligaon D/C lines. At 22:34 Hrs on 21.06.2023, 132 kv BTPS - Dhaligaon D/C lines tripped. Due to tripping of these elements, Dhaligaon, Barpeta, Jogighopa,Gossalgaon, IOCL load, Bornagar and Nalbari areas of Assam Power System got separated from rest of NER Grid and subsequently collapsed due to no source available in these areas. Power supply was extended to Dhaligaon, Barpeta, Jogighopa,Gossalgaon, IOCL load, Bornagar and Nalbari areas of Assam Power System by charging 132 kv BTPS - Dhaligaon 1 line at 22:39 Hrs on 21.06.2023.	132 kv BTPS - Dhaligaon D/C lines

20.Details of Grid Events during the Month of June 2023													
North-Eastern Region													
Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM:SS)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the		Antecedent Generation/Load in the Regional Grid		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(G1 to G2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
26	GD 1	400/220 kV Misa Substation and Smaguri areas of Assam Power System	22-Jun-23 23:04	22-Jun-23 23:45	00:41	0	62	0%	2%	3165	2526	400/220 kV Misa Substation and Smaguri areas of Assam Power System were connected with rest of NER grid through 400 kV New Mariani - Misa D/C, 400 kV Balipara - Misa D/C, 400 kV Silchar - Misa 2, 220 kV Misa - Dimapur D/C, 220 kV Misa - Byrnihat(Killing) D/C and 220 kV Misa- Samaguri D/C lines. 400 kV Silchar - Misa 1 line was under outage because it tripped on charging attempt after shut down return at 20:08 Hrs on 22.06.2023. At 23:04 Hrs on 22.06.2023, 400 kV New Mariani - Misa D/C, 400 kV Balipara - Misa D/C, 400 kV Silchar - Misa 2, 220 kV Misa - Dimapur D/C, 220 kV Misa - Byrnihat(Killing) D/C and 220 kV Misa-Samaguri D/C lines tripped. Due to tripping of these elements, 400/220 kV Misa Substation and Smaguri areas of Assam Power System got separated from rest of NER Grid and subsequently collapsed due to no source available in these areas. Power supply was extended to 400/220 kV Misa Substation and Smaguri areas of Assam Power System by charging 220 kV Dimapur - Misa line 2 at 00:45 Hrs on 23.06.2023.	400 kV New Mariani - Misa D/C, 400 kV Balipara - Misa D/C, 400 kV Silchar - Misa 2, 220 kV Misa - Dimapur D/C, 220 kV Misa - Byrnihat(Killing) D/C and 220 kV Misa- Samaguri D/C lines
27	GD 1	Rangia area of Assam Power System	25-Jun-23 02:16	25-Jun-23 02:40	00:24	0	21	0%	1%	2160	2707	Rangia area of Assam Power System was connected with rest of NER grid through 132 kV Rangia-Motonga line. 220 kV BTPS-Rangia D/C lines were under outage due to tower collapse at loc.no. 452. 132kV Rangia - Sipajhar & 132kV Rangia - Tanga lines were under shutdown to avoid overloading of 132 kV Sonabil-Ghoramari & 132 kV Sonabil-Depota lines. 132 kV Rangia-Kamalpur D/C lines were under shutdown to avoid overloading of 132 kV Kahilipara - AIIMS line. At 02:16 Hrs on 25.06.2023, 132 kV Rangia-Motonga line tripped. Due to tripping of this element, Rangia area of Assam Power System got separated from rest of NER Grid and subsequently collapsed due to no source available in this area. Power supply was extended to Rangia area of Assam Power System by charging 132 kV Tanga-Rangia line at 02:40 Hrs on 25.06.2023.	132 kV Rangia-Motonga line
28	GD 1	Rangia area of Assam Power System	25-Jun-23 11:50	25-Jun-23 11:55	00:05	0	21	0%	1%	2102	2584	Rangia area of Assam Power System was connected with rest of NER grid through 132 kV Rangia-Motonga line. 220 kV BTPS-Rangia D/C lines were under outage due to tower collapse at loc.no. 452. 132kV Rangia - Sipajhar & 132kV Rangia - Tanga lines were under shutdown to avoid overloading of 132 kV Sonabil-Ghoramari & 132 kV Sonabil-Depota lines. 132 kV Rangia-Kamalpur D/C lines were under shutdown to avoid low volatage at 132kV Rangia Substation. At 11:50 Hrs on 25.06.2023, 132 kV Rangia-Motonga line tripped. Due to tripping of this element, Rangia area of Assam Power System got separated from rest of NER Grid and subsequently collapsed due to no source available in this area. Power supply was extended to Rangia area of Assam Power System by charging 132 kV Rangia - Motanga line at 11:55 Hrs on 25.06.2023.	132 kV Rangia-Motonga line
29	GD 1	Rangia area of Assam Power System	25-Jun-23 14:37	25-Jun-23 14:48	00:11	0	21	0%	1%	2101	2650	Rangia area of Assam Power System was connected with rest of NER grid through 132 kV Rangia-Motonga line. 220 kV BTPS-Rangia D/C lines were under outage due to tower collapse at loc.no. 452. 132kV Rangia - Sipajhar & 132kV Rangia - Tanga lines were under shutdown to avoid overloading of 132 kV Sonabil-Ghoramari & 132 kV Sonabil-Depota lines. 132 kV Rangia-Kamalpur D/C lines were under shutdown to avoid overloading of 132 kV Kahilipara - AIIMS line. At 14:37 Hrs on 25.06.2023, 132 kV Rangia-Motonga line tripped. Due to tripping of this element, Rangia area of Assam Power System got separated from rest of NER Grid and subsequently collapsed due to no source available in this area. Power supply was extended to Rangia area of Assam Power System by charging 132 kV Rangia - Tanga line at 14:48 Hrs on 25.06.2023.	132 kV Rangia-Motonga line
30	GD 1	Meluri & Kiphire areas of Nagaland Power System	26-Jun-23 10:24	26-Jun-23 10:53	00:29	15	4	1%	0%	2409	2657	Meluri & Kiphire areas of Nagaland Power System were connected with rest of NER grid through 132 kV Kohima-Meluri line. At 10:24 Hrs on 26.06.2023, 132 kV Kohima-Meluri line tripped. Due to tripping of this element, Meluri & Kiphire areas of Nagaland Power System got separated from rest of NER Grid and subsequently collapsed due to load generation mismatch in these areas. Power supply was extended to Meluri & Kiphire areas of Nagaland Power System by charging 132 kV Kohima-Meluri line at 10:53 Hrs on 26.06.2023.	132 kV Kohima-Meluri line
31	GD 1	Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System	27-Jun-23 03:52	27-Jun-23 04:30	00:38	7.8	18.8	0%	1%	2349	2424	Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System were connected with rest of NER grid through 132 kV Balipara - Tenga line. At 03:52 Hrs on 27.06.2023, 132 kV Balipara - Tenga line tripped. Due to tripping of this element, Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System got separated from rest of NER Grid and subsequently collapsed due to load generation mismatch in these areas. Power supply was extended to Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System by charging 132 kV Balipara - Tenga line at 04:30 Hrs on 27.06.2023.	132 kV Balipara - Tenga line

20.Details of Grid Events during the Month of June 2023														
North-Eastern Region														
Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM:SS)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the		Antecedent Generation/Load in the Regional Grid		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped	
	(G1 1or 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)			
32	GD 1	Churachandrapur and Thanlon areas of Manipur Power System	28-Jun-23 19:03	28-Jun-23 19:57	00:54	0	10	0%	0%	2658	3230	Churachandrapur and Thanlon areas of Manipur Power System was connected with rest of NER grid through 132 kV Ningthoukhong -Churachandpur 1 line. 132 kV Kakching - Churachandpur and 132kV Elangkangpokpi - Churachandpur lines were under outage since 12:21 Hrs on 08.06.2023. Also, 132 kV Ningthoukhong - Churachandpur 2 line was under outage since 11:02 Hrs on 15.06.2023. At 19:03 Hrs on 28.06.2023, 132 kV Ningthoukhong -Churachandpur 1 line tripped. Due to tripping of this element, Churachandrapur and Thanlon areas of Manipur Power System got separated from rest of NER Grid and subsequently collapsed due to no source available in these areas. Power supply was extended to Churachandrapur and Thanlon areas of Manipur Power System by charging 132 kV Ningthoukhong - Churachandpur 1 line at 19:57 Hrs on 28.06.2023.	132 kV Ningthoukhong - Churachandpur 1 line	

21. NEW ELEMENTS COMMISSIONED* IN JUNE 2023

COMMISSIONING OF NEW GENERATING UNITS

REGION	S.NO.	ENTITY	UNIT NAME / LOCATION	ADD. CAPACITY (MW)	UNIT NO.	INS. CAPACITY (MW)	DATE®
NR	1	TP SAURYA LIMITED (TPSL)	TP Saurya Limited (Solar)/Rajasthan	18.75	-	110	20-06-2023
WR	2	NPCL	KAPS III & IV(Nuclear)/Gujarat	700	I	700	30-06-2023
	3	MASAYA SOLAR ENERGY PVT. LTD	Masaya Solar Energy Pvt. Ltd(Solar)/Madhya Pradesh	150	I	150	21-06-2023
	4	TORRENT SOLARGEN LIMITED	Torrent Solargen Limited (Wind)/Gujarat	13.5	I	40.5	17-06-2023
	5	TORRENT SOLARGEN LIMITED	Torrent Solargen Limited (Wind)/Gujarat	16.2	I	56.7	22-06-2023
	6	SRIJAN ENERGY SYSTEM PRIVATE LTD.	Srijan Energy System Private Ltd.(Wind)/ Gujarat	24.3	I	116.1	03-06-2023
	7	SRIJAN ENERGY SYSTEM PRIVATE LTD.	Srijan Energy System Private Ltd.(Wind)/ Gujarat	16.2	I	132.3	04-06-2023
	8	SRIJAN ENERGY SYSTEM PRIVATE LTD.	Srijan Energy System Private Ltd.(Wind)/ Gujarat	13.5	I	145.8	09-06-2023
	9	SRIJAN ENERGY SYSTEM PRIVATE LTD.	Srijan Energy System Private Ltd.(Wind)/ Gujarat	2.7	I	148.5	17-06-2023
SR	10	NTPC	NTPC Gandhar (Solar)/ Gujarat	10	I	20	07-06-2023
	11	JSW RENEW TWO	JSW Renew Two(Wind)/Tamilnadu	13.5	-	129.6	06-06-2023

®RE (Solar & Wind generation added capacity FTC is in phases. Date mentioned is the date by which complete (Added) capacity

COMMISSIONING OF NEW ICTS

REGION	S.NO.	ENTITY	SUB-STATION	VOLTAGE (kV)	ICT NO.	CAPACITY (MVA)	DATE
NR	1	PGCIL	Sohawal	400/220/33	III	500	28-06-2023
SR	2	KPTCL	Kalburgi	400/220	I	500	14-06-2023

COMMISSIONING OF NEW TRANSMISSION LINES

REGION	S.NO.	ENTITY	LINE NAME	CKT NO.	VOLTAGE (kV)	DATE
NR	1	THDC	400kV Khurja STPP-Aligarh	I	400	03-06-2023
	2	THDC	400kV Khurja STPP -Aligarh	II	400	08-06-2023
	3	PBTSL	400kV Bikaner_2-Khetri	I	400	22-06-2023
	4	PBTSL	400kV Bikaner_2-Khetri	II	400	23-06-2023
	5	PBTSL	400kV Bikaner_2-Khetri	III	400	23-06-2023
	6	PBTSL	400kV Bikaner_2-Khetri	IV	400	23-06-2023
	7	PBTSL	400kV Khetri-Bhiwadi	I	400	25-06-2023
	8	PBTSL	400kV Khetri- Bhiwadi	II	400	25-06-2023
WR	9	GETCO	400 kV Kansari-Soja	III	400	01-06-2023
SR	10	KPTCL	400kV Kalaburgi - YTPS	I	400	14-06-2023
	11	WKTL	400kv Warangal_New - Warangal_Old	I	400	13-06-2023
	12	WKTL	400kv Warangal_New - Warangal_Old	II	400	13-06-2023
	13	TSTRANSCO	400kV Dindi - Yedula	II	400	16-06-2023
NER	14	AEGCL & POWERGRID	220 kV Balipara-Sonabil	II	220	14-06-2023

LILO OF TRANSMISSION LINES

REGION	S.NO.	ENTITY	LINE NAME (LILOed LINE)	LILO AT	VOLTAGE (kV)	DATE

COMMISSIONING OF BUS/LINE REACTORS

REGION	S.NO.	ENTITY	SUB-STATION / LINE (@SUB-STATION)	VOLTAGE (kV)	CAPACITY (MVAR)	DATE
NR	1	PBTSL	Bus Reactor-I@Bikaner_2	400	125	23-06-2023
	2	PBTSL	Bus Reactor-II@Bikaner_2	400	125	23-06-2023
	3	PBTSL	400KV Bikaner_2-Khetri Ckt-I @Bikaner_2	400	80	22-06-2023
	4	PBTSL	400KV Bikaner_2-Khetri Ckt-II @Bikaner_2	400	80	23-06-2023
	5	PBTSL	400KV Bikaner_2-Khetri Ckt-III @Bikaner_2	400	80	23-06-2023
	6	PBTSL	400KV Bikaner_2-Khetri Ckt-IV @Bikaner_2	400	80	23-06-2023
SR	7	KPTCL	Bus Reactor-I @Kalaburgi	420	125	20-06-2023

COMMISSIONING OF HVDC/FACTS DEVICE/SYSTEM

REGION	S.NO.	NAME	SUB-STATION / CONSTITUENT	RATINGS	VOLTAGE (kV)	DATE

*Includes first time charging (FTC) as well

22. Voltage Profile

विद्युत विभव रूपरेखा माह - जून 2023

VOLTAGE PROFILE - JUNE 2023

Date of reporting: 05-Jul-23

क्र.स. Sl. No.	क्षेत्र REGION	उपकेंद्र SUBSTATION	VOLTAGE < V(lower)* (V=380,728 kV)	V(lower) < VOLTAGE < V(upper)*	VOLTAGE > V(upper)* (V=420,800 kV)	Voltage Deviation Index (%age of time voltage is outside range)	Number of hours voltage was outside IEGC band during month	उच्चतम (कि.वो.) Maximum(kV)	निम्नतम(कि.वो.) Minimum(kV)	औसत (कि.वो.) Average(kV)
1	पूर्वी क्षेत्र ER	अंगुल ANGUL	0%	100%	0%	0%	0	797	751	774
2		दालिपली DARLIPALI	0%	100%	0%	0%	0	793	767	778
3		गया GAYA	0%	100%	0%	0%	0	782	743	761
4		जेरत JEERAT	0%	99%	1%	1%	4	806	733	770
5		झारसुगड़ा JHARSUGUDA	0%	100%	0%	0%	1	802	772	786
6		मिदनापुर MEDINIPUR	0%	100%	0%	0%	0	801	743	772
7		रांची RANCHI	0%	100%	0%	0%	0	797	760	781
8		सासाराम SASARAM	0%	100%	0%	0%	0	787	745	767
1	उत्तरी क्षेत्र NR	आगरा AGRA	0%	100%	0%	0%	0	801	747	778
2		आगरा (फतेहगढ़) AGRA (FATEHABAD)	0%	100%	0%	0%	0	791	733	768
3		अजमेर AJMER	0%	100%	0%	0%	2	805	755	780
4		अलीगढ़ ALIGARH	0%	100%	0%	0%	0	799	744	773
5		अनपरा सी ANPARA-C	0%	100%	0%	0%	0	776	748	764
6		अनपरा डी ANPARA-D	0%	100%	0%	0%	0	776	748	762
7		अन्ता ANTA	0%	99%	1%	1%	4	802	767	785
8		बलिया BALLIA	0%	100%	0%	0%	0	791	738	767
9		बारा BARA	0%	100%	0%	0%	0	785	761	773
10		भादला BHADLA	0%	100%	0%	0%	0	795	744	771
11		भादला-2 BHADLA-2	0%	100%	0%	0%	0	801	745	773
12		भिवानी BHIWANI	0%	100%	0%	0%	0	799	753	776
13		बिकानेर BIKANER	0%	100%	0%	0%	0	798	749	771
14		बरेली BAREILLY	0%	100%	0%	0%	3	806	743	772
15		चित्तौड़गढ़ CHITTORGARH	0%	99%	1%	1%	6	805	757	782
16		फतेहगढ़-2 FATEHGARH-2	0%	100%	0%	0%	0	797	741	770
17		फतेहपुर FATEHPUR	0%	100%	0%	0%	0	792	740	770
18		ग्रेटर नोएडा GREATER NOIDA	0%	100%	0%	0%	0	801	747	774
19		हापड़ HAPUR	0%	99%	1%	1%	5	809	734	769
21		झाटिकरा JHATIKARA	0%	100%	0%	0%	0	792	744	769
22		कानपुर जीआईएस KANPUR GIS	0%	100%	0%	0%	0	790	743	769
23		खेतरी KHETRI	0%	100%	0%	0%	0	796	742	770
24		कोटेश्वर KOTESHWAR	0%	100%	0%	0%	0	797	739	770
25		लालितपुर LALITPUR	0%	100%	0%	0%	0	773	744	757
26		लखनऊ LUCKNOW	0%	100%	0%	0%	0	795	741	767
27		मैनपुरी MAINPURI	0%	100%	0%	0%	0	801	749	778
28		मेरठ MEERUT	0%	100%	0%	0%	2	803	746	775
29		मोहा MOHA	0%	100%	0%	0%	0	803	739	767
30		ओबरा सी OBRA C	0%	100%	0%	0%	0	769	747	755
31		उरई ORAI	0%	99%	1%	1%	4	805	755	784
32		फागी PHAGI	0%	100%	0%	0%	0	801	754	780
33		उन्नाव UNNAO	0%	100%	0%	0%	0	785	729	760
34		वाराणसी VARANASI	0%	100%	0%	0%	0	791	749	771
1	पश्चिमी क्षेत्र WR	अकोला AKOLA	0%	100%	0%	0%	0	795	749	775
2		औरंगाबाद AURANGABAD	0%	99%	1%	1%	4	804	751	780
3		भोपाल (बीडीटीसीएल) BHOPAL (BDTCL)	0%	100%	0%	0%	0	794	747	774
4		भुज BHUJ	0%	100%	0%	0%	0	800	749	775
5		भुज-2 BHUJ-II	0%	100%	0%	0%	0	795	747	771
6		बिलासपुर BILASPUR	0%	100%	0%	0%	0	791	758	773
7		बिना BINA	0%	100%	0%	0%	0	799	760	780
8		बनारकाठा BANASKANTHA	0%	99%	1%	1%	4	806	760	783
9		चाण CHAMPA	0%	94%	6%	6%	43	810	765	786
10		धुले (बीडीटीसीएल) DHULE (BDTCL)	0%	0	100%	0%	0	797	747	776
11		धर्मजगढ़ DHARAMJAGARH	0%	0	100%	0%	0	786	760	772
12		रायपुर पूलिंग RAIPUR POOLING	0%	100%	0%	0%	0	798	770	783
13		एकतुनी EKTUNI	0%	100%	0%	0%	0	796	744	771
14		गदरवाड़ा GADARWARA	0%	100%	0%	0%	0	801	770	784
15		ग्वालियर GWALIOR	0%	100%	0%	0%	1	802	753	781
16		इंदौर INDORE	0%	100%	0%	0%	0	790	747	771
17		जबलपुर JABALPUR	0%	100%	0%	0%	1	802	765	785
18		खंडवा KHANDWA	0%	100%	0%	0%	0	791	749	773
19		कोरडी KORADI	0%	100%	0%	0%	0	786	751	768
20		लकाडिया LAKADIYA	0%	98%	2%	2%	11	809	752	784
21		रायगढ़ पूलिंग RAIGARH POOLING	0%	100%	0%	0%	0	800	769	787
22		पड़घे PADGHE	0%	99%	1%	1%	8	808	745	778
23		परली PARLI	0%	99%	1%	1%	8	806	749	782
24		पुणे PUNE	0%	99%	1%	1%	7	810	738	775
25		राजनन्दगांव RAJNANDGAON	0%	97%	3%	3%	24	808	709	790
26		सासन SASAN	0%	100%	0%	0%	0	789	762	775
27		सतना SATNA	0%	100%	0%	0%	0	789	763	779
28		सिवनी SEONI	0%	100%	0%	0%	0	801	760	779
29		सीपत SIPAT	0%	100%	0%	0%	0	793	761	774
30		सोलापुर SOLAPUR	0%	98%	2%	2%	13	806	752	784
31		तिरुठा TIRORA	0%	100%	0%	0%	0	778	752	765
32		तामना TAMNAR	0%	100%	0%	0%	0	799	773	786
33		वडोदरा VADODARA	0%	98%	2%	2%	11	805	745	782
34		विंध्याचल पूलिंग VINDHYACHAL PS	0%	100%	0%	0%	0	791	757	778
35	दक्षिणी क्षेत्र SR	वर्धा WARDHA	0%	99%	1%	1%	9	808	761	786
36		वरार वावरा WARORA	0%	100%	0%	0%	0	802	758	782
1		कडपा CUDDAPAH	0%	93%	7%	7%	49	815	758	785
2		चिल्कलरीपेट CHILAKALURIPETA	0%	99%	1%	1%	4	814	749	780
3		कुरुनल KURNOOL	0%	100%	0%	0%	0	797	748	775
4		महेश्वरम MAHESWARAM	0%	100%	0%	0%	2	802	744	776
5		निजामाबाद NIZAMABAD	0%	90%	10%	10%	74	810	755	789
6		नेल्लूर पूलिंग NELLORE PS	0%	100%	0%	0%	0	797	752	773
7	पूर्वोत्तर क्षेत्र NER	रायचूर RAICHUR	0%	100%	0%	0%	0	799	752	779
8		श्रीकाकुलम SRIKAKULAM	0%	98%	2%	2%	15	805	750	784
9		थिरुवल्लम THIRUVALEM	0%	99%	1%	1%	7	804	743	773
10		वेमगिरि VEMAGIRI	0%	97%	3%	3%	19	808	752	785
2		बिस्वनाथ चौराई BISWANATH CHARIALI (400 kV)	0%	100%	0%	0%	0	416	363	406
3		बोंगाईगांव BONGAIGAON (400 kV)	0%	100%	0%	0%	0	416	392	406
4		बोंगाईगांव टीपीएस BONGAIGAON TPS (400 kV)	0%	100%	0%	0%	0	418	401	409
5		इम्फाल IMPHAL (400 kV)	0%	100%	0%	0%	0	417	394	405
6		बर्निहाट BYRNHAT (400 kV)	0%	100%	0%	0%	0	419	400	410
7		कामेंग KAMENG (400 kV)	0%	100%	0%	0%	0	412	393	402
8		अज़ारा AZARA (400 kV)	0%	100%	0%	0%	0	400	387	396
9		मीसा MISA (400 kV)	0%	100%	0%	0%	0	415	393	403
10		न्यू मारियानी NEW MARIANI (400 kV)	0%	100%	0%	0%	0	419	387	406
11		न्यू कोहिमा NEW KOHIMA (400 kV)	0%	100%	0%	0%	0	420	393	406
12		पालाटाना PALATANA (400 kV)	0%	100%	0%	0%	0	416	399	407
13		पुर्वकंचनबारी PK BARI (400 kV)	0%	100%	0%	0%	0	415	379	404
14		रंगानादी RANGANADI (400 kV)	0%	100%	0%	0%	0	418	399	408
15		सिलचर SILCHAR (400 kV)	0%	100%	0%	0%	0	418	396	407
18		थोबाल THOUBAL (400 kV)	0%	100%	0%	0%	0	407	381	394

All listed stations are 765 kV stations unless otherwise mentioned
*Percentage is calculated w.r.t. Time of one month.

23.List of Outages of Elements monitored by NLDC for the month of June-2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
Inter Regional Elements										
1	+/- 500kV HVDC Talcher - Kolar Pole-I	HVDC	ER , SR	ER-I	MO	04-Jun-2023 20:45	To bring back Takcher-Kolar Pole-1 from un-defined state to defined state	04-Jun-2023 21:07	00:22:00	0
2	+/- 500kV HVDC Talcher - Kolar Pole-II	HVDC	ER , SR	POWERGRID	TS	06-Jun-2023 09:37	pole-2 got blocked, L3(B-Phase) Buchholz relay for main tank alarm, Transformer differential protection operation .	17-Jun-2023 05:59	260:22:00	1
3	+/- 500kV HVDC Talcher - Kolar Pole-I	HVDC	ER , SR	POWERGRID	SE	06-Jun-2023 20:39	for replacement of finger contact along with arm of disconnector switch.	07-Jun-2023 05:24	08:45:00	0
4	800kV HVDC AGRA-BNC Pole-I	HVDC	NR, NER	POWERGRID	MO	01-Jun-2023 00:00	Voltage Regulation	15-Jun-2023 15:23	351:23	0
5	+/- 800kV HVDC Champa - Kurukshetra Pole-I	HVDC	WR , NR	POWERGRID	SE	09-Jun-2023 08:45	Due to hot spot in converter transformer	09-Jun-2023 13:26	04:41:00	0
6	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-II	HVDC	WR , NR	Adani Trans Ind Ltd	SO	09-Jun-2023 18:49	for remove pachur roller arrangement which stuck during OPGW earth wire replacement work	09-Jun-2023 21:39	02:50:00	0
7	+/- 800kV HVDC Champa - Kurukshetra Pole-III	HVDC	WR , NR	POWERGRID	SE	10-Jun-2023 07:41	To attend hotspots in Pole-3 Converter Transformer	10-Jun-2023 12:32	04:51:00	0
8	+/- 800kV HVDC Raigarh - Pugalur Pole-III	HVDC	WR , SR	POWERGRID	MO	11-Jun-2023 02:36	Voltage Regulation	11-Jun-2023 05:53	03:17:00	0
9	+/- 800kV HVDC Raigarh - Pugalur Pole-IV	HVDC	WR , SR	POWERGRID	MO	11-Jun-2023 02:36	Voltage Regulation	11-Jun-2023 05:58	03:22:00	0
10	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-II	HVDC	WR , NR	Adani Trans Ind Ltd	TL	14-Jun-2023 14:50	Tripped on line fault, DC line fault location near Tower no. 65.	14-Jun-2023 19:00	04:10:00	1
11	800kV HVDC AGRA-BNC Pole-II	HVDC	NR, NER	POWERGRID	MO	15-Jun-2023 13:49	To change direction from BNC to Agra	19-Jun-2023 14:00	96:11:00	0
12	+/- 500kV HVDC Talcher - Kolar Pole-I	HVDC	ER , SR	POWERGRID	TS	16-Jun-2023 10:02	tripped due to disturbance in 220V DC supply	16-Jun-2023 10:40	00:38:00	1
13	+/- 205kV HVDC Bhadravati Pole-II	HVDC	WR , SR	POWERGRID	SE	16-Jun-2023 14:15	To attend oil leakage through neutral bushing of Pole-2 West Y Ph Converter transformer	17-Jun-2023 11:46	21:31:00	0
14	+/- 70kV HVDC Vindhyachal Pole-II	HVDC	NR , WR	POWERGRID	SE	16-Jun-2023 18:50	For transformer oil leakage arresting work.	17-Jun-2023 01:26	06:36:00	0
15	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-I	HVDC	WR , NR	Adani Trans Ind Ltd	MO	16-Jun-2023 19:11	Voltage Regulation	19-Jun-2023 22:08	74:57:00	0
16	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-I	HVDC	WR , NR	Adani Trans Ind Ltd	MO	20-Jun-2023 09:59	Blocked to reverse the power flow	20-Jun-2023 15:49	05:50:00	0
17	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-II	HVDC	WR , NR	Adani Trans Ind Ltd	MO	20-Jun-2023 10:06	Blocked to reverse the power flow	20-Jun-2023 15:40	05:34:00	1
18	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-I	HVDC	WR , NR	Adani Trans Ind Ltd	MO	20-Jun-2023 19:23	TO control APL-Varsana line loading	21-Jun-2023 09:45	14:22:00	0
19	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-II	HVDC	WR , NR	Adani Trans Ind Ltd	MO	20-Jun-2023 19:34	To control APL Varsana line loading	21-Jun-2023 13:34	18:00:00	1
20	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-II	HVDC	WR , NR	Adani Trans Ind Ltd	TS	21-Jun-2023 17:24	due to lightning strike in 400 KV Dhanonda Ckt-1 flashover observed in R phase Series Reactor, due to which 87 D1 operated	21-Jun-2023 19:50	02:26:00	2
21	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-I	HVDC	WR , NR	Adani Trans Ind Ltd	MO	21-Jun-2023 20:41	To reduce line loading of APL-varsana	24-Jun-2023 09:17	60:36:00	0
22	800kV HVDC AGRA-APD-BNC Line 2	HVDC	NR , ER	POWERGRID	SO	23-Jun-2023 11:39	Snapping of Conductor To rectify broken sub conductor dead end pad of Ckt-2 at tower no. 2845	23-Jun-2023 15:22	03:43:00	0
23	800kV HVDC AGRA-APD-BNC Line 2	HVDC	NR , ER	POWERGRID	SO	23-Jun-2023 11:39	Snapping of Conductor To rectify broken sub conductor dead end pad of Ckt-2 at tower no. 2845	23-Jun-2023 15:22	03:43:00	0
24	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-II	HVDC	WR , NR	Adani Trans Ind Ltd	SE	24-Jun-2023 09:50	ESD to remove traction machine arrangement which stuck during OPGW earth wire replacement work.	24-Jun-2023 14:27	04:37:00	2
25	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-II	HVDC	WR , NR	Adani Trans Ind Ltd	MO	24-Jun-2023 14:27	Blocked to reverse the power flow	24-Jun-2023 21:20	06:53:00	2
26	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-I	HVDC	WR , NR	Adani Trans Ind Ltd	MO	24-Jun-2023 15:43	Blocked to reverse the power flow	24-Jun-2023 21:26	05:43:00	0
27	+/- 70kV HVDC Vindhyachal Pole-II	HVDC	NR , WR	POWERGRID	SE	25-Jun-2023 01:20	to rectify "Valve winding GND fault 59ACVW DBLK INH".	25-Jun-2023 03:44	02:24:00	0
28	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-I	HVDC	WR , NR	Adani Trans Ind Ltd	MO	25-Jun-2023 04:40	Blocked to reverse the power flow	25-Jun-2023 10:52	06:12:00	0
29	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-II	HVDC	WR , NR	Adani Trans Ind Ltd	MO	25-Jun-2023 04:45	Blocked to reverse power flow from NR-WR	25-Jun-2023 11:03	06:18:00	2
30	+/- 800kV HVDC Champa - Kurukshetra Pole-I	HVDC	WR , NR	POWERGRID	MO	25-Jun-2023 13:15	Voltage Regulation	25-Jun-2023 22:52	09:37:00	0
31	+/- 800kV HVDC Champa - Kurukshetra Pole-II	HVDC	WR , NR	POWERGRID	MO	25-Jun-2023 13:15	Voltage Regulation	25-Jun-2023 21:58	08:43:00	0
32	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-I	HVDC	WR , NR	Adani Trans Ind Ltd	MO	25-Jun-2023 21:05	To control loading of APL Varsana	26-Jun-2023 09:30	12:25:00	0
33	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-II	HVDC	WR , NR	Adani Trans Ind Ltd	MO	25-Jun-2023 21:10	To control loading of APL Varsana	26-Jun-2023 09:22	12:12:00	2
34	+/- 800kV HVDC Raigarh - Pugalur Pole-III	HVDC	WR , SR	POWERGRID	TS	26-Jun-2023 10:09	Differential protection operation in convertor transformer	26-Jun-2023 11:27	01:18:00	1
35	+/- 205kV HVDC Bhadravati Pole-I	HVDC	WR , SR	POWERGRID	TS	26-Jun-2023 11:23	Blocked on DC>AC protection operation	26-Jun-2023 19:51	08:28:00	1
36	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-I	HVDC	WR , NR	Adani Trans Ind Ltd	MO	26-Jun-2023 18:35	to control the loading of 400KV APL-Varsana	27-Jun-2023 09:19	14:44:00	0
37	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-II	HVDC	WR , NR	Adani Trans Ind Ltd	MO	27-Jun-2023 03:35	to control the loading of 400KV APL-Varsana because of tripping of APL-Mansar	27-Jun-2023 10:30	06:55:00	2

23.List of Outages of Elements monitored by NLDC for the month of June-2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
38	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-I	HVDC	WR , NR	Adani Trans Ind Ltd	MO	27-Jun-2023 18:52	power regulation	28-Jun-2023 07:18	12:26:00	0
39	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-II	HVDC	WR , NR	Adani Trans Ind Ltd	MO	27-Jun-2023 18:56	Power Regulation	28-Jun-2023 07:18	12:22:00	2
40	800KV BNC-ALIPURDUAR-2	HVDC	ER , NER	POWERGRID	SO	28-Jun-2023 12:46	for trimming the tree in between the spam 780 to 781 .	28-Jun-2023 17:24	04:38:00	0
41	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-I	HVDC	WR , NR	Adani Trans Ind Ltd	MO	28-Jun-2023 16:26	SUO MOTO outage	29-Jun-2023 07:34	15:08:00	0
42	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-II	HVDC	WR , NR	Adani Trans Ind Ltd	MO	28-Jun-2023 16:31	SUO MOTO Outage	29-Jun-2023 07:34	15:03:00	2
43	800KV HVDC AGRA- ALIPURDUAR-IV	HVDC	ER , NR	POWERGRID	MO	01-Jun-2023 00:00	Voltage Regulation	16-Jun-2023 17:46	377:46:00	0
44	800KV HVDC AGRA- ALIPURDUAR-III	HVDC	ER , NR	POWERGRID	MO	01-Jun-2023 00:00	Voltage Regulation	16-Jun-2023 11:49	371:49:00	0
45	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-II	HVDC	WR , NR	Adani Trans Ind Ltd	TL	30-Jun-2023 12:26	Tripped on DC line fault	30-Jun-2023 15:46	03:20:00	3
46	400kV Binaguri - Bongaigaon Ckt-II	Line	ER , NER	POWERGRID	SO	01-Jun-2023 00:00	Re- Conductoring work under NERSS - XII	08-Jun-2023 16:30	184:30:00	0
47	220kV Ponda - Ambewadi Ckt-I	Line	WR , SR	GOA/KPTCL	TL	01-Jun-2023 06:50	B-N Fault	01-Jun-2023 10:15	03:25:00	1
48	220kV Xeldom - Ambewadi Ckt-I	Line	WR , SR	GOA/KPTCL	TL	01-Jun-2023 06:50	B-N Fault	01-Jun-2023 10:10	03:20:00	1
49	765kV Angul - Srikaulam Ckt-II	Line	ER , SR	POWERGRID	SO	01-Jun-2023 07:57	for repositioning of Piolet String and Jumper clearance rectification works at tower location no 487.	01-Jun-2023 17:38	09:41:00	0
50	400KV-SHUJALPUR-RAPP-1	Line	WR , NR	BDTCL-Sterlite	SO	02-Jun-2023 09:58	FOR AMP WORK	03-Jun-2023 01:05	15:07:00	0
51	400KV-SHUJALPUR-RAPP-1	Line	WR , NR	BDTCL-Sterlite	SO	02-Jun-2023 09:58	FOR AMP WORK	02-Jun-2023 20:13	10:15:00	0
52	400KV-SHUJALPUR-RAPP-2	Line	WR , NR	BDTCL-Sterlite	SO	03-Jun-2023 09:46	FOR AMP WORK	03-Jun-2023 20:25	10:39:00	0
53	220kV Raigarh - Budhipadar Ckt-I	Line	WR , ER	POWERGRID/GRI DCO	TL	03-Jun-2023 12:44	Auto- reclosure operated from Budhipadar end and Breaker tripped at Raigarh end	03-Jun-2023 15:28	02:44:00	1
54	765KV-SATNA-ORAI-1	Line	WR , NR	POWERGRID	SO	04-Jun-2023 07:35	For Switching of Spare with Y-Ph (For taking Y-Ph in Service) at Satna end. Due date 24.06.23. Dia to be kept open at both ends.	04-Jun-2023 13:33	05:58:00	0
55	765KV-SATNA-ORAI-1	Line	WR , NR	POWERGRID	SO	04-Jun-2023 07:35	For Switching of Spare with Y-Ph (For taking Y-Ph in Service) at Satna end. Due date 24.06.23. Dia to be kept open at both ends.	04-Jun-2023 18:00	10:25:00	0
56	400kV Raigarh - Jharsuguda Ckt-IV	Line	WR , ER	POWERGRID	TL	04-Jun-2023 16:06	R-N,M1,Z1,4.75 KA, 73.8 KM M2,Z1, R-N,4.72 KA, 73.81 KM	04-Jun-2023 17:58	01:52:00	1
57	400kV Raigarh - Jharsuguda Ckt-III	Line	WR , ER	POWERGRID	TL	04-Jun-2023 16:11	B-N,M1,Z1,4.95 KA, 70 KM M2,Z1, B-N,4.96 KA, 72.7 KM	04-Jun-2023 17:46	01:35:00	1
58	765kV Satna - Orai Ckt-I	Line	WR , NR	POWERGRID	MO	04-Jun-2023 18:46	Voltage Regulation	04-Jun-2023 23:23	04:37:00	0
59	765KV-SOLAPUR-RAICHUR-2	Line	WR , SR	POWERGRID WR1	SO	06-Jun-2023 07:27	Line terminal equipments AMP at 765kV Solapur Substation	06-Jun-2023 17:52	10:25:00	0
60	220kV New Karamnasa - Sahupuri	Line	ER , NR	UPPCL/BSPHCL	SO	06-Jun-2023 09:00	removing the defect for uninterrupted supply.	06-Jun-2023 12:33	03:33:00	0
61	400KV-JHARSUGUDA-RAIGARH-2	Line	ER , WR	PG (ODISHA PROJECT)	SO	06-Jun-2023 09:32	Rectification of damage Bottom conductor between Location 466-467	06-Jun-2023 20:15	10:43:00	0
62	220kV Xeldom - Ambewadi Ckt-I	Line	WR , SR	GOA/KPTCL	TL	06-Jun-2023 14:49	relay indication from xeldom end Zone: None, Trip: A, B, C; Ia: 400.1A, Ib: 350.1A, Ic: 527.7A	06-Jun-2023 15:34	00:45:00	2
63	765 KV CHITTORGARH-BANASKANTHA (PG) CKT-2	Line	NR , WR	POWERGRID	SO	06-Jun-2023 17:11	Switching of spare reactor with B Phase LR.	06-Jun-2023 22:07	04:56:00	0
64	132kV Rihand - Garwah Ckt-I	Line	ER , NR	UPPCL/ISEB	SE	07-Jun-2023 10:50	Due to safety reasons above two lines were hand trip	07-Jun-2023 12:21	01:31:00	0
65	132kV Rihand - Nagar Untari Ckt-I	Line	ER , NR	UPPCL/ISEB	SE	07-Jun-2023 10:50	Due to safety reasons above two lines were hand trip	07-Jun-2023 12:08	01:18:00	0
66	220kV Raigarh - Budhipadar Ckt-I	Line	WR , ER	POWERGRID/GRI DCO	SO	08-Jun-2023 10:25	Tree trimming at loc no.40-45, 77 to 87, 105 to 109 of the line	08-Jun-2023 15:43	05:18:00	1
67	220KV-BUDHIPADAR-KORBA-1	Line	ER , WR	GRIDCO	SO	09-Jun-2023 10:15	Tree trimming at loc no.40-45, 77 to 87, 105 to 109 of the line	09-Jun-2023 17:34	07:19:00	0
68	765kV Gwalior - Agra Ckt-II	Line	WR , NR	POWERGRID	TL	09-Jun-2023 14:08	FAULT CURRENT: LOCATION: 45km from Agra, 7.6KA	09-Jun-2023 14:42	00:34:00	1
69	400 KV BALIA(PG)-NAUBATPUR (BS) (PG) CKT-1	Line	NR , ER	POWERGRID	SO	10-Jun-2023 09:08	For fixing of aviation globule for OPGW erection work under Strengthening of OPGW Network in ER Project. A/R OFF on CKT 2 to facilitate S/D works on CKT 1	10-Jun-2023 19:50	10:42:00	0
70	220kV Ponda - Ambewadi Ckt-I	Line	WR , SR	GOA/KPTCL	TL	10-Jun-2023 12:48	tripped from Ambewadi end on Zone 1, A-B-C TO N Phase, Ambewadi End: Dist: 37.1 kms, Fault Current :IA=3.45KA,IB=3.98KA,IC=3.19KA	23-Jun-2023 21:16	320:28:00	2
71	220kV Xeldom - Ambewadi Ckt-I	Line	WR , SR	GOA/KPTCL	TL	10-Jun-2023 12:59	tripped from Ambewadi end on Zone 1, A-B-C TO N Phase, Ambewadi End: Dist: 37.58 kms, Fault Current :IA=3.22KA,IB=3.56KA,IC=3.47KA .	10-Jun-2023 21:08	08:09:00	3
72	400 KV BALIA(PG)-NAUBATPUR (BS) (PG) CKT-1	Line	NR , ER	POWERGRID	SO	11-Jun-2023 07:15	For fixing of aviation globule for OPGW erection work under Strengthening of OPGW Network in ER Project. A/R OFF on CKT 2 to facilitate S/D works on CKT 1	11-Jun-2023 20:19	13:04:00	0
73	400kV Binaguri - Bongaigaon Ckt-II	Line	ER , NER	POWERGRID	SO	11-Jun-2023 12:19	Rectification of De-capped Pilot insulator string damaged due to lightning.	11-Jun-2023 18:28	06:09:00	0
74	400 KV BALIA(PG)-NAUBATPUR (BS) (PG) CKT-1	Line	NR , ER	POWERGRID	SO	12-Jun-2023 10:51	For fixing of aviation globule for OPGW erection work under Strengthening of OPGW Network in ER Project. A/R OFF on CKT 2 to facilitate S/D works on CKT 1	12-Jun-2023 20:35	09:44:00	0
75	220kV Xeldom - Ambewadi Ckt-I	Line	WR , SR	GOA/KPTCL	SO	13-Jun-2023 07:02	for pulling out an old 110kV (Supa-Goa line) tower that has been fallen on 220kv Ambewadi-Ponda (AP-2) line	13-Jun-2023 11:08	04:06:00	3

23.List of Outages of Elements monitored by NLDC for the month of June-2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
76	765kV Dharmjaygarh - New Ranchi Ckt-II	Line	WR , ER	POWERGRID	TL	13-Jun-2023 14:36	B-N FAULT, RANCHI end detail M1 FC-3.675KA,FD-137 M2-FC-3.683KA,FD-137.809KM	13-Jun-2023 17:31	02:55:00	1
77	765kV Dharmjaygarh - New Ranchi Ckt-II	Line	WR , ER	POWERGRID	MO	13-Jun-2023 17:31	Voltage Regulation	14-Jun-2023 10:44	17:13:00	1
78	765kV Durg - Jharsuguda Ckt-II	Line	WR , ER	POWERGRID	MO	14-Jun-2023 13:19	Voltage Regulation	20-Jun-2023 10:54	141:35:00	0
79	132kV Rihand - Nagar Untari Ckt-I	Line	ER , NR	UPPCL/JSEB	SO	18-Jun-2023 10:55	Isolator alignment issue . For rectification of R-phase line isolator mis-alignment at Nagar Untari(JS).	18-Jun-2023 16:34	05:39:00	0
80	765kV Gaya - Varanasi Ckt-I	Line	ER , NR	POWERGRID	TL	19-Jun-2023 18:10	R-N fault. Relay Data Gaya End: FD-114.2KM, FC-4.48KA Varanasi End: 133.5 Km & 5.928 KA	29-Jun-2023 01:12	223:02:00	1
81	220kV New Karamnasa - Sahupuri	Line	ER , NR	UPPCL/BSPHCL	TL	19-Jun-2023 20:33	The line tripped on Y phase trip in the main relay 2 and MTR 86 and the fault data are as follows Ir 534.4 A Iy- 596.2 A Ib- 567.6 A Vrn 126.9 kV Vyn 128.2 kV Vbn 126.9 kV Fault duration 25.67 s Relay trip time 80.09 ms	19-Jun-2023 21:40	01:07:00	1
82	400kV Zerda - Bhinmal Ckt-I	Line	WR , NR	GETCO/POWERGRID	SE	19-Jun-2023 22:50	to attend hotspot in 401 89L Line Side- B ph Temp =218 Deg at Bhinmal	20-Jun-2023 09:19	10:29:00	0
83	765kV Gwalior - Phagi Ckt-II	Line	NR , WR	POWERGRID NR	TL	20-Jun-2023 17:34	At phagi end :- B Phase PRD-2 operated At Gwalior End :- DT received	20-Jun-2023 22:59	05:25:00	1
84	400kV Raigarh - Jharsuguda Ckt-I	Line	WR , ER	POWERGRID	TL	20-Jun-2023 20:26	Y-B ground fault	20-Jun-2023 23:57	03:31:00	1
85	400kV Raigarh - Jharsuguda Ckt-II	Line	WR , ER	POWERGRID	TL	20-Jun-2023 20:26	Bph G fault,33.62 KA ,4.7 KM.	21-Jun-2023 00:08	03:42:00	1
86	400kV Zerda - Bhinmal Ckt-I	Line	WR , NR	GETCO/POWERGRID	SE	20-Jun-2023 22:04	Hot spot observed in 89 C Isolator of TBC bay at Zerda	21-Jun-2023 08:26	10:22:00	0
87	220kV Korba(East) - Budhipadar Ckt-I	Line	WR , ER	CSPTCL/GRIDCO	TL	20-Jun-2023 22:19	Korba End- FD:165.28 Km, R-ph, FC:1.07 kA, Z-2	21-Jun-2023 00:05	01:46:00	1
88	765kV Gaya - Varanasi Ckt-II	Line	ER , NR	POWERGRID	TL	21-Jun-2023 14:29	R Phase to Ground Fault FAULT CURRENT: 4.694 kA LOCATION: 114.113km (41.780%)	21-Jun-2023 15:11	00:42:00	1
89	132kV Rihand - Garwah Ckt-I	Line	ER , NR	UPPCL/JSEB	TL	21-Jun-2023 16:24	Relay Garhwa end Zone:- 1 PHASE:-B Dis.43.5km Ia:-0.21kA Ib:-0.40kA Ic:-0.29kA	21-Jun-2023 17:25	01:01:00	1
90	765 kV-JHARSUGUDA-RAIPUR PS (DURG)-I	Line	ER , WR	ER-I	MO	21-Jun-2023 19:17	Voltage Regulation	06-Jul-2023 03:56	344:39:00	0
91	400kV Patna - Balia Ckt-I	Line	ER , NR	POWERGRID	TL	21-Jun-2023 20:53	R-N Fault ;PATNA- 128.63 KM, 3.282 KA.	22-Jun-2023 07:09	10:16:00	1
92	132kV Rihand - Garwah Ckt-I	Line	ER , NR	UPPCL/JSEB	TL	22-Jun-2023 15:08	Y- phase, Z1, Distance- 21.1 km Ia=0.30 kA Ib= 0.53 kA Ic= 0.40 kA	22-Jun-2023 16:04	00:56:00	2
93	220kV Korba(East) - Budhipadar Ckt-I	Line	WR , ER	CSPTCL/GRIDCO	SO	22-Jun-2023 18:48	for removal of snapped earthwire from loc 01 to 05.	22-Jun-2023 22:55	04:07:00	1
94	132kV Rihand - Garwah Ckt-I	Line	ER , NR	UPPCL/JSEB	TL	22-Jun-2023 23:49	Phase to earth fault Y-N , Fault current 8.421kA from Rihand(UP)	23-Jun-2023 09:00	09:11:00	3
95	132kV Chandauli - Karmanasa Ckt-I	Line	ER , NR	UPPCL/BSPHCL	SO	22-Mar-2023 07:05	Line is kept charged from Karmanasa End only, will be charged from Chandauli as per requirement of UP.	06-Jun-2023 12:23	1829:18:00	0
96	765 kV-JHARSUGUDA-RAIPUR PS (DURG)-I	Line	ERLDC, WRLD	POWERGRID	MO	01-Jun-2023 00:00	Voltage Regulation	06-Jun-2023 12:51	132:51	0
97	220kV Xeldom - Ambewadi Ckt-I	Line	WR , SR	GOA/KPTCL	SO	23-Jun-2023 09:42	to attend the work of " replacement / repair of damaged conductor/tower of Ambewadi-Ponda line (AP-2) line between Loc No. 75 & 76 in Karnataka Jurisdiction	23-Jun-2023 21:12	11:30:00	3
98	220kV Xeldom - Ambewadi Ckt-I	Line	WR , SR	GOA/KPTCL	TL	25-Jun-2023 13:17	Ph C-N, Zone 1, Dist: 23kms, Fault current 4.17kA	25-Jun-2023 17:11	03:54:00	4
99	220kV Ponda - Ambewadi Ckt-I	Line	WR , SR	GOA/KPTCL	MO	25-Jun-2023 18:46	Line Idle charged from Ambewadi End	01-Jul-2023 00:00	125:14:00	2
100	132kV Rihand - Nagar Untari Ckt-I	Line	ER , NR	UPPCL/JSEB	TL	26-Jun-2023 19:09	Rihand :- R-n fault, Z-1, , 1.9KA, 45KM	26-Jun-2023 21:07	01:58:00	1
101	400KV-NAUBATPUR(BH)-BALIA-1	Line	ER , NR	ER-I	SO	28-Jun-2023 11:01	OPGW erection work under Strengthening of OPGW Network in ER Project	28-Jun-2023 15:02	04:01:00	0
102	132kV Rihand - Nagar Untari Ckt-I	Line	ER , NR	UPPCL/JSEB	TL	29-Jun-2023 02:26	132kV Rihand -Nagaruntari T/L ideally charged from Rihand end tripped at 02:26 hrs	29-Jun-2023 04:38	02:12:00	2
103	132kV Rihand - Garwah Ckt-I	Line	ER , NR	UPPCL/JSEB	TL	29-Jun-2023 03:46	Line tripped at 03:46 hrs from both end. The relay at Garhwa end are RY phase ,zone1 ,Distance 56.9 km IA=0.63kA IB=0.62kA IC=0.20kA	29-Jun-2023 06:30	02:44:00	4
104	765kV Naubatpur - Balia Ckt-I	Line	ER , NR	BPDC/POWER GRID	TL	29-Jun-2023 07:01	400KV Balia-Naubatpur-1 tripped at 07:01hrs due to Y-N fault, AFAS: FD=32.289km from Balia, FC=10.80KA	29-Jun-2023 08:03	01:02:00	1
105	765kV Naubatpur - Balia Ckt-I	Line	ER , NR	BPDC/POWER GRID	SO	29-Jun-2023 11:25	for polymer insulator replacement to avoid recurrence of fault	29-Jun-2023 16:05	04:40:00	1
106	765kV Gaya - Varanasi Ckt-I	Line	ER , NR	POWERGRID	SE	30-Jun-2023 12:09	To attend Hotspot detected in B-ph Line Isolator at Gaya end	30-Jun-2023 15:27	03:18:00	1
107	400KV-MUZAFFARPUR(PG)-GORAKHPUR-2	Line	ER , NR	ER-I	SO	15-Jun-2023 11:10	LBB RELAY RETROFITTING AT MUZAFFARPUR SS	15-Jun-2023 19:00	07:50:00	0
108	400KV-MUZAFFARPUR(PG)-GORAKHPUR-2	Line	ER , NR	ER-I	SO	20-Jun-2023 10:32	LBB RELAY RETROFITTING AT MUZAFFARPUR SS	20-Jun-2023 18:29	07:57:00	0
109	400KV-MUZAFFARPUR(PG)-GORAKHPUR-1	Line	ER , NR	ER-I	SO	21-Jun-2023 10:19	LBB RELAY RETROFITTING AT MUZAFFARPUR SS	21-Jun-2023 19:34	09:15:00	0
110	400KV-NAUBATPUR(BH)-BALIA-1	Line	ER , NR	ER-I	SO	27-Jun-2023 08:26	OPGW erection work under Strengthening of OPGW Network in ER Project	27-Jun-2023 19:50	11:24:00	0

23.List of Outages of Elements monitored by NLDC for the month of June-2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
Transnational Elements										
1	400kV Alipurduar - Jigmeling Ckt-II	Line	ER , BHUTAN	POWERGRID/B HUTAN	MO	01-Jun-2023 00:00	Voltage Regulation	05-Jun-2023 10:30	106:30:00	0
2	400kV Binaguri - Malbase Ckt-I	Line	ER , BHUTAN	POWERGRID/T HEP	TL	01-Jun-2023 00:00	relay indication Zone 1, Y-phase fault, IY- 580.8kA at distance 49.40km.	01-Jun-2023 00:38	00:38:00	1
3	400kV Binaguri -Tala Ckt-II	Line	ER , BHUTAN	POWERGRID/T HEP	SO	01-Jun-2023 00:00	for GDM (Gas Density Monitoring)	01-Jun-2023 18:50	18:50:00	0
4	132kV Salakati - Gelephu Ckt-I	Line	NER , BHUTAN	POWERGRID/B HUTAN	TL	01-Jun-2023 09:40	B-N Fault	01-Jun-2023 10:44	01:04:00	1
5	132kV Salakati - Gelephu Ckt-I	Line	NER , BHUTAN	POWERGRID/B HUTAN	SO	02-Jun-2023 09:00	To check breaker operation	02-Jun-2023 17:15	08:15:00	1
6	400KV-MUZAFFARPUR(PG)-GORAKHPUR-1	Line	ER ,Nepal	ER-I	SO	03-Jun-2023 09:47	LB8 RELAY RETROFITTING AT MUZAFFARPUR SS	03-Jun-2023 20:43	10:56:00	0
7	132kV Raxul - Parwanipur Ckt-I	Line	ER , NEPAL	BSPCL/NEPAL	TS	04-Jun-2023 17:17	over current Operated, relay details below IA 463 amps Ib 484 amps Ic 463 amps	04-Jun-2023 18:18	01:01:00	1
8	132kV Salakati - Gelephu Ckt-I	Line	NER , BHUTAN	POWERGRID/B HUTAN	SO	05-Jun-2023 09:20	to check breaker operation	05-Jun-2023 18:02	08:42:00	1
9	400KV-ALIPURDUAR (PG)-JIGMELLING-2	Line	ER , BHUTAN	ER-II	SO	05-Jun-2023 10:30	INSULATOR REPLACEMENT WORK	05-Jun-2023 18:51	08:21:00	0
10	400kV Alipurduar - Jigmeling Ckt-II	Line	ER , BHUTAN	POWERGRID/B HUTAN	MO	05-Jun-2023 18:51	Voltage Regulation	06-Jun-2023 07:55	13:04:00	0
11	400KV-ALIPURDUAR (PG)-JIGMELLING-2	Line	ER , BHUTAN	ER-II	SO	06-Jun-2023 08:01	INSULATOR REPLACEMENT WORK	06-Jun-2023 19:07	11:06:00	0
12	400kV Binaguri -Tala Ckt-IV	Line	ER , BHUTAN	POWERGRID/T HEP	SO	06-Jun-2023 09:38	cleaning of XLPE cables at THP end	06-Jun-2023 18:04	08:26:00	0
13	400kV Binaguri -Tala Ckt-IV	Line	ER , BHUTAN	POWERGRID/T HEP	MO	06-Jun-2023 18:04	Voltage Regulation	16-Jun-2023 08:08	230:04:00	0
14	400kV Alipurduar - Jigmeling Ckt-II	Line	ER , BHUTAN	POWERGRID/B HUTAN	MO	06-Jun-2023 19:07	Voltage Regulation	07-Jun-2023 09:05	13:58:00	0
15	400KV-ALIPURDUAR (PG)-JIGMELLING-2	Line	ER , BHUTAN	ER-II	SO	07-Jun-2023 09:35	INSULATOR REPLACEMENT WORK	07-Jun-2023 22:26	12:51:00	0
16	400KV-ALIPURDUAR (PG)-JIGMELLING-2	Line	ER , BHUTAN	ER-II	SO	07-Jun-2023 09:35	INSULATOR REPLACEMENT WORK	07-Jun-2023 22:26	12:51:00	0
17	132kV Salakati - Gelephu Ckt-I	Line	NER , BHUTAN	POWERGRID/B HUTAN	SO	08-Jun-2023 09:49	for testing of CB and rectification of tripping and closing of ckt from TNC switch.	08-Jun-2023 17:12	07:23:00	1
18	400KV-ALIPURDUAR (PG)-JIGMELLING-1	Line	ER , BHUTAN	ER-II	SO	10-Jun-2023 09:13	INSULATOR REPLACEMENT AT VARIOUS LOCATIONS	10-Jun-2023 19:28	10:15:00	0
19	400kV Alipurduar - Jigmeling Ckt-I	Line	ER , BHUTAN	POWERGRID/B HUTAN	MO	10-Jun-2023 19:30	Voltage Regulation	11-Jun-2023 06:14	10:44:00	0
20	400kV Alipurduar - Jigmeling Ckt-II	Line	ER , BHUTAN	POWERGRID/B HUTAN	TL	11-Jun-2023 03:35	Alipurduar End: RYB Fault,170kM(under bhutan jurusdiction), Ir-4.4kA, Iy3.8kA, Ib:4.6kA.	11-Jun-2023 16:02	12:27:00	1
21	400kV Alipurduar - Jigmeling Ckt-I	Line	ER , BHUTAN	POWERGRID/B HUTAN	MO	11-Jun-2023 16:25	Voltage Regulation	20-Jun-2023 17:52	217:27:00	0
22	132kV Salakati - Gelephu Ckt-I	Line	NER , BHUTAN	POWERGRID/B HUTAN	SO	13-Jun-2023 09:12	to check the circuit breaker timing and operation	13-Jun-2023 17:09	07:57:00	1
23	220kV Birpara - Chukha Ckt-I	Line	ER , BHUTAN	POWERGRID/B HUTAN	SO	13-Jun-2023 09:12	for replacement of old disc with polymer insulator	15-Jun-2023 17:34	56:22:00	0
24	220kV Birpara - Chukha Ckt-I	Line	ER , BHUTAN	POWERGRID/B HUTAN	TL	16-Jun-2023 14:37	Birpara End: R-N, 41.06 km, 2.94 kA.	16-Jun-2023 15:54	01:17:00	1
25	400kV Behrampur - Behramara Ckt-IV	Line	ER , BANGLADESH	POWERGRID/B ANGLADESH	TL	17-Jun-2023 14:20	Baharampur, AR successful: R-ph, 14.94km, 13.456 kA, Z-1	17-Jun-2023 15:45	01:25:00	1
26	220kV Birpara - Chukha Ckt-I	Line	ER , BHUTAN	POWERGRID/B HUTAN	TL	18-Jun-2023 12:31	Distance relay optd; Zone -I at a distance of 70.2km from CHP towards Bipara R phase to Neutral fault	18-Jun-2023 12:52	00:21:00	2
27	400kV Behrampur - Behramara Ckt-II	Line	ER , BANGLADESH	POWERGRID/B ANGLADESH	TL	18-Jun-2023 15:29	Berhampur end:- R-Ph Zone-1, FD:12.28km, FC:13.08kA	18-Jun-2023 17:22	01:53:00	1
28	220kV Birpara - Malbase Ckt-I	Line	ER , BHUTAN	POWERGRID/B HUTAN	TL	19-Jun-2023 18:19	Distance relay optd; Zone -I at a distance of 2.8km from Malbase towards Bipara B phase to Neutral fault	19-Jun-2023 20:09	01:50:00	1
29	220kV Birpara - Malbase Ckt-I	Line	ER , BHUTAN	POWERGRID/B HUTAN	SO	20-Jun-2023 13:39	expedite the OPGW cable lying	20-Jun-2023 20:09	06:30:00	1

NLDC Outage report of Month June 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
30	400kV Alipurduar - Jigmeling Ckt-I	Line	ER , BHUTAN	POWERGRID/BHUTAN	TL	20-Jun-2023 17:36	Alipurduar End: Line remained charged, No indication. Jigmelling End: Tripped from bhutan End only. Indiction yet to be received.	20-Jun-2023 20:16	02:40:00	1
31	400kV Alipurduar - Jigmeling (bypass at Punatsangchhu) Ckt-I	Line	ER , BHUTAN	POWERGRID/BHUTAN	MO	01-Jun-2023 00:00	Voltage Regulation	10-Jun-2023 09:13	225:13	0
32	132kV Surajpura-Ramnagar circuit	Line	ER , NEPAL		TL	22-Jun-2023 14:25	Overcurrent earth fault, Ir= 409 A, Iy= 435 A, Ib= 396A	22-Jun-2023 15:45	01:20:00	1
33	400KV-MUZAFFARPUR(PG)-DHALKEBAR-2	Line	ER ,Nepal	ER-I	SO	24-Jun-2023 09:57	LBB RELAY RETROFITTING AT MUZAFFARPUR SS	24-Jun-2023 19:04	09:07:00	0
34	132kV Rangia - Motanga Ckt-I	Line	NER , BHUTAN	AEGCL/BHUTAN	TL	25-Jun-2023 02:15	no relay indication from Bhutan ends for the external line.	25-Jun-2023 11:55	09:40:00	1
35	132kV Rangia - Motanga Ckt-I	Line	NER , BHUTAN	AEGCL/BHUTAN	TS	25-Jun-2023 14:37	loss of voltage reported, further details yet to be received.	25-Jun-2023 19:52	05:15:00	2
36	400kV Alipurduar - Jigmeling Ckt-II	Line	ER , BHUTAN	POWERGRID/BHUTAN	MO	25-Jun-2023 16:56	Voltage Regulation	01-Jul-2023 00:00	127:04:00	1
37	132kV Tanakpur - Mahendernagar Ckt-I	Line	NR , NEPAL	NHPC/NEPAL	SE	27-Jun-2023 21:52	sparking is seen in Wave Trap in Mahendranagar Sub station in Nepal	28-Jun-2023 00:10	02:18:00	0
38	132kV Tanakpur - Mahendernagar Ckt-I	Line	NR , NEPAL	NHPC/NEPAL	TL	28-Jun-2023 19:32	Line tripped on Phase-B, Distance protection in Zone-3	28-Jun-2023 20:26	00:54:00	1
39	132kV Rangia - Motanga Ckt-I	Line	NER , BHUTAN	AEGCL/BHUTAN	TS	29-Jun-2023 10:31	Due to internal shutdown in bhutan	29-Jun-2023 12:18	01:47:00	3

Northern Region Elements

1	330 MVAR BUS REACTOR NO 1 AT 765KV LALITPUR(LPG)	Bus Reactor	NR	UPPCL	SO	01-Jun-2023 12:16	"To perform Preventive Checking "	16-Jun-2023 16:22	364:06:00	0
2	240MVAR 765kV Bus Reactor-II at Bhiwani	Bus Reactor	NR	POWERGRID	SO	17-Jun-2023 17:30	abnormal loud sound is being observed	17-Jun-2023 22:15	04:45:00	0
3	240 MVAR BUS REACTOR NO 1 AT 765KV BHIWANI(PG)	Bus Reactor	NR	POWERGRID	SE	22-Jun-2023 06:47	for AMP work and attending the oil leakage from the top cover of Y phase of BR-1.	22-Jun-2023 18:52	12:05:00	0
4	240 MVAR BUS REACTOR NO 1 AT 765KV BHIWANI(PG)	Bus Reactor	NR	POWERGRID	SE	23-Jun-2023 09:47	for AMP work and attending the oil leakage from the top cover of Y phase of BR-1.	23-Jun-2023 18:04	08:17:00	0
5	240MVAR 765kV Bus Reactor-I at Meerut	Bus Reactor	NR	POWERGRID	TS	29-Jun-2023 13:30	Low SF6 gas pressure G-GD26-R/Y/B STG-3 Zone Trip	30-Jun-2023 00:19	10:49:00	1
6	765/400 KV 1500 MVA ICT 1 AT ANTA(RS)	ICT	NR	SLDC	SO	06-Jun-2023 16:20	Half Yearly and Quarterly Maintenance	06-Jun-2023 20:50	04:30:00	0
7	765/400kV 1500MVA ICT-III at Phagi	ICT	NR	Rajasthan/RRV PNL	SE	07-Jun-2023 18:19	To attend mis-alignment of R & Y-Phase Isolator of 400kV side of ICT-3.	08-Jun-2023 05:08	10:49:00	0
8	765/400kV 1500MVA ICT-I at Anta	ICT	NR	Rajasthan/RRV PNL	TS	09-Jun-2023 11:46	during change of faulty cable.	09-Jun-2023 19:42	07:56:00	1
9	765/400 KV 1500 MVA ICT 1 AT RAMPUR_PRSTL (UP)	ICT	NR	POWERGRID	SO	10-Jun-2023 10:56	For CSD Fine Tuning of 765kV 1500MVA ICT-1 at 765/400/220kV Rampur GIS	10-Jun-2023 17:10	06:14:00	0
10	765/400 KV 1500 MVA ICT 2 AT RAMPUR_PRSTL (UP)	ICT	NR	POWERGRID	SO	11-Jun-2023 12:23	For CSD Fine Tuning of 765kV 1500MVA ICT-2 at 765/400/220kV Rampur GIS	11-Jun-2023 13:49	01:26:00	0
11	765/400 KV 1500 MVA ICT 2 AT PHAGI(RS)	ICT	NR	SLDC	SO	12-Jun-2023 13:16	1. Testing and maintenance of Transforers. 2. Tightening of clamps and connectors	12-Jun-2023 22:48	09:32:00	0
12	765/400kV 1500MVA ICT-II at Agra(PG)	ICT	NR	POWERGRID	SO	15-Jun-2023 09:50	to attend critical Hotspot developed in 765/400KV ICT-2 Y-phase Neutral Isolator	15-Jun-2023 13:34	03:44:00	0
13	765/400 KV 1500 MVA ICT 2 AT AGRA(PG)	ICT	NR	POWERGRID	SO	19-Jun-2023 09:40	For Erection of interface module for connection of ICT-3 bay with existing Bus-1. After erection, internal conductor link will be removed and corona shield applied on both ends to isolate existing & new GIS. Internal conductor will be connected after HV test.	20-Jun-2023 02:43	17:03:00	0
14	765/400 KV 1500 MVA ICT 1 AT KANPUR_GIS(PG)	ICT	NR	POWERGRID	SO	20-Jun-2023 08:27	for AMP works	21-Jun-2023 01:43	17:16:00	0
15	765/400kV 1500MVA ICT-II at Jhatikara	ICT	NR	POWERGRID	SO	22-Jun-2023 18:37	for replacement of broken IPS conductor clamp	22-Jun-2023 21:25	02:48:00	0
16	765/400 KV 1500 MVA ICT 2 AT BHADLA_2 (PG)	ICT	NR	POWERGRID	SO	27-Jun-2023 18:05	For AMP work	28-Jun-2023 04:24	10:19:00	0
17	765 KV VARANASI-KANPUR_GIS (PG) CKT-1	Line	NR	POWERGRID	SC	01-Jun-2023 00:00	Transmission Line Diversion work due to construction of Ganga Expressway by UPEIDA	06-Jun-2023 07:16	127:16:00	0
18	765 KV VARANASI-KANPUR_GIS (PG) CKT-2	Line	NR	POWERGRID	SC	01-Jun-2023 00:00	Transmission Line Diversion work due to construction of Ganga Expressway by UPEIDA	06-Jun-2023 19:30	139:30:00	0

NLDC Outage report of Month June 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
19	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	01-Jun-2023 00:00	Voltage Regulation	01-Jun-2023 10:27	10:27:00	0
20	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	01-Jun-2023 00:00	Voltage Regulation	01-Jun-2023 09:33	09:33:00	0
21	765kV KOTESHWAR - MEERUT Ckt-II	Line	NR	POWERGRID	SE	01-Jun-2023 00:00	Hand Tripped (for inspection of 706 CB due to high SO2 contents.)	02-Jun-2023 22:13	46:13:00	0
22	765kV ORAI - ALIGARH Ckt-I	Line	NR	POWERGRID	MO	01-Jun-2023 00:00	Voltage Regulation	03-Jun-2023 10:07	58:07:00	0
23	765kV PHAGI - BHIWANI Ckt-I	Line	NR	RRVPNL/PG	TL	01-Jun-2023 00:00	Tower number- 556, 557, 558, 559 damaged upto waist level , Tower number- 560, 561, 562 damaged upto stub level	05-Jun-2023 17:06	113:06:00	1
24	765kV Fatehgarh II - Bhadla II Ckt-I	Line	NR	PFTL	SO	10-Jun-2023 18:48	For cutting down the length of the dropper to avoid tripping	11-Jun-2023 02:48	08:00:00	0
25	765kV BHADLA - BIKANER Ckt-II	Line	NR	POWERGRID	SE	21-Jun-2023 19:23	Snapping of Jumper . To attend broken conductor of B-phase at Bhadla end.	22-Jun-2023 06:12	10:49:00	0
26	765kV FATEHPUR - AGRA Ckt-I	Line	NR	POWERGRID	MO	01-Jun-2023 00:40	Voltage Regulation	02-Jun-2023 10:46	34:06:00	0
27	765kV AJMER - CHITTORGARH Ckt-I	Line	NR	POWERGRID	MO	01-Jun-2023 00:41	Voltage Regulation	01-Jun-2023 13:00	12:19:00	0
28	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	01-Jun-2023 16:59	Voltage Regulation	02-Jun-2023 08:43	15:44:00	0
29	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	01-Jun-2023 17:09	Voltage Regulation	02-Jun-2023 09:23	16:14:00	0
30	765kV AJMER - CHITTORGARH Ckt-II	Line	NR	POWERGRID	MO	02-Jun-2023 02:24	Voltage Regulation	02-Jun-2023 08:57	06:33:00	0
31	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	02-Jun-2023 17:13	Voltage Regulation	03-Jun-2023 08:49	15:36:00	0
32	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	02-Jun-2023 17:33	Voltage Regulation	03-Jun-2023 09:08	15:35:00	0
33	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	03-Jun-2023 17:32	Voltage Regulation	04-Jun-2023 08:50	15:18:00	0
34	765kV AJMER - CHITTORGARH Ckt-I	Line	NR	POWERGRID	MO	03-Jun-2023 18:00	Voltage Regulation	04-Jun-2023 09:54	15:54:00	0
35	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	03-Jun-2023 18:39	Voltage Regulation	04-Jun-2023 09:18	14:39:00	0
36	765kV BHADLA - BIKANER Ckt-I	Line	NR	POWERGRID	TL	03-Jun-2023 23:54	Fault details: Bikaner: Y Phase to Ground Fault, 6.000 kA, 159.637KM from Bikaner end.	04-Jun-2023 01:43	01:49:00	1
37	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	TL	04-Jun-2023 00:10	R-N fault, 290 Mtr 11kA,	04-Jun-2023 01:31	01:21:00	1
38	765kV Fatehgarh II - Bhadla II Ckt-I	Line	NR	PFTL	TL	04-Jun-2023 00:10	Distance 50.99 mtr Y-N fault, 14 Ka	04-Jun-2023 01:16	01:06:00	1
39	765kV Fatehgarh II - Bhadla II Ckt-II	Line	NR	PFTL	TL	04-Jun-2023 00:10	Distance 71.68mtr R-N fault, 14 kA	04-Jun-2023 01:25	01:15:00	1
40	765kV FATEHPUR - AGRA Ckt-II	Line	NR	POWERGRID	MO	04-Jun-2023 05:24	Voltage Regulation	04-Jun-2023 21:18	15:54:00	0
41	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	04-Jun-2023 17:09	Voltage Regulation	05-Jun-2023 08:26	15:17:00	0
42	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	04-Jun-2023 17:12	Voltage Regulation	05-Jun-2023 09:23	16:11:00	1
43	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	05-Jun-2023 16:47	Voltage Regulation	06-Jun-2023 08:39	15:52:00	0
44	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	05-Jun-2023 17:17	Voltage Regulation	06-Jun-2023 08:52	15:35:00	0
45	765kV Fatehgarh II - Bhadla II Ckt-II	Line	NR	PFTL	SO	05-Jun-2023 18:10	for cutting down the length of the dropper to avoid tripping and flashover of dropper with gantry tower..	06-Jun-2023 05:06	10:56:00	1
46	765kV PHAGI - BHIWANI Ckt-II	Line	NR	RRVPNL/PG	MO	05-Jun-2023 19:11	taken out on over voltage	06-Jun-2023 09:37	14:26:00	0
47	765kV KOTESHWAR - MEERUT Ckt-I	Line	NR	POWERGRID	SE	06-Jun-2023 10:09	to attend flashover marks in insulator on emergency basis.	06-Jun-2023 14:23	04:14:00	0

NLDC Outage report of Month June 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
48	765kV PHAGI - BHIWANI Ckt-II	Line	NR	RRVPNL/PG	SO	06-Jun-2023 16:04	To attend broken jumper at Tower loc no-5	06-Jun-2023 21:03	04:59:00	0
49	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	06-Jun-2023 16:07	Voltage Regulation	07-Jun-2023 07:48	15:41:00	0
50	765kV AJMER - CHITTORGARH Ckt-I	Line	NR	POWERGRID	MO	06-Jun-2023 16:15	Voltage Regulation	07-Jun-2023 09:27	17:12:00	0
51	765kV Fatehgarh II - Bhadla I Ckt-I	Line	NR	PFTL	TL	06-Jun-2023 16:43	Bhadla:-Main1 R-N, 28.8Km, 8.50Ka. Main2- 29.5Km, 8.5Ka	06-Jun-2023 18:53	02:10:00	1
52	765kV FATEHPUR - AGRA Ckt-II	Line	NR	POWERGRID	MO	06-Jun-2023 17:23	Voltage Regulation	07-Jun-2023 09:17	15:54:00	0
53	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	06-Jun-2023 17:39	Voltage Regulation	07-Jun-2023 08:42	15:03:00	1
54	765 KV AJMER-BHADLA_2 (PG) CKT-1	Line	NR	POWERGRID	SO	07-Jun-2023 16:53	For AMP work(ALONG WITH LINE REACTOR AT Bhadla-2 (PG) and AJMER(PG)	08-Jun-2023 07:47	14:54:00	0
55	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	07-Jun-2023 17:41	Voltage Regulation	08-Jun-2023 08:54	15:13:00	0
56	765kV AJMER - CHITTORGARH Ckt-II	Line	NR	POWERGRID	MO	07-Jun-2023 18:07	Voltage Regulation	08-Jun-2023 08:59	14:52:00	0
57	765 KV MOGA-MEERUT (PG) CKT-1	Line	NR	POWERGRID	SO	08-Jun-2023 09:31	Rectification of shutdown nature defects.	08-Jun-2023 19:46	10:15:00	0
58	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	08-Jun-2023 16:58	Voltage Regulation	09-Jun-2023 07:35	14:37:00	0
59	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	08-Jun-2023 17:55	Voltage Regulation	09-Jun-2023 08:36	14:41:00	0
60	765kV AJMER - CHITTORGARH Ckt-II	Line	NR	POWERGRID	MO	08-Jun-2023 18:05	Voltage Regulation	09-Jun-2023 09:13	15:08:00	0
61	765kV Ajmer - Phagi Ckt-II	Line	NR	POWERGRID	TL	08-Jun-2023 18:29	Ajmer: M1:27.62kM, Ir=11.27kA, ly=10.82kA M2:26.8kM, Ir=10.9kA, ly=8.95kA Phagi: 109.5kM, Ir=7.43kA, ly=6.84kA	08-Jun-2023 19:53	01:24:00	1
62	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	09-Jun-2023 17:19	Voltage Regulation	10-Jun-2023 07:33	14:14:00	0
63	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	09-Jun-2023 17:47	Voltage Regulation	10-Jun-2023 08:28	14:41:00	0
64	765kV PHAGI - BHIWANI Ckt-I	Line	NR	RRVPNL/PG	MO	09-Jun-2023 18:20	Voltage Regulation	10-Jun-2023 09:56	15:36:00	1
65	765kV AJMER - CHITTORGARH Ckt-I	Line	NR	POWERGRID	MO	09-Jun-2023 18:51	Voltage Regulation	10-Jun-2023 08:55	14:04:00	0
66	765kV PHAGI - BHIWANI Ckt-II	Line	NR	RRVPNL/PG	MO	10-Jun-2023 17:22	Voltage Regulation	11-Jun-2023 09:45	16:23:00	0
67	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	10-Jun-2023 17:41	Voltage Regulation	11-Jun-2023 07:56	14:15:00	0
68	765kV AJMER - CHITTORGARH Ckt-II	Line	NR	POWERGRID	MO	10-Jun-2023 17:50	Voltage Regulation	11-Jun-2023 09:25	15:35:00	0
69	765kv Gr.Noida -Jawaharpur Line.	Line	NR	POWERGRID NR	TS	10-Jun-2023 18:55	due to LA clamp disconnection during bad weather	10-Jun-2023 22:13	03:18:00	1
70	765kV AJMER - CHITTORGARH Ckt-I	Line	NR	POWERGRID	MO	11-Jun-2023 16:36	Voltage Regulation	12-Jun-2023 09:09	16:33:00	0
71	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	11-Jun-2023 18:01	Voltage Regulation	12-Jun-2023 08:16	14:15:00	1
72	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	11-Jun-2023 18:03	Voltage Regulation	12-Jun-2023 07:33	13:30:00	0
73	765kV PHAGI - BHIWANI Ckt-II	Line	NR	RRVPNL/PG	MO	11-Jun-2023 18:27	Voltage Regulation	12-Jun-2023 09:34	15:07:00	0
74	765kV AJMER - CHITTORGARH Ckt-II	Line	NR	POWERGRID	MO	12-Jun-2023 17:43	Voltage Regulation	13-Jun-2023 09:06	15:23:00	0
75	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	12-Jun-2023 17:47	Voltage Regulation	13-Jun-2023 08:08	14:21:00	0

NLDC Outage report of Month June 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
76	765kV BHADLA - BIKANER Ckt-I	Line	NR	POWERGRID	SE	13-Jun-2023 12:01	to attend broken jumper of wave trap of B phase.	13-Jun-2023 15:16	03:15:00	1
77	765kV AJMER - CHITTORGARH Ckt-I	Line	NR	POWERGRID	MO	13-Jun-2023 18:02	Voltage Regulation	14-Jun-2023 08:56	14:54:00	0
78	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	13-Jun-2023 18:02	Voltage Regulation	14-Jun-2023 07:49	13:47:00	0
79	765kV PHAGI - BHIWANI Ckt-I	Line	NR	RRVPNL/PG	SO	14-Jun-2023 17:23	to attend jumper issue at loc 597	15-Jun-2023 20:42	27:19:00	1
80	765kV AJMER - CHITTORGARH Ckt-II	Line	NR	POWERGRID	MO	14-Jun-2023 17:45	Voltage Regulation	15-Jun-2023 09:18	15:33:00	0
81	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	14-Jun-2023 17:58	Voltage Regulation	15-Jun-2023 07:21	13:23:00	0
82	765kV BHADLA - BIKANER Ckt-I	Line	NR	POWERGRID	SE	14-Jun-2023 18:49	To attend the damaged line conductor	14-Jun-2023 23:17	04:28:00	1
83	765kV BHADLA - BIKANER Ckt-II	Line	NR	POWERGRID	SE	15-Jun-2023 05:13	to attend hot spot at Bhadla	15-Jun-2023 06:39	01:26:00	0
84	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	15-Jun-2023 16:43	Voltage Regulation	16-Jun-2023 08:17	15:34:00	0
85	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	15-Jun-2023 17:21	Voltage Regulation	16-Jun-2023 09:15	15:54:00	0
86	765kV AJMER - CHITTORGARH Ckt-I	Line	NR	POWERGRID	MO	15-Jun-2023 18:32	Voltage Regulation	16-Jun-2023 08:21	13:49:00	0
87	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	16-Jun-2023 16:06	Voltage Regulation	17-Jun-2023 09:28	17:22:00	1
88	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	16-Jun-2023 16:09	Voltage Regulation	17-Jun-2023 09:24	17:15:00	0
89	765kV AJMER - CHITTORGARH Ckt-II	Line	NR	POWERGRID	MO	16-Jun-2023 18:00	Voltage Regulation	17-Jun-2023 09:45	15:45:00	0
90	765kV Bara-Mainpuri ckt 2	Line	NR	Uttar Pradesh/UPPTCL	SE	17-Jun-2023 11:41	Snapping of Jumper . Jumper broken at Tower no. 241.	17-Jun-2023 15:26	03:45:00	0
91	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	17-Jun-2023 15:26	Voltage Regulation	18-Jun-2023 09:27	18:01:00	0
92	765kV PHAGI - BHIWANI Ckt-II	Line	NR	RRVPNL/PG	MO	17-Jun-2023 16:23	Voltage Regulation	19-Jun-2023 09:43	41:20:00	0
93	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	17-Jun-2023 17:16	Voltage Regulation	18-Jun-2023 09:18	16:02:00	0
94	765kV AJMER - CHITTORGARH Ckt-I	Line	NR	POWERGRID	MO	17-Jun-2023 18:47	Voltage Regulation	18-Jun-2023 10:11	15:24:00	0
95	765kV KOTESHWAR - MEERUT Ckt-I	Line	NR	POWERGRID	TL	18-Jun-2023 08:44	B-Phase FSC of 765 kV Meerut-Koteshwar Line-I tripped at Meerut S5	18-Jun-2023 10:41	01:57:00	1
96	765kV AJMER - CHITTORGARH Ckt-II	Line	NR	POWERGRID	MO	18-Jun-2023 16:13	Voltage Regulation	19-Jun-2023 09:32	17:19:00	0
97	765kV FATEHPUR - AGRA Ckt-I	Line	NR	POWERGRID	MO	18-Jun-2023 16:24	Voltage Regulation	20-Jun-2023 09:48	41:24:00	0
98	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	18-Jun-2023 17:05	Voltage Regulation	19-Jun-2023 08:09	15:04:00	0
99	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	18-Jun-2023 18:05	Voltage Regulation	19-Jun-2023 09:05	15:00:00	1
100	765kV KOTESHWAR - MEERUT Ckt-I	Line	NR	POWERGRID	SO	19-Jun-2023 07:54	To attend damaged V-pilot string at tower location number 199.	19-Jun-2023 13:43	05:49:00	1
101	765kV PHAGI - BHIWANI Ckt-I	Line	NR	RRVPNL/PG	MO	19-Jun-2023 17:06	voltage regulation	20-Jun-2023 09:38	16:32:00	1
102	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	19-Jun-2023 17:18	Voltage Regulation	20-Jun-2023 09:20	16:02:00	0
103	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	19-Jun-2023 17:40	Voltage Regulation	20-Jun-2023 08:03	14:23:00	0

NLDC Outage report of Month June 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
104	765KV AJMER - CHITTORGARH Ckt-I	Line	NR	POWERGRID	MO	20-Jun-2023 17:08	Voltage Regulation	21-Jun-2023 09:12	16:04:00	0
105	765KV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	20-Jun-2023 17:32	Voltage Regulation	21-Jun-2023 08:22	14:50:00	1
106	765KV PHAGI - BHIWANI Ckt-II	Line	NR	RRVPLN/PG	MO	20-Jun-2023 17:35	Voltage Regulation	20-Jun-2023 21:14	03:39:00	0
107	765KV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	20-Jun-2023 17:41	Voltage Regulation	21-Jun-2023 07:37	13:56:00	0
108	765KV AJMER - CHITTORGARH Ckt-II	Line	NR	POWERGRID	MO	21-Jun-2023 17:21	Voltage Regulation	22-Jun-2023 09:33	16:12:00	0
109	765KV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	21-Jun-2023 18:26	Voltage Regulation	22-Jun-2023 09:07	14:41:00	0
110	765KV PHAGI - BHIWANI Ckt-II	Line	NR	RRVPLN/PG	MO	21-Jun-2023 18:43	Voltage Regulation	22-Jun-2023 09:30	14:47:00	0
111	765KV AJMER - CHITTORGARH Ckt-I	Line	NR	POWERGRID	MO	22-Jun-2023 17:33	Voltage Regulation	23-Jun-2023 08:59	15:26:00	0
112	765KV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	22-Jun-2023 17:36	Voltage Regulation	23-Jun-2023 08:23	14:47:00	0
113	765KV PHAGI - BHIWANI Ckt-I	Line	NR	RRVPLN/PG	MO	22-Jun-2023 18:00	Voltage Regulation	23-Jun-2023 09:39	15:39:00	1
114	765 KV BIKANER-BHADLA_2 (PG) CKT-1	Line	NR	POWERGRID	SO	23-Jun-2023 17:22	for AMP works	24-Jun-2023 04:32	11:10:00	0
115	765KV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	23-Jun-2023 17:58	Voltage Regulation	24-Jun-2023 08:46	14:48:00	0
116	765KV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	23-Jun-2023 18:11	Voltage Regulation	24-Jun-2023 08:50	14:39:00	0
117	765 KV AGRA-JHATIKARA (PG) CKT-1	Line	NR	POWERGRID	SO	24-Jun-2023 09:25	For diamond arrangement of E/w with Existing line	25-Jun-2023 20:30	35:05:00	0
118	765 KV BIKANER-BHADLA_2 (PG) CKT-2	Line	NR	POWERGRID	SO	24-Jun-2023 16:54	FOR AMP WORK.	25-Jun-2023 06:13	13:19:00	0
119	765KV Ajmer - Phagi Ckt-II	Line	NR	POWERGRID	MO	24-Jun-2023 17:06	Voltage Regulation	25-Jun-2023 10:05	16:59:00	1
120	765KV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	24-Jun-2023 17:26	Voltage Regulation	25-Jun-2023 08:50	15:24:00	0
121	765KV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	24-Jun-2023 17:36	Voltage Regulation	25-Jun-2023 08:54	15:18:00	1
122	765KV Varanasi - Vindhyachal PS Ckt-I	Line	NR	PVTSL	TL	24-Jun-2023 22:50	due to R-N fault, FD- 54.0km, FC- 11.03KA.	24-Jun-2023 23:36	00:46:00	1
123	765KV FATEHPUR - AGRA Ckt-I	Line	NR	POWERGRID	MO	25-Jun-2023 03:11	Voltage Regulation	26-Jun-2023 21:26	42:15:00	0
124	765KV ORAI - ALIGARH Ckt-II	Line	NR	POWERGRID	MO	25-Jun-2023 03:33	Voltage Regulation	27-Jun-2023 20:38	65:05:00	0
125	765KV PHAGI - BHIWANI Ckt-II	Line	NR	RRVPLN/PG	MO	25-Jun-2023 05:31	Voltage Regulation	26-Jun-2023 10:52	29:21:00	0
126	765KV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	25-Jun-2023 16:51	Voltage Regulation	26-Jun-2023 08:21	15:30:00	0
127	765KV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	25-Jun-2023 17:34	Voltage Regulation	26-Jun-2023 09:19	15:45:00	0
128	765KV PHAGI - BHIWANI Ckt-I	Line	NR	RRVPLN/PG	MO	26-Jun-2023 16:29	Voltage Regulation	27-Jun-2023 09:43	17:14:00	1
129	765KV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	26-Jun-2023 16:45	Voltage Regulation	27-Jun-2023 09:33	16:48:00	1
130	765 KV AGRA-JHATIKARA (PG) CKT-1	Line	NR	POWERGRID	SO	27-Jun-2023 09:49	For diamond formation work with under construction 765 kV D/C (Hexa) Sikar Aligarh TL	27-Jun-2023 19:46	09:57:00	0
131	765KV Varanasi - Vindhyachal PS Ckt-I	Line	NR	PVTSL	SE	27-Jun-2023 14:45	Severe Hot Spot observed on Contact of Rph line isolator of Vindhyachal(PS)-Varanasi-1 TL	27-Jun-2023 20:17	05:32:00	1

NLDC Outage report of Month June 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
132	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	27-Jun-2023 17:41	Voltage Regulation	28-Jun-2023 09:21	15:40:00	1
133	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	27-Jun-2023 17:44	Voltage Regulation	28-Jun-2023 08:28	14:44:00	0
134	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	27-Jun-2023 17:44	Voltage Regulation	28-Jun-2023 08:28	14:44:00	0
135	765kV PHAGI - BHIWANI Ckt-I	Line	NR	RRVNL/PG	MO	27-Jun-2023 17:47	Voltage Regulation	30-Jun-2023 10:57	65:10:00	1
136	765kV AJMER - CHITTORGARH Ckt-I	Line	NR	POWERGRID	MO	27-Jun-2023 18:04	Voltage Regulation	28-Jun-2023 10:06	16:02:00	0
137	765kV FATEHPUR - AGRA Ckt-II	Line	NR	POWERGRID	MO	28-Jun-2023 04:04	Voltage Regulation	28-Jun-2023 23:08	19:04:00	0
138	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	TL	28-Jun-2023 10:31	Y phase to earth fault	28-Jun-2023 19:46	09:15:00	2
139	765kV AJMER - CHITTORGARH Ckt-II	Line	NR	POWERGRID	MO	28-Jun-2023 16:10	Voltage Regulation	29-Jun-2023 09:55	17:45:00	0
140	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	28-Jun-2023 17:02	Voltage Regulation	29-Jun-2023 08:42	15:40:00	0
141	765kV FATEHPUR - AGRA Ckt-I	Line	NR	POWERGRID	MO	29-Jun-2023 03:18	Voltage Regulation	30-Jun-2023 09:50	30:32:00	0
142	765 KV BAREILLY_2-LUCKNOW_2 (PG) CKT-1	Line	NR	POWERGRID	SO	29-Jun-2023 09:30	for AMP work.	29-Jun-2023 20:00	10:30:00	0
143	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	29-Jun-2023 16:53	Voltage Regulation	30-Jun-2023 10:38	17:45:00	0
144	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	29-Jun-2023 17:14	Voltage Regulation	30-Jun-2023 05:39	12:25:00	0
145	765kV AJMER - CHITTORGARH Ckt-I	Line	NR	POWERGRID	MO	30-Jun-2023 02:41	Voltage Regulation	30-Jun-2023 09:22	06:41:00	0
146	765kV ORAI - ALIGARH Ckt-I	Line	NR	POWERGRID	MO	30-Jun-2023 03:12	Voltage Regulation	01-Jul-2023 00:00	20:48:00	0
147	765kV MOGA - MEERUT Ckt-I	Line	NR	POWERGRID	SE	30-Jun-2023 12:40	due to insulator break of Y-ph at tower location no. 822	30-Jun-2023 21:07	08:27:00	0
148	765kV AJMER - CHITTORGARH Ckt-II	Line	NR	POWERGRID	MO	30-Jun-2023 17:15	Voltage Regulation	01-Jul-2023 00:00	06:45:00	0
149	765kV PHAGI - BHIWANI Ckt-II	Line	NR	RRVNL/PG	MO	30-Jun-2023 17:24	Voltage Regulation	01-Jul-2023 00:00	06:36:00	0
150	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	30-Jun-2023 18:42	Voltage Regulation	01-Jul-2023 00:00	05:18:00	0
151	240MVAR LR(S) of 765kV Bhadla - Bikaner Ckt-I at Bikaner	Line Reactor	NR	POWERGRID	SE	06-Jun-2023 18:32	to attend the oil leakage	06-Jun-2023 19:22	00:50:00	0
152	240 MVAR SWITCHABLE LR ON 765 KV BIKANER-BHADLA_2 (PG) CKT-2 @BHADLA_2 (PG)	Line Reactor	NR	POWERGRID	SO	24-Jun-2023 17:42	for AMP works	25-Jun-2023 06:16	12:34:00	0
Western Region Elements										
1	SOLAPUR - 765KV B/R 2	Bus Reactor	WR	POWERGRID WR1	SO	02-Jun-2023 09:39	765kV Bus Reactor#2 Shutdown required for following works 1.Live tuning of 765kV Bus Reactor CBs CSD via 715 & 714-Bay CBs. (Note : Minimum 3 No.of live operations shall be taken from each bay i.e.714 & 715-Bays for fine tuning of CSD. 2. Normalisation of Spare Change over as per CEA norms	02-Jun-2023 20:21	10:42:00	0
2	INDORE - 765KV B/R 2	Bus Reactor	WR	POWERGRID	SO	02-Jun-2023 10:43	FOR ROTATION OF SPARE REACTOR BEFORE 6 MONTHS. DIA TO BE KEPT OPEN AT BOTH ENDS.	02-Jun-2023 18:06	07:23:00	0
3	BINA - 765KV B/R 2	Bus Reactor	WR	POWERGRID	SO	05-Jun-2023 09:49	For AMP of Bus Reactor.	05-Jun-2023 20:25	10:36:00	0
4	INDORE - 765KV B/R 1	Bus Reactor	WR	POWERGRID	SO	05-Jun-2023 10:16	FOR ROTATION OF SPARE REACTOR BEFORE 6 MONTHS. DIA TO BE KEPT OPEN AT BOTH ENDS.	05-Jun-2023 19:27	09:11:00	0
5	240MVAR 765kV Bus Reactor-I at VADODARA	Bus Reactor	WR	POWERGRID	TS	05-Jun-2023 13:00	PRV OPERATED	05-Jun-2023 22:17	09:17:00	1
6	240MVAR 765kV Bus Reactor-II at RAIGARH PS (Kotra)	Bus Reactor	WR	POWERGRID	TS	05-Jun-2023 15:20	tripped due to inclement weather	06-Jun-2023 02:25	11:05:00	1

NLDC Outage report of Month June 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
7	BILASPUR - 765KV B/R 1	Bus Reactor	WR	POWERGRID WR1	SO	08-Jun-2023 09:42	For Bus reactor spare change over works. Last spare change over carried out on 08.01.2023	08-Jun-2023 18:07	08:25:00	0
8	VINDHYACHAL(PS) - 765KV B/R 1	Bus Reactor	WR	POWERGRID	SO	09-Jun-2023 10:28	Bus Reactor AMP at Vindhyachal PS. DIA TO BE KEPT OPEN.	09-Jun-2023 20:29	10:01:00	0
9	240MVAR 765KV Bus Reactor-I at DHULE	Bus Reactor	WR	BDTCL	TS	13-Jun-2023 17:08	suspected fault in secondary CT circuit	13-Jun-2023 22:30	05:22:00	1
10	SATNA - 765KV B/R 2	Bus Reactor	WR	POWERGRID	SE	16-Jun-2023 14:22	To attend oil seepage in Y-ph Reactor neutral bushing turret	16-Jun-2023 20:10	05:48:00	0
11	KORADI-III - 765KV B/R 1	Bus Reactor	WR	MEGPTCL	SO	22-Jun-2023 08:01	Spare reactor changeover activity spare reactor to be taken into service in place of B-Phase reactor.	22-Jun-2023 15:48	07:47:00	0
12	DHARAMJAYGARH - 765KV B/R 1	Bus Reactor	WR	POWERGRID WR1	SO	23-Jun-2023 08:38	For BR AMP works	23-Jun-2023 17:46	09:08:00	0
13	240MVAR 765KV Bus Reactor-I at DHULE	Bus Reactor	WR	BDTCL	TS	24-Jun-2023 02:41	Backup Impedance relay operated	24-Jun-2023 07:26	04:45:00	2
14	BANASKANTHA - 765KV B/R 1	Bus Reactor	WR	POWERGRID	SO	28-Jun-2023 06:50	For attending Oil leakage in R phase reactor switching of spare reactor with R phase unit required	28-Jun-2023 09:02	02:12:00	0
15	240MVAR 765KV Bus Reactor-I at AKOLA-II	Bus Reactor	WR	Maharashtra/ MEGPTCL	SO	28-Jun-2023 09:35	Changeover of R-Ph Reactor with Spare Reactor at Akola(2) SS as per CEA guideline. Last spare changeover date- 07.01.2023	28-Jun-2023 14:51	05:16:00	0
16	BINA - 765KV B/R 2	Bus Reactor	WR	POWERGRID	SO	30-Jun-2023 09:56	For AMP of Bus Reactor.	30-Jun-2023 20:14	10:18:00	0
17	765KV/400KV BHUJ-ICT-1	ICT	WR	POWERGRID	SO	01-Jun-2023 10:05	PRV modification works.. Dia to be kept open at both sides	01-Jun-2023 14:28	04:23:00	0
18	765/400kv 1500MVA ICT-II at SASAN	ICT	WR	SASAN UMPP	SO	01-Jun-2023 20:44	Y Phase, LA Counter connection restoration work at 765 kV side	01-Jun-2023 22:05	01:21:00	0
19	765KV/132KV GADARWARA-ICT-1	ICT	WR	NTPC	SO	02-Jun-2023 09:34	IBT-1B shall be taken in service and IBT-spare shall be taken out.	02-Jun-2023 17:47	08:13:00	0
20	765KV/400KV SEONI-ICT-3	ICT	WR	POWERGRID WR1	SO	02-Jun-2023 09:37	For AMP Works@Seoni SS	02-Jun-2023 19:51	10:14:00	0
21	765/400kv 1500MVA ICT-III at RAIGARH PS (Kotra)	ICT	WR	POWERGRID	TS	04-Jun-2023 15:20	ICT3_765/400kv at KOTRA PS was tripped at 15:20 hrs/04.06.2023 on differential due to connector damage	04-Jun-2023 22:33	07:13:00	1
22	765/400kv 1500MVA ICT-IV at RAIGARH PS (Kotra)	ICT	WR	POWERGRID	TS	04-Jun-2023 15:20	Tripped due to inclement weather. R-ph & Y-ph LA of 765/400 kV ICT-2 has fallen. Connector broken at 400 kV side of 765/400 kV ICT-3. Isolator arm broken in 765 kV Bus reactor-2, 400 kV SKS - Kotra D/C. Spacer between phases of 400 kV REGLKotra- 2 damaged at 400 kV Kotra PS	04-Jun-2023 23:49	08:29:00	1
23	765KV/400KV DHULE-ICT-2	ICT	WR	BDTCL-Sterlite	SO	05-Jun-2023 11:06	ICT-Spare switching with in place of ICT-2 R phase. Last switching date was on 20-12-22	05-Jun-2023 15:19	04:13:00	0
24	765KV/132KV GADARWARA-ICT-2	ICT	WR	NTPC	SO	06-Jun-2023 09:16	IBT-spare shall be taken in service and IBT-2R shall be taken out for annual testing and PM. Spare IBT will serve as IBT-2R	06-Jun-2023 17:48	08:32:00	0
25	765KV/400KV AURANGABAD-ICT-2	ICT	WR	POWERGRID WR1	SO	07-Jun-2023 08:12	AMP WORK.	08-Jun-2023 12:23	28:11:00	0
26	765KV/400KV SATNA-ICT-2	ICT	WR	POWERGRID	SO	07-Jun-2023 09:26	For WTI & OTI Modification work, Scheme checking and AMP work. Dia to be kept open at both sides.	07-Jun-2023 18:30	09:04:00	0
27	765KV/400KV BHUJ-ICT-2	ICT	WR	POWERGRID	SO	08-Jun-2023 10:47	PRV modification works.. Dia to be kept open at both sides	08-Jun-2023 15:02	04:15:00	0
28	765/400kv 1500MVA ICT-II at DHULE	ICT	WR	BDTCL	SE	08-Jun-2023 15:55	to attend sparking in isolator at 400kv site	08-Jun-2023 20:51	04:56:00	0
29	765KV/400KV WARORA-PG-ICT-1	ICT	WR	POWERGRID WR1	SO	09-Jun-2023 09:15	FOR SPARE CHANGEOVER WORK	09-Jun-2023 15:37	06:22:00	0
30	765KV/400KV WARDHA-ICT-3	ICT	WR	POWERGRID WR1	SO	09-Jun-2023 10:07	For Amp work of ICT, For Spare Change over works	10-Jun-2023 00:52	14:45:00	0
31	765/400kv 1500MVA ICT-I at DHULE	ICT	WR	BDTCL	TP	09-Jun-2023 11:28	765/400KV ICT-01 at Dhule tripped at 11:28 Hrs on today(i.e. 09-06-2023) due to malfunction of Differential relay	09-Jun-2023 13:15	01:47:00	1
32	765KV/400KV BILASPUR-ICT-2	ICT	WR	POWERGRID WR1	SO	13-Jun-2023 08:12	ICT AMP works	13-Jun-2023 19:30	11:18:00	0
33	765KV/400KV BILASPUR-ICT-3	ICT	WR	POWERGRID WR1	SO	15-Jun-2023 09:01	ICT AMP works	16-Jun-2023 09:21	24:20:00	0
34	765/400kv 1500 MVA ICT-2 at Lakadiya	ICT	WR	POWERGRID WR	TS	16-Jun-2023 06:54	Tripped on Buchholz-2 in Y-ph due to DC Earth Fault	16-Jun-2023 11:46	04:52:00	1

NLDC Outage report of Month June 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
35	765/400kV 1500MVA ICT-III at BHUJ PS	ICT	WR	POWERGRID	SE	16-Jun-2023 14:20	hand tripped due to broken B Phase Jumper string of ICT & extremely High Wind and rain due to cyclone biparjoy.	17-Jun-2023 14:00	23:40:00	0
36	765KV/400KV SOLAPUR-ICT-1	ICT	WR	POWERGRID WR1	SO	20-Jun-2023 09:40	Spare Change over as per CEA norms	20-Jun-2023 16:58	07:18:00	0
37	765KV/400KV KHANDWA-PS-ICT-2	ICT	WR	KTL-Sterlite	SO	21-Jun-2023 09:30	2 Y Testing of ICT 1 & (Rph & Y ph conservator tank Air cell rectification	21-Jun-2023 21:46	12:16:00	0
38	765KV/400KV KHANDWA-PS-ICT-2	ICT	WR	KTL-Sterlite	SO	22-Jun-2023 09:07	2 Y Testing of ICT 1 & (Rph & Y ph conservator tank Air cell rectification	22-Jun-2023 16:49	07:42:00	0
39	765KV/400KV PARLI NEW-ICT-1	ICT	WR	POWERGRID WR1	SO	23-Jun-2023 08:06	AMP works	23-Jun-2023 18:18	10:12:00	0
40	765KV/400KV GWALIOR-ICT-2	ICT	WR	POWERGRID	SO	24-Jun-2023 10:02	AMP Works.Dia to be kept open at both sides.	24-Jun-2023 18:29	08:27:00	0
41	765KV/400KV AKOLA (2)-ICT-1	ICT	WR	MEGPTCL	SO	25-Jun-2023 10:47	Changeover of Spare phase with B-ph ICT at Akola(2) SS as per CEA guideline	25-Jun-2023 18:56	08:09:00	0
42	765KV/132KV GADARWARA-ICT-2	ICT	WR	NTPC	SO	26-Jun-2023 09:32	IBT-2R shall be taken in service and IBT-2Y shall be taken out for annual testing and PM.	26-Jun-2023 17:16	07:44:00	0
43	765KV/400KV SOLAPUR-ICT-1	ICT	WR	POWERGRID WR1	SO	27-Jun-2023 08:27	Normalisation of Spare Change over as per CEA norms	27-Jun-2023 16:19	07:52:00	0
44	765KV AURANGABAD - PUNE Ckt-I	Line	WR	POWERGRID	MO	01-Jun-2023 00:00	to control the loading of pune aurangabad line	17-Jun-2023 07:29	391:29:00	0
45	765kv BINA - GWALIOR Ckt-III	Line	WR	POWERGRID	TL	01-Jun-2023 00:00	on R-ph/E fault Gwalior:- 23.2km/15.01kA Bina:- 231.7km/2.77kA	01-Jun-2023 17:33	17:33:00	1
46	765kv BINA - JABALPUR PS Ckt-I	Line	WR	POWERGRID	MO	01-Jun-2023 00:00	Voltage Regulation	13-Jun-2023 17:53	305:53:00	0
47	765kv Lakadia - Banaskantha Ckt-II	Line	WR	Adani Trans Ind Ltd	MO	01-Jun-2023 00:00	Voltage Regulation	06-Jun-2023 16:23	136:23:00	0
48	765KV RAIPUR-PS(DURG) - WARDHA Ckt-III	Line	WR	POWERGRID	MO	01-Jun-2023 00:00	taken out on over voltage	05-Jun-2023 20:08	116:08:00	0
49	765KV AKOLA(2) - EKTUNI (AURANGABAD-3) Ckt-II	Line	WR	Maharashtra/ MEGPTCL	TL	04-Jun-2023 13:46	Fault Current :- 5.4kA Fault Location :- 70.3km Zone :- 1 Fault Type :- Y-Phase to Earth	04-Jun-2023 15:30	01:44:00	1
50	765KV WARORA - PARLI NEW Ckt-II	Line	WR	PWTL-PG/PPTL-PG	TL	04-Jun-2023 14:34	Tripping may be occurred due to rain and lightening	04-Jun-2023 17:31	02:57:00	1
51	765kv RAIGARH-PS(KOTRA) - CHAMPA PS Ckt-I	Line	WR	POWERGRID	TL	04-Jun-2023 15:20	line tripped on Y-G fault	04-Jun-2023 19:48	04:28:00	1
52	765KV RAIGARH-PS(KOTRA) - CHAMPA PS Ckt-II	Line	WR	POWERGRID	TL	04-Jun-2023 15:20	Tripped due to inclement weather. R-ph & Y-ph LA of 765/400 kV ICT-2 has fallen. Connector broken at 400 kV side of 765/400 kV ICT-3. Isolator arm broken in 765 kV Bus reactor-2, 400 kV SKS - Kotra D/C. Spacer between phases of 400 kV REG-L- Kotra-2 damaged at 400 kV Kotra PS.	04-Jun-2023 22:45	07:25:00	1
53	765KV DHULE - VADODARA PS Ckt-I	Line	WR	BDTCL/POWER GRID	SO	05-Jun-2023 16:21	For change the LR of 765 kV Dhule Vadodara line with it's Y ph unit at Vadodara	05-Jun-2023 18:28	02:07:00	0
54	765KV RAIPUR-PS(DURG) - WARDHA Ckt-III	Line	WR	POWERGRID	MO	05-Jun-2023 20:08	Voltage Regulation	01-Jul-2023 00:00	603:52:00	0
55	765KV-BILASPUR-SEONI-2	Line	WR	POWERGRID WR1	SO	06-Jun-2023 10:04	Spare LR change over works. Previous spare change over carried out on 14.12.2023	06-Jun-2023 17:18	07:14:00	0
56	765KV-WARDHA-AURANGABAD-2	Line	WR	POWERGRID WR1	SO	06-Jun-2023 14:57	For Spare normalization i.e. taking Spare out of service	06-Jun-2023 22:32	07:35:00	0
57	765KV-BHUJ-BANASKANTHA-2	Line	WR	POWERGRID	SO	07-Jun-2023 11:35	Spare L/R changeover at Bhuj PS, Due date 23.06.2023.DIA TO BE KEPT OPEN AT BOTH ENDS.	07-Jun-2023 19:38	08:03:00	0
58	765KV BILASPUR - SEONI Ckt-I	Line	WR	POWERGRID	SE	07-Jun-2023 18:51	replacement of broker polymer insulator	08-Jun-2023 00:23	05:32:00	0
59	765KV-SOLAPUR-PARLI NEW-1	Line	WR	POWERGRID WR1	SO	08-Jun-2023 08:14	Line terminal equipments AMP at 765kV Solapur Substation	08-Jun-2023 20:09	11:55:00	0
60	765KV SEONI - WARDHA Ckt-I	Line	WR	POWERGRID	TL	10-Jun-2023 18:19	Fault details at Wardha: 216.4km and 3.41kA & from Seoni: 51.5km and 8.63kA.	10-Jun-2023 19:53	01:34:00	1
61	765KV KHANDWA PS - DHULE Ckt-I	Line	WR	KTL-STERLITE/BDTC	TL	13-Jun-2023 17:08	R-phase to Earth fault	13-Jun-2023 19:20	02:12:00	1
62	765kv GADARWARA - WARORA Ckt-II	Line	WR	NTPC/PWTL-PG	TL	13-Jun-2023 21:36	B-Yph fault at distance of 146.3Km (FC= 6.767KA & 6.942KA) from Warora end	13-Jun-2023 23:19	01:43:00	1
63	765KV-TAMNAR-DHARAMJAYGARH-1	Line	WR	POWERGRID WR1	SO	15-Jun-2023 08:59	For line eq AMP works	15-Jun-2023 21:25	12:26:00	0
64	765KV-BHOPAL-BDTCL-JABALPUR-1	Line	WR	BDTCL-Sterlite	SO	15-Jun-2023 10:01	Spare Switching of 765kV Jabalpur Bhopal Line Reactor.	15-Jun-2023 11:58	01:57:00	0

NLDC Outage report of Month June 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Category	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
65	765kV Lakadia - Banaskantha Ckt-I	Line	WR	Adani Trans Ind Ltd	MO	15-Jun-2023 13:37	Voltage Regulation	16-Jun-2023 22:50	33:13:00	0
66	765KV Lakadia -Vadodara Ckt-II	Line	WR	STERLITE	MO	15-Jun-2023 20:17	Voltage Regulation	19-Jun-2023 16:29	92:12:00	0
67	765KV-TAMNAR-DHARAMJAYGARH-2	Line	WR	POWERGRID WR1	SO	16-Jun-2023 09:14	For line eq AMP works	16-Jun-2023 18:51	09:37:00	0
68	765kV Lakadia - Banaskantha Ckt-II	Line	WR	Adani Trans Ind Ltd	SE	16-Jun-2023 15:02	hand tripped due to (Biporjoy Cyclone) Heavy Rain and thunder storm occur continuously at Lakadia SS	21-Jun-2023 12:58	117:56:00	0
69	765KV-PUNE-GIS-SOLAPUR-1	Line	WR	POWERGRID WR1	SO	17-Jun-2023 07:40	POST OCC Outage:Sant Shri Tukaram Maharaj Palki	17-Jun-2023 19:54	12:14:00	0
70	765kV BINA - GWALIOR Ckt-II	Line	WR	POWERGRID	SO	17-Jun-2023 10:12	AMP Works. Dia to be kept open at both sides. For spare changover also.	18-Jun-2023 17:58	31:46:00	0
71	765kV Lakadia - Banaskantha Ckt-I	Line	WR	Adani Trans Ind Ltd	SO	17-Jun-2023 11:14	Dropper connector clamp broken in Y-ph	18-Jun-2023 18:58	31:44:00	0
72	765kV AURANGABAD - PUNE Ckt-I	Line	WR	POWERGRID	MO	17-Jun-2023 20:13	Voltage Regulation	21-Jun-2023 11:39	87:26:00	0
73	765 kV Bhuj PS-1 to Bhuj ps II - Ckt-2	Line	WR	POWERGRID WR	SO	19-Jun-2023 12:55	Gantry Jumper One support insulator removed at Bhuj PS-1 End In Yph	19-Jun-2023 20:28	07:33:00	0
74	765kV VINDHYACHAL PS - JABALPUR PS Ckt-I	Line	WR	POWERGRID	SE	19-Jun-2023 14:23	for taking R-ph unit of L/R out of service due to heavy oil leakage	19-Jun-2023 20:04	05:41:00	0
75	765KV-RAIGARH-PS-TAMNAR-1	Line	WR	POWERGRID WR1	SO	20-Jun-2023 07:42	LINE MAINTENANCE	20-Jun-2023 11:38	03:56:00	0
76	765kV RAIGARH-PS(KOTRA) - TAMNAR Ckt-II	Line	WR	POWERGRID	TL	20-Jun-2023 09:03	conductor snapped at Loc no 85-86	21-Jun-2023 05:32	20:29:00	1
77	765kV PUNE - SOLAPUR Ckt-I	Line	WR	POWERGRID	SO	21-Jun-2023 11:37	FOR THE PASSING OF SHRITUKARAM MAHARAJ PALKI	21-Jun-2023 22:41	11:04:00	0
78	765kV PUNE - SOLAPUR Ckt-I	Line	WR	POWERGRID	MO	21-Jun-2023 22:42	After planned shutdown,converted to overvoltage	22-Jun-2023 08:23	09:41:00	0
79	765kV AURANGABAD - PUNE Ckt-I	Line	WR	POWERGRID	MO	22-Jun-2023 08:22	Voltage regulation	23-Jun-2023 09:24	25:02:00	0
80	765kV AURANGABAD - PUNE Ckt-I	Line	WR	POWERGRID	MO	22-Jun-2023 08:22	To control loading in Mumbai network	23-Jun-2023 09:24	25:02:00	0
81	765KV-AURANGABAD-SOLAPUR-2	Line	WR	POWERGRID WR1	SO	22-Jun-2023 09:03	Attending of Shutdown nature defects at Loc No.88,298 (Opening of jumper sub conductor) at 765kV Solapur TLM jurisdiction. Note: 765kV Aurangabad-Solapur#1 line AR to be kept in Non-Auto Mode/ Rescheduled from 14.06.23 to 22.06.23	22-Jun-2023 20:24	11:21:00	0
82	765KV-PUNE-GIS-SOLAPUR-1	Line	WR	POWERGRID WR1	SO	23-Jun-2023 09:28	For the passing of Sri Tukaram Maharaj Palki	23-Jun-2023 19:40	10:12:00	0
83	765KV-CHAMPA-DHARAMJAYGARH-2	Line	WR	POWERGRID WR1	SO	23-Jun-2023 11:40	For alingment of Main Bay Isolator 721-89B at Champa.	23-Jun-2023 19:25	07:45:00	0
84	765kV AURANGABAD - PUNE Ckt-I	Line	WR	POWERGRID	MO	23-Jun-2023 21:41	Voltage Regulation	27-Jun-2023 09:25	83:44:00	0
85	765kV Lakadia - Banaskantha Ckt-I	Line	WR	Adani Trans Ind Ltd	MO	24-Jun-2023 04:40	Voltage Regulation	15-Jul-2023 10:32	509:52:00	0
86	765kV RAIPUR-PS(DURG) - CHAMPA PS Ckt-I	Line	WR	POWERGRID	TL	25-Jun-2023 06:15	R-Y fault at FC= 16.403KA, FD= 41.728km from Durg	25-Jun-2023 09:01	02:46:00	1
87	765kV RAIPUR-PS(DURG) - CHAMPA PS Ckt-II	Line	WR	POWERGRID	MO	25-Jun-2023 11:45	Due to high voltage at Champa end	04-Jul-2023 11:07	215:22:00	0
88	765kV SASAN - SATNA Ckt-I	Line	WR	SASAN UMPP/POWER	TL	25-Jun-2023 18:02	At Satna end: 3.27kA/240.59km At Sasan end: 32.75kA/6.2km Yph-E/Fault	25-Jun-2023 19:31	01:29:00	1
89	765kV SASAN - SATNA Ckt-I	Line	WR	SASAN UMPP/POWER GRID	TL	25-Jun-2023 18:02	At Satna end: 3.27kA/240.59km At Sasan end: 32.75kA/6.2km charging attempt taken at 19:31 but failed due to conductor snapping work permit code issue	26-Jun-2023 00:27	06:25:00	2
90	765kV DHARAMJAYGARH - JABALPUR PS Ckt-III	Line	WR	POWERGRID	MO	25-Jun-2023 18:07	Voltage Regulation	01-Jul-2023 00:00	125:53:00	0
91	765kV VINDHYACHAL PS - JABALPUR PS Ckt-II	Line	WR	POWERGRID	TL	25-Jun-2023 19:15	Tripped on Rph-Yph Fault. Indications: Jabalpur end: IR:4.99 kA-IY:5.1 kA/244km. Vindhyachal end: IR:8.24kA-IY:8.05kA/124.8km.	25-Jun-2023 21:53	02:38:00	1
92	765KV-PUNE-GIS-PADGHE-PG-1	Line	WR	CWRTL	SO	26-Jun-2023 11:14	Replacement of faulty insulators.	26-Jun-2023 19:53	08:39:00	0

NLDC Outage report of Month June 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
93	765KV-PUNE-GIS-AURANGABAD-1	Line	WR	CWRTL	SO	27-Jun-2023 09:49	Replacement of faulty insulators.	27-Jun-2023 20:36	10:47:00	0
94	765KV AURANGABAD - SOLAPUR Ckt-I	Line	WR	POWERGRID	MO	27-Jun-2023 22:06	Voltage Regulation	03-Jul-2023 10:17	132:11:00	0
95	765KV AURANGABAD - PUNE Ckt-I	Line	WR	POWERGRID	MO	28-Jun-2023 07:59	Voltage Regulation	01-Jul-2023 00:00	64:01:00	0
96	765KV-DHULE-KHANDWA-STERLITE-2	Line	WR	IndiGrid	SO	28-Jun-2023 08:46	Shutdown required for Tower strengthening Work	28-Jun-2023 18:44	09:58:00	0
97	765KV Lakadia -Vadodara Ckt-I	Line	WR	STERLITE	MO	29-Jun-2023 13:36	Voltage Regulation	01-Jul-2023 00:00	34:24:00	0
98	765KV DHULE - VADODARA PS Ckt-I	Line	WR	BDTCL/POWER GRID	TL	30-Jun-2023 06:15	Line tripped due to heavy rain and lightning	30-Jun-2023 07:51	01:36:00	1
99	765KV DHULE - VADODARA PS Ckt-I	Line	WR	BDTCL/POWER GRID	TL	30-Jun-2023 07:51	Line tripped due to heavy rain and lightning	30-Jun-2023 22:22	14:31:00	2
100	765KV-SEONI-BINA-1	Line	WR	POWERGRID WR1	SO	30-Jun-2023 08:57	For AR relay issue rectification work@Seoni SS	01-Jul-2023 00:00	15:03:00	0
101	240MVAR LR(S) of 765kv Bhopal - Indore Ckt-I at Bhopal	Line Reactor	WR	BDTCL/POWER GRID	TS	03-Jun-2023 17:31	under the tripping scheme implemented against Ferro-Resonance effect	03-Jun-2023 18:06	00:35:00	1
102	765KV-SATNA-ORAI-1 L/R@ SATNA - 765KV	Line Reactor	WR	POWERGRID	SO	04-Jun-2023 07:35	For Switching of Spare with Y-Ph (For taking Y-Ph in Service) at Satna end. Due date 24.06.23. Dia to be kept open at both ends.	04-Jun-2023 19:47	12:12:00	0
103	765KV-SOLAPUR-RAICHUR-2 L/R@ SOLAPUR - 765KV	Line Reactor	WR	POWERGRID WR1	SO	06-Jun-2023 07:27	1.Line Reactor & Reactor CB AMP works at 765kv Solapur Substation. 2.Normalisation of Spare Change over as per CEA norms	06-Jun-2023 17:52	10:25:00	0
104	765KV-BILASPUR-SEONI-2 L/R@ BILASPUR - 765KV	Line Reactor	WR	POWERGRID WR1	SO	06-Jun-2023 10:04	Spare LR change over works. Previous spare change over carried out on 14.12.2023	06-Jun-2023 17:18	07:14:00	0
105	765KV-WARDHA-AURANGABAD-2 L/R@ WARDHA - 765KV	Line Reactor	WR	POWERGRID WR1	SO	06-Jun-2023 14:58	For Spare normalization i.e. taking Spare out of service	06-Jun-2023 22:32	07:34:00	0
106	765KV-BANASKANTHA-CHITTORGARH-2 L/R@ BANASKANTHA	Line Reactor	WR	POWERGRID	SO	06-Jun-2023 17:11	Switching of spare reactor with B Phase LR. DIA TO BE KEPT OPEN AT BOTH ENDS	06-Jun-2023 22:07	04:56:00	0
107	765KV-BHUJ-BANASKANTHA-2 L/R@ BHUJ - 765KV	Line Reactor	WR	POWERGRID	SO	07-Jun-2023 11:35	Spare L/R changeover at Bhuj PS, Due date 23.06.2023.	07-Jun-2023 19:34	07:59:00	0
108	765KV-AKOLA (2)-EKTUNI-1 L/R@ AKOLA (2) - 765KV	Line Reactor	WR	MEGPTCL	SO	09-Jun-2023 17:11	Changeover of BPh line Reactor with Spare Reactor at Akola- II SS as per CEA guideline. Last changeover date 10-12-2022	09-Jun-2023 22:45	05:34:00	0
109	240MVAR LR(S) of 765 kv Raigarh-PS(Kotra) - Raipur-PS(K)	Line Reactor	WR	POWERGRID	TS	14-Jun-2023 18:43	TRIPPED ON POLE DISCREPENCY	15-Jun-2023 22:03	27:20:00	1
110	765KV-JABALPUR-BHOPAL-1 L/R@ BHOPAL - 765KV	Line Reactor	WR	BDTCL-Sterlite	SO	15-Jun-2023 10:01	Spare Switching of 765kv Jabalpur Bhopal Line Reactor a. Present Switching combination: Y, B, SP	15-Jun-2023 11:58	01:57:00	0
111	Vadodara-Lakadia ckt-1 LR at Lakadia	Line Reactor	WR	POWERGRID	TS	17-Jun-2023 06:13	due to water leakage in PRV terminal box	17-Jun-2023 10:01	03:48:00	1
112	240MVAR LR(S) of 765kv Banaskantha-Lakadia Ckt-II at Banaskantha	Line Reactor	WR	POWERGRID	TS	18-Jun-2023 12:53	Pole discrepancy	18-Jun-2023 17:59	05:06:00	1
113	240MVAR LR(S) of 765kv Khandwa PS - Dhule-BDTCL Ckt-I	Line Reactor	WR	KTL/STERLITE	TS	24-Jun-2023 02:41	Backup Impedance relay operated	24-Jun-2023 06:24	03:43:00	1
114	240MVAR LR(S) of 765kv Aurangabad - Solapur Ckt-I at Solapur	Line Reactor	WR	POWERGRID	TS	24-Jun-2023 16:18	'SLR tripped on R phase Buchholz' alarm operate	24-Jun-2023 21:34	05:16:00	1
115	330MVAR LR(S) of 765kv Gadarwara - Warora Ckt-I at Gadarwara	Line Reactor	WR	NTPC/PWTL-PG	TS	25-Jun-2023 23:25	Bucholz trip of Warora-Gadarwara Line 2 Reactor	27-Jun-2023 19:06	43:41:00	1
116	765KV-VADODARA-LAKADIA-1 L/R@ VADODARA - 765KV	Line Reactor	WR	LVTPL	SO	29-Jun-2023 11:12	For CSD Fine Tuning of Line Reactor 1 at Vadodara end. Live switching of Reactor required, atleast 5-6 operations	29-Jun-2023 16:18	05:06:00	0
117	765KV-VADODARA-LAKADIA-2 L/R@ VADODARA - 765KV	Line Reactor	WR	LVTPL	SO	29-Jun-2023 16:59	For CSD Fine Tuning of Line Reactor 2 at Vadodara end. Live switching of Reactor required, atleast 5-6 operations	29-Jun-2023 18:39	01:40:00	0
Eastern Region Elements										
1	765KV/400KV 1500 MVA ICT 1 AT NEW JEERAT	ICT	ER	WBSETCL	SO	04-Jun-2023 05:07	Testing of ICT-1 R phase unit	05-Jun-2023 00:01	18:54:00	0
2	765/400KV 1500MVA ICT-I at JHARSUGUDA	ICT	ER	POWERGRID	TS	20-Jun-2023 20:26	Tripped due to LBB operation and inter trip.	20-Jun-2023 22:22	01:56:00	1

NLDC Outage report of Month June 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
3	765 kV ANGUL - JHARSUGUDA Ckt-IV	Line	ER	POWERGRID	MO	01-Jun-2023 00:00	Voltage Regulation	26-Jun-2023 08:34	608:34:00	0
4	765kV Medinipur - New Jeerut Ckt-II	Line	ER	PMJTL	TL	11-Jun-2023 18:33	MEDINIPUR: R-Y, 126.7 KM F/C R phase:4.54 kA, Y phase 3.26 kA Jeerat: R-Y, 49.2 KM, R phase: 5.9 kA Y phase: 5.8 kA	11-Jun-2023 20:05	01:32:00	1
5	765kV NEW RANCHI - MEDINIPUR Ckt-II	Line	ER	POWERGRID/P MJTL	SO	18-Jun-2023 06:19	For replacement of CLR insulator damaged due to lightening at tower no. 698 (B-phase)	18-Jun-2023 19:53	13:34:00	0
6	765kV Medinipur - New Jeerut Ckt-I	Line	ER	PMJTL	TL	19-Jun-2023 10:53	Medinipur:- R-N, FAULT CUREENT :- 4.83KA, 118km, NIL	19-Jun-2023 19:03	08:10:00	1
7	765KV-ANGUL-JHARSUGUDA-1	Line	ER	PG (ODISHA PROJECT)	SO	26-Jun-2023 08:55	AMP of Line and associated LR	26-Jun-2023 22:58	14:03:00	0
8	765 kV ANGUL - JHARSUGUDA Ckt-III	Line	ER	POWERGRID	MO	26-Jun-2023 23:14	Voltage Regulation	27-Jun-2023 08:34	09:20:00	0
9	765KV-ANGUL-JHARSUGUDA-2	Line	ER	PG (ODISHA PROJECT)	SO	27-Jun-2023 08:57	Yearly AMP	27-Jun-2023 20:32	11:35:00	0
10	240MVAR SWITCHABLE L/R OF 765KV-ANGUL-JHARSUGUDA-1	Line Reactor	ER	PG (ODISHA PROJECT)	SO	26-Jun-2023 08:55	AMP Work	26-Jun-2023 22:58	14:03:00	0
11	240MVAR SWITCHABLE L/R OF 765KV-JHARSUGUDA-ANGUL-1	Line Reactor	ER	PG (ODISHA PROJECT)	SO	26-Jun-2023 08:55	AMP of Line and associated LR	26-Jun-2023 22:58	14:03:00	0
12	240MVAR SWITCHABLE L/R OF 765KV-JHARSUGUDA-ANGUL-2	Line Reactor	ER	PG (ODISHA PROJECT)	SO	27-Jun-2023 08:57	AMP WORK	27-Jun-2023 20:32	11:35:00	0
13	240MVAR SWITCHABLE L/R OF 765KV-JHARSUGUDA-ANGUL-3	Line Reactor	ER	PG (ODISHA PROJECT)	SO	27-Jun-2023 08:57	Yearly AMP	27-Jun-2023 20:32	11:35:00	0

Southern Region Elements

1	+/- 320kV PUGALUR - THRISSUR Pole-II	HVDC	SR	POWERGRID	SO	07-Jun-2023 10:39	Replacement of faulty/failed electronic module of zero flux CT at Transition station	07-Jun-2023 12:47	02:08:00	0
2	765KV/400KV NIZAMABAD-ICT-1	ICT	SR	pgsr1_sd	SO	04-Jun-2023 09:05	AMP WORKS	04-Jun-2023 18:54	09:49:00	0
3	765KV/400KV RAICHUR_PG-ICT-2	ICT	SR	pgsr1_sd	SO	16-Jun-2023 08:22	AMP WORKS	16-Jun-2023 22:15	13:53:00	0
4	765kV CHILAKALURIPETA - CUDDAPAH Ckt-I	Line	SR	POWERGRID	MO	01-Jun-2023 00:00	Voltage Regulation	19-Jun-2023 09:49	441:49:00	0
5	765kV NIZAMABAD - MAHESHWARAM Ckt-I	Line	SR	POWERGRID	MO	01-Jun-2023 00:00	Voltage Regulation	12-Jun-2023 07:52	271:52:00	0
6	765kV SRIKAKULAM - VEMAGIRI Ckt-II	Line	SR	POWERGRID	TL	07-Jun-2023 20:02	R-G fault	07-Jun-2023 21:32	01:30:00	1
7	765kV SRIKAKULAM - VEMAGIRI Ckt-II	Line	SR	POWERGRID	TL	12-Jun-2023 12:18	Tripped on Y-N fault ,VMG:M1-FD:172.8KM,FC-2.74KA,M2-FD:197.9KM,FC-2.73KA SKLM:M1-FD:126.1KM,FC-3.57KA,M2-FD:130.5KM,FC-4.31KA	12-Jun-2023 13:05	00:47:00	2
8	765kV NIZAMABAD - MAHESHWARAM Ckt-II	Line	SRLDC	POWERGRID	MO	15-Jun-2023 17:46	Voltage Regulation	01-Jul-2023 00:00	366:14:00	0
9	765kV CUDDAPAH - THIRUVALAM Ckt-I	Line	SRLDC	POWERGRID	MO	19-Jun-2023 20:00	Voltage Regulation	01-Jul-2023 00:00	268:00:00	0
10	765kV CHILAKALURIPETA - CUDDAPAH Ckt-I	Line	SRLDC	POWERGRID	MO	19-Jun-2023 20:46	Voltage Regulation	01-Jul-2023 00:00	267:14:00	0

North Eastern Region Elements

Nil

	TL= Tripping due to Line Fault
	TS= Tripping due to S/S Fault
	MO= Opened due to system constraints
	TV= Tripped on Overvoltage
	SC= Planned Shutdown for construction activities
	SO= Planned Shutdown for O&M activities
	SE= Emergency Shutdown
	TP= Protection Maloperation
	ME= Miscellaneous outage

24. ALL TIME HIGHEST

30-06-2023

	Maximum Demand Met during the day (MW)	Demand Met during Evening Peak hrs(MW)	Energy Met (MU)	Hydro Gen. (MU)	Wind Gen. (MU)	Solar Gen. (MU)
NR	77341 23-06-2023 (22:55)	76072 23-06-2023	1737 28-06-2022	420 22-08-2022	78 09-06-2022	147 10-05-2023
WR	71321 27-12-2022	63593 18-04-2023 (20:00)	1539 18-04-2023	167 18-12-2014	272 22-05-2022	70.69 12-05-2023
SR	64314 15-03-2023	52366 18-04-2023 (20:00)	1329 19-04-2023	208 31-08-2018	297 12-07-2022	142.7 21-03-2023
ER	29325 09-06-2023 (00:13)	28579 18-04-2023 (20:00)	639 08-06-2023	157 14-09-2022	-	7 23-03-2023
NER	3603 17-08-2022	3510 12-08-2022	69 11-08-2022	41 01-08-2022	-	2 22-06-2022
All India	223235 09-06-2023 (14:52)	211250 22-06-2023	4914 13-06-2023	877 30-08-2022	555 22-05-2022	351 10-05-2023

Regions	States	Max. Demand Met during the day (MW)		Energy Consumption (MU)	
			As on date		As on date
NR	Punjab	15237	23-06-2023 (13:00)	343.5	24-06-2023
	Haryana	12540	28-06-2022	266.2	07-07-2021
	Rajasthan	17097	23-01-2023	332.2	13-06-2023
	Delhi	7770	29-06-2022	153.5	28-06-2022
	UP	27292	13-06-2023 (23:00)	568.5	17-06-2023
	Uttarakhand	2594	14-06-2022	55.8	17-06-2023
	HP	2071	06-01-2023	39.6	05-06-2022
	J&K(UT) and Ladakh(UT)	3636	29-06-2023 (08:00)	65.4	20-01-2023
	Chandigarh	426	08-07-2021	8.4	08-07-2021
	Railways NR ISTS	-	-	-	-
WR	Chhattisgarh	5642	18-04-2023	129.8	19-04-2023
	Gujarat	22225	09-06-2023 (15:00)	462.3	09-06-2023
	MP	17238	13-01-2023	329.3	10-01-2023
	Maharashtra	28846	14-04-2022	636.1	21-06-2023
	Goa	776	07-06-2023	17.1	08-06-2023
	DD & DNH	1311	21-06-2023 (17:00)	30.7	24-06-2023
	AMNSIL	977	18-08-2021	21.0	31-05-2022
	Balco	-	-	-	-
SR	Andhra Pradesh*	12900	17-06-2023 (13:42)	263.8	16-06-2023
	Telangana*	15497	30-03-2023	303.4	03-03-2023
	Karnataka	16110	20-04-2023	309.5	20-04-2023
	Kerala	5024	18-04-2023	103.3	19-04-2023
	Tamil Nadu	19387	20-04-2023	415.4	20-04-2023
	Pondy	512	17-05-2023	11.6	18-05-2023
ER	Bihar	7071	16-06-2023 (21:00)	148.5	08-06-2023
	DVC	3751	18-04-2023	81.2	22-04-2022
	Jharkhand	1923	16-06-2023 (20:36)	43.3	17-06-2023
	Odisha	7192	19-04-2023	145.5	25-09-2022
	West Bengal	11868	18-04-2023	245.7	18-04-2023
	Sikkim	137	03-02-2022	2.5	28-01-2020
	Railways ER ISTS	-	-	-	-
NER	Arunachal Pradesh	172	31-05-2023	3.1	07-06-2023
	Assam	2376	12-08-2022	47.6	07-06-2023
	Manipur	258	31-01-2022	3.7	10-02-2022
	Meghalaya	415	09-02-2022	7.8	31-01-2022
	Mizoram	157	16-01-2023	2.3	18-01-2023
	Nagaland	170	08-06-2023 (19:06)	3.1	15-07-2022
	Tripura	370	07-06-2023	7.0	06-06-2023
*SR	Andhra Pradesh (Undivided)	13162	23-03-2014	284.8	22-03-2014

25. System Reliability Indices Report for the month of June 2023

Percentage (%) of times ATC was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	0	0.00	0.00
2	ER-NR	0	0.00	0.00
3	Import of NR	0	0.00	0.00
4	NEW-SR	0	0.00	0.00
5	NER Import	0	0.00	0.00

Percentage(%) of times (N-1) Criteria was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	0	0.00	0.00
2	ER-NR	0	0.00	0.00
3	Import of NR	0	0.00	0.00
4	NEW-SR	0	0.00	0.00
4	NER Import	0	0.00	0.00

Remarks: Flows crossing Total Transfer Capability (TTC) on interregional corridors has been worked out as a proxy for (N-1) violation.



POWER SYSTEM OPERATION CORPORATION LIMITED

पावर सिस्टम ऑपरेशन कारपोरेशन लिमिटेड

NATIONAL LOAD DESPATCH CENTRE – राष्ट्रीय भार प्रेषण केन्द्र

First floor, B-9, Qutab Institutional Area,
Katwaria Sarai, New Delhi-110016.
