

संदर्भ संख्या : - GRID-INDIA/NLDC/MR/

दिनांक : 23.11.2023

सेवा में,

वितरण सूची के अनुसार

विषय:- निष्पादन रिपोर्ट - अक्टूबर 2023

महोदय,

आई०ई०जी०सी०-2010 के प्रावधान के अनुसार, अक्टूबर 2023 माह की अखिल भारतीय प्रणाली की निष्पादन रिपोर्ट संलग्न है।

धन्यवाद

भवदीय



(सुरजीत बनर्जी)

मुख्य महाप्रबन्धक (प्रणाली प्रचालन)

(रा०भा०प्रे०के०)

संलग्नक : मासिक प्रणाली रिपोर्ट

वितरण सूची Distribution List

- 1 सचिव, के.वि.नि.आ. तीसरा एवं चौथा तल, चंद्रलोक भवन, 36, जनपथ, नई दिल्ली-110001
Secretary, CERC, 3rd & 4th Floor, Chanderlok Building, 36, Janpath, New Delhi-110001
- 2 मुख्य अभियंता (जी एम), के.वि.प्रा., सेवा भवन, आर. के. पुरम, नई दिल्ली-110066
Chief Engineer (GM), CEA, Sewa Bhavan, R.K.Puram, New Delhi-110066
- 3 सदस्य सचिव, उ. क्षेत्र. वि. स., 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली - 110016
Member Secretary, NRPC, 18/A, SJSS Marg, Katwaria Sarai, New Delhi-110016
- 4 सदस्य सचिव, प. क्षेत्र. वि. स., एफ-3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई - 400093
Member Secretary, WRPC, F-3, MIDC Area, Andheri (East), Mumbai-400093
- 5 सदस्य सचिव, द. क्षेत्र. वि. स., 29, रेस कोर्स क्रॉस रोड, बंगलूरु - 560009
Member Secretary, SRPC, 29, Race Course Cross Road, Bangalore-560009
- 6 सदस्य सचिव, पू. क्षेत्र. वि. स., 14, गोल्फ क्लब रोड, कोलकाता - 700033
Member Secretary, ERPC, 14, Golf Club Road, Kolkata-700033
- 7 सदस्य सचिव, उ. पू. क्षेत्र. वि. स., मेघालय राज्य आवासीय वित्त सहकारी समिति लिमिटेड भवन, नॉग्रिम हिल्स, शिलोंग - 793003
Member Secretary, NERPC, Meghalaya State Housing Finance Cooperative Society Ltd. Building, Nongrim Hills, Shillong -793003
- 8 मुख्य अभियंता, राष्ट्रीय विद्युत समिति, एनआरपीसी भवन, तृतीय तल, 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली - 110016
Chief Engineer, National Power Committee, NRPC Building, 3rd floor, 18/A, SJSS Marg, Katwaria Sarai, New Delhi-110016
- 9 कार्यपालक निदेशक, पू. क्षेत्र. भा. प्रे. के., 14, गोल्फ क्लब रोड, कोलकाता - 700033
Executive Director, ERLDC, 14, Golf Club Road, Kolkata-700033
- 10 कार्यपालक निदेशक, प. क्षेत्र. भा. प्रे. के., एफ-3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई - 400093
Executive Director, WRLDC, F-3, MIDC Area, Andheri (East), Mumbai-400093
- 11 कार्यपालक निदेशक, उ. क्षेत्र. भा. प्रे. के., 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली - 110016
Executive Director, NRPC, 18/A, SJSS Marg, Katwaria Sarai, New Delhi-110016
- 12 कार्यपालक निदेशक, द. क्षेत्र. भा. प्रे. के., 29, रेस कोर्स क्रॉस रोड, बंगलूरु - 560009
Executive Director, SRLDC, 29, Race Course Cross Road, Bangalore-560009
- 13 मुख्य महाप्रबंधक, पू. क्षेत्र. भा. प्रे. के., डोंगतिह, लोअर नॉग्रह, लापलंग, शिलोंग- 793006
Chief General Manager, NERLDC, Dongtiah, Lower Nongrah, Laplang, Shillong-793006



ग्रिड-इंडिया
GRID-INDIA

GRID CONTROLLER OF INDIA LIMITED

Formerly Power System Operation Corporation Limited

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड

NATIONAL LOAD DESPATCH CENTRE –राष्ट्रीय भार प्रेषण केन्द्र

मासिक ऑपरेशन रिपोर्ट

**Monthly
Operation Report**



अक्टूबर 2023

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड
राष्ट्रीय भार प्रेषण केंद्र, नई दिल्ली

GRID CONTROLLER OF INDIA LIMITED

Formerly Power System Operation Corporation Limited

NATIONAL LOAD DESPATCH CENTRE, NEW DELHI



ग्रिड-इंडिया
GRID-INDIA

माह अक्टूबर 2023 के लिए प्रचालन निष्पादन रिपोर्ट
OPERATIONAL PERFORMANCE REPORT FOR THE
MONTH OF OCTOBER-2023


पृष्ठसूची CONTENTS

1	माह अक्टूबर 2023 की सारांश रिपोर्ट Summary of report for the month of OCTOBER 2023	1-5
2	क्षेत्रवार स्थापित विद्युत क्षमता Region wise Installed Capacity	6
3	राष्ट्रीय स्तर पर सांध्यकालीन शिखर मांगपूर्ति Peak demand met at National level	7-8
4	राष्ट्रीय स्तर पर विद्युत ऊर्जा खपत Energy consumption at National level	9-10
5	फ्रिक्वेंसी रूपरेखा Frequency profile	11-12
6	राष्ट्रीय स्तर पर जल विद्युत ऊर्जा उत्पादन Hydro generation at National level	13-14
7	राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन Wind generation at National level	15
8	राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन Solar generation at National level	16
9	राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग पूर्ति Daily maximum demand met at National level	17
10	10 अक्टूबर के माँग एवं उत्पादन प्लॉट (अधिकतम माँग पूर्ति) व माँग का डाटा (15 मिनट अंतराल) Demand and generation plots for 10-OCTOBER (Max Demand Met) and Demand data (15-minute interval)	18-22
11	ऊर्जा आपूर्ति की वास्तविक स्थिति Actual power supply position	23
12	ऊर्जा आवश्यकता एवं आपूर्ति की पिछले वर्ष माह अक्टूबर 2022 से तुलना Energy requirement and met comparison with OCTOBER 2022	24
13	शिखर माँग आवश्यकता एवं आपूर्ति की पिछले वर्ष माह अक्टूबर 2022 से तुलना Peak demand requirement and met comparison with OCTOBER 2022	25


14	क्षेत्रीय स्तर पर शिड्यूल एवं ड्रावल Schedule & drawal at regional level	26
15	अंतर क्षेत्रीय विनिमय Inter-regional exchanges	27-36
16	अंतर राष्ट्रीय विद्युत विनिमय Inter-national exchanges	37-39
17	एसटीओए (द्विपक्षीय एवं सामूहिक) एवं यू आइ का ब्यौरा Bilateral and collective short-term open access & UI details	40
18	पावर मार्केट की सूचना Power market information	41-44
19	अक्षय ऊर्जा प्रमाण पत्र प्रक्रिया Renewable energy certificate mechanism	45-47
20	मुख्य घटनाएँ एवं डिस्टर्बेंस Important events/disturbances	48-54
21	नए कमीशंड पारेषण तत्व New elements commissioned	55
22	विभव रूपरेखा Voltage profile	56
23	अक्टूबर 2023 के दौरान रा. भा. प्रे. के. द्वारा निगरानी में तत्वों के आउटेज की सूची List of outage of elements monitored by NLDC for the month of OCTOBER 2023 (To be updated)	-
24	अब तक उच्चतम (मांग व ऊर्जा) आँकड़े : माह अक्टूबर 2023 तक All Time Highest (Demand & Energy) figures: Till OCTOBER 2023	57
25	अक्टूबर 2023 के लिए सिस्टम रिलाइबिलिटी सूचकांक System Reliability Indices for OCTOBER 2023	58

1. SUMMARY OF REPORT FOR THE MONTH OF OCTOBER-2023

EVENING PEAK HOUR (at 1900hrs) DEMAND MET AT NATIONAL LEVEL (MW)

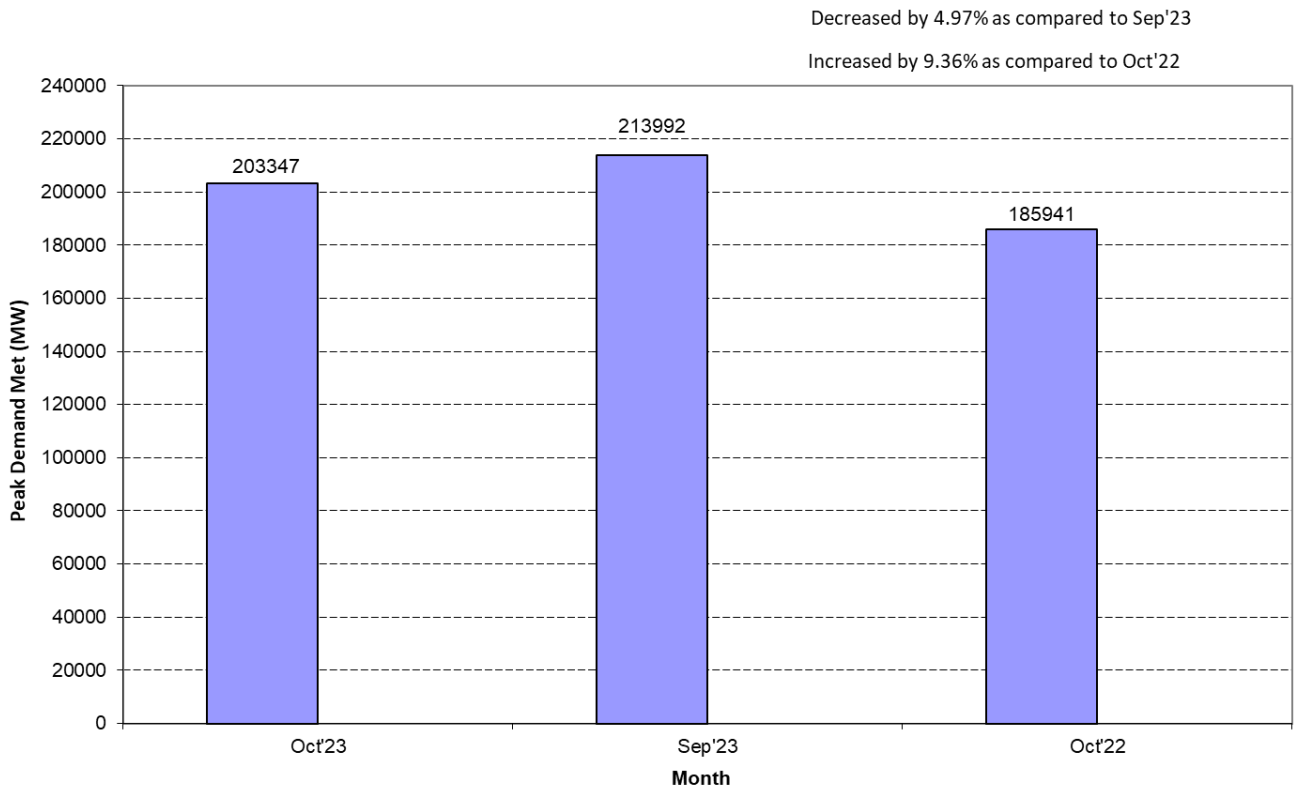


Frequency within IEGC Band

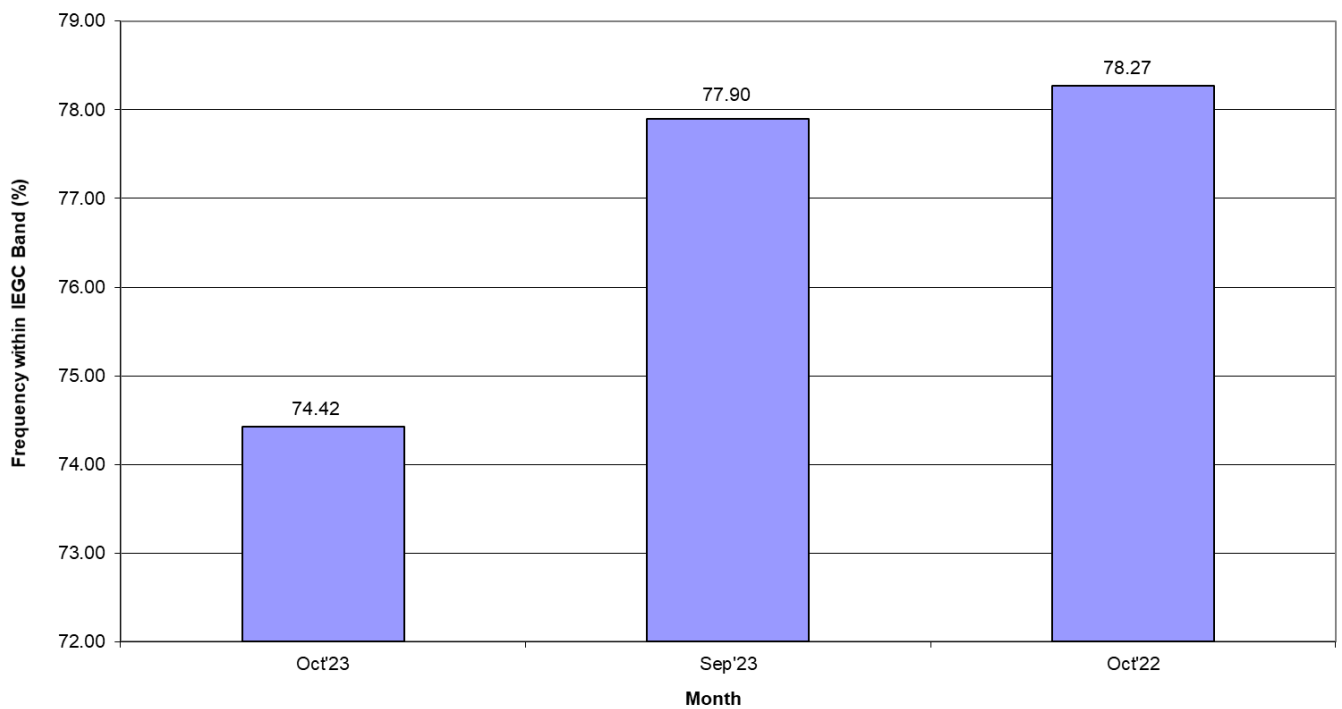

ENERGY MET AT NATIONAL LEVEL (MU)


Decreased by 1.10% as compared to Sep'23

Increased by 21.07% as compared to Oct'22

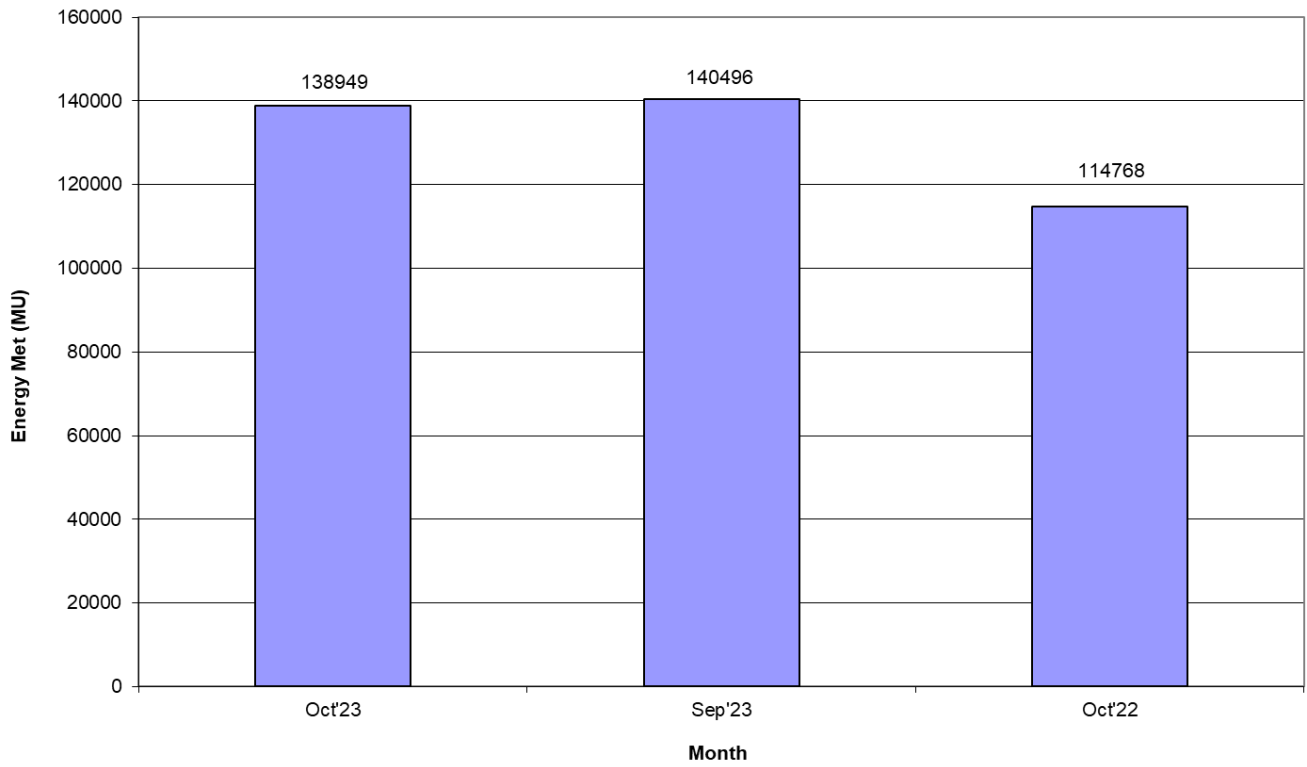

AVERAGE ENERGY MET AT NATIONAL LEVEL (MU/Day)


Increased by 21.07% as compared to Oct'22

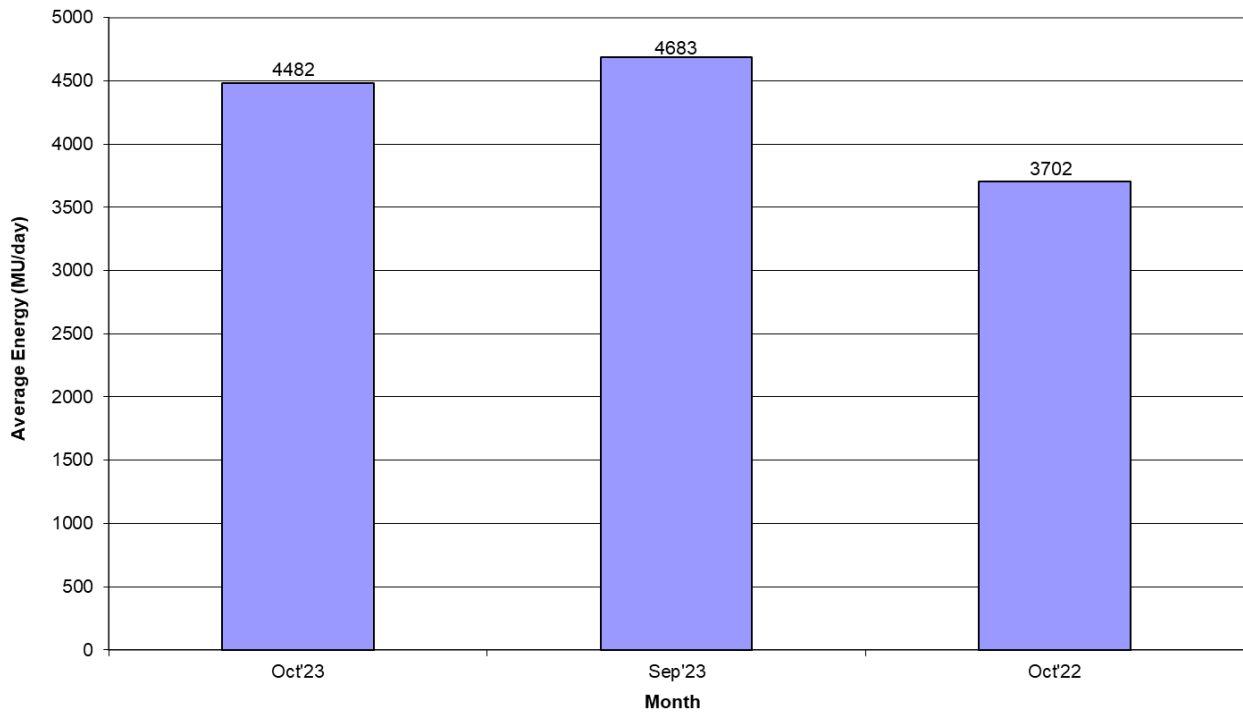

HYDRO GENERATION AT NATIONAL LEVEL (MU)


Decreased by 30.23% as compared to Sep'23

Decreased by 29.87% as compared to Oct'22

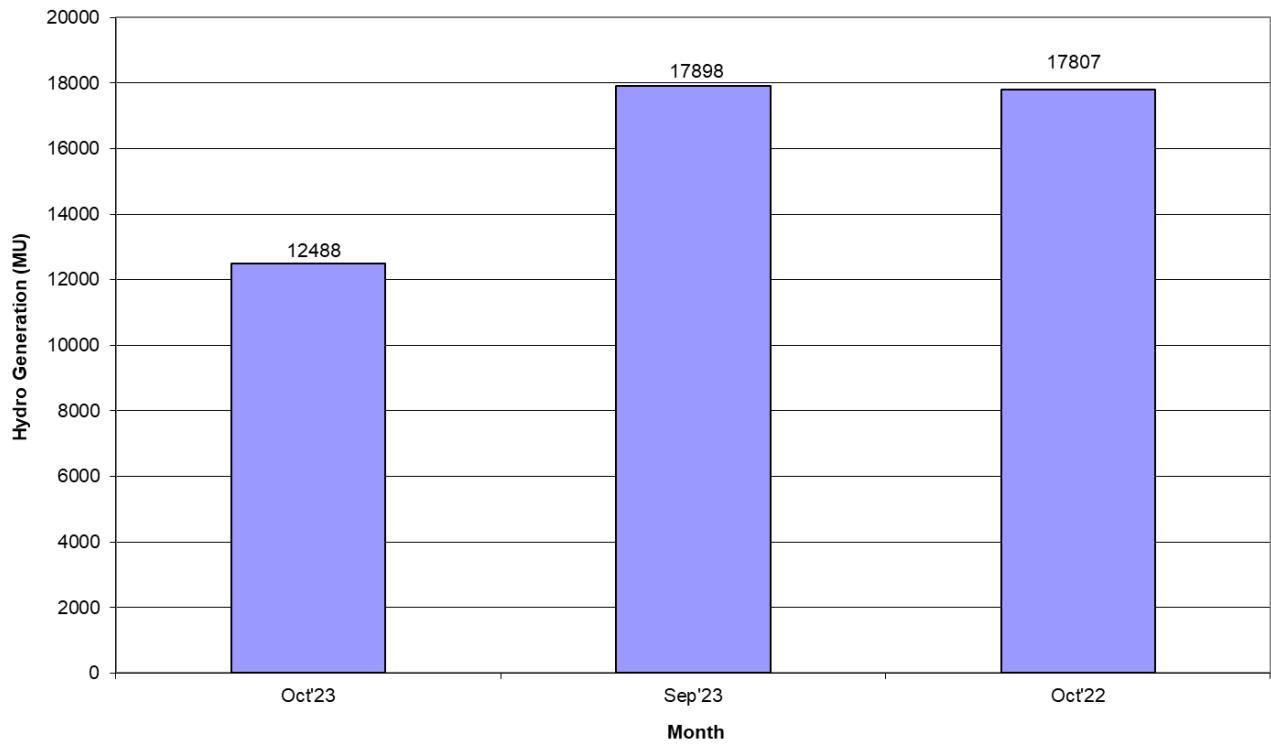

AVERAGE HYDRO GENERATION AT NATIONAL LEVEL (MU/Day)


Decreased by 29.87% as compared to Oct'22

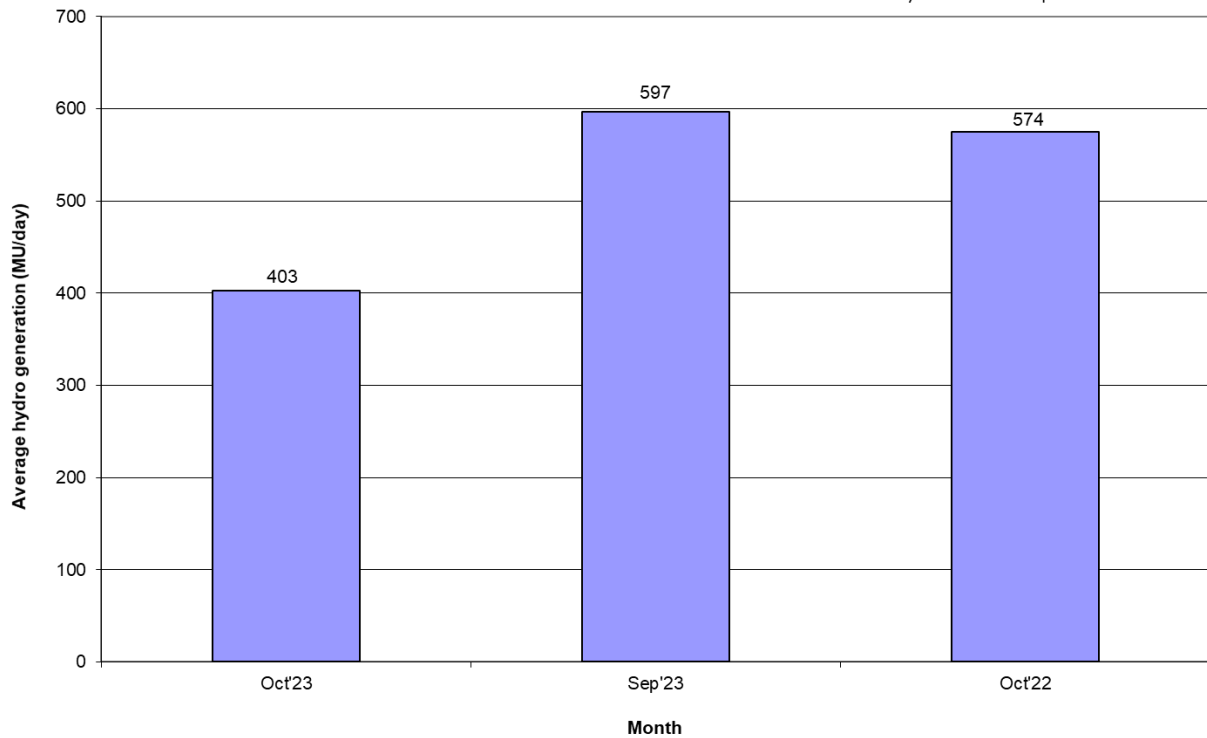

WIND GENERATION AT NATIONAL LEVEL (MU)


Decreased by 59.20% as compared to Sep'23

Increased by 10.25% as compared to Oct'22

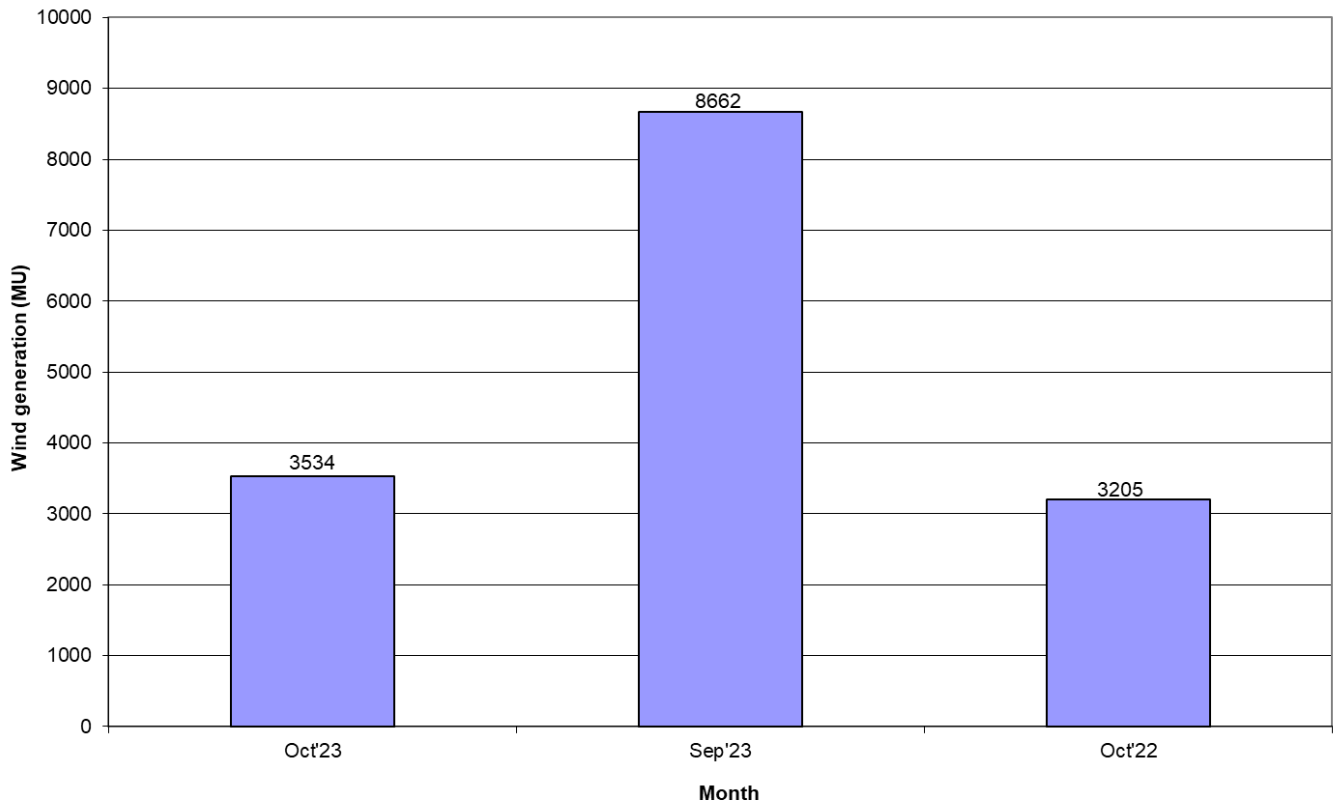

AVERAGE WIND GENERATION AT NATIONAL LEVEL (MU/Day)


Increased by 10.25% as compared to Oct'22

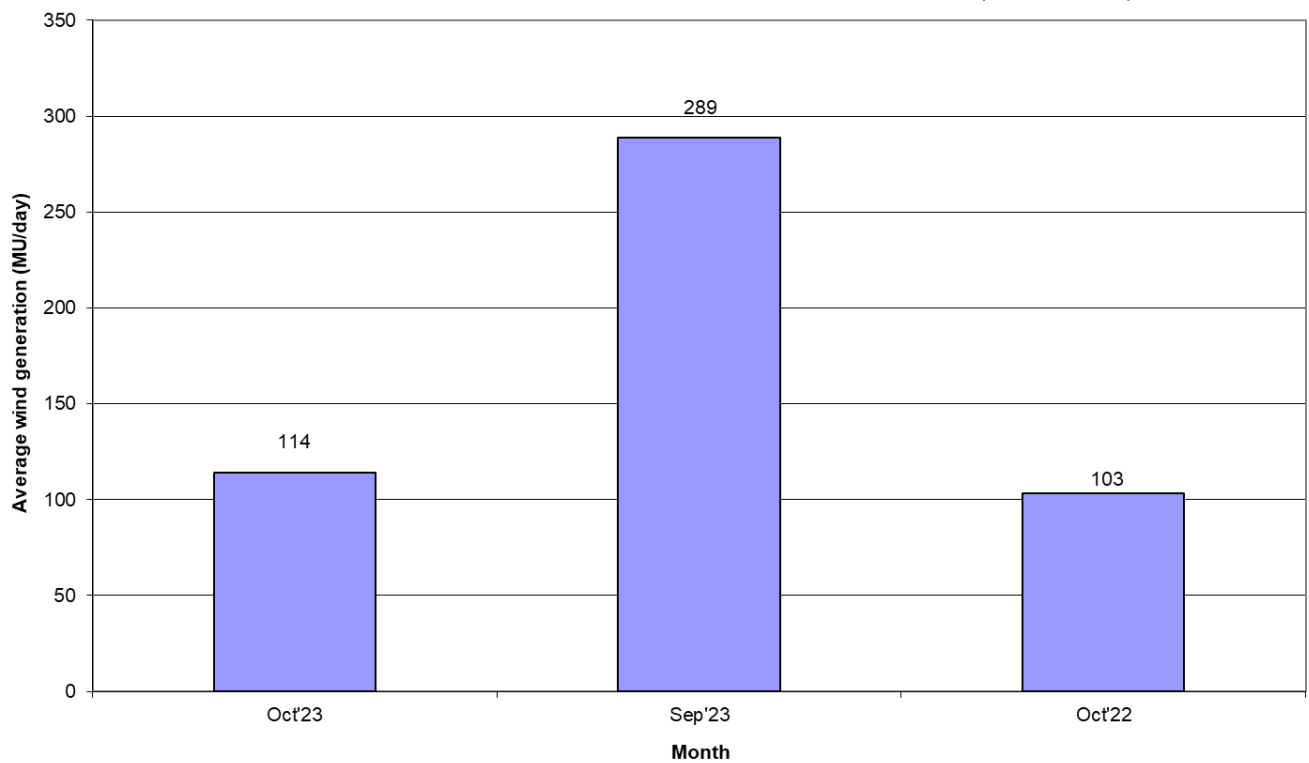

SOLAR GENERATION AT NATIONAL LEVEL (MU)


Increased by 9.22% as compared to Sep'23

Increased by 13.22% as compared to Oct'22

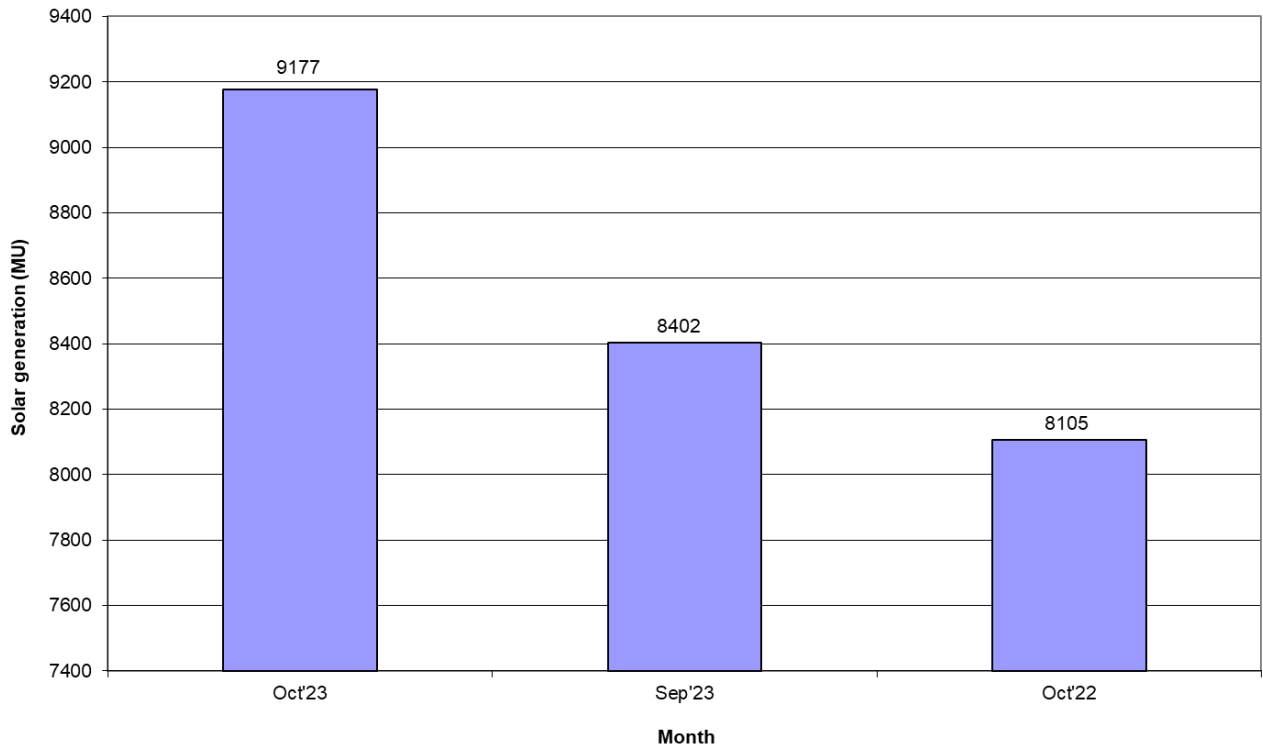

AVERAGE SOLAR GENERATION AT NATIONAL LEVEL (MU/Day)

Increased by 13.22% as compared to Oct'22

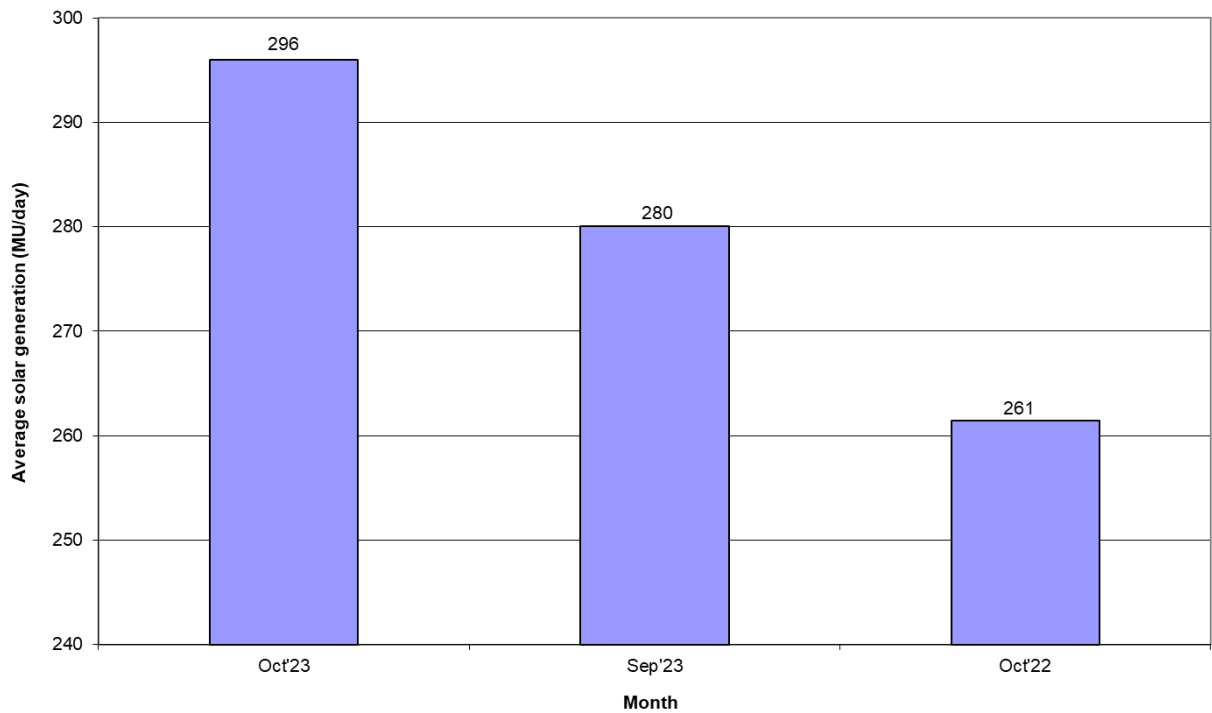

2. ALL INDIA REGIONWISE INSTALLED CAPACITY

As on 31.10.2023
(All figures are in MW)

S No	Region	THERMAL					NUCLEAR	HYDRO	RES @ MNRE	GRAND TOTAL
		COAL	LIGNITE	GAS	DIESEL	TOTAL				
1	NR	55517	1580	5995	0	63092	1620	20752	34540	120004
2	WR	74513	1400	10806	0	86719	2540	7563	42755	139577
3	SR	47578	3640	6492	434	58144	3320	11827	52326	125617
4	ER	28448	0	80	0	28528	0	4764	1896	35188
5	NER	770	0	1665	36	2471	0	1944	574	4989
6	ISLANDS	0	0	0	120	120	0	0	40	159
	ALL INDIA	206825	6620	25038	589	239073	7480	46850	132132	425536

Remarks: Data from CEA website

3. राष्ट्रीय स्तर पर संध्याकालीन शिखर विद्युत मांग पूर्ति
EVENING PEAK HOUR DEMAND MET AT NATIONAL LEVEL


माह: अक्टूबर 2023 MONTH:- OCT 2023

सभी आंकड़े मेगावाट मे All figures in MW

दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
1-Oct-23	64342	56337	41049	22966	3354	188048
2-Oct-23	59602	58555	43735	23549	3397	188838
3-Oct-23	62644	61052	48612	22976	3374	198658
4-Oct-23	62892	61821	48485	22992	3170	199360
5-Oct-23	61972	62954	48843	23694	3131	200594
6-Oct-23	62576	63178	48804	24309	2946	201813
7-Oct-23	61256	63450	48024	24435	2945	200110
8-Oct-23	60967	61107	44794	23988	2979	193835
9-Oct-23	60787	64571	48151	24383	2928	200820
10-Oct-23	61156	64753	47743	25338	3111	202101
11-Oct-23	60305	64674	49324	25839	3150	203292
12-Oct-23	59562	64668	48735	25472	3118	201555
13-Oct-23	60244	65518	49160	25311	3114	203347
14-Oct-23	58864	64891	47599	24982	3236	199572
15-Oct-23	56959	61759	44284	24425	2993	190420
16-Oct-23	48483	64367	48032	24716	3171	188769
17-Oct-23	52052	63938	48956	23720	3089	191755
18-Oct-23	53762	65252	49146	23998	3065	195223
19-Oct-23	52662	65453	49545	23994	3047	194701
20-Oct-23	52740	64926	48554	23365	3055	192640
21-Oct-23	53010	63842	47719	22200	2958	189729
22-Oct-23	49875	61119	47304	21285	2630	182213
23-Oct-23	51659	61443	45259	20003	2536	180900
24-Oct-23	45392	55136	48078	18827	2458	169891
25-Oct-23	52776	62806	48827	20973	2691	188073
26-Oct-23	52760	63577	49306	22438	2820	190901
27-Oct-23	52438	62108	48888	21974	2838	188246
28-Oct-23	52200	61652	48838	21656	2836	187182
29-Oct-23	49812	59546	43076	20915	2698	176047
30-Oct-23	53254	62389	47244	22068	2811	187766
31-Oct-23	53662	62406	47744	22134	2901	188847
उच्चतम MAXIMUM	64342	65518	49545	25839	3397	203347
निम्नतम MINIMUM	45392	55136	41049	18827	2458	169891
औसत AVERAGE	56150	62556	47544	23191	2985	192427
अब तक का उच्चतम All Time Max.	76274	65518	52366	28579	3510	215592
दिनांक Date	04.09.23	13.10.23	18.04.23	18.04.23	12.08.22	28.08.23

नोट : सभी आंकड़े 1900 बजे की मांगपूर्ति पर आधारित है ।
 Note: The above figures correspond to value at 2000 Hrs

EVENING PEAK HOUR DEMAND(at 1900hrs)MET DURING THE MONTH OF OCTOBER 2023

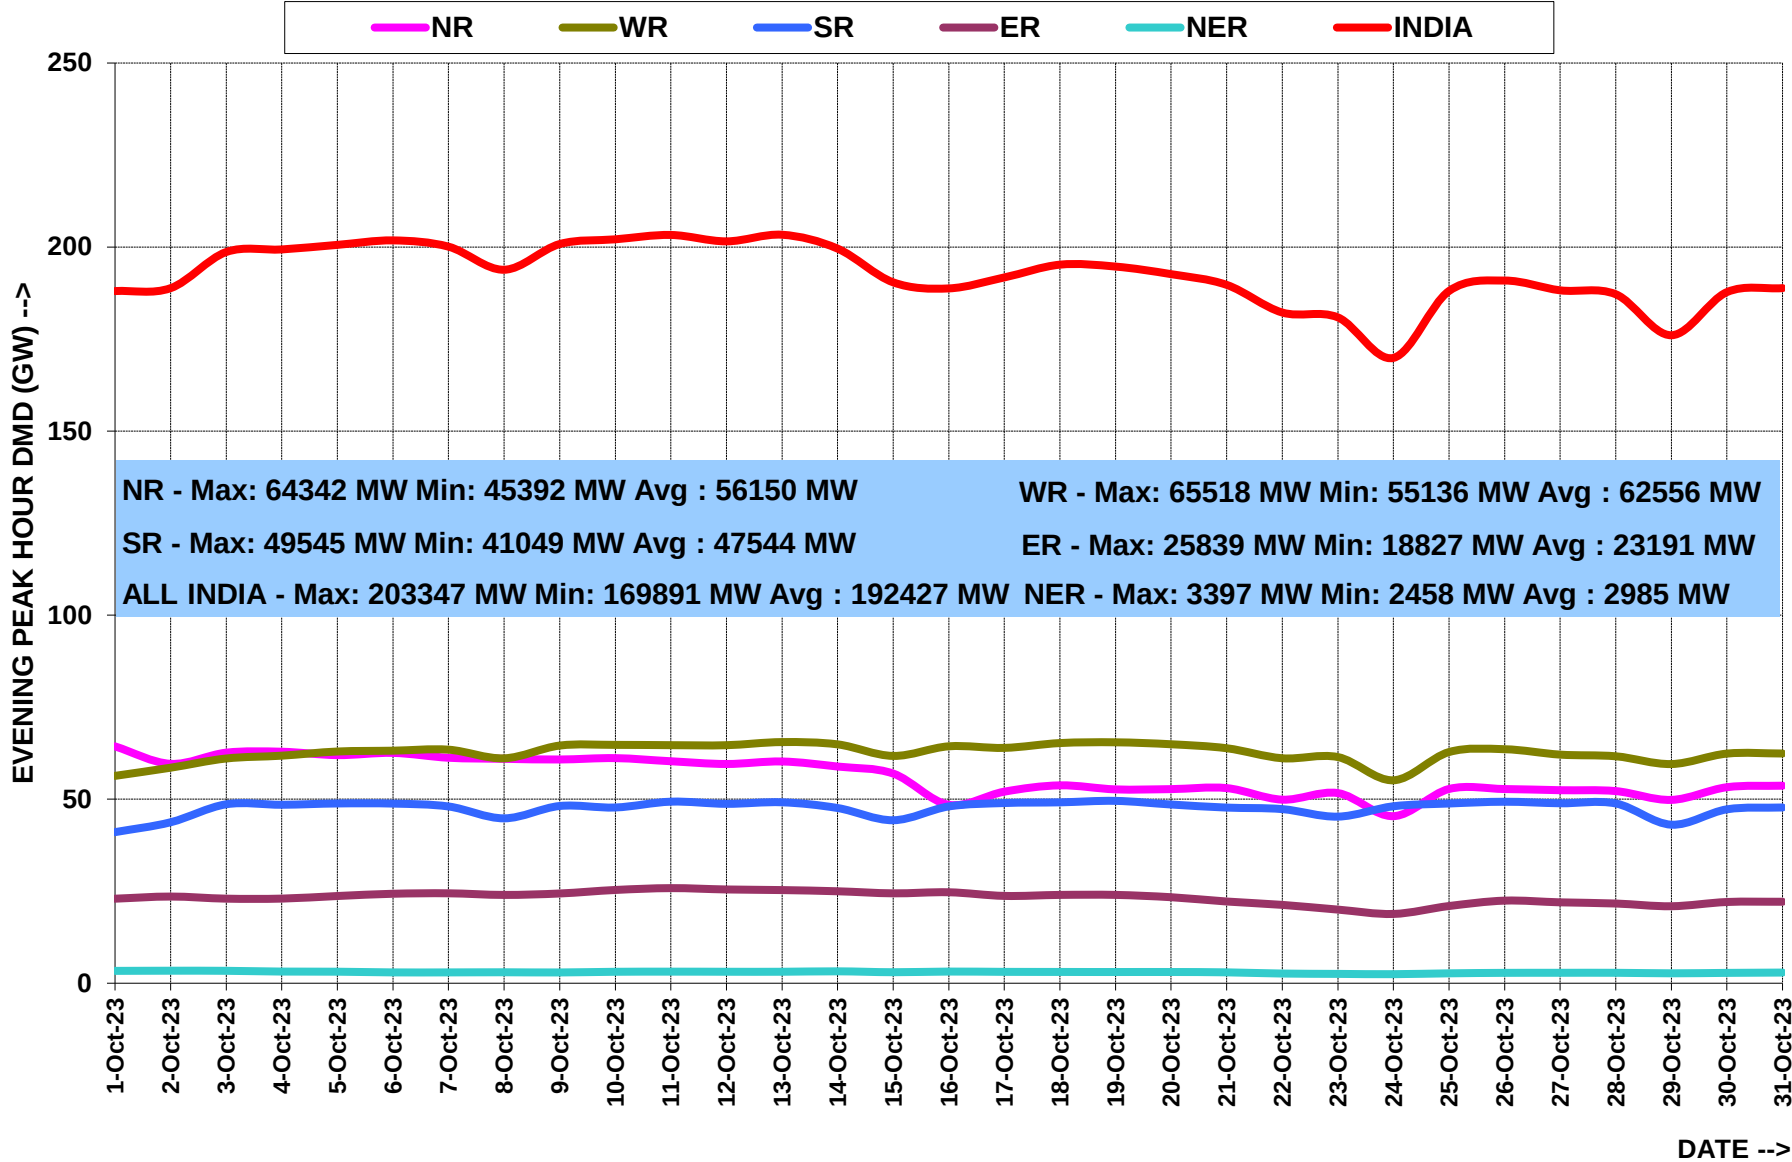


4. राष्ट्रीय स्तर पर विद्युत ऊर्जा आपूर्ति ENERGY MET AT NATIONAL LEVEL

माह: अक्टूबर 2023 MONTH:- OCT 2023

सभी आंकड़े मिलियन यूनिट में All figures in MU

दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Oct-23	1415	1297	1041	501	62	4317
02-Oct-23	1335	1305	1039	501	64	4245
03-Oct-23	1347	1359	1156	502	63	4427
04-Oct-23	1367	1376	1219	494	61	4517
05-Oct-23	1378	1390	1233	498	59	4558
06-Oct-23	1401	1430	1243	525	53	4651
07-Oct-23	1398	1433	1230	546	56	4662
08-Oct-23	1406	1422	1187	548	54	4618
09-Oct-23	1422	1472	1226	560	55	4735
10-Oct-23	1425	1495	1221	564	59	4764
11-Oct-23	1423	1509	1215	570	62	4779
12-Oct-23	1399	1519	1215	564	61	4758
13-Oct-23	1397	1526	1234	558	59	4773
14-Oct-23	1360	1528	1225	549	59	4721
15-Oct-23	1270	1489	1152	528	56	4494
16-Oct-23	1141	1469	1205	545	55	4415
17-Oct-23	1053	1520	1206	535	58	4372
18-Oct-23	1119	1532	1223	529	58	4461
19-Oct-23	1130	1552	1240	523	58	4503
20-Oct-23	1149	1536	1249	502	57	4493
21-Oct-23	1151	1536	1218	480	56	4441
22-Oct-23	1103	1508	1178	458	51	4298
23-Oct-23	1126	1514	1132	444	48	4264
24-Oct-23	1079	1425	1151	442	45	4142
25-Oct-23	1116	1481	1207	460	49	4313
26-Oct-23	1151	1529	1232	484	52	4449
27-Oct-23	1152	1520	1240	474	53	4439
28-Oct-23	1141	1507	1227	467	54	4395
29-Oct-23	1101	1480	1152	449	50	4233
30-Oct-23	1148	1515	1157	461	51	4332
31-Oct-23	1171	1522	1164	469	53	4378
कुल TOTAL	38774	45693	37018	15729	1735	138949
उच्चतम MAXIMUM	1425	1552	1249	570	64	4779
निम्नतम MINIMUM	1053	1297	1039	442	45	4142
औसत AVERAGE	1251	1474	1194	507	56	4482
संचयी 2023-24 Cumulative 2023-24	300884	297829	245815	119153	12474	976155
अब तक का उच्चतम All Time Max.	1796	1618	1329	639	72	5224
दिनांक Date	04.09.23	02.09.23	19.04.23	08.06.23	15.09.23	02.09.23

ENERGY MET DURING THE MONTH OF OCTOBER' 2023

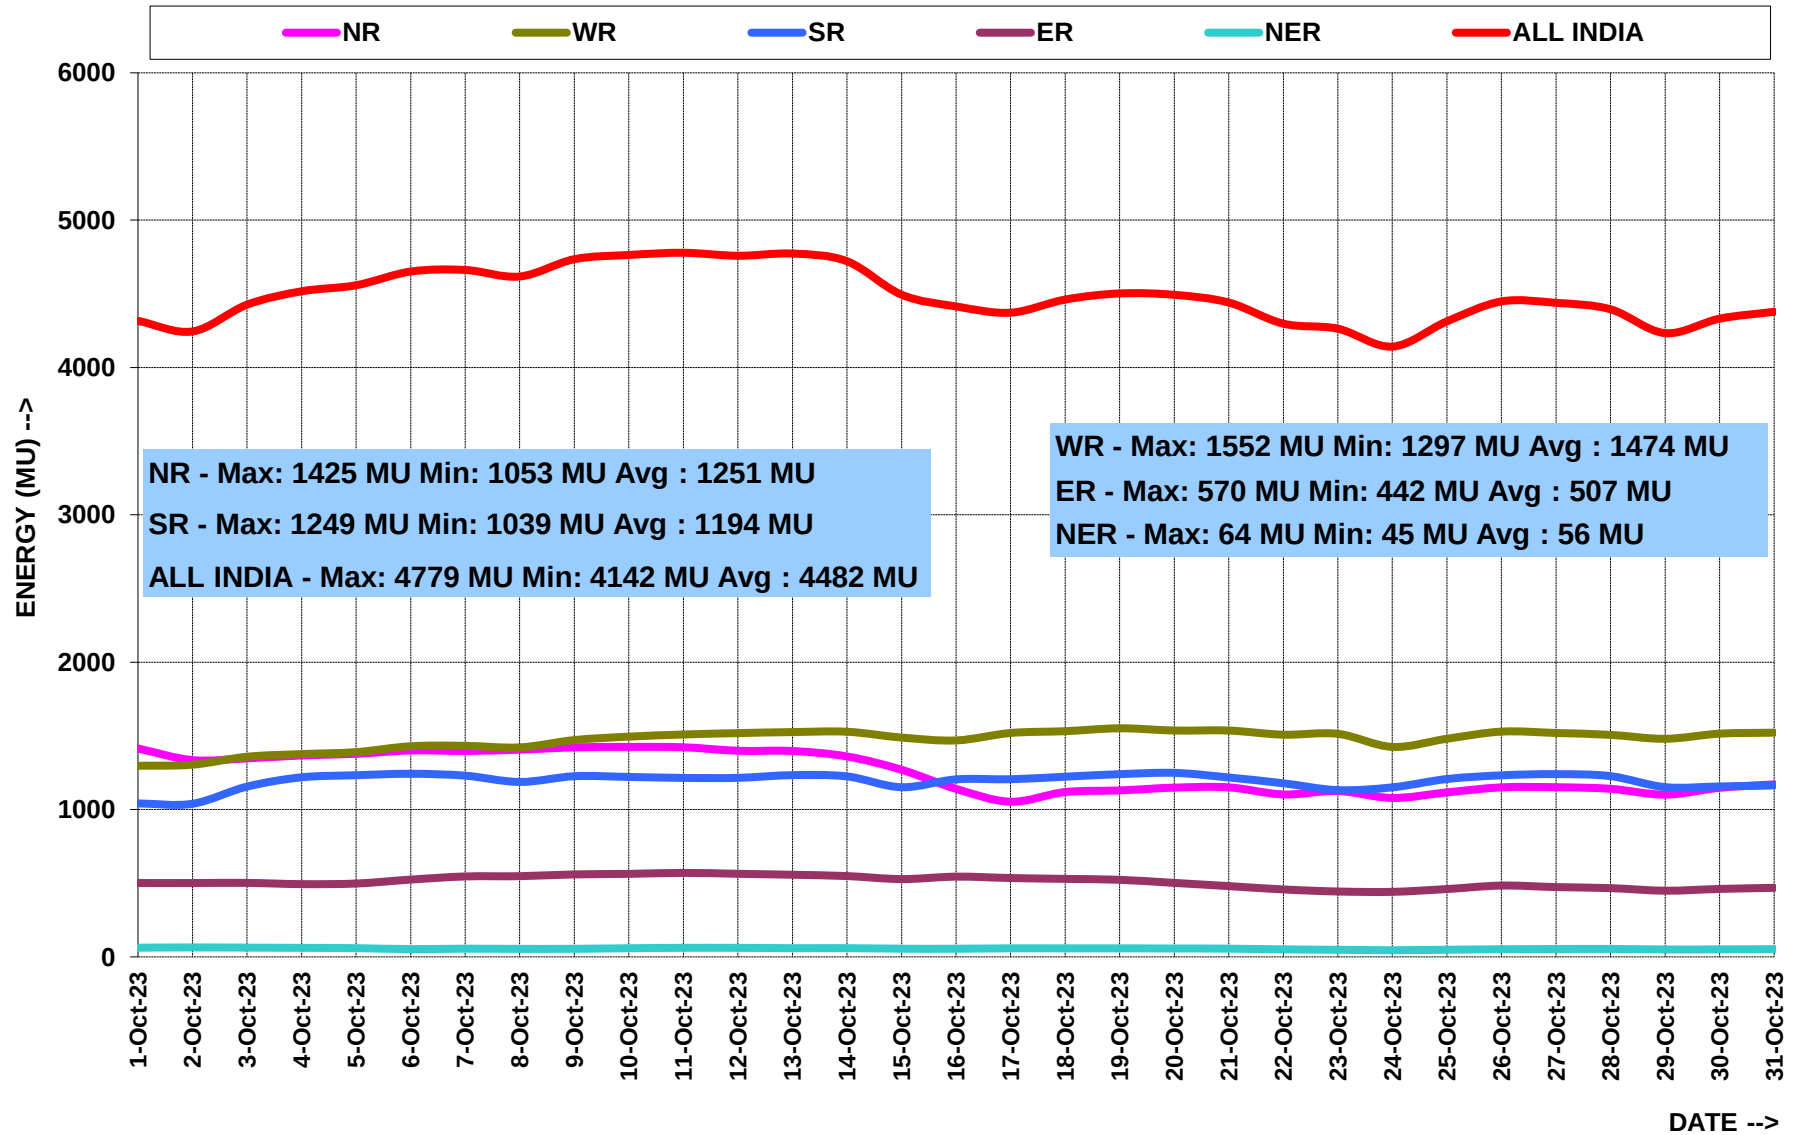

5. वर्ष 2023-24 के लिए आवृत्ति रूपरेखा FREQUENCY PROFILE FOR YEAR 2023-24

राष्ट्रीय ग्रिड NATIONAL GRID								
फ्रिक्वेंसी रूपरेखा (Hz)			<49.9	49.9-50.05	>50.05	उच्चतम फ्रिक्वेंसी	निम्नतम फ्रिक्वेंसी	औसत फ्रिक्वेंसी
% समय	Apr-23	All India Grid	10.54	67.90	21.56	50.33	49.49	49.99
	May-23	All India Grid	9.83	68.48	21.69	50.43	49.48	49.99
	Jun-23	All India Grid	6.47	67.82	25.71	50.41	49.51	50.01
	Jul-23	All India Grid	4.60	74.96	20.44	50.23	49.76	50.01
	Aug-23	All India Grid	7.08	77.28	15.63	50.20	49.74	50.00
	Sep-23	All India Grid	5.26	77.90	16.84	50.21	49.77	50.00
	Oct-23	All India Grid	8.87	74.42	16.71	50.21	49.71	49.99
	2023-24 (upto Oct)	All India Grid	7.53	72.70	19.77	50.43	49.48	50.00

5.1 अक्टूबर 2023 के लिए आवृत्ति रूपरेखा FREQUENCY PROFILE FOR OCTOBER 2023

फ्रिक्वेंसी रूपरेखा (Hz)		<49.9	49.9-50.05	>50.05	उच्चतम फ्रिक्वेंसी	निम्नतम फ्रिक्वेंसी	औसत फ्रिक्वेंसी	एफ़.वी.आई.
% समय	01-Oct-23	6.27	77.52	16.20	50.21	49.73	50.00	0.04
	02-Oct-23	4.77	82.93	12.30	50.17	49.80	49.99	0.03
	03-Oct-23	12.13	66.92	20.95	50.20	49.64	49.99	0.07
	04-Oct-23	21.10	68.47	10.43	50.15	49.56	49.96	0.09
	05-Oct-23	9.56	75.67	14.77	50.17	49.69	49.99	0.05
	06-Oct-23	9.62	73.62	16.76	50.25	49.66	49.99	0.05
	07-Oct-23	21.11	69.94	8.95	50.20	49.56	49.96	0.12
	08-Oct-23	7.97	71.26	20.76	50.21	49.66	50.00	0.05
	09-Oct-23	19.10	67.84	13.07	50.24	49.57	49.97	0.10
	10-Oct-23	18.51	63.50	18.00	50.17	49.57	49.98	0.10
	11-Oct-23	18.47	70.06	11.47	50.14	49.62	49.97	0.08
	12-Oct-23	9.61	72.00	18.39	50.20	49.74	50.00	0.05
	13-Oct-23	5.13	75.19	19.69	50.20	49.77	50.01	0.03
	14-Oct-23	10.91	69.69	19.40	50.22	49.71	50.00	0.05
	15-Oct-23	6.13	78.01	15.86	50.21	49.71	50.00	0.03
	16-Oct-23	9.90	67.88	22.22	50.24	49.47	49.99	0.14
	17-Oct-23	9.93	69.83	20.24	50.22	49.65	50.00	0.06
	18-Oct-23	7.96	77.09	14.94	50.21	49.72	49.99	0.04
	19-Oct-23	10.42	73.29	16.30	50.27	49.72	49.99	0.05
	20-Oct-23	3.17	80.44	16.39	50.21	49.76	50.01	0.03
	21-Oct-23	3.69	81.50	14.80	50.20	49.77	50.00	0.03
	22-Oct-23	5.69	74.92	19.39	50.22	49.79	50.00	0.04
	23-Oct-23	2.42	75.84	21.74	50.29	49.84	50.01	0.03
	24-Oct-23	1.57	81.01	17.42	50.19	49.84	50.01	0.02
	25-Oct-23	4.16	79.58	16.26	50.17	49.78	50.00	0.03
	26-Oct-23	5.35	78.29	16.37	50.19	49.77	50.00	0.03
	27-Oct-23	3.60	76.32	20.08	50.30	49.80	50.01	0.04
	28-Oct-23	12.06	74.64	13.30	50.18	49.69	49.98	0.05
	29-Oct-23	4.18	79.95	15.87	50.21	49.83	50.00	0.03
	30-Oct-23	4.80	74.28	20.91	50.20	49.77	50.00	0.04
	31-Oct-23	5.74	79.61	14.65	50.18	49.75	49.99	0.03


6.राष्ट्रीय स्तर पर जल विद्युत उत्पादन
HYDRO GENERATION AT NATIONAL LEVEL

माह: अक्टूबर 2023 MONTH:- OCT 2023

सभी आंकड़े मिलियन यूनिट में All figures in MU

दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Oct-23	217	69	53	99	24	462
02-Oct-23	213	72	63	112	23	484
03-Oct-23	209	59	78	126	25	497
04-Oct-23	205	83	91	84	28	490
05-Oct-23	196	91	76	93	29	485
06-Oct-23	196	80	94	91	32	493
07-Oct-23	204	85	101	88	33	510
08-Oct-23	203	73	83	84	33	475
09-Oct-23	198	64	100	80	37	479
10-Oct-23	197	73	91	79	35	474
11-Oct-23	192	91	88	75	35	481
12-Oct-23	182	104	77	74	31	468
13-Oct-23	178	103	68	75	30	453
14-Oct-23	172	95	70	69	30	435
15-Oct-23	170	90	59	68	27	414
16-Oct-23	165	91	64	63	27	410
17-Oct-23	175	75	65	65	26	406
18-Oct-23	168	60	72	60	24	384
19-Oct-23	160	55	71	60	24	370
20-Oct-23	158	54	64	57	23	357
21-Oct-23	163	47	57	46	22	336
22-Oct-23	161	40	54	49	21	325
23-Oct-23	163	39	49	46	21	318
24-Oct-23	163	36	48	45	20	312
25-Oct-23	158	37	57	44	20	317
26-Oct-23	155	43	61	45	21	325
27-Oct-23	149	36	63	42	20	311
28-Oct-23	150	44	66	44	20	324
29-Oct-23	142	33	46	38	19	278
30-Oct-23	143	44	57	42	19	304
31-Oct-23	146	47	56	45	18	311
कुल TOTAL	5450	2013	2139	2088	797	12488
उच्चतम MAXIMUM	217	104	101	126	37	510
निम्नतम MINIMUM	142	33	46	38	18	278
औसत AVERAGE	176	65	69	67	26	403
संचयी 2023-24 Cumulative 2023-24	59432	11635	14491	19509	5059	110125
अब तक का उच्चतम All Time Max.	443	167	208	157	41	877
दिनांक Date	01.08.23	18.12.14	31.08.18	14.09.22	29.08.23	30.08.22

HYDRO ENERGY DURING THE MONTH OF OCTOBER' 2023

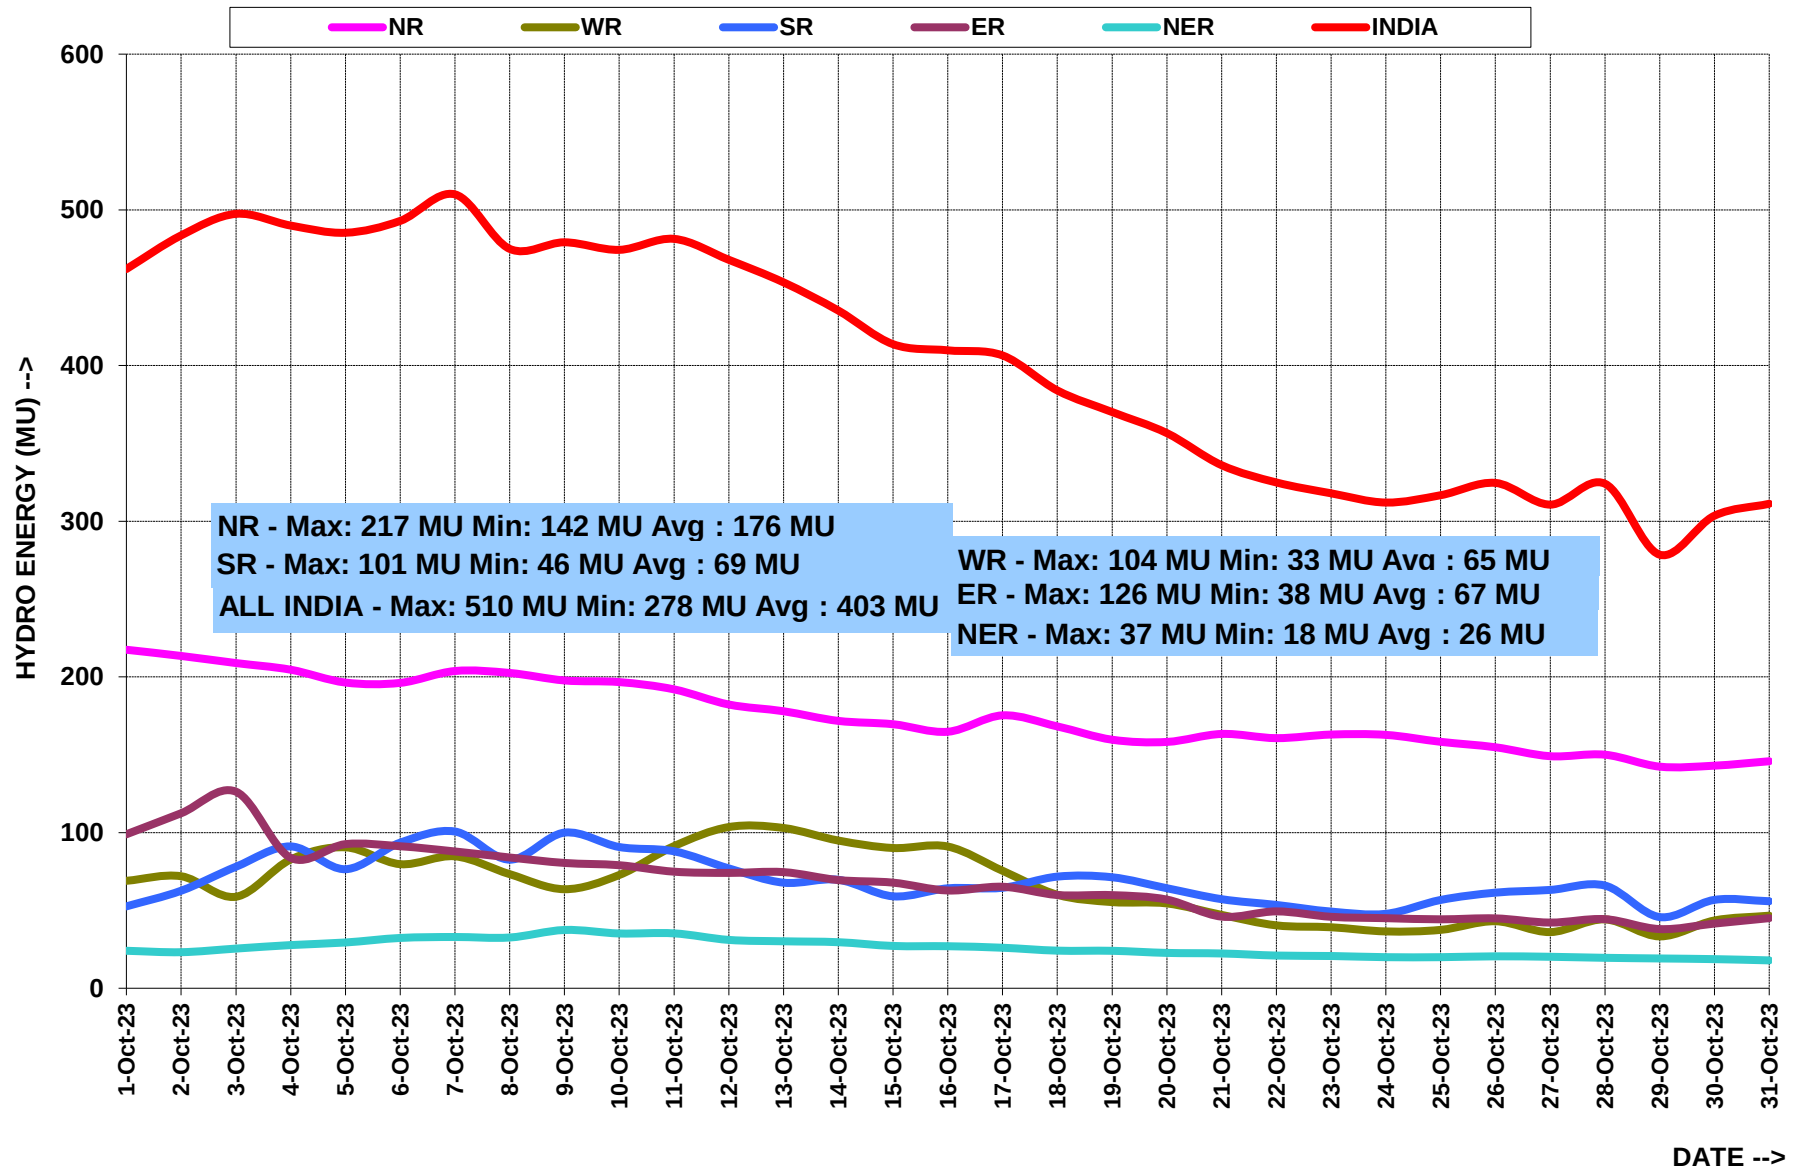

7. राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन
WIND GENERATION AT NATIONAL LEVEL
 माह: अक्टूबर 2023 MONTH:- OCT 2023

सभी आंकड़े मिलियन यूनिट में All figures in MU

दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Oct-23	11	62	192	-----	-----	265
02-Oct-23	4	62	158	-----	-----	225
03-Oct-23	10	56	118	-----	-----	184
04-Oct-23	22	61	95	-----	-----	179
05-Oct-23	32	77	68	-----	-----	177
06-Oct-23	46	87	57	-----	-----	190
07-Oct-23	46	65	34	-----	-----	146
08-Oct-23	44	54	28	-----	-----	126
09-Oct-23	44	76	23	-----	-----	143
10-Oct-23	26	80	26	-----	-----	132
11-Oct-23	8	34	39	-----	-----	80
12-Oct-23	18	31	39	-----	-----	87
13-Oct-23	22	32	31	-----	-----	85
14-Oct-23	41	37	26	-----	-----	104
15-Oct-23	24	48	25	-----	-----	98
16-Oct-23	32	52	31	-----	-----	115
17-Oct-23	31	46	22	-----	-----	98
18-Oct-23	12	42	23	-----	-----	77
19-Oct-23	4	36	21	-----	-----	61
20-Oct-23	8	40	25	-----	-----	74
21-Oct-23	12	34	28	-----	-----	74
22-Oct-23	12	37	28	-----	-----	77
23-Oct-23	10	43	35	-----	-----	88
24-Oct-23	9	36	26	-----	-----	70
25-Oct-23	3	33	34	-----	-----	69
26-Oct-23	4	33	41	-----	-----	78
27-Oct-23	10	32	41	-----	-----	83
28-Oct-23	15	23	34	-----	-----	72
29-Oct-23	6	29	41	-----	-----	76
30-Oct-23	7	49	41	-----	-----	97
31-Oct-23	22	46	35	-----	-----	104
कुल TOTAL	594	1473	1466	-----	-----	3534
उच्चतम MAXIMUM	46	87	192	-----	-----	265
निम्नतम MINIMUM	3	23	21	-----	-----	61
औसत AVERAGE	19	48	47	-----	-----	114
संचयी 2023-24 Cumulative 2023-24	6005	25651	27069	-----	-----	58725
अब तक का उच्चतम All Time Max.	86	273	298	-----	-----	611
दिनांक Date	07.08.23	07.08.23	21.07.23	-----	-----	02.08.23

*Source: As reported by SLDCs. Limited visibility of embedded wind generator data.

8. राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन
SOLAR GENERATION AT NATIONAL LEVEL

माह: अक्टूबर 2023 MONTH:- OCT 2023

सभी आंकड़े मिलियन यूनिट में All figures in MU

दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Oct-23	121	59	99	4.9	0.8	284
02-Oct-23	132	61	95	1.7	1.1	290
03-Oct-23	140	62	115	1.7	0.9	320
04-Oct-23	137	67	117	2.0	0.9	324
05-Oct-23	138	67	119	2.3	0.5	327
06-Oct-23	137	67	128	2.4	0.4	334
07-Oct-23	136	66	124	2.7	0.5	329
08-Oct-23	133	66	118	5.2	0.7	323
09-Oct-23	133	67	111	5.3	0.9	316
10-Oct-23	134	65	111	2.8	1.1	314
11-Oct-23	131	63	110	3.0	1.0	308
12-Oct-23	130	61	116	2.9	1.1	311
13-Oct-23	134	60	120	2.9	1.1	317
14-Oct-23	130	56	115	2.8	1.1	305
15-Oct-23	124	58	115	2.8	1.1	301
16-Oct-23	85	57	100	5.4	1.2	248
17-Oct-23	99	58	114	5.3	1.2	278
18-Oct-23	132	59	121	2.7	1.0	316
19-Oct-23	127	59	117	2.9	1.1	308
20-Oct-23	125	60	114	2.8	1.2	303
21-Oct-23	121	64	117	2.9	1.3	306
22-Oct-23	114	63	119	2.8	1.3	300
23-Oct-23	123	64	120	2.6	1.0	311
24-Oct-23	119	63	124	5.7	0.7	313
25-Oct-23	124	63	121	5.3	0.7	314
26-Oct-23	126	64	125	2.9	1.1	319
27-Oct-23	122	66	124	3.2	1.2	316
28-Oct-23	99	61	113	2.8	1.3	277
29-Oct-23	120	65	100	2.9	1.2	289
30-Oct-23	112	62	96	2.6	1.3	274
31-Oct-23	102	62	97	2.7	1.3	265
कुल TOTAL	3839	1875	3437	98	30	9177
उच्चतम MAXIMUM	140	67	128	6	1	334
निम्नतम MINIMUM	85	56	95	2	0	248
औसत AVERAGE	124	62	114	3	1	305
संचयी 2023-24 Cumulative 2023-24	27111	11519	24416	683	203.4	63829
अब तक का उच्चतम All Time Max.	147	71	143	6.7	2.4	351
दिनांक Date	10.05.23	12.05.23	21.03.23	23.03.23	22.06.22	10.05.23

*Source: RLDCs for solar connected to ISTS; SLDCs for embedded solar. Limited visibility of embedded solar data.

9. राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग पूर्ति
DAILY MAXIMUM DEMAND MET AT NATIONAL LEVEL

माह: अक्टूबर 2023 MONTH:- OCT 2023

सभी आंकड़े मेगावाट में All figures in MW


दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL	विभिन्नता फैक्टर Diversity Factor*
01-Oct-23	64756	59083	49128	23664	3266	191315	1.045
02-Oct-23	60720	61007	49868	23870	3276	190972	1.041
03-Oct-23	63124	63244	56019	23042	3420	201337	1.037
04-Oct-23	63430	63870	58834	23277	3267	203442	1.045
05-Oct-23	63263	65413	59561	23991	3162	207184	1.040
06-Oct-23	63937	65975	60444	24613	3009	211251	1.032
07-Oct-23	64234	66079	60748	24928	3041	211534	1.035
08-Oct-23	64949	64400	58210	25109	3062	210077	1.027
09-Oct-23	67013	68058	61730	25585	3077	219781	1.026
10-Oct-23	67829	69048	61337	25642	3298	221627	1.025
11-Oct-23	66332	69696	60950	26287	3146	220980	1.025
12-Oct-23	65197	70455	59662	25525	3162	218918	1.023
13-Oct-23	65576	70861	60640	25335	3225	220362	1.024
14-Oct-23	61754	71184	59784	25100	3314	215858	1.024
15-Oct-23	57485	67940	55668	24419	3068	200980	1.038
16-Oct-23	52548	70769	59579	25186	3232	206826	1.022
17-Oct-23	53373	70576	58366	24587	3206	200887	1.046
18-Oct-23	55785	70151	59425	24562	3163	203357	1.048
19-Oct-23	54397	71717	61553	24392	3153	206736	1.041
20-Oct-23	55161	70971	62200	23550	3201	209025	1.029
21-Oct-23	55826	71219	60384	22289	3172	204716	1.040
22-Oct-23	52357	69416	56539	21719	2868	197037	1.030
23-Oct-23	55113	71514	55511	20622	2746	199617	1.030
24-Oct-23	51412	65714	56665	19704	2494	192544	1.018
25-Oct-23	55602	70210	59674	21566	2849	204240	1.028
26-Oct-23	56925	71205	60503	22327	3015	206927	1.034
27-Oct-23	56231	70638	61319	22250	3054	207407	1.029
28-Oct-23	55867	70559	60963	21747	3024	206604	1.027
29-Oct-23	53028	68278	57147	22363	2857	197158	1.033
30-Oct-23	56425	71309	57786	22533	3001	204397	1.033
31-Oct-23	57032	71123	57621	22913	3102	203826	1.039
उच्चतम MAXIMUM	67829	71717	62200	26287	3420	221627	1.048
निम्नतम MINIMUM	51412	59083	49128	19704	2494	190972	1.018
औसत AVERAGE	59248	68441	58639	23635	3095	206352	1.033
अब तक का उच्चतम All Time Max.	81220	74035	64314	29641	3712	239978	
दिनांक Date	04.09.23	01.09.23	15.03.23	28.07.23	04.09.23	01.09.23	

* Diversity factor = (Sum of regional max demands) / All India max demand


नोट : यह आंकड़े एनएलडीसी स्काडा प्रणाली में दर्ज दैनिक अधिकतम मांगपूर्ति दर्शाते हैं ।

Note: The above figures denote daily maximum demand met recorded in NLDC SCADA.


10. DEMAND AND GENERATION PLOTS FOR 10 OCTOBER (MAXIMUM DEMAND MET)

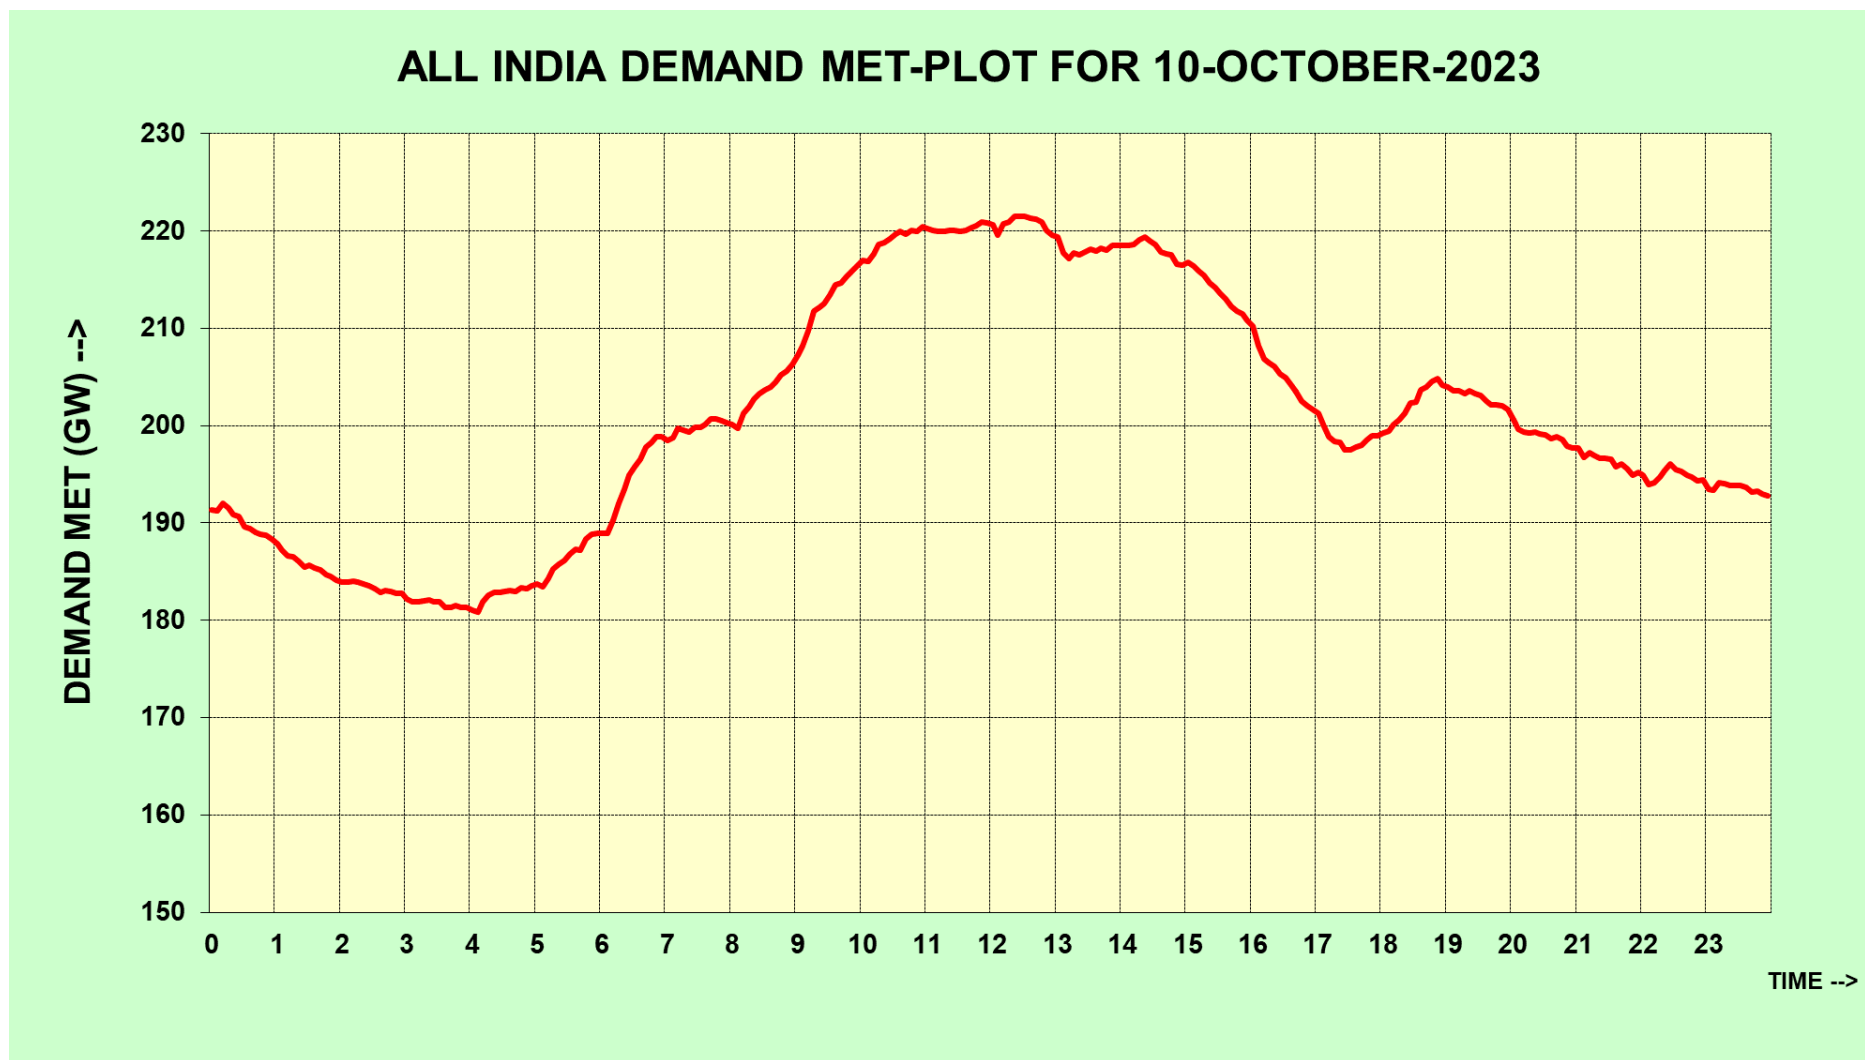


REGIONAL DEMAND MET-PLOT FOR 10-OCTOBER-2023

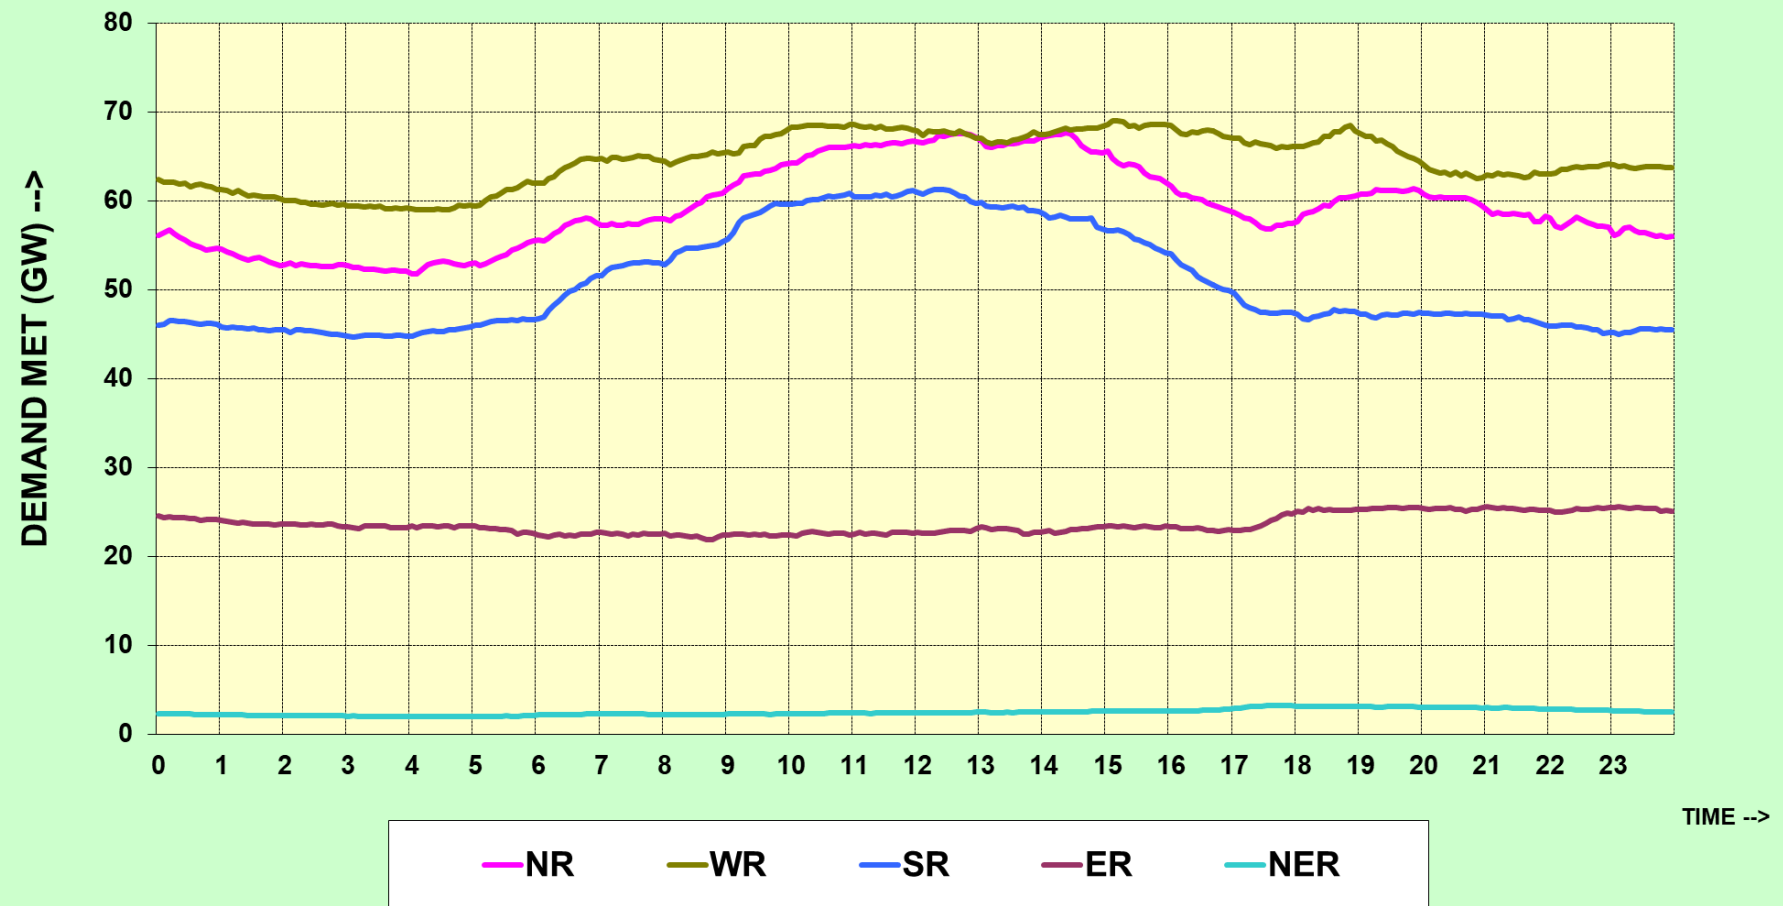

All India Fuel-wise Generation Patterns for 10-OCTOBER-2023

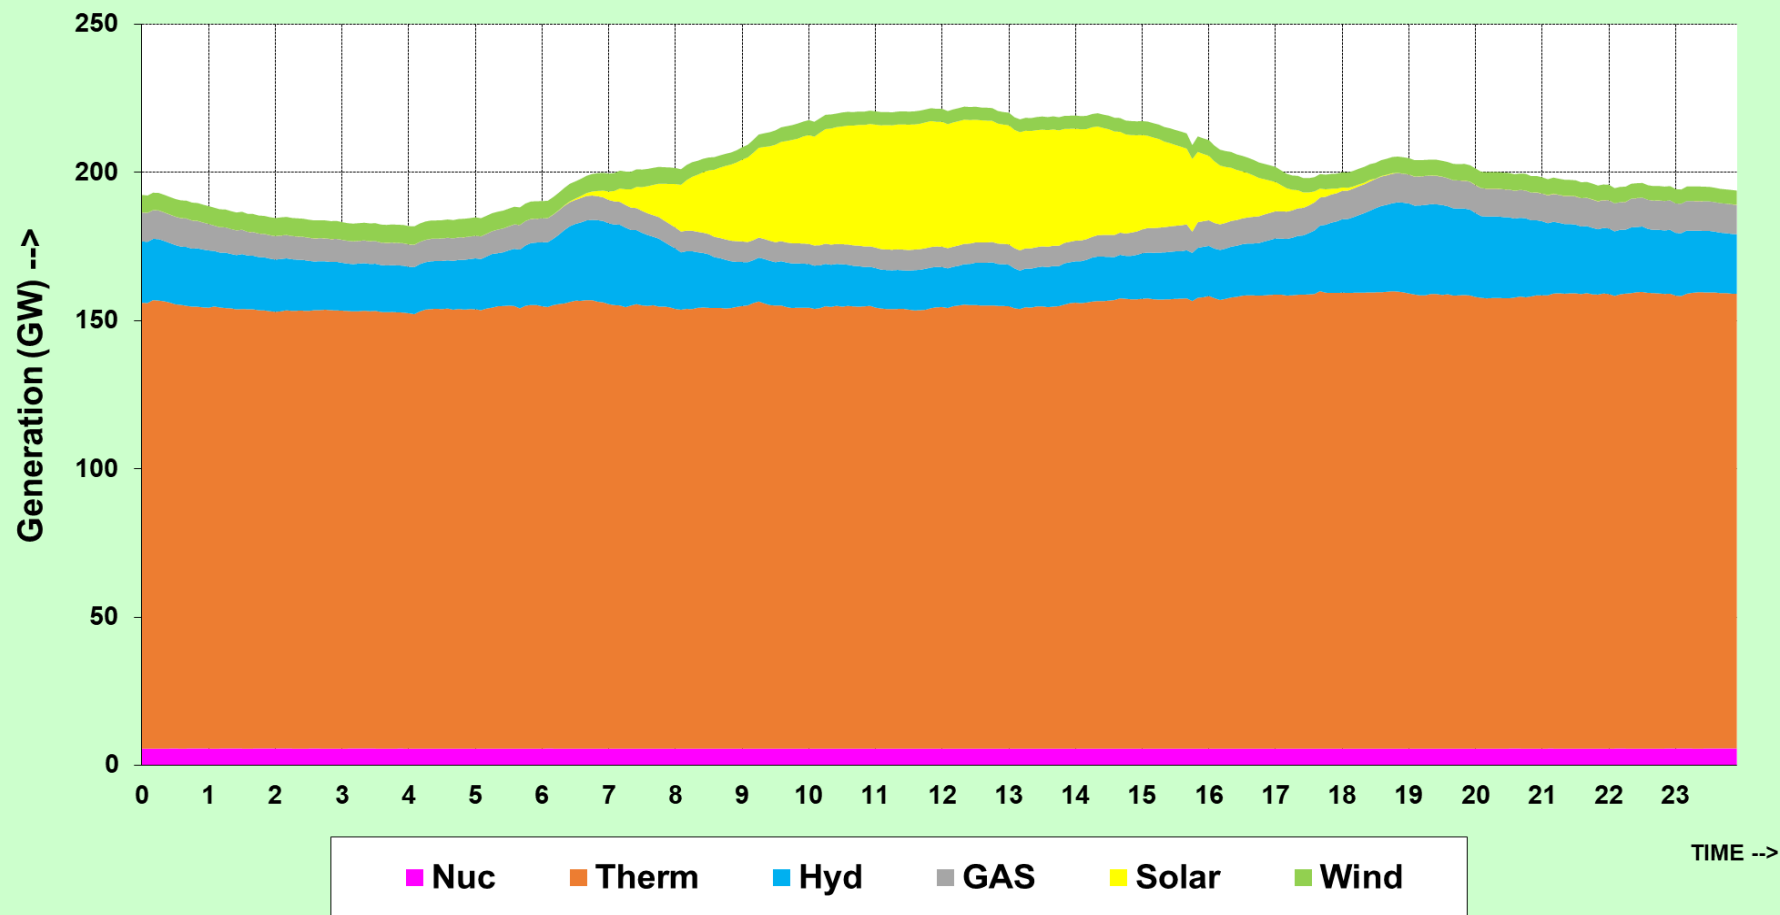

ALL INDIA GENERATION PLOT FOR 10-OCTOBER-2023

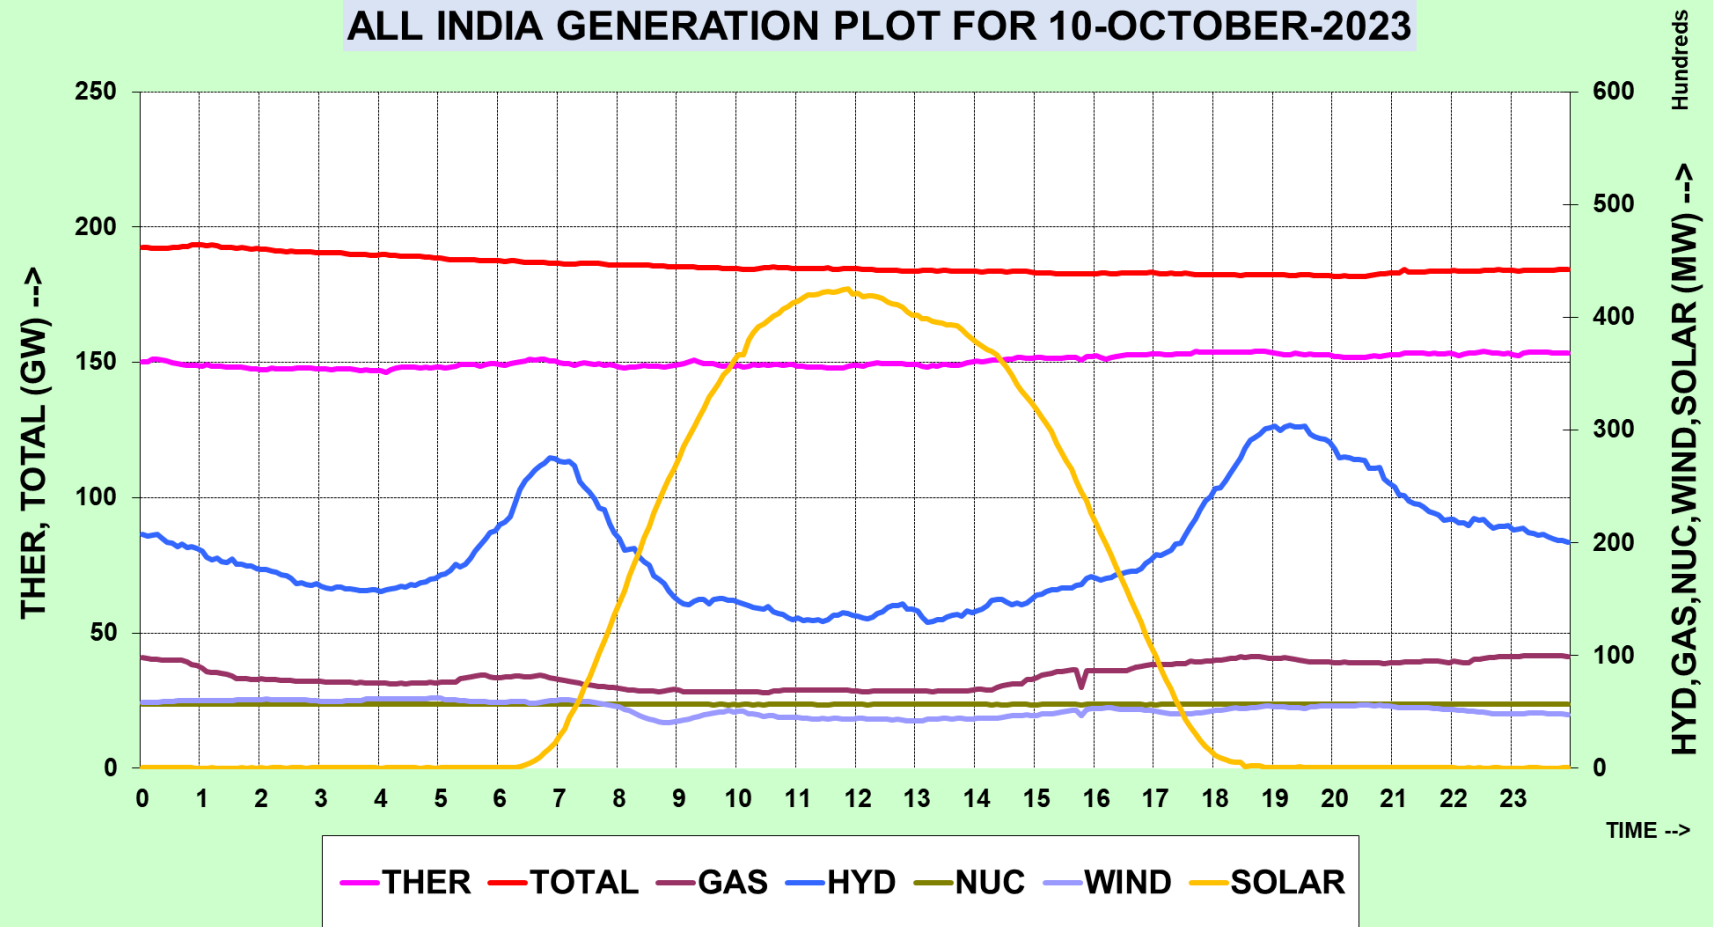

10 अक्टूबर 2023 (अधिकतम माँग) की आल इंडिया माँग आपूर्ति
ALL INDIA DEMAND MET FOR 10 OCTOBER 2023 (MAXIMUM DEMAND*)

Time (hrs)	All India Demand (MW)		Time (hrs)	All India Demand (MW)
00:05	191264		12:05	219581
00:20	190851		12:20	221492
00:35	189437		12:35	221276
00:50	188702		12:50	220113
01:05	187195		13:05	217779
01:20	186082		13:20	217573
01:35	185399		13:35	217994
01:50	184516		13:50	218494
02:05	183943		14:05	218482
02:20	183760		14:20	219369
02:35	182896		14:35	217870
02:50	182724		14:50	216580
03:05	181904		15:05	216403
03:20	182067		15:20	214682
03:35	181371		15:35	213039
03:50	181313		15:50	211466
04:05	180830		16:05	208248
04:20	182861		16:20	206102
04:35	183018		16:35	204160
04:50	183275		16:50	202093
05:05	183450		17:05	200135
05:20	185710		17:20	198336
05:35	187345		17:35	197776
05:50	188817		17:50	199002
06:05	188974		18:05	199477
06:20	193503		18:20	201256
06:35	196571		18:35	203675
06:50	198875		18:50	204816
07:05	198742		19:05	203615
07:20	199316		19:20	203609
07:35	200125		19:35	202546
07:50	200490		19:50	202079
08:05	199704		20:05	199607
08:20	202734		20:20	199311
08:35	203948		20:35	198654
08:50	205579		20:50	197905
09:05	208195		21:05	196729
09:20	212157		21:20	196647
09:35	214447		21:35	195820
09:50	215866		21:50	194887
10:05	216917		22:05	193949
10:20	218846		22:20	195413
10:35	219941		22:35	195256
10:50	220022		22:50	194384
11:05	220061		23:05	193356
11:20	220052		23:20	193820
11:35	220084		23:35	193615
11:50	220959		23:50	192953
Maximum Demand of 221627 MW met@12:31 hrs (from 1 min. interval SCADA DATA)				

* 15 minute interval SCADA DATA of instantaneous demand

11. ACTUAL POWER SUPPLY POSITION - OCTOBER 2023

REGION	STATE	Requirement/Availability in MU/DAY			Requirement/Availability in MU				Peak Demand/Peak Met in MW			
		Requirement	Energy met	Surplus(+)/ Deficit(-)	Requirement	Energy met	Surplus(+)/ Deficit(-)	% Shortage	Requirement	Peak Demand Met	Surplus(+)/ Deficit(-)	% Shortage
NR	Chandigarh	4	4	0.0	127	127	0	0.0	265	265	0	0.0
	Delhi	90	90	0.0	2805	2805	0	0.0	5583	5583	0	0.0
	Haryana	173	172	-1.0	5377	5346	-31	-0.6	9947	9947	0	0.0
	Himachal Pradesh	33	33	-0.1	1013	1010	-3	-0.3	1871	1871	0	0.0
	J&K(UT) and Ladakh(UT)	50	49	-1.2	1540	1504	-36	-2.3	2735	2735	0	0.0
	Punjab	174	174	0.0	5391	5391	0	0.0	12491	12491	0	0.0
	Rajasthan	295	294	-0.2	9137	9129	-7	-0.1	15641	15641	0	0.0
	Uttar Pradesh	393	391	-1.7	12178	12124	-54	-0.4	24096	24096	0	0.0
	Uttarakhand	40	40	-0.2	1246	1240	-6	-0.5	2259	2259	0	0.0
	Railway	3	3	0.0	107	107	0	0.0	207	207	0	0.0
	NFL	0	0	0.0	2	2	0	0.0	11	11	0	0.0
	TOTAL	1256	1251	-4.4	38923	38785	-137	-0.4	67382	67025	-357	-0.5
WR	Gujarat	425	425	0.0	13162	13162	0	0.0	21689	21689	0	0.0
	Madhya Pradesh	290	290	0.0	8976	8976	0	0.0	15245	15209	-36	-0.2
	Chhattisgarh	110	110	-0.3	3423	3414	-10	-0.3	5325	5325	0	0.0
	Maharashtra	582	582	-0.2	18049	18044	-5	0.0	28206	28206	0	0.0
	Goa	14	14	0.0	426	426	0	0.0	734	734	0	0.0
	DNHDDPDCL	29	29	0.0	898	898	0	0.0	1316	1316	0	0.0
	AMNSIL	18	18	0.0	555	555	0	0.0	924	924	0	0.0
	BALCO*	12	12	0.0	385	385	0	0.0	525	525	0	0.0
	TOTAL	1480	1479	-0.5	45874	45859	-15	0.0	71411	71411	0	0.0
SR	Andhra Pradesh	237	235	-2.5	7357	7280	-77	-1.0	13039	13039	0	0.0
	Telangana	271	268	-2.9	8386	8296	-90	-1.1	15285	15266	-19	-0.1
	Karnataka	263	260	-2.9	8138	8048	-90	-1.1	15978	15978	0	0.0
	Kerala	81	80	-0.9	2496	2467	-29	-1.2	4191	4191	0	0.0
	Tamil Nadu	346	342	-3.8	10734	10617	-117	-1.1	17484	17386	-98	-0.6
	Puducherry	10	10	-0.1	310	307	-3	-1.1	477	474	-3	-0.6
	TOTAL	1207	1194	-13.1	37420	37014	-406	-1.1	62166	62166	0	0.0
ER	Bihar	115	113	-2.1	3576	3510	-66	-1.8	6597	6475	-122	-1.8
	Jharkhand	33	32	-1.0	1016	984	-32	-3.2	1891	1672	-219	-11.6
	DVC	71	71	0.0	2191	2191	0	0.0	3477	3477	0	0.0
	Odisha	114	114	0.0	3536	3536	0	0.0	6028	6028	0	0.0
	West Bengal	177	177	0.0	5473	5473	0	0.0	9684	9684	0	0.0
	Sikkim	1	1	0.0	29	29	0	0.0	86	86	0	0.0
	Railways_ER ISTS**	0	0	0.0	5	5	0	0.0	32	32	0	0.0
	TOTAL	511	507	-3.2	15826	15728	-98	-0.6	26999	26208	-791	-2.9
NER	Arunachal Pradesh	3	3	0.0	82	82	0	0.0	167	167	0	0.0
	Assam	35	35	-0.2	1090	1085	-5	-0.5	2226	2226	0	0.0
	Manipur	3	3	0.0	80	80	0	0.0	214	214	0	0.0
	Meghalaya	6	6	-0.1	177	173	-4	-2.4	334	334	0	0.0
	Mizoram	2	2	0.0	53	53	0	0.0	141	141	0	0.0
	Nagaland	3	3	0.0	79	79	0	0.0	166	166	0	0.0
	Tripura	5	5	0.0	162	162	0	0.0	349	349	0	0.0
	TOTAL	56	55	-0.3	1723	1714	-9	-0.5	3418	3418	0	0.0
ALL INDIA		4509	4487	-21.5	139767	139101	-666	-0.5				

* BALCO has been added as new entity wef 20.12.2022

** Railways_ER ISTS has been added as new entity wef 29.04.2023

NOTE: BASED ON THE DATA FURNISHED BY ENTITIES ON DAILY BASIS

12. ENERGY COMPARISON OF OCTOBER 2023 vs OCTOBER 2022

REGION	STATE	Energy Requirement (MU)					Energy Met (MU)				
		Oct-22	Oct-23	Difference	% Change	Average MU/day for Oct-23	Oct-22	Oct-23	Difference	% Change	Average MU/day for Oct-23
NR	Chandigarh	121	127	6	5	4	121	127	6	5	4
	Delhi	2434	2805	371	15	90	2434	2805	371	15	90
	Haryana	4345	5377	1032	24	173	4344	5346	1002	23	172
	Himachal Pradesh	940	1013	73	8	33	937	1010	73	8	33
	J&K(UT) and Ladakh(UT)	1573	1540	-32	-2	50	1557	1504	-52	-3	49
	Punjab	5053	5391	337	7	174	5053	5391	337	7	174
	Rajasthan	7903	9137	1233	16	295	7886	9129	1244	16	294
	Uttar Pradesh	10059	12178	2119	21	393	10052	12124	2073	21	391
	Uttarakhand	1121	1246	126	11	40	1116	1240	124	11	40
	Railway/NFL	93	109	16	17	4	93	109	16	17	4
	TOTAL	33642	38923	5281	16	1256	33593	38785	5193	15	1251
WR	Gujarat	11808	13162	1354	11	425	11808	13162	1354	11	425
	Madhya Pradesh	6449	8976	2527	39	290	6449	8976	2527	39	290
	Chhattisgarh	2966	3423	458	15	110	2966	3414	448	15	110
	Maharashtra	13945	18049	4104	29	582	13945	18044	4099	29	582
	Goa	364	426	61	17	14	364	426	61	17	14
	DNHDDPDCL	797	898	100	13	29	797	898	100	13	29
	AMNSIL	439	555	116	26	18	439	555	116	26	18
	BALCO*		385	-	-	12		385	-	-	12
	TOTAL	36769	45874	9105	25	1480	36769	45859	9090	25	1479
SR	Andhra Pradesh	5525	7357	1832	33	237	5525	7280	1755	32	235
	Telangana	5379	8386	3007	56	271	5443	8296	2853	52	268
	Karnataka	5056	8138	3082	61	263	5121	8048	2927	57	260
	Kerala	2302	2496	194	8	81	2325	2467	142	6	80
	Tamil Nadu	8922	10734	1812	20	346	9010	10617	1607	18	342
	Puducherry	261	310	49	19	10	264	307	43	16	10
	TOTAL	27445	37420	9975	36	1207	27688	37014	9327	34	1194
ER	Bihar	3305	3576	271	8	115	3288	3510	222	7	113
	Jharkhand	1005	1016	11	1	33	977	984	7	1	32
	DVC	2194	2191	-3	0	71	2194	2191	-3	0	71
	Odisha	3857	3536	-321	-8	114	3857	3536	-322	-8	114
	West Bengal	4923	5473	550	11	177	4922	5473	551	11	177
	Sikkim	40	29	-10	-26	1	40	29	-10	-26	1
	Railways_ER ISTS**		5	-	-	0		5	-	-	0
	TOTAL	15324	15826	502	3	511	15278	15728	450	3	507
NER	Arunachal Pradesh	74	82	7	10	3	74	82	7	10	3
	Assam	1004	1090	87	9	35	1004	1085	82	8	35
	Manipur	80	80	0	0	3	80	80	0	0	3
	Meghalaya	188	177	-11	-6	6	188	173	-15	-8	6
	Mizoram	52	53	1	2	2	52	53	1	2	2
	Nagaland	74	79	5	7	3	74	79	5	7	3
	Tripura	150	162	12	8	5	150	162	12	8	5
	TOTAL	1622	1723	102	6	56	1622	1714	93	6	55
ALL INDIA		114802	139767	24965	22	4509	114949	139101	24152	21	4487

* BALCO has been added as new entity wef 20.12.2022

** Railways_ER ISTS has been added as new entity wef 29.04.2023

13. DEMAND COMPARISON OF OCTOBER 2023 vs OCTOBER 2022

REGION	STATE	Peak Requirement (MW)				Peak Met (MW)			
		Oct-22	Oct-23	Difference	% Change	Oct-22	Oct-23	Difference	% Change
NR	Chandigarh	260	265	5	1.9	260	265	5	1.9
	Delhi	4990	5583	593	11.9	4990	5583	593	11.9
	Haryana	8663	9947	1284	14.8	8663	9947	1284	14.8
	Himachal Pradesh	1771	1871	100	5.6	1771	1871	100	5.6
	J&K(UT) and Ladakh(UT)	2823	2735	-88	-3.1	2823	2735	-88	-3.1
	Punjab	11498	12491	993	8.6	11498	12491	993	8.6
	Rajasthan	14072	15641	1569	11.1	14072	15641	1569	11.1
	Uttar Pradesh	22631	24096	1465	6.5	22631	24096	1465	6.5
	Uttarakhand	2092	2259	167	8.0	2092	2259	167	8.0
	Railway/NFL	169	218	48	28.4	169	218	48	28.4
WR	Gujarat	20275	21689	1414	7	20254	21689	1435	7.1
	Madhya Pradesh	11752	15245	3493	30	11752	15209	3457	29.4
	Chhattisgarh	4648	5325	677	15	4644	5325	682	14.7
	Maharashtra	22513	28206	5693	25	22513	28206	5693	25.3
	Goa	655	734	80	12	655	734	80	12.1
	DNHDDPDCL	1243	1316	73	5.9	1243	1316	73	5.9
	AMNSIL	746	924	178	23.9	746	924	178	23.9
	BALCO*		525	-	-		525	-	-
SR	Andhra Pradesh	9734	13039	3305	34.0	9734	13039	3305	34.0
	Telangana	11839	15285	3446	29.1	11821	15266	3445	29.1
	Karnataka	10292	15978	5686	55.2	10292	15978	5686	55.2
	Kerala	3947	4191	244	6.2	3947	4191	244	6.2
	Tamil Nadu	15532	17484	1952	12.6	15532	17386	1854	11.9
	Puducherry	424	477	53	12.5	424	474	50	11.8
ER	Bihar	6625	6597	-28	-0.4	6466	6475	9	0.1
	Jharkhand	1907	1891	-16	-0.8	1676	1672	-4	-0.2
	DVC	3299	3477	178	5.4	3299	3477	178	5.4
	Odisha	6049	6028	-21	-0.3	6049	6028	-21	-0.3
	West Bengal	9239	9684	445	4.8	9239	9684	445	4.8
	Sikkim	119	86	-33	-27.7	119	86	-33	-27.7
	Railways_ER ISTS**		32	32	-		32	32	-
NER	Arunachal Pradesh	121	167	46	38.1	121	167	46	38.1
	Assam	2312	2226	-86	-3.7	2275	2226	-49	-2.2
	Manipur	202	214	11	5.6	202	214	11	5.6
	Meghalaya	356	334	-22	-6.1	356	334	-22	-6.1
	Mizoram	127	141	14	11.3	127	141	14	11.3
	Nagaland	167	166	-1	-0.7	167	166	-1	-0.7
	Tripura	321	349	29	8.9	321	349	29	8.9

* BALCO has been added as new entity wef 20.12.2022

** Railways_ER ISTS has been added as new entity wef 29.04.2023

14. SCHEDULE AND DRAWAL OF CONSTITUENTS - OCTOBER 2023

REGION	STATE	SCHEDULE (MU)	ACTUAL DRAWAL (MU)	Over drawal(+)/ Under Drawal(-) (MU)	% OD/UD	SCHEDULE (MU/DAY)	ACTUAL DRAWAL (MU/DAY)	Over drawal(+)/ Under Drawal(-) (MU/DAY)
NR	Chandigarh	128.79	129.65	0.86	0.66	4.15	4.18	0.03
	Delhi	2288.22	2301.18	12.96	0.57	73.81	74.23	0.42
	Haryana	3467.56	3500.65	33.09	0.95	111.86	112.92	1.07
	Himachal Pradesh	588.25	585.00	-3.25	-0.55	18.98	18.87	-0.10
	J&K(UT) and Ladakh(UT)	1100.05	1177.31	77.26	7.02	35.49	37.98	2.49
	Punjab	2130.23	2097.02	-33.21	-1.56	68.72	67.65	-1.07
	Rajasthan	2715.05	2661.71	-53.34	-1.96	87.58	85.86	-1.72
	Uttar Pradesh	4532.00	4557.25	25.25	0.56	146.19	147.01	0.81
	Uttarakhand	815.03	829.90	14.87	1.82	26.29	26.77	0.48
	Railway	104.71	109.19	4.47	4.27	3.38	3.52	0.14
	NFL	2.15	1.92	-0.22	-10.49	0.07	0.06	-0.01
	Total	17872.04	17950.78	78.74	0.44	576.52	579.06	2.54
WR	Gujarat	5478.47	5460.85	-17.62	-0.32	176.72	176.16	-0.57
	Madhya Pradesh	5235.46	5142.19	-93.27	-1.78	168.89	165.88	-3.01
	Chhattisgarh	1600.93	1583.97	-16.96	-1.06	51.64	51.10	-0.55
	Maharashtra	7285.85	7208.01	-77.84	-1.07	235.03	232.52	-2.51
	Goa	391.31	412.66	21.35	5.46	12.62	13.31	0.69
	DNHDDPDCL	899.12	897.62	-1.50	-0.17	29.00	28.96	-0.05
	AMNSIL	246.58	242.71	-3.87	-1.57	7.95	7.83	-0.12
	BALCO*	388.34	385.32	-3.02	-0.78	12.53	12.43	-0.10
	Total	21526.06	21333.32	-192.74	-0.90	694.39	688.17	-6.22
SR	Andhra Pradesh	3301.11	3307.20	6.09	0.18	106.49	106.68	0.20
	Telangana	4271.17	4269.80	-1.37	-0.03	137.78	137.74	-0.04
	Karnataka	2995.41	3004.80	9.39	0.31	96.63	96.93	0.30
	Kerala	1851.11	1886.88	35.77	1.93	59.71	60.87	1.15
	Tamil Nadu	6104.32	6075.50	-28.82	-0.47	196.91	195.98	-0.93
	Puducherry	292.63	285.67	-6.96	-2.38	9.44	9.22	-0.22
	Goa (SR)	65.73	58.04	-7.69	-11.70	2.12	1.87	-0.25
	Total	18881.48	18887.89	6.41	0.03	609.08	609.29	0.21
ER	Bihar	3229.74	3213.40	-16.34	-0.51	104.19	103.66	-0.53
	Jharkhand	743.22	740.47	-2.76	-0.37	23.97	23.89	-0.09
	DVC	-1078.37	-1052.07	26.30	-2.44	-34.79	-33.94	0.85
	Odisha	1144.99	1098.90	-46.10	-4.03	36.94	35.45	-1.49
	West Bengal	1599.24	1539.54	-59.70	-3.73	51.59	49.66	-1.93
	Sikkim	27.27	29.45	2.18	7.99	0.88	0.95	0.07
	Railways_ER ISTS*	4.93	4.91	-0.02	-0.36	0.16	0.16	0.00
	Total	5671.03	5574.59	-96.43	-1.70	182.94	179.83	-3.11
NER	Arunachal Pradesh	74.76	73.74	-1.02	-1.36	2.41	2.38	-0.03
	Assam	823.19	837.91	14.72	1.79	26.55	27.03	0.47
	Manipur	85.32	79.92	-5.40	-6.33	2.75	2.58	-0.17
	Meghalaya	90.45	80.11	-10.34	-11.43	2.92	2.58	-0.33
	Mizoram	36.23	26.33	-9.90	-27.33	1.17	0.85	-0.32
	Nagaland	75.15	69.42	-5.73	-7.62	2.42	2.24	-0.18
	Tripura	155.61	152.68	-2.93	-1.88	5.02	4.93	-0.09
	Total	1340.71	1320.11	-20.60	-1.54	43.25	42.58	-0.66
All India Total		65291.31	65066.69	-224.62	-0.34	2106.17	2098.93	-7.25

* BALCO has been added as new entity wef 20.12.2022

** Railways_ER ISTS has been added as new entity wef 29.04.2023

15. INTER REGIONAL EXCHANGES 2023-24

(All figures in MU)

	Apr'23	May'23	June'23	July'23	Aug'23	Sep'23	Oct'23	Fin. Year 2023-24
Name of Line								
Import of NR from WR (WR-NR)								
WR - NR 765 kV Gwalior - Agra 2xS/C	635.95	996.71	863.68	972.77	772.12	902.82	479.75	5623.80
WR-NR 765 kV Gwalior - Phagi 2xS/C	553.05	453.93	342.56	671.61	397.70	687.31	582.69	3688.85
WR-NR 765 kV Jabalpur-Orai D/C	430.29	804.53	778.33	964.77	658.94	991.15	602.03	5230.04
WR-NR 765 kV Satna-Orai	505.37	598.85	574.83	615.77	543.29	593.66	548.69	3980.46
WR-NR 765 kV Gwalior-Orai	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
WR - NR HVDC Champa - Kurukshetra	804.26	1126.68	2069.11	2235.18	1955.13	2230.56	739.22	11160.14
WR - NR HVDC Vindhyachal	0.49	3.23	3.13	94.78	21.55	7.26	50.51	180.95
WR - NR 400 kV Zerda Kankroli	0.00	0.00	1.48	15.36	13.10	8.58	0.00	38.52
WR - NR 400 kV Zerda Bhinmal	0.00	0.00	0.00	12.54	13.56	23.81	0.34	50.25
WR - NR 400 kV RAPP C - Shujalpur D/C	2.28	31.04	16.05	164.49	80.51	147.53	18.12	460.02
WR - NR 220 kV Bhanpura - Ranpur	9.67	65.53	68.13	70.02	74.29	61.03	65.71	414.38
WR - NR 220 kV Bhanpura - Modak	0.00	0.00	0.00	0.00	0.00	38.00	62.92	100.92
WR - NR 220 kV Auraiya - Malanpur/Mehgaon	0.00	0.15	0.00	0.00	0.00	0.00	0.00	0.15
WR - NR 400 kV Vindhyachal-Rihand D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
WR - NR HVDC Mundra - Mohindergarh	132.55	340.75	234.27	124.89	667.23	827.57	920.93	3248.19
WR-NR 765 kV Banaskata-Chittorgarh D/C	0.00	3.26	16.02	169.31	260.02	66.60	0.00	515.21
WR-NR 765 kV Varanasi-Vindhyachal	1030.05	1663.34	1854.30	1854.38	1551.38	1697.01	1174.50	10824.96
Total WR - NR	4103.96	6088.00	6821.89	7965.87	7008.82	8282.89	5245.41	45516.84
Export of NR to WR (NR-WR)								
NR - WR 765 kV Gwalior - Agra 2xS/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
NR - WR 765 kV Gwalior - Phagi 2xS/C	0.00	5.41	0.00	0.00	0.00	0.00	0.00	5.41
NR - WR 765 kV Jabalpur-Orai D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
NR - WR 765 kV Satna-Orai	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
NR - WR 765 kV Gwalior-Orai	440.87	385.11	301.32	367.88	368.83	385.80	399.85	2649.66
NR - WR HVDC Champa - Kurukshetra	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
NR - WR HVDC Vindhyachal	289.83	273.88	267.04	184.43	225.73	180.86	26.34	1448.11
NR - WR 400 kV Zerda Kankroli	185.75	94.43	108.34	24.78	31.17	41.36	96.48	582.31
NR - WR 400 kV Zerda Bhinmal	282.42	181.64	200.56	73.76	74.62	64.65	158.50	1036.15
NR - WR 400 kV RAPP C - Shujalpur D/C	85.74	45.64	45.64	0.00	3.36	0.00	46.93	227.31
NR - WR 220 kV Bhanpura - Ranpur	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
NR - WR 220 kV Bhanpura - Modak	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
NR - WR 220 kV Auraiya - Malanpur/Mehgaon	56.56	28.58	50.82	47.16	97.78	68.03	111.08	460.01
NR-WR 400 kV Rihand-Vindhyachal D/C	644.30	672.49	642.32	664.33	653.25	658.85	669.33	4604.87
NR - WR HVDC Mundra - Mohindergarh	243.86	54.36	36.25	94.16	0.00	0.00	0.00	428.63
NR - WR 765 kV Banaskata-Chittorgarh D/C	976.83	428.19	421.52	94.53	51.63	180.84	597.81	2751.35
NR-WR 765 kV Varanasi-Vindhyachal	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Total NR - WR	3206.16	2169.73	2073.81	1551.03	1506.37	1580.39	2106.32	14193.81

	Apr'23	May'23	June'23	July'23	Aug'23	Sep'23	Oct'23	Fin. Year 2023-24
Name of Line								
Import of NR from ER (ER-NR)								
ER - NR 765 kV Sasaram - Fatehpur	166.02	114.36	82.57	74.16	131.29	131.20	192.41	892.01
ER - NR 765 kV Gaya - Varanasi 2*S/C	224.56	107.46	28.46	47.20	75.64	115.88	182.55	781.75
ER - NR 765 kV Gaya - Balia	246.38	335.46	321.28	300.74	224.31	332.43	250.12	2010.72
ER - NR HVDC Alipurduar - Agra	0.00	0.00	375.05	784.99	444.13	750.81	497.43	2852.41
ER-NR 400 kV Patna - Balia D/C	219.16	246.32	242.35	242.23	300.66	262.01	203.70	1716.43
ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	127.03	223.63	277.35	376.44	415.21	330.20	255.04	2004.90
ER - NR 400 kV Biharshariff - Balia D/C	22.11	72.32	102.97	92.77	101.30	90.47	56.79	538.73
ER - NR 400 kV Motihari - Gorakhpur D/C	156.88	188.70	180.09	228.59	251.16	190.46	142.10	1337.98
ER - NR 400 kV Biharshariff - Varanasi D/C	67.56	47.21	34.66	24.65	44.14	47.88	63.00	329.10
ER - NR 400 kV Sasaram -Varanasi	74.99	38.68	46.09	55.64	28.71	57.56	16.47	318.14
ER - NR 400 kV Sasaram -Allahabad	51.91	33.39	21.29	28.77	17.25	52.61	27.20	232.42
ER - NR 220 kV Sahupuri-Karnanasa	78.64	82.22	82.32	43.45	51.19	29.26	36.16	403.24
ER - NR 132 kV Sahupuri - Karnanasa	1.92	0.00	0.96	1.12	0.96	2.02	3.28	10.26
ER - NR 132 kV 132 kV Rihand - Nagar Untari	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
ER - NR 132 kV Rihand - Garhwa	0.46	0.00	0.00	0.00	0.00	0.00	0.00	0.46
ER-NR 400 kV Naubatpur - Balia D/C	211.13	243.59	239.56	236.53	300.12	264.57	198.04	1693.54
Total ER-NR	1648.75	1733.34	2035.00	2537.28	2386.07	2657.36	2124.29	15122.09
Import of NR from NER (NER-NR)								
NER-NR HVDC Biswanath Chariali - Agra	0.00	0.00	153.62	339.28	465.76	447.38	470.05	1876.09
Total NER - NR	0.00	0.00	153.62	339.28	465.76	447.38	470.05	1876.09
Export of NR to ER (NR-ER)								
NR - ER 765 kV Sasaram - Fatehpur	0.00	2.65	7.74	3.45	0.00	4.62	0.00	18.46
NR - ER 765 kV Gaya - Varanasi 2*S/C	0.30	38.74	102.98	45.94	11.70	32.51	8.41	240.58
NR - ER 765 kV Gaya - Balia	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
NR - ER HVDC Alipurduar - Agra	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
NR - ER 400 kV Patna - Balia 2xD/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
NR - ER 400 kV Muzaffarpur - Gorakhpur D/C	3.47	0.00	0.00	0.00	0.00	0.00	0.00	3.47
NR - ER 400 kV Biharshariff - Balia D/C	17.15	4.18	13.06	0.00	0.00	3.12	4.14	41.65
ER - NR 400 kV Motihari - Gorakhpur D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
NR - ER 400 kV Biharshariff - Varanasi D/C	2.90	7.31	20.53	10.39	0.22	12.39	4.69	58.43
NR - ER 400 kV Sasaram -Varanasi	0.00	0.00	0.00	0.00	1.67	0.00	0.85	2.52
NR - ER 400 kV Sasaram -Allahabad	2.25	0.00	0.00	0.82	2.28	0.00	0.23	5.58
NR - ER 220 kV Sahupuri-Karnanasa	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
NR - ER 132 kV Sahupuri - Karnanasa	0.01	0.96	0.48	0.96	0.00	0.58	0.48	3.47
NR - ER 132 kV 132 kV Rihand - Nagar Untari	1.74	2.20	1.08	3.37	2.39	3.46	1.80	16.04
ER - NR 132 kV Rihand - Garhwa	10.23	8.48	19.67	18.35	14.38	11.19	11.51	93.81
NR-ER 400 kV Balia- Naubatpur D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Total NR - ER	38.05	64.52	165.54	83.28	32.64	67.87	32.11	484.01
Export of NR to NER (NER-NR)								
NR-NR HVDC Biswanath Chariali - Agra	261.93	291.71	104.47	0.00	0.00	0.00	0.00	658.11
Total NR - NER	261.93	291.71	104.47	0.00	0.00	0.00	0.00	658.11

	Apr'23	May'23	June'23	July'23	Aug'23	Sep'23	Oct'23	Fin. Year 2023-24
Name of Line								
Export of WR to ER (WR-ER)								
WR - ER 765 kV Ranchi - Dharamjaygarh 2x5/C	139.81	504.96	673.15	734.00	331.39	537.29	228.34	3148.94
WR - ER 765 kV Dharamjaygarh - Jharsuguda 2xD/C	652.31	469.82	490.99	593.61	768.89	177.22	238.94	3391.78
WR - ER 765 kV Durg - Jharsuguda D/C	0.00	0.64	1.75	26.78	7.42	1.32	0.00	37.91
WR - ER 400 kV Sipat - Ranchi D/C	15.97	93.84	118.29	133.75	52.57	87.51	30.29	532.22
WR - ER 400 kV Raigarh - Jharsuguda 2xD/C	0.44	6.23	8.79	6.26	28.69	11.41	0.82	62.64
WR - ER 220 kV Korba - Budhipadar D/C	36.08	80.04	73.19	22.96	28.75	29.18	26.25	296.46
WR - ER 220 kV Raigarh - Budhipadar	0.15	0.57	1.17	0.00	0.35	0.34	0.00	2.58
Total WR - ER	844.75	1156.11	1367.33	1517.34	1218.07	844.29	524.64	7472.53
Import of WR from ER (ER - WR)								
ER - WR 765 kV Ranchi - Dharamjaygarh 2x5/C	144.10	11.95	15.57	10.81	83.69	14.84	62.72	343.68
ER - WR 765 kV Dharamjaygarh - Jharsuguda 2xD/C	25.46	58.29	33.08	15.65	2.33	214.83	131.20	480.84
ER - WR 765 kV Durg - Jharsuguda D/C	394.08	204.42	148.02	71.84	73.64	163.98	298.15	1354.12
ER - WR 400 kV Sipat - Ranchi D/C	55.56	5.71	9.07	7.22	29.65	8.91	40.59	156.70
ER - WR 400 kV Raigarh - Jharsuguda 2xD/C	248.78	148.94	125.69	125.00	127.87	110.94	267.35	1154.56
ER - WR 220 kV Korba - Budhipadar D/C	1.45	0.00	0.14	6.23	1.99	1.46	3.18	14.46
ER - WR 220 kV Raigarh - Budhipadar	55.98	38.46	41.41	66.29	74.76	49.37	81.54	407.80
Total ER - WR	925.41	467.76	372.98	303.04	393.92	564.32	884.73	3912.16
Export of ER to NER (ER - NER)								
ER - NER 400 kV Binaguri - Bongaigaon D/C	6.99	16.15	105.81	142.19	71.19	215.10	134.98	692.41
ER - NER 400 kV Alipurduar - Bongaigaon D/C	4.62	34.31	135.94	83.03	84.82	161.59	95.15	599.46
ER - NER 220 kV Birpara - Salakati D/C	0.54	3.12	31.19	37.25	25.19	47.94	25.71	170.93
Total ER - NER	12.16	53.58	272.93	262.48	181.20	424.63	255.83	1462.80
Import of ER from NER (NER - ER)								
NER - ER 400 kV Binaguri - Bongaigaon D/C	52.83	40.19	37.75	2.10	10.62	0.07	5.53	149.09
NER - ER 400 kV Alipurduar - Bongaigaon D/C	182.37	135.22	72.81	20.59	29.76	3.08	23.52	467.35
NER - ER 220 kV Birpara - Salakati D/C	34.59	31.32	10.78	0.62	2.83	0.14	2.65	82.91
Total NER - ER	269.78	206.73	121.33	23.31	43.22	3.29	31.70	699.35
Export of ER to SR (ER - SR)								
ER - SR HVDC Gazuwaka	375.93	395.23	208.61	178.44	321.36	201.99	378.26	2059.82
ER - SR HVDC Talchar - Kolar	1233.20	1204.28	984.75	977.61	1284.58	1076.42	1294.48	8055.31
ER - SR 765 kV Angul- Srikakulam D/C	1683.42	1561.33	1412.42	1184.37	1380.27	1160.32	1534.32	9916.46
Total ER - SR	3292.55	3160.85	2605.77	2340.42	2986.21	2438.74	3207.06	20031.59
Import of ER from SR (SR - ER)								
SR - ER HVDC Gazuwaka	0.00	0.00	55.34	114.11	32.48	0.00	0.00	201.93
SR - ER HVDC Talchar - Kolar	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.01
SR - ER 765 kV Angul- Srikakulam D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Total SR - ER	0.00	0.00	55.34	114.11	32.48	0.00	0.00	201.94

	Apr'23	May'23	June'23	July'23	Aug'23	Sep'23	Oct'23	Fin. Year 2023-24
Name of Line								
Export of WR to SR (WR-SR)								
WR - SR HVDC Bhadrawati	544.41	411.52	171.68	139.64	464.81	222.80	593.89	2548.76
WR - SR 765 kV Sholapur - Raichur 2xS/C	417.69	222.76	146.07	83.93	451.70	125.10	226.89	1674.15
WR - SR 765 kV Wardha - Nizamabad D/C	1323.51	873.44	1018.25	852.05	1313.80	864.24	1099.04	7344.33
WR - SR 400KV Kolhapur-Kudgi D/C	0.00	0.00	0.00	0.00	0.06	0.00	0.00	0.06
WR-SR HVDC Raigarh-Pugalur	3004.35	1791.86	1182.91	885.62	2135.69	1450.16	2583.88	13034.46
WR-SR 220kV Xeldem - Ambewadi S/C	77.16	70.18	68.17	61.74	68.61	67.55	69.49	482.90
WR-SR 220kV Ponda - Ambewadi S/C	0.29	1.54	0.28	0.16	5.23	0.04	0.08	7.61
Total WR - SR	5367.41	3371.30	2587.37	2023.14	4439.89	2729.89	4573.27	25092.26
Import of WR from SR (SR - WR)								
SR - WR HVDC Bhadrawati	4.11	25.09	178.09	308.60	10.36	114.86	0.00	641.13
SR - WR 765 kV Raichur - Sholapur 2xS/C	29.13	205.27	344.82	478.51	54.56	420.76	215.80	1748.84
SR - WR 765 kV Wardha - Nizamabad D/C	0.00	3.90	0.32	18.33	0.00	19.87	0.03	42.45
SR - WR 400KV Kolhapur-Kudgi D/C	623.59	719.30	784.98	796.02	623.43	850.54	765.68	5163.55
SR-WR HVDC Pugalur-Raigarh	0.00	3.73	14.87	16.65	0.00	0.09	0.00	35.33
WR-SR 220kV Ambewadi - Xeldem S/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
WR-SR 220kV Ambewadi-Ponda S/C	0.00	0.00	0.01	0.00	0.01	0.01	0.02	0.05
Total SR - WR	656.84	957.30	1323.09	1618.10	688.36	1406.13	981.53	7631.35
TOTAL ALL INDIA	20628	19721	20060	20679	21383	21447	20437	144355

*In case of mutiple ckt / DC pole year corres. to the commissioning of final element

Date	15.1 Import-Export of NR with WR during October 2023																	
	Import of NR from WR (WR-NR)																	
	WR - NR 765 kV Gwalior - Agra 2x5/C	WR-NR 765 kV Gwalior-Phagi 2x5/C	WR-NR 765 kV Jabalpur- Orai D/C	WR-NR 765 kV Satna- Orai	WR-NR 765 kV Gwalior-Orai	WR - NR HVDC Champa- Kurukshetra	WR - NR HVDC Vindhyachal	WR - NR 400 kV Zerd- Kankroli	WR - NR 400 kV Zerd- Bhinmal	WR-NR 400 kV RAPP C - Shujalpur D/C	WR - NR 220 kV Bhanpura - Ranpur	WR - NR 220 kV Bhanpura - Modak	WR - NR 220 kV Auraiya - Malanpur / Mehgaon	WR-NR 400 kV Rihand Vindhyachal D/C	WR - NR HVDC Mundra - M'garh	WR -NR 765 kV Banaskata - Chittorgarh D/C	WR-NR 765 kV Varanasi- Vindhyachal	Total WR - NR
1-Oct-23	28.42	22.24	24.50	22.66	0.00	59.20	0.00	0.00	0.00	3.03	2.26	1.62	0.00	0.00	19.39	0.00	47.71	231.03
2-Oct-23	25.34	19.60	30.75	19.36	0.00	35.02	0.00	0.00	0.00	3.20	2.21	1.67	0.00	0.00	19.39	0.00	44.22	200.76
3-Oct-23	20.21	19.15	25.82	19.31	0.00	34.96	0.00	0.00	0.00	1.66	2.18	1.74	0.00	0.00	29.56	0.00	36.15	190.74
4-Oct-23	15.20	18.21	20.43	18.37	0.00	43.23	0.00	0.00	0.00	1.29	2.20	1.49	0.00	0.00	34.71	0.00	35.03	190.16
5-Oct-23	17.48	9.70	16.92	17.64	0.00	47.81	0.00	0.00	0.00	0.28	2.24	1.60	0.00	0.00	34.71	0.00	34.40	182.78
6-Oct-23	18.02	5.95	13.47	17.43	0.00	59.65	0.00	0.00	0.00	0.00	2.42	1.78	0.00	0.00	32.20	0.00	38.64	189.56
7-Oct-23	15.65	5.47	12.81	16.93	0.00	59.80	0.00	0.00	0.00	0.00	2.41	1.94	0.00	0.00	36.27	0.00	41.21	192.49
8-Oct-23	16.80	7.23	16.45	16.31	0.00	57.97	0.00	0.00	0.00	0.00	2.42	1.69	0.00	0.00	38.59	0.00	42.76	200.22
9-Oct-23	15.56	5.78	16.48	17.35	0.00	57.81	0.00	0.00	0.00	0.00	2.45	1.35	0.00	0.00	43.50	0.00	42.80	203.08
10-Oct-23	19.18	7.44	20.10	17.30	0.00	58.10	0.00	0.00	0.00	0.00	2.36	1.12	0.00	0.00	43.50	0.00	47.12	216.22
11-Oct-23	23.34	14.70	27.57	18.06	0.00	57.56	0.00	0.00	0.34	2.37	2.40	1.13	0.00	0.00	44.80	0.00	44.97	237.24
12-Oct-23	14.75	15.31	27.05	16.58	0.00	57.78	0.30	0.00	0.00	0.93	2.54	1.40	0.00	0.00	48.32	0.00	43.40	228.36
13-Oct-23	18.74	16.54	24.59	17.33	0.00	58.02	1.24	0.00	0.00	0.81	2.67	1.70	0.00	0.00	48.33	0.00	44.68	234.65
14-Oct-23	22.60	18.25	29.70	18.55	0.00	20.86	1.24	0.00	0.00	0.75	2.43	1.80	0.00	0.00	39.01	0.00	44.89	200.08
15-Oct-23	22.75	16.10	26.58	17.36	0.00		1.24	0.00	0.00	0.10	2.28	0.89	0.00	0.00	27.94	0.00	43.81	159.05
16-Oct-23	10.31	14.69	14.86	15.37	0.00		1.24	0.00	0.00	0.00	2.23	1.89	0.00	0.00	29.02	0.00	35.92	125.53
17-Oct-23	3.90	9.62	5.41	12.80	0.00		1.24	0.00	0.00	0.00	2.10	1.82	0.00	0.00	25.61	0.00	30.99	93.49
18-Oct-23	6.42	12.47	7.88	12.51	0.00		1.24	0.00	0.00	0.00	2.09	2.24	0.00	0.00	22.76	0.00	34.44	102.05
19-Oct-23	9.74	21.13	13.38	14.05	0.00	0.00	1.24	0.00	0.00	0.00	2.15	2.54	0.00	0.00	14.87	0.00	31.62	110.72
20-Oct-23	12.62	25.04	17.41	16.81	0.00	0.00	1.24	0.00	0.00	0.00	2.12	2.01	0.00	0.00	20.36	0.00	34.53	132.14
21-Oct-23	13.90	26.86	21.51	18.90	0.00		1.24	0.00	0.00	0.00	2.01	2.70	0.00	0.00	19.37	0.00	37.94	144.43
22-Oct-23	11.42	25.81	17.72	17.43	0.00	0.00	1.24	0.00	0.00	0.00	2.00	2.58	0.00	0.00	29.03	0.00	31.17	138.40
23-Oct-23	10.71	25.05	16.52	18.27	0.00		1.24	0.00	0.00	0.00	1.99	2.55	0.00	0.00	27.95	0.00	32.28	136.56
24-Oct-23	7.06	18.91	15.35	17.07	0.00		1.24	0.00	0.00	0.00	1.85	2.40	0.00	0.00	27.95	0.00	32.35	124.18
25-Oct-23	6.40	22.03	11.95	16.27	0.00		1.24	0.00	0.00	0.00	1.79	2.38	0.00	0.00	28.50	0.00	23.73	114.29
26-Oct-23	10.84	25.60	17.98	17.85	0.00		4.16	0.00	0.00	0.00	1.77	2.60	0.00	0.00	24.09	0.00	27.11	132.00
27-Oct-23	15.20	27.47	21.70	19.63	0.00		5.97	0.00	0.00	0.00	1.90	2.72	0.00	0.00	20.70	0.00	41.20	156.49
28-Oct-23	18.33	34.58	25.45	21.73	0.00		6.00	0.00	0.00	1.83	1.59	2.81	0.00	0.00	24.21	0.00	38.75	175.28
29-Oct-23	13.78	31.28	21.72	20.12	0.00	4.20	6.01	0.00	0.00	0.86	1.49	2.96	0.00	0.00	24.21	0.00	36.34	162.97
30-Oct-23	16.12	30.49	20.34	19.39	0.00	11.81	6.02	0.00	0.00	1.01	1.62	2.90	0.00	0.00	24.21	0.00	34.35	168.26
31-Oct-23	18.96	29.99	19.63	19.95	0.00	15.44	5.93	0.00	0.00	0.00	1.54	2.90	0.00	0.00	17.87	0.00	39.99	172.20
Total	479.75	582.69	602.03	548.69	0.00	739.22	50.51	0.00	0.34	18.12	65.71	62.92	0.00	0.00	920.93	0.00	1174.50	5245.41
Disclaimer:- Blank entry if the line under outage/shutdown on corrsponding day																		

Date	15.1 Import-Export of NR with WR during October 2023																	
	Export of NR to WR (NR- WR)																	
	NR - WR 765 kV Gwalior - Agra 2x5/C	NR-WR 765 kV Gwalior-Phagi 2x5/C	NR-WR 765 kV Jabalpur- Orai D/C	NR-WR 765 kV Satna- Orai	NR-WR 765 kV Gwalior-Orai	NR - WR HVDC Champa- Kurukshetra	NR - WR HVDC Vindhyachal	NR - WR 400 kV Zerda- Kankrol	NR - WR 400 kV Zerda- Bhinmal	NR-WR 400 kV RAPP C - Shujalpur D/C	WR - NR 220 kV Bhanpura - Ranpur	WR - NR 220 kV Bhanpura - Modak	NR - WR 220 kV Auraiya - Malanpur / Mehgaon	NR-WR 400 kV Rihand- Vindhyachal D/C	NR - WR HVDC Mundra - M'garh	NR - WR 765 kV Banaskata - Chittorgarh D/C	NR-WR 765 kV Varanasi- Vindhyachal	Total NR - WR
1-Oct-23	0.00	0.00	0.00	0.00	7.57	0.00	1.23	0.80	1.01	0.00	0.00	0.00	2.17	21.04	0.00	5.41	0.00	39.23
2-Oct-23	0.00	0.00	0.00	0.00	11.45	0.00	1.22	2.13	2.82	0.00	0.00	0.00	2.48	22.77	0.00	12.87	0.00	55.74
3-Oct-23	0.00	0.00	0.00	0.00	12.53	0.00	1.23	3.15	4.18	0.00	0.00	0.00	3.00	22.21	0.00	18.12	0.00	64.42
4-Oct-23	0.00	0.00	0.00	0.00	11.55	0.00	1.23	3.68	5.62	0.00	0.00	0.00	3.27	22.10	0.00	20.41	0.00	67.86
5-Oct-23	0.00	0.00	0.00	0.00	10.01	0.00	1.23	2.86	5.39	0.00	0.00	0.00	3.72	22.10	0.00	13.30	0.00	58.61
6-Oct-23	0.00	0.00	0.00	0.00	8.29	0.00	1.23	2.15	7.29	2.41	0.00	0.00	4.42	21.95	0.00	9.68	0.00	57.42
7-Oct-23	0.00	0.00	0.00	0.00	8.22	0.00	1.23	2.13	6.68	1.89	0.00	0.00	4.56	22.39	0.00	10.33	0.00	57.43
8-Oct-23	0.00	0.00	0.00	0.00	9.53	0.00	1.23	1.55	5.27	0.93	0.00	0.00	4.55	22.16	0.00	9.84	0.00	55.06
9-Oct-23	0.00	0.00	0.00	0.00	10.10	0.00	1.23	1.32	4.46	1.97	0.00	0.00	4.70	22.50	0.00	5.82	0.00	52.10
10-Oct-23	0.00	0.00	0.00	0.00	9.17	0.00	4.68	0.35	0.61	0.46	0.00	0.00	5.03	22.43	0.00	0.31	0.00	43.04
11-Oct-23	0.00	0.00	0.00	0.00	12.19	0.00	6.10	0.69	0.00	0.00	0.00	0.00	4.90	22.52	0.00	5.44	0.00	51.84
12-Oct-23	0.00	0.00	0.00	0.00	11.74	0.00	4.50	1.39	1.72	0.00	0.00	0.00	4.86	22.10	0.00	12.73	0.00	59.04
13-Oct-23	0.00	0.00	0.00	0.00	11.84	0.00	0.00	1.77	3.18	0.00	0.00	0.00	4.95	22.10	0.00	14.47	0.00	58.31
14-Oct-23	0.00	0.00	0.00	0.00	12.37	0.00	0.00	1.94	5.46	0.00	0.00	0.00	3.92	22.21	0.00	11.27	0.00	57.17
15-Oct-23	0.00	0.00	0.00	0.00	12.36		0.00	1.68	2.98	0.00	0.00	0.00	2.68	22.13	0.00	10.94	0.00	52.77
16-Oct-23	0.00	0.00	0.00	0.00	12.02		0.00	2.34	5.28	4.86	0.00	0.00	3.56	22.17	0.00	13.38	0.00	63.61
17-Oct-23	0.00	0.00	0.00	0.00	12.23		0.00	3.87	9.02	6.38	0.00	0.00	3.27	22.16	0.00	22.86	0.00	79.79
18-Oct-23	0.00	0.00	0.00	0.00	14.24		0.00	3.92	7.18	5.51	0.00	0.00	3.61	22.31	0.00	23.56	0.00	80.33
19-Oct-23	0.00	0.00	0.00	0.00	17.42	0.00	0.00	3.38	5.28	2.37	0.00	0.00	3.50	22.29	0.00	23.53	0.00	77.77
20-Oct-23	0.00	0.00	0.00	0.00	16.18	0.00	0.00	3.36	4.96	1.19	0.00	0.00	3.29	22.10	0.00	22.36	0.00	73.44
21-Oct-23	0.00	0.00	0.00	0.00	15.79		0.00	3.93	6.30	1.44	0.00	0.00	3.35	22.10	0.00	25.56	0.00	78.47
22-Oct-23	0.00	0.00	0.00	0.00	17.15	0.00	0.00	2.58	7.37	1.98	0.00	0.00	3.18	22.10	0.00	27.66	0.00	82.02
23-Oct-23	0.00	0.00	0.00	0.00	15.81		0.00	5.78	8.16	2.74	0.00	0.00	3.12	21.73	0.00	35.86	0.00	93.20
24-Oct-23	0.00	0.00	0.00	0.00	13.66		0.00	5.56	7.75	4.19	0.00	0.00	3.26	21.52	0.00	34.75	0.00	90.69
25-Oct-23	0.00	0.00	0.00	0.00	15.36		0.00	5.06	6.78	3.78	0.00	0.00	3.53	10.82	0.00	31.49	0.00	76.82
26-Oct-23	0.00	0.00	0.00	0.00	14.23		0.00	4.92	6.82	2.45	0.00	0.00	3.35	16.81	0.00	30.30	0.00	78.88
27-Oct-23	0.00	0.00	0.00	0.00	13.76		0.00	6.88	4.85	1.75	0.00	0.00	3.08	22.12	0.00	30.26	0.00	82.70
28-Oct-23	0.00	0.00	0.00	0.00	16.08		0.00	4.86	6.53	0.00	0.00	0.00	2.63	22.10	0.00	32.48	0.00	84.68
29-Oct-23	0.00	0.00	0.00	0.00	15.06	0.00	0.00	4.78	5.94	0.00	0.00	0.00	2.87	22.10	0.00	33.42	0.00	84.17
30-Oct-23	0.00	0.00	0.00	0.00	16.30	0.00	0.00	4.11	4.67	0.00	0.00	0.00	3.25	22.08	0.00	26.36	0.00	76.77
31-Oct-23	0.00	0.00	0.00	0.00	15.64	0.00	0.00	3.56	4.94	0.63	0.00	0.00	3.02	22.11	0.00	23.04	0.00	72.94
Total	0.00	0.00	0.00	0.00	399.85	0.00	26.34	96.48	158.50	46.93	0.00	0.00	111.08	669.33	0.00	597.81	0.00	2106.32
Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day																		

Date	15.2 Import-Export of NR with ER & NER during October 2023																		
	Import of NR from ER (ER-NR)																	Import of NR from NER (NER-NR)	
	ER - NR 765 kV Sasaram - Fatehpur	ER - NR 765 kV Gaya - Varanasi 2*5/C	ER - NR 765 kV Gaya Ballia	ER - NR HVDC Alipurduar - Agra	ER-NR 400 kV Patna - Ballia D/C	ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	ER - NR 400 kV Biharsharif - Ballia D/C	ER - NR 400 kV Motihari - Gorakhpur D/C	ER - NR 400 kV Biharsharif - Varanasi D/C	ER-NR 400 kV Sasaram - Varanasi	ER-NR 400 kV Sasaram - Allahabad	ER - NR 220 kV Sahupuri - Karamnasa	ER - NR 132 kV Sahupuri - Karamnasa	ER - NR 132 kV Rihand - Nagar Untari	NR - ER 132 kV Rihand - Garhwa	ER-NR 400 kV Naubatpur - Ballia D/C	Total ER - NR	NER-NR HVDC Biswanath Chariali - Agra	Total NER-NR
1-Oct-23	7.87	11.18	9.07	33.50	8.48	12.60	3.55	6.76	3.60	0.00	0.53	1.78	0.00		0.00	8.51	107.43	12.20	12.20
2-Oct-23	6.67	8.80	11.70	29.60	8.73	12.38	3.69	7.04	3.68	0.43	1.52	2.00			0.00	8.66	104.90	12.34	12.34
3-Oct-23	8.93	10.83	10.02	31.50	9.59	12.66	4.11	7.14	3.95	0.60	1.72	1.83	0.00		0.00	9.75	112.63	11.38	11.38
4-Oct-23	6.67	8.22	8.83	22.26	8.12	9.40	2.35	5.12	2.34	0.77	1.41	1.14			0.00	8.17	84.80	11.58	11.58
5-Oct-23	5.95	4.90	8.18	18.44	7.26	11.50	2.41	5.63	1.18	0.88	0.96	1.24	0.48		0.00	7.30	76.31	12.20	12.20
6-Oct-23	4.02	1.68	7.71	16.35	6.32	11.27	2.11	5.55	0.01	1.20	1.09	1.10			0.00	6.21	64.62	12.28	12.28
7-Oct-23	3.32	0.15	7.50	12.21	5.59	8.31	0.40	4.23	0.00	1.23	1.02	0.64		0.00		5.19	49.79	17.00	17.00
8-Oct-23	4.68	1.75	8.17	12.09	5.78	9.36	0.99	4.68	0.28	1.14	1.20	1.24	0.00	0.00		5.53	56.89	16.88	16.88
9-Oct-23	5.02	0.23	7.80	12.03	5.28	8.24	1.22	3.96	0.33	1.16	1.13	1.10		0.00		4.94	52.44	17.01	17.01
10-Oct-23	4.21	0.00	8.43	12.20	5.02	9.14	1.13	4.64	0.16	1.34	0.96	1.41			0.00	4.66	53.30	13.09	13.09
11-Oct-23	3.65	1.19	8.90	11.69	6.30	8.56	1.34	5.38	1.12	0.87	0.80	1.19			0.00	5.64	56.63	16.36	16.36
12-Oct-23	3.28	2.26	8.90	11.61	8.74	9.06	1.45	5.49	1.57	0.47	0.64		1.36		0.00	7.07	61.90	13.71	13.71
13-Oct-23	3.53	1.17	8.30	11.97	6.79	7.22	1.21	4.50	0.80	0.42	0.77	1.41			0.00	5.82	53.91	15.67	15.67
14-Oct-23	6.58	4.40	9.33	10.58	7.97	8.44	2.04	4.12	1.80	0.00	0.88	0.00	0.48		0.00	7.89	64.51	15.97	15.97
15-Oct-23	5.56	4.42	9.01	11.19	7.43	8.84	2.07	4.49	1.31	0.45	0.73	1.65			0.00	7.32	64.47	16.48	16.48
16-Oct-23	4.06	0.86	5.70	11.96	5.68	4.15	0.00	2.99	0.00	0.80	0.21	1.35			0.00	5.38	43.14	16.51	16.51
17-Oct-23	2.57	0.00	3.59	12.38	1.87	0.39	0.00	0.16	0.00	1.21	0.00	0.76	0.00		0.00	1.31	24.24	16.71	16.71
18-Oct-23	3.44	0.00	4.21	12.08	2.63	2.03	0.00	1.09	0.00	1.37	0.00	0.60			0.00	2.07	29.52	14.28	14.28
19-Oct-23	5.81	1.76	5.02	11.59	4.56	3.73	0.04	1.94	0.34	0.77	0.33	1.05		0.00	0.00	4.27	41.21	13.35	13.35
20-Oct-23	4.45	6.10	7.19	11.39	6.00	5.50	0.52	3.22	2.28	0.28	0.83	1.51	0.00	0.00	0.00	5.99	55.26	13.67	13.67
21-Oct-23	8.19	10.25	9.28	14.06	7.03	7.47	1.92	4.05	3.91	0.00	1.13	1.49		0.00	0.00	7.04	75.82	14.97	14.97
22-Oct-23	8.85	12.03	9.55	17.32	7.61	9.57	3.24	5.24	4.72	0.00	1.26	1.73			0.00	7.78	88.90	14.66	14.66
23-Oct-23	8.83	11.92	9.99	17.79	7.89	9.47	2.43	5.55	3.27	0.01	0.95	1.55			0.00	8.11	87.76	16.77	16.77
24-Oct-23	7.30	7.40	8.23	16.87	6.31	8.55	1.95	4.72	2.82	0.18	0.93	1.36			0.00	6.37	72.99	16.86	16.86
25-Oct-23	9.00	10.50	7.87	16.66	6.44	7.86	2.40	4.07	4.08	0.17	1.01	1.29	0.00		0.00	6.41	77.76	16.98	16.98
26-Oct-23	8.47	10.20	8.42	16.45	5.91	7.57	2.11	4.25	2.97	0.19	0.99	1.14			0.00	5.94	74.61	16.91	16.91
27-Oct-23	8.00	7.02	9.54	17.29	4.65	8.69	3.35	3.50	3.35	0.00	0.00		0.48		0.00	4.50	70.37	16.94	16.94
28-Oct-23	8.70	9.56	9.66	17.10	6.74	9.28	2.67	5.27	3.66	0.51	0.52	1.20			0.00	6.81	81.68	16.28	16.28
29-Oct-23	7.40	13.04	5.28	17.30	7.54	8.38	2.36	5.56	3.60	0.00	1.21	1.25	0.48		0.00	7.73	81.13	17.12	17.12
30-Oct-23	8.68	11.51	5.40	17.27	8.32	7.88	2.03	6.33	2.42	0.00	1.29	1.04			0.00	8.53	80.70	16.83	16.83
31-Oct-23	8.72	9.22	9.34	12.70	7.12	7.54	1.70	5.43	3.45	0.02	1.18	1.11			0.00	7.14	74.67	17.06	17.06
Total	192.41	182.55	250.12	497.43	203.70	255.04	56.79	142.10	63.00	16.47	27.20	36.16	3.28	0.00	0.00	198.04	2124.29	470.05	470.05
Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day																			

Date	15.2 Import-Export of NR with ER & NER during October 2023																		
	Export of NR to ER (NR- ER)																	Export of NR to NER (NR-NER)	
	NR - ER 765 kV Sasaram - Fatehpur	NR - ER 765 kV Gaya - Varanasi 2*5/C	NR - ER 765 kV Gaya Balia	NR - ER HVDC Alipurduar - Agra	NR-ER 400 kV Patna - Balia D/C	NR - ER 400 kV Muzaffarpur - Gorakhpur D/C	NR - ER 400 kV Biharshariff - Balia D/C	NR - ER 400 kV Motihari - Gorakhpur D/C	NR - ER 400 kV Biharshariff - Varanasi D/C	NR-ER 400 kV Sasaram - Varanasi	NR-ER 400 kV Sasaram - Allahabad	NR - ER 220 kV Sahupuri- Karamnasa	NR - ER 132 kV Sahupuri - Karamnasa	NR - ER 132 kV Rihand - Nagar Untari	NR - ER 132 kV Rihand - Garhwa	NR-ER 400 kV Balia- Naubatpur D/C	Total NR -ER	NR-NER HVDC Biswanath Chariali - Agra	Total NR-NER
1-Oct-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.41	0.00	0.00	0.00		0.40	0.00	0.81	0.00	0.00
2-Oct-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.26	0.00	0.26	0.00	0.00
3-Oct-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.33	0.00	0.33	0.00	0.00
4-Oct-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.38	0.00	0.38	0.00	0.00
5-Oct-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.35	0.00	0.35	0.00	0.00
6-Oct-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.38	0.00	0.38	0.00	0.00
7-Oct-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.58	0.00	0.00	0.00		0.48		0.00	1.06	0.00	0.00
8-Oct-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.52		0.00	0.52	0.00	0.00
9-Oct-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.63		0.00	0.63	0.00	0.00
10-Oct-23	0.00	1.40	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.49	0.00	1.89	0.00	0.00
11-Oct-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.46	0.00	0.46	0.00	0.00
12-Oct-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00		0.47	0.00	0.47	0.00	0.00
13-Oct-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.47	0.00	0.47	0.00	0.00
14-Oct-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.09	0.00	0.00	0.00		0.41	0.00	0.50	0.00	0.00
15-Oct-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.44	0.00	0.44	0.00	0.00
16-Oct-23	0.00	0.00	0.00	0.00	0.00	0.00	0.27	0.00	0.13	0.00	0.00	0.00			0.51	0.00	0.91	0.00	0.00
17-Oct-23	0.00	2.78	0.00	0.00	0.00	0.00	2.38	0.00	2.12	0.00	0.04	0.00	0.00		0.37	0.00	7.69	0.00	0.00
18-Oct-23	0.00	4.23	0.00	0.00	0.00	0.00	1.49	0.00	1.86	0.00	0.19	0.00			0.43	0.00	8.20	0.00	0.00
19-Oct-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.40	0.00	0.40	0.00	0.00
20-Oct-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.48	0.07	0.44	0.00	0.99	0.00	0.00
21-Oct-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.10	0.00	0.00		0.10	0.45	0.00	0.65	0.00	0.00
22-Oct-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.06	0.00	0.00			0.46	0.00	0.52	0.00	0.00
23-Oct-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.45	0.00	0.45	0.00	0.00
24-Oct-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.39	0.00	0.39	0.00	0.00
25-Oct-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.33	0.00	0.33	0.00	0.00
26-Oct-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00				0.38	0.00	0.38	0.00	0.00
27-Oct-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.03	0.00		0.00		0.41	0.00	0.44	0.00	0.00
28-Oct-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.40	0.00	0.40	0.00	0.00
29-Oct-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.06	0.00	0.00	0.00		0.42	0.00	0.48	0.00	0.00
30-Oct-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.10	0.00	0.00			0.42	0.00	0.52	0.00	0.00
31-Oct-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.41	0.00	0.41	0.00	0.00
Total	0.00	8.41	0.00	0.00	0.00	0.00	4.14	0.00	4.69	0.85	0.23	0.00	0.48	1.80	11.51	0.00	32.11	0.00	0.00
Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day																			

Date	15.3 Import and Export of ER with WR & NER during October 2023																							
	Export of WR to ER (WR-ER)								Import of WR from ER (ER - WR)								Export of ER to NER (ER-NER)				Import of ER from NER (NER-ER)			
	WR - ER 765 kV Dharamjaygarh - Ranchi 2x5/C	WR - ER 765 kV Dharamjaygarh - Jharsuguda Q/C	WR - ER 765 kV Durg - Jharsuguda D/C	WR - ER 400 kV Sipat - Ranchi D/C	WR - ER 400 kV Raigarh - Jharsuguda- 2x2D/C	WR - ER 220 kV Korba - Budhipadar D/C	WR - ER 220 kV Raigarh - Budhipadar	Total WR - ER	ER - WR 765 kV Dharamjaygarh - Ranchi 2x5/C	ER-WR 765 kV Dharamjaygarh - Jharsuguda D/C	ER-WR 765 kV Durg - Jharsuguda D/C	ER - WR 400 kV Sipat - Ranchi D/C	ER - WR 400 kV Raigarh - Jharsuguda- 2x2D/C	ER - WR 220 kV Korba - Budhipadara D/C	ER - WR 220 kV Raigarh - Budhipadar	Total ER - WR	ER - NER 400 kV Binaguri - Bongaigaon D/C	ER - NER 400 kV Alipurduar - Bongaigaon D/C	ER - NER 220 kV Birpara - Salakati D/C	Total ER - NER	NER - ER 400 kV Binaguri - Bongaigaon D/C	NER - ER 400 kV Alipurduar - Bongaigaon 2x2D/C	NER - ER 220 kV Birpara - Salakati D/C	Total NER - ER
1-Oct-23	11.4	2.7	0.0	1.7	0.2	0.8	0.0	16.85	1.2	8.7	6.6	0.7	3.8	0.0	0.9	22.04	9.25	4.93	1.71	15.90	0.00	0.00	0.00	0.00
2-Oct-23	12.8	12.1	0.0	1.5	0.4	1.0	0.0	27.74	0.1	1.2	5.9	0.4	4.0	0.0	1.6	13.26	9.53	5.59	1.94	17.06	0.00	0.00	0.00	0.00
3-Oct-23	5.9	8.1	0.0	0.3	0.0	0.8	0.0	15.05	1.1	2.3	8.9	1.1	5.8	0.0	0.0	19.17	7.66	3.07	1.44	12.16	0.00	0.18	0.00	0.18
4-Oct-23	6.0	8.7	0.0	0.4	0.0	1.0	0.0	16.08	1.9	2.3	8.4	1.1	5.2	0.0	2.2	21.09	4.33	1.99	0.91	7.23	0.00	0.46	0.00	0.46
5-Oct-23	7.1	14.7	0.0	0.8	0.0	2.0	0.0	24.63	2.0	0.0	6.8	1.1	3.9	0.0	2.4	16.27	1.93	1.75	0.41	4.10	0.40	1.45	0.15	1.99
6-Oct-23	9.0	16.8	0.0	1.2	0.1	2.2	0.0	29.34	1.3	0.0	5.5	0.6	2.8	0.0	2.0	12.12	0.20	0.07	0.03	0.30	1.26	4.17	0.64	6.06
7-Oct-23	10.7	17.8	0.0	1.7	0.1	1.5	0.0	31.68	0.1	0.0	4.2	0.1	2.7	0.0	1.1	8.26	1.28	0.70	0.20	2.18	0.27	1.02	0.13	1.41
8-Oct-23	9.6	9.6	0.0	1.3	0.1	1.2	0.0	21.83	0.4	0.4	5.4	0.2	2.4	0.0	3.1	11.89	0.77	0.49	0.16	1.42	0.57	2.37	0.37	3.31
9-Oct-23	7.7	10.8	0.0	1.3	0.0	0.8	0.0	20.61	0.5	0.4	5.5	0.3	3.3	0.1	3.0	13.02	0.75	0.38	0.13	1.26	2.00	4.92	0.64	7.57
10-Oct-23	14.4	12.7	0.0	2.6	0.0	0.8	0.0	30.48	0.0	1.7	4.4	0.0	3.2	0.0	3.4	12.63	1.64	0.94	0.46	3.04	0.47	2.03	0.19	2.70
11-Oct-23	16.3	8.9	0.0	3.6	0.0	1.0	0.0	29.75	0.0	3.9	4.3	0.0	4.0	0.0	3.1	15.31	2.39	2.08	0.57	5.04	0.55	1.73	0.17	2.45
12-Oct-23	14.3	6.6	0.0	2.7	0.0	0.1	0.0	23.69	0.0	3.6	5.1	0.0	7.2	0.3	3.6	19.78	2.45	1.47	0.81	4.73	0.00	0.56	0.00	0.56
13-Oct-23	13.8	5.0	0.0	1.9	0.0	0.5	0.0	21.14	0.0	2.3	6.1	0.1	8.8	0.1	3.8	21.10	3.18	2.36	0.84	6.39	0.00	0.31	0.02	0.33
14-Oct-23	12.3	9.5	0.0	1.6	0.0	0.7	0.0	24.02	0.5	2.2	6.6	0.3	9.5	0.0	3.5	22.52	3.02	2.13	0.77	5.91	0.00	0.09	0.00	0.09
15-Oct-23	8.8	10.3	0.0	1.0	0.0	0.3	0.0	20.48	0.0	1.8	7.2	0.3	11.4	0.2	3.7	24.48	3.85	3.36	0.77	7.98	0.01	0.26	0.02	0.28
16-Oct-23	9.8	19.4	0.0	1.0	0.0	0.5	0.0	30.78	0.5	0.0	6.8	0.4	11.6	0.2	3.7	23.35	3.48	2.44	0.41	6.33	0.00	0.65	0.07	0.72
17-Oct-23	10.5	19.7	0.0	1.1	0.0	0.9	0.0	32.18	0.3	0.0	8.2	0.5	11.3	0.0	3.9	24.23	5.96	4.91	0.65	11.53	0.00	0.00	0.00	0.00
18-Oct-23	16.3	15.2	0.0	2.6	0.0	1.2	0.0	35.23	0.0	0.2	9.0	0.1	9.7	0.0	3.8	22.65	4.71	3.32	0.52	8.54	0.00	0.40	0.08	0.48
19-Oct-23	10.5	8.2	0.0	1.2	0.0	1.0	0.0	20.89	0.0	0.5	11.4	0.3	12.3	0.0	3.8	28.30	4.20	1.65	0.34	6.19	0.00	0.07	0.04	0.12
20-Oct-23	9.3	4.8	0.0	0.8	0.0	1.0	0.0	15.93	0.3	1.0	11.4	0.6	13.0	0.0	2.8	29.12	4.64	2.95	0.57	8.17	0.00	0.02	0.01	0.02
21-Oct-23	2.2	3.8	0.0	0.0	0.0	0.5	0.0	6.59	2.1	3.9	13.3	2.4	12.0	0.3	2.0	35.98	7.16	4.59	1.16	12.91	0.00	0.28	0.00	0.28
22-Oct-23	0.0	4.1	0.0	0.0	0.0	0.1	0.0	4.23	5.2	6.9	14.5	4.0	13.3	0.7	2.4	46.96	5.43	1.62	0.71	7.76	0.00	0.69	0.03	0.72
23-Oct-23	0.1	4.5	0.0	0.0	0.0	0.6	0.0	5.16	5.3	6.4	14.9	3.9	12.7	0.2	2.4	45.97	6.18	2.54	0.88	9.60	0.00	0.54	0.03	0.57
24-Oct-23	0.0	1.8	0.0	0.0	0.0	1.1	0.0	2.89	7.2	3.8	14.4	3.4	10.5	0.0	2.3	41.70	5.97	2.31	0.78	9.06	0.00	0.67	0.05	0.72
25-Oct-23	0.0	1.6	0.0	0.0	0.0	0.5	0.0	2.10	10.2	3.9	14.6	4.3	10.4	0.1	2.9	46.30	6.70	2.91	1.05	10.65	0.00	0.34	0.00	0.34
26-Oct-23	1.8	0.6	0.0	0.0	0.0	0.6	0.0	2.99	3.7	4.7	13.7	2.6	11.1	0.1	2.7	38.58	6.51	3.08	1.11	10.70	0.00	0.13	0.00	0.13
27-Oct-23	2.8	0.2	0.0	0.0	0.0	0.8	0.0	3.91	1.8	6.7	14.3	2.0	12.4	0.1	2.1	39.36	5.01	5.39	1.28	11.68	0.00	0.04	0.00	0.04
28-Oct-23	3.2	0.7	0.0	0.0	0.0	0.8	0.0	4.71	1.8	7.9	13.9	1.5	12.2	0.1	2.1	39.46	4.17	6.21	1.26	11.63	0.00	0.08	0.00	0.08
29-Oct-23	0.2	0.0	0.0	0.0	0.0	0.7	0.0	0.90	4.6	19.2	16.0	2.6	12.8	0.2	2.3	57.72	4.26	6.52	1.26	12.05	0.00	0.09	0.00	0.09
30-Oct-23	0.5	0.2	0.0	0.0	0.0	0.5	0.0	1.25	5.4	17.3	15.9	3.0	12.7	0.2	2.4	57.02	4.07	5.67	1.14	10.88	0.00	0.00	0.00	0.00
31-Oct-23	0.9	0.0	0.0	0.0	0.0	0.6	0.0	1.55	5.4	18.0	15.2	2.6	11.4	0.1	2.4	55.10	4.32	7.73	1.43	13.48	0.00	0.00	0.00	0.00
Total	228.34	238.94	0.00	30.29	0.82	26.25	0.00	524.64	62.72	131.20	298.15	40.59	267.35	3.18	81.54	884.73	134.98	95.15	25.71	255.83	5.53	23.52	2.65	31.70

Date	15.4 Import and Export of SR with ER & WR during October 2023																							
	Export of ER to SR (ER - SR)				Import of ER from SR (SR - ER)				Export of WR to SR (WR-SR)								Import of WR from SR (SR - WR)							
	ER - SR HVDC Gazuwaka	ER - SR HVDC Talchar - Kolar	ER-SR 765 kV Angul-Srikakulam D/C	Total ER - SR	SR - ER HVDC Gazuwaka	SR - ER HVDC Talchar -	SR-ER 765 kV Angul-Srikakulam D/C	Total SR - ER	WR - SR HVDC Bhadravati	WR - SR 765 kV Sholapur - Raichur 2x5/C	WR-SR 765 kV Wardha - Nizamabad D/C	WR-SR 400kV Kolhapur-Kudgi D/C	WR-SR HVDC Raigarh-Puglur	WR-SR 220kV Xeldem - Ambewadi S/C	WR-SR 220kV Ponda - Ambewadi S/C	Total WR - SR	SR - WR HVDC Bhadravati	SR - WR 765 kV Raichur - Sholapur 2x5/C	SR-WR 765 kV Wardha - Nizamabad D/C	SR-WR 400kV Kolhapur-Kudgi D/C	SR-WR HVDC Raigarh-Puglur	WR-SR 220kV Xeldem - Ambewadi S/C	WR-SR 220kV Ponda - Ambewadi S/C	Total SR - WR
1-Oct-23	8.71	37.04	35.38	81.12	0.00	0.00	0.00	0.00	8.57	0.76	18.83	0.00	34.23	2.01	0.00	64.40	0.00	19.82	0.03	28.48	0.00	0.00	0.00	48.34
2-Oct-23	8.20	39.71	41.55	89.47	0.00	0.00	0.00	0.00	7.28	3.96	28.09	0.00	35.48	1.93	0.00	76.75	0.00	8.41	0.00	20.62	0.00	0.00	0.00	29.02
3-Oct-23	8.61	39.71	48.89	97.21	0.00	0.00	0.00	0.00	19.21	8.68	37.13	0.00	68.75	2.31	0.00	136.08	0.00	2.32	0.00	18.62	0.00	0.00	0.00	20.94
4-Oct-23	11.35	39.51	51.89	102.75	0.00	0.00	0.00	0.00	22.06	15.79	41.83	0.00	81.97	2.30	0.00	163.95	0.00	1.44	0.00	16.22	0.00	0.00	0.00	17.66
5-Oct-23	10.72	44.72	56.19	111.63	0.00	0.00	0.00	0.00	22.55	25.48	50.34	0.00	90.54	2.34	0.00	191.26	0.00	0.00	0.00	14.11	0.00	0.00	0.00	14.11
6-Oct-23	13.47	44.38	48.79	106.64	0.00	0.00	0.00	0.00	24.12	15.91	45.01	0.00	100.88	2.30	0.00	188.22	0.00	0.00	0.00	18.89	0.00	0.00	0.00	18.89
7-Oct-23	14.79	42.13	45.78	102.69	0.00	0.00	0.00	0.00	24.11	16.46	45.33	0.00	92.01	2.09	0.00	180.00	0.00	0.00	0.00	19.30	0.00	0.00	0.00	19.30
8-Oct-23	12.68	45.26	45.37	103.31	0.00	0.00	0.00	0.00	20.51	15.86	43.34	0.00	95.63	2.14	0.00	177.49	0.00	0.04	0.00	21.40	0.00	0.00	0.00	21.44
9-Oct-23	12.70	46.52	49.75	108.97	0.00	0.00	0.00	0.00	23.32	19.21	47.45	0.00	107.95	2.46	0.00	200.39	0.00	0.00	0.00	23.88	0.00	0.00	0.00	23.88
10-Oct-23	12.70	48.04	52.53	113.27	0.00	0.00	0.00	0.00	21.49	23.60	50.69	0.00	95.84	2.37	0.00	194.01	0.00	0.00	0.00	19.43	0.00	0.00	0.00	19.43
11-Oct-23	12.69	48.02	45.43	106.14	0.00	0.00	0.00	0.00	14.01	11.30	38.68	0.00	93.84	2.31	0.00	160.14	0.00	0.80	0.00	23.21	0.00	0.00	0.00	24.02
12-Oct-23	12.67	46.02	42.11	100.79	0.00	0.00	0.00	0.00	12.98	10.15	39.25	0.00	93.73	2.37	0.05	158.53	0.00	1.39	0.00	23.56	0.00	0.00	0.00	24.95
13-Oct-23	12.69	41.24	46.01	99.94	0.00	0.00	0.00	0.00	20.76	9.84	40.34	0.00	90.62	2.32	0.00	163.88	0.00	1.53	0.00	25.76	0.00	0.00	0.00	27.29
14-Oct-23	12.70	44.90	53.72	111.32	0.00	0.00	0.00	0.00	21.55	14.08	45.18	0.00	88.85	2.38	0.00	172.05	0.00	0.04	0.00	22.97	0.00	0.00	0.00	23.01
15-Oct-23	12.69	46.58	55.66	114.94	0.00	0.00	0.00	0.00	15.58	10.26	43.03	0.00	67.79	2.29	0.00	138.95	0.00	0.64	0.00	24.49	0.00	0.00	0.00	25.14
16-Oct-23	12.38	45.75	60.93	119.06	0.00	0.00	0.00	0.00	19.40	17.54	50.05	0.00	69.62	2.26	0.00	158.88	0.00	0.17	0.00	20.88	0.00	0.00	0.00	21.05
17-Oct-23	12.42	48.09	53.20	113.71	0.00	0.00	0.00	0.00	24.06	1.95	35.35	0.00	94.45	2.29	0.00	158.11	0.00	5.15	0.00	26.04	0.00	0.00	0.00	31.19
18-Oct-23	12.39	43.11	47.44	102.93	0.00	0.00	0.00	0.00	24.07	0.55	28.40	0.00	96.33	2.31	0.00	151.66	0.00	10.01	0.00	29.97	0.00	0.00	0.00	39.99
19-Oct-23	12.44	45.88	47.91	106.23	0.00	0.00	0.00	0.00	24.07	0.77	27.34	0.00	94.01	2.34	0.00	148.52	0.00	10.24	0.00	30.07	0.00	0.00	0.00	40.31
20-Oct-23	12.63	48.05	47.91	108.60	0.00	0.00	0.00	0.00	24.09	0.47	26.41	0.00	85.58	1.26	0.00	137.80	0.00	8.38	0.00	29.19	0.00	0.00	0.00	37.56
21-Oct-23	12.62	40.09	50.29	103.00	0.00	0.00	0.00	0.00	12.60	0.99	29.78	0.00	80.56	2.48	0.00	126.41	0.00	5.26	0.00	26.68	0.00	0.00	0.00	31.94
22-Oct-23	12.60	39.76	52.26	104.62	0.00	0.00	0.00	0.00	12.07	0.14	29.41	0.00	72.28	2.40	0.00	116.30	0.00	9.72	0.00	28.57	0.00	0.00	0.00	38.29
23-Oct-23	12.60	37.46	54.18	104.23	0.00	0.00	0.00	0.00	9.61	0.02	28.69	0.00	59.21	2.37	0.00	99.89	0.00	13.05	0.00	28.53	0.00	0.00	0.00	41.58
24-Oct-23	12.61	36.57	53.72	102.90	0.00	0.00	0.00	0.00	14.37	2.09	30.25	0.00	77.02	2.29	0.00	126.02	0.00	7.94	0.00	23.09	0.00	0.00	0.00	31.04
25-Oct-23	12.61	45.77	51.88	110.26	0.00	0.00	0.00	0.00	22.08	0.49	26.75	0.00	91.82	2.36	0.00	143.50	0.00	9.45	0.00	27.58	0.00	0.00	0.00	37.03
26-Oct-23	12.60	48.05	51.26	111.91	0.00	0.00	0.00	0.00	17.01	0.17	28.80	0.00	84.75	2.35	0.00	133.09	0.00	13.62	0.00	29.19	0.00	0.00	0.00	42.80
27-Oct-23	12.61	48.03	50.61	111.25	0.00	0.00	0.00	0.00	20.88	0.09	32.98	0.00	78.33	2.22	0.00	134.50	0.00	16.82	0.00	31.07	0.00	0.00	0.00	47.89
28-Oct-23	12.60	44.54	49.51	106.66	0.00	0.00	0.00	0.00	24.16	0.00	28.84	0.00	72.92	2.13	0.00	128.05	0.00	17.64	0.00	29.80	0.00	0.00	0.00	47.43
29-Oct-23	12.60	21.33	45.10	79.04	0.00	0.00	0.00	0.00	24.13	0.00	23.38	0.00	111.21	2.18	0.00	160.90	0.00	22.36	0.00	28.93	0.00	0.00	0.00	51.29
30-Oct-23	12.60	24.01	50.40	87.01	0.00	0.00	0.00	0.00	24.10	0.28	29.01	0.00	87.04	2.22	0.00	142.64	0.00	13.66	0.00	26.75	0.00	0.00	0.00	40.41
31-Oct-23	12.60	24.19	48.66	85.45	0.00	0.00	0.00	0.00	19.08	0.00	29.10	0.00	90.64	2.11	0.00	140.93	0.00	15.89	0.00	28.41	0.00	0.00	0.00	44.30
TOTAL	378.26	1294.48	1534.32	3207.06	0.00	0.00	0.00	0.00	593.89	226.89	1099.04	0.00	2583.88	69.49	0.08	4573.27	0.00	215.80	0.03	765.68	0.00	0.00	0.02	981.53

16. भूटान , नेपाल, बांग्लादेश एवं म्यान्मार के साथ अंतरराष्ट्रीय विद्युत विनिमय

अप्रैल 2023 से मार्च 2024 April 2023 to March 2024

अंतरराष्ट्रीय विद्युत विनिमय [भारत 'से निर्यात'/'को आयात']

Transnational Exchange ('Export from'/'Import to' India)

माह MONTH	भूटान BHUTAN		नेपाल NEPAL		बांग्लादेश BANGLADESH		म्यान्मार MYANMAR	
	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)
अप्रैल 2023 APR'23	19.40	41.40	357.99	0.00	687.30	0.00	0.73	0.00
मई 2023 MAY'23	2.27	117.99	271.80	0.34	775.10	0.00	0.61	0.00
जून 2023 JUN'23	0.00	626.15	80.00	88.86	743.92	0.00	0.77	0.00
जुलाई 2023 JUL'23	0.00	1291.66	0.00	223.72	780.77	0.00	1.02	0.00
अगस्त 2023 AUG'23	0.00	1244.52	0.00	281.61	767.79	0.00	0.94	0.00
सितंबर 2023 SEP'23	0.00	924.25	0.00	323.59	-754.88	0.00	0.77	0.00
अक्टूबर 2023 OCT'23	0.00	588.64	0.00	460.97	-755.92	0.00	0.84	0.00
कुल Total	21.67	4834.61	709.78	1379.09	2244.08	0.00	5.69	0.00

* Based on daily operational data

Date	16.1 Import from neighbouring countries during October 2023													
	(All figures in MU)													
	Import from Bhutan								Import from Bangladesh		Import from Nepal			Import from Myanmar
	400 kV Tala-Binaguri I,II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurwar D/C*	400 kV Jigmeling-Alipurwar D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-Oct-23	10.49	2.75	0.74	0.00	2.30	3.48	1.07	0.25	0.00	0.00	0.74	13.44	0.00	0.00
2-Oct-23	13.43	3.69	1.19	0.00	2.60	3.93	1.18	0.29	0.00	0.00	0.29	13.18	0.00	0.00
3-Oct-23	15.06	4.23	1.48	0.00	2.64	4.42	1.18	0.25	0.00	0.00	1.04	13.37	0.00	0.00
4-Oct-23	17.17	4.94	1.80	0.00	4.25	6.45	1.32	0.46	0.00	0.00	1.16	14.67	0.00	0.00
5-Oct-23	18.05	5.24	1.43	0.00	5.94	8.97	1.23	0.63	0.00	0.00	1.16	14.49	0.00	0.00
6-Oct-23	18.17	5.31	1.57	0.00	4.51	6.80	1.04	0.35	0.00	0.00	1.28	14.15	0.00	0.00
7-Oct-23	18.08	5.25	1.55	0.00	3.84	5.79	1.12	0.35	0.00	0.00	1.31	15.08	0.00	0.00
8-Oct-23	18.06	5.24	1.48	0.00	3.58	5.40	1.07	0.28	0.00	0.00	1.22	14.18	0.00	0.00
9-Oct-23	15.86	4.55	1.41	0.00	3.33	5.03	1.09	0.22	0.00	0.00	1.18	14.10	0.00	0.00
10-Oct-23	13.86	3.91	1.34	0.00	2.81	4.25	1.14	0.20	0.00	0.00	1.11	13.91	0.00	0.00
11-Oct-23	13.03	3.65	1.40	0.00	3.29	4.97	1.18	0.27	0.00	0.00	1.38	11.49	0.00	0.00
12-Oct-23	12.33	3.47	1.52	0.00	2.74	4.13	1.18	0.26	0.00	0.00	1.44	13.94	0.00	0.00
13-Oct-23	13.02	1.83	1.64	0.00	2.52	3.81	0.94	0.29	0.00	0.00	1.37	13.90	0.00	0.00
14-Oct-23	10.85	2.99	1.08	0.00	2.21	3.36	0.89	0.29	0.00	0.00	1.49	14.23	0.00	0.00
15-Oct-23	10.49	2.83	0.63	0.00	2.25	3.41	1.00	0.17	0.00	0.00	1.40	13.85	0.00	0.00
16-Oct-23	10.12	3.64	0.00	0.00	2.08	3.16	1.00	0.14	0.00	0.00	1.42	12.74	0.00	0.00
17-Oct-23	10.12	4.90	0.00	0.00	1.48	2.25	0.91	0.09	0.00	0.00	1.16	13.03	0.00	0.00
18-Oct-23	9.36	4.52	0.00	0.00	1.39	2.13	0.87	0.05	0.00	0.00	1.10	13.27	0.00	0.00
19-Oct-23	8.91	4.16	0.00	0.00	1.27	1.96	0.85	0.00	0.00	0.00	1.10	13.95	0.00	0.00
20-Oct-23	7.67	3.29	0.00	0.00	1.27	1.95	0.85	0.03	0.00	0.00	1.37	13.89	0.00	0.00
21-Oct-23	6.50	2.46	0.00	0.00	1.20	1.84	0.87	0.04	0.00	0.00	1.52	14.73	0.00	0.00
22-Oct-23	6.54	2.51	0.00	0.00	1.20	1.84	0.66	0.00	0.00	0.00	1.57	15.39	0.00	0.00
23-Oct-23	5.90	2.22	0.00	0.00	1.05	1.62	0.61	0.00	0.00	0.00	1.63	15.54	0.00	0.00
24-Oct-23	5.95	2.24	0.00	0.00	1.01	1.55	0.45	0.00	0.00	0.00	1.63	15.75	0.00	0.00
25-Oct-23	8.33	0.14	0.00	0.00	1.08	1.67	0.24	0.00	0.00	0.00	1.65	15.28	0.00	0.00
26-Oct-23	6.32	0.93	0.00	0.00	1.00	1.54	0.20	0.00	0.00	0.00	1.65	14.52	0.00	0.00
27-Oct-23	7.05	0.00	0.00	0.00	0.84	1.32	0.20	0.00	0.00	0.00	1.63	13.68	0.00	0.00
28-Oct-23	6.88	0.00	0.00	0.00	0.45	0.79	0.69	0.08	0.00	0.00	1.61	13.69	0.00	0.00
29-Oct-23	6.10	0.00	0.00	0.00	0.43	0.74	0.68	0.08	0.00	0.00	1.57	11.66	0.00	0.00
30-Oct-23	6.68	0.00	0.00	0.00	0.39	0.70	0.61	0.00	0.00	0.00	1.51	9.92	0.00	0.00
31-Oct-23	5.72	0.00	0.00	0.00	0.18	0.40	0.68	0.00	0.00	0.00	1.59	9.01	0.00	0.00
Total	336.10	90.89	20.27	0.00	65.13	99.65	27.00	5.07	0.00	0.00	41.28	424.03	0.00	0.00
Based on SEM/Energy meter data for links where available (*Mangdechu generation receipt at APD through a bypassed arrangement at 400kV Punatsanchu station)														

Date	16.2 Export to neighbouring countries during October 2023													
	(All figures in MU)													
	Export to Bhutan								Export to Bangladesh		Export to Nepal			Export to Myanmar
	400 kV Tala-Binaguri I,II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurwar D/C*	400 kV Jigmeling-Alipurwar D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-Oct-23	0.00	0.00	0.00	0.69	0.00	0.00	0.00	0.00	21.90	3.31	0.00	0.00	0.00	0.06
2-Oct-23	0.00	0.00	0.00	0.38	0.00	0.00	0.00	0.00	21.89	3.36	0.00	0.00	0.00	0.02
3-Oct-23	0.00	0.00	0.00	0.23	0.00	0.00	0.00	0.00	21.42	3.16	0.00	0.00	0.00	0.03
4-Oct-23	0.00	0.00	0.00	0.26	0.00	0.00	0.00	0.00	21.26	2.81	0.00	0.00	0.00	0.03
5-Oct-23	0.00	0.00	0.00	0.58	0.00	0.00	0.00	0.00	20.76	3.03	0.00	0.00	0.00	0.03
6-Oct-23	0.00	0.00	0.00	0.58	0.00	0.00	0.00	0.00	20.61	3.20	0.00	0.00	0.00	0.03
7-Oct-23	0.00	0.00	0.00	0.45	0.00	0.00	0.00	0.00	20.89	3.38	0.00	0.00	0.00	0.02
8-Oct-23	0.00	0.00	0.00	0.52	0.00	0.00	0.00	0.00	20.95	2.96	0.00	0.00	0.00	0.03
9-Oct-23	0.00	0.00	0.00	0.61	0.00	0.00	0.00	0.00	21.08	3.23	0.00	0.00	0.00	0.03
10-Oct-23	0.00	0.00	0.00	0.54	0.00	0.00	0.00	0.00	21.24	3.38	0.00	0.00	0.00	0.03
11-Oct-23	0.00	0.00	0.00	0.49	0.00	0.00	0.00	0.00	21.00	3.41	0.00	0.00	0.00	0.03
12-Oct-23	0.00	0.00	0.00	0.34	0.00	0.00	0.00	0.00	21.20	3.19	0.00	0.00	0.00	0.02
13-Oct-23	0.00	0.00	0.00	0.10	0.00	0.00	0.00	0.00	21.08	3.08	0.00	0.00	0.00	0.03
14-Oct-23	0.00	0.00	0.00	0.46	0.00	0.00	0.00	0.00	21.27	3.11	0.00	0.00	0.00	0.03
15-Oct-23	0.00	0.00	0.00	0.78	0.00	0.00	0.00	0.00	21.12	3.30	0.00	0.00	0.00	0.03
16-Oct-23	0.00	0.00	0.27	2.11	0.00	0.00	0.00	0.00	21.08	3.26	0.00	0.00	0.00	0.03
17-Oct-23	0.00	0.00	0.82	2.88	0.00	0.00	0.00	0.00	21.00	2.79	0.00	0.00	0.00	0.03
18-Oct-23	0.00	0.00	0.78	2.69	0.00	0.00	0.00	0.00	21.04	2.78	0.00	0.00	0.00	0.03
19-Oct-23	0.00	0.00	0.93	2.77	0.00	0.00	0.00	0.00	21.10	2.60	0.00	0.00	0.00	0.03
20-Oct-23	0.00	0.00	0.81	1.96	0.00	0.00	0.00	0.00	19.83	2.39	0.00	0.00	0.00	0.03
21-Oct-23	0.00	0.00	0.68	1.30	0.00	0.00	0.00	0.00	21.31	2.54	0.00	0.00	0.00	0.03
22-Oct-23	0.00	0.00	0.87	1.41	0.00	0.00	0.00	0.05	21.83	2.63	0.00	0.00	0.00	0.02
23-Oct-23	0.00	0.00	0.93	1.39	0.00	0.00	0.00	0.03	21.89	2.99	0.00	0.00	0.00	0.02
24-Oct-23	0.00	0.00	1.12	1.50	0.00	0.00	0.00	0.07	21.97	2.72	0.00	0.00	0.00	0.03
25-Oct-23	0.00	0.00	1.27	1.72	0.00	0.00	0.00	0.28	19.70	3.04	0.00	0.00	0.00	0.02
26-Oct-23	0.00	0.00	1.62	1.06	0.00	0.00	0.00	0.46	21.97	2.95	0.00	0.00	0.00	0.03
27-Oct-23	0.00	0.00	1.52	1.17	0.00	0.00	0.00	0.28	21.88	2.91	0.00	0.00	0.00	0.00
28-Oct-23	0.00	0.00	1.31	1.47	0.00	0.00	0.00	0.00	21.59	3.27	0.00	0.00	0.00	0.02
29-Oct-23	0.00	0.00	1.48	1.64	0.00	0.00	0.00	0.00	21.83	3.15	0.00	0.00	0.00	0.03
30-Oct-23	0.00	0.00	1.35	1.48	0.00	0.00	0.00	0.02	21.65	3.00	0.00	0.00	0.00	0.03
31-Oct-23	0.00	0.00	1.45	1.50	0.00	0.00	0.00	0.02	21.60	2.91	0.00	0.00	0.00	0.03
Total	0.00	0.00	17.21	35.05	0.00	0.00	0.00	1.21	658.94	93.81	0.00	0.00	0.00	0.84

Based on SEM/Energy meter data for links where available (*Mangdechu generation receipt at APD through a bypassed arrangement at 400kV Punatsanchu station)

17. एसटीओए (द्विपक्षीय एवं सामूहिक) एवं डी एस एम बिलिंग का ब्योरा – अक्टूबर 2023

STOA (BILATERAL AND COLLECTIVE) & DSM BILLING DETAILS - OCTOBER 2023

द्विपक्षीय एसटीओए BILATERAL SHORT TERM OPEN ACCESS

अक्टूबर 2023 OCTOBER 2023			Apr'23- Oct'23	
नोडल क्षे.भा.प्रे.के. का नाम Name of Nodal RLDC	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Energy Approved(MU)	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Energy Approved (MU)
ऊ. क्षे. NR	1424	1744	7805	30558
प.क्षे. WR	1714	2268	7681	15012
द.क्षे. SR	1058	1499	7096	18090
पू.क्षे. ER	343	332	5024	5977
पूर्वोत्तर क्षे. NER	119	24	962	463
कुल TOTAL	4658	5866	28568	70100

एसटीओए SHORT TERM OPEN ACCESS

	सामूहिक एसटीओए Collective STOA		द्विपक्षीय एसटीओए Bilateral STOA	
माह MONTH	क्रेताओं / विक्रेताओं की स. NO. of Buyers/Sellers	अनुमोदित ऊर्जा (मि.यु.) Approved Energy (MU)	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Approved Energy (MU)
अप्रैल 2023 Apr'23	5580	6941	3322	9714
मई 2023 May'23	5798	6626	3469	8418
जून 2023 Jun'23	5783	6966	3925	10583
जुलाई 2023 Jul'23	6428	6719	3872	10780
अगस्त 2023 Aug'23	5954	6805	4841	12338
सितंबर 2023 Sep'23	6440	6506	4481	12402
अक्टूबर 2023 Oct'23	6571	7388	4658	5866
कुल TOTAL	42554	47951	28568	70100

मासिक डी एस एम बिलिंग का ब्योरा* 2021-22
MONTHLY DSM BILLING DETAILS* 2021-22

अनंतिम आँकड़े
Provisional data
subject to change
करोड़ रु. में (RS. IN CRORES)

क्षेत्र REGION →	उत्तरी क्षेत्र NORTH	पश्चिमी क्षेत्र WEST	दक्षिणी क्षेत्र SOUTH	पूर्वी क्षेत्र EAST	पूर्वोत्तर क्षेत्र NORTH EAST
सप्ताह WEEK ↓					
02.10.23 to 08.10.23	191.47	333.95	425.54	314.16	---
09.10.23 to 15.10.23	258.13	403.55	636.03	468.23	---
16.10.23 to 22.10.23	166.91	287.43	491.27	346.41	---
23.10.23 to 29.10.23	171.82	238.01	285.69	302.44	---

* Amount shown is Payable to DSM pool ^Provisional Data

18. पावर मार्केट की सूचना (स्रोत : आई ई एक्स. एच पो एक्स.आई एच.) POWER MARKET INFORMATION (Source IEX & PXIL) पावर एक्सचेंज के माध्यम से विनिमय - माह:- अक्टूबर 2023 EXCHANGES THROUGH POWER EXCHANGES - OCTOBER 2023			
क्र. स. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्सचेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU (DAM+HP DAM+RTM)
1	पंजाब Punjab	उत्तरी क्षेत्र NR	966.81
2	हरियाणा Haryana		320.60
3	राजस्थान Rajasthan		705.59
4	दिल्ली Delhi		436.00
5	उत्तर प्रदेश Uttar Pradesh		2759.34
6	उत्तराखंड Uttarakhand		953.81
7	हिमाचल प्रदेश Himachal Pradesh		127.22
8	जम्मू और कश्मीर J & K		966.82
9	केद्र भास्ति बड़ीगढ़ UT Chandigarh		24.91
10	ए डी हाइड्रो AD Hydro		0.00
11	करचम वांग्तू Karcham Wangtoo		0.00
12	श्री सीमेंट Shree Cement		0.37
13	नाथा झाकरी Nathpa Jhakri		0.00
14	लंको बुधिल Lanco Budhil		0.00
15	सिंगरौली Singrauli		0.00
16	दादरी I Dadri TPS		0.00
17	दादरी II Dadri stg-II		0.00
18	ऊंचाहार I Unchahar I TPS		0.00
19	ऊंचाहार II Unchahar II TPS		0.00
20	ऊंचाहार III Unchahar III TPS		0.00
21	रिहंद I Rihand STPS-I		0.00
22	रिहंद II Rihand STPS-II		0.00
23	रिहंद III Rihand STPS-III		0.00
24	एपीसीपीएल झुज्जर APCPL Jhajjar		0.00
25	सैज Sainj HEP		0.06
26	दादरी गैस Dadri GPP		0.00
27	औरंगा गैस NTPC Auranga		0.00
28	अंता गैस NTPC Anta		0.00
29	रामपुर एफईसी RAMPUR HEP		0.00
30	ऊंचाहार-IV UNCHAHAR-IV		0.00
31	एनटीपीसी कोलहाम NTPC KOLDAM		0.00
32	कोटेश्वर Koteswar		0.00
33	टांडा टैज-2 Tanda Stg-2		0.00
34	अदानी सौर एनर्जी टू लिमिटेड Adani Solar Energy Jodhpur Two Limited		0.00
35	सिंगौली भटवारी हेप Singoli Bhatwari HEP		0.00
36	रेलवे Railways		124.30
37	तेहरी Tehri		0.00
38	Renew Solar Energy (Jharkhand Three) Private Limited (RSETP4)		0.00
39	सोरांग एच.ई.पी. Sorang HEP, (Himachal Sorang Power Private Ltd)		0.00
40	अदानी संकर ऊर्जा जैसलमेर वन लिमिटेड (सौर) Adani Hybrid Energy Jaisalmer One Limited (Solar)		0.00
41	अदानी संकर ऊर्जा जैसलमेर टू लिमिटेड (सौर) Adani Hybrid Energy Jaisalmer Two Limited (Solar)		0.00
42	अदानी संकर ऊर्जा जैसलमेर थ्री लिमिटेड (सौर) Adani Hybrid Energy Jaisalmer Three Limited (Solar)		0.00
43	अयाना रिनूवेबल पावर वन लिमिटेड Ayana Renewable Power One Private Limited		0.00
44	Adani Hybrid Energy Jaisalmer Four Limited (सौर)अदानी संकर ऊर्जा जैसलमेर चार लिमिटेड (सौर)		0.00
45	रिणीव सोलर ऊर्जा प्राइवेट लिमिटेड Renew Solar Urja private limited		0.00
46	NEA-NR एन ई ए स्न और		0.00
47	रेनेव सूर्या प्राइवेट लिमिटेड (सौर) Renew Surya Ravi Private Limited (Solar)		0.00
48	अजुर् पावर मग्ले प्राइवेट लिमिटेड (सौर) Azure Power Maple Pvt Ltd (Solar)		0.00
49	अदानी ग्रीन हाइब्रिड सौर जैसलमेर Adani Green Hybrid Solar Jaisalmer		0.00
50	अदानी ग्रीन हाइब्रिड पवन जैसलमेरAdani Green Hybrid Wind Jaisalmer		0.00
51	अदानी ग्रीन सौर जैसलमेर Adani Green Solar Jaisalmer		0.00
52	ABC Renewable Energy (RJ-01) Private Limited एबीसी नवीकरणीय ऊर्जा (आर-01) प्राइवेट लिमिटेड		0.00
53	SBSR Power Cleantech Eleven Private Limited एस्बीएसआर पावर क्लीनटेक लिमिटेड		0.00
54	टनकपुर पावर स्टेशन Tanakpur Power Station		0.00
55	उरी पावर स्टेशन Uri I Power Station		0.00
56	उरी पावर स्टेशन Uri II Power Station		0.00
57	चमेरा पावर स्टेशन Chamera I Power Station		0.00
58	चमेरा पावर स्टेशन Chamera II Power Station		0.00
59	चमेरा पावर स्टेशन Chamera III Power Station		0.00
60	धौलीगंगा पावर स्टेशन Dhauliganga Power Station		0.00
61	दुधबहाली पावर स्टेशन Dulhaadi Power Station		0.00
62	किशनगंगा पावर स्टेशन Kishanganga Power Station		0.00
63	पार्वती पावर स्टेशन Parbati III Power Station		0.00
64	सेवा पावर स्टेशन Sewa II Power Station		0.00
65	सलाल पावर स्टेशन Salal Power Station		0.00
66	ADANI SOLAR ENERGY JAISALMER ONE PRIVATE LIMITED AHS अदानी सौर ऊर्जा जैसलमेर वन प्राइवेट लिमिटेड ए एच अल		0.00
67	पार्वती H. ई. प्रोजेक्ट Parbati II HE Project		0.00
68	एनटीपीसी अंटा जीपीएस NTPC ANT A GPS RLNG		0.00
69	एनटीपीसी औरंगा जीपीएस NTPC AURANGA GPS RLNG		0.00
70	एनटीपीसी दादरी जीपीएस NTPC DADRI GPS RLNG		0.00
71	अदानी संकर ऊर्जा जैसलमेर चार लिमिटेड ADANI HYBRID ENERGY JAISALMER FOUR LIMITED AHW		0.00
72	NTPC ANT A GPS spot RJ एनटीपीसी आन्टा जीपीएस स्पॉट आरएफ		0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एस. एवं पी.एस.आई.एल.) POWER MARKET INFORMATION (Source IEX & P&L) पावर एक्सचेंज के माध्यम से विनिमय - माह:- अक्टूबर 2023 EXCHANGES THROUGH POWER EXCHANGES - OCTOBER 2023			
क्र. स. 5. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्सचेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU (DAM+HP DAM+RTM)
73	मध्य प्रदेश Madhya Pradesh	पश्चिमी क्षेत्र WR	594.23
74	महाराष्ट्र Maharashtra		4690.35
75	गुजरात Gujarat		2333.87
76	छत्तीसगढ़ Chhattisgarh		47.75
77	गोवा डब्ल्यू और Goa WR		42.86
78	जिंदल पावर JINDAL POWER		1.77
79	लान्को Lanco		0.00
80	ए सी बी आई एल ACBIL		1.42
81	जिंदल स्टील JINDAL STEEL		0.00
82	बालको 2 BALCO 2		0.00
83	जीएसआर वरीरा GMR Warora		0.00
84	एस्सार पावर एम ली Essar Power MP Ltd		2.33
85	के एस के महानदी KSK Mahanadi		0.00
86	जिंदल पावर लिमिटेड Jindal Power Ltd. Stg-II		108.35
87	रायगढ़ एनर्जी लिमिटेड Raigarh Energy Ltd.		3.24
88	डी बी पावर DB Power		0.00
89	धारीवाल Dhariwal		0.00
90	जेपी निगरी JAYPEE NIGRIE		0.00
91	डीजेन मेगा पावर DGEN Mega power		0.00
92	एम बी पावर MB Power		0.00
93	अदानी पावर स्टेज 3 Adani Power STG3		0.00
94	टोरेंट पावर Torrent Power		0.00
95	मारुति क्लीन कोल पावर Maruti Clean Coal Power		4.79
96	झाबुआ पावर Jhabua Power		6.38
97	विंध्याचल स्टेज-1 Vindhyachal stg-1		0.00
98	विंध्याचल स्टेज-2 Vindhyachal stg-2		0.00
99	विंध्याचल स्टेज-3 Vindhyachal stg-3		0.00
100	विंध्याचल स्टेज-4 Vindhyachal stg-4		0.00
101	विंध्याचल स्टेज-5 Vindhyachal stg-5		0.00
102	मौदा स्टेज-1 Mouda Stg-1		0.00
103	सिपत स्टेज-1 Sipat Stg-1		0.00
104	सिपत स्टेज-2 Sipat Stg-2		0.00
105	सासन Sasan UMPP		0.00
106	भिलाई एनर्जी लिमिटेड NSPCL Bhilai		0.00
107	कोरबा स्टेज-3 Korba Stg 3		0.00
108	टीआरएन एनर्जी TRN Energy		0.00
109	गांधार Gandhar		0.00
110	कोरबा Korba		0.00
111	आर के एम पावर RKM Power		0.00
112	कावस Kaws		2.17
113	मौदा स्टेज-2 Mouda Stg-2		0.00
114	एस के एस पावर SKS Power		0.00
115	एन टी पि सी शोलापुर NTPC Sholapur		0.00
116	एन टी पि सी गढ़वारा NTPC Gadarwara		0.00
117	एन टी पि सी लारा NTPC Lara		0.00
118	रायपुर एनर्जी Raipur Energen		0.00
119	आर्सेल मितल ArcelorMittal Nippon steel (ESIL)		798.78
120	खरगोन Khargone STPP		0.00
121	कोस्टल गुजरात पावर लिमिटेड Coastal Gujarat Power Limited		0.00
122	कंटीन्यूम पावर ट्रेडिंग Continuum Power Trading (TN) Private Limited		0.00
123	ऑस्ट्रो एनर्जी प्राइवेट लिमिटेड Ostro Energy Private Limited (OEPL)		0.00
124	दमन दीपु/दादरा और नगर हवेली Daman & Diu/Dadar and Nagar Haveli		214.44
125	अदानी विंड एनर्जी Adani Wind Energy Kutchi Five Limited		0.00
126	आर जी पि पि एल RGPPL		4.15
127	Kakrapar Atomic Power Station काकरपर अटॉमिक पावर स्टेशन		0.00
128	BALCO बालको		120.55
129	अदानी विंड एनर्जी कच फोर लिमिटेड नखट्राना ADANI WIND ENERGY KUTCHI FOUR Ltd. Nakhtrana		0.00
130	एनटीपीसी झनोर गांधार जीपीएल NTPC Jhanor Gandhar GPS RLNG		3.18
131	एनटीपीसी कावस गढ़ NTPC Kaws GPS RLNG		0.00
132	रात्रागिरी गैस और पावर प्राइवेट लिमिटेड Ratnagiri Gas and Power Private Limited-LTRLNG		0.00
133	विंड फाइव एनर्जी लिमिटेड WIND FIVE RENEERGY LIMITED		0.00
134	एनटीपीसी झनोर गांधार जीपीएल कॉम गैस NTPC Jhanor Gandhar GPS_COMGAS		0.00
135	धारीवाल एस टी यू DHARIWAL STU OTH		0.00
136	धारीवाल आइ एस टी एस Dhariwal ITS		0.00
137	इनोक्स ग्रीन एनर्जी सर्विसेस लिमिटेड INOX GREEN ENERGY SERVICES LIMITED		0.00
138	अदानी पावर लिमिटेड रायपुर टीपीसी Adani Power Limited Raipur TPP		0.00
139	टाटा पावर कंपनी लिमिटेड (MTPS) The Tata Power Co Ltd (MTPS)		0.00
140	NTPC Ltd Jhanor Gandhar Gas Power Project ComRLNG		0.00
141	NTPC KAWAS GPS COMGAS		0.00
142	मसाया सोलर एनर्जी प्राइवेट लिमिटेड Masaya Solar Energy Private Limited		0.00

18. पावर मार्केट की सूचना (स्रोत : आई ई एक्स. एन पी एक्स.आई एन.) POWER MARKET INFORMATION (Source IEX & PXL) पावर एक्सचेंज के माध्यम से विनिमय - माह:- अक्टूबर 2023 EXCHANGES THROUGH POWER EXCHANGES - OCTOBER 2023			
क्र. स. 5. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्सचेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU (DAM+HP DAM+RTM)
143	आंध्र प्रदेश Andhra Pradesh	पश्चिमी क्षेत्र SR	2404.58
144	कर्नाटक Karnataka		1451.37
145	केरल Kerala		794.20
146	तमिलनाडु Tamilnadu		1065.67
147	पण्डिचेरी Pondicherry		0.00
148	गोवा एस और Goa SR		71.40
149	तेलंगाना TELANGANA		3985.26
150	कोस्टल एनर्जेन Costal Energen		0.00
151	आई एन और एन एन I&F5		0.00
152	सिंहगिरी स्टेज -2 Simhadri Stg-2		0.00
153	एनएलसी इंडिया स्टेशन 1 विस्तार NLC India Station I Expansion		0.00
154	एन एन सी स्टेज-1 NLC TPS-II Stg-1		0.00
155	एन एन सी स्टेज-2 NLC TPS-II Stg-2		0.00
156	रामगुंडम स्टेज-1 Ramagundam Stg-1		0.00
157	तलचर स्टेज -2 Talcher Stg-2		0.00
158	रामगुंडम स्टेज-3 Ramagundam Stg-3		0.00
159	सेम्कोर्प गायत्री Sembcorp Gayatri		0.00
160	वल्लूर Vallur		0.00
161	कुदगी NTPC Kudgi		0.00
162	सिंहगिरी स्टेज -1 Simhadri Stg-1		0.00
163	एन एन सी टी पी एन -11 एक्सपन NLC TPS-II Expn		0.00
164	एनटीपीएल NTPL		0.00
165	नयवेली न्यू थर्मल पावर प्रोजेक्ट Neyveli New Thermal Power Project		0.00
166	रामगुंडम फ्लोटिंग सोलर पी वी स्टेशन Ramagundam Floating Solar PV Station		0.00
167	सिंहगिरी फ्लोटिंग सोलर Simhadri Floating solar		0.00
168	सिंहगिरी एफएसपी 15 एमबी प्रोजेक्ट Simhadri FSP 15 MW Project		0.00
169	सेम्कोर्प एनर्जी इंडिया लिमिटेड Sembcorp energy india limited		0.00
170	जे एस डब्ल्यू रिनोव एनर्जी टू लिमिटेड JSW RENEW ENERGY TWO LIMITED		0.00
171	ओस्ट्रो कन्नडा पावर प्राइवेट लिमिटेड Ostro Kannada Power Private Limited		0.00
172	सिमहापुरी एनर्जी लिमिटेड Simhapuri Energy Limited		9.38
173	परम्पुल्लु सोलर एनर्जी प्राइवेट लिमिटेड PARAMPULUVA SOLAR ENERGY PRIVATE LIMITED		0.00
174	Pondicherry U1 पुडुचेरी		0.41
175	पश्चिम बंगाल West Bengal	पूर्वी क्षेत्र ER	1752.34
176	ओडिशा Odisha		488.25
177	बिहार Bihar		452.38
178	झारखंड Jharkhand		70.62
179	सिक्किम Sikkim		1.84
180	दामोदर घाटी परियोजना DVC		463.49
181	मैथन पावर लिमिटेड Maithon P. Ltd		0.00
182	आधुनिक पा. लिमिटेड Adhunik P.Ltd		0.00
183	चुआचन Chuzachen HEP		0.00
184	जीएमआर कमलंगा GMR Kamalanga		0.00
185	बिदल आई पी टी एल BPTL		0.00
186	जोरथंग Jorethang		0.00
187	फरक्का-III Farakka-III		0.00
188	बाई-II Barh Stage-II		0.00
189	कहलगाँव-II Kahalgaon Stage-II		0.00
190	फरक्का Farakka		0.00
191	कहलगाँव Kahalgaon		0.00
192	तलचर Talcher		0.00
193	टीस्ता-III Teesta-III		0.00
194	दिखु Dikchu HEP		0.00
195	ताशिदिंग Tashiding HEP		0.00
196	केबीपूरनरुल KBUNL		0.00
197	दरिपल्ली Daripalli		0.00
198	नबीनगर NPGC Nabhinagar		0.00
199	नेपाल विद्युत प्राधिकरण Nepal Electricity Authority		0.00
200	Barh STPS Stage-I बाई एलटीएस स्टेज-1		0.00
201	NTPC North Karanpura STPS नॉर्थ करनपुरा		0.00
202	Druk Green Power Corporation Limited-Bhutan ड्रुक ग्रीन पावर कार्पोरेशन लिमिटेड. भूटान		0.00
203	NTPC BARH1 Unit 2 एनटीपीसी बाई 1		0.00
204	सिक्किम ऊर्जा लिमिटेड Sikkim Urja Limited		12.33

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एस.एच.पी.एस.आई.एच.) POWER MARKET INFORMATION (Source IEX & PXL) पावर एक्स्चेंज के माध्यम से विनिमय - माह:- अक्टूबर 2023 EXCHANGES THROUGH POWER EXCHANGES - OCTOBER 2023			
क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU
			(DAM+HP DAM+RTM)
205	अरुणाचल प्रदेश Arunachal Pradesh	पूर्वोत्तर क्षेत्र NER	4.72
206	असम Assam		81.68
207	मणिपुर Manipur		4.69
208	मेघालय Meghalaya		29.87
209	मिज़ोरम Mizoram		0.00
210	नागालैंड Nagaland		0.00
211	त्रिपुरा Tripura		11.23
212	आगरतला जीटीपीसी Agartala GTPP_AGO		0.00
213	असम जीबीपीसी Assam GBPP_KTO		0.00
214	पलताना Palatana		0.00
215	Doyang HEP डोयंग हेप		0.00
216	बोंगाईगाँव Bongaigaon TPP		0.00
217	कामेंग Kameng HEP		0.00
218	रंगानदी हाइड्रो पावर स्टेशन Rangasadi Hydro Power Station		0.00
219	लौकटक पावर स्टेशन LOKTAK POWER STATION	0.00	
			29581

19. INFORMATION ABOUT RENEWABLE ENERGY
CERTIFICATE MECHANISM
MONTH : OCTOBER 2023

RE Source & Unit wise break up (01.10.2023-31.10.2023)

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	9	3	1	1
2	Urban or Municipal Waste	0	0	0	0
3	Solar Thermal	0	0	0	0
4	Solar PV	35	9	1	1
5	Small Hydro	0	0	0	0
6	Others	0	0	0	0
7	Geothermal	0	0	0	0
8	Biomass	0	0	0	0
9	Bio-fuel cogeneration	0	0	0	0
	Total	44	12	2	2

RECs Issued (01.10.2023-31.10.2023)

Sr.No.	Non Solar	Solar	Total
1	599791	83409	683200

Redemption of REC (01.10.2023-31.10.2023)

Sr.No.	Non Solar	Solar	Total
1	187092	148821	335913

19. INFORMATION ABOUT RENEWABLE ENERGY
CERTIFICATE MECHANISM
MONTH : OCTOBER 2023

RE Source & Unit wise break up (Apr'23-Oct'23)

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	348	14	438	14
2	Urban or Municipal Waste	0	0	0	0
3	Solar Thermal	0	0	0	0
4	Solar PV	166	50	66	4
5	Small Hydro	42	7	42	7
6	Others	0	0	0	0
7	Geothermal	0	0	0	0
8	Biomass	5	1	5	1
9	Bio-fuel cogeneration	8	2	23	5
	Total	569	74	574	31

RECs Issued (Apr'23-Oct'23)

Sr.No.	Non Solar	Solar	Total
1	2645260	712901	3358161

Redemption of REC (Apr'23-Oct'23)

Sr.No.	Non Solar	Solar	Total
1	3209787	582199	3791986

19. INFORMATION ABOUT RENEWABLE ENERGY
CERTIFICATE MECHANISM
MONTH : OCTOBER 2023

RE Source & Unit wise break up Since Inception to Oct'23

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	3062	519	2894	517
2	Urban or Municipal Waste	0	0	0	0
3	Solar Thermal	0	0	0	0
4	Solar PV	1435	542	1251	469
5	Small Hydro	686	40	698	42
6	Others	4	2	3	1
7	Geothermal	0	0	0	0
8	Biomass	402	37	378	35
9	Bio-fuel cogeneration	817	90	383	55
	Total	6406	1230	5607	1119

RECs Issued since Inception to Oct'23

Sr.No.	Non Solar	Solar	Total
1	90525400	13123639	103649039

Redemption of REC since Inception to Oct'23

Sr.No.	Non Solar	Solar	Total
1	70737972	12210587	82948559

REC Closing balance as on 31.10.2023

Sr.No.	Non Solar	Solar	Total
1	19787428	913052	20700480

20.Details of Grid Events during the Month of October 2023

Northern Region



Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI for GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-1	Jammu & Kashmir	03-Oct-2023 11:39	03-Oct-2023 14:20	02:41	0	90	0.000	0.146	54859	61505	i) 220/132kV Udhampur(JK) has double main bus scheme at 220kV level. During antecedent condition, active power flow in 220 KV Kishenpur(PG)-Udhampur(PDD) (PG) Ckt-1 & 2 and 220 KV Sarma(PG)-Udhampur(PDD) (PDD) Ckt were 91MW, 91MW and 97MW respectively. ii) As reported, at 11:39 hrs, 220 KV Kishenpur(PG)-Udhampur(PDD) (PG) Ckt-1 tripped on Y-B phase to phase fault with fault current of Iy=Ib=6.886kA and fault distance of 19.043km from Kishenpur(PG) end. iii) During the same time, 220 KV Kishenpur(PG)-Udhampur(PDD) (PDD) Ckt-2 also tripped on Y-B phase to phase fault with fault current of Iy=Ib=4.159kA and fault distance of 22.030km from Kishenpur(PG) end. Forest fire was observed at loc. no. 5-6. iv) Due to tripping of, 220 KV Kishenpur(PG)-Udhampur(PDD) (PG) Ckt-1 & 2, 220 KV Sarma(PG)-Udhampur(PDD) (PDD) Ckt got overloaded and tripped. v) As per PMU at Kishenpur(PG), Y-B phase to phase fault is observed with delayed fault clearing time of 120ms. vi) As per SCADA, change in demand of approx. 90MW is observed in J&K control area.	1) 220 KV Kishenpur(PG)-Udhampur(PDD) (PG) Ckt-1 2) 220 KV Kishenpur(PG)-Udhampur(PDD) (PG) Ckt-2 3) 220 KV Sarma(PG)-Udhampur(PDD) (PDD) Ckt
2	GI-2	Himachal Pradesh	04-Oct-2023 19:30	05-Oct-2023 18:25	22:55	165	0	0.324	0.000	50874	62750	i) As reported, at 09:28hrs, sparking was observed on the B-phase of 220 KV Bus Isolator of 220KV/ Hissar _JA(Har)-Hissar(PG) ckt-1 at Hissar _JA(Har) end. ii) During the same time, 400/220 KV 315 MVA ICT 1 at Dehar(BB) tripped due to restricted earth fault (REF) protection operation. 165MW Unit-1 at Dehar(BB) also tripped at this time. (Exact reason yet to be shared) iii) As per PMU at Dehar(BB), R-B phase to phase fault is observed with fault clearing time of 80ms. iv) As per SCADA, change in generation of approx. 165MW is observed at Dehar(BBMB).	1) 400/220 KV 315 MVA ICT 1 at Dehar(BB) 2) 165MW Unit-1 at Dehar(BB)
3	GD-1	Haryana	05-Oct-2023 09:28	05-Oct-2023 10:00	00:32	0	300	0.000	0.520	53017	57708	i) During antecedent condition, 220KV Hissar _JA(Har) Mainbus Ckt 1 & 2 and 220/132KV 100MVA ICT 1 at Hissar _JA(Har) were already in open condition. ii) As reported, at 09:28hrs, sparking was observed on the B-phase of 220KV/ Hissar _JA(Har)-Hissar(PG) ckt-1 at Hissar _JA(Har) end. iii) As per DR at Hissar _JA(Har), Bus Bar differential protection operated at 220KV level of Hissar _JA(Har) which led to tripping of all the elements connected to both the buses. (Exact reason of tripping of both the buses yet to be shared) iv) Due to tripping of all the elements connected to both the buses, both 220KV Bus-1 & 2 at Hissar _JA(Har) and eventually the complete 220KV Hissar _JA(Har) S/s became dead. v) As per PMU at Hissar(PG), B-N phase to earth fault with fault clearing time of 80ms is observed. vi) As per SCADA, change in demand of approx. 90MW is observed in Haryana control area. But as reported by SLDC-Haryana, change in demand of approx. 300MW is observed in Haryana control area.	1) 220KV Hissar _JA(Har)-Narwana ckt 2) 220KV Hissar(BB)-Hissar _JA(Har) ckt-1 3) 220KV Hissar(BB)-Hissar _JA(Har) ckt-2 4) 220KV Hissar _JA(Har)-Hissar(PG) ckt-1 5) 220KV Hissar _JA(Har)-Hissar(PG) ckt-2 7) 220/132KV 100MVA ICT-1 at Hissar _JA(Har)
4	GD-1	Punjab	07-Oct-2023 08:37	07-Oct-2023 10:10	01:33	0	280	0.000	0.501	51438	55849	i) During antecedent condition, 220 KV Ludhiana(PG)-Lalton Kalan(PG) (PSTCL) Ckt-2, 220 KV Humbran-Lalton Kalan(PG) Ckt and 220 KV Dhandhar Kalan-Lalton Kalan(PG) Ckt were connected to 220KV Bus-1 at Lalton Kalan(PG) and 220 KV Ludhiana(PG)-Lalton Kalan(PG) (PSTCL) Ckt-1 and 220 KV Ferozepur Road-Lalton Kalan(PG) Ckt were connected to 220KV Bus-2 at Lalton Kalan(PG). 220 KV Jagraon-Lalton Kalan(PG) Ckt was already in off condition due to overload. ii) As reported, at 08:37hrs, snapped conductor of 11kV Midland feeder comes in contact with 220KV Ferozepur Road R-Phase CVT causing damaging of bus post insulator trip and tripping of 220KV Bus-2 at Lalton Kalan(PG). iii) Further at 09:22hrs, during isolation of Bus-2 and further switchover of load to Bus-1, flashover occurred leading to tripping of 220 KV Ludhiana(PG)-Lalton Kalan(PG) (PSTCL) Ckt-2, 220 KV Humbran-Lalton Kalan(PG) Ckt and 220 KV Dhandhar Kalan-Lalton Kalan(PG) Ckt from Lalton Kalan(PG) end. iv) Due to this tripping, complete blackout occurred at 220/66kV Lalton Kalan(PG) S/s. v) As per PMU at Ludhiana(PG), B-N phase to earth fault with delayed clearance of 360ms is observed. vi) As per SCADA, change in demand of approx. 155MW is observed in Punjab control area. But as reported by SLDC Punjab, change in demand of approx. 280MW is observed in Punjab control area.	1) 220 KV Ludhiana(PG)-Lalton Kalan(PG) (PSTCL) Ckt-1 2) 220 KV Ferozepur Road-Lalton Kalan(PG) Ckt 3) 220 KV Ludhiana(PG)-Lalton Kalan(PG) (PSTCL) Ckt-2 4) 220 KV Humbran-Lalton Kalan(PG) Ckt 5) 220 KV Dhandhar Kalan-Lalton Kalan(PG) Ckt
5	GI-2	Uttar Pradesh	09-Oct-2023 20:16	09-Oct-2023 21:50	01:34	0	0	0.000	0.000	51481	60698	i) As reported, at 20:16hrs, 400KV B-Ph CT of main bay 410 of 400/132 KV 200 MVA ICT 3 at Nehtaur(UF) busted and caught fire and 400/132 KV 200 MVA ICT 3 at Nehtaur(UF) tripped on differential protection operation with B-phase fault current of 4.4kA. ii) At the same time, 400/132 KV 200 MVA ICT 2 at Nehtaur(UF) also tripped on differential protection operation with R-phase fault current of 7.11kA (Exact reason yet to be shared) iii) Due to CT burst, the oil of CT got spread out on the cable trench and certain cables also got burnt and badly damaged. So in view of safety, 400/132 KV 200 MVA ICT 1 at Nehtaur(UF) was manually tripped at 20:30hrs due to fire attack on main cable trench. iv) After tripping of all three 400/132KV ICTs, all 7, 132kV lines tripped due to loss of supply. v) After fire quenching of CT & cables, ICT-1 was normalized and charged successfully at 21:50 hrs on 09/10/2023. vi) As per PMU at Roorkee(PG), B-N phase to earth fault with delayed fault clearing time of 640ms followed by R-N phase to earth fault with fault clearance time of 80ms are observed. vii) As per SCADA, no change in demand is observed in UP control area. As reported by SLDC-UP, before tripping average load on ICTs was around 240MW, after tripping it was shifted to Nehtaur 220KV.	1) 400/132 KV 200 MVA ICT 3 at Nehtaur(UF) 2) 400/132 KV 200 MVA ICT 2 at Nehtaur(UF) 3) 400/132 KV 200 MVA ICT 1 at Nehtaur(UF) 4) 132KV Nehtaur- Bijpur Ckt 5) 132KV Nehtaur- Chandpur Ckt 6) 132KV Nehtaur- Morra Ckt 7) 132KV Nehtaur- Kintpur Ckt 8) 132KV Nehtaur- Nagina Ckt-1 9) 132KV Nehtaur- Nagina Ckt-2 10) 132KV Nehtaur- Najibabad Ckt
6	GI-1	Himachal Pradesh	10-Oct-2023 18:46	10-Oct-2023 23:11	04:25	120	0	0.234	0.000	51254	60340	i) During antecedent condition, 66MW unit-1, 2, 3, 5 & 6 were running and generating approx. 307 MW in total. Unit-1, 3 & 5, 220/66kV 40MVA Transformer and 220KV feeders to Betrawal, Jalandhar ckt-1 and Dasuya ckt-1 were connected at 220KV Bus-1 and Unit-2 & 6 & 220KV feeders to Jessore, Jalandhar ckt-2 and Dasuya ckt-2 were connected at 220KV Bus-2. ii) As reported, at 18:46 hrs, bus bar protection operated at 220KV Bus-2 at Pong(BBMB) and all the elements connected to Bus-2 got tripped and Bus-2 became dead. The jumper between 220KV Bus-2 and connecting isolator of B-ph of 220 KV Pong(BB) Dasuya(PG) (BBMB) Ckt-2 was found broken. iii) As per SCADA SOE, 220/66kV 40MVA ICT-1 at Pong(BB) also tripped during the same time. (Exact reason yet to be shared) iv) As per PMU at Pong(BBMB), B-N phase to earth fault is observed with fault clearing time of 80 ms. v) As per SCADA, total generation loss of approx. 120MW is observed at Pong HEP(BBMB).	1) 220KV Bus 2 at Pong(BB) 2) 220 KV Pong(BB)-Dasuya(PG) (BBMB) Ckt-2 3) 220 KV Jalandhar(PG)-Pong (BB) Ckt-1 4) 220 KV Jessore(HP)-Pong(BB) (PG) Ckt 5) 66 MW Pong HPS - UNIT 2 6) 66 MW Pong HPS - UNIT 6 7) 220/66kV 40MVA ICT-1 at Pong(BB)
7	GI-2	Rajasthan	10-Oct-2023 10:21	10-Oct-2023 11:32	01:11	110	70	0.251	0.116	43865	60246	i) 400/220KV Akaal(RS) has one and half breaker scheme at 400KV level and double main transfer bus scheme at 220KV level. ii) As reported, at 10:21hrs, 220 KV Akaal(RS)-Jaisalmer(RS) Ckt tripped on phase to earth fault (N fault as per PMU at Bhadla(PG)). iii) At the same time, 400/220 KV 500 MVA ICT 1 & 2 at Akaal(RS) also tripped. (Exact reason yet to be shared, but it is suspected that there is delay in CB opening due to which ICTs also got tripped. Also O/C protection settings of ICTs need to be shared.) iv) As per SCADA SOE, 220KV Akaal(RS)-Barme(RS) Ckt also tripped during the same time. (Exact reason yet to be shared) v) As per PMU at Bhadla(PG), Y-N phase to earth fault is observed with delayed fault clearing time of 220ms. vi) As per SCADA, change in demand of approx. 70MW is observed in Rajasthan control area. vii) As per SCADA, change in Rajasthan wind generation of approx. 110MW is observed.	1) 220 KV Akaal(RS)-Jaisalmer(RS) Ckt 2) 400/220 KV 500 MVA ICT 1 at Akaal(RS) 3) 400/220 KV 500 MVA ICT 2 at Akaal(RS)
8	GD-1	Uttarakhand	12-Oct-2023 15:36	12-Oct-2023 16:28	00:52	90	0	0.175	0.000	51528	61412	i) 765/400KV Koteswar(PG) has one and half breaker scheme at 765kV level and double main bus scheme at 400KV level. During antecedent condition, only 100MW Unit-1 at Koteswar HEP was in running condition and was generating approx. 90MW and active power loading on 765kV Koteswar(PG)-Meerut(PG) Ckt-1 & 2 was approx. 45MW each. ii) As reported, at 15:36hrs, "Protection operated in FSC" signal came at Meerut(PG) and which tripped group relays and sent DT to Koteswar(PG). 765kV Koteswar(PG)-Meerut(PG) Ckt-1 & 2 tripped due to DT received at Koteswar(PG) end. iii) During the same time, 100MW Unit-1 at Koteswar(TH) tripped on over-excitation due to loss of evacuation path. iv) Cbs from both the ends of 400KV Koteswar(PG)-Tehri(TH) (PG) Ckt-1 & 2 and 400KV Koteswar(PG)-Koteswar (TH) (PG) Ckt-1 & 2 opened due to safety purpose. v) Due to this tripping, complete blackout occurred at 765/400KV Koteswar(PG) & 400KV Koteswar(TH). vi) Although no generation was there at Tehri(TH) during the event time, but Tehri(TH) generation was affected from 16:00hrs to 17:14hrs. vii) As per PMU Meerut(PG), no fault is observed in the system. viii) As per SCADA, change in generation of approx. 90MW is observed at Koteswar(TH).	1) 765kV Koteswar(PG)-Meerut(PG) Ckt-1 2) 765kV Koteswar(PG)-Meerut(PG) Ckt-2 3) 400KV Koteswar(PG)-Tehri(TH) (PG) Ckt-1 4) 400KV Koteswar(PG)-Tehri(TH) (PG) Ckt-2 5) 400KV Koteswar(PG)-Koteswar (TH) (PG) Ckt-1 6) 400KV Koteswar(PG)-Koteswar (TH) (PG) Ckt-2 7) 100 MW Unit-1 at Koteswar(TH)

20.Details of Grid Events during the Month of October 2023



Northern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load v.t.1 Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(Gl 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
9	GD-1	Jammu and Kashmir	14-Oct-2023 04:23	14-Oct-2023 06:32	02:09	72	0	0.180	0.000	39982	52071	i) During antecedent condition, 60 MW Unit-2 & 3 at Uri-2(NH) were running and generating approx. 36MW each and total MW generation of 72MW was evacuating through 400 KV Uri-2(NH) Uri-2(NH) (PG) Ckt and 400 KV Uri-2(NH) Wagaura(PG) (PG) Ckt. ii) As reported, at 04:23hrs, 400 KV Uri-2(NH)-Wagaura(PG) Ckt tripped on B-N phase to ground fault with fault current of approx. 1.89kA and fault distance of 11.87km from Wagaura(PG) and due to heavy wind and storm in the area. iii) As per DR, 400 KV Uri-2(NH) Uri-2(NH) (PG) Ckt also tripped on B-N phase to ground fault at the same time with delayed fault clearance time of approx. 690ms and fault current of approx. 2.53kA from Uri-2(NH) end. Over-current protection operated at both Uri-2(NH) and Uri-2(NH) end as per DR. iv) Due to tripping of both the lines, 60 MW Unit-2 & 3 at Uri-2(NH) tripped on over-excitation due to loss of evacuation path. v) On this, complete blackout occurred at 400KV Uri-2(NH). vi) As per PMU at Wagaura(PG), two consecutive B-N phase to ground fault is observed in the system with delayed fault clearance time of 720ms and 440ms respectively. vii) As per SCADA, generation loss of approx. 72MW is observed at Uri-2(NH).	1) 400 KV Uri-2(NH)-Uri-2(NH) (PG) Ckt 2) 400 KV Uri-2(NH)-Wagaura(PG) (PG) Ckt 3) 60 MW Unit-2 at Uri-2(NH) 4) 60 MW Unit-3 at Uri-2(NH)
10	GI-2	Rajasthan	16-Oct-2023 02:26	16-Oct-2023 06:42	04:16	0	0	0.000	0.000	39913	49814	i) 765/400/220kV Bhadla(PG) has one and half breaker scheme at 765 & 400kV side and double main bus scheme at 220kV level. 220kV level at Bhadla(PG) S/s is hybrid (Partly Air-Splitter (GIS) in nature). ii) As reported, at 02:26 hrs, Bus Bar Protection Operated at Bhadla (PG) Substation due to suspected malfunctioning of Gas Density relay. 220kV Bus-1,2&3 along with elements connected to them tripped during the event. iii) As per PMU at Bhadla(PG), no fault in system is observed. iv) POWERGRID has been communicated to share the exact details of event along with remedial action taken.	1) 220 KV Bhadla(PG) - Bus 1 2) 220 KV Bhadla(PG) - Bus 2 3) 220 KV Bhadla(PG) - Bus 3 4) 400/220 KV 500 MVA ICT 1 at Bhadla(PG) 5) 400/220 KV 500 MVA ICT 2 at Bhadla(PG) 6) 400/220 KV 500 MVA ICT 3 at Bhadla(PG) 7) 400/220 KV 500 MVA ICT 4 at Bhadla(PG) 8) 400/220 KV 500 MVA ICT 5 at Bhadla(PG) 9) 220 KV Bhadla(PG) Saurya Urja Solar Ckt-1 10) 220 KV Bhadla(PG) Saurya Urja Solar Ckt-2 11) 220 KV Bhadla(PG)-AREPRL Ckt-1 12) 220 KV Bhadla(PG)-AREPRL Ckt-2 13) 220 KV Bhadla(PG)-CSPJP Ckt 14) 220 KV Bhadla(PG)-Mahoba Solar Ckt 15) 220 KV Bhadla(PG)-ACME Ckt
11	GD-1	Rajasthan	16-Oct-2023 12:32	16-Oct-2023 20:58	08:26	700	0	1.376	0.000	50859	52036	i) Total generation of 220kV TPGL & 220kV TPSE stations evacuates through 220 KV TATA Noorsar SL_BKN PG (TPGL)-Bikaner(PG) (TPGL) Ckt. During antecedent condition, total generation evacuating through TPGL line was 325MW (220MW TPGL and 105MW TPSE). ii) As reported, at 12:32hrs, 220 KV TATA Noorsar SL_BKN PG (TPGL)-Bikaner(PG) (TPGL) Ckt tripped on Y-B phase to phase fault. iii) As per PMU at Bikaner(PG), Y-B phase to phase fault which cleared within 80msec is observed. iv) Due to tripping of 220kV TPGL line, total solar generation (235MW) evacuating through the line lost. v) As per PMU plots of voltage at RE stations of 220kV lines connected at different pooling stations, it is observed that during the fault phase voltage dropped to ~0.85pu at Bikaner(PG), 0.91pu at Bhadla2(PG), 0.93pu at Bhadla(PG), 0.91pu at Fatehgarh2(PG) and 0.93pu at AFSPS. vi) Total drop in RE generation for the event was approx. 700MW (as per SCADA) including 325MW RE generation at TPGL & TPSE. Further, within 03 minutes of the occurrence of event, approx. 350MW RE generation recovered. vii) MVAR profile of STATCOM 1&2 connected at Bhadla2(PG) changed from ~65MVar injection each to 170MVar & 230MVar injection respectively.	1) 220 KV TATA Noorsar SL_BKN PG (TPGL)-Bikaner(PG) (TPGL) Ckt
12	GD-1	Rajasthan	16-Oct-2023 14:54	16-Oct-2023 16:43	01:49	144	0	0.338	0.000	42560	48686	i) Generation of 220kV AHEJAL PSS IV RE stations evacuates through 220 KV Adani RenewPark_SL_FGARH_FBTL (AREPRL)-AHEJAL PSS 4 HB_FGARH_FBTL (AHEJAL) (AREPRL) Ckt. During antecedent condition, AHEJAL PSS IV RE station was generating approx. 144MW. ii) As reported, at 14:54hrs, 220 KV Adani RenewPark_SL_FGARH_FBTL (AREPRL)-AHEJAL PSS 4 HB_FGARH_FBTL (AHEJAL) (AREPRL) Ckt tripped on R-N phase to earth fault. iii) As per PMU at SOE data, R-N phase to earth fault with unsuccessful A/R operation at AFSPS end is observed. Line instantaneously tripped from AHEJAL PSS IV end. iv) Due to tripping of 220kV AHEJAL PSS IV line, RE [wind] generation (144MW) of the RE station lost due to loss of evacuation path. v) As per PMU plots of voltage at RE stations of 220kV lines connected at different pooling stations, voltage was above 0.9pu at RE station end. It was in the range of 0.95-0.98pu. No drop in solar generation connected at ISTS pooling station in Rajasthan RE complex is observed.	1) 220 KV Adani RenewPark_SL_FGARH_FBTL (AREPRL)-AHEJAL PSS 4 HB_FGARH_FBTL (AHEJAL) (AREPRL) Ckt
13	GI-2	Rajasthan	21-Oct-2023 16:50	16-Oct-2023 18:45	01:55	150	0	0.347	0.000	43166	49311	i) 765/400/220kV Bhadla(PG) has double main single breaker bus scheme at 220kV level, there are total six (06) buses. Parallel buses are separated bus coupler and adjacent busses are separated by bus sectionizers. During antecedent condition, all bus coupler and sectionialiser were in closed condition. ii) As reported, at 16:50 hrs, R-N fault occurred on 220kV Bhadla(PG) ESUCRL(SBEPFL) ckt. On this fault, line protection operated however, CB didn't open at Bhadla end. Further, as CB of ESUCRL(SBEPFL) ckt didn't open at Bhadla(PG) end, LBH of ESUCRL bay operated which resulted into tripping of all the elements connected to the 220kV Bus-4 i.e., 220kV circuits to TPREL, MRPL & ESUCRL RE station and 400/220kV 500MVA ICT-6 at Bhadla(PG). iii) Bus sectionializer and bus coupler breaker also opened instantaneously and elements connected to other buses remained intact. iv) As per PMU at Bhadla(PG), R-N phase to earth fault with delayed clearance of approx. 280msec is observed. v) As per SCADA, change in ISTS solar generation of approx. 150MW is observed.	1) 220kV Bhadla(PG)-ESUCRL(SBEPFL) ckt 2) 220kV Bhadla(PG)-TPREL ckt 3) 220kV Bhadla(PG)-MRPL ckt 4) 400/220kV 500MVA ICT-6 at Bhadla(PG) 5) 220kV Bhadla(PG) Bus-4
14	GD-1	Uttar Pradesh	22-Oct-2023 06:00	22-Oct-2023 08:31	02:31	0	100	0.000	0.225	35812	44496	i) 220/132kV Sikandra (Agra2) (UP) S/s has double main transfer bus scheme at 220kV level. However, during antecedent condition, all the elements were connected to 220kV Bus-1 only. 220kV Bus-2 and transfer were not in service condition. ii) As reported, at 06:00 hrs, 220 KV Aauraya(NT)-Agra2(UP) (PG) Ckt-1&2 tripped. At the same time, bus bar protection of 220kV Bus-1 at 220kV Agra2(UP) operated and as all elements at Agra2(UP) were connected to 220kV Bus-1 only, all 220kV element at Agra2(UP) tripped. Details related to exact location and nature of fault yet to be received from UP. iii) As per PMU at Agra2(UP), R-N phase to earth fault with unsuccessful A/R operation is observed. As per SCADA SOE at NRIIDC, it seems that A/R operation occurred in 220kV Agra2(UP)-Agra2(UP) ckt-1. UP has been communicated to share the DTR to ascertain the exact sequence of the event. iv) Due to tripping of 220kV Bus-1, supply to 132kV side of Sikandra (Agra2) (UP) also lost which resulted into total blackout of 220/132kV Sikandra (Agra2) (UP) S/s. v) As per SCADA, change in demand of approx. 100MW is observed in UP control area.	1) 220 KV Aauraya(NT)-Agra2(UP) (PG) Ckt-1 2) 220 KV Aauraya(NT)-Agra2(UP) (PG) Ckt-2 3) 220kV Agra2(UP)-Agra2(UP) Ckt-1 4) 220kV Agra2(UP)-Agra2(UP) Ckt-2 5) 220kV Agra2(UP)-Mirzapur Ckt 6) 220/132kV 160MVA ICT-1 at Agra2(UP) 7) 220/132kV 160MVA ICT-2 at Agra2(UP) 8) 220/132kV 160MVA ICT-3 at Agra2(UP) 9) 220/132kV 60MVA ICT-4 at Agra2(UP)
15	GD-1	Rajasthan	31-Oct-2023 15:28	31-Oct-2023 18:45	03:17	47	0	0.131	0.000	35896	51145	i) During antecedent condition, total generation of 220kV AHEJ3L was evacuating through 220 KV Fatehgarh_II(PG)-AHEJ3L PSS HB_FGARH_PG (AHEJ3L) (AHEJ3L) Ckt which was carrying approx. 47MW. ii) As reported, at 15:28 hrs, 220 KV Fatehgarh_II(PG)-AHEJ3L PSS HB_FGARH_PG (AHEJ3L) (AHEJ3L) Ckt tripped on earth fault due to high wind condition. iii) As per PMU plots of voltage at RE stations connected at 220kV or 400kV level of different pooling stations, it is observed that during the fault phase voltage dropped to ~0.95pu at Bikaner(PG), ~0.86pu at Bhadla2(PG), ~0.86pu at Bhadla(PG), ~0.86pu at Fatehgarh2(PG) and ~0.74pu at AFSPS. iv) At the same time, dip in RE generation is observed in some plants, e.g., ACME, Azure43, TPREL, Avada RHN, Avada Sunce, RSWPL, AHEJ2L, Azure43, NTPC Kolayat, NTPC Nokhra etc. As per SCADA, total reduction in NR RE generation of approx. 160MW is observed. v) As per PMU at AHEJ2L(UP) connected at 220kV level of Fatehgarh2(PG), AHPP(UP) connected at 220kV level of Bhadla2(PG) and Azure43(UP) connected at 400kV level of Bikaner(PG), R-N phase to phase fault with fault clearing time of approx. 80ms is observed in the system. But as per PMU at AFSPS(UP) connected at 220kV level of Fatehgarh2(PG) and AREPRL(UP) connected at 220kV level of Bhadla(PG), R-B phase to phase fault with fault clearing time of approx. 80ms is observed in the system. (Phase sequence issue is observed) vi) As per PMU at 220kV AHEJ3L, MW generation loss of approx. 47MW is observed at AHEJ3L.	1) 220 KV Fatehgarh_II(PG)-AHEJ3L PSS HB_FGARH_PG (AHEJ3L) (AHEJ3L) Ckt

20.Details of Grid Events during the Month of October 2023													
Western Region													
Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (Hrs:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-1	WR	01-Oct-23 16:30	01-Oct-23 17:34	01:04	-	54	-	0.10%	61714	55518	At 16:29 hrs/ 01-10-2023, failure of R phase potential transformer of 220 kV Ratlam-Bus-2 resulted in bus bar protection operation and 220 kV Ratlam-Bus-2 and all connected elements tripped. Load loss of 54 MW occurred at 220 kV Ratlam (Madhya Pradesh) due to the event.	Tripping of following elements- 1. 220 kV Ratlam-Bus-2 2. 220/132 kV Ratlam-ICT-2&3 3. 220 kV Ratlam-Nagra-2 4. 220 kV Badnawar-Ratlam-2
2	GI-2	WR	09-Oct-23 16:15	09-Oct-23 17:15	01:00	-	-	-	-	79626	67090	At 16:15 hrs/ 09-10-2023, Blast of B phase HV side current transformer of 400/220 kV Jetpur-ICT-1 resulted in bus bar protection operation in 400 kV Jetpur-Bus-1, 400 kV Jetpur-Bus-1 and all connected elements tripped. No Load loss occurred due to the event.	Tripping of following lines- 1. 400 kV Jetpur-Bus-1 2. 400 kV CGPI-Jetpur-1 3. 400 kV Jetpur-Ammeli-1 4. 400/220 kV Jetpur-ICT-1&3
3	GD-1	WR	12-Oct-23 06:49	12-Oct-23 07:15	00:26	-	314	-	0.48%	76937	65523	At 06:49 Hrs / 12-10-2023, HV side B phase CT of 220/66 kV 50MVA Navsari(GI) ICT-5 failed and resulted in tripping of 220 kV Navsari Main Bus and all the connected elements on LBB protection operation resulting in blackout at 220 kV Navsari(GI). As per PMU plot, initially fault was in B phase and converted into three phase fault due to fumes from burst CT. Load loss of 314 MW reported during the event.	Tripping of following elements- 1. 220 kV Navsari-Nasik-1&2 2. 220 kV Navsari-Dastan-1&2 3. 220 kV Navsari-Talagpore 4. 220 kV Navsari-Podda 5. 220 kV Navsari-Atul 6. 220 kV Navsari-Ambetha 7. 220/66 kV Navsari-ICT- 1,2,5&7 8. 220/66 kV Navsari-ICT- 3,4&6
4	GD-1	WR	13-Oct-23 12:20	13-Oct-23 16:02	03:42	186	-	0.24%	-	78304	69113	At 12:20Hrs/13.10.2023, 220 kV Kanwari- Bhawasinghpura line tripped on Y-B phase to phase fault due to strike of bird (Eagle) with Line(found out after patrolling). At the same time 220 kV Khandwa-Bhawasinghpura line also tripped from Bhawasinghpura end only on Y-B phase fault (weak infeed) resulting in total blackout at 220 kV Bhawasinghpura and 220 kV Kanwari. Generation loss of 186 MW at Masaya Solar (101MW at 220 kV Bhawasinghpura and 85 MW at 220 kV Kanwari) observed due to loss of evacuation path.	Tripping of following elements- 1. 220 kV Khandwa- Bhawasinghpura 2. 220 kV Kanwari- Bhawasinghpura
5	GI-1	WR	17-Oct-23 12:47	17-Oct-23 13:29	00:42	-	286	-	0.42%	73315	68694	At 12:47 Hrs /17.10.2023, 220 kV Boisar(PG) Bus-1 tripped due to mechanical failure of Bus coupler R phase isolator(B9A/204 Bay). Mechanical failure of isolator Bus Post Insulator (BPI) led to falling of Bus coupler R phase isolator, 220 kV Boisar(PG) Bus-1 and all connected element tripped. Load loss of 286 MW reported by MSLDC due to LTS operation in 220 kV Boisar(PG) Boisar(MH)-3	Tripping of following elements- 1. 220 kV Boisar(PG)-Boisar(MH)-1 2. 220 kV Boisar(PG)-Boisar(MH)-2, 3. 220 kV Boisar-Tarapur, 4. 400/220 kV ICT-2(315 MVA) 5. 400/220 kV ICT-4(500 MVA)
6	GI-1	WR	22-Oct-23 14:28	22-Oct-23 14:47	00:19	-	188	-	0.27%	68537	68684	At 14:28 Hrs /22.10.2023, 220 kV Boisar(PG)-Boisar(MH)-1 Tripped from Boisar(PG) end on R-E fault with A/R successful at Boisar(MH) end. 220 kV Boisar(PG)-Boisar(MH)-2 Tripped on R-N fault at both ends. 220kV Boisar(MH)-Ghodbunder Line tripped on R-N fault from Boisar end and holding from Ghodbunder end. 220kV Boisar(PG)-Boisar Line-3 and 220kV Tarapur-Boisar were already under outage. This led to 188 MW of load loss at 132kV Palghar Substation- 75.8MW and 132kV MIDC Substation-112.87 MW as reported by SLDC Maharashtra.	Tripping of following elements- 1. 220 kV Boisar(PG)-Boisar(MH)-1 2. 220 kV Boisar(PG)-Boisar(MH)-2, 3. 220kV Boisar(MS)-Ghodbunder
7	GD-1	WR	29-Oct-23 12:59	29-Oct-23 14:39	01:40	-	-	-	-	70573	66592	At 12:59 hrs /29-10-2023, 220 kV Bachau-Ostro-1&2 tripped on B-E fault and blackout occurred at 220 kV Ostro due to loss of evacuation path. No generation loss occurred due to the event.	Tripping of following elements- 1. 220 kV Bachau-Ostro-1&2
8	GI-2	WR	30-Oct-23 19:19	30-Oct-23 21:04	01:45	600	-	0.84%	-	71078	64716	At 19:19 hrs /30-10-2023, LBB protection operated and 400 kV SSP-Bus-2 and all connected elements tripped (presently SSP is being run with split bus arrangement). During inspection feeder due to which LBB operated couldn't be identified and there was no fault during the tripping. Generation loss of 600 MW occurred at 400/220 kV SSP (Sardar Sarovar Power Plant) due to the event.	Tripping of following elements- 1. 400 kV SSP-Bus-2 2. 400 kV Dhuile-SSP-1&2 3. 400 kV SSP-Rajgarh-2 4. 400/220 kV SSP-ICT-1&2 5. SSP (RBPH)-Unit-2&4 (200 MW) 6. 220 kV CHPH-RBPH-1&2 7. SSP (CHPH)-Unit-3,3.4&5 (50 MW)

20.Details of Grid Events during the Month of October 2023



Southern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI for GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-1	Tamil Nadu	02-Oct-23 10:40	02-Oct-23 12:09	01:29	573	0	1.20%	0.00%	47699	49492	Tripping of 230kV Bus-2 of 400kV/230kV Alammathy SS of TANTRANSCO and Complete Outage of 230kV OPG_CPP SS: As per the reports submitted, the triggering incident was R-Y fault in Bus-2 at Alammathy end. Immediately, 230kV Alammathy Bus-2 BBP operated and all the elements connected to the bus tripped which included 230kV Alammathy-OPG-2. With the tripping of 230kV Alammathy-OPG-2, 230kV Alammathy-OPG-3 got overloaded and due to which B-phase jumper failure created a B-N fault in 230kV Alammathy OPG Line-1 and the line tripped resulted in a complete outage of 230kV OPG_CPP SS. At the same time, NTEC, Vallur Unit-3 tripped on Low forward power protection.	1. 230kV Alammathy OPG Line-1&2 2. 400kV/230kV Alammathy ICT-3 3. 230kV Alammathy Mosur 4. 230kV Alammathy Manali Line-2 5. 230kV Alammathy Thiruvarkadu line 6. NTEC Vallur Unit-3
2	GD-1	Andhra Pradesh	03-Oct-23 14:10	03-Oct-23 15:02	00:52	0	0	0.00%	0.00%	48363	54821	Complete Outage of Gautami_CCCP - During antecedent conditions, 400kV Vemagiri Gautami_CCCP line-1 was under idle charged condition. As per the reports submitted, the triggering incident was B-N fault in 400kV Vemagiri Gautami_CCCP lin-2. Tripping of the only connected line resulted in complete outage of Gautami_CCCP.	1. 400kV Vemagiri Gautami_CCCP line-2
3	GD-1	Tamil Nadu	05-Oct-23 14:51	05-Oct-23 15:12	00:21	0	182	0.00%	0.31%	48447	59379	Complete Outage of 230kV/110kV Taramani SS of TANTRANSCO: During antecedent conditions, 230kV Kalivendapattu Taramani, and 230kV Taramani Rapuram, 220kV Taramani Mysapuram, 220kV Taramani Taramani, New were under outage. 230kV Taramani Rapuram and 220kV Taramani Mysapuram were idle charged from Taramani end. As per the reports submitted, the triggering incident was Y-N fault in the 230kV Taramani Sripurambudur line. Tripping of the only power supply source resulted in complete outage of 230kV/110kV Taramani SS.	1. 230kV Sripurambudur Taramani Line
4	GD-1	Karnataka	06-Oct-23 11:30	06-Oct-23 12:09	00:39	0	180	0.00%	0.30%	51272	59928	Complete Outage of 220kV/66kV Koramangala SS and 220kV/66kV Nimhans SS of KPTCL: During antecedent conditions, 220kV EDC Nimhans was under outage. 220kV/66kV Koramangala SS and 220kV/66kV Nimhans's SS, were being radially fed through 220kV Koramangala HSR line. As per the reports submitted, the triggering incident was a Y-N fault in the 220kV Koramangala Nimhans line and the line tripped. At the same time, 220kV HSR Koramangala line tripped at HSR end and further details are awaited. This resulted in a complete outage of 220kV/66kV Koramangala SS and 220kV/66kV Nimhans SS.	1. 220kV Koramangala Nimhans 2. 220kV Koramangala HSR
5	GD-1	Karnataka	09-Oct-23 09:16	09-Oct-23 09:32	00:16	0	372	0.00%	0.63%	49644	58974	Complete Outage of 220kV/66kV A Station, 220kV/66kV Subramanyapura SS, 220kV/66kV Peenya SS, 220kV/66kV Brindavan SS, 220kV/66kV/11kV NRS station and 220kV/66kV Khodays SS of KPTCL: During antecedent conditions, 220kV Somanahally Khodays and 220kV EDC A-Station were under outage. 220kV/66kV A Station, 220kV/66kV Subramanyapura SS, 220kV/66kV Peenya SS, 220kV/66kV Brindavan SS, 220kV/66kV/11kV NRS station and 220kV/66kV Khodays SS were being radially fed through 220kV Nelamangala Peenya Line-2,3 and 220kV Nelamangala Brindavan line. As per the reports submitted, the triggering incident was 220kV Nelamangala Peenya Line-2 and the line tripped. Subsequently, 220kV Nelamangala Peenya Line-3 and 220kV Nelamangala Brindavan lines tripped on overloading at Nelamangala end. Tripping of all these lines resulted in complete outage of 220kV/66kV A Station, 220kV/66kV Subramanyapura SS, 220kV/66kV Peenya SS, 220kV/66kV Brindavan SS, 220kV/66kV/11kV NRS station and 220kV/66kV Khodays SS.	1. 220kV Nelamangala Peenya Line-2&3 2. 220kV Nelamangala Brindavan
6	GD-1	Karnataka	09-Oct-23 16:46	09-Oct-23 17:15	00:29	1085	0	2.48%	0.00%	43670	53133	Complete Outage of 400kV/22kV UPL SS and Tripping of 220kV Bus-1 of 220kV/110kV Kemar SS of KPTCL: During antecedent conditions, 220kV/110kV Kemar SS was operating with split bus condition at 220kV level. As per the reports submitted, the triggering incident was Y-N fault in 400kV UPLC Hebbanahalli Line-2. Immediately, UPLC Unit-2 tripped on SP5 operation. At 16:54hrs, 400kV UPLC Hebbanahalli Line-1 tripped on R-N fault. Subsequently, UPLC Unit-1 tripped on over frequency. Tripping of units and lines resulted in complete outage of 400kV/22kV UPL SS. Since, 220kV Kemar Bus-1 was radially fed from 400kV/22kV UPL SS, this resulted in loss of supply to 220kV Bus-1 of 220kV/110kV Kemar SS.	1. 400kV Hebbanahally UPLC Line-1&2 2. UPLC Unit-1&2
7	GD-1	Karnataka	10-Oct-23 12:35	10-Oct-23 15:45	03:10	16	258	0.03%	0.42%	51512	60930	Complete Outage of 220kV Nandihalli , 220kV/11kV Bijapur SS, 220kV/110kV Indi SS and 220kV/110kV Aheri SS of KPTCL and 220kV/33kV Vaishali: During antecedent conditions, all elements were connected to 220kV bus-1 at 220kV Nandihalli SS. As per the reports submitted, the triggering incident was R-N fault in 220kV Kudgi, NTPC Nandihalli line-4. At the same time, 220kV Kudgi, NTPC Nandihalli Line-3(which was under outage) sensed the fault. In zone-1 for 220ms, this led to 220kV LBB operation. Immediately all the elements connected to the 220kV Bus-1 tripped resulting in complete outage of 220kV Nandihalli SS. Since, 220kV/11kV Bijapur SS, 220kV/110kV Indi SS, 220kV/110kV Aheri SS and 220kV/33kV Vaishali were being radially connected to 220kV Nandihalli, outage of Nandihalli resulted in complete outage of these stations.	1. 220kV Nandihalli Kudgi, NTPC Line-1,2 & 4 2. 220kV Nandihalli Bijapur Line-1&2 3. 220kV Nandihalli BB Wadi Line-1&2
8	GD-1	Karnataka	15-Oct-23 09:42	15-Oct-23 11:15	01:33	24	150	0.05%	0.27%	48432	55187	Complete Outage of 220kV/110kV Bagewadi SS of KPTCL , 220kV Baluthi, 220kV Fortune SS, 220kV Atria SS and 220kV RBKX SS - As per the reports submitted, the triggering incident was a failure of the 220kV bus coupler at 220kV/110kV Bagewadi SS causing R-N fault in 220kV Bus-1 and 220kV Bus-2. Immediately, 220kV Bus-1 and Bus-2 BBP operated and all the elements connected to the buses tripped resulting in a complete outage of 220kV/110kV Bagewadi SS. Since 220kV Baluthi, 220kV Fortune SS, 220kV Atria SS and 220kV RBKX SS are radially connected with 220kV/110kV Bagewadi SS outage of 220kV/66kV Bagewadi SS resulted in complete outage of these stations.	1. 220kV Bagewadi Lingsugur Line-1&2 2. 220kV Bagewadi Aimatti Line-1&2 3. 220kV Bagewadi Nandihalli Line-1&2 4. 220kV Bagewadi Fortune Line-1&2 5. 220kV Bagewadi Atria Line-1&2 6. 220kV Bagewadi RBKX
9	GD-1	Karnataka	17-Oct-23 12:06	17-Oct-23 14:06	02:00	0	400	0.00%	0.69%	50141	58117	Tripping of 400kV Bus-2 of 400kV/220kV Guttur SS and complete outage of 220kV/110kV Ranebenur SS, 220kV/66kV Davanagere SS, 220kV/66kV Hosadurga SS, 220kV/66kV Bemkikere SS, 220kV/66kV Honnali SS, 220kV/66kV Neelagunda SS and 220kV/66kV Guttur SAS SS of KPTCL: As per the reports submitted, the triggering incident was Y-N fault in 400kV Bus-2 of 400kV/220kV Guttur SS. Immediately, Bus-2 BBP operated and all the elements connected to the bus tripped. Since, 220kV/110kV Ranebenur SS, 220kV/66kV Davanagere SS, 220kV/66kV Hosadurga SS, 220kV/66kV Bemkikere SS, 220kV/66kV Honnali SS, 220kV/66kV Neelagunda SS and 220kV/66kV Guttur SAS SS were being radially connected to 400kV Bus-2 of 400kV/220kV Guttur SS, tripping of the bus resulted in complete outage of these stations.	1. 400kV Guttur Hiriyur Line-1&2 2. 400kV Guttur Naendra Line-2 3. 400kV Guttur Doni Line 4. 400kV Guttur BTPS Line 5. 400kV/220kV Guttur ICT-1&2
10	GD-1	Karnataka	17-Oct-23 12:10	17-Oct-23 13:43	01:33	0	160	0.00%	0.28%	49912	58158	Complete Outage of 220kV/66kV Alipura SS of KPTCL: As per the reports submitted, the triggering incident was B-N fault in 220kV Alipur BTPS line. At BTPS end, the fault was sensed in zone-1 and the line tripped. Alipur end failed to clear the fault, and the fault was cleared by 220kV Alipur Regulpadu end on operation of zone-3 at Regulpadu end with a delay of 750ms. Tripping of both connected lines resulted in complete outage of 220kV/66kV Alipura SS.	1. 220kV Alipura BTPS 2. 220kV Alipura Regulpadu
11	GD-1	Karnataka	27-Oct-23 04:05	27-Oct-23 10:00	05:55	2	30	0.01%	0.07%	37968	43970	Complete Outage of 220kV/66kV HN_Pura_SS of KPTCL and 220kV/33kV Gopalpura SS of Suzlon_KA: As per the reports submitted, due to issue in DC supply at Gopalpura end, 220kV Gopalpura Hassan and 220kV Gopalpura Tubnikere lines tripped only at Gopalpura end. Tripping of both these lines resulted in complete outage of 220kV/33kV Gopalpura SS which further resulted in complete outage of 220kV/66kV HN_Pura_SS.	1. 220kV Gopalpura Hassan 2. 220kV Gopalpura Tubnikere
12	GI-1	Telangana	15-Oct-23 00:35	15-Oct-23 02:07	01:32	250	0	0.62%	0.00%	40419	46104	Tripping of 220kV Bus-2 of 220kV/220kV Nsagar PH of TSENGCO: As per the reports submitted, the triggering incident was maloperation of 220kV Nsagar PH Bus-2. Immediately all the elements connected to the bus tripped.	1. 220kV Tallapalli Nsagar_PH Line-2&3 2. 220kV Nsagar Chalakurthy 3. Nsagar Unit-4&5&6 4. 220kV/132kV 100MVA PTR-2

20.Details of Grid Events during the Month of October 2023													
Southern Region													
Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
13	GI-1	Karnataka	18-Oct-23 15:17	18-Oct-23 17:09	01:52	0	0	0.00%	0.00%	49397	57864	Tripping of 220kV Bus-1 of 400kV/220kV Munirabad SS of PGCL SR-1: During antecedent conditions, at 400kV/220kV Munirabad SS, main circuit breaker of 220kV Munirabad Lingapur line-2 was bypassed and the line was charged through Bus Coupler by connecting to 220kV Bus-1. The triggering incident was the tripping of 220kV Munirabad Lingapur line 2 on the R-N Fault. Since this is the only line connected to Bus-1 at Munirabad, this resulted in the de-energization of 220kV Bus-1 of 400kV/220kV Munirabad SS.	1. 220kV Munirabad Lingapur line-2
14	GI-2	Telangana	26-Oct-23 05:25	26-Oct-23 10:34	05:09	460	0	1.15%	0.00%	39878	44291	Tripping of 400kV Bus-2 of 400kV Boopalpally Generating station of TSGENCO: As per the reports submitted, the triggering incident was Breaker failure in GT-2 of 400kV Boopalpally causing an R-N fault near the breaker. The fault was cleared by remote ends on DEF operation resulting in outage of 400kV Bus-2 of 400kV Boopalpally Generating station.	1. 400kV Boopalpally Warangal Line-1&2 2. 400kV Boopalpally Chandrapur Line-2
15	GI-1	Andhra Pradesh	28-Oct-23 11:15	28-Oct-23 15:47	04:32	0	0	0.00%	0.00%	56344	60366	Tripping of 220kV Bus-1 of 400kV/220kV Sattenapally SS of APTRANSCO: As per the reports submitted, the triggering incident was Y-N fault in 220kV Bus-1 of 400kV/220kV Sattenapally SS. Immediately, 220kV BBP operated and all the elements connected to the bus tripped.	1. 400kV/220kV Sattenapally ICT-1&3 2. 220kV Sattenapally Narsaraopet Line-1 3. 220kV Sattenapally Parchuru Line-1 4. 220kV Sattenapally Prathipadu Line-1

20.Details of Grid Events during the Month of Octoberber 2023													
Eastern Region													
Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation/ loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-1	Teesta V, Teesta III, Dikchu	04-Oct-23 02:55	Still Out	-	0	0	0.00%	0.00%	27350	20289	At 00:50 hrs on 04-10-2023, due to continuous high silt and rise in inflow in the upstream area of the reservoir, all units at Teesta-III (6*200 MW) (On bar gen 1300 MW) taken out of bar. 400 kV Teesta III – Dikchu & 400 kV Teesta-III- Rangpo lines were hand tripped from Teesta III HEP at 01:08 hrs and consequently Teesta-III substation became dead. Both units at Dikchu (2*48 MW) taken out of bar at 01:49 hrs due to flash flood. All units of Teesta V (3*170 MW, generating around 504 MW) were taken out of service at 02:37 hrs due to high silt. 400 kV RANGPO-TEESTA-V- D/C tower collapsed at loc. No. 1 at 02:55 hrs and Teesta-V substation became dead. 400 kV Dikchu- Rangpo line breaker opened from Dikchu HEP at 06:15 hrs and Dikchu substation became dead.	400 kV Rangpo-Teesta V D/C Hand-tripped/De-synchronized: 400 kV Teesta 3-Rangpo 400 kV Teesta 3-Dikchu 400 kV Rangpo-Dikchu 6*200 MW Units at Teesta 3 3*168 MW Units at Teesta 5 2*48 MW Units at Dikchu HEP
2	GD-1	Rongnichu	09-Oct-23 11:13	09-Oct-23 18:17	07:04	103	0	0.39%	0.00%	26407	22285	At 11:13 Hrs, 220 kV Rangpo-Rongnichu-2 tripped on Y_B fault, leading to loss of evacuation path for two running units at Rongnichu as 220 kV Rangpo-Rongnichu-1 was already under emergency shutdown. Consequently, total power failed at Rongnichu 5/s and around 103 MW generation loss occurred.	220 kV Rangpo-Rongnichu-2
3	GI-2	Barh	27-Oct-23 10:15	27-Oct-23 18:29	08:14	570	0	2.04%	0.00%	27960	19636	At 10:15 Hrs, A/r observed in 400 kV Barh-Mothihari-2 which was successful from both ends, however, teed protection operated in its tie bay at Barh and the dia element 400 kV Kahalgaon-Barh-2 tripped. At the same time, 660 MW UR2 at Barh also tripped on GT differential protection and 570 MW generation loss occurred.	400 kV Barh-Mothihari-2 (A/r successful) 400 kV Kahalgaon-Barh-2 660 MW UR2 at Barh

20.Details of Grid Events during the Month of October 2023											
North-Eastern Region											
Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*	
	(GI for GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)
1	GD-1	Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System	03-Oct-23 03:00	03-Oct-23 03:32	00:32	14.5	17.5	0.62%	0.80%	2344	2183
Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System were connected with the rest of the grid by 132 kV Balipara - Tenga line. At 03:00 Hrs of 03/10/2023, 132 kV Balipara - Tenga line tripped. Due to tripping of this element, Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System got separated from rest of the grid due to load generation mismatch in these areas. Power was extended to Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System by charging 132 kV Balipara - Tenga line at 03:32 Hrs.											
2	GD-1	Sarupathar and Golaghat areas of Assam Power System	04-Oct-23 13:58	04-Oct-23 15:12	01:14	0	43	0.00%	1.79%	2376	2408
Sarupathar and Golaghat areas of Assam Power System were connected with the rest of the grid by 132 kV Sarupathar-Bokajan line. 132 kV Golaghat-Mariani(AS) line was under planned shutdown prior to event. At 13:58 Hrs of 04/10/2023, 132 kV Sarupathar-Bokajan line tripped. Due to tripping of this element, Sarupathar and Golaghat areas of Assam Power System got separated from rest of NER grid due to no source available in these areas. Power was extended to Sarupathar and Golaghat areas of Assam Power System by charging 132 kV Sarupathar-Bokajan line at 15:12 Hrs on 04/10/2023.											
3	GD-1	Zuangtui, and radially connected 132 kV Saitual,Vankal, Serchhip and Lunglei substations of Mizoram Power System	04-Oct-23 19:57	04-Oct-23 21:31	01:34	0	34	0.00%	1.09%	3361	3128
Zuangtui, and radially connected 132 kV Saitual,Vankal, Serchhip and Lunglei substations of Mizoram Power System were connected with the rest of the grid by 132kV Melriat(PG) - Zuangtui line. At 19:57 Hrs of 04/10/2023, 132kV Melriat(PG) - Zuangtui line tripped. Due to tripping of this element, Zuangtui, and radially connected 132 kV Saitual,Vankal, Serchhip and Lunglei substations of Mizoram Power System got separated from rest of NER grid due to no source available in these areas. Power was extended to Zuangtui, and radially connected 132 kV Saitual,Vankal, Serchhip and Lunglei substations of Mizoram Power System by charging 132kV Melriat(PG) - Zuangtui line at 21:31 Hrs on 04/10/2023.											
4	GD-1	Margherita(Ledo), Rupai and Chapakhowa areas of Assam Power system and Roing, Pasighat areas of Arunachal Pradesh Power System	15-Oct-23 09:38	15-Oct-23 10:14	00:36	0	52	0.00%	2.57%	2461	2020
Margherita(Ledo), Rupai and Chapakhowa areas of Assam Power system and Roing, Pasighat areas of Arunachal Pradesh Power System were connected with the rest of the grid by 132 kV Tinsukia-Margherita(Ledo) line. At 09:38 Hrs of 15/10/2023, 132 kV Tinsukia-Margherita(Ledo) line tripped. Due to tripping of this element, Margherita(Ledo), Rupai and Chapakhowa areas of Assam Power system and Roing, Pasighat areas of Arunachal Pradesh Power System got separated from rest of the grid due to no source available in these areas. Power was extended to Margherita(Ledo), Rupai and Chapakhowa areas of Assam Power system and Roing, Pasighat areas of Arunachal Pradesh Power System by charging 132 kV Tinsukia-Rupai line at 10:14 Hrs.											
5	GD-1	Lakwa area of Assam Power System	17-Oct-23 19:32	17-Oct-23 20:55	01:23	150	0	4.13%	0.00%	3635	3029
Lakwa area of Assam Power system, LTPS & LRPP generation was connected with the rest of the grid by 132 kV LTPS-Nazira D/C, 132 kV LTPS-Moran, 132 kV LTPS-Sonari, 132 kV LTPS-NTPS and 132 kV LTPS-Mariani(AS) lines. At 19:32 Hrs of 17/10/2023, 132 kV LTPS Bus tripped. Due to this tripping, all the lines connected to LTPS i.e., 132 kV LTPS-Nazira D/C, 132 kV LTPS-Moran, 132 kV LTPS-Sonari, 132 kV LTPS-NTPS and 132 kV LTPS-Mariani(AS) lines tripped and LTPS & LRPP generation of Assam Power system got separated from rest of the grid due to load generation mismatch in this area. 132 kV LTPS Bus was charged by charging 132 kV LTPS-Mariani(AS) line at 20:55 Hrs.											
6	GD-1	Dharmanagar area of Tripura Power system	19-Oct-23 01:47	19-Oct-23 02:25	00:38	0	22	0%	1%	2700	2149
Dharmanagar area of Tripura Power system was connected with the rest of the grid by 132 kV Dharmanagar-Dullachherra and 132 kV PK Bari-Dharmanagar lines. At 01:47 Hrs of 19/10/2023, 132 kV Dharmanagar-Dullachherra and 132 kV PK Bari-Dharmanagar lines tripped. Due to tripping of these elements, Dharmanagar area of Tripura Power system got separated from rest of the grid due to no source available in this area. Power was extended to Dharmanagar area of Tripura Power system by charging 132 kV Dharmanagar-Dullachherra line at 02:25 Hrs.											
7	GD-1	Mokokchung area of Nagaland Power System	27-Oct-23 11:56	27-Oct-23 13:20	01:24	0	12	0%	1%	2170	2173
Mokokchung area of Nagaland Power system was connected with the rest of the grid by 132 kV Doyang-Mokokchung & 132 kV Mokokchung(PG)-Mokokchung(NL) D/C lines. At 11:56 Hrs of 27/10/2023, 132 kV Doyang-Mokokchung & 132 kV Mokokchung(PG)-Mokokchung(NL) D/C lines tripped. Due to this trippings, Mokokchung area of Nagaland Power system got separated from rest of the grid due to no source available in this area. Power was extended to Mokokchung area of Nagaland Power system by charging 132 kV Mokokchung(PG)-Mokokchung(NL)-H & 132 kV Doyang-Mokokchung line at 13:20 Hrs of 27/10/2023.											
8	GD-1	Pailapool area of Assam Power system	30-Oct-23 12:47	30-Oct-23 12:53	00:06	20	23	0.92%	1.12%	2169	2045
Pailapool area of Assam Power system was connected with the rest of the grid by 132 kV Jiribam(PG)-Pailapool and 132 kV Srikon-Pailapool lines. 132 kV Srikon-Pailapool line was under planned shutdown prior to the event. At 12:47 Hrs of 30/10/2023, 132 kV Jiribam(PG)-Pailapool line tripped. Due to tripping of this element, Pailapool area of Assam Power system got separated from rest of the grid due to load generation mismatch in this area. Power was extended to Pailapool area of Assam Power system by charging 132 kV Srikon-Pailapool line at 12:53 Hrs of 30/10/2023.											
9	GI-1	Tripura	08-Oct-23 06:20	08-Oct-23 08:00	01:40	26	0	1%	0%	3096	1859
AGTCCPP GT-IV & ST-VI tripped at 06:20 Hrs on 08.10.2023 due to Control MCC trouble. Revision done from Block No. 33 on 08.10.2023											
10	GI-2	BGTPP	21-Oct-23 19:35	21-Oct-23 21:30	01:55	178	0	5%	0%	3544	2854
BGTPP Unit-3 tripped at 19:35 Hrs on 21.10.2023 due to Furnace Pressure high. Revision done from Block No. 87 on 21.10.2023											
11	GI-2	Kopili	22-Oct-23 03:35	22-Oct-23 06:30	02:55	50	0	2%	0%	2043	1770
Kopili Unit-3 tripped at 03:35 Hrs on 22.10.2023 due to excitation problem. Revision done from Block No. 27 on 22.10.2023											
12	GI-1	Kopili Stg II	22-Oct-23 08:38	22-Oct-23 12:00	03:22	25	0	1%	0%	2385	1979
Kopili Stg-2 tripped at 08:38 Hrs on 22.10.2023 due to Overspeed forced trip. Revision done from Block No. 49 on 22.10.2023											

21. NEW ELEMENTS COMMISSIONED* IN OCTOBER 2023							
COMMISSIONING OF NEW GENERATING UNITS							
REGION	S.NO.	ENTITY	UNIT NAME / LOCATION	ADD. CAPACITY (MW)	UNIT NO.	INS. CAPACITY (MW)	DATE®
NR	1	SBSR POWER CLEANTECH ELEVEN PRIVATE LIMITED	SBSR Power Cleantech Eleven Private Limited(Solar)/Rajasthan	25	-	300	04-10-2023
	2	RSEKPL	Rising Sun Energy (K) Private Limited(Solar)/Rajasthan	164	-	190	21-10-2023
WR	3	ADANI WIND ENERGY KUTCHH FOUR LTD	Adani Wind Energy Kutchh Four Ltd(Wind)/Gujarat	14.7	I	189	12-10-2023
	®RE (Solar & Wind generation added capacity FTC is in phases. Date mentioned is the date by which complete (Added) capacity						
COMMISSIONING OF NEW ICTs							
REGION	S.NO.	ENTITY	SUB-STATION	VOLTAGE (kV)	ICT NO.	CAPACITY (MVA)	DATE
NR	1	PRTL	Fatehgarh_III	400/220/33	II	500	02-10-2023
	2	UPPTCL	Rasra	400/220/33	II	500	04-10-2023
	3	PRTL	Fatehgarh_III	400/220/33	I	500	05-10-2023
WR	4	MPPTCL	Kirnapur	400/132	III	100	05-10-2023
	5	PGCIL	Bhatapara	400/220	III	500	09-10-2023
SR	6	KPTCL	Hebbanahalli	400/220	I	500	30-10-2023
	7	KNTL	Koppal	400/220	I	500	16-10-2023
	8	KNTL	Koppal	400/220	II	500	16-10-2023
	9	KNTL	Koppal	400/220	III	500	16-10-2023
	10	TANTRANSCO	Vellalaviduthi	400/230	IV	315	07-10-2023
COMMISSIONING OF NEW TRANSMISSION LINES							
REGION	S.NO.	ENTITY	LINE NAME	CKT NO.	VOLTAGE (kV)	DATE	
WR	1	WKTL	765 kV Warora-Warangal	I	765	16-10-2023	
	2	WKTL	765 kV Warora-Warangal	II	765	16-10-2023	
SR	3	TANTRANSCO	765kV-Thiruvalam-Ariyalur	II	765	20-10-2023	
	4	TSTRANSCO	400kV-Yedula-Vattem	I	400	20-10-2023	
	5	KNTL	400kV-Koppal-New Narendra	I	400	16-10-2023	
	6	KNTL	400kV-Koppal-New Narendra	II	400	16-10-2023	
ER	7	JUSNL	400KV-Tenughat-PVUNL	I	400	06-10-2023	
NER	8	AEGCL	220kV Tinsukia -Behiating	I	220	10-10-2023	
	9	AEGCL	220kV Tinsukia - Behiating	II	220	10-10-2023	
LILO OF TRANSMISSION LINES							
REGION	S.NO.	ENTITY	LINE NAME (LILOed LINE)	LILO AT	VOLTAGE (kV)	DATE	
NR	1	WUPPTCL,PGYTL	400kV Ataur-Noida Sec 123 Ckt-I (400kV Ataur-Indirapuram Ckt-II)	Noida Sector 123	400	20-10-2023	
	2	WUPPTCL,PGYTL	400kV Indirapuram-Noida Sec 123Ckt-I (400kV Ataur-Indirapuram Ckt-II)	Noida Sector 123	400	20-10-2023	
WR	3	BALCO & PGCIL	400kV BALCO_MRSDS-Korba_NTPC (400kV Korba-Birsinghpur)	BALCO (MRSDS)	400	01-10-2023	
	4	BALCO & PGCIL	400kV BALCO_MRSDS-Birsinghpur (400kV Korba-Birsinghpur)	BALCO (MRSDS)	400	01-10-2023	
SR	5	TANTRANSCO	400kV Vellalaviduthi-Karaiudi Ckt_I	-	400	04-10-2023	
	6	TANTRANSCO	400kV Pugalur-Vellalaviduthi Ckt-I	-	400	04-10-2023	
	7	KPTCL	400kV Hassan-Hebbanahalli Ckt-II	-	400	03-10-2023	
	8	KPTCL	400kV Hebbanahalli-UPCL Ckt-I	-	400	02-10-2023	
	9	KPTCL	400kV Hassan-Hebbanahalli Ckt-I	-	400	02-10-2023	
	10	KPTCL	400kV Hebbanahalli-UPCL Ckt-II	-	400	03-10-2023	
	11	KARUR TRANSMISSION LTD	400kV Karur PS-Pugalur HVDC Ckt-I	-	400	24-10-2023	
	12	KARUR TRANSMISSION LTD	400kV Karur PS-Pugalur HVDC Ckt-II	-	400	24-10-2023	
	13	KARUR TRANSMISSION LTD	400kV Karur PS-Pugalur Ckt-II	-	400	24-10-2023	
	14	KARUR TRANSMISSION LTD	400kV Karur PS-Pugalur Ckt-I	-	400	24-10-2023	
COMMISSIONING OF BUS/LINE REACTORS							
REGION	S.NO.	ENTITY	SUB-STATION / LINE (@SUB-STATION)	VOLTAGE (kV)	CAPACITY (MVAR)	DATE	
NR	1	PRTL	Bus Reactor-II@Fatehgarh_III	400	125	02-10-2023	
WR	2	WKTL	Warora-Warangal Ckt-I@Warora	765	240	16-10-2023	
	3	WKTL	Warora-Warangal Ckt-II@Warora	765	240	16-10-2023	
SR	4	KARUR TRANSMISSION LTD	Bus Reactor-II@Karur	400	125	24-10-2023	
	5	KARUR TRANSMISSION LTD	Bus Reactor-I@Karur	400	125	24-10-2023	
	6	TANTRANSCO	Thiruvalam-Ariyalur Ckt-II@Ariyalur	765	240	20-10-2023	
	7	WKTL	Warangal_New -Warora Ckt_II@Warangal_New	765	240	17-10-2023	
	8	KNTL	Bus Reactor-II@Koppal	400	125	16-10-2023	
	9	KNTL	Bus Reactor-I@Koppal	400	125	16-10-2023	
	10	WKTL	Warangal_New -Warora Ckt_I@Warangal_New	765	240	16-10-2023	
	11	TANTRANSCO	Bus Reactor-I@Vellaviduthi	400	80	07-10-2023	
ER	12	PVUNL	Bus Reactor-II@PVUNL	400	125	10-10-2023	
COMMISSIONING OF HVDC/FACTS DEVICE/SYSTEM							
REGION	S.NO.	NAME	SUB-STATION / CONSTITUENT	RATINGS	VOLTAGE (kV)	DATE	
*Includes first time charging (FTC) as well							

22.Voltage Profile

विद्युत विभव रूपरेखा माह - अक्टूबर 2023

VOLTAGE PROFILE - OCTOBER 2023

Date of reporting: 03-Nov-23

क्र.स. Sl. No.	क्षेत्र REGION	उपकेंद्र SUBSTATION	VOLTAGE < V(lower)* (V=380,728 kV)	V(lower) < VOLTAGE < V(upper)*	VOLTAGE > V(upper)* (V=420,800 kV)	Voltage Deviation Index (%age of time voltage is outside range)	Number of hours voltage was outside IEGC band during month	उच्चतम (कि.वो.) Maximum(kV)	निम्नतम(कि.वो.) Minimum(kV)	औसत (कि.वो.) Average(kV)
1	पूर्वी क्षेत्र ER	अंगुल ANGUL	0%	100%	0%	0%	0	795	751	779
2		दालिपली DARPALI	0%	100%	0%	0%	0	788	763	780
3		गया GAYA	0%	100%	0%	0%	0	783	755	772
4		जोरत JEERAT	0%	100%	0%	0%	0	788	735	758
5		झारसुगडा JHARSUGUDA	0%	100%	0%	0%	0	799	770	789
6		मिदनापुर MEDINIPUR	0%	100%	0%	0%	0	790	750	769
7		रांची RANCHI	0%	100%	0%	0%	0	794	764	782
8		सासाराम SASARAM	0%	100%	0%	0%	0	800	749	764
1	उत्तरी क्षेत्र NR	आगरा AGRA	0%	100%	0%	0%	0	798	753	779
2		आगरा (फतेहाबाद) AGRA (FATEHABAD)	0%	100%	0%	0%	0	792	741	770
3		अजमेर AJMER	0%	100%	0%	0%	1	802	750	778
4		अलीगढ़ ALIGARH	0%	100%	0%	0%	0	794	744	774
5		अनपरा सी ANPARA-C	0%	100%	0%	0%	0	780	762	770
6		अनपरा डी ANPARA-D	0%	100%	0%	0%	0	778	761	769
7		अंता ANTA	0%	100%	0%	0%	0	796	759	778
8		बलिया BALLIA	0%	100%	0%	0%	0	781	745	767
9		बारा BARA	0%	100%	0%	0%	0	787	761	774
10		भादला BHADLA	0%	100%	0%	0%	0	794	750	773
11		भादला-2 BHADLA-2	0%	100%	0%	0%	0	796	753	774
12		भिवानी BHIWANI	0%	100%	0%	0%	0	800	754	782
13		बीकानेर BIKANER	0%	100%	0%	0%	0	796	752	774
14		बरैली BAREILLY	0%	100%	0%	0%	2	802	744	775
15		चित्तौड़गढ़ CHITTORGARH	0%	100%	0%	0%	1	803	747	779
16		फतेहाबाद-2 FATEHABAD-2	0%	100%	0%	0%	0	796	741	773
17		फतेहपुर FATEHPUR	0%	100%	0%	0%	0	791	744	768
18		ग्रेंटर नोएडा GREATER NOIDA	0%	100%	0%	0%	0	798	743	777
19		हापड़ HAPUR	0%	99%	1%	1%	5	805	730	773
20		जवाहरपुर JAWAHARPUR	0%	100%	0%	0%	0	794	743	772
21		झाटिकरा JHATIKARA	0%	100%	0%	0%	0	794	746	775
22		कानपुर जीआईएस KANPUR GIS	0%	100%	0%	0%	0	790	755	775
23		खेतरी KHETRI	0%	100%	0%	0%	0	799	749	778
24		कोटेश्वर KOTESHWAR	0%	100%	0%	0%	0	797	739	774
25		लालितपुर LALITPUR	0%	100%	0%	0%	0	772	740	758
26		लखनऊ LUCKNOW	0%	100%	0%	0%	0	794	749	773
27		मैनपुरी MAINPURI	0%	100%	0%	0%	0	793	741	771
28		मेरठ MEERUT	0%	100%	0%	0%	1	802	741	779
29		मोहा MOHA	0%	100%	0%	0%	0	800	741	772
30		ओबरा सी OBRA C	0%	100%	0%	0%	0	779	757	767
31		उरई ORAI	0%	100%	0%	0%	1	803	763	785
32		फागी PHAGI	0%	100%	0%	0%	0	801	751	779
33		उन्नाव UNNAO	0%	100%	0%	0%	0	786	740	764
34		वाराणसी VARANASI	0%	100%	0%	0%	0	789	764	777
1	पश्चिमी क्षेत्र WR	अकोला AKOLA	0%	100%	0%	0%	0	793	753	773
2		औरंगाबाद AURANGABAD	0%	100%	0%	0%	2	805	750	776
3		भोपाल (बीडीटीसीएल) BHOPAL (BDTCL)	0%	100%	0%	0%	0	789	749	769
4		भुज BHUJ	0%	100%	0%	0%	0	797	746	777
5		भुज-2 BHUJ-II	0%	100%	0%	0%	0	790	748	772
6		बिलासपुर BILASPUR	0%	100%	0%	0%	0	783	760	772
7		बिना BINA	0%	100%	0%	0%	0	795	758	778
8		बनारस BANARSKANTHA	0%	100%	0%	0%	3	803	755	784
9		चाण CHAMPA	0%	100%	0%	0%	1	801	752	786
10		धुले (बीडीटीसीएल) DHULE (BDTCL)	0%	100%	0%	0%	0	799	751	774
11		धर्मजगढ़ DHARMJAGARH	0%	100%	0%	0%	0	787	761	777
12		रायपुर पूलिंग RAIPUR POOLING	0%	100%	0%	0%	0	790	767	780
13		एकतुनी EKTUNI	0%	100%	0%	0%	0	794	747	770
14		गदरवाड़ा GADARWARA	0%	100%	0%	0%	0	799	767	783
15		ग्वालियर GWALIOR	0%	100%	0%	0%	0	799	760	781
16		इंदौर INDORE	0%	100%	0%	0%	0	791	750	771
17		जबलपुर JABALPUR	0%	100%	0%	0%	1	804	769	786
18		खंडवा KHANDWA	0%	100%	0%	0%	0	793	753	773
19		कोरडी KORADI	0%	100%	0%	0%	0	783	754	769
20		लाकाडिया LAKADIYA	0%	99%	1%	1%	8	805	756	783
21		रायगढ़ पूलिंग RAIGARH POOLING	0%	100%	0%	0%	0	796	776	786
22		पड़घे PADGHE	0%	99%	1%	1%	5	811	743	776
23		परली PARLI	0%	99%	1%	1%	4	806	756	781
24		पुणे PUNE	0%	99%	1%	1%	5	809	742	776
25		राजनंदगांव RAJNANDGAON	0%	100%	0%	0%	0	801	769	786
26		सासन SASAN	0%	100%	0%	0%	0	789	769	780
27		सतना SATNA	0%	100%	0%	0%	0	797	768	784
28		सिवनी SEONI	0%	100%	0%	0%	0	793	758	775
29		सीपत SIPAT	0%	100%	0%	0%	0	784	762	773
30		सोलापुर SOLAPUR	0%	99%	1%	1%	6	810	757	783
31		तिरुठा TIRUTHA	0%	100%	0%	0%	0	777	756	766
32		तामनार TAMNAR	0%	100%	0%	0%	0	794	775	784
33		वडोदरा VADODARA	0%	100%	0%	0%	3	804	746	776
34		विंध्याचल पूलिंग VINDHYACHAL PS	0%	100%	0%	0%	0	790	772	783
35	दक्षिणी क्षेत्र SR	वर्धा WARDHA	0%	100%	0%	0%	4	805	752	779
36		वरारो WARORA	0%	100%	0%	0%	0	798	759	781
1		कडपा CUDDAH	0%	96%	4%	4%	30	812	751	783
2		चिक्लरीचिक्ल CHILAKALURIPETA	0%	100%	0%	0%	2	802	738	772
3		कुरुन कुरुन KURNOOL	0%	100%	0%	0%	0	799	743	773
4		महेश्वरम MAHESHWARAM	0%	95%	5%	5%	41	811	749	782
5		निजामाबाद NIZAMABAD	0%	92%	8%	8%	60	815	752	785
6		नेल्लूर पूलिंग NELLORE PS	0%	100%	0%	0%	0	796	745	770
7		रायचूर RAICHUR	0%	100%	0%	0%	2	805	749	777
8		श्रीकाकुलम SRIKAKULAM	0%	99%	1%	1%	7	804	749	782
9	पूर्वोत्तर क्षेत्र NER	तिरुवल्लम THIRUVALLEM	0%	99%	1%	1%	4	801	740	772
10		वेमगिरी VEMAGIRI	0%	100%	0%	0%	3	807	742	774
1		बिस्वनाथ चौराहा BISWANATH CHARIALI (400 kV)	0%	100%	0%	0%	0	421	400	410
2		बोंगाईगांव BONGAIGAON (400 kV)	0%	100%	0%	0%	0	415	397	408
3		बोंगाईगांव टीपीएस BONGAIGAON TPS (400 kV)	0%	100%	0%	0%	0	418	402	411
4		इम्फाल IMPHAL (400 kV)	0%	100%	0%	0%	0	415	395	405
5		बर्निहाट BYRNHAT (400 kV)	0%	100%	0%	0%	0	420	402	412
6		कामेंग KAMENG (400 kV)	0%	100%	0%	0%	0	414	396	405
7		अज़रा AZARA (400 kV)	0%	100%	0%	0%	0	401	391	396
8		मिसा MISA (400 kV)	0%	100%	0%	0%	0	414	394	404
9	पूर्वोत्तर क्षेत्र NER	न्यू मारियानी NEW MARIANI (400 kV)	0%	100%	0%	0%	0	416	393	406
10		न्यू कोहिमा NEW KOHIMA (400 kV)	0%	100%	0%	0%	0	417	381	397
11		पालाताना PALATANA (400 kV)	0%	100%	0%	0%	0	412	401	407
12		पुर्वकंचनबारी PK BARI (400 kV)	0%	100%	0%	0%	0	411	390	404
13		रंगानादी RANGANADI (400 kV)	0%	94%	6%	6%	46	425	402	413
14		सिलचर SILCHAR (400 kV)	0%	100%	0%	0%	0	416	397	408
15		सूर्ययामोनिनगर SURJYAMANINAGAR (400 kV)	0%	100%	0%	0%	0	409	391	403
16		थोबाल THOUBAL (400 kV)	0%	100%	0%	0%	0	412	386	400

All listed stations are 765 kV stations unless otherwise mentioned

*Percentage is calculated w.r.t. Time of one month.

24.ALL TIME HIGHEST

31-10-2023

	Maximum Demand Met during the day (MW)	Demand Met during Evening Peak hrs(MW)	Energy Met (MU)	Hydro Gen. (MU)	Wind Gen. (MU)	Solar Gen. (MU)
NR	81220 04-09-2023	76274 04-09-2023	1796 04-09-2023	443 01-08-2023	86 07-08-2023	147 10-05-2023
WR	74035 01-09-2023	65518 13-10-2023	1618 02-09-2023	167 18-12-2014	273 07-08-2023	70.69 12-05-2023
SR	64314 15-03-2023	52366 18-04-2023	1329 19-04-2023	208 31-08-2018	298 21-07-2023	142.7 21-03-2023
ER	29641 28-07-2023	28579 18-04-2023	639 08-06-2023	157 14-09-2022	-	7 23-03-2023
NER	3712 04-09-2023	3510 12-08-2022	72 15-09-2023	41 29-08-2023	-	2 22-06-2022
All India	239978 01-09-2023	215592 28-08-2023	5224 02-09-2023	877 30-08-2022	611 02-08-2023	351 10-05-2023

Regions	States	Max. Demand Met during the day (MW)		Energy Consumption (MU)	
			As on date		As on date
NR	Punjab	15237	23-06-2023	343.5	24-06-2023
	Haryana	12692	18-08-2023	273.1	18-08-2023
	Rajasthan	17772	02-09-2023	371.6	04-09-2023
	Delhi	7770	29-06-2022	153.5	28-06-2022
	UP	28553	25-07-2023	580.0	03-09-2023
	Uttarakhand	2594	14-06-2022	55.8	17-06-2023
	HP	2071	06-01-2023	40.7	22-08-2023
	J&K(UT) and Ladakh(UT)	3636	29-06-2023	65.4	20-01-2023
	Chandigarh	426	08-07-2021	8.4	08-07-2021
	Railways NR ISTS	-	-	-	-
WR	Chhattisgarh	5832	02-09-2023	133.5	28-08-2023
	Gujarat	24544	01-09-2023	511.6	02-09-2023
	MP	17238	13-01-2023	329.3	10-01-2023
	Maharashtra	28846	14-04-2022	636.1	21-06-2023
	Goa	776	07-06-2023	17.1	08-06-2023
	DD & DNH	1327	17-08-2023	30.9	10-08-2023
	AMNSIL	977	18-08-2021	21.0	31-05-2022
	Balco	-	-	-	-
SR	Andhra Pradesh*	13039	19-10-2023	263.8	16-06-2023
	Telangana*	15497	30-03-2023	303.4	03-03-2023
	Karnataka	16950	25-08-2023	309.5	20-04-2023
	Kerala	5024	18-04-2023	103.3	19-04-2023
	Tamil Nadu	19387	20-04-2023	415.4	20-04-2023
	Pondy	512	17-05-2023	11.6	18-05-2023
ER	Bihar	7578	27-07-2023	161.3	28-07-2023
	DVC	3751	18-04-2023	81.2	22-04-2022
	Jharkhand	1923	16-06-2023	43.3	17-06-2023
	Odisha	7192	19-04-2023	145.5	25-09-2022
	West Bengal	11868	18-04-2023	245.7	18-04-2023
	Sikkim	137	03-02-2022	2.5	28-01-2020
	Railways ER ISTS	-	-	-	-
NER	Arunachal Pradesh	179	16-09-2023	3.2	04-09-2023
	Assam	2498	16-09-2023	50.0	15-09-2023
	Manipur	258	31-01-2022	3.7	10-02-2022
	Meghalaya	415	09-02-2022	7.8	31-01-2022
	Mizoram	157	16-01-2023	2.3	18-01-2023
	Nagaland	179	28-09-2023	3.29	05-09-2023
	Tripura	370	07-06-2023	7.0	06-06-2023
*SR	Andhra Pradesh (Undivided)	13162	23-03-2014	284.8	22-03-2014

25.System Reliability Indices Report for the month of October 2023

Percentage (%) of times ATC was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	0	0.00	0.00
2	ER-NR	0	0.00	0.00
3	Import of NR	0	0.00	0.00
4	NEW-SR	0	0.00	0.00
5	NER Import	0	0.00	0.00

Percentage(%) of times (N-1) Criteria was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	0	0.00	0.00
2	ER-NR	0	0.00	0.00
3	Import of NR	0	0.00	0.00
4	NEW-SR	0	0.00	0.00
4	NER Import	0	0.00	0.00

Remarks: Flows crossing Total Transfer Capability (TTC) on interregional corridors has been worked out as a proxy for (N-1) violation.



POWER SYSTEM OPERATION CORPORATION LIMITED

पावर सिस्टम ऑपरेशन कारपोरेशन लिमिटेड

NATIONAL LOAD DESPATCH CENTRE – राष्ट्रीय भार प्रेषण केन्द्र

First floor, B-9, Qutab Institutional Area,
Katwaria Sarai, New Delhi-110016.
