

संदर्भ संख्या : - GRID-INDIA/NLDC/MR/

दिनांक : 25.09.2023

सेवा में,

वितरण सूची के अनुसार

विषय:- निष्पादन रिपोर्ट – अगस्त 2023

महोदय,

आई०ई०जी०सी०-2010 के प्रावधान के अनुसार, अगस्त 2023 माह की अखिल भारतीय प्रणाली की निष्पादन रिपोर्ट संलग्न है।

धन्यवाद

भवदीय



(सुरजीत बनर्जी)

मुख्य महाप्रबन्धक (प्रणाली प्रचालन)

(रा०भा०प्रे०के०)

संलग्नक : मासिक प्रणाली रिपोर्ट

वितरण सूची Distribution List

- 1 सचिव, के.वि.नि.आ. तीसरा एवं चौथा तल, चंद्रलोक भवन, 36, जनपथ, नई दिल्ली-110001
Secretary, CERC, 3rd & 4th Floor, Chanderlok Building, 36, Janpath, New Delhi-110001
- 2 मुख्य अभियंता (जी एम), के.वि.प्रा., सेवा भवन, आर. के. पुरम, नई दिल्ली-110066
Chief Engineer (GM), CEA, Sewa Bhavan, R.K.Puram, New Delhi-110066
- 3 सदस्य सचिव, उ. क्षेत्र. वि. स., 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली - 110016
Member Secretary, NRPC, 18/A, SJSS Marg, Katwaria Sarai, New Delhi-110016
- 4 सदस्य सचिव, प. क्षेत्र. वि. स., एफ-3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई - 400093
Member Secretary, WRPC, F-3, MIDC Area, Andheri (East), Mumbai-400093
- 5 सदस्य सचिव, द. क्षेत्र. वि. स., 29, रेस कोर्स क्रॉस रोड, बंगलूरु - 560009
Member Secretary, SRPC, 29, Race Course Cross Road, Bangalore-560009
- 6 सदस्य सचिव, पू. क्षेत्र. वि. स., 14, गोल्फ क्लब रोड, कोलकाता - 700033
Member Secretary, ERPC, 14, Golf Club Road, Kolkata-700033
- 7 सदस्य सचिव, उ. पू. क्षेत्र. वि. स., मेघालय राज्य आवासीय वित्त सहकारी समिति लिमिटेड भवन, नॉग्रिम हिल्स, शिलोंग - 793003
Member Secretary, NERPC, Meghalaya State Housing Finance Cooperative Society Ltd. Building, Nongrim Hills, Shillong -793003
- 8 मुख्य अभियंता, राष्ट्रीय विद्युत समिति, एनआरपीसी भवन, तृतीय तल, 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली - 110016
Chief Engineer, National Power Committee, NRPC Building, 3rd floor, 18/A, SJSS Marg, Katwaria Sarai, New Delhi-110016
- 9 कार्यपालक निदेशक, पू. क्षेत्र. भा. प्रे. के., 14, गोल्फ क्लब रोड, कोलकाता - 700033
Executive Director, ERLDC, 14, Golf Club Road, Kolkata-700033
- 10 कार्यपालक निदेशक, प. क्षेत्र. भा. प्रे. के., एफ-3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई - 400093
Executive Director, WRLDC, F-3, MIDC Area, Andheri (East), Mumbai-400093
- 11 कार्यपालक निदेशक, उ. क्षेत्र. भा. प्रे. के., 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली - 110016
Executive Director, NRPC, 18/A, SJSS Marg, Katwaria Sarai, New Delhi-110016
- 12 कार्यपालक निदेशक, द. क्षेत्र. भा. प्रे. के., 29, रेस कोर्स क्रॉस रोड, बंगलूरु - 560009
Executive Director, SRLDC, 29, Race Course Cross Road, Bangalore-560009
- 13 मुख्य महाप्रबंधक, पू. क्षेत्र. भा. प्रे. के., डोंगतिह, लोअर नॉग्रह, लापलंग, शिलोंग- 793006
Chief General Manager, NERLDC, Dongtiah, Lower Nongrah, Laplang, Shillong-793006



ग्रिड-इंडिया
GRID-INDIA

GRID CONTROLLER OF INDIA LIMITED

Formerly Power System Operation Corporation Limited

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड

NATIONAL LOAD DESPATCH CENTRE –राष्ट्रीय भार प्रेषण केन्द्र

मासिक ऑपरेशन रिपोर्ट

Monthly
Operation Report



अगस्त 2023

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड
राष्ट्रीय भार प्रेषण केंद्र, नई दिल्ली

GRID CONTROLLER OF INDIA LIMITED

Formerly Power System Operation Corporation Limited

NATIONAL LOAD DESPATCH CENTRE, NEW DELHI



ग्रिड-इंडिया
GRID-INDIA

माह अगस्त 2023 के लिए प्रचालन निष्पादन रिपोर्ट
OPERATIONAL PERFORMANCE REPORT FOR THE
MONTH OF AUGUST-2023


पृष्ठसूची CONTENTS

1	माह अगस्त 2023 की सारांश रिपोर्ट Summary of report for the month of AUGUST 2023	1-5
2	क्षेत्रवार स्थापित विद्युत क्षमता Region wise Installed Capacity	6
3	राष्ट्रीय स्तर पर सांध्यकालीन शिखर मांगपूर्ति Peak demand met at National level	7-8
4	राष्ट्रीय स्तर पर विद्युत ऊर्जा खपत Energy consumption at National level	9-10
5	फ्रिक्वेंसी रूपरेखा Frequency profile	11-12
6	राष्ट्रीय स्तर पर जल विद्युत ऊर्जा उत्पादन Hydro generation at National level	13-14
7	राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन Wind generation at National level	15
8	राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन Solar generation at National level	16
9	राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग पूर्ति Daily maximum demand met at National level	17
10	31 अगस्त के माँग एवं उत्पादन प्लॉट (अधिकतम माँग पूर्ति) व माँग का डाटा (15 मिनट अंतराल) Demand and generation plots for 21-AUGUST (Max Demand Met) and Demand data (15-minute interval)	18-22
11	ऊर्जा आपूर्ति की वास्तविक स्थिति Actual power supply position	23
12	ऊर्जा आवश्यकता एवं आपूर्ति की पिछले वर्ष माह अगस्त 2022 से तुलना Energy requirement and met comparison with AUGUST 2022	24
13	शिखर माँग आवश्यकता एवं आपूर्ति की पिछले वर्ष माह अगस्त 2022 से तुलना Peak demand requirement and met comparison with AUGUST 2022	25


14	क्षेत्रीय स्तर पर शिड्यूल एवं ड्रावल Schedule & drawal at regional level	26
15	अंतर क्षेत्रीय विनिमय Inter-regional exchanges	27-36
16	अंतर राष्ट्रीय विद्युत विनिमय Inter-national exchanges	37-39
17	एसटीओए (द्विपक्षीय एवं सामूहिक) एवं यू आइ का ब्यौरा Bilateral and collective short-term open access & UI details	40
18	पावर मार्केट की सूचना Power market information	41-44
19	अक्षय ऊर्जा प्रमाण पत्र प्रक्रिया Renewable energy certificate mechanism	45-47
20	मुख्य घटनाएँ एवं डिस्टर्बेंस Important events/disturbances	48-61
21	नए कमीशंड पारेषण तत्व New elements commissioned	62
22	विभव रूपरेखा Voltage profile	63
23	अगस्त 2023 के दौरान रा. भा. प्रे. के. द्वारा निगरानी में तत्वों के आउटेज की सूची List of outage of elements monitored by NLDC for the month of AUGUST 2023	64-76
24	अब तक उच्चतम (मांग व ऊर्जा) आँकड़े : माह अगस्त 2023 तक All Time Highest (Demand & Energy) figures: Till AUGUST 2023	77
25	अगस्त 2023 के लिए सिस्टम रिलाइबिलिटी सूचकांक System Reliability Indices for AUGUST 2023	78

1. SUMMARY OF REPORT FOR THE MONTH OF AUGUST-2023

EVENING PEAK HOUR (at 2000hrs) DEMAND MET AT NATIONAL LEVEL (MW)

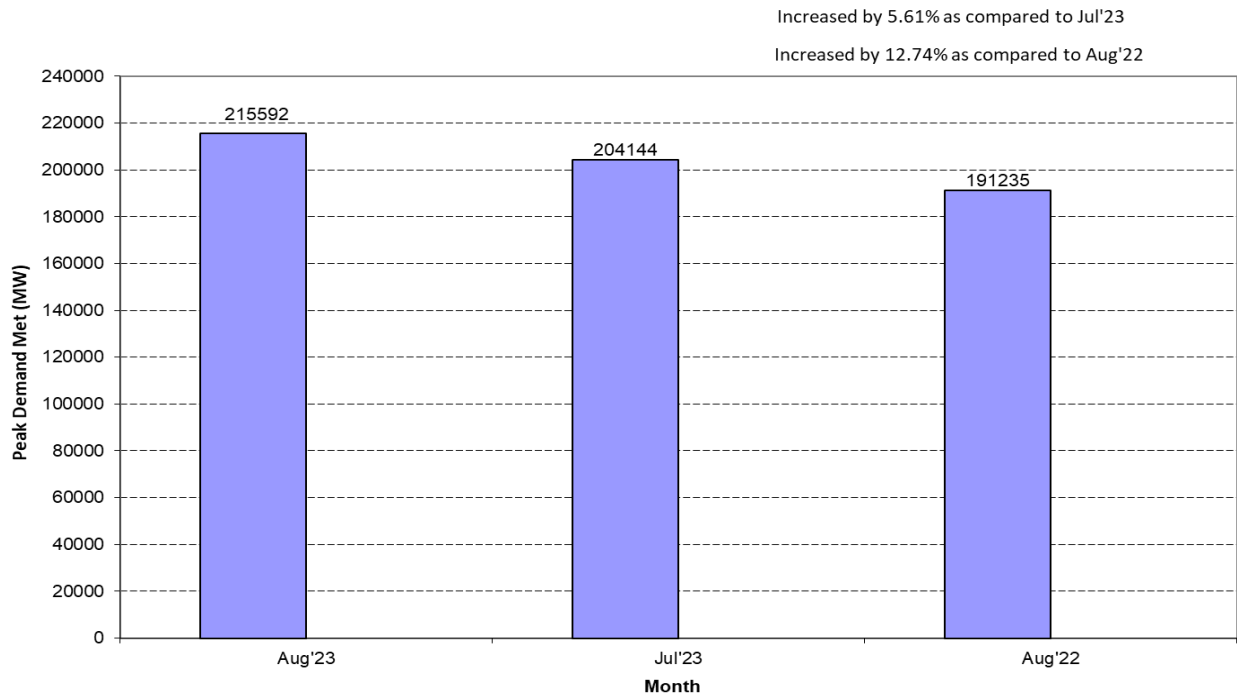


Frequency within IEGC Band

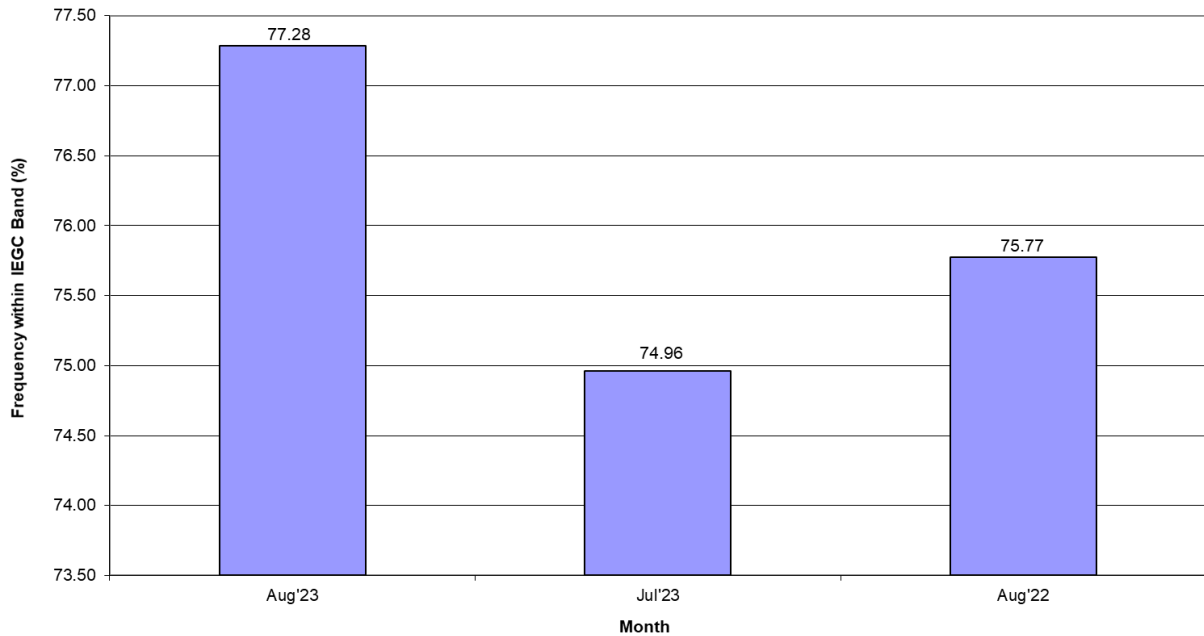

ENERGY MET AT NATIONAL LEVEL (MU)


Increased by 9.11% as compared to Jul'23

Increased by 16.34% as compared to Aug'22

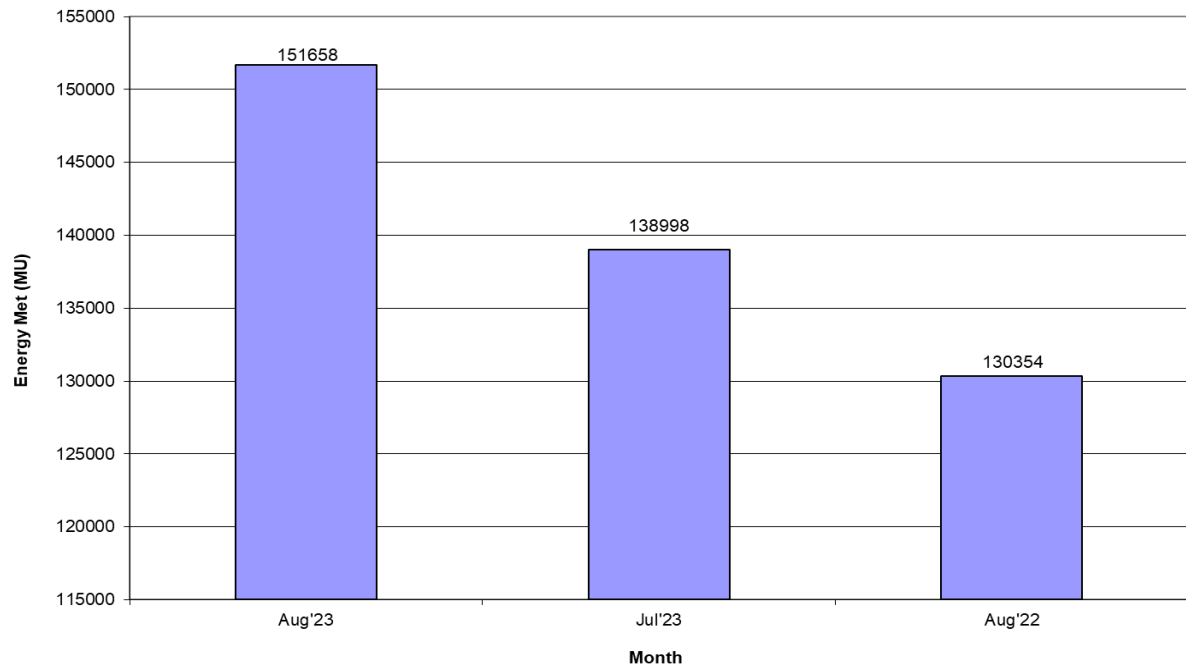

AVERAGE ENERGY MET AT NATIONAL LEVEL (MU/Day)


Increased by 16.34% as compared to Aug'22

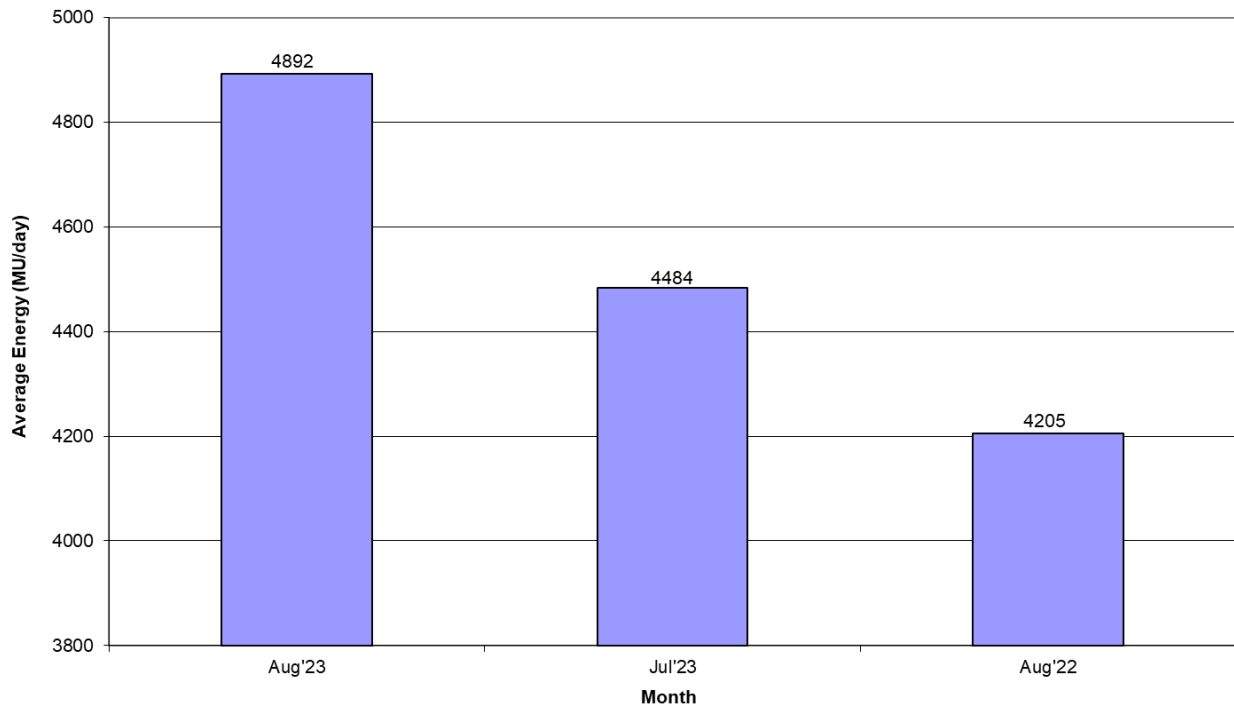

HYDRO GENERATION AT NATIONAL LEVEL (MU)


Increased by 22.65% as compared to Jul'23

Decreased by 3.38% as compared to Aug'22

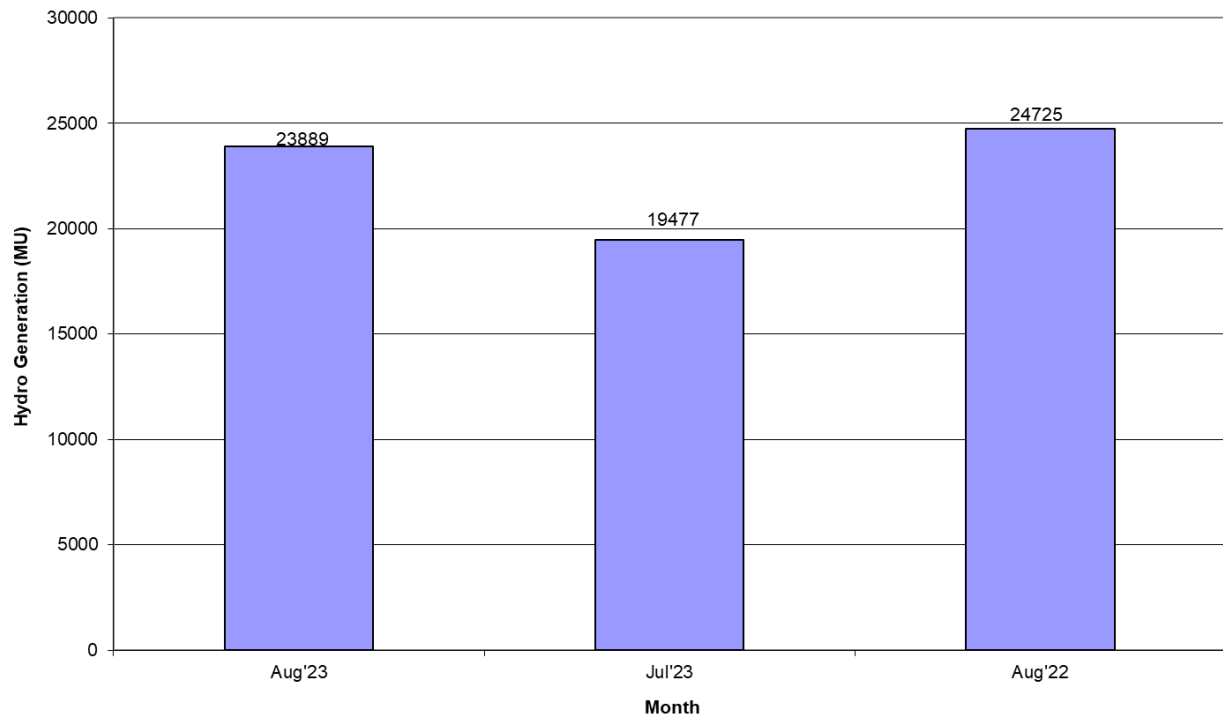


AVERAGE HYDRO GENERATION AT NATIONAL LEVEL (MU/Day)

Decreased by 3.38% as compared to Aug'22

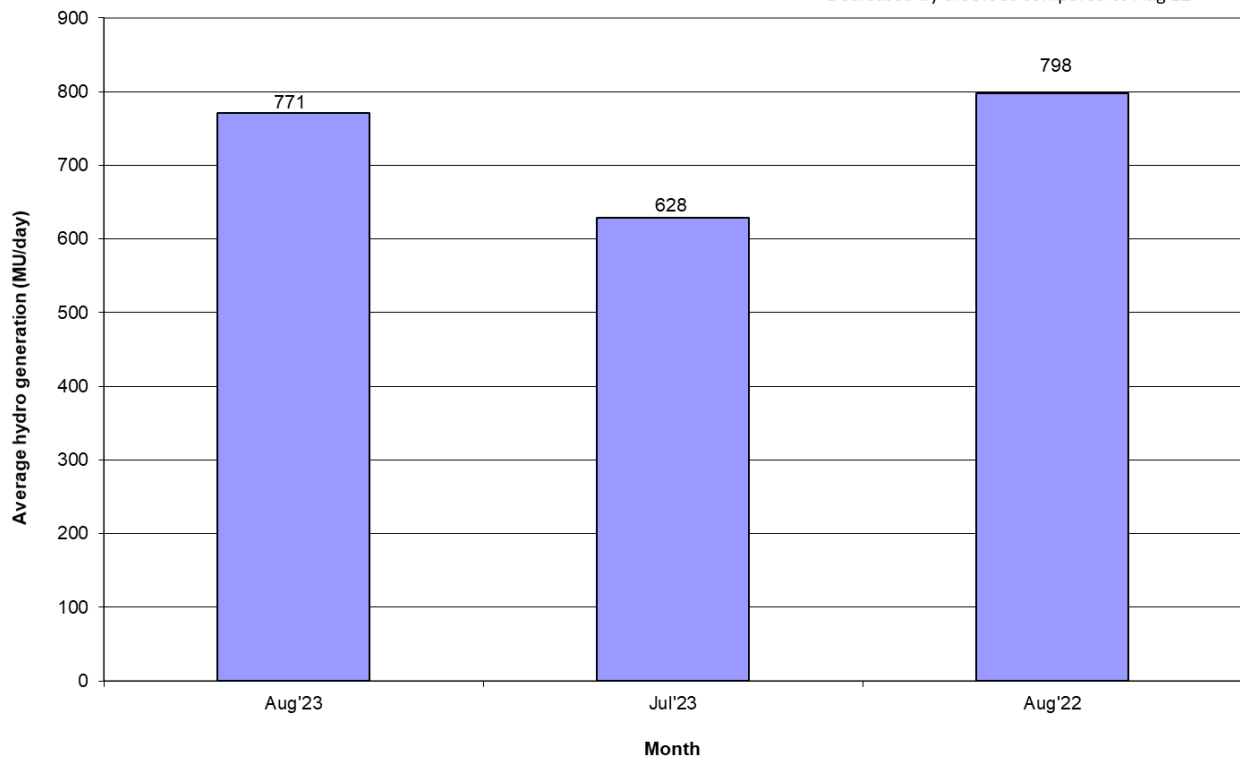


WIND GENERATION AT NATIONAL LEVEL (MU)

Decreased by 0.98% as compared to Jul'23
Increased by 37.44% as compared to Aug'22

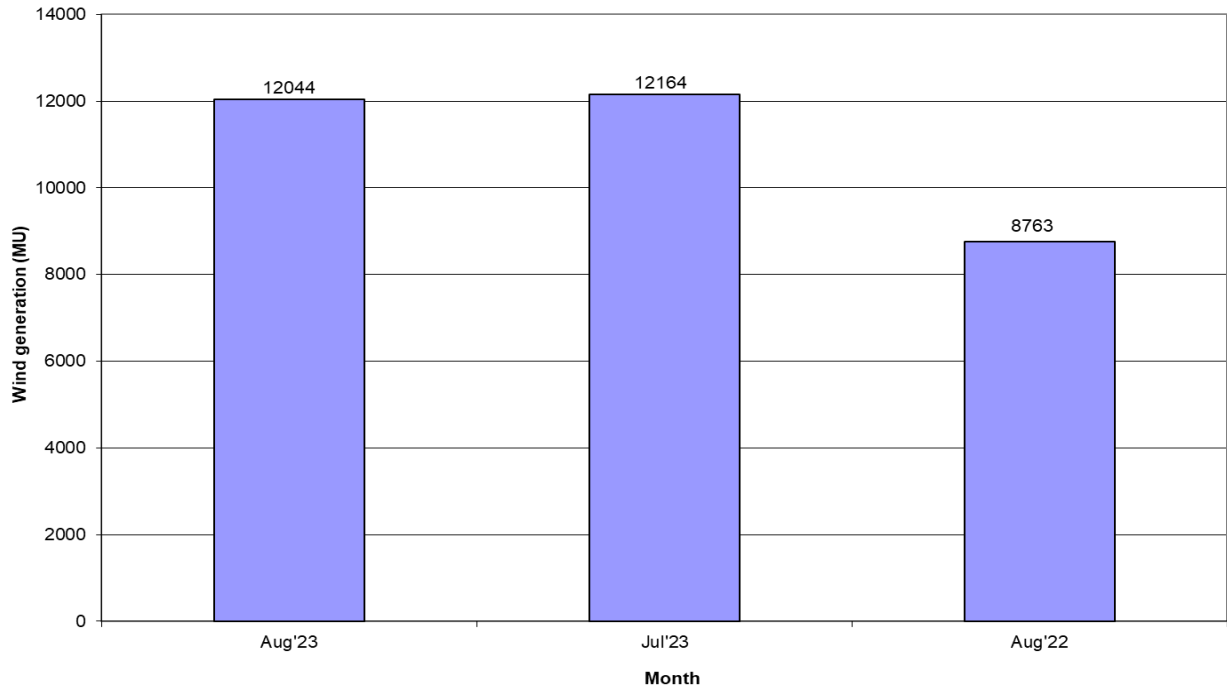

AVERAGE WIND GENERATION AT NATIONAL LEVEL (MU/Day)


Increased by 37.44% as compared to Aug'22

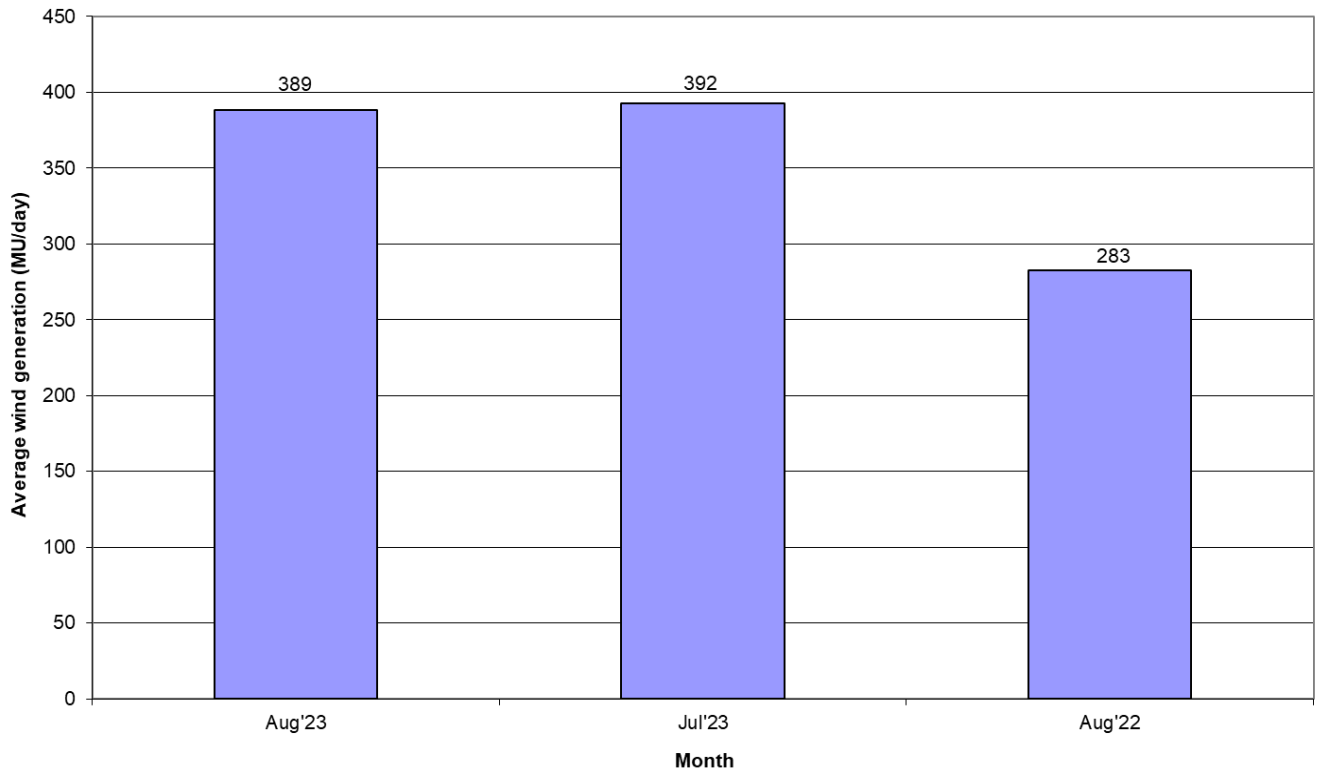

SOLAR GENERATION AT NATIONAL LEVEL (MU)


Increased by 18.29% as compared to Jul'23

Increased by 27.83% as compared to Aug'22

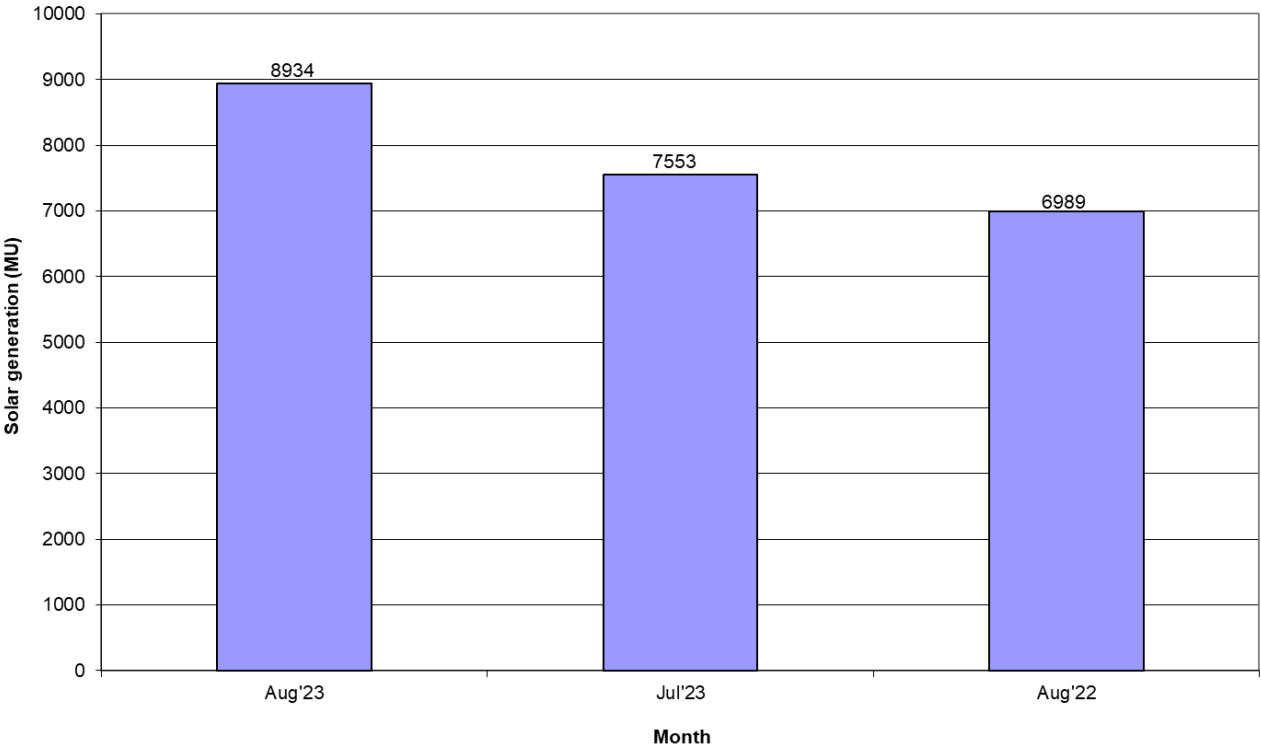

AVERAGE SOLAR GENERATION AT NATIONAL LEVEL (MU/Day)

Increased by 27.83% as compared to Aug'22

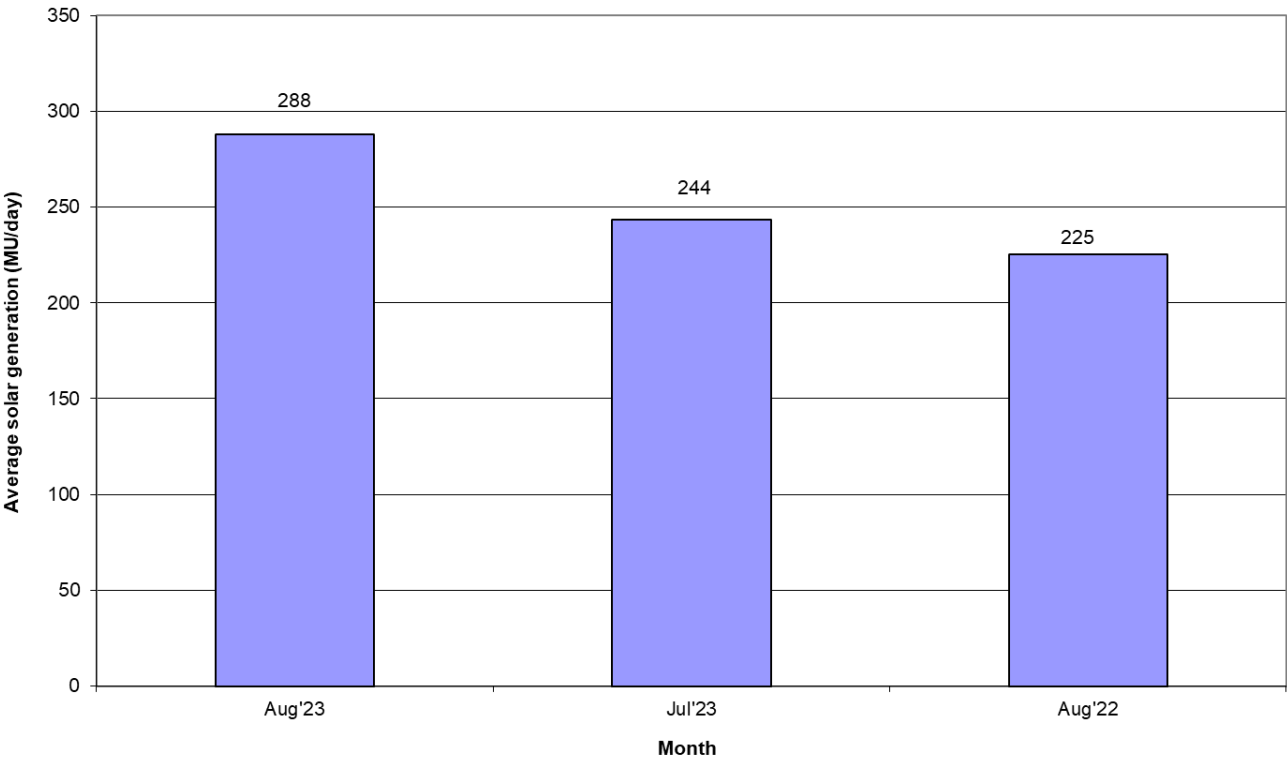

2. ALL INDIA REGIONWISE INSTALLED CAPACITY

As on 31.08.2023
(All figures are in MW)

S No	Region	THERMAL					NUCLEAR	HYDRO	RES @ MNRE	GRAND TOTAL
		COAL	LIGNITE	GAS	DIESEL	TOTAL				
1	NR	55737	1580	5995	0	63312	1620	20752	34501	120184
2	WR	74602	1400	10806	0	86808	2540	7563	42381	139292
3	SR	46858	3640	6492	434	57424	3320	11827	52129	124700
4	ER	28229	0	80	0	28309	0	4764	1891	34964
5	NER	770	0	1665	36	2471	0	1944	574	4989
6	ISLANDS	0	0	0	120	120	0	0	38	158
	ALL INDIA	206195	6620	25038	589	238443	7480	46850	131515	424288

Remarks: Data from CEA website

3. राष्ट्रीय स्तर पर संध्याकालीन शिखर विद्युत मांग पूर्ति
EVENING PEAK HOUR DEMAND MET AT NATIONAL LEVEL

माह: अगस्त 2023 MONTH:- AUG 2023


सभी आंकड़े मेगावाट मे All figures in MW

दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
1-Aug-23	75526	53919	48089	24819	3393	205746
2-Aug-23	72418	52200	49037	23402	3241	200298
3-Aug-23	74152	51272	48882	25738	3360	203404
4-Aug-23	71206	52969	49962	26468	3220	203825
5-Aug-23	71939	53587	49829	26840	3313	205508
6-Aug-23	68983	51945	46645	26061	3030	196664
7-Aug-23	73415	55465	50563	25851	3150	208444
8-Aug-23	74085	57684	45917	25664	3139	206489
9-Aug-23	73165	57711	45302	24927	3076	204181
10-Aug-23	72269	58485	47036	24818	3369	205977
11-Aug-23	73544	60020	45368	25469	3228	207629
12-Aug-23	75301	59790	48267	24065	3165	210588
13-Aug-23	74350	57817	47071	23900	3147	206285
14-Aug-23	72161	59400	48027	25274	3199	208061
15-Aug-23	70836	55476	46636	25915	3201	202064
16-Aug-23	71998	60622	48339	25993	3203	210155
17-Aug-23	72683	60369	49500	24448	3277	210277
18-Aug-23	74841	58062	48995	24787	3181	209866
19-Aug-23	73356	57923	46818	25282	3222	206601
20-Aug-23	73577	55903	43797	25346	3206	201829
21-Aug-23	72602	58599	46350	25300	3130	205981
22-Aug-23	71152	59318	48544	24980	2947	206941
23-Aug-23	67842	60287	50706	25520	3049	207404
24-Aug-23	70680	60623	49775	25017	2917	209012
25-Aug-23	72003	60549	49403	24334	3121	209410
26-Aug-23	71736	60750	48860	25256	2969	209571
27-Aug-23	72643	58527	45434	26691	2834	206129
28-Aug-23	73922	62501	48681	27419	3069	215592
29-Aug-23	72012	64447	46845	26630	2998	212932
30-Aug-23	71295	59337	45817	26601	3002	206052
31-Aug-23	72504	64346	45977	26563	3089	212479
उच्चतम MAXIMUM	75526	64447	50706	27419	3393	215592
निम्नतम MINIMUM	67842	51272	43797	23402	2834	196664
औसत AVERAGE	72522	58061	47757	25464	3143	206948
अब तक का उच्चतम All Time Max.	76072	64447	52366	28579	3510	215592
दिनांक Date	23.06.23	29.08.23	18.04.23	18.04.23	12.08.22	28.08.23

नोट : सभी आंकड़े 2000 बजे की मांगपूर्ति पर आधारित है ।

Note: The above figures correspond to value at 2000 Hrs

EVENING PEAK HOUR DEMAND(at 2000hrs)MET DURING THE MONTH OF AUGUST 2023

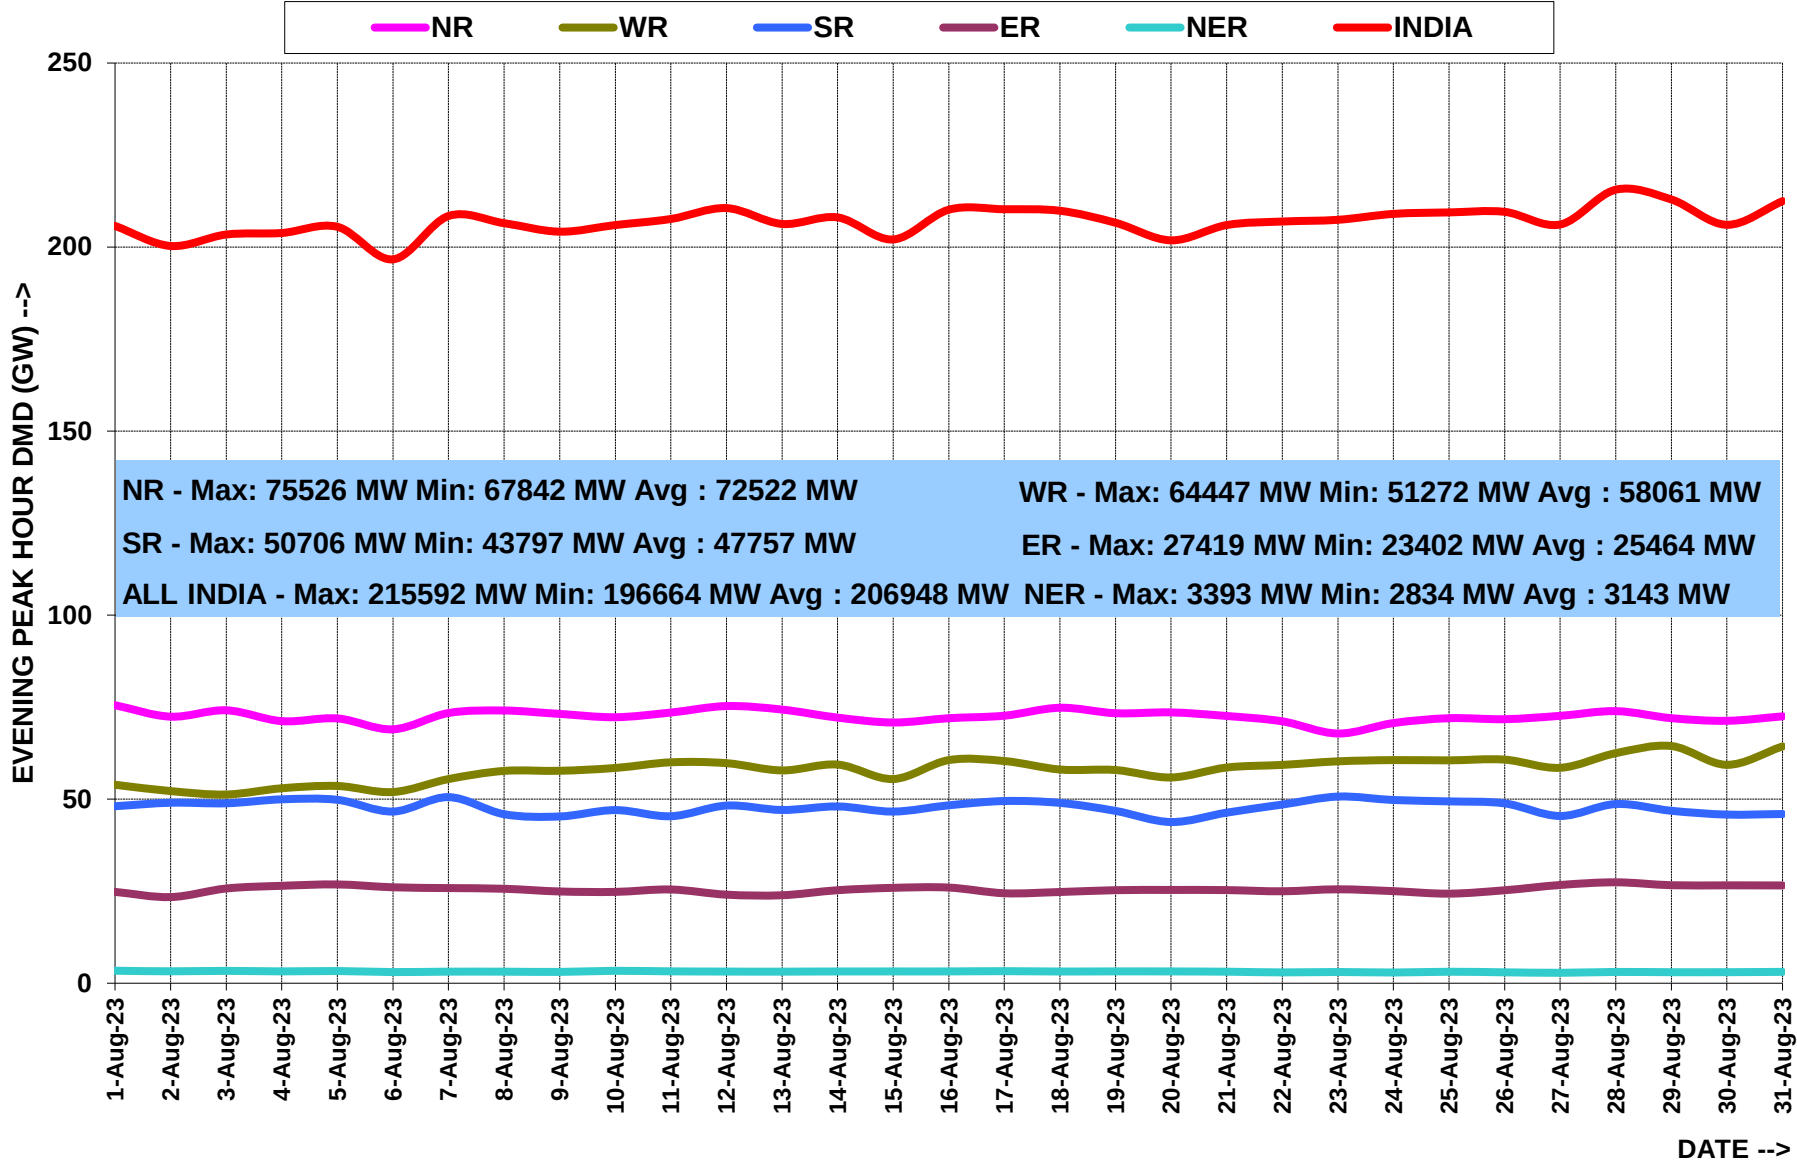


4. राष्ट्रीय स्तर पर विद्युत ऊर्जा आपूर्ति ENERGY MET AT NATIONAL LEVEL

माह: अगस्त 2023 MONTH:- AUG 2023

सभी आंकड़े मिलियन यूनिट में All figures in MU

दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Aug-23	1684	1257	1104	584	70	4700
02-Aug-23	1678	1230	1127	504	68	4607
03-Aug-23	1640	1197	1147	558	65	4606
04-Aug-23	1605	1215	1186	588	64	4658
05-Aug-23	1603	1235	1192	581	64	4675
06-Aug-23	1555	1212	1147	559	61	4534
07-Aug-23	1587	1294	1213	533	60	4687
08-Aug-23	1650	1350	1224	529	62	4815
09-Aug-23	1676	1371	1220	532	63	4862
10-Aug-23	1678	1395	1205	564	65	4907
11-Aug-23	1707	1421	1205	579	66	4978
12-Aug-23	1746	1437	1183	571	65	5001
13-Aug-23	1715	1412	1154	554	61	4896
14-Aug-23	1691	1445	1200	560	64	4960
15-Aug-23	1670	1371	1148	574	64	4827
16-Aug-23	1703	1461	1212	591	63	5031
17-Aug-23	1754	1484	1251	567	66	5122
18-Aug-23	1777	1449	1237	568	68	5099
19-Aug-23	1750	1415	1150	579	66	4960
20-Aug-23	1715	1363	1103	579	65	4824
21-Aug-23	1720	1409	1185	589	64	4967
22-Aug-23	1722	1445	1218	586	60	5032
23-Aug-23	1558	1440	1269	570	61	4899
24-Aug-23	1557	1459	1278	547	61	4902
25-Aug-23	1584	1462	1299	533	62	4940
26-Aug-23	1601	1486	1261	531	59	4939
27-Aug-23	1617	1435	1196	568	56	4873
28-Aug-23	1627	1516	1246	604	57	5050
29-Aug-23	1661	1535	1248	603	62	5110
30-Aug-23	1668	1497	1234	609	65	5073
31-Aug-23	1691	1530	1216	622	67	5125
कुल TOTAL	51588	43228	37259	17619	1964	151658
उच्चतम MAXIMUM	1777	1535	1299	622	70	5125
निम्नतम MINIMUM	1555	1197	1103	504	56	4534
औसत AVERAGE	1664	1394	1202	568	63	4892
संचयी 2023-24 Cumulative 2023-24	215381	210873	175304	86393	8758	696710
अब तक का उच्चतम All Time Max.	1777	1539	1329	639	70	5125
दिनांक Date	18.08.23	18.04.23	19.04.23	08.06.23	01.08.23	31.08.23

ENERGY MET DURING THE MONTH OF AUGUST' 2023

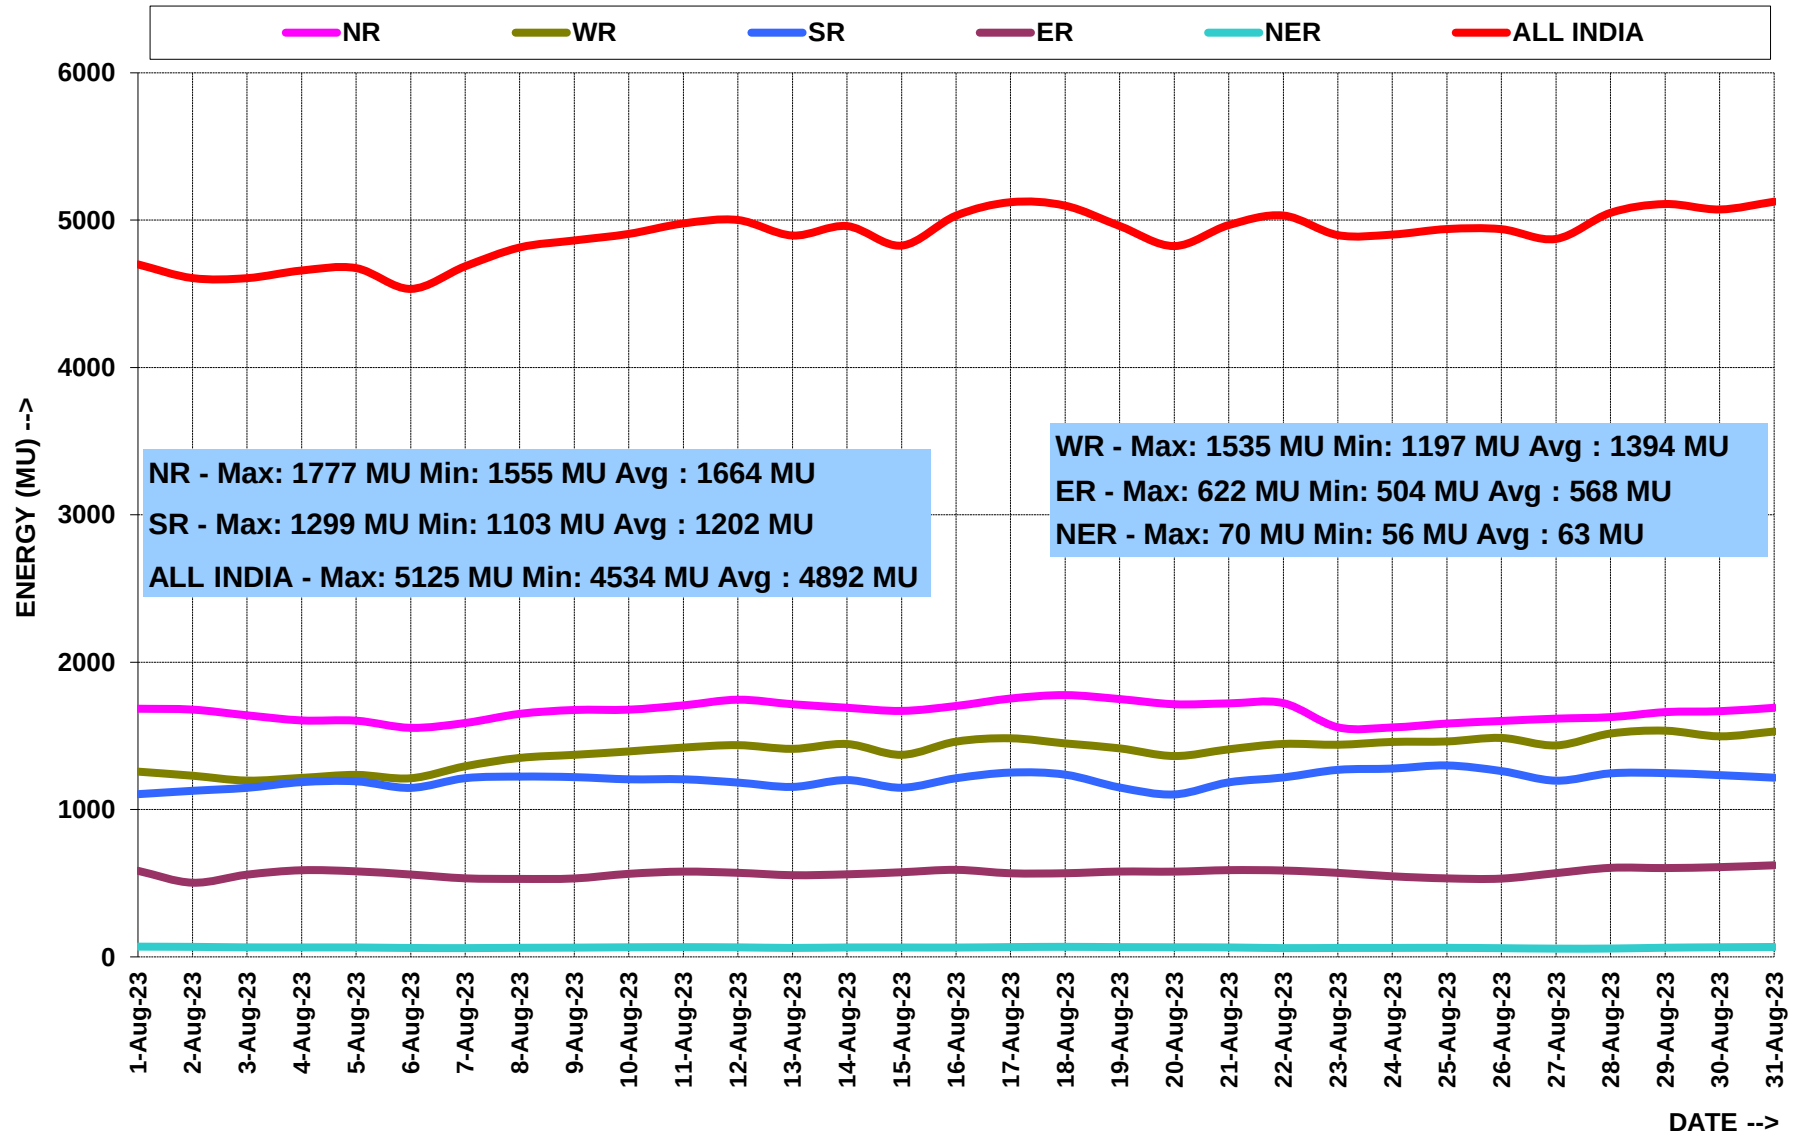

5. वर्ष 2023-24 के लिए आवृत्ति रूपरेखा FREQUENCY PROFILE FOR YEAR 2023-24

राष्ट्रीय ग्रीड NATIONAL GRID								
फ्रिक्वेंसी रूपरेखा (Hz)			<49.9	49.9-50.05	>50.05	उच्चतम फ्रिक्वेंसी	निम्नतम फ्रिक्वेंसी	औसत फ्रिक्वेंसी
% समय	Apr-23	All India Grid	10.54	67.90	21.56	50.33	49.49	49.99
	May-23	All India Grid	9.83	68.48	21.69	50.43	49.48	49.99
	Jun-23	All India Grid	6.47	67.82	25.71	50.41	49.51	50.01
	Jul-23	All India Grid	4.60	74.96	20.44	50.23	49.76	50.01
	Aug-23	All India Grid	7.08	77.28	15.63	50.20	49.74	50.00
	2023-24 (upto Aug)	All India Grid	7.70	71.33	20.97	50.43	49.48	50.00

5.1 अगस्त 2023 के लिए आवृत्ति रूपरेखा FREQUENCY PROFILE FOR AUGUST 2023

फ्रिक्वेंसी रूपरेखा (Hz)		<49.9	49.9-50.05	>50.05	उच्चतम फ्रिक्वेंसी	निम्नतम फ्रिक्वेंसी	औसत फ्रिक्वेंसी	एफ़.वी.आई.
% समय	01-Aug-23	2.59	74.59	22.81	50.21	49.75	50.01	0.03
	02-Aug-23	2.69	82.63	14.69	50.29	49.81	50.00	0.03
	03-Aug-23	5.14	84.95	9.91	50.13	49.80	49.99	0.02
	04-Aug-23	6.17	80.07	13.76	50.20	49.70	49.99	0.04
	05-Aug-23	6.32	83.22	10.46	50.22	49.75	49.99	0.03
	06-Aug-23	1.19	79.44	19.36	50.20	49.81	50.01	0.03
	07-Aug-23	6.20	79.32	14.48	50.15	49.77	49.99	0.03
	08-Aug-23	13.61	75.22	11.17	50.19	49.55	49.97	0.08
	09-Aug-23	22.93	68.63	8.44	50.18	49.51	49.95	0.12
	10-Aug-23	9.48	79.24	11.28	50.17	49.65	49.99	0.04
	11-Aug-23	4.16	76.86	18.98	50.24	49.77	50.01	0.03
	12-Aug-23	1.63	76.25	22.12	50.19	49.83	50.02	0.02
	13-Aug-23	1.78	87.08	11.13	50.16	49.85	50.00	0.02
	14-Aug-23	6.70	80.75	12.55	50.26	49.80	49.99	0.04
	15-Aug-23	7.87	82.85	9.28	50.14	49.77	49.98	0.03
	16-Aug-23	3.61	79.81	16.57	50.24	49.79	50.01	0.03
	17-Aug-23	1.26	72.05	26.69	50.19	49.84	50.03	0.03
	18-Aug-23	1.67	68.99	29.34	50.24	49.77	50.03	0.03
	19-Aug-23	3.24	69.64	27.12	50.24	49.81	50.02	0.03
	20-Aug-23	4.75	82.64	12.62	50.20	49.74	50.00	0.03
	21-Aug-23	18.06	72.88	9.06	50.17	49.58	49.96	0.08
	22-Aug-23	6.47	74.41	19.12	50.20	49.68	50.00	0.04
	23-Aug-23	1.75	67.64	30.61	50.28	49.80	50.03	0.03
	24-Aug-23	2.04	81.86	16.10	50.29	49.81	50.01	0.03
	25-Aug-23	5.29	82.35	12.36	50.18	49.81	50.00	0.03
	26-Aug-23	2.36	83.10	14.54	50.25	49.84	50.00	0.03
	27-Aug-23	0.42	83.44	16.15	50.18	49.85	50.01	0.02
	28-Aug-23	1.88	76.32	21.81	50.27	49.83	50.02	0.04
	29-Aug-23	18.06	73.84	8.10	50.15	49.51	49.96	0.10
	30-Aug-23	25.10	66.06	8.83	50.14	49.53	49.95	0.13
	31-Aug-23	25.16	69.68	5.16	50.13	49.51	49.94	0.12


6.राष्ट्रीय स्तर पर जल विद्युत उत्पादन
HYDRO GENERATION AT NATIONAL LEVEL

माह: अगस्त 2023 MONTH:- AUG 2023

सभी आंकड़े मिलियन यूनिट में All figures in MU

दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Aug-23	443	72	77	132	32	756
02-Aug-23	439	78	73	116	30	736
03-Aug-23	436	86	74	138	33	767
04-Aug-23	434	95	89	135	33	786
05-Aug-23	428	96	86	137	33	779
06-Aug-23	413	97	69	136	33	749
07-Aug-23	417	104	107	140	33	800
08-Aug-23	424	107	118	140	36	824
09-Aug-23	421	109	113	139	34	816
10-Aug-23	417	111	108	139	35	810
11-Aug-23	421	115	110	126	35	807
12-Aug-23	426	100	84	133	32	776
13-Aug-23	421	99	68	132	36	756
14-Aug-23	396	102	90	133	37	759
15-Aug-23	406	99	95	142	34	775
16-Aug-23	407	113	96	143	34	793
17-Aug-23	410	120	84	137	33	784
18-Aug-23	405	121	75	135	33	769
19-Aug-23	413	100	69	141	32	755
20-Aug-23	413	105	65	138	33	754
21-Aug-23	415	111	114	138	33	813
22-Aug-23	417	118	106	141	36	818
23-Aug-23	389	108	80	137	39	752
24-Aug-23	387	102	79	133	39	739
25-Aug-23	387	107	90	132	38	754
26-Aug-23	376	104	89	132	37	738
27-Aug-23	373	99	67	134	41	713
28-Aug-23	366	103	73	136	40	717
29-Aug-23	371	119	102	138	41	769
30-Aug-23	363	110	119	138	40	770
31-Aug-23	360	112	112	135	38	757
कुल TOTAL	12593	3219	2780	4206	1091	23889
उच्चतम MAXIMUM	443	121	119	143	41	824
निम्नतम MINIMUM	360	72	65	116	30	713
औसत AVERAGE	406	104	90	136	35	771
संचयी 2023-24 Cumulative 2023-24	44697	7338	10439	13936	3330	79740
अब तक का उच्चतम All Time Max.	443	167	208	157	41	877
दिनांक Date	01.08.23	18.12.14	31.08.18	14.09.22	29.08.23	30.08.22

HYDRO ENERGY DURING THE MONTH OF AUGUST' 2023

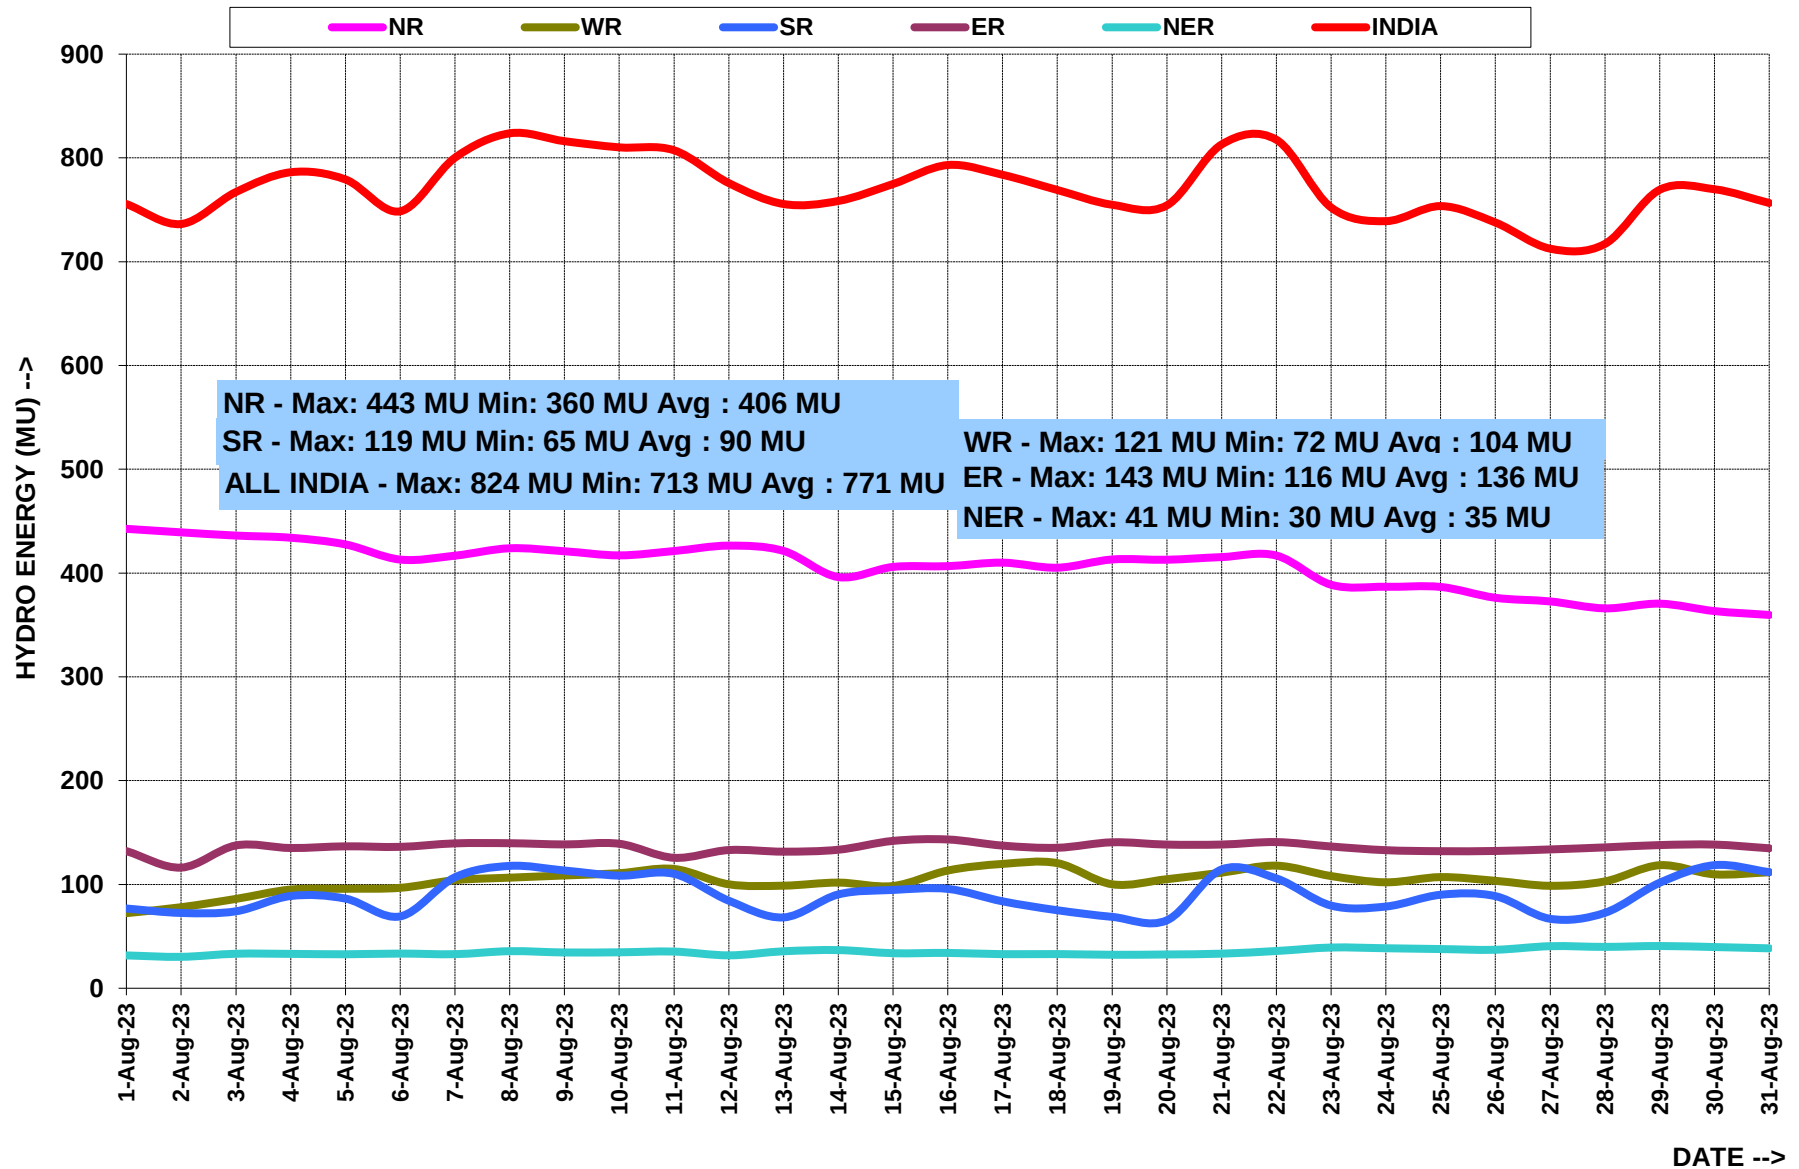

7. राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन
WIND GENERATION AT NATIONAL LEVEL
 माह: अगस्त 2023 MONTH:- AUG 2023

सभी आंकड़े मिलियन यूनिट में All figures in MU

दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Aug-23	50	253	283	-----	-----	587
02-Aug-23	64	270	276	-----	-----	611
03-Aug-23	44	252	275	-----	-----	571
04-Aug-23	31	191	235	-----	-----	457
05-Aug-23	34	181	210	-----	-----	425
06-Aug-23	72	244	207	-----	-----	523
07-Aug-23	86	273	189	-----	-----	547
08-Aug-23	73	235	158	-----	-----	466
09-Aug-23	66	207	108	-----	-----	381
10-Aug-23	47	200	78	-----	-----	325
11-Aug-23	37	170	59	-----	-----	265
12-Aug-23	54	216	134	-----	-----	404
13-Aug-23	74	242	148	-----	-----	464
14-Aug-23	53	205	127	-----	-----	384
15-Aug-23	15	139	129	-----	-----	283
16-Aug-23	24	144	129	-----	-----	296
17-Aug-23	39	187	193	-----	-----	420
18-Aug-23	28	189	220	-----	-----	437
19-Aug-23	13	171	227	-----	-----	412
20-Aug-23	9	138	178	-----	-----	325
21-Aug-23	8	124	105	-----	-----	237
22-Aug-23	42	149	83	-----	-----	274
23-Aug-23	85	212	116	-----	-----	414
24-Aug-23	71	212	156	-----	-----	439
25-Aug-23	63	193	135	-----	-----	391
26-Aug-23	46	172	118	-----	-----	336
27-Aug-23	54	188	134	-----	-----	376
28-Aug-23	70	219	158	-----	-----	447
29-Aug-23	35	131	107	-----	-----	273
30-Aug-23	16	71	60	-----	-----	147
31-Aug-23	21	52	54	-----	-----	127
कुल TOTAL	1425	5830	4790	-----	-----	12044
उच्चतम MAXIMUM	86	273	283	-----	-----	611
निम्नतम MINIMUM	8	52	54	-----	-----	127
औसत AVERAGE	46	188	155	-----	-----	389
संचयी 2023-24 Cumulative 2023-24	4864	20890	20776	-----	-----	46529
अब तक का उच्चतम All Time Max.	86	273	298	-----	-----	611
दिनांक Date	07.08.23	07.08.23	21.07.23	-----	-----	02.08.23

*Source: As reported by SLDCs. Limited visibility of embedded wind generator data.

8. राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन
SOLAR GENERATION AT NATIONAL LEVEL

माह: अगस्त 2023 MONTH:- AUG 2023

सभी आंकड़े मिलियन यूनिट में All figures in MU

दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Aug-23	131	38	106	1.3	1.3	278
02-Aug-23	117	32	101	1.1	1.0	252
03-Aug-23	115	28	101	1.5	0.8	246
04-Aug-23	119	34	115	2.0	0.9	271
05-Aug-23	124	40	129	4.7	0.8	298
06-Aug-23	125	40	126	4.3	0.6	296
07-Aug-23	128	37	113	1.6	0.8	281
08-Aug-23	125	40	103	2.0	0.9	271
09-Aug-23	122	41	115	2.2	1.0	281
10-Aug-23	122	47	108	2.5	0.8	281
11-Aug-23	122	48	117	2.3	0.9	290
12-Aug-23	133	48	114	2.1	0.6	297
13-Aug-23	127	41	124	2.3	0.7	295
14-Aug-23	120	37	114	2.3	1.0	275
15-Aug-23	106	46	124	2.6	1.0	281
16-Aug-23	127	50	125	2.3	0.8	306
17-Aug-23	123	50	121	1.3	1.3	296
18-Aug-23	129	45	101	1.6	1.0	278
19-Aug-23	123	39	89	2.4	0.7	254
20-Aug-23	104	30	119	2.3	1.0	257
21-Aug-23	130	39	128	5.2	0.6	302
22-Aug-23	133	43	117	4.9	0.3	298
23-Aug-23	125	41	115	2.2	0.8	284
24-Aug-23	122	44	124	1.5	0.6	292
25-Aug-23	125	49	125	1.6	0.8	301
26-Aug-23	123	53	113	2.4	0.5	291
27-Aug-23	126	56	124	2.2	0.5	309
28-Aug-23	131	56	128	2.8	0.7	319
29-Aug-23	128	56	123	5.8	1.1	314
30-Aug-23	138	58	115	5.9	1.5	319
31-Aug-23	141	60	116	2.5	1.3	320
कुल TOTAL	3863	1369	3594	82	27	8934
उच्चतम MAXIMUM	141	60	129	6	2	320
निम्नतम MINIMUM	104	28	89	1	0	246
औसत AVERAGE	125	44	116	3	1	288
संचयी 2023-24 Cumulative 2023-24	15675	6816	14291	418	115.8	37315
अब तक का उच्चतम All Time Max.	147	71	143	6.7	2.4	351
दिनांक Date	10.05.23	12.05.23	21.03.23	23.03.23	22.06.22	10.05.23

*Source: RLDCs for solar connected to ISTS; SLDCs for embedded solar. Limited visibility of embedded solar data.

9. राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग पूर्ति
DAILY MAXIMUM DEMAND MET AT NATIONAL LEVEL

माह: अगस्त 2023 MONTH:- AUG 2023

सभी आंकड़े मेगावाट में All figures in MW

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL	विभिन्नता फ़ैक्टर Diversity Factor*
01-Aug-23	76438	56283	51185	28282	3392	206579	1.044
02-Aug-23	74638	54623	53049	24825	3257	202247	1.040
03-Aug-23	75245	53886	54431	27865	3398	205393	1.046
04-Aug-23	72355	55371	57212	27845	3271	206265	1.047
05-Aug-23	72353	55849	56403	27842	3357	207385	1.041
06-Aug-23	71452	54214	54523	27495	3076	198671	1.061
07-Aug-23	73586	58394	58606	26231	3230	209855	1.049
08-Aug-23	74123	60042	59440	26093	3257	215457	1.035
09-Aug-23	74523	61734	60570	26715	3328	220957	1.027
10-Aug-23	76473	62975	59445	28714	3365	224840	1.027
11-Aug-23	78434	63827	60531	28066	3387	228963	1.023
12-Aug-23	78884	64004	56025	27534	3238	225637	1.018
13-Aug-23	76915	63260	54699	27103	3148	219375	1.026
14-Aug-23	76709	66304	59272	26520	3343	227645	1.020
15-Aug-23	73805	60182	54781	26706	3210	214418	1.020
16-Aug-23	78748	67368	60107	26370	3457	233032	1.013
17-Aug-23	80056	68677	61020	26003	3503	234058	1.022
18-Aug-23	81097	66284	60551	26109	3342	231611	1.025
19-Aug-23	77906	65107	54621	26026	3239	220724	1.028
20-Aug-23	75993	62310	52277	26896	3306	214773	1.028
21-Aug-23	78456	64506	59217	26650	3356	226242	1.026
22-Aug-23	78098	66001	60984	26524	3089	230041	1.020
23-Aug-23	68960	64638	61084	26488	3294	216520	1.037
24-Aug-23	70670	65322	61849	25548	3184	218998	1.035
25-Aug-23	72829	66558	64098	25037	3176	223936	1.035
26-Aug-23	73672	67238	61418	25748	3098	224108	1.032
27-Aug-23	73211	65882	57412	27626	2907	217926	1.042
28-Aug-23	75275	69312	60783	28219	3218	229194	1.033
29-Aug-23	75860	71012	61383	27674	3395	233768	1.024
30-Aug-23	74657	68090	62678	28176	3216	233289	1.015
31-Aug-23	76022	71708	61657	27795	3302	236598	1.016
उच्चतम MAXIMUM	81097	71708	64098	28714	3503	236598	1.061
निम्नतम MINIMUM	68960	53886	51185	24825	2907	198671	1.013
औसत AVERAGE	75401	63257	58429	26927	3269	220597	1.031
अब तक का उच्चतम All Time Max.	81097	71708	64314	29641	3596	236598	
दिनांक Date	18.08.23	31.08.23	15.03.23	28.07.23	17.08.22	31.08.23	

* Diversity factor = (Sum of regional max demands) / All India max demand

नोट : यह आंकड़े एनएलडीसी स्काडा प्रणाली में दर्ज दैनिक अधिकतम मांगपूर्ति दर्शाते हैं ।

Note: The above figures denote daily maximum demand met recorded in NLDC SCADA.

11. ACTUAL POWER SUPPLY POSITION - AUGUST 2023

REGION	STATE	Requirement/Availability in MU/DAY			Requirement/Availability in MU				Peak Demand/Peak Met in MW			
		Requirement	Energy met	Surplus(+)/ Deficit(-)	Requirement	Energy met	Surplus(+)/ Deficit(-)	% Shortage	Requirement	Peak Demand Met	Surplus(+)/ Deficit(-)	% Shortage
NR	Chandigarh	7	7	0.0	213	213	0	0.0	411	411	0	0.0
	Delhi	131	131	0.0	4076	4076	0	0.0	7437	7437	0	0.0
	Haryana	248	245	-2.9	7680	7592	-89	-1.2	12844	12844	0	0.0
	Himachal Pradesh	34	34	-0.1	1059	1056	-3	-0.3	1724	1724	0	0.0
	J&K(UT) and Ladakh(UT)	52	51	-0.6	1606	1585	-20	-1.2	2735	2735	0	0.0
	Punjab	314	314	0.0	9719	9719	0	0.0	15220	15220	0	0.0
	Rajasthan	332	328	-3.7	10286	10173	-114	-1.1	17420	17266	-154	-0.9
	Uttar Pradesh	509	506	-3.6	15784	15672	-112	-0.7	27689	27689	0	0.0
	Uttarakhand	46	45	-0.6	1420	1401	-20	-1.4	2303	2228	-75	-3.3
	Railway	3	3	0.0	107	107	0	0.0	201	201	0	0.0
	NFL	0	0	0.0	2	2	0	0.0	5	5	0	0.0
	TOTAL	1676	1664	-11.5	51953	51596	-357	-0.7	80980	80548	-432	-0.5
WR	Gujarat	416	416	-0.1	12895	12893	-2	0.0	23012	22972	-40	-0.2
	Madhya Pradesh	253	253	0.0	7836	7836	0	0.0	13624	13605	-19	-0.1
	Chhattisgarh	117	116	-0.6	3612	3592	-20	-0.5	5827	5827	0	0.0
	Maharashtra	540	537	-3.4	16737	16632	-106	-0.6	31178	27996	-3182	-10.2
	Goa	13	13	0.0	409	409	0	0.0	667	666	-1	-0.1
	DNHDDPDCL	30	30	0.0	916	916	0	0.0	1327	1327	0	0.0
	AMNSIL	19	19	0.0	587	587	0	0.0	942	942	0	0.0
	BALCO*	12	12	0.0	385	385	0	0.0	522	522	0	0.0
	TOTAL	1399	1395	-4.1	43377	43250	-128	-0.3	76050	72556	-3494	-4.6
SR	Andhra Pradesh	233	231	-1.2	7212	7175	-37	-0.5	12508	12508	0	0.0
	Telangana	256	255	-1.4	7933	7890	-44	-0.6	14835	14816	-19	-0.1
	Karnataka	258	257	-1.4	7997	7954	-44	-0.5	16968	16950	-19	-0.1
	Kerala	84	83	-0.5	2598	2584	-14	-0.5	4366	4366	0	0.0
	Tamil Nadu	368	366	-1.8	11406	11349	-57	-0.5	18252	18252	0	0.0
	Puducherry	10	10	-0.1	312	311	-2	-0.5	492	492	0	0.0
	TOTAL	1208	1202	-6.4	37460	37263	-197	-0.5	64103	64103	0	0.0
ER	Bihar	139	137	-1.9	4299	4239	-60	-1.4	7258	7185	-73	-1.0
	Jharkhand	39	37	-1.6	1203	1153	-50	-4.1	1827	1827	0	0.0
	DVC	74	74	0.0	2299	2299	0	0.0	3673	3673	0	0.0
	Odisha	117	117	-0.1	3627	3625	-2	-0.1	6816	6816	0	0.0
	West Bengal	202	202	0.0	6263	6263	0	0.0	10642	10642	0	0.0
	Sikkim	1	1	0.0	33	33	0	0.0	92	92	0	0.0
	Railways_ER ISTS**	0	0	0.0	5	5	0	0.0	31	31	0	0.0
	TOTAL	572	568	-3.6	17729	17617	-112	-0.6	29958	28711	-1247	-4.2
NER	Arunachal Pradesh	3	3	0.0	83	83	0	0.0	155	155	0	0.0
	Assam	44	43	-1.0	1352	1320	-32	-2.4	2353	2353	0	0.0
	Manipur	3	3	0.0	81	81	0	0.0	209	209	0	0.0
	Meghalaya	6	5	-0.5	175	160	-15	-8.6	322	322	0	0.0
	Mizoram	2	2	0.0	53	53	0	0.0	126	126	0	0.0
	Nagaland	3	3	0.0	89	89	0	0.0	174	174	0	0.0
	Tripura	5	5	0.0	168	168	0	0.0	330	330	0	0.0
	TOTAL	65	63	-1.5	2001	1954	-47	-2.4	3501	3501	0	0.0
ALL INDIA		4920	4893	-27.1	152520	151679	-841	-0.6				

* BALCO has been added as new entity wef 20.12.2022

** Railways_ER ISTS has been added as new entity wef 29.04.2023

NOTE: BASED ON THE DATA FURNISHED BY ENTITIES ON DAILY BASIS

12. ENERGY COMPARISON OF AUGUST 2023 vs AUGUST 2022

REGION	STATE	Energy Requirement (MU)					Energy Met (MU)				
		Aug-22	Aug-23	Difference	% Change	Average MU/day for Aug-23	Aug-22	Aug-23	Difference	% Change	Average MU/day for Aug-23
NR	Chandigarh	198	213	16	8	7	198	213	16	8	7
	Delhi	3573	4076	502	14	131	3572	4076	503	14	131
	Haryana	6532	7680	1148	18	248	6500	7592	1092	17	245
	Himachal Pradesh	955	1059	103	11	34	949	1056	107	11	34
	J&K(UT) and Ladakh(UT)	1546	1606	60	4	52	1537	1585	49	3	51
	Punjab	8724	9719	995	11	314	8724	9719	995	11	314
	Rajasthan	7140	10286	3147	44	332	7095	10173	3078	43	328
	Uttar Pradesh	14327	15784	1457	10	509	14250	15672	1422	10	506
	Uttarakhand	1400	1420	21	1	46	1385	1401	16	1	45
	Railway/NFL	87	109	22	25	4	87	109	22	25	4
	TOTAL	44482	51953	7471	17	1676	44296	51596	7300	16	1664
WR	Gujarat	10049	12895	2846	28	416	10049	12893	2844	28	416
	Madhya Pradesh	6501	7836	1335	21	253	6500	7836	1336	21	253
	Chhattisgarh	3123	3612	490	16	117	3120	3592	472	15	116
	Maharashtra	14427	16737	2310	16	540	14427	16632	2204	15	537
	Goa	375	409	35	9	13	374	409	35	9	13
	DNHDDPDCL	836	916	80	10	30	836	916	80	10	30
	AMNSIL	577	587	10	2	19	577	587	10	2	19
	BALCO*		385	-	-	12		385	-	-	12
	TOTAL	35888	43377	7489	21	1399	35883	43250	7366	21	1395
SR	Andhra Pradesh	6135	7212	1077	18	233	6096	7175	1079	18	231
	Telangana	6306	7933	1627	26	256	6260	7890	1629	26	255
	Karnataka	5643	7997	2354	42	258	5596	7954	2358	42	257
	Kerala	2216	2598	382	17	84	2200	2584	385	17	83
	Tamil Nadu	9756	11406	1650	17	368	9694	11349	1656	17	366
	Puducherry	286	312	27	9	10	284	311	27	10	10
	TOTAL	30342	37460	7118	23	1208	30129	37263	7134	24	1202
ER	Bihar	4096	4299	203	5	139	3942	4239	297	8	137
	Jharkhand	1039	1203	164	16	39	979	1153	174	18	37
	DVC	2254	2299	46	2	74	2254	2299	46	2	74
	Odisha	4038	3627	-411	-10	117	4032	3625	-407	-10	117
	West Bengal	5504	6263	759	14	202	5499	6263	764	14	202
	Sikkim	43	33	-11	-24	1	43	33	-11	-24	1
	Railways_ER ISTS**		5	-	-	0		5	-	-	0
	TOTAL	16974	17729	755	4	572	16750	17617	867	5	568
NER	Arunachal Pradesh	87	83	-4	-4	3	87	83	-4	-4	3
	Assam	1315	1352	38	3	44	1314	1320	6	0	43
	Manipur	84	81	-3	-3	3	83	81	-3	-3	3
	Meghalaya	185	175	-11	-6	6	185	160	-26	-14	5
	Mizoram	53	53	0	0	2	53	53	0	0	2
	Nagaland	87	89	3	3	3	87	89	3	3	3
	Tripura	274	168	-106	-39	5	274	168	-106	-39	5
	TOTAL	2083	2001	-82	-4	65	2083	1954	-129	-6	63
ALL INDIA		129769	152520	22751	18	4920	129141	151679	22538	17	4893

* BALCO has been added as new entity wef 20.12.2022

** Railways_ER ISTS has been added as new entity wef 29.04.2023

13. DEMAND COMPARISON OF AUGUST 2023 vs AUGUST 2022

REGION	STATE	Peak Requirement (MW)				Peak Met (MW)			
		Aug-22	Aug-23	Difference	% Change	Aug-22	Aug-23	Difference	% Change
NR	Chandigarh	381	411	30	7.9	381	411	30	7.9
	Delhi	6446	7437	991	15.4	6446	7437	991	15.4
	Haryana	12028	12844	816	6.8	12015	12844	829	6.9
	Himachal Pradesh	1711	1724	13	0.8	1711	1724	13	0.8
	J&K(UT) and Ladakh(UT)	2783	2735	-48	-1.7	2783	2735	-48	-1.7
	Punjab	14295	15220	925	6.5	14295	15220	925	6.5
	Rajasthan	13808	17420	3612	26.2	13808	17266	3458	25.0
	Uttar Pradesh	25547	27689	2142	8.4	25437	27689	2252	8.9
	Uttarakhand	2339	2303	-36	-1.5	2339	2228	-111	-4.7
	Railway/NFL	159	206	47	29.3	159	206	47	29.3
WR	Gujarat	17632	23012	5380	31	17632	22972	5340	30.3
	Madhya Pradesh	10957	13624	2667	24	10957	13605	2648	24.2
	Chhattisgarh	5073	5827	754	15	5069	5827	758	14.9
	Maharashtra	24186	31178	6992	29	24178	27996	3818	15.8
	Goa	622	667	45	7	619	666	47	7.6
	DNHDDPDCL	1216	1327	111	9.1	1216	1327	111	9.1
	AMNSIL	880	942	61	7.0	880	942	61	7.0
	BALCO*		522	-	-		522	-	-
SR	Andhra Pradesh	11300	12508	1208	10.7	11300	12508	1208	10.7
	Telangana	13079	14835	1756	13.4	13079	14816	1737	13.3
	Karnataka	11268	16968	5700	50.6	11268	16950	5681	50.4
	Kerala	3807	4366	559	14.7	3807	4366	559	14.7
	Tamil Nadu	16058	18252	2194	13.7	16058	18252	2194	13.7
	Puducherry	446	492	46	10.3	446	492	46	10.3
ER	Bihar	7508	7258	-250	-3.3	6778	7185	407	6.0
	Jharkhand	2001	1827	-174	-8.7	1666	1827	161	9.7
	DVC	3370	3673	303	9.0	3370	3673	303	9.0
	Odisha	6787	6816	29	0.4	6537	6816	279	4.3
	West Bengal	9764	10642	878	9.0	9745	10642	897	9.2
	Sikkim	105	92	-13	-12.4	105	92	-13	-12.4
	Railways_ER ISTS**		31	31	-		31	31	-
NER	Arunachal Pradesh	155	155	0	0.2	155	155	0	0.2
	Assam	2376	2353	-23	-1.0	2376	2353	-23	-1.0
	Manipur	207	209	2	0.8	207	209	2	0.8
	Meghalaya	349	322	-26	-7.5	349	322	-26	-7.5
	Mizoram	119	126	8	6.3	119	126	8	6.3
	Nagaland	162	174	12	7.3	162	174	12	7.3
	Tripura	324	330	6	1.7	324	330	6	1.7

* BALCO has been added as new entity wef 20.12.2022

** Railways_ER ISTS has been added as new entity wef 29.04.2023

14. SCHEDULE AND DRAWAL OF CONSTITUENTS - AUGUST

REGION	STATE	SCHEDULE (MU)	ACTUAL DRAWAL (MU)	Over drawal(+)/ Under Drawal(-) (MU)	% OD/UD	SCHEDULE (MU/DAY)	ACTUAL DRAWAL (MU/DAY)	Over drawal(+)/ Under Drawal(-) (MU/DAY)
NR	Chandigarh	218.59	217.43	-1.16	-0.53	7.05	7.01	-0.04
	Delhi	3582.21	3529.23	-52.98	-1.48	115.56	113.85	-1.71
	Haryana	5657.86	5642.56	-15.30	-0.27	182.51	182.02	-0.49
	Himachal Pradesh	-19.13	-10.77	8.36	-43.69	-0.62	-0.35	0.27
	J&K(UT) and Ladakh(UT)	800.92	748.17	-52.75	-6.59	25.84	24.13	-1.70
	Punjab	5666.76	5587.05	-79.71	-1.41	182.80	180.23	-2.57
	Rajasthan	3215.23	3173.48	-41.75	-1.30	103.72	102.37	-1.35
	Uttar Pradesh	7184.18	7128.41	-55.77	-0.78	231.75	229.95	-1.80
	Uttarakhand	638.34	654.73	16.39	2.57	20.59	21.12	0.53
	Railway	99.64	107.04	7.41	7.43	3.21	3.45	0.24
	NFL	2.40	2.44	0.04	1.67	0.08	0.08	0.00
	Total	27047.00	26779.77	-267.22	-0.99	872.48	863.86	-8.62
WR	Gujarat	4905.10	4868.55	-36.55	-0.75	158.23	157.05	-1.18
	Madhya Pradesh	3642.53	3558.81	-83.72	-2.30	117.50	114.80	-2.70
	Chhattisgarh	1766.83	1736.21	-30.62	-1.73	56.99	56.01	-0.99
	Maharashtra	5960.82	5878.20	-82.62	-1.39	192.28	189.62	-2.67
	Goa	396.80	399.61	2.81	0.71	12.80	12.89	0.09
	DNHDDPDCL	917.15	915.59	-1.56	-0.17	29.59	29.54	-0.05
	AMNSIL	268.41	268.91	0.50	0.19	8.66	8.67	0.02
	BALCO*	385.53	384.68	-0.85	-0.22	12.44	12.41	-0.03
	Total	18243.17	18010.56	-232.61	-1.28	588.49	580.99	-7.50
SR	Andhra Pradesh	2700.92	2747.02	46.10	1.71	87.13	88.61	1.49
	Telangana	3812.43	3823.55	11.12	0.29	122.98	123.34	0.36
	Karnataka	2646.06	2703.79	57.73	2.18	85.36	87.22	1.86
	Kerala	1983.50	2025.39	41.89	2.11	63.98	65.34	1.35
	Tamil Nadu	5381.09	5380.84	-0.25	0.00	173.58	173.58	-0.01
	Puducherry	295.66	289.48	-6.18	-2.09	9.54	9.34	-0.20
	Goa (SR)	69.74	69.83	0.09	0.13	2.25	2.25	0.00
	Total	16889.40	17039.90	150.50	0.89	544.82	549.67	4.85
ER	Bihar	4088.01	4089.94	1.93	0.05	131.87	131.93	0.06
	Jharkhand	959.61	964.50	4.90	0.51	30.96	31.11	0.16
	DVC	-1218.99	-1223.29	-4.31	0.35	-39.32	-39.46	-0.14
	Odisha	1332.85	1312.77	-20.08	-1.51	43.00	42.35	-0.65
	West Bengal	2493.45	2448.84	-44.62	-1.79	80.43	78.99	-1.44
	Sikkim	33.19	32.63	-0.56	-1.69	1.07	1.05	-0.02
	Railways_ER ISTS*	4.91	4.63	-0.27	-5.59	0.16	0.15	-0.01
	Total	7693.03	7630.02	-63.02	-0.82	248.16	246.13	-2.03
NER	Arunachal Pradesh	85.28	82.52	-2.76	-3.24	2.75	2.66	-0.09
	Assam	1048.44	1093.42	44.98	4.29	33.82	35.27	1.45
	Manipur	84.29	80.79	-3.50	-4.15	2.72	2.61	-0.11
	Meghalaya	27.44	21.91	-5.53	-20.15	0.89	0.71	-0.18
	Mizoram	48.13	42.35	-5.78	-12.01	1.55	1.37	-0.19
	Nagaland	80.61	76.28	-4.33	-5.38	2.60	2.46	-0.14
	Tripura	175.68	176.25	0.57	0.32	5.67	5.69	0.02
	Total	1549.86	1573.51	23.65	1.53	50.00	50.76	0.76
All India Total		71422.46	71033.76	-388.70	-0.54	2303.95	2291.41	-12.54

* BALCO has been added as new entity wef 20.12.2022

** Railways_ER ISTS has been added as new entity wef 29.04.2023

15. INTER REGIONAL EXCHANGES 2023-24

(All figures in MU)

	Apr'23	May'23	June'23	July'23	Aug'23	Fin. Year 2023-24
Name of Line						
Import of NR from WR (WR-NR)						
WR - NR 765 kV Gwalior - Agra 2xS/C	635.95	996.71	863.68	972.77	772.12	4241.23
WR-NR 765 kV Gwalior - Phagi 2xS/C	553.05	453.93	342.56	671.61	397.70	2418.85
WR-NR 765 kV Jabalpur-Orai D/C	430.29	804.53	778.33	964.77	658.94	3636.86
WR-NR 765 kV Satna-Orai	505.37	598.85	574.83	615.77	543.29	2838.11
WR-NR 765 kV Gwalior-Orai	0.00	0.00	0.00	0.00	0.00	0.00
WR - NR HVDC Champa - Kurukshetra	804.26	1126.68	2069.11	2235.18	1955.13	8190.36
WR - NR HVDC Vindhyachal	0.49	3.23	3.13	94.78	21.55	123.18
WR - NR 400 kV Zerda Kankroli	0.00	0.00	1.48	15.36	13.10	29.94
WR - NR 400 kV Zerda Bhinmal	0.00	0.00	0.00	12.54	13.56	26.10
WR - NR 400 kV RAPP C - Shujalpur D/C	2.28	31.04	16.05	164.49	80.51	294.37
WR - NR 220 kV Bhanpura - Ranpur	9.67	65.53	68.13	70.02	74.29	287.64
WR - NR 220 kV Bhanpura - Modak	0.00	0.00	0.00	0.00	0.00	0.00
WR - NR 220 kV Auraiya - Malanpur/Mehgaon	0.00	0.15	0.00	0.00	0.00	0.15
WR - NR 400 kV Vindhyachal-Rihand D/C	0.00	0.00	0.00	0.00	0.00	0.00
WR - NR HVDC Mundra - Mohindergarh	132.55	340.75	234.27	124.89	667.23	1499.69
WR-NR 765 kV Banaskata-Chittorgarh D/C	0.00	3.26	16.02	169.31	260.02	448.61
WR-NR 765 kV Varanasi-Vindhyachal	1030.05	1663.34	1854.30	1854.38	1551.38	7953.45
Total WR - NR	4103.96	6088.00	6821.89	7965.87	7008.82	31988.54
Export of NR to WR (NR-WR)						
NR - WR 765 kV Gwalior - Agra 2xS/C	0.00	0.00	0.00	0.00	0.00	0.00
NR - WR 765 kV Gwalior - Phagi 2xS/C	0.00	5.41	0.00	0.00	0.00	5.41
NR - WR 765 kV Jabalpur-Orai D/C	0.00	0.00	0.00	0.00	0.00	0.00
NR - WR 765 kV Satna-Orai	0.00	0.00	0.00	0.00	0.00	0.00
NR - WR 765 kV Gwalior-Orai	440.87	385.11	301.32	367.88	368.83	1864.01
NR - WR HVDC Champa- Kurukshetra	0.00	0.00	0.00	0.00	0.00	0.00
NR - WR HVDC Vindhyachal	289.83	273.88	267.04	184.43	225.73	1240.91
NR - WR 400 kV Zerda Kankroli	185.75	94.43	108.34	24.78	31.17	444.47
NR - WR 400 kV Zerda Bhinmal	282.42	181.64	200.56	73.76	74.62	813.00
NR - WR 400 kV RAPP C - Shujalpur D/C	85.74	45.64	45.64	0.00	3.36	180.38
NR - WR 220 kV Bhanpura - Ranpur	0.00	0.00	0.00	0.00	0.00	0.00
NR - WR 220 kV Bhanpura - Modak	0.00	0.00	0.00	0.00	0.00	0.00
NR - WR 220 kV Auraiya - Malanpur/Mehgaon	56.56	28.58	50.82	47.16	97.78	280.90
NR-WR 400 kV Rihand-Vindhyachal D/C	644.30	672.49	642.32	664.33	653.25	3276.69
NR - WR HVDC Mundra - Mohindergarh	243.86	54.36	36.25	94.16	0.00	428.63
NR - WR 765 kV Banaskata-Chittorgarh D/C	976.83	428.19	421.52	94.53	51.63	1972.70
NR-WR 765 kV Varanasi-Vindhyachal	0.00	0.00	0.00	0.00	0.00	0.00
Total NR - WR	3206.16	2169.73	2073.81	1551.03	1506.37	10507.10

	Apr'23	May'23	June'23	July'23	Aug'23	Fin. Year 2023-24
Name of Line						
Import of NR from ER (ER-NR)						
ER - NR 765 kV Sasaram - Fatehpur	166.02	114.36	82.57	74.16	131.29	568.40
ER - NR 765 kV Gaya - Varanasi 2*S/C	224.56	107.46	28.46	47.20	75.64	483.32
ER - NR 765 kV Gaya - Balia	246.38	335.46	321.28	300.74	224.31	1428.17
ER - NR HVDC Alipurduar - Agra	0.00	0.00	375.05	784.99	444.13	1604.17
ER-NR 400 kV Patna - Balia D/C	219.16	246.32	242.35	242.23	300.66	1250.72
ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	127.03	223.63	277.35	376.44	415.21	1419.66
ER - NR 400 kV Biharshariff - Balia D/C	22.11	72.32	102.97	92.77	101.30	391.47
ER - NR 400 kV Motihari - Gorakhpur D/C	156.88	188.70	180.09	228.59	251.16	1005.42
ER - NR 400 kV Biharshariff - Varanasi D/C	67.56	47.21	34.66	24.65	44.14	218.22
ER - NR 400 kV Sasaram -Varanasi	74.99	38.68	46.09	55.64	28.71	244.11
ER - NR 400 kV Sasaram -Allahabad	51.91	33.39	21.29	28.77	17.25	152.61
ER - NR 220 kV Sahupuri-Karnamasa	78.64	82.22	82.32	43.45	51.19	337.82
ER - NR 132 kV Sahupuri - Karnamasa	1.92	0.00	0.96	1.12	0.96	4.96
ER - NR 132 kV 132 kV Rihand - Nagar Untari	0.00	0.00	0.00	0.00	0.00	0.00
ER - NR 132 kV Rihand - Garhwa	0.46	0.00	0.00	0.00	0.00	0.46
ER-NR 400 kV Naubatpur - Balia D/C	211.13	243.59	239.56	236.53	300.12	1230.93
Total ER-NR	1648.75	1733.34	2035.00	2537.28	2386.07	10340.44
Import of NR from NER (NER-NR)						
NER-NR HVDC Biswanath Chariati - Agra	0.00	0.00	153.62	339.28	465.76	958.66
Total NER - NR	0.00	0.00	153.62	339.28	465.76	958.66
Export of NR to ER (NR-ER)						
NR - ER 765 kV Sasaram - Fatehpur	0.00	2.65	7.74	3.45	0.00	13.84
NR - ER 765 kV Gaya - Varanasi 2*S/C	0.30	38.74	102.98	45.94	11.70	199.66
NR - ER 765 kV Gaya - Balia	0.00	0.00	0.00	0.00	0.00	0.00
NR - ER HVDC Alipurduar - Agra	0.00	0.00	0.00	0.00	0.00	0.00
NR - ER 400 kV Patna - Balia 2xD/C	0.00	0.00	0.00	0.00	0.00	0.00
NR - ER 400 kV Muzaffarpur - Gorakhpur D/C	3.47	0.00	0.00	0.00	0.00	3.47
NR - ER 400 kV Biharshariff - Balia D/C	17.15	4.18	13.06	0.00	0.00	34.39
ER - NR 400 kV Motihari - Gorakhpur D/C	0.00	0.00	0.00	0.00	0.00	0.00
NR - ER 400 kV Biharshariff - Varanasi D/C	2.90	7.31	20.53	10.39	0.22	41.35
NR - ER 400 kV Sasaram -Varanasi	0.00	0.00	0.00	0.00	1.67	1.67
NR - ER 400 kV Sasaram -Allahabad	2.25	0.00	0.00	0.82	2.28	5.35
NR - ER 220 kV Sahupuri-Karnamasa	0.00	0.00	0.00	0.00	0.00	0.00
NR - ER 132 kV Sahupuri - Karnamasa	0.01	0.96	0.48	0.96	0.00	2.41
NR - ER 132 kV 132 kV Rihand - Nagar Untari	1.74	2.20	1.08	3.37	2.39	10.78
ER - NR 132 kV Rihand - Garhwa	10.23	8.48	19.67	18.35	14.38	71.11
NR-ER 400 kV Balia- Naubatpur D/C	0.00	0.00	0.00	0.00	0.00	0.00
Total NR - ER	38.05	64.52	165.54	83.28	32.64	384.03
Export of NR to NER (NER-NR)						
NR-NER HVDC Biswanath Chariati - Agra	261.93	291.71	104.47	0.00	0.00	658.11
Total NR - NER	261.93	291.71	104.47	0.00	0.00	658.11

	Apr'23	May'23	June'23	July'23	Aug'23	Fin. Year 2023-24
Name of Line						
Export of WR to ER (WR-ER)						
WR - ER 765 kV Ranchi - Dharamjaygarh 2xS/C	139.81	504.96	673.15	734.00	331.39	2383.31
WR - ER 765 kV Dharamjaygarh - Jharsuguda 2xD/C	652.31	469.82	490.99	593.61	768.89	2975.62
WR - ER 765 kV Durg - Jharsuguda D/C	0.00	0.64	1.75	26.78	7.42	36.59
WR - ER 400 kV Sipat - Ranchi D/C	15.97	93.84	118.29	133.75	52.57	414.42
WR - ER 400 kV Raigarh - Jharsuguda 2xD/C	0.44	6.23	8.79	6.26	28.69	50.42
WR - ER 220 kV Korba - Budhipadar D/C	36.08	80.04	73.19	22.96	28.75	241.02
WR - ER 220 kV Raigarh - Budhipadar	0.15	0.57	1.17	0.00	0.35	2.24
Total WR - ER	844.75	1156.11	1367.33	1517.34	1218.07	6103.60
Import of WR from ER (ER - WR)						
ER - WR 765 kV Ranchi - Dharamjaygarh 2xS/C	144.10	11.95	15.57	10.81	83.69	266.13
ER - WR 765 kV Dharamjaygarh - Jharsuguda 2XD/C	25.46	58.29	33.08	15.65	2.33	134.81
ER - WR 765 kV Durg - Jharsuguda D/C	394.08	204.42	148.02	71.84	73.64	891.99
ER - WR 400 kV Sipat - Ranchi D/C	55.56	5.71	9.07	7.22	29.65	107.20
ER - WR 400 kV Raigarh - Jharsuguda 2xD/C	248.78	148.94	125.69	125.00	127.87	776.28
ER - WR 220 kV Korba - Budhipadar D/C	1.45	0.00	0.14	6.23	1.99	9.81
ER - WR 220 kV Raigarh - Budhipadar	55.98	38.46	41.41	66.29	74.76	276.89
Total ER - WR	925.41	467.76	372.98	303.04	393.92	2463.11
Export of ER to NER (ER - NER)						
ER - NER 400 kV Binaguri - Bongaigaon D/C	6.99	16.15	105.81	142.19	71.19	342.34
ER - NER 400 kV Alipurduar - Bongaigaon D/C	4.62	34.31	135.94	83.03	84.82	342.72
ER - NER 220 kV Birpara - Salakati D/C	0.54	3.12	31.19	37.25	25.19	97.28
Total ER - NER	12.16	53.58	272.93	262.48	181.20	782.34
Import of ER from NER (NER - ER)						
NER - ER 400 kV Binaguri - Bongaigaon D/C	52.83	40.19	37.75	2.10	10.62	143.49
NER - ER 400 kV Alipurduar - Bongaigaon D/C	182.37	135.22	72.81	20.59	29.76	440.74
NER - ER 220 kV Birpara - Salakati D/C	34.59	31.32	10.78	0.62	2.83	80.13
Total NER - ER	269.78	206.73	121.33	23.31	43.22	664.36
Export of ER to SR (ER - SR)						
ER - SR HVDC Gazuwaka	375.93	395.23	208.61	178.44	321.36	1479.57
ER - SR HVDC Talchar - Kolar	1233.20	1204.28	984.75	977.61	1284.58	5684.41
ER - SR 765 kV Angul- Srikakulam D/C	1683.42	1561.33	1412.42	1184.37	1380.27	7221.81
Total ER - SR	3292.55	3160.85	2605.77	2340.42	2986.21	14385.80
Import of ER from SR (SR - ER)						
SR - ER HVDC Gazuwaka	0.00	0.00	55.34	114.11	32.48	201.93
SR - ER HVDC Talchar - Kolar	0.00	0.00	0.00	0.00	0.00	0.01
SR - ER 765 kV Angul- Srikakulam D/C	0.00	0.00	0.00	0.00	0.00	0.00
Total SR - ER	0.00	0.00	55.34	114.11	32.48	201.94

	Apr'23	May'23	June'23	July'23	Aug'23	Fin. Year 2023-24
Name of Line						
Export of WR to SR (WR-SR)						
WR - SR HVDC Bhadrawati	544.41	411.52	171.68	139.64	464.81	1732.06
WR - SR 765 kV Sholapur - Raichur 2xS/C	417.69	222.76	146.07	83.93	451.70	1322.16
WR - SR 765 kV Wardha - Nizamabad D/C	1323.51	873.44	1018.25	852.05	1313.80	5381.05
WR - SR 400KV Kolhapur-Kudgi D/C	0.00	0.00	0.00	0.00	0.06	0.06
WR-SR HVDC Raigarh-Pugalur	3004.35	1791.86	1182.91	885.62	2135.69	9000.42
WR-SR 220kV Xeldem - Ambewadi S/C	77.16	70.18	68.17	61.74	68.61	345.86
WR-SR 220kV Ponda - Ambewadi S/C	0.29	1.54	0.28	0.16	5.23	7.49
Total WR - SR	5367.41	3371.30	2587.37	2023.14	4439.89	17789.10
Import of WR from SR (SR - WR)						
SR - WR HVDC Bhadrawati	4.11	25.09	178.09	308.60	10.36	526.26
SR - WR 765 kV Raichur - Sholapur 2xS/C	29.13	205.27	344.82	478.51	54.56	1112.29
SR - WR 765 kV Wardha - Nizamabad D/C	0.00	3.90	0.32	18.33	0.00	22.55
SR - WR 400KV Kolhapur-Kudgi D/C	623.59	719.30	784.98	796.02	623.43	3547.33
SR-WR HVDC Pugalur-Raigarh	0.00	3.73	14.87	16.65	0.00	35.24
WR-SR 220kV Ambewadi - Xeldem S/C	0.00	0.00	0.00	0.00	0.00	0.00
WR-SR 220kV Ambewadi-Ponda S/C	0.00	0.00	0.01	0.00	0.01	0.02
Total SR - WR	656.84	957.30	1323.09	1618.10	688.36	5243.69
TOTAL ALL INDIA	20628	19721	20060	20679	21383	102471

*In case of mutiple ckt / DC pole year corres. to the commissioning of final element

Date	15.1 Import-Export of NR with WR during August 2023																	
	Import of NR from WR (WR-NR)																	
	WR - NR 765 kV Gwalior - Agra 2x5/C	WR-NR 765 kV Gwalior-Phagi 2x5/C	WR-NR 765 kV Jabalpur- Orai D/C	WR-NR 765 kV Satna- Orai	WR-NR 765 kV Gwalior-Orai	WR - NR HVDC Champa- Kurukshetra	WR - NR HVDC Vindhyachal	WR - NR 400 kV Zerd- Kankroli	WR - NR 400 kV Zerd- Bhinmal	WR-NR 400 kV RAPP C - Shujalpur D/C	WR - NR 220 kV Bhanpura - Ranpur	WR - NR 220 kV Bhanpura - Modak	WR - NR 220 kV Auraiya - Malanpur / Mehgaon	WR-NR 400 kV Rihand Vindhyachal D/C	WR - NR HVDC Mundra - M'garh	WR - NR 765 kV Banaskata - Chittorgarh D/C	WR-NR 765 kV Varanasi- Vindhyachal	Total WR - NR
1-Aug-23	26.42	5.95	19.62	15.06	0.00	106.40	6.91	0.25	0.00	1.06	2.15		0.00	0.00	24.21	12.43	55.82	276.28
2-Aug-23	33.54	10.66	23.60	16.55	0.00	86.29	2.92	0.00	0.00	3.46	2.16		0.00	0.00	17.43	18.56	52.80	267.97
3-Aug-23	36.74	15.20	25.92	18.81	0.00	66.47	2.42	0.00	0.00	5.07	2.24		0.00	0.00	13.71	14.48	59.22	260.28
4-Aug-23	33.90	17.40	23.16	17.94	0.00	60.54	3.13	0.28	0.00	5.53	2.26		0.00	0.00	9.98	5.75	58.17	238.04
5-Aug-23	29.15	14.76	19.20	17.50	0.00	57.40	6.17	0.00	0.00	3.87	2.31		0.00	0.00	20.43	1.09	55.61	227.49
6-Aug-23	34.58	7.47	21.85	17.13	0.00	50.02	0.00	0.39	0.00	2.65	2.31		0.00	0.00	8.82	16.53	59.51	221.26
7-Aug-23	33.60	7.40	21.78	17.81	0.00	46.67	0.00	0.05	0.00	2.79	2.32		0.00	0.00	16.44	17.95	49.01	215.82
8-Aug-23	22.45	6.85	15.08	17.01	0.00	53.91	0.00	0.00	0.00	0.66	2.34		0.00	0.00	34.02	6.19	40.08	198.59
9-Aug-23	18.64	7.35	15.38	17.63	0.00	55.14	0.00	0.00	0.00	0.61	2.37		0.00	0.00	36.48	3.10	36.10	192.80
10-Aug-23	25.76	10.90	20.13	17.02	0.00	47.50	0.00	1.07	0.00	0.68	2.47		0.00	0.00	17.29	15.09	41.45	199.36
11-Aug-23	24.40	14.16	23.24	17.94	0.00	48.25	0.00	0.97	0.26	3.25	2.40		0.00	0.00	24.21	11.67	49.56	220.31
12-Aug-23	22.32	11.78	21.80	18.76	0.00	52.24	0.00	1.30	0.00	2.17	2.47		0.00	0.00	30.35	16.75	50.27	230.21
13-Aug-23	24.20	11.50	24.41	18.68	0.00	42.21	0.00	1.35	0.00	3.12	2.49		0.00	0.00	20.14	19.48	48.11	215.69
14-Aug-23	24.66	17.09	24.73	19.08	0.00	50.51	0.00	0.86	0.00	4.09	2.54		0.00	0.00	12.17	14.17	47.22	217.12
15-Aug-23	24.58	22.88	28.85	18.86	0.00	69.58	0.00	1.23	3.04	7.17	2.44		0.00	0.00	12.18	6.36	54.98	252.15
16-Aug-23	22.13	14.12	24.30	18.06	0.00	72.32	0.00	0.00	0.36	2.55	2.51		0.00	0.00	12.32	4.63	53.45	226.75
17-Aug-23	23.26	12.17	21.90	18.27	0.00	74.20	0.00	0.81	0.00	2.25	2.37		0.00	0.00	24.22	13.56	54.97	247.98
18-Aug-23	31.75	16.82	37.37	20.31	0.00	79.21	0.00	1.89	2.11	4.68	2.58		0.00	0.00	24.22	18.31	63.95	303.20
19-Aug-23	36.32	20.41	31.54	21.36	0.00	80.05	0.00	1.22	3.75	6.60	2.59		0.00	0.00	24.23	15.07	60.33	303.47
20-Aug-23	35.20	23.53	35.72	21.02	0.00	84.67	0.00	0.75	2.45	8.96	2.44		0.00	0.00	24.22	5.69	61.20	305.85
21-Aug-23	30.64	18.19	30.44	19.84	0.00	55.59	0.00	0.68	1.59	4.70	2.38		0.00	0.00	23.32	6.88	50.97	245.22
22-Aug-23	18.54	9.36	19.04	16.28	0.00	37.18	0.00	0.00	0.00	0.50	2.46		0.00	0.00	36.27	6.08	43.84	189.55
23-Aug-23	16.51	5.80	9.46	15.74	0.00	26.10	0.00	0.00	0.00	0.00	2.50		0.00	0.00	32.11	4.53	41.90	154.65
24-Aug-23	21.36	6.56	13.89	16.71	0.00	45.99	0.00	0.00	0.00	0.00	2.34		0.00	0.00	24.22	5.67	41.14	177.88
25-Aug-23	15.80	9.51	9.50	16.46	0.00	73.07	0.00	0.00	0.00	0.00	2.44		0.00	0.00	24.22	0.00	35.32	186.32
26-Aug-23	20.78	15.93	17.32	17.23	0.00	55.56	0.00	0.00	0.00	1.56	2.41		0.00	0.00	24.22	0.00	39.56	194.57
27-Aug-23	14.42	11.12	13.61	15.44	0.00	80.91	0.00	0.00	0.00	0.32	2.43		0.00	0.00	24.22	0.00	47.24	209.71
28-Aug-23	17.80	7.46	13.94	15.25	0.00	76.73	0.00	0.00	0.00	0.00	2.49		0.00	0.00	17.80	0.00	53.25	204.72
29-Aug-23	13.49	12.10	14.60	14.27	0.00	95.55	0.00	0.00	0.00	0.00	2.46		0.00	0.00	19.03	0.00	47.49	218.99
30-Aug-23	18.92	15.12	17.64	15.17	0.00	60.29	0.00	0.00	0.00	0.77	2.34		0.00	0.00	12.83	0.00	48.62	191.70
31-Aug-23	20.26	18.15	19.92	16.10	0.00	64.58	0.00	0.00	0.00	1.44	2.28		0.00	0.00	21.92	0.00	50.24	214.89
Total	772.12	397.70	658.94	543.29	0.00	1955.13	21.55	13.10	13.56	80.51	74.29	0.00	0.00	0.00	667.23	260.02	1551.38	7008.82
Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day																		

Date	15.1 Import-Export of NR with WR during August 2023																	
	Export of NR to WR (NR- WR)																	
	NR - WR 765 kV Gwalior - Agra 2x5/C	NR-WR 765 kV Gwalior-Phagi 2x5/C	NR-WR 765 kV Jabalpur- Orai D/C	NR-WR 765 kV Satna- Orai	NR-WR 765 kV Gwalior-Orai	NR - WR HVDC Champa- Kurukshetra	NR - WR HVDC Vindhyachal	NR - WR 400 kV Zerda- Kankrol	NR - WR 400 kV Zerda- Bhinmal	NR-WR 400 kV RAPP C - Shujalpur D/C	WR - NR 220 kV Bhanpura - Ranpur	WR - NR 220 kV Bhanpura - Modak	NR - WR 220 kV Auraiya - Malanpur / Mehgaon	NR-WR 400 kV Rihand- Vindhyachal D/C	NR - WR HVDC Mundra - M'garh	NR - WR 765 kV Banaskata - Chittorgarh D/C	NR-WR 765 kV Varanasi- Vindhyachal	Total NR - WR
1-Aug-23	0.00	0.00	0.00	0.00	11.60	0.00	1.37	0.00	3.70	0.00	0.00		0.33	20.78	0.00	0.00	0.00	37.78
2-Aug-23	0.00	0.00	0.00	0.00	12.50	0.00	0.00	0.95	3.20	0.00	0.00		2.33	19.30	0.00	0.00	0.00	38.28
3-Aug-23	0.00	0.00	0.00	0.00	13.79	0.00	0.00	0.94	0.84	0.00	0.00		1.21	21.29	0.00	0.00	0.00	38.07
4-Aug-23	0.00	0.00	0.00	0.00	13.75	0.00	0.00	0.00	0.65	0.00	0.00		0.47	22.05	0.00	0.00	0.00	36.92
5-Aug-23	0.00	0.00	0.00	0.00	12.96	0.00	0.13	0.55	2.11	0.00	0.00		1.38	22.37	0.00	0.00	0.00	39.50
6-Aug-23	0.00	0.00	0.00	0.00	9.90	0.00	1.56	0.00	4.21	0.00	0.00		1.23	19.35	0.00	0.00	0.00	36.25
7-Aug-23	0.00	0.00	0.00	0.00	9.51	0.00	12.18	0.00	5.61	0.00	0.00		1.88	12.57	0.00	0.00	0.00	41.75
8-Aug-23	0.00	0.00	0.00	0.00	9.79	0.00	12.18	1.24	6.84	0.00	0.00		3.16	10.75	0.00	0.00	0.00	43.96
9-Aug-23	0.00	0.00	0.00	0.00	9.06	0.00	12.18	6.43	1.50	0.00	0.00		4.93	21.09	0.00	0.00	0.00	55.19
10-Aug-23	0.00	0.00	0.00	0.00	9.46	0.00	12.13	0.00	0.78	0.00	0.00		4.79	21.31	0.00	0.00	0.00	48.47
11-Aug-23	0.00	0.00	0.00	0.00	11.08	0.00	12.15	0.00	0.00	0.00	0.00		4.56	21.97	0.00	0.00	0.00	49.76
12-Aug-23	0.00	0.00	0.00	0.00	10.28	0.00	12.13	0.00	1.12	0.00	0.00		4.25	22.06	0.00	0.00	0.00	49.84
13-Aug-23	0.00	0.00	0.00	0.00	9.61	0.00	10.96	0.00	2.18	0.00	0.00		4.14	22.14	0.00	0.00	0.00	49.03
14-Aug-23	0.00	0.00	0.00	0.00	11.95	0.00	12.17	0.00	1.04	0.00	0.00		4.79	22.24	0.00	0.00	0.00	52.19
15-Aug-23	0.00	0.00	0.00	0.00	12.94	0.00	12.14	0.00	0.00	0.00	0.00		2.46	22.26	0.00	0.00	0.00	49.80
16-Aug-23	0.00	0.00	0.00	0.00	11.40	0.00	11.69	0.12	0.00	0.00	0.00		3.30	22.05	0.00	0.00	0.00	48.56
17-Aug-23	0.00	0.00	0.00	0.00	10.81	0.00	4.85	0.00	0.76	0.00	0.00		4.17	21.58	0.00	0.00	0.00	42.17
18-Aug-23	0.00	0.00	0.00	0.00	11.42	0.00	4.82	0.00	0.00	0.00	0.00		3.07	21.62	0.00	0.00	0.00	40.93
19-Aug-23	0.00	0.00	0.00	0.00	12.32	0.00	5.73	0.00	0.00	0.00	0.00		2.55	21.81	0.00	0.00	0.00	42.41
20-Aug-23	0.00	0.00	0.00	0.00	13.55	0.00	1.44	0.00	0.00	0.00	0.00		1.89	22.07	0.00	0.00	0.00	38.95
21-Aug-23	0.00	0.00	0.00	0.00	11.34	0.00	1.22	0.00	0.00	0.00	0.00		2.76	22.13	0.00	0.00	0.00	37.45
22-Aug-23	0.00	0.00	0.00	0.00	8.72	0.00	1.98	0.55	1.99	0.00	0.00		4.27	22.02	0.00	0.00	0.00	39.53
23-Aug-23	0.00	0.00	0.00	0.00	9.54	0.00	8.56	1.85	7.15	1.72	0.00		3.98	21.77	0.00	0.00	0.00	54.57
24-Aug-23	0.00	0.00	0.00	0.00	11.54	0.00	12.17	1.70	5.04	0.29	0.00		1.42	21.99	0.00	0.00	0.00	54.15
25-Aug-23	0.00	0.00	0.00	0.00	12.84	0.00	12.24	3.19	5.50	0.59	0.00		4.16	21.60	0.00	5.47	0.00	65.59
26-Aug-23	0.00	0.00	0.00	0.00	15.45	0.00	12.04	2.57	3.38	0.00	0.00		4.09	22.26	0.00	7.26	0.00	67.05
27-Aug-23	0.00	0.00	0.00	0.00	12.85	0.00	12.15	2.70	4.55	0.00	0.00		3.98	21.90	0.00	7.07	0.00	65.20
28-Aug-23	0.00	0.00	0.00	0.00	12.29	0.00	11.00	2.38	5.67	0.56	0.00		3.76	21.91	0.00	1.82	0.00	59.39
29-Aug-23	0.00	0.00	0.00	0.00	14.37	0.00	4.87	2.87	3.93	0.20	0.00		3.85	22.19	0.00	11.10	0.00	63.38
30-Aug-23	0.00	0.00	0.00	0.00	15.41	0.00	4.84	1.25	0.65	0.00	0.00		3.99	22.30	0.00	6.55	0.00	54.99
31-Aug-23	0.00	0.00	0.00	0.00	16.80	0.00	4.85	1.88	2.22	0.00	0.00		4.63	22.52	0.00	12.36	0.00	65.26
Total	0.00	0.00	0.00	0.00	368.83	0.00	225.73	31.17	74.62	3.36	0.00	0.00	97.78	653.25	0.00	51.63	0.00	1506.37
Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day																		

Date	15.2 Import-Export of NR with ER & NER during August 2023																		
	Import of NR from ER (ER-NR)																	Import of NR from NER (NER-NR)	
	ER - NR 765 kV Sasaram - Fatehpur	ER - NR 765 kV Gaya - Varanasi 2*5/C	ER - NR 765 kV Gaya Ballia	ER - NR HVDC Alipurduar - Agra	ER-NR 400 kV Patna - Ballia D/C	ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	ER - NR 400 kV Biharsharif - Ballia D/C	ER - NR 400 kV Motihari - Gorakhpur D/C	ER - NR 400 kV Biharsharif - Varanasi D/C	ER-NR 400 kV Sasaram - Varanasi	ER-NR 400 kV Sasaram - Allahabad	ER - NR 220 kV Sahupuri - Karamnasa	ER - NR 132 kV Sahupuri - Karamnasa	ER - NR 132 kV Rihand - Nagar Untari	NR - ER 132 kV Rihand - Garhwa	ER-NR 400 kV Naubatpur - Ballia D/C	Total ER - NR	NER-NR HVDC Biswanath Chariiali - Agra	Total NER-NR
1-Aug-23	0.61	0.00	8.05	12.60	6.34	10.05	1.91	7.25	1.25	0.67	0.00	1.49			0.00	5.92	56.14	11.61	11.61
2-Aug-23	4.89	2.54	9.35	11.85	8.59	15.34	4.87	9.82	1.87	0.28	0.25	1.92	0.00		0.00	8.49	80.06	12.10	12.10
3-Aug-23	5.56	3.50	9.72	12.54	10.53	15.33	4.43	9.25	2.77	0.00	0.33	1.86			0.00	8.58	84.40	12.18	12.18
4-Aug-23	4.74	1.53	9.05	12.31	10.73	14.61	3.95	8.73	2.06	0.00	0.12	1.74	0.00		0.00	8.85	78.42	12.16	12.16
5-Aug-23	3.99	0.30	8.61	11.92	11.23	14.08	3.76	8.40	0.75	0.27	0.00	1.57		0.00	0.00	9.39	74.27	11.97	11.97
6-Aug-23	3.02	0.54	8.77	11.94	10.51	13.94	3.90	7.82	2.01	0.00	0.26	1.62	0.00		0.00	9.70	74.03	11.45	11.45
7-Aug-23	5.84	3.38	7.43	11.72	10.13	15.01	3.91	8.17	2.80	0.00	0.48	1.79			0.00	10.28	80.94	16.72	16.72
8-Aug-23	6.08	3.65	6.27	12.09	10.59	16.10	5.01	8.54	2.80	0.04	0.00	1.87		0.00		10.78	83.82	16.18	16.18
9-Aug-23	4.46	2.83	5.05	11.96	11.65	16.45	5.24	8.95	2.93	0.25	0.00	1.51		0.00		11.40	82.68	16.04	16.04
10-Aug-23	2.87	1.23	5.94	12.40	8.80	11.05	3.00	6.57	1.44	0.52	0.00	1.34		0.00	0.00	8.75	63.91	16.97	16.97
11-Aug-23	3.55	0.59	7.14	12.56	8.68	10.87	2.41	6.37	1.26	0.00	0.43	1.39			0.00	8.52	63.77	16.98	16.98
12-Aug-23	4.84	3.64	7.97	12.03	9.83	13.79	3.44	8.63	1.88	0.37	0.00	1.52			0.00	9.81	77.75	17.04	17.04
13-Aug-23	4.00	3.73	8.41	12.44	10.40	15.78	3.70	8.79	1.93	1.16	0.67	1.51			0.00	10.49	83.01	16.66	16.66
14-Aug-23	3.92	3.80	7.98	11.87	10.84	13.88	3.39	8.10	1.60	1.61	0.74	1.51			0.00	10.92	80.16	16.85	16.85
15-Aug-23	3.48	3.42	9.03	11.90	10.91	14.51	3.90	8.87	1.43	1.18	1.25	2.07			0.00	11.10	83.05	16.82	16.82
16-Aug-23	3.55	3.12	4.90	11.55	9.84	12.36	3.38	7.46	1.40	0.80	1.42	1.71		0.00	0.00	9.61	71.10	16.17	16.17
17-Aug-23	3.97	2.01	8.26	11.64	9.44	11.83	3.27	7.76	0.90	1.23	0.80	1.79			0.00	9.35	72.25	16.29	16.29
18-Aug-23	3.80	3.45	10.00	12.28	9.74	13.05	3.80	7.91	1.52	1.13	1.18	1.77	0.48		0.00	9.31	79.42	17.23	17.23
19-Aug-23	3.46	3.49	10.78	12.31	9.38	14.30	4.05	7.70	1.80	0.96	1.30	1.79	0.00		0.00	9.26	80.58	16.82	16.82
20-Aug-23	3.78	4.67	10.54	12.23	8.55	14.73	4.65	8.35	1.56	0.95	1.26	1.88			0.00	10.35	83.50	16.87	16.87
21-Aug-23	3.80	2.66	8.66	12.01	6.20	11.51	2.70	7.27	0.60	1.24	0.73	1.51	0.00		0.00	9.72	68.61	16.84	16.84
22-Aug-23	2.91	0.50	5.90	15.28	8.60	11.12	1.10	6.23	0.00	1.81	0.27		0.00	0.00	0.00	8.39	62.11	15.72	15.72
23-Aug-23	2.75	0.52	3.88	19.23	9.03	10.53	0.31	7.70	0.00	1.73	0.41	1.48			0.00	8.93	66.50	17.36	17.36
24-Aug-23	3.37	0.59	4.42	20.23	9.23	12.80	0.70	8.21	0.31	1.09	1.07	1.39			0.00	8.98	72.39	17.04	17.04
25-Aug-23	5.70	6.00	3.75	18.59	9.95	14.30	1.70	8.78	1.55	1.10	1.11	1.45			0.00	9.97	83.95	14.36	14.36
26-Aug-23	8.57	9.83	6.32	18.36	12.58	18.15	5.48	11.18	2.49	0.66	1.29	2.51	0.48		0.00	12.94	110.84	12.63	12.63
27-Aug-23	6.10	3.74	5.66	20.03	12.14	16.00	5.11	9.40	2.52	1.29	1.03	2.38			0.00	12.45	97.85	13.36	13.36
28-Aug-23	3.67	0.00	5.21	19.67	8.98	11.81	2.97	7.28	0.00	1.87	0.41	1.94		0.00	0.00	9.45	73.26	13.42	13.42
29-Aug-23	4.58	0.00	4.24	19.58	7.90	10.91	2.17	7.29	0.00	2.21	0.13	1.76		0.00	0.00	9.34	70.11	13.22	13.22
30-Aug-23	4.88	0.00	5.60	18.76	9.54	10.99	1.90	7.58	0.55	2.04	0.28	1.72	0.00		0.00	9.40	73.24	13.41	13.41
31-Aug-23	4.55	0.38	7.42	20.25	9.80	10.03	1.19	6.80	0.16	2.25	0.03	1.40	0.00		0.00	9.69	73.95	13.29	13.29
Total	131.29	75.64	224.31	444.13	300.66	415.21	101.30	251.16	44.14	28.71	17.25	51.19	0.96	0.00	0.00	300.12	2386.07	465.76	465.76
Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day																			

Date	15.2 Import-Export of NR with ER & NER during August 2023																		
	Export of NR to ER (NR- ER)																	Export of NR to NER (NR-NER)	
	NR - ER 765 kV Sasaram - Fatehpur	NR - ER 765 kV Gaya - Varanasi 2*5/C	NR - ER 765 kV Gaya Balia	NR - ER HVDC Alipurduar - Agra	NR-ER 400 kV Patna - Balia D/C	NR - ER 400 kV Muzaffarpur - Gorakhpur D/C	NR - ER 400 kV Biharshariff - Balia D/C	NR - ER 400 kV Motihari - Gorakhpur D/C	NR - ER 400 kV Biharshariff - Varanasi D/C	NR-ER 400 kV Sasaram - Varanasi	NR-ER 400 kV Sasaram - Allahabad	NR - ER 220 kV Sahupuri- Karamnasa	NR - ER 132 kV Sahupuri - Karamnasa	NR - ER 132 kV Rihand - Nagar Untari	NR - ER 132 kV Rihand - Garhwa	NR-ER 400 kV Balia- Naubatpur D/C	Total NR - ER	NR-NER HVDC Biswanath Chariali - Agra	Total NR-NER
1-Aug-23	0.00	4.41	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.72	0.00			0.72	0.00	5.85	0.00	0.00
2-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.52	0.00	0.52	0.00	0.00
3-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.32	0.00	0.00			0.62	0.00	0.94	0.00	0.00
4-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.17	0.00	0.00	0.00		0.78	0.00	0.95	0.00	0.00
5-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.27	0.00		0.00	0.75	0.00	1.02	0.00	0.00
6-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.28	0.00	0.00	0.00		0.25	0.00	0.53	0.00	0.00
7-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.48	0.00	0.00			0.36	0.00	0.84	0.00	0.00
8-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.12	0.00		0.26		0.00	0.38	0.00	0.00
9-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.31	0.00		0.35		0.00	0.66	0.00	0.00
10-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.46	0.00		0.49	0.48	0.00	1.43	0.00	0.00
11-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.42	0.00	0.00			0.51	0.00	0.93	0.00	0.00
12-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.40	0.00			0.50	0.00	0.90	0.00	0.00
13-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.51	0.00	0.51	0.00	0.00
14-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.50	0.00	0.50	0.00	0.00
15-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.40	0.00	0.40	0.00	0.00
16-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.09	0.40	0.00	0.49	0.00	0.00
17-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.46	0.00	0.46	0.00	0.00
18-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.39	0.00	0.39	0.00	0.00
19-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.42	0.00	0.42	0.00	0.00
20-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.50	0.00	0.50	0.00	0.00
21-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.47	0.00	0.47	0.00	0.00
22-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.13	0.00	0.00		0.00	0.00	0.48	0.00	0.61	0.00	0.00
23-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.03	0.00	0.00	0.00			0.43	0.00	0.46	0.00	0.00
24-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.46	0.00	0.46	0.00	0.00
25-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.48	0.00	0.48	0.00	0.00
26-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.49	0.00	0.49	0.00	0.00
27-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.50	0.00	0.50	0.00	0.00
28-Aug-23	0.00	3.24	0.00	0.00	0.00	0.00	0.00	0.00	0.02	0.00	0.00	0.00		0.82	0.62	0.00	4.70	0.00	0.00
29-Aug-23	0.00	2.91	0.00	0.00	0.00	0.00	0.00	0.00	0.04	0.00	0.00	0.00		0.38	0.53	0.00	3.86	0.00	0.00
30-Aug-23	0.00	1.14	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.43	0.00	1.57	0.00	0.00
31-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.42	0.00	0.42	0.00	0.00
Total	0.00	11.70	0.00	0.00	0.00	0.00	0.00	0.00	0.22	1.67	2.28	0.00	0.00	2.39	14.38	0.00	32.64	0.00	0.00
Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day																			

Date	15.3 Import and Export of ER with WR & NER during August 2023																							
	Export of WR to ER (WR-ER)								Import of WR from ER (ER - WR)								Export of ER to NER (ER-NER)				Import of ER from NER (NER-ER)			
	WR - ER 765 kV Dharamjaygarh - Ranchi 2x5/C	WR - ER 765 kV Dharamjaygarh - Jharsuguda Q/C	WR - ER 765 kV Durg - Jharsuguda D/C	WR - ER 400 kV Sipat - Ranchi D/C	WR - ER 400 kV Raigarh - Jharsuguda- 2x2D/C	WR - ER 220 kV Korba - Budhipadar D/C	WR - ER 220 kV Raigarh - Budhipadar	Total WR - ER	ER - WR 765 kV Dharamjaygarh - Ranchi 2x5/C	ER-WR 765 kV Dharamjaygarh - Jharsuguda D/C	ER-WR 765 kV Durg - Jharsuguda D/C	ER - WR 400 kV Sipat - Ranchi D/C	ER - WR 400 kV Raigarh - Jharsuguda- 2x2D/C	ER - WR 220 kV Korba - Budhipadara D/C	ER - WR 220 kV Raigarh - Budhipadar	Total ER - WR	ER - NER 400 kV Binaguri - Bongaigaon D/C	ER - NER 400 kV Alipurduar - Bongaigaon D/C	ER - NER 220 kV Birpara - Salakati D/C	Total ER - NER	NER - ER 400 kV Binaguri - Bongaigaon D/C	NER - ER 400 kV Alipurduar - Bongaigaon 2x2D/C	NER - ER 220 kV Birpara - Salakati D/C	Total NER - ER
1-Aug-23	18.4	23.1	1.0	3.6	0.6	1.3	0.0	48.06	0.8	0.0	1.1	0.3	1.3	0.0	2.0	5.47	4.40	6.20	1.46	12.06	0.00	0.00	0.00	0.00
2-Aug-23	11.9	15.9	0.1	2.3	2.4	1.3	0.0	34.03	1.8	0.1	2.7	0.5	0.5	0.0	1.7	7.40	4.98	6.82	1.83	13.64	0.00	0.00	0.00	0.00
3-Aug-23	10.9	18.0	0.1	3.0	7.6	1.9	0.1	41.63	2.3	0.0	2.9	0.4	0.0	0.0	0.3	6.02	2.53	3.50	0.91	6.93	0.20	0.35	0.03	0.58
4-Aug-23	15.0	26.7	0.1	3.6	5.2	2.6	0.0	53.31	1.5	0.0	2.3	0.3	0.1	0.0	0.6	4.83	2.04	2.88	0.83	5.74	0.39	0.62	0.02	1.02
5-Aug-23	14.2	27.7	0.1	3.7	4.6	2.4	0.0	52.65	1.7	0.0	2.3	0.4	0.1	0.0	0.6	5.14	2.18	3.11	0.99	6.28	0.51	0.77	0.04	1.31
6-Aug-23	11.4	30.8	0.6	3.0	3.1	2.3	0.1	51.37	1.1	0.0	1.2	0.2	0.2	0.0	0.5	3.16	1.51	2.07	0.82	4.39	0.06	0.12	0.00	0.18
7-Aug-23	7.7	26.9	0.0	1.7	1.2	2.2	0.0	39.77	3.5	0.0	2.9	1.0	1.3	0.0	0.5	9.24	2.47	3.45	1.06	6.98	0.07	0.10	0.00	0.17
8-Aug-23	3.2	24.9	0.1	0.9	0.9	1.8	0.0	31.68	6.8	0.0	3.5	1.3	1.7	0.0	1.0	14.29	1.71	2.14	0.72	4.57	0.70	1.06	0.08	1.84
9-Aug-23	3.6	27.0	0.1	0.9	1.2	1.9	0.0	34.62	7.9	0.0	2.4	1.3	1.2	0.0	1.2	14.03	1.97	2.76	0.79	5.52	0.45	0.63	0.02	1.11
10-Aug-23	8.7	27.1	0.5	2.0	1.1	0.8	0.0	40.23	2.5	0.0	1.1	0.5	1.3	0.0	2.0	7.46	2.54	3.55	0.93	7.02	0.20	0.38	0.02	0.60
11-Aug-23	11.2	26.9	0.3	2.0	0.5	0.7	0.0	41.59	1.3	0.0	1.6	0.6	2.7	0.0	2.7	8.92	3.42	2.00	1.19	6.60	0.04	0.49	0.00	0.53
12-Aug-23	8.4	27.2	0.0	1.1	0.0	0.4	0.0	37.13	3.0	0.0	2.9	1.3	5.3	0.0	3.2	15.77	4.27	4.44	1.45	10.16	0.00	0.03	0.00	0.03
13-Aug-23	7.2	31.3	0.0	1.1	0.0	0.4	0.0	40.06	3.1	0.0	3.0	1.4	6.1	0.2	3.5	17.23	1.64	1.67	0.68	3.99	0.32	0.82	0.07	1.21
14-Aug-23	8.3	27.5	0.0	1.0	0.0	0.3	0.0	37.13	3.3	0.0	2.8	1.5	6.0	0.2	3.2	17.11	1.64	1.88	0.76	4.28	0.43	0.79	0.01	1.23
15-Aug-23	11.4	28.9	0.2	1.3	0.0	0.5	0.0	42.23	0.5	0.0	1.8	0.7	6.6	0.3	3.3	13.19	1.62	2.04	0.89	4.55	0.01	0.03	0.00	0.05
16-Aug-23	10.8	27.3	0.1	1.1	0.0	0.3	0.0	39.61	1.2	0.0	1.7	0.7	6.7	0.3	3.2	13.69	1.95	2.64	0.72	5.31	0.24	0.40	0.01	0.65
17-Aug-23	12.7	31.8	0.3	1.3	0.0	0.2	0.0	46.27	1.1	0.0	1.6	1.0	6.9	0.3	3.3	14.21	4.16	5.71	1.44	11.31	0.00	0.00	0.00	0.00
18-Aug-23	14.9	26.5	0.5	1.9	0.0	0.4	0.0	44.08	1.5	0.1	1.6	0.8	5.5	0.1	3.0	12.50	3.70	5.37	1.14	10.22	0.00	0.00	0.00	0.00
19-Aug-23	16.2	23.8	0.5	2.1	0.0	0.6	0.0	43.09	0.5	0.2	2.0	0.5	4.5	0.0	2.9	10.60	4.13	5.98	1.30	11.40	0.00	0.00	0.00	0.00
20-Aug-23	14.6	20.4	0.7	2.2	0.1	0.7	0.0	38.63	0.4	0.0	1.6	0.5	3.3	0.0	2.7	8.57	3.15	4.55	1.14	8.84	0.00	0.00	0.00	0.00
21-Aug-23	15.1	21.0	0.1	2.0	0.0	0.6	0.0	38.85	0.2	0.0	1.5	0.3	4.8	0.0	2.9	9.68	2.24	3.43	1.00	6.66	0.00	0.00	0.00	0.00
22-Aug-23	12.4	25.1	0.5	1.8	0.0	0.6	0.0	40.45	0.6	0.0	1.1	0.4	4.3	0.0	2.8	9.17	1.42	1.50	0.44	3.36	0.09	0.52	0.04	0.64
23-Aug-23	7.2	34.2	0.5	1.1	0.0	0.8	0.0	43.69	4.2	0.1	1.3	1.5	4.4	0.0	2.9	14.31	2.12	2.22	0.66	5.00	0.78	2.04	0.22	3.04
24-Aug-23	7.0	27.3	0.1	0.9	0.0	1.0	0.0	36.31	4.8	0.0	2.9	1.4	4.2	0.0	2.7	16.02	2.17	1.55	0.55	4.28	0.14	0.71	0.06	0.91
25-Aug-23	3.2	24.1	0.0	0.2	0.1	0.8	0.0	28.48	10.2	0.0	4.4	2.9	5.3	0.0	2.7	25.50	1.17	0.55	0.18	1.89	0.41	1.93	0.17	2.51
26-Aug-23	4.5	21.4	0.0	0.6	0.0	0.3	0.0	26.77	8.3	0.4	4.6	2.9	9.5	0.0	3.0	28.66	0.41	0.06	0.10	0.56	0.91	3.30	0.32	4.52
27-Aug-23	6.6	23.6	0.0	0.7	0.0	0.4	0.0	31.34	5.0	0.1	3.1	2.5	7.2	0.0	3.3	21.11	0.27	0.09	0.03	0.39	1.92	4.99	0.68	7.59
28-Aug-23	14.2	20.3	0.3	2.0	0.0	0.5	0.0	37.26	2.6	1.1	2.9	1.1	5.0	0.0	3.3	16.05	1.40	0.97	0.37	2.73	1.80	4.13	0.65	6.57
29-Aug-23	9.6	12.0	0.0	1.1	0.0	0.3	0.0	22.89	1.4	0.2	4.9	0.9	7.7	0.0	3.6	18.73	0.77	0.29	0.18	1.24	0.57	2.51	0.25	3.33
30-Aug-23	14.9	19.9	0.2	1.6	0.0	0.3	0.0	36.89	0.4	0.0	2.4	0.3	7.5	0.0	3.7	14.34	1.51	1.03	0.32	2.86	0.35	1.91	0.13	2.39
31-Aug-23	16.0	20.3	0.4	1.2	0.0	0.1	0.0	37.97	0.0	0.0	1.4	0.2	7.1	0.4	2.4	11.51	1.71	0.40	0.33	2.43	0.03	1.14	0.03	1.20
Total	331.39	768.89	7.42	52.57	28.69	28.75	0.35	1218.07	83.69	2.33	73.64	29.65	127.87	1.99	74.76	393.92	71.19	84.82	25.19	181.20	10.62	29.76	2.83	43.22

Date	15.4 Import and Export of SR with ER & WR during August 2023																							
	Export of ER to SR (ER - SR)				Import of ER from SR (SR - ER)				Export of WR to SR (WR-SR)								Import of WR from SR (SR - WR)							
	ER - SR HVDC Gazuwaka	ER - SR HVDC Talchar -Kolar	ER-SR 765 kV Angul- Srikakulam D/C	Total ER - SR	SR - ER HVDC Gazuwaka	SR - ER HVDC Talchar - 765 kV Angul- Srikakulam D/C	SR-ER 765 kV Angul- Srikakulam D/C	Total SR - ER	WR - SR HVDC Bhadravati	WR - SR 765 kV Sholapur - Raichur 2x5/C	WR-SR 765 kV Wardha - Nizamabad D/C	WR-SR 400kV Kolhapur-Kudgi D/C	WR-SR HVDC Raigarh- Puglur	WR-SR 220kV Xeldem - Ambewadi S/C	WR-SR 220kV Ponda - Ambewadi S/C	Total WR - SR	SR - WR HVDC Bhadravati	SR - WR 765 kV Raichur - Sholapur 2x5/C	SR-WR 765 kV Wardha - Nizamabad D/C	SR-WR 400kV Kolhapur- Kudgi D/C	SR-WR HVDC Raigarh- Puglur	WR-SR 220kV Xeldem - Ambewadi S/C	WR-SR 220kV Ponda - Ambewadi S/C	Total SR - WR
1-Aug-23	0.00	36.60	41.10	77.69	4.78	0.00	0.00	4.78	12.22	5.35	28.31	0.00	29.71	2.14	0.00	77.73	0.00	5.57	0.00	25.36	0.00	0.00	0.00	30.93
2-Aug-23	0.00	40.30	46.35	86.65	7.28	0.00	0.00	7.28	7.21	6.73	34.17	0.00	40.86	2.18	0.00	91.15	0.00	3.20	0.00	25.13	0.00	0.00	0.00	28.33
3-Aug-23	0.00	37.89	48.71	86.60	10.13	0.00	0.00	10.13	4.20	7.60	43.51	0.00	52.24	2.13	0.00	109.68	8.01	3.41	0.00	25.46	0.00	0.00	0.00	36.89
4-Aug-23	0.00	38.54	54.03	92.56	7.20	0.00	0.00	7.20	4.80	15.06	49.96	0.00	32.91	2.27	0.00	105.01	2.35	0.27	0.00	22.92	0.00	0.00	0.00	25.54
5-Aug-23	3.75	38.73	50.90	93.38	3.10	0.00	0.00	3.10	8.28	13.53	45.91	0.00	48.47	2.36	0.94	119.49	0.00	0.39	0.00	23.16	0.00	0.00	0.00	23.55
6-Aug-23	11.79	38.79	45.20	95.78	0.00	0.00	0.00	0.00	10.10	8.90	42.05	0.00	56.90	2.27	0.95	121.15	0.00	1.50	0.00	22.73	0.00	0.00	0.00	24.24
7-Aug-23	12.44	41.35	47.36	101.15	0.00	0.00	0.00	0.00	17.07	9.63	43.94	0.00	86.66	2.33	0.00	159.62	0.00	1.75	0.00	18.64	0.00	0.00	0.00	20.39
8-Aug-23	12.93	45.77	50.54	109.23	0.00	0.00	0.00	0.00	17.70	15.47	49.86	0.00	111.84	2.30	0.00	197.16	0.00	0.75	0.00	17.50	0.00	0.00	0.00	18.24
9-Aug-23	14.46	48.00	52.92	115.37	0.00	0.00	0.00	0.00	14.41	25.17	55.14	0.00	99.59	2.18	0.00	196.48	0.00	0.41	0.00	16.49	0.00	0.00	0.00	16.90
10-Aug-23	12.42	46.57	47.04	106.04	0.00	0.00	0.00	0.00	19.08	17.41	47.53	0.00	86.37	2.19	0.00	172.58	0.00	0.77	0.00	18.48	0.00	0.00	0.00	19.25
11-Aug-23	13.27	47.07	43.44	103.78	0.00	0.00	0.00	0.00	11.62	15.20	44.02	0.00	96.03	2.38	0.00	169.26	0.00	0.21	0.00	19.64	0.00	0.00	0.00	19.85
12-Aug-23	12.11	39.12	48.09	99.32	0.00	0.00	0.00	0.00	17.26	14.90	42.94	0.00	74.71	2.23	0.00	152.05	0.00	1.28	0.00	18.94	0.00	0.00	0.00	20.22
13-Aug-23	12.41	41.55	47.01	100.97	0.00	0.00	0.00	0.00	11.62	11.59	44.03	0.00	67.91	2.07	0.60	137.83	0.00	1.64	0.00	19.11	0.00	0.00	0.00	20.74
14-Aug-23	12.41	42.59	42.40	97.40	0.00	0.00	0.00	0.00	11.07	5.68	38.49	0.00	102.32	2.18	0.00	159.74	0.00	3.26	0.00	23.13	0.00	0.00	0.00	26.40
15-Aug-23	12.43	45.15	38.98	96.56	0.00	0.00	0.00	0.00	19.74	6.95	35.50	0.00	61.32	2.18	0.00	125.69	0.00	4.21	0.00	19.13	0.00	0.00	0.00	23.33
16-Aug-23	12.48	44.51	41.54	98.53	0.00	0.00	0.00	0.00	15.45	9.01	42.60	0.00	85.55	2.13	0.00	154.72	0.00	1.34	0.00	19.99	0.00	0.00	0.00	21.33
17-Aug-23	12.51	34.90	41.70	89.11	0.00	0.00	0.00	0.00	11.43	10.92	44.45	0.00	60.81	2.15	0.00	129.76	0.00	1.59	0.00	17.34	0.00	0.00	0.00	18.94
18-Aug-23	8.76	36.24	42.18	87.18	0.00	0.00	0.00	0.00	12.73	12.03	40.16	0.00	36.16	2.16	0.00	103.24	0.00	1.73	0.00	18.29	0.00	0.00	0.00	20.03
19-Aug-23	8.72	29.18	37.87	75.76	0.00	0.00	0.00	0.00	13.05	5.03	29.63	0.00	22.65	2.11	0.00	72.46	0.00	5.57	0.00	20.13	0.00	0.00	0.00	25.70
20-Aug-23	8.71	36.02	34.28	79.01	0.00	0.00	0.00	0.00	7.25	6.79	26.72	0.00	29.55	2.20	0.00	72.50	0.00	9.38	0.00	20.79	0.00	0.00	0.00	30.17
21-Aug-23	11.46	38.85	40.59	90.90	0.00	0.00	0.00	0.00	16.71	16.54	39.32	0.00	64.85	2.30	0.00	139.72	0.00	0.22	0.00	19.62	0.00	0.00	0.00	19.84
22-Aug-23	14.92	42.45	40.08	97.45	0.00	0.00	0.00	0.00	20.93	19.89	42.08	0.00	92.32	2.36	0.00	177.59	0.00	0.08	0.00	20.02	0.00	0.00	0.00	20.10
23-Aug-23	14.92	46.63	46.98	108.53	0.00	0.00	0.00	0.00	24.08	28.45	52.13	0.00	108.37	2.33	0.00	215.37	0.00	0.50	0.00	16.97	0.00	0.00	0.00	17.47
24-Aug-23	14.21	46.71	43.11	104.03	0.00	0.00	0.00	0.00	21.42	18.60	46.61	0.00	95.34	2.36	0.00	184.33	0.00	0.20	0.00	19.86	0.00	0.00	0.00	20.06
25-Aug-23	13.37	41.60	47.97	102.94	0.00	0.00	0.00	0.00	15.66	27.91	54.81	0.00	97.39	2.33	0.00	198.11	0.00	0.34	0.00	18.03	0.00	0.00	0.00	18.38
26-Aug-23	10.98	44.27	45.59	100.84	0.00	0.00	0.00	0.00	23.25	22.87	45.09	0.00	88.02	2.25	0.73	182.20	0.00	0.97	0.00	17.79	0.00	0.00	0.00	18.76
27-Aug-23	12.40	41.14	45.61	99.16	0.00	0.00	0.00	0.00	21.31	21.22	44.04	0.00	53.34	2.16	0.70	142.76	0.00	0.04	0.00	16.73	0.00	0.00	0.00	16.76
28-Aug-23	12.39	40.32	44.44	97.15	0.00	0.00	0.00	0.00	16.30	20.05	42.50	0.06	66.72	1.66	0.53	147.82	0.00	1.29	0.00	17.78	0.00	0.00	0.00	19.08
29-Aug-23	12.40	40.63	44.90	97.93	0.00	0.00	0.00	0.00	13.24	22.68	45.48	0.00	62.16	2.33	0.00	145.89	0.00	0.00	0.00	17.39	0.00	0.00	0.00	17.39
30-Aug-23	12.39	45.08	42.91	100.39	0.00	0.00	0.00	0.00	21.52	22.08	41.17	0.00	64.59	2.28	0.75	152.39	0.00	0.00	0.00	20.73	0.00	0.00	0.00	20.73
31-Aug-23	10.33	48.03	36.46	94.81	0.00	0.00	0.00	0.00	24.10	8.46	31.67	0.00	60.05	2.11	0.00	126.38	0.00	2.69	0.00	26.14	0.00	0.00	0.00	28.83
TOTAL	321.36	1284.58	1380.27	2986.21	32.48	0.00	0.00	32.48	464.81	451.70	1313.80	0.06	2135.69	68.61	5.23	4439.89	10.36	54.56	0.00	623.43	0.00	0.00	0.01	688.36

16. भूटान , नेपाल, बांग्लादेश एवं म्यान्मार के साथ अंतरराष्ट्रीय विद्युत विनिमय

अप्रैल 2023 से मार्च 2024 April 2023 to March 2024

अंतरराष्ट्रीय विद्युत विनिमय [भारत 'से निर्यात'/'को आयात']

Transnational Exchange ('Export from'/'Import to' India)

माह MONTH	भूटान BHUTAN		नेपाल NEPAL		बांग्लादेश BANGLADESH		म्यान्मार MYANMAR	
	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)
अप्रैल 2023 APR'23	19.40	41.40	357.99	0.00	687.30	0.00	0.73	0.00
मई 2023 MAY'23	2.27	117.99	271.80	0.34	775.10	0.00	0.61	0.00
जून 2023 JUN'23	0.00	626.15	80.00	88.86	743.92	0.00	0.77	0.00
जुलाई 2023 JUL'23	0.00	1291.66	0.00	223.72	780.77	0.00	1.02	0.00
अगस्त 2023 AUG'23	0.00	1244.52	0.00	281.61	767.79	0.00	0.94	0.00
कुल Total	21.67	3321.72	709.78	594.53	3754.88	0.00	4.08	0.00

* Based on daily operational data

Date	16.1 Import from neighbouring countries during August 2023 (All figures in MU)													
	Import from Bhutan								Import from Bangladesh		Import from Nepal			Import from Myanmar
	400 kV Tala-Binaguri I,II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurwar D/C*	400 kV Jigmeling-Alipurwar D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-Aug-23	18.48	5.49	2.89	0.71	5.52	8.33	1.21	0.56	0.00	0.00	0.00	5.29	0.00	0.00
2-Aug-23	18.51	5.51	2.64	0.62	5.22	8.11	1.15	0.56	0.00	0.00	0.00	6.72	0.00	0.00
3-Aug-23	18.41	5.45	2.28	0.41	5.62	8.49	1.06	0.56	0.00	0.00	0.04	7.38	0.00	0.00
4-Aug-23	18.45	5.49	2.33	0.37	5.62	8.50	1.03	0.54	0.00	0.00	0.12	7.69	0.00	0.00
5-Aug-23	18.51	5.52	2.67	0.39	5.69	8.59	1.06	0.55	0.00	0.00	0.20	8.59	0.00	0.00
6-Aug-23	18.58	5.55	2.48	0.37	5.58	8.43	1.14	0.49	0.00	0.00	0.27	7.78	0.00	0.00
7-Aug-23	17.78	5.31	2.60	0.36	5.63	8.51	1.03	0.58	0.00	0.00	0.42	8.65	0.00	0.00
8-Aug-23	17.75	5.28	2.40	0.17	5.59	8.47	1.18	0.47	0.00	0.00	0.60	10.18	0.00	0.00
9-Aug-23	17.62	5.24	2.57	0.33	5.75	8.70	1.10	0.40	0.00	0.00	0.31	10.35	0.00	0.00
10-Aug-23	17.38	5.12	2.25	0.12	5.62	8.49	1.06	0.60	0.00	0.00	0.14	9.47	0.00	0.00
11-Aug-23	17.34	5.10	2.50	0.20	1.67	2.55	1.00	0.00	0.00	0.00	0.10	8.84	0.00	0.00
12-Aug-23	18.35	5.42	2.70	0.33	3.87	5.86	1.25	0.43	0.00	0.00	0.37	10.38	0.00	0.00
13-Aug-23	18.38	5.47	2.38	0.13	4.42	6.73	1.14	0.38	0.00	0.00	0.28	8.92	0.00	0.00
14-Aug-23	17.89	5.30	2.68	0.16	5.19	7.84	0.82	0.41	0.00	0.00	0.16	9.73	0.00	0.00
15-Aug-23	18.40	5.45	2.19	0.00	5.45	8.26	1.29	0.49	0.00	0.00	0.00	7.47	0.00	0.00
16-Aug-23	18.45	5.47	2.63	0.17	5.49	8.33	1.28	0.53	0.00	0.00	0.00	6.72	0.00	0.00
17-Aug-23	18.22	5.33	2.24	0.15	5.30	8.04	0.03	0.49	0.00	0.00	0.04	6.72	0.00	0.00
18-Aug-23	18.22	5.33	2.36	0.08	5.74	8.67	1.29	0.64	0.00	0.00	0.20	7.08	0.00	0.00
19-Aug-23	18.22	5.33	2.37	0.14	5.69	8.59	1.33	0.64	0.00	0.00	0.39	9.30	0.00	0.00
20-Aug-23	18.27	5.37	2.22	0.06	5.71	8.63	1.26	0.60	0.00	0.00	0.26	7.90	0.00	0.00
21-Aug-23	18.28	5.37	2.03	0.00	6.04	9.14	1.20	0.38	0.00	0.00	0.29	8.27	0.00	0.00
22-Aug-23	18.19	5.33	1.76	0.00	6.04	10.16	0.93	0.15	0.00	0.00	0.73	8.86	0.00	0.00
23-Aug-23	18.20	5.36	1.95	0.00	4.07	12.32	1.02	0.11	0.00	0.00	0.48	10.00	0.00	0.00
24-Aug-23	18.18	5.33	1.87	0.00	3.77	11.40	1.12	0.35	0.00	0.00	0.46	10.67	0.00	0.00
25-Aug-23	18.06	5.25	1.44	0.00	3.80	11.47	1.11	0.32	0.00	0.00	0.40	10.15	0.00	0.00
26-Aug-23	18.25	5.36	1.85	0.00	3.80	11.47	1.19	0.28	0.00	0.00	0.32	11.48	0.00	0.00
27-Aug-23	17.23	5.07	1.62	0.00	3.82	11.53	1.01	0.26	0.00	0.00	0.00	10.13	0.00	0.00
28-Aug-23	17.90	5.31	2.02	0.00	3.86	11.65	0.98	0.27	0.00	0.00	0.30	9.64	0.00	0.00
29-Aug-23	18.47	5.50	1.76	0.00	3.82	11.50	1.14	0.32	0.00	0.00	0.27	9.47	0.00	0.00
30-Aug-23	18.16	5.30	1.89	0.00	3.75	11.29	1.18	0.30	0.00	0.00	0.32	7.82	0.00	0.00
31-Aug-23	18.07	5.24	1.82	0.00	3.33	10.02	1.17	0.27	0.00	0.00	0.60	10.34	0.00	0.00
Total	562.20	165.94	69.39	5.26	150.46	280.08	33.76	12.93	0.00	0.00	8.08	271.97	0.00	0.00
Based on SEM/Energy meter data for links where available (*Mangdechu generation receipt at APD through a bypassed arrangement at 400kV Punatsanchu station)														

Date	16.2 Export to neighbouring countries during August 2023													
	(All figures in MU)													
	Export to Bhutan								Export to Bangladesh		Export to Nepal			Export to Myanmar
	400 kV Tala-Binaguri I,II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurwar D/C*	400 kV Jigmeling-Alipurwar D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.69	3.05	0.47	0.00	0.01	0.03
2-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.87	3.20	0.29	0.00	0.02	0.03
3-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.73	3.10	0.00	0.00	0.00	0.03
4-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.66	3.18	0.00	0.00	0.00	0.03
5-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.43	3.59	0.00	0.00	0.04	0.03
6-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.77	3.48	0.00	0.00	0.00	0.01
7-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	20.69	3.23	0.00	0.00	0.00	0.03
8-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.47	3.22	0.00	0.00	0.00	0.03
9-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.48	3.53	0.00	0.00	0.00	0.03
10-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.19	3.58	0.00	0.00	0.00	0.03
11-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.03	21.25	3.23	0.00	0.00	0.00	0.03
12-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.61	3.35	0.00	0.00	0.00	0.03
13-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.68	3.25	0.00	0.00	0.00	0.02
14-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.37	3.29	0.00	0.00	0.00	0.03
15-Aug-23	0.00	0.00	0.00	0.05	0.00	0.00	0.00	0.00	21.68	3.46	0.01	0.00	0.00	0.03
16-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.50	3.36	0.09	0.00	0.00	0.03
17-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.42	2.76	0.00	0.00	0.00	0.03
18-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	19.77	3.22	0.00	0.00	0.00	0.03
19-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.31	3.50	0.00	0.00	0.00	0.03
20-Aug-23	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.40	3.23	0.00	0.00	0.00	0.03
21-Aug-23	0.00	0.00	0.00	0.07	0.00	0.00	0.00	0.00	21.57	3.37	0.00	0.00	0.20	0.03
22-Aug-23	0.00	0.00	0.00	0.15	0.00	0.00	0.00	0.00	21.39	3.25	0.00	0.00	0.00	0.03
23-Aug-23	0.00	0.00	0.00	0.09	0.00	0.00	0.00	0.00	21.43	3.12	0.00	0.00	0.00	0.02
24-Aug-23	0.00	0.00	0.00	0.16	0.00	0.00	0.00	0.00	21.46	3.10	0.00	0.00	0.00	0.03
25-Aug-23	0.00	0.00	0.00	0.25	0.00	0.00	0.00	0.00	21.31	2.71	0.00	0.00	0.00	0.04
26-Aug-23	0.00	0.00	0.00	0.21	0.00	0.00	0.00	0.00	21.38	3.02	0.00	0.00	0.04	0.01
27-Aug-23	0.00	0.00	0.00	0.45	0.00	0.00	0.00	0.00	21.49	2.99	0.08	0.00	0.24	0.03
28-Aug-23	0.00	0.00	0.00	0.48	0.00	0.00	0.00	0.00	21.72	3.47	0.00	0.00	0.15	0.03
29-Aug-23	0.00	0.00	0.00	0.44	0.00	0.00	0.00	0.00	21.57	3.53	0.00	0.00	0.00	0.03
30-Aug-23	0.00	0.00	0.00	0.10	0.00	0.00	0.00	0.00	21.37	3.39	0.00	0.00	0.00	0.05
31-Aug-23	0.00	0.00	0.00	0.14	0.00	0.00	0.00	0.00	21.32	3.53	0.00	0.00	0.00	0.04
Total	0.00	0.00	0.00	2.60	0.00	0.00	0.00	0.03	664.00	101.28	0.95	0.00	0.73	0.94

Based on SEM/Energy meter data for links where available (*Mangdechu generation receipt at APD through a bypassed arrangement at 400kV Punatsanchu station)

17. एसटीओए (द्विपक्षीय एवं सामूहिक) एवं डी एस एम बिलिंग का ब्योरा – अगस्त 2023

STOA (BILATERAL AND COLLECTIVE) & DSM BILLING DETAILS - AUGUST 2023

द्विपक्षीय एसटीओए BILATERAL SHORT TERM OPEN ACCESS

अगस्त 2023	AUG 2023		Apr'23- AUG'23	
नोडल क्षे.भा.प्रे.के. का नाम Name of Nodal RLDC	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Energy Approved(MU)	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Energy Approved (MU)
ऊ. क्षे. NR	1209	6224	5345	22415
प.क्षे. WR	872	1537	4714	10855
द.क्षे. SR	1697	3651	4935	13586
पू.क्षे. ER	835	827	3780	4623
पूर्वोत्तर क्षे. NER	228	99	655	353
कुल TOTAL	4841	12338	19429	51832

एसटीओए SHORT TERM OPEN ACCESS

	सामूहिक एसटीओए Collective STOA		द्विपक्षीय एसटीओए Bilateral STOA	
माह MONTH	क्रेताओं / विक्रेताओं की सं. NO. of Buyers/Sellers	अनुमोदित ऊर्जा (मि.यु.) Approved Energy (MU)	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Approved Energy (MU)
अप्रैल 2023 Apr'23	5580	6941	3322	9714
मई 2023 May'23	5798	6626	3469	8418
जून 2023 Jun'23	5783	6966	3925	10583
जुलाई 2023 Jul'23	6428	6719	3872	10780
अगस्त 2023 Aug'23	5954	6805	4841	12338
कुल TOTAL	29543	34057	19429	51832

* Approved Energy (MU) includes the Real Time Market (RTM) transactions (started from 1st Jun-20) as well, while No. of Buyers/Sellers are excluding RTM transactions.

** Approved Energy (MU) includes the Real Time Market (RTM) transactions (started from 1st Jun-20) as well, while No. of Buyers/Sellers are excluding RTM transactions

मासिक डी एस एम बिलिंग का ब्योरा* 2021-22
MONTHLY DSM BILLING DETAILS* 2021-22

अनंतिम आँकड़े
Provisional data
subject to change
करोड़ रु. में (RS. IN CRORES)

क्षेत्र REGION →	उत्तरी क्षेत्र NORTH	पश्चिमी क्षेत्र WEST	दक्षिणी क्षेत्र SOUTH	पूर्वी क्षेत्र EAST	पूर्वोत्तर क्षेत्र NORTH EAST
सप्ताह WEEK ↓					
31.07.23 to 06.08.23	90.05	159.27	167.19	131.50	---
07.08.23 to 13.08.23	184.16	328.08	376.24	289.29	---
14.08.23 to 20.08.23	210.64	300.98	340.78	315.87	---
21.08.23 to 27.08.23	263.84	382.95	309.29	271.51	---

* Amount shown is Payable to DSM pool ^Provisional Data

18. पावर मार्केट की सूचना (स्रोत : आई ई एक्स. एच पी एक्स.आई एच.) POWER MARKET INFORMATION (Source IEX & PXIL) पावर एक्स्चेंज के माध्यम से बिनिमय - माह:- अगस्त 2023 EXCHANGES THROUGH POWER EXCHANGES - AUGUST 2023						
क्र. सं. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU			
			Integrated Day Ahead Market (I-DAM)		Real Time Market (RTM)	
			बिक्रय Sale	क्रय Purchase	बिक्रय Sale	क्रय Purchase
1	पंजाब Punjab	उत्तरी क्षेत्र NR	117.72	30.56	48.70	82.37
2	हरियाणा Haryana		62.59	70.00	22.32	87.63
3	राजस्थान Rajasthan		27.62	302.72	118.52	173.51
4	दिल्ली Delhi		312.67	25.84	124.40	33.93
5	उत्तर प्रदेश Uttar Pradesh		448.66	162.31	94.97	152.30
6	उत्तराखण्ड Uttarakhand		23.23	7.56	23.02	15.72
7	हिमाचल प्रदेश Himachal Pradesh		134.77	3.31	95.45	8.06
8	जम्मू और कश्मीर J & K		39.31	0.00	97.05	0.00
9	केन्द्र शासित चंडीगढ़ UT Chandigarh		54.71	0.06	0.57	0.15
10	ए डी हाइड्रो AD Hydro		33.52	0.00	5.57	0.00
11	कारगम वॉंगतू Karcham Wangtoo		61.17	0.00	1.28	0.00
12	श्री सीमेंट Shree Cement		23.63	0.00	5.49	0.00
13	नाथपा झाकरी Nathpa Jhakri		0.00	0.00	0.00	0.00
14	लॉको बुधिल Lanco Budhil		6.27	0.00	0.06	0.00
15	सिंगरौली Singrauli		0.47	0.00	4.83	0.00
16	दादरी-I Dadri TPS		0.14	0.00	4.41	0.00
17	दादरी-II Dadri stg-II		1.45	0.00	8.38	0.00
18	उंचाहार-I Unchahar-I TPS		0.27	0.00	1.87	0.00
19	उंचाहार-II Unchahar-II TPS		0.91	0.00	2.23	0.00
20	उंचाहार-III Unchahar-III TPS		0.34	0.00	1.39	0.00
21	रिहंद-I Rihand STPS-I		12.98	0.00	3.96	0.00
22	रिहंद-II Rihand STPS-II		10.15	0.00	8.77	0.00
23	रिहंद-III Rihand STPS-III		12.58	0.00	4.05	0.00
24	एपीसीपीएल झुझर APCPL Jhajar		0.97	0.00	7.33	0.00
25	सैज Sainj HEP		40.38	0.00	0.58	0.60
26	दादरी गैस Dadri GPP		0.00	0.00	0.00	0.00
27	औरंगा गैस NTPC Auraya		0.00	0.00	0.00	0.00
28	अंता गैस NTPC Anta		0.00	0.00	0.00	0.00
29	रामपुर एवर्होपी RAMPUR HEP		0.00	0.00	0.00	0.00
30	उंचाहार-IV UNCHAHAR-IV		0.52	0.00	3.65	0.00
31	एनटीपीसी कोलहाम NTPC KOLDAM		0.00	0.00	0.00	0.00
32	कोटेश्वर Koteswar		0.00	0.00	0.00	0.00
33	टांडा स्टेज-२ Tando Stg-2		0.96	0.00	4.33	0.00
34	अदानी सौर एनर्जि टू लिमिटेड Adani Solar Energy Jodhpur Two Limited		11.61	0.00	0.00	0.00
35	सिंगोली भटवारी ह्ये Singoli Bhatwari HEP		13.50	0.00	4.33	0.29
36	रेलवे Railways		0.00	18.31	0.00	9.15
37	तिहरी Tehri		0.00	0.00	0.00	0.00
38	Renew Solar Energy (Uarkhand Three) Private Limited (RSE/TP1)		0.00	0.00	0.00	0.00
39	सोरंग एच ई सी. Sorang HEP, (Himachal Sorang Power Private Ltd)		0.00	0.00	1.48	0.00
40	अदानी सौर ऊर्जा जैसलमेर वन लिमिटेड (सौर) Adani Hybrid Energy Jaisalmer One Limited (Solar)		0.00	0.00	0.00	0.00
41	अदानी सौर ऊर्जा जैसलमेर टू लिमिटेड (सौर) Adani Hybrid Energy Jaisalmer Two Limited (Solar)		0.00	0.00	0.00	0.00
42	अदानी सौर ऊर्जा जैसलमेर थ्री लिमिटेड (सौर) Adani Hybrid Energy Jaisalmer Three Limited (Solar)		0.00	0.00	0.00	0.00
43	अयाना रिन्यूएबल पावर वन लिमिटेड Ayana Renewable Power One Private Limited		0.00	0.00	0.00	0.00
44	Adani Hybrid Energy Jaisalmer Four Limited (Solar)अदानी सौर ऊर्जा जैसलमेर चार लिमिटेड (सौर)		0.00	0.00	0.00	0.00
45	रिनीव सौर ऊर्जा प्राइवेट लिमिटेड Renew Solar Urja private limited.		0.00	0.00	0.00	0.00
46	NEA-NR एन ई ए एन और		0.00	0.11	0.00	0.00
47	रेनैव सूर्या रवि प्राइवेट लिमिटेड (सौर) Renew Surya Ravi Private Limited (Solar)		26.80	0.00	0.26	0.00
48	अजुंजे पावर प्राइवेट लिमिटेड (सौर) Azure Power Maple Pvt Ltd (Solar)		0.00	0.00	0.00	0.00
49	अदानी ग्रीन हाइब्रिड सौर जैसलमेर Adani Green Hybrid Solar Jaisalmer		0.00	0.00	0.00	0.00
50	अदानी ग्रीन हाइब्रिड पवन जैसलमेरAdani Green Hybrid Wind Jaisalmer		0.00	0.00	0.00	0.00
51	अदानी ग्रीन सौर जैसलमेर Adani Green Solar Jaisalmer		0.00	0.00	0.00	0.00
52	ABC Renewable Energy (RJ-01) Private Limited एबीसी रीनोवैबल एनर्जी (आर-01) प्राइवेट लिमिटेड		0.00	0.00	0.00	0.00
53	SBSR Power Cleantech Eleven Private Limited एसबीएसआर पावर क्लीन्टेक लिमिटेड		12.15	0.00	0.00	0.00
54	टनकपुर पावर स्टेशन Tanakpur Power Station		0.00	0.00	0.00	0.00
55	उरी पावर स्टेशन Uri I Power Station		0.00	0.00	0.00	0.00
56	उरी पावर स्टेशन Uri II Power Station		0.00	0.00	0.00	0.00
57	चमेरा पावर स्टेशन Chamera I Power Station		0.00	0.00	0.00	0.00
58	चमेरा पावर स्टेशन Chamera II Power Station		0.00	0.00	0.00	0.00
59	चमेरा पावर स्टेशन Chamera III Power Station		0.00	0.00	0.00	0.00
60	धौलीगंगा पावर स्टेशन Dhauliganga Power Station		0.00	0.00	0.00	0.00
61	दुलहासती पावर स्टेशन Dulhashti Power Station		0.00	0.00	0.00	0.00
62	किशनगंगा पावर स्टेशन Kishanganga Power Station		0.00	0.00	0.00	0.00
63	पार्वती पावर स्टेशन Parbati III Power Station		0.00	0.00	0.00	0.00
64	सेवा पावर स्टेशन Sewa II Power Station		0.00	0.00	0.00	0.00
65	सलाव पावर स्टेशन Salal Power Station		0.00	0.00	0.00	0.00
66	ADANI SOLAR ENERGY JAISALMER ONE PRIVATE LIMITED AHS अदानी सौर ऊर्जा जैसलमेर वन प्राइवेट लिमिटेड ए एच वन		0.00	0.00	0.00	0.00
67	पार्वती H-ई प्रोजेक्ट Parbati II HE Project		0.00	0.00	0.00	0.00
68	एनटीपीसी अंता जीपीएस NTPC ANTGA GPS RLNG		0.00	0.00	0.00	0.00
69	एनटीपीसी औरंगा जीपीएस NTPC AURAYA GPS RLNG		0.00	0.00	0.00	0.00
70	एनटीपीसी दादरी जीपीएस NTPC DADRI GPS RLNG		0.00	0.00	0.00	0.00
71	अदानी सौर ऊर्जा जैसलमेर चार लिमिटेड ADANI HYBRID ENERGY JAISALMER FOUR LIMITED AHW		0.00	0.00	0.00	0.00

18. पावर मार्केट की सूचना (स्रोत : आई ई एक्स. एच पी एक्स.आई ई एच.) POWER MARKET INFORMATION (Source IEX & PXIL) पावर एक्चेंज के माध्यम से बिनिमय - माह:- अगस्त 2023 EXCHANGES THROUGH POWER EXCHANGES- AUGUST 2023								
क्र. सं. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU					
			Integrated Day Ahead Market (I-DAM)		Real Time Market (RTM)		Total (I-DAM-RTM)	
			विक्रय Sale	क्रय Purchase	विक्रय Sale	क्रय Purchase	विक्रय Sale	क्रय Purchase
72	मध्य प्रदेश Madhya Pradesh	पश्चिमी क्षेत्र WR	264.37	52.83	812.85	14.32	1077.22	67.15
73	महाराष्ट्र Maharashtra		125.20	391.30	80.42	173.50	205.62	564.80
74	गुजरात Gujarat		62.55	458.19	30.25	73.02	92.80	531.21
75	छत्तीसगढ़ Chhattisgarh		212.99	25.87	116.46	21.67	329.45	47.54
76	गोवा डब्लू और Goa WR		3.68	5.14	6.26	0.24	9.94	5.38
77	जिंदल पावर JINDAL POWER		28.44	0.00	4.02	3.11	32.46	3.11
78	लॉको Lanco		0.00	0.00	0.00	0.00	0.00	0.00
79	ए सी बी आई एल ACBL		30.44	0.00	8.49	0.04	38.93	0.04
80	जिंदल स्टील JINDAL STEEL		116.46	0.00	2.68	1.85	119.14	1.85
81	बालको 2 BALCO 2		0.00	0.00	0.55	0.00	0.55	0.00
82	जीएमआर वरौरा GMR Warora		14.07	0.00	1.44	0.00	15.51	0.00
83	एस्सर पावर एम पी Essar Power MP Ltd		25.64	0.00	9.57	0.00	35.21	0.00
84	के एस के महानदी KSK Mahanadi		0.00	0.00	0.00	0.00	0.00	0.00
85	जिंदल पावर लिमिटेड Jindal Power Ltd. Stg-II		34.95	0.00	7.40	0.01	42.35	0.01
86	रायगढ़ एनर्जि लिमिटेड Raigarh Energy Ltd.		30.63	0.00	1.26	0.29	31.89	0.29
87	डी बी पावर DB Power		122.00	0.00	1.32	0.00	123.32	0.00
88	धारीवाल Dhariwal		0.00	0.00	0.00	0.00	0.00	0.00
89	जेपी निगरी JAYPEE NIGRIE		41.17	0.00	0.15	0.00	41.32	0.00
90	डीजेन मेगा पावर DGEN Mega power		0.00	0.00	0.00	0.00	0.00	0.00
91	एम बी पावर MB Power		111.67	0.00	18.86	0.00	130.53	0.00
92	अदानी पावर स्टेज 3 Adani Power STG3		0.00	0.00	0.00	0.00	0.00	0.00
93	टोरेंट पावर Torrent Power		0.00	0.00	0.00	0.00	0.00	0.00
94	मारुति क्लीन कोल पावर Maruti Clean Coal Power		8.54	0.00	2.54	0.06	11.08	0.06
95	झाबुआ पावर Jhabua Power		8.38	0.00	4.54	0.18	12.92	0.18
96	विंध्याचल स्टेज-1 Vindhyachal stg-1		0.04	0.00	1.07	0.00	1.11	0.00
97	विंध्याचल स्टेज-2 Vindhyachal stg-2		0.00	0.00	0.92	0.00	0.92	0.00
98	विंध्याचल स्टेज-3 Vindhyachal stg-3		0.00	0.00	0.62	0.00	0.62	0.00
99	विंध्याचल स्टेज-4 Vindhyachal stg-4		0.00	0.00	0.44	0.00	0.44	0.00
100	विंध्याचल स्टेज-5 Vindhyachal stg-5		0.00	0.00	0.63	0.00	0.63	0.00
101	मौदा स्टेज-1 Mouda Stg-1		0.00	0.00	1.66	0.00	1.66	0.00
102	सिपत स्टेज-1 Sipat Stg-1		0.00	0.00	0.56	0.00	0.56	0.00
103	सिपत स्टेज-2 Sipat Stg-2		0.00	0.00	0.53	0.00	0.53	0.00
104	सासन Sasan UMPP		0.00	0.00	6.14	0.00	6.14	0.00
105	भिलाई एनएसएससीएल NSPCL Bhilai		0.00	0.00	0.00	0.00	0.00	0.00
106	कोरबा स्टेज-3 Korba Stg 3		0.00	0.00	0.22	0.00	0.22	0.00
107	टीआरएन एनर्जी TRN Energy		0.00	0.00	10.81	0.00	10.81	0.00
108	गांधार Gandhar		0.00	0.00	0.00	0.56	0.00	0.56
109	कोरबा Korba		0.00	0.00	0.68	0.00	0.68	0.00
110	आर के एम पावर RKM Power		7.61	0.00	10.84	0.00	18.45	0.00
111	कावस Kawas		0.00	0.00	0.00	0.32	0.00	0.32
112	मौदा स्टेज-2 Mouda Stg-2		0.04	0.00	3.81	0.00	3.85	0.00
113	एस के एस पावर SKS Power		21.15	0.00	3.33	0.75	24.48	0.75
114	एन टी पि सी सोलापुर NTPC Solapur		0.00	0.00	4.03	0.00	4.03	0.00
115	एन टी पि सी गदखरा NTPC Gadakhara		0.00	0.00	7.63	0.00	7.63	0.00
116	एन टी पि सी लारा NTPC Lara		0.00	0.00	0.28	0.00	0.28	0.00
117	रायपुर एनर्जिन Raipur Energen	0.00	0.00	0.00	0.00	0.00	0.00	
118	आर्सेलर मितल ArcelorMittal Nippon steel (ESL)	0.00	41.52	0.00	17.41	0.00	58.92	
119	खरगोन Khargone STPP	0.00	0.00	5.67	0.00	5.67	0.00	
120	कोस्टल गुजरात पावर लिमिटेड Coastal Gujarat Power Limited	0.00	0.00	0.00	0.00	0.00	0.00	
121	कंटीन्यूम पावर ट्रेडिंग Continuum Power Trading (TN) Private Limited	0.52	0.00	0.00	0.00	0.52	0.00	
122	ऑस्ट्रो एनर्जी प्राइवेट लिमिटेड Ostro Energy Private Limited (OEPL)	0.00	0.00	0.00	0.00	0.00	0.00	
123	दमन डीयू/दादरा और नगर हवेलीDaman & Diu/Dadar and Nagar Haveli	0.00	50.97	9.13	18.19	9.13	69.16	
124	अदानी विंड एनर्जी Adani Wind Energy Kutchh Five Limited	0.00	0.00	0.00	0.00	0.00	0.00	
125	आर जी पि पि एल RGPPL	3.60	0.00	0.00	0.49	3.60	0.49	
126	Kakrapar Atomic Power Station काकरपर अटॉमिक पावर स्टेशन	0.00	0.00	0.00	0.00	0.00	0.00	
127	BALCO बालको	0.00	7.22	0.00	10.91	0.00	18.13	
128	अदानी विंड एनर्जी कच कोर लिमिटेड नखलन ADANI WIND ENERGY KUTCHH FOUR Ltd. Nakhilnana	80.55	0.00	0.00	0.00	80.55	0.00	
129	एनटीपीसी झनोर गांधार जीपीएस NTPC Jhanor Gandhar GPS RLNG	0.00	0.00	0.00	0.00	0.00	0.00	
130	एनटीपीसी कावस गपद NTPC Kawas GPS RLNG	0.00	0.00	0.00	0.00	0.00	0.00	
131	रातनागरी गैस और पावर प्राइवेट लिमिटेड Ratnagiri Gas and Power Private Limited-LTRLNG	0.00	0.00	0.00	0.00	0.00	0.00	
132	विंड फाइव एनर्जी लिमिटेड WIND FIVE RENERGY LIMITED	7.44	0.00	0.00	0.00	7.44	0.00	
133	एनटीपीसी झनोर गांधार जीपीएस कॉम गैस NTPC Jhanor Gandhar GPS_COMGAS	0.00	0.00	0.00	0.00	0.00	0.00	
134	धारीवाल एस टी यू DHARIWAL STU OTH	5.99	0.00	0.27	0.00	6.26	0.00	
135	धारीवाल आइ एस टी एस Dhariwal ISTS	0.96	0.00	0.16	0.00	1.12	0.00	
136	इनोक्स ग्रीन एनर्जि सर्विसेस लिमिटेड INOX GREEN ENERGY SERVICES LIMITED	2.84	0.00	0.00	0.00	2.84	0.00	
137	अदानी पावर लिमिटेड रायपुर टीपीपी Adani Power Limited Raipur TPP	21.82	0.00	3.23	0.00	25.06	0.00	
138	टाटा पावर कंपनी लिमिटेड (MTPS) The Tata Power Co Ltd (MTPS)	0.79	0.00	3.24	0.00	4.03	0.00	
139	मसाया सोलर एनर्जी प्राइवेट लिमिटेड Masaya Solar Energy Private Limited	0.00	0.00	0.07	0.00	0.07	0.00	

18. पावर मार्केट की सूचना (स्रोत : आई ई एक्स. एच पी एक्स.आई एच.) POWER MARKET INFORMATION (Source IEX & PXI) पावर एक्चेंज के माध्यम से विनिमय - माह:- अगस्त 2023 EXCHANGES THROUGH POWER EXCHANGES- AUGUST 2023						
क्र. सं. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU			
			Integrated Day Ahead Market (I-DAM)		Real Time Market (RTM)	
			बिक्री Sale	क्रय Purchase	बिक्री Sale	क्रय Purchase
140	आंध्र प्रदेश Andhra Pradesh	दक्षिणी क्षेत्र SR	48.94	496.20	54.10	263.14
141	कर्नाटक Karnataka		91.46	226.57	23.67	290.09
142	केरल Kerala		2.33	105.46	2.53	236.70
143	तमिलनाडु Tamilnadu		72.00	181.41	46.43	105.99
144	पांडिचेरी Pondicherry		35.49	0.00	11.40	0.03
145	गोवा एस आर Goa SR		0.00	5.96	0.28	1.16
146	तेलंगाना TELANGANA		48.06	488.53	23.39	571.65
147	कोस्टल एनर्जेन Costal Energen		0.00	0.00	0.00	0.00
148	आई एल और एफ एस IL&FS		10.14	0.00	3.32	0.00
149	सिंहद्री स्टेज -2 Simhadri Stag-2		0.00	0.00	1.34	0.00
150	एनएससी इंडिया स्टेशन 1 विस्तार NLC India Station I Expansion		0.00	0.00	0.62	0.00
151	एन एल सी स्टेज-1 NLC TPS-I Stag-1		0.00	0.00	0.00	0.00
152	एन एल सी स्टेज-2 NLC TPS-II Stag-2		0.00	0.00	0.00	0.00
153	रामगुंडम स्टेज-1 Ramagundam Stag-1		0.01	0.00	1.87	0.00
154	तलचर स्टेज -2 Talcher Stag-2		0.00	0.00	0.70	0.00
155	रामगुंडम स्टेज-3 Ramagundam Stag-3		0.00	0.00	0.46	0.00
156	सेम्कोर्प गायात्री Sembcorp Gayatri		39.35	0.00	12.42	0.00
157	वल्लूर Vallur		0.00	0.00	0.00	0.00
158	कुड्गी NTPC Kudgi		7.01	0.00	4.10	0.00
159	सिंहद्री स्टेज -1 Simhadri Stag-1		0.00	0.00	0.32	0.00
160	एन एल सी टी पी एस -11 एक्सपन NLC TPS-II Expn		0.00	0.00	0.00	0.00
161	एनटीपीएल NTPL	पूर्वी क्षेत्र ER	0.00	0.00	1.38	0.00
162	नयवेली न्यू थर्मल पावर प्रोजेक्ट Neyveli New Thermal Power Project		0.00	0.00	1.22	0.00
163	रामगुंडम फ्लोटिंग सोलर पी वी स्टेशन Ramagundam Floating Solar PV Station		6.71	0.00	0.00	0.00
164	सिंहद्री फ्लोटिंग सोलर Simhadri Floating solar		1.76	0.00	0.00	0.00
165	सिंहद्री एफएसपी 15 एससी प्रोजेक्ट Simhadri FSP 15 MW Project		2.65	0.00	0.00	0.00
166	सेम्कोर्प एनर्जी इंडिया लिमिटेड Sembcorp energy india limited		15.20	0.00	6.20	0.00
167	जे एन डब्ल्यू रिनैव एनर्जी टू लिमिटेड JSW RENEW ENERGY TWO LIMITED		0.00	0.00	0.00	0.00
168	ओस्ट्रो कन्नड पावर प्राइवेट लिमिटेड Ostro Kannada Power Private Limited		14.60	0.00	2.95	0.00
169	सिम्हापुरी एनर्जी लिमिटेड Simhapuri Energy Limited		10.84	0.00	11.39	0.00
170	परमपुञ्ज सोलर एनर्जी प्राइवेट लिमिटेड PARAMPUJA SOLAR ENERGY PRIVATE LIMITED		0.00	0.00	0.00	0.00
171	पश्चिम बंगाल West Bengal		18.65	729.58	66.80	153.09
172	ओडिशा Odisha		25.24	40.94	135.09	89.14
173	बिहार Bihar		224.13	12.34	239.38	15.04
174	झारखंड Jharkhand		23.29	24.43	43.63	26.08
175	सिक्किम Sikkim		5.05	0.00	3.78	0.82
176	दामोदर घाटी परियोजना DVC		16.03	30.72	9.18	40.07
177	मैथन पावर लिमिटेड Maithon P. Ltd		0.00	0.00	0.00	0.00
178	आधुनिक पा. लिमिटेड Adhunik P.Ltd		0.35	0.00	1.91	0.00
179	चुराचन Churachen HEP		11.98	0.00	0.00	0.00
180	जीएमआर कमलंगा GMR Kamalanga		0.96	0.00	0.07	0.00
181	खिदर आई पी टी एल JPPL		34.06	0.00	2.14	0.00
182	जोरथांग Jorethang		0.00	0.00	0.79	0.00
183	फरक्का-III Farakka-III		0.00	0.00	0.83	0.00
184	बाढ़-II Barh Stage-II		0.00	0.00	4.65	0.00
185	कहालगाँव-II Kahalgaon Stage-II		0.04	0.00	5.19	0.00
186	फरक्का Farakka		0.07	0.00	2.43	0.00
187	कहालगाँव Kahalgaon		1.86	0.00	2.30	0.00
188	तालचर Talcher		0.00	0.00	0.53	0.00
189	तीस्ता-III Teesta-III		0.00	0.00	0.00	0.00
190	दिखु Diichu HEP		4.68	0.00	0.00	0.00
191	ताशिदिंग Tashiding HEP		0.00	0.00	3.75	0.00
192	केबीपुएनएल KBUNL		0.00	0.00	0.50	0.00
193	दर्लिपल्ली Darlipalli		0.00	0.00	0.74	0.00
194	नबीनगर NPGC Nabnagar		0.00	0.00	16.46	0.00
195	नेपाल विद्युत प्राधिकरण Nepal Electricity Authority		269.61	0.00	0.00	269.61
196	Barh STPS Stage-I बाढ़ एसटीपीएस स्टेज-1		0.06	0.00	4.21	0.00
197	NTPC North Karanpura STPS नॉर्थ करनपुरा		0.00	0.00	0.00	0.00
198	Druk Green Power Corporation Limited-Bhutan ड्रुक ग्रीन पावर कॉर्पोरेशन लिमिटेड-भूटान		0.00	0.00	0.00	0.00
199	NTPC BARH Unit 2 एनटीपीसी बाढ़ 1		0.00	0.00	0.00	0.00
200	सिक्किम ऊर्जा लिमिटेड Sikkim Urja Limited		35.11	0.00	0.02	0.00

18. पावर मार्केट की सूचना (स्रोत : आई ई एक्स. एन पी एक्स.आई एन.)								
POWER MARKET INFORMATION (Source IEX & PEX)								
पावर एक्स्चेंज के माध्यम से विनिमय - माह:- अगस्त 2023								
EXCHANGES THROUGH POWER EXCHANGES- AUGUST 2023								
क्र. सं. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU					
			Integrated Day Ahead Market (I-DAM)		Real Time Market (RTM)		Total (I-DAM+RTM)	
			विक्रय Sale	क्रय Purchase	विक्रय Sale	क्रय Purchase	विक्रय Sale	क्रय Purchase
201	अरुणाचल प्रदेश Arunachal Pradesh	पूर्वोत्तर क्षेत्र NER	18.45	0.00	6.06	2.95	24.51	2.95
202	असम Assam		21.05	53.41	34.65	31.92	55.70	85.33
203	मणिपुर Manipur		1.14	0.00	22.34	1.01	23.48	1.01
204	मेघालय Meghalaya		21.56	14.42	0.69	4.37	22.25	18.79
205	मिज़ोरम Mizoram		12.11	0.00	0.07	0.00	12.18	0.00
206	नागालैंड Nagaland		6.92	0.00	2.94	0.00	9.86	0.00
207	त्रिपुरा Tripura		0.00	0.92	16.36	1.96	16.36	2.88
208	अगरतला जीटीपीपी Agartala GTPP_AGO		0.00	0.00	0.17	0.00	0.17	0.00
209	असम जीबीपीपी Assam GBPP_KTD		0.00	0.00	0.12	0.00	0.12	0.00
210	पलाताना Palatana		8.55	0.00	8.71	0.00	17.26	0.00
211	दोयांग HEP दोयांग हेप		0.00	0.00	0.00	0.00	0.00	0.00
212	बोंगाईगाँव Bongaigaon TPP		6.08	0.00	6.44	0.00	12.52	0.00
213	कामेंग Kameng HEP		4.10	0.00	2.58	0.00	6.68	0.00
214	रंगानन्दी हाइड्रो पावर स्टेशन Ranganadi Hydro Power Station		0.00	0.00	0.00	0.00	0.00	0.00
215	लोकटक पावर स्टेशन LOKTAK POWER STATION		0.00	0.00	0.00	0.00	0.00	0.00
			4065	4065	2740	2740	6804	6804

19. INFORMATION ABOUT RENEWABLE ENERGY
CERTIFICATE MECHANISM
MONTH : AUGUST 2023

RE Source & Unit wise break up (01.08.2023-31.08.2023)

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	0	0	9	3
2	Urban or Municipal Waste	0	0	0	0
3	Solar Thermal	0	0	0	0
4	Solar PV	46	22	0	0
5	Small Hydro	0	0	0	0
6	Others	0	0	0	0
7	Geothermal	0	0	0	0
8	Biomass	0	0	0	0
9	Bio-fuel cogeneration	4	1	4	1
	Total	50	23	13	4

RECs Issued (01.08.2023-31.08.2023)

Sr.No.	Non Solar	Solar	Total
1	434667	135030	569697

Redemption of REC (01.08.2023-31.08.2023)

Sr.No.	Non Solar	Solar	Total
1	237461	104112	341573

19. INFORMATION ABOUT RENEWABLE ENERGY
CERTIFICATE MECHANISM
MONTH : AUGUST 2023

RE Source & Unit wise break up (Apr'23-Aug'23)

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	339	11	434	11
2	Urban or Municipal Waste	0	0	0	0
3	Solar Thermal	0	0	0	0
4	Solar PV	104	32	65	3
5	Small Hydro	42	7	36	6
6	Others	0	0	0	0
7	Geothermal	0	0	0	0
8	Biomass	5	1	5	1
9	Bio-fuel cogeneration	8	2	23	5
	Total	498	53	563	26

RECs Issued (Apr'23-Aug'23)

Sr.No.	Non Solar	Solar	Total
1	1751720	550648	2302368

Redemption of REC (Apr'23-Aug'23)

Sr.No.	Non Solar	Solar	Total
1	1973616	402640	2376256

19. INFORMATION ABOUT RENEWABLE ENERGY
CERTIFICATE MECHANISM
MONTH : AUGUST 2023

RE Source & Unit wise break up Since Inception to Aug'23

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	3057	518	2895	517
2	Urban or Municipal Waste	0	0	0	0
3	Solar Thermal	0	0	0	0
4	Solar PV	1373	524	1250	468
5	Small Hydro	686	40	692	41
6	Others	4	2	3	1
7	Geothermal	0	0	0	0
8	Biomass	402	37	378	35
9	Bio-fuel cogeneration	817	90	383	55
	Total	6339	1211	5601	1117

RECs Issued since Inception to Aug'23

Sr.No.	Non Solar	Solar	Total
1	89631860	12961386	102593246

Redemption of REC since Inception to Aug'23

Sr.No.	Non Solar	Solar	Total
1	69501801	12031028	81532829

REC Closing balance as on 31.08.2023

Sr.No.	Non Solar	Solar	Total
1	20130059	930358	21060417

20.Details of Grid Events during the Month of August 2023



Northern Region

Sl No.	Category of Grid Event (GI for 2/ GD-1 to GD-3)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GI-2	Haryana	01-Aug-2023 07:51	01-Aug-2023 08:29	00:38	0	0	0.000	0.000	54742	62652	i) During antecedent condition, 800 KV HVDC Kurukshetra(PG) Pole-1, 2, 3 & 4 were carrying 1187 MW, 1198 MW, 1191 MW and 1195 MW respectively from Champa to Kurukshetra. Total power order was approx. 5000MW. ii) As reported, at 07:51:00hrs, 800 KV HVDC Kurukshetra(PG) Pole-02 & 04 got blocked. "Pole 2 T-zone" protection latched at Kurukshetra end. Due to T-zone protection Pole 2 blocked and generated CAT B sequence as per protection philosophy to isolate Parallel Pole also. Due to this, Pole 4 got blocked on CAT B protection initiated by Pole 2. iii) As per protection philosophy, T-zone protection in Pole 2 compare following three currents – Pole 2 Idt current, Pole 2 Ihi current & Parallel Pole 4 Idt current. The parallel Pole 4 Idt current signal is received by Pole 2 through Bipole cable. iv) As reported by POWERGRID, Pole 2 T-zone protection got latched due to faulty Pole 4 Idt current measurement in Bipole 2 lane 1. The probable cause of faulty measurement was suspected to be failure of 5008 card. v) As per PMU at Kurukshetra(PG), no fault is observed in the system, but fluctuation in voltage is observed. vi) As per SCADA, no load loss is observed in Haryana control area.	1) 800 KV HVDC Kurukshetra(PG) Pole-02 2) 800 KV HVDC Kurukshetra(PG) Pole-04
2	GI-2	Uttar Pradesh	03-Aug-2023 05:07	03-Aug-2023 08:10	03:03	0	0	0.000	0.000	48238	61353	i) Both 400 & 220 KV side of 400/220KV Baghat(PG) has double main bus scheme. 220 KV Baghat(PG)-Shamli(UP) (UP) Ckt. 220 KV Baghat(PG)-Modipuram, 2 (UP) (UP) Ckt-1, 220 KV Baghat(PG)-Baghat(UP) (UP) Ckt-1, 220 KV Baghat(PG)-Barot(UP) (UP) Ckt-1 and 400/220 KV 500 MVA ICT 1 at Baghat(PG) are connected to 220KV Bus 1 at Baghat(PG) and 220 KV Baghat(PG)-Mandola Vihar(UP) (UP) Ckt, 220 KV Baghat(PG)-Modipuram, 2 (UP) (UP) Ckt-2, 220 KV Baghat(PG)-Baghat(UP) (UP) Ckt-2, 220 KV Baghat(PG)-Barot(UP) (UP) Ckt-2 and 400/220 KV 500 MVA ICT 2 at Baghat(PG) are connected to 220KV Bus 2 at Baghat(PG). ii) As reported, at 05:07 hrs, B-N phase to earth fault occurred on 220 KV Baghat(PG)-Shamli(UP) (UP) Ckt, fault distance was 9.3km & fault current was 11.6kA. From Baghat end, fault was in zone-1 from Baghat end (as per DR of Baghat end). iii) On this fault, distance protection at Baghat end initiated tripping command however, B-ph CB didn't open on time which led to the LBB protection operation after ~120msec(as per DR). This resulted into tripping of all the elements connected at 220KV Bus 1 at Baghat(PG). 220KV Bus 1 became dead. iv) As per PMU at Meerut(PG), B-N phase to earth fault with delayed fault clearance time of 360 ms is observed. v) As per SCADA, no change in demand is observed in UP control area.	1) 220KV Bus 1 at Baghat(PG) 2) 400/220 KV 500 MVA ICT 1 at Baghat(PG) 3) 220 KV Baghat(PG)-Shamli(UP) (UP) Ckt 4) 220 KV Baghat(PG)-Modipuram, 2 (UP) (UP) Ckt-1 5) 220 KV Baghat(PG)-Baghat(UP) (UP) Ckt-1 6) 220 KV Baghat(PG)-Barot(UP) (UP) Ckt-1
3	GD-1	Uttar Pradesh & Uttarakhand	04-Aug-2023 03:09	04-Aug-2023 04:42	01:33	892	65	1.839	0.101	48512	64451	i) Power of 82.5*4 MW Alaknanda HEP, 100*4MW Vishnuprayag HEP and 33*4MW Singoli Bhawari HEP evacuates through 400 KV Alaknanda GVK (UPC) Musaffarnagar(UP) ckt and 400 KV Musaffarnagar(UP) Vishnuprayag(UP) (UP) Ckt. ii) As reported, at 03:09 hrs, 400 KV Alaknanda GVK(UPC) Musaffarnagar (UP) (end) Ckt tripped on B-N phase to earth fault. As per PMU, fault current was approx. 2.4kA from Musaffarnagar end. As per DR, fault was sensed in zone-1 at Musaffarnagar end and in zone-2 at Alaknanda end. A/R started in B-ph at both the ends and three phase opening occurred after ~400ms. iii) With the tripping of, 400 KV Alaknanda GVK(UPC) Musaffarnagar (UP) (end) Ckt, loading of 400 KV Alaknanda GVK(UPC) Musaffarnagar (UP) (UP) Ckt and 400 KV Alaknanda GVK(UPC) Vishnuprayag(UP) (UP) Ckt shifted to 400 KV Vishnuprayag(UP) Musaffarnagar(UP) (UP) Ckt. The load of Singrai Substation (evacuating Singoli Bhawari HEP generation), which is connected to Musaffarnagar(UP) through 400 KV Alaknanda GVK(UPC) Musaffarnagar (UP) (UP) Ckt, also shifted to 400 KV Vishnuprayag(UP) Musaffarnagar(UP) (UP) Ckt. At this time, more than 873 MW (~1260A line current) load was catered by 400 KV Vishnuprayag(UP) Musaffarnagar(UP) (UP) Ckt (Vishnuprayag HPS-441 MW, Alaknanda HEP-343 MW, Singrai- 38 MW). iv) After further 13sec, 400 KV Vishnuprayag(UP) Musaffarnagar(UP) (UP) Ckt tripped on over current protection operation (~1260A line current). v) With the tripping of 400 KV Vishnuprayag(UP) Musaffarnagar(UP) (UP) Ckt, all the generation of Alaknanda HEP & Vishnuprayag HEP tripped due to unavailability of power evacuating path. vi) During the same time, 220 KV Singoli Bhawari(Singoli)(TUPH) (end) Singrai(UP) (PTCL) Ckt-1 & 2 also tripped. As per DR, 07 mVed at Singli Bhawari end. Unbalance in voltage is also observed. vii) Due to tripping of 220 KV Singoli Bhawari(Singoli)(TUPH) (end) Singrai(UP) (PTCL) Ckt-1 & 2, 3 & 3 MW Singoli Bhawari(Singoli)(TUPH) HPS - UNIT 1, 2 & 3 tripped due to unavailability of power evacuating path. viii) At the same time, 400 KV Alaknanda GVK(UPC) Singrai(UP) (end) (UK) Ckt-1 & 2 also tripped (exact reason yet to be shared). As per DR, over-voltage stage-1 operation started at Singrai(UP) (end), however voltage was in operational limit. As per SCADA SDC, 400 KV Alaknanda GVK(UPC) Vishnuprayag(UP) (UP) Ckt-1 also tripped during the same time (reason yet to be shared). ix) Due to this event, complete blackout occurred at 400V Alaknanda HEP(UP), 400V Vishnuprayag HPS(UP), 220V Singoli Bhawari HEP(Singoli)(TUPH) and 400/220/132V Singrai(UP) 5/s. x) As per PMU at Meerut(PG), B-N phase to earth fault with fault clearance time of 120 ms is observed. xi) As per SCADA, no change in demand in UP control area and change in demand of approx. 65MW in Uttarakhand control area are observed. Generation loss of approx. 343MW, 441MW and 108MW are also observed at Alaknanda, Vishnuprayag and Singoli Bhawari HEP respectively.	1) 400 KV Alaknanda GVK(UPC) Musaffarnagar (UP) (UP) Ckt 2) 400 KV Vishnuprayag(UP) Musaffarnagar (UP) (UP) Ckt 3) 400 KV Alaknanda GVK(UPC) Vishnuprayag(UP) (UP) Ckt 4) 110 MW Vishnuprayag HPS - UNIT 1 5) 110 MW Vishnuprayag HPS - UNIT 2 6) 110 MW Vishnuprayag HPS - UNIT 3 7) 110 MW Vishnuprayag HPS - UNIT 4 8) 220 KV Singoli Bhawari (Singoli)(TUPH) (end) Singrai(UP) (PTCL) Ckt-1 9) 220 KV Singoli Bhawari (Singoli)(TUPH) (end) Singrai(UP) (PTCL) Ckt-2 10) 33 MW Singoli Bhawari (Singoli)(TUPH) HPS - UNIT 1 11) 33 MW Singoli Bhawari (Singoli)(TUPH) HPS - UNIT 2 12) 33 MW Singoli Bhawari (Singoli)(TUPH) HPS - UNIT 3 13) 400 KV Alaknanda GVK(UPC) Singrai(UP) (end) (UK) Ckt-1 14) 400 KV Alaknanda GVK(UPC) Singrai(UP) (end) (UK) Ckt-2 15) 82.5 MW Alaknanda HEP - UNIT 1 16) 82.5 MW Alaknanda HEP - UNIT 2 17) 82.5 MW Alaknanda HEP - UNIT 3 18) 82.5 MW Alaknanda HEP - UNIT 4
4	GD-1	Punjab	05-Aug-2023 20:15	05-Aug-2023 22:13	01:58	0	125	0.000	0.176	54875	70983	i) During antecedent condition, 220 KV Dhuri-14(Nabha)PS Ckt-1 & 2 were already under shutdown. ii) As reported, at 20:15hrs, B-N phase to earth fault occurred in 220 KV Patiala(PG) Nabha(PS) (PSTCL) Ckt-1, fault sensed in zone-1 at Nabha(PS) end and in zone-2 at Patiala(PG) end; flashover in insulator disc was observed. Fault distance was 42.3km from Patiala(PG) end. As per DR, fault current in 220 KV Patiala(PG)-Nabha(PS) (PSTCL) Ckt-1 was approx. 5.469kA from Nabha(PS) end and 6.123kA from Patiala(PG) end. On this fault, A/R operation started at Nabha(PS) end and as the fault was of permanent nature A/R operation was unsuccessful and line tripped from Patiala(PG) end without A/R operation. However 3-ph tripping after A/R operation was delayed by almost 225ms due to some issue in breaker. iii) At the same time, 220 KV Patiala(PG) Nabha(PS) (PSTCL) Ckt-2 tripped from Patiala(PG) end only with fault distance of 32km from Patiala(PG) end; fault was sensed in zone-2 from Patiala(PG) end. Time delay setting of zone-2 at Patiala(PG) end need to be reviewed. iv) Due to this tripping, complete blackout occurred at 220/66kV Nabha(PS) 5/s. v) As per PMU at Patiala(PG), B-N phase to earth fault with delayed clearance of 240msec and unsuccessful A/R operation is observed. vi) As per SCADA, change in demand of approx. 125MW is observed in Punjab control area.	1) 220 KV Patiala(PG)-Nabha(PS) (PSTCL) Ckt-1 2) 220 KV Patiala(PG)-Nabha(PS) (PSTCL) Ckt-2
5	GI-2	Haryana	05-Aug-2023 11:18	05-Aug-2023 12:45	01:27	0	290	0.000	0.428	61500	67733	i) During antecedent condition, active power loading on 400/220 KV 450 MVA ICT 1 and 400/220 KV 500 MVA ICT 2 at Panipat(BB) were 282 MW and 302 MW respectively. ii) As reported by BMBB, at 11:18hrs, 220 KV Panipat(HV) Panipat(BB) (HVNL) Ckt-3 tripped on R-N phase to earth fault with fault current of 2.341 kA and fault distance of 45.98 km from Panipat(BB) end; fault sensed in zone-3 at Panipat(BB) end. As reported by Panipat(HV), no relay operated at Panipat TPS end. iii) As reported by BMBB, 220 KV Panipat(HV) Panipat(BB) (HVNL) Ckt-4 also tripped at the same time on R-N phase to earth fault with fault current of 2.793 kA and fault distance of 30.32 km from Panipat(BB) end; fault sensed in zone-3 at Panipat(BB) end. As reported by Panipat(HV), no relay operated at Panipat TPS end. iv) During the same time, 400/220 KV 450 MVA ICT 1 and 400/220 KV 500 MVA ICT 2 at Panipat(BB) also tripped from both 400 and 220 KV sides. (exact reason yet to be shared) v) As per PMU at Panipat(BB), B-N phase to earth fault with delayed clearance of 1720msec is observed. vi) As per SCADA, change in demand of approx. 290MW is observed in Haryana control area.	1) 400/220 KV 450 MVA ICT 1 at Panipat(BB) 2) 400/220 KV 500 MVA ICT 2 at Panipat(BB) 3) 220 KV Panipat(HV) Panipat(BB) (HVNL) Ckt-3 4) 220 KV Panipat(HV) Panipat(BB) (HVNL) Ckt-4
6	GI-1	Rajasthan	06-Aug-2023 09:48	06-Aug-2023 10:24	00:36	0	1740	0.000	2.824	55398	61622	i) As reported by SLDC Rajasthan, at 09:48hrs on 06th August, 2023, Y phase jumper of 132kV Amarsagar – Ludarva Ckt-2 snapped. (Bus bar protection is not available at 132kV side). ii) On this fault, 132kV Amarsagar-Jaisalmer Ckt-2 tripped at the same time sensing fault in zone-4 (B-N fault) and 220/132 KV 100 MVA ICT-1 & 3 and 220/132 KV 160 MVA ICT-2 at Amarsagar(RS) tripped from 132kV side on over-current earth fault protection operation. iii) At the same time, 220kV Amarsagar-Akal (RS) Ckt also tripped from Akal end only on R-Y phase to phase fault with fault distance of 216.6km from Akal end; fault sensed in zone-3 at Akal end. iv) During the same time, 220kV Amarsagar-Ramgarh (RS) Ckt also tripped from Ramgarh end only on R-N phase to ground fault with fault distance of 227km from Ramgarh end; fault sensed in zone-3 at Ramgarh end. v) As per PMU at Jodhpur(RS), R-Y phase to phase fault is observed with delayed fault clearance time of 1560 ms. vi) As per SCADA, change in Rajasthan wind generation of approx. 1740MW is observed.	1) 132 KV Ludarva-Amarsagar (RS) Ckt-2 2) 132kV Amarsagar-Jaisalmer (RS) Ckt-2 3) 220/132 KV 100 MVA ICT-1 at Amarsagar(RS) 4) 220/132 KV 160 MVA ICT-2 at Amarsagar(RS) 5) 220/132 KV 100 MVA ICT-3 at Amarsagar(RS) 6) 220kV Amarsagar-Akal (RS) Ckt 7) 220kV Amarsagar-Ramgarh (RS) Ckt
7	GD-1	Rajasthan	07-Aug-2023 05:29	07-Aug-2023 06:20	00:51	550	0	1.162	0.000	47351	58675	i) As reported by SLDC Rajasthan, at 05:29hrs on 07th August, 2023, B phase jumper of 220 KV Amarsagar-Phalodi (RS) Ckt snapped and created bus fault at 220kV level of Amarsagar(RS). ii) On this fault, bus bar protection operated at 220kV level of Amarsagar(RS). 220 KV Bus-1 & 2 at Amarsagar(RS) was directly coupled through isolator and bus coupler CB was not present between the buses. Hence all the elements connected to both Bus-1 & 2 tripped and both the buses became dead. iii) Due to loss of supply in 132kV and 33kV level, blackout occurred at 220/132/33kV Amarsagar(RS). iv) As per DR, B-N phase to earth fault (P, B, R=915A) is observed in 220 KV Amarsagar-Phalodi (RS) Ckt; fault sensed in zone-4 at Amarsagar(RS) end. Line tripped after ~350msec from Amarsagar end. v) As per SCADA, change in Rajasthan wind generation of approx. 550MW is observed. vi) As per PMU at Jodhpur(RS), Y-N phase to earth fault is observed with delayed fault clearance time of 360 ms. Phase sequence at Amarsagar(RS) and Jodhpur(RS) may be reviewed.	1) 220 KV Amarsagar-Phalodi (RS) Ckt 2) 220 KV Amarsagar-Akal (RS) Ckt 3) 220 KV Amarsagar-Dechu (RS) Ckt 4) 220 KV Amarsagar-Mada (RS) Ckt 5) 220 KV Amarsagar-RGTTP (RS) Ckt 6) 220 KV Tejawa-Amarsagar (RS) Ckt-1 7) 220 KV Tejawa-Amarsagar (RS) Ckt-2 8) 220kV Amarsagar-Ramgarh (RS) Ckt 9) 220/132 KV 100 MVA ICT-1 at Amarsagar(RS) 10) 220/132 KV 160 MVA ICT-2 at Amarsagar(RS) 11) 220/132 KV 100 MVA ICT-3 at Amarsagar(RS) 12) 220 KV Bus-1 at Amarsagar(RS) 13) 220 KV Bus-2 at Amarsagar(RS)

20.Details of Grid Events during the Month of August 2023



Northern Region

Sl No.	Category of Grid Event (GI 1or 2/ GD-1 to GD-5)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
8	GD-1	Uttar Pradesh	08-Aug-2023 20:54	09-Aug-2023 04:30	07:36	580	0	1.022	0.000	56779	73852	i) 220kV Dadri Gas(NTPC) has 4*130.19MW units (Gas turbine driven) and 2*154.51MW units (Steam turbine driven). During antecedent condition, GT-1, GT-2, GT-3, GT-4 and ST-2 were running. ST-1 main breaker was out of order due to oil leakage in Y phase, hence ST-1 synchronization with transfer bus breaker activities were in progress. ii) As reported, at 20:54hrs on 08th August, 2023, interposing relay panel control supply tripped due to earth fault in both positive and negative supply. Relay panel gives the status of all 220 kV breakers and isolators and excitation gets trip when excitation current is 0.48 pu and unit is off grid. iii) As supply of panel was dead "ON" status of 220 kV breakers going in control circuit got "OFF" and machine came in speed control mode from load control mode and came on minimum load of 0.9 MW only. Due to this, GT-2 and GT-4 got tripped on failure of DC excitation system. iv) GT-1, running in speed control mode at 0.9 MW, was taken back in load control mode and loaded to 25 MW and then load was increased to 60 MW but it tripped on excitation failure due to operation of over excitation limiter. v) GT-3 was tripped manually as it was running at low load of 0.9 MW and ST-2 was running with GT-3 (exhaust of GT-3 and GT-4 are used to feed into the boiler to produce steam which drives the steam turbine) and steam parameters started deteriorating. With this, ST-2 also tripped and 220kV Dadri Gas(NTPC) S/s became dead. vi) As per SCADA, generation loss of approx. 580MW is observed at Dadri Gas (NTPC). vii) As per PMU at Panipat(BB), no fault is observed in the system.	1) 130.19 MW Dadri GPS - UNIT 1 2) 130.19 MW Dadri GPS - UNIT 2 3) 130.19 MW Dadri GPS - UNIT 3 4) 130.19 MW Dadri GPS - UNIT 4 5) 154.51 MW Dadri GPS - UNIT 6
9	GD-1	Punjab	09-Aug-2023 09:54	09-Aug-2023 10:58	01:04	77	0	0.125	0.000	61496	67911	i) During antecedent condition, 28.93 MW Unit-1 at Kotla(BB) and 24.2 MW Unit-2 & 3 at Kotla(BB) were generating at their full capacity. ii) As reported by BMBB, at 09:54hrs, bus bar protection operated due to snapping of Y-phase conductor of bus coupler at Kotla(BB). This led to tripping of both 132kV Bus 1 & 2 at Kotla(BB) along with all the lines and generating units connected at 132kV Kotla(BB) end which resulted in blackout of 132kV Kotla(BB) S/s. iii) As per PMU at Panipat(BB), no fault is observed in the system. iv) As per SCADA, no change in demand is observed in Punjab control area. v) As per SCADA, generation loss of approx. 77MW is observed at Kotla(BB). vi) As reported, generation at Kotla(BB) revived by 11:10hrs.	1) 132 KV Kotla(BB)-Ropar(PS) Ckt-1 2) 132 KV Kotla(BB)-Ropar(PS) Ckt-2 3) 132 KV Kotla(BB)-Ropar(PS) Ckt-3 4) 132 KV Kotla(BB)-Gangwal (PS) Ckt-1 5) 132 KV Kotla(BB)-Gangwal (PS) Ckt-2 6) 28.93 MW Unit-1 at Kotla(BB) 7) 24.2 MW Unit-2 at Kotla(BB) 8) 24.2 MW Unit-3 at Kotla(BB)
10	GD-1	Uttar Pradesh & Uttarakhand	10-Aug-2023 03:50	10-Aug-2023 05:23	01:33	892	60	2.029	0.091	43955	65920	i) Power of 82.5*4 MW Alaknanda HEP, 100*4MW Vishnuprayag HEP and 33*3MW Singoli Bhatwari HEP evacuates through 400 KV Alaknanda GVK (UPC)-Muzaffarnagar(UP) ckt and 400 KV Muzaffarnagar(UP)-Vishnuprayag(UP) (UP) ckt. ii) As reported, at 03:50 hrs, 400 KV Alaknanda GVK(UPC)-Muzaffarnagar (UP) (end) Ckt tripped from Muzaffarnagar(UP) end only as DT received at Muzaffarnagar end. It was reported that there was problem in DT sent circuit at Alaknanda end. iii) With the tripping of , 400 KV Alaknanda GVK(UPC)-Muzaffarnagar (UP) (end) Ckt, loading of 400 KV Alaknanda GVK(UPC)-Muzaffarnagar (UP) (UP) Ckt and 400 KV Alaknanda GVK(UPC)-Vishnuprayag(UP) (UP) Ckt shifted to 400 KV Vishnuprayag(UP)-Muzaffarnagar (UP) (UP) Ckt. The load of Srinagar Substation (evacuating Singoli Bhatwari HEP generation), which is connected to Muzaffarnagar(UP) through 400 KV Alaknanda GVK(UPC)-Muzaffarnagar (UP) (UP) Ckt, also shifted to 400 KV Vishnuprayag(UP)-Muzaffarnagar(UP) (UP) Ckt. iv) After this, 400 KV Vishnuprayag(UP)-Muzaffarnagar(UP) (UP) Ckt tripped on over current protection operation. v) With the tripping of 400 KV Vishnuprayag(UP)-Muzaffarnagar(UP) (UP) Ckt, all the generation of Alaknanda HEP & Vishnuprayag HEP tripped due to unavailability of power evacuating path. vi) During the same time, 220 KV Singoli Bhatwari(Singoli(TUHP)) (end)-Srinagar(UK) (PTCL) Ckt-1 & 2 also tripped. As per DR, DT received at Singoli Bhatwari end. Unbalance in voltage is also observed. vii) Due to tripping of 220 KV Singoli Bhatwari(Singoli(TUHP)) (end)-Srinagar(UK) (PTCL) Ckt-1 & 2, 33 MW Singoli Bhatwari(Singoli(TUHP)) HPS - UNIT 1, 2 & 3 tripped due to unavailability of power evacuating path. viii) At the same time, 400 KV Alaknanda GVK(UPC)-Srinagar(UK) (end) (UK) Ckt-1 & 2 also tripped (exact reason yet to be shared). As per DR, over-voltage stage 1 operation started at Srinagar(UK) end, maximum transient voltage ~288kV. As per SCADA SIZE, 400 KV Alaknanda GVK(UPC)-Vishnuprayag(UP) (UP) Ckt-1 also tripped during the same time (reason yet to be shared). ix) Due to this event, complete blackout occurred at 400KV Alaknanda HEP(UP), 400KV Vishnuprayag HPS(UP), 220KV Singoli Bhatwari HEP(Singoli(TUHP)) and 400/220/132kV Srinagar(UK) S/s. x) As per PMU at Muzaffarnagar(UP), no fault is observed in the system. xi) As per SCADA, no change in demand in UP control area and change in demand of approx. 60MW in Uttarakhand control area are observed. Generation loss of approx. 342MW, 442MW and 108MW are also observed at Alaknanda, Vishnuprayag and Singoli Bhatwari HEP respectively.	1) 400 KV Alaknanda GVK(UPC)-Muzaffarnagar (UP) (UP) Ckt 2) 400 KV Vishnuprayag(UP)-Muzaffarnagar (UP) (UP) Ckt 3) 400 KV Alaknanda GVK(UPC)-Vishnuprayag(UP) (UP) Ckt 4) 110 MW Vishnuprayag HPS - UNIT 1 5) 110 MW Vishnuprayag HPS - UNIT 2 6) 110 MW Vishnuprayag HPS - UNIT 3 7) 110 MW Vishnuprayag HPS - UNIT 4 8) 220 KV Singoli Bhatwari (Singoli(TUHP)) (end)-Srinagar(UK) (PTCL) Ckt-1 9) 220 KV Singoli Bhatwari (Singoli(TUHP)) (end)-Srinagar(UK) (PTCL) Ckt-2 10) 33 MW Singoli Bhatwari (Singoli(TUHP)) HPS - UNIT 1 11) 33 MW Singoli Bhatwari (Singoli(TUHP)) HPS - UNIT 2 12) 33 MW Singoli Bhatwari (Singoli(TUHP)) HPS - UNIT 3 13) 400 KV Alaknanda GVK(UPC)-Srinagar(UK) (end) (UK) Ckt-1 14) 400 KV Alaknanda GVK(UPC)-Srinagar(UK) (end) (UK) Ckt-2 15) 82.5 MW Alaknanda HEP - UNIT 1 16) 82.5 MW Alaknanda HEP - UNIT 2 17) 82.5 MW Alaknanda HEP - UNIT 3 18) 82.5 MW Alaknanda HEP - UNIT 4
11	GI-1	Rajasthan	13-Aug-2023 09:35	13-Aug-2023 11:08	01:33	45	0	0.072	0.000	62125	67296	i) Total MW generation of ASEJOL are pooled through 220/33 KV 150 MVA ICT 1, 2 & 3 at ASEJOL_HB FTGH2 (ASEJOL) and total generation is evacuated through 220 KV ASEJOL_HB FTGH2 (ASEJOL)-Fatehgarh2(PG) Ckt 1& 2. ii) As reported, at 09:35hrs, 220/33 KV 150 MVA ICT 1 at ASEJOL_HB FTGH2 (ASEJOL) tripped due to false PRV signal. iii) As per PMU at Fatehgarh2(PG), no fault is observed in the system. iv) As per SCADA, generation loss of approx. 45MW at ASEJOL is observed.	1) 220/33 KV 150 MVA ICT 1 at ASEJOL_HB FTGH2 (ASEJOL)
12	GD-1	Rajasthan	13-Aug-2023 09:55	13-Aug-2023 11:24	01:29	195	0	0.309	0.000	63195	68977	i) During antecedent condition, total MW generation of Azure Maple was approx. 200MW and it was evacuated through 220 KV Bhadla(PG)-Azure Maple (APMPL) Ckt. ii) As reported, at 09:55hrs, 220 KV Bhadla(PG)-Azure Maple (APMPL) Ckt tripped due to sparking at the CT terminal box of the line CRP panel. iii) As per PMU at Azure Maple (PL), no fault is observed in the system. iv) As per PMU, generation loss of approx. 195MW at Azure Maple is observed.	1) 220 KV Bhadla(PG)-Azure Maple (APMPL) Ckt
13	GI-1	Jammu & Kashmir	14-Aug-2023 18:34	14-Aug-2023 19:51	01:17	120	0	0.212	0.000	56595	66402	i) During antecedent condition, total MW generation of Salal(NH) was approx. 735MW (each of the six units was generating approx. 123 MW). ii) As reported, at 18:34hrs, transient V-N phase to earth fault occurred on 220 KV Kishenpur(PG)-Salal(NH) (PG) Ckt-1. Line successfully auto-reclosed from Kishenpur(PG) end, but tripped from Salal(NH) end due to non-operation of A/R at Salal(NH) end. As per DR at Kishenpur(PG), fault current was ~2.18kA; fault sensed in zone-2. iii) At the same time, 115 MW Salal HPS - UNIT 1 also tripped. (exact reason yet to be shared) iv) As per PMU, V-N phase to earth fault is observed with fault clearing time of 80 ms. v) As per SCADA, generation loss of approx. 120MW is observed at Salal(NH).	1) 220 KV Kishenpur(PG)-Salal(NH) (PG) Ckt-1 2) 115 MW Salal HPS - UNIT 1
14	GI-2	Himachal Pradesh	18-Aug-2023 10:59	18-Aug-2023 11:05	00:06	670	0	0.993	0.000	67496	77328	i) During antecedent condition, total MW loading of 400 KV Panchkula(PG)-Gumma(HP) (PG) Ckt-1 & 2 were approx. 575MW each. ii) As reported, at 10:59hrs, 400 KV Panchkula(PG)-Gumma(HP) (PG) Ckt-2 tripped at DT received at Panchkula(PG) end due to mal-operation of relay. Due to tripping of 400 KV Panchkula(PG)-Gumma(HP) (PG) Ckt-2, MW loading of 400 KV Panchkula(PG)-Gumma(HP) (PG) Ckt-1 increased and eventually exceeded 850MW (max. MW loading reached was 853MW as per PMU), hence SPS operated for reliable evacuation of power. iii) Due to SPS operation, 250 MW Nathpa-Jharki HPS - UNIT 3, 250 MW Karcham Wangtoo HPS - UNIT 2, 68.67 MW Rampur HEP - UNIT 5 and 40MW Sawra Kuddu HPS- UNIT 1 tripped. iv) As per DR of 400 KV Panchkula(PG)-Gumma(HP) (PG) Ckt-2, no fault is observed at Gumma(HP) and DT received at Panchkula(PG) which clearly indicates mal-operation of relay. v) As per DR of 400 KV Panchkula(PG)-Gumma(HP) (PG) Ckt-1, currents in R, Y and B phase are respectively ~1222A, ~1291A and ~1228A. Current loading required for SPS operation is [BSQ/(1.732*400)]~1227A. This indicates correct operation of SPS. vi) As per PMU at Panchkula(PG), no fault is observed in the system. vii) As per SCADA, generation loss of approx. 260MW at Nathpa Jharki, 80MW at Rampur, 250MW at Karcham and 40MW at Sawra Kuddu is observed.	1) 400 KV Panchkula(PG)-Gumma(HP) (PG) Ckt-2 2) 250 MW Nathpa-Jharki HPS - UNIT 3 3) 250 MW Karcham Wangtoo HPS - UNIT 2 4) 68.67 MW Rampur HEP - UNIT 5 5) 40MW Sawra Kuddu HPS- UNIT 1

20.Details of Grid Events during the Month of August 2023



Northern Region

Sl No.	Category of Grid Event (GI for 2/ GD-1 to GD-3)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
15	GD-1	Himachal Pradesh	18-Aug-2023 12:29	18-Aug-2023 14:07	01:38	364	0	0.528	0.000	68967	79716	i) During antecedent condition, all 6*66MW units were running and generating approx. 364 MW in total. Unit-1, 3 & 5, 220/66kV 40MVA Transformer and 220kV feeders to Baisraf, Jalandhar ckt-1 and Dasuya ckt-1 were connected at 220kV Bus-1 and Unit-2, 4 & 6 & 220kV feeders to Jalandhar ckt-2, Jessore ckt-1 and Dasuya ckt-2 were connected at 220kV Bus-2. ii) As reported, at 12:29 hrs, 220 KV Pong(BB)-Dasuya(PS) (BBMB) Ckt-1 tripped on Y-B phase to phase fault with fault current of 5.895kA and 5.21kA in Y and B phase respectively and fault distance of 17.09 km from Dasuya(PS) end, zone-1 distance protection operated at Dasuya(PS) end. Line tripped from Dasuya(PS) end due to disc flashover at Dasuya(PS) end, but did not trip from Pong(BB) end as relay did not operate at Pong(BB) end (relay was not healthy). iii) As per protection logic at Pong(BB), if earth fault is picked up and CB is open (auxiliary contact of CB closed), tripping to bus bar is initiated detecting CB flashover condition. As reported, on the above fault, back up earth fault protection of 66MW Pong HPS – Unit 5 picked up and auxiliary contact of the CB got closed. However due to inherent delay in CB opening, earth fault protection did not get reset immediately and thus as per CB flashover protection logic tripping initiated to bus bar and all the elements connected to 220kV Bus-1 at Pong(BB) tripped. BBMB has already been communicated to share the exact protection logic of the tripping. iv) At the same time, all the elements connected to 220kV Bus-2 at Pong(BB) also tripped. (Exact reason of bus bar protection operation yet to be shared) v) Due to tripping of both 220kV Bus-1 & 2 at Pong(BB), 220kV Pong(BB) 5/s became dead. vi) As per PMU at Jalandhar(PG), Y-B phase to phase fault is observed with fault clearing time of 2160 ms. vii) As per SCADA, total generation loss of approx. 364MW is observed at Pong HEP(BBMB).	1) 220 KV Pong(BB)-Dasuya(PS) (BBMB) Ckt-1 2) 220KV Bus 1 at Pong(BB) 3) 220KV Bus 2 at Pong(BB) 4) 220 KV Pong(BB)-Dasuya(PS) (BBMB) Ckt-2 5) 220 KV Jalandhar-Pong (BB) Ckt-1 6) 220 KV Jalandhar-Pong (BB) Ckt-2 7) 220 KV Jessore(P)-Pong(BB) (PG) Ckt 8) 220 KV Baisraf(BH)-Pong(BB) (PG) Ckt 9) 66 MW Pong HPS - UNIT 1 10) 66 MW Pong HPS - UNIT 2 11) 66 MW Pong HPS - UNIT 3 12) 66 MW Pong HPS - UNIT 4 13) 66 MW Pong HPS - UNIT 5 14) 66 MW Pong HPS - UNIT 6
16	GD-1	Uttar Pradesh	18-Aug-2023 16:33	18-Aug-2023 17:53	01:20	440	0	0.907	0.000	48512	64451	i) Power of 4*110MW Vishnuprayag HEP evacuates through 400 KV Alaknanda GVK (UPC)- Vishnuprayag(UP) (UP) ckt and 400 KV Muzaffarnagar(UP)-Vishnuprayag(UP) (UP) ckt. During antecedent condition, 400 KV Muzaffarnagar(UP)-Vishnuprayag(UP) (UP) ckt was under emergency shutdown. ii) As reported, at 16:33 hrs, 400 KV Alaknanda GVK (UPC)- Vishnuprayag(UP) (UP) ckt tripped on Y-B phase to phase fault with fault distance of 56.6km from Vishnuprayag(UP) and 38.3km from Alaknanda(UP) end. As further reported, fault was sensed in zone-1 at Vishnuprayag(UP) end and fault current was 1.83kA nad 1.19kA in Y and B phase respectively from Vishnuprayag(UP) end. As per DR at Alaknanda(UP) end, fault was sensed in zone-1 at Alaknanda(UP) end and fault current was 3.27kA nad 3.89kA in Y and B phase respectively from Alaknanda(UP) end; fault clearing time was ~35ms. iii) With the tripping of , 400 KV Alaknanda GVK (UPC)- Vishnuprayag(UP) (UP) ckt, all the generation of Vishnuprayag HEP, i.e., 110 MW Vishnuprayag HPS - UNIT 1, 2, 3 and 4 tripped due to unavailability of power evacuating path. iv) As per PMU at Muzaffarnagar(UP), Y-B phase to phase fault with fault clearance time of 80 ms is observed. v) As per SCADA, no change in demand in UP control area is observed. Generation loss of approx. 440MW is also observed at Vishnuprayag HEP.	1) 400 KV Alaknanda GVK(UPC)-Vishnuprayag(UP) (UP) Ckt 2) 110 MW Vishnuprayag HPS - UNIT 1 3) 110 MW Vishnuprayag HPS - UNIT 2 4) 110 MW Vishnuprayag HPS - UNIT 3 5) 110 MW Vishnuprayag HPS - UNIT 4
17	GI-1	Jammu & Kashmir	19-Aug-2023 11:25	19-Aug-2023 12:21	00:56	0	285	0.000	0.383	65971	74490	i) As reported, at 11:25hrs, 220 KV Barn(K)-Kishenpur(PG) Ckt-2 tripped on R-N phase to earth fault with fault distance of 12 km from Barn(K) end. ii) Due to tripping of 220 KV Barn(K)-Kishenpur(PG) Ckt-2, loading on 220 KV Barn(K)-Kishenpur(PG) Ckt-1 increased and line CB at 220kV Barn(PDO K) end of 220 KV Barn(K)-Kishenpur(PG) Ckt-2 opened due to over-loading, but line remain charged from Kishenpur(PG) end. iii) As per PMU at Kishenpur(PG), R-N phase to earth fault is observed in system with fault clearance time of 80 ms. iv) As per SCADA, load loss of approx. 285MW occurred in J&K control area.	1) 220 KV Barn(K)-Kishenpur(PG) Ckt-2 2) 220 KV Barn(K)-Kishenpur(PG) Ckt-1
18	GI-2	Uttar Pradesh	19-Aug-2023 09:26	19-Aug-2023 09:53	00:27	0	215	0.000	0.304	61240	70678	i) During antecedent condition, only 400/220 kV 315 MVA ICT 1 at Jaunpur (UP) was in service and MVA loading of ICT 1 was 329 MVA (MW: 317MW and MVA: 88MVA). It was feeding the 220kV and 132kV level of Jaunpur(UP). ii) As reported, at 09:26 hrs, 400/220 kV 315 MVA ICT 1 at Jaunpur (UP) tripped due to over-loading; over-current protection operated; currents in R, Y and B-phase are 0.462kA, 0.472kA and 0.76kA respectively. iii) Due to tripping of 400/220 kV 315 MVA ICT 1 at Jaunpur (UP), 220kV Bus 1 & 2 and 132kV Bus 1 & 2 of Jaunpur(UP) became dead due to loss of supply to 220kV and 132kV level of Jaunpur(UP). iv) As per PMU at Varanasi(PG), no fault is observed in the system. v) As per SCADA, change in demand of approx. 215 MW in UP control area is observed.	1) 400/220 kV 315 MVA ICT 1 at Jaunpur (UP)
19	GD-1	Himachal Pradesh	19-Aug-2023 08:49	19-Aug-2023 09:16	00:27	300	150	0.503	0.217	59590	69018	i) As reported, at 08:49 hrs, 220 KV Wangtoo-Bhabha-Kunihar ckt (T-connection) got tripped on R-N phase to ground fault. (Exact reason and location of fault yet to be shared) ii) At the same time, 220 KV Jeori-Kunihar(HP) Ckt, 220 KV Bhabha-Jeori(HP) Ckt, 220 KV Baddi-Kunihar(HP) Ckt and 220 KV Baddi-Pinjore Ckt-2 also tripped due to overloading. iii) With the tripping of both 220 KV Wangtoo-Bhabha-Kunihar ckt (T-connection) and 220 KV Bhabha-Jeori(HP) Ckt, 40MW Unit-1, 2 & 3 at Bhabha(HP) tripped due to loss of evacuation path and 220KV Bhabha(HP) 5/s became dead. iv) As per SCADA SOE, 220/66kV 31.5 MVA ICT-4 at Jeori(HP) tripped during the same time. (Exact reason yet to be shared) v) As per PMU at Panchkula(PG), R-N phase to ground fault with fault clearance time of 80 ms is observed. vi) As per SCADA, change in demand of approx. 150MW in HP control area is observed [affected load areas are Kunihar, Shimla, Kotla and Solan as reported by SLDC-HP]. vii) As reported by SLDC-HP, generation loss of approx. 300MW occurred (MW generation affected at Bhabha(330MW), Giv(50MW), Surya Kantia(14MW), Nanti(13MW), Goodwell(27MW), Ghanvi(23MW), Ghanvi-2(10MW) and other IPPs(30MW)). But as per SCADA, HP Hydro generation loss of approx. 140MW is observed.	1) 220 KV Wangtoo –Bhabha-Kunihar(HP) ckt (T-connection) 2) 220 KV Jeori-Kunihar(HP) Ckt 3) 220 KV Bhabha-Jeori(HP) Ckt 4) 220 KV Baddi –Pinjore(HP) Ckt-2 5) 220 KV Baddi-Kunihar(HP) Ckt 6) 220/66kV 31.5 MVA ICT-4 at Jeori(HP) 7) 132 KV Kunihar-Shimla(HP) Ckt 1 8) 132 KV Kunihar-Shimla(HP) Ckt 2 9) 132 KV Kunihar Barotwala Ckt-1 10) 40MW Unit-1 at Bhabha(HP) 11) 40MW Unit-2 at Bhabha(HP) 12) 40MW Unit-3 at Bhabha(HP)
20	GI-1	Jammu & Kashmir	20-Aug-2023 19:52	20-Aug-2023 21:16	01:24	0	375	0.000	0.519	55019	72313	i) As reported, at 19:52hrs, 220 KV Barn(K)-Kishenpur(PG) Ckt-1 tripped from Barn(K) end only due to damage of R-phase CB clamp at Barn(K) end. ii) Due to tripping of 220 KV Barn(K)-Kishenpur(PG) Ckt-1, loading on 220 KV Barn(K)-Kishenpur(PG) Ckt-2 increased and line CB at 220kV Barn(PDO K) end of 220 KV Barn(K)-Kishenpur(PG) Ckt-2 opened due to over-loading, but line remain charged from Kishenpur(PG) end. iii) As per PMU at Kishenpur(PG), no fault is observed in the system. iv) As per SCADA, load loss of approx. 375MW occurred in J&K control area.	1) 220 KV Barn(K)-Kishenpur(PG) Ckt-2 2) 220 KV Barn(K)-Kishenpur(PG) Ckt-1
21	GI-2	Rajasthan	20-Aug-2023 09:18	20-Aug-2023 04:11	00:53	0	465	0.000	0.644	52928	72256	i) During antecedent condition, MW loading on 400/220kV 315MVA ICT-1 & 2 at Bikaner(RS) were 200MW and 205MW respectively. ii) As reported, at 03:18hrs, 400/220kV 315MVA ICT-2 at Bikaner(RS) tripped due to heavy sparking of B phase isolator at 220kV side of ICT-2. As per DR, differential protection operated (Differential current in R, Y and B phase of approx. 2.67A, 2.64A and 5.31A respectively); current observed in B-phase was ~3.16kA. iii) With tripping of 400/220kV 315MVA ICT-2 at Bikaner(RS), 400/220kV 315MVA ICT-1 at Bikaner(RS) also tripped due to over-loading. As per DR, over-current earth-fault protection operated. iv) As per SCADA SOE, 200/132kV 100MVA ICT 3 at Bikaner(RS) also tripped during the same time. (Exact reason yet to be shared) v) As per PMU at Bikaner(PG), no fault is observed in the system, but fluctuation in voltage is observed. vi) As per SCADA, change in demand of approx. 465MW is observed in Rajasthan control area.	1) 400/220kV 315MVA ICT-1 at Bikaner(RS) 2) 400/220kV 315MVA ICT-2 at Bikaner(RS)
22	GI-1	Punjab	21-Aug-2023 22:53	22-Aug-2023 17:35	18:42	0	0	0.000	0.000	58971	72894	i) During antecedent condition, MW loading of 220 KV Baghapurana(PS)-Mogan(PS) Ckt-1 & 2 were approx. 72MW and 62MW respectively. ii) As reported, at 22:53hrs, 220 KV Baghapurana(PS)-Mogan(PS) Ckt-1 tripped due to R-phase CT damage at Moga(PS) end, fault observed in zone-1 from Moga(PS) end. Due to tripping of 220 KV Baghapurana(PS)-Mogan(PS) Ckt-1, load was shifted to 220 KV Baghapurana(PS)-Mogan(PS) Ckt-2 and no load loss occurred. iii) As per PMU at Moga(PG), R-N phase to earth fault with fault clearance time of 120ms is observed. iv) As per SCADA, change in demand of approx. 670MW is observed in Punjab control area. But as reported by SLDC Punjab no other major tripping occurred during the same time and no load loss occurred during the event.	1) 220 KV Baghapurana(PS)-Mogan(PS) Ckt-1

20.Details of Grid Events during the Month of August 2023



Northern Region

Sl No.	Category of Grid Event (GI for 2/ GD-1 to GD-3)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
23	GD-1	Rajasthan	21-Aug-2023 12:11	21-Aug-2023 12:24	00:13	0	1750	0.000	2.276	69275	76900	i) During antecedent condition, 220 kV F-G Bus. between 400 kV & 220 kV GSS Heerapura were under shutdown due to which the load of 220 kV GSS Chomu, Niwana, NPH and VKI were shifted to parallelly connected 220 kV D-A & E-C Bus between 400 kV & 220 kV GSS Heerapura. 2. The above load management was managed through 400/220 kV 250 MVA ICT 1 & 2 connected at 220 kV D-A & E-C Bus between 400 kV & 220 kV GSS Heerapura, and the load was around 210 MW on each ICT. ii) On the other hand, the 220 kV GSS Niwana is connected in ring from 400 kV GSS Heerapura and 400 kV GSS, Babai. 220 kV GSS Niwana was drawing power around 130MW from 400 kV GSS Heerapura and around 30 MW power was drawing from 400 kV GSS, Babai. The load on 400/220 kV 315 MVA ICT – 1 & 2 at 400 kV GSS Babai were 270 MW. iii) As reported, the details of event is as follows: a. At 12:11hrs, 220 kV Vatia – Sangarer line which was carrying around 170 MW towards 220 kV Sangarer, tripped due to jumper snapping. As a result of this, Sangarer started drawing load from 220 kV GSS Mansarovar and Mansarovar from 400 kV GSS Heerapura. b. Due to tripping of 220 kV Vatia-Sangarer line the extra loading of around 170 MW was put on 400/220 kV 250 MVA ICT 1 & 2 at Heerapura400(RS), resulting tripping of both the ICTs on overload. c. Due to the failure of both ICTs at 400 kV GSS, Heerapura, 220 kV GSS Niwana started to draw around 130 MW power from 400 kV GSS Babai resulting in overloading of 400/220 kV 315 MVA ICT – 1 & 3 at 400 kV GSS Babai (ICT-2 was out during the event) and eventually both the ICTs also tripped on overload. iv) As per SCADA data and SOE, at the same time, 220/132kV 160MVA ICT 1, 2 & 4 and 100MVA ICT 3 at Heerapura220(RS), 220/132kV 100MVA ICT 1 & 2 at Sangarer(RS) and 220/132kV 160MVA ICT 1 & 100MVA ICT 2 at Sawal Madhopur(RS) tripped during the same time. (Exact reason yet to be shared) v) As per PMU at Bassi(PG), R-N phase to earth fault is observed with fault clearing time of 80ms. vi) As per SCADA, change in demand of approx. 1750MW is observed in Rajasthan control area.	1) 220 kV Vatia-Sangarer(RS) Ckt 2) 400/220 kV 250 MVA ICT 1 at Heerapura400(RS) 3) 400/220 kV 250 MVA ICT 2 at Heerapura400(RS) 4) 400/220 kV 315 MVA ICT 1 at Babai(RS) 5) 400/220 kV 315 MVA ICT 3 at Babai(RS) 6) 220/132kV 160MVA ICT 1 at Heerapura220(RS) 7) 220/132kV 160MVA ICT 2 at Heerapura220(RS) 8) 220/132kV 100MVA ICT 3 at Heerapura220(RS) 9) 220/132kV 160MVA ICT 4 at Heerapura220(RS) 10) 220/132kV 100MVA ICT 1 at Sangarer(RS) 11) 220/132kV 100MVA ICT 2 at Sangarer(RS) 12) 220/132kV 160MVA ICT 2 at Sawal Madhopur(RS) 13) 220/132kV 100MVA ICT 2 at Sawal Madhopur(RS)
24	GI-1	Himachal Pradesh	21-Aug-2023 11:27	21-Aug-2023 11:34	00:07	60	250	0.083	0.118	72329	78601	i) As reported, at 11:27 hrs, bus-bar protection operated at 220 kV Bus 2 at Kunihar(HP). (Exact reason yet to be shared) ii) Due to this, all the elements connected to 220 kV Bus 2 at Kunihar(HP) got tripped and Bus-2 became dead. iii) At the same time, as reported by SLDC HP, 132 kV Kunihar-Barotiwala (HP) Ckt 1, 132 kV Kunihar-Solan (HP) Ckt 1 & 2, 132 kV Kunihar-Shimla (HP) Ckt 1 and 132 kV Kunihar-Malyana (HP) Ckt 2 also tripped. (Exact reason yet to be shared) iv) As per SCADA SOE, 30MW Unit-1 at Gir(HP) and 132 kV Kunihar-Jutog (HP) Ckt-2 also tripped during the same time. As per communication with SLDC HP, 30MW Unit-1 & 2 at Gir(HP) (connected at 132kV level) tripped during the same time. (Exact reason yet to be shared) v) As per PMU at Panchkula(PG), no fault is observed in the system, but fluctuation in voltage is observed. vi) As per SCADA, change in demand of approx. 330MW in HP control area is observed. But as reported by SLDC-HP, load loss of approx. 250MW occurred during the event. vii) As per SCADA, generation loss of approx. 60MW is observed in HP Hydro generation.	1) 220 kV Kunihar-Bhaba (HP) Ckt 2) 220 kV Baddi-Kunihar(HP) Ckt 2 3) 132 kV Kunihar-Barotiwala Ckt 1 4) 132 kV Kunihar-Solan(HP) Ckt 1 5) 132 kV Kunihar-Solan(HP) Ckt 2 6) 132 kV Kunihar-Shimla(HP) Ckt 1 7) 132 kV Kunihar-Malyana(HP) Ckt 2 8) 220/132kV 160/200MVA ICT-1 at Kunihar(HP) 9) 220/132kV 160/200MVA ICT-2 at Kunihar(HP)
25	GD-1	Uttar Pradesh	22-Aug-2023 12:39	22-Aug-2023 13:05	00:26	550	55	0.781	0.071	70464	77308	i) During antecedent condition, 300MW Rosa TPS(UP) Unit-1 and 2 were generating 274MW and 278MW respectively. Rosa TPS is connected with 220kV Shahjahanpur through 220kV Rosa-Shahjahanpur ckt-1&2. ii) As reported, at 12:39 hrs, R-N phase to earth fault occurred in 220kV Shahjahanpur(UP)-Aizpur(UP) Ckt; fault sensed in zone-1 at both the ends. Fault distance was 12.92km from Aizpur(UP) end and 22.125km from Shahjahanpur(UP) end. As per DR, fault current was approx. 6.5kA from Shahjahanpur(UP) end. Line tripped only from Aizpur(UP) end, line didn't trip from Shahjahanpur end. iii) As fault didn't clear from Shahjahanpur end, all other lines connected at 220kV Shahjahanpur(UP) tripped from remote end on zone-3 distance protection operation. iv) Due to this tripping, 220/132/138kV Shahjahanpur(UP) S/s became dead. v) During the same time, 300MW Rosa TPS(UP) Unit-1 & 2 tripped on standby earth fault protection operation. As per DR of 300MW Rosa TPS(UP) Unit-1, fault current was approx. 13.37kA. vi) As per SCADA SOE, 132kV Lalabad-Aizpur (UP) Ckt and 400kV Bareilly -Unnao (UP) Ckt-1 tripped during the same time. (Exact reason yet to be shared) vii) As per PMU at Lucknow(PG), R-N phase to earth fault converted to R-Y phase to phase fault is observed in the system with delayed fault clearance time of 2840ms. viii) As reported by SLDC-UP, load loss of ~55MW and generation loss of approx. 550MW occurred in UP control area.	1) 220kV Shahjahanpur(UP)-Shahjahanpur(PG) Ckt 2) 220kV Shahjahanpur(UP)-Bareilly(UP) Ckt 3) 220kV Shahjahanpur(UP)-Rosa TPS(UP) Ckt-1 4) 220kV Shahjahanpur(UP)-Rosa TPS(UP) Ckt-2 5) 220kV Shahjahanpur(UP)-Aizpur(UP) Ckt 6) 220kV Shahjahanpur(UP)-Gola-Ikshampur(UP) Ckt 7) 220kV Shahjahanpur(UP)-Hardoi(UP) Ckt 8) 220/132kV 200MVA ICT-1 at Shahjahanpur(UP) 9) 220/132kV 200MVA ICT-2 at Shahjahanpur(UP) 10) 220/132kV 160MVA ICT-3 at Shahjahanpur(UP) 11) 300MW Rosa TPS(UP) Unit-1 12) 300MW Rosa TPS(UP) Unit-2
26	GD-1	Punjab	22-Aug-2023 21:51	23-Aug-2023 00:20	02:29	0	590	0.000	0.835	58294	70663	i) 220/132/66kV Verpal(Ps) has double main bus scheme at 220kV level. ii) As reported, at 21:51 hrs, R-N phase to earth fault occurred in 220kV Verpal(Ps)-Rashiana(Ps) Ckt; fault sensed in zone-1 at Rashiana(Ps) end. Line tripped only from Rashiana(Ps) end. iii) As CB at Verpal(Ps) end of 220kV Verpal(Ps)-Rashiana(Ps) Ckt failed to operate, all other lines connected at 220kV Verpal(Ps) tripped from remote end on zone-3 distance protection operation. iv) Due to this tripping, 220/132/66kV Verpal(Ps) S/s became dead. v) As per DR at Amritsar(PG) end, 220 kV Verpal(Ps) ckt-1&2 tripped on R-N phase to earth fault with fault current of ~13.2kA from Amritsar(PG) end with fault clearance time of ~830ms; fault was sensed in zone-3. vi) As per PMU at Lucknow(PG), R-N phase to earth fault is observed in the system with delayed fault clearance time of 880ms. vii) As per SCADA, change in demand of approx. 590 MW is observed in Punjab control area.	1) 220 kV Verpal(Ps) –Amritsar(PG) ckt-1 2) 220 kV Verpal(Ps) –Amritsar(PG) ckt-2 3) 220kV Verpal(Ps)-Rashiana(Ps) Ckt 4) 220kV Verpal(Ps)-Patte(Ps) Ckt 5) 220kV Verpal(Ps)-Butri(Ps) Ckt
27	GI-1	Jammu & Kashmir	23-Aug-2023 14:55	23-Aug-2023 17:14	02:19	0	245	0.000	0.366	62178	66986	i) 220/132kV Barn(J&K) have feeding from 220kV Kishenpur-Barn ckt-1&2 only. There are 3*160MVA 220/132kV ICTs at Barn S/s and 132kV feeders to Kala Kotla, Jauria, Katra & Barn Canal. ii) During antecedent condition, 220kV Kishenpur-Barn ckt-1&2 were carrying 167MW & 170MW respectively. iii) As reported, at 14:55hrs, 220 kV Barn(J&K)-Kishenpur(PG) Ckt-2 tripped on B-N phase to earth fault with fault distance of ~6.9km from Kishenpur(PG) end. At the same time, 132kV feeders to Kala Kotla, Barn Canal & Jauria tripped. iv) Due to tripping of aforementioned elements, load of Kala Kotla, Barn Canal & Jauria affected. Load of Katra was remained intact through 220kV Kishenpur-Barn ckt-1. v) As per DR at Kishenpur(PG) end of 220 kV Barn(J&K)-Kishenpur(PG) Ckt-2, zone-1 distance protection operated; fault current was approx. 10.52kA from Kishenpur(PG) end. vi) As per PMU at Kishenpur(PG), B-N phase to earth fault with no R/N operation and cleared within 80msec is observed. vii) As per SCADA, load loss of approx. 245MW occurred in J&K control area.	1) 220 kV Barn(J&K)-Kishenpur(PG) Ckt-2
28	GI-1	Delhi	23-Aug-2023 17:07	23-Aug-2023 17:28	00:21	0	206	0.000	0.330	55558	62466	i) During antecedent condition, 220kV Geeta Colony-Patpargan (DTL) Ckt-1 was connected to 220kV Bus-1 at Geeta Colony(DTL) and 220kV Geeta Colony-Patpargan (DTL) Ckt-2, 220kV Geeta Colony - South wazirabad (DTL) Ckt-2 and 220/138kV 100MVA ICT-1&2 were connected to 220kV Bus-2 at Geeta Colony(DTL) and 220kV bus coupler was in closed position. 220kV Geeta Colony - South wazirabad (DTL) Ckt-1 was under shutdown and entire load of 220kV Geeta Colony and Patpargan was catered by 220kV Geeta Colony - South wazirabad (DTL) Ckt-2. ii) As reported, at 17:07 hrs, 220kV Geeta Colony - South wazirabad (DTL) ckt-2 tripped on Y-B phase to phase fault, fault sensed in zone-1 from Wazirabad end. iii) Due to tripping of the line, load of Shakarpur, Jhilmil, Kanti nager, Akshardham, CBD-1, Dhalpuria, Geeta Colony, Guru Angad Nagar, Kallash Nagar, Khichpur, Krishna Nagar, Mayur Vihar-I & II, GH-I, Preet Vihar and Patpargan were affected. iv) As per PMU at Mandaula(PG), Y-N phase to earth fault followed by Y-B phase to phase fault is observed with fault clearing time of 80 ms. v) As per SCADA, load loss of approx. 300MW is observed in Delhi control area. But as reported by SLDC Delhi, load loss of approx. 300MW occurred in Delhi control area.	1) 220kV Geeta Colony - South wazirabad (DTL) ckt-2
29	GI-1	Jammu & Kashmir	23-Aug-2023 15:17	23-Aug-2023 17:33	02:16	0	60	0.000	0.091	61147	66251	i) 220/132kV Ziankote S/s have two bus at 220kV side i.e., main bus & reserve bus. ii) During antecedent condition, 220kV Ziankote was operating in bus split mode vs. 220kV Amargah(INDIGRI)-Ziankote(J&K) D/C (carrying 95MW each) was feeding Ziankote load. 220kV Wagoor-Ziankote(J&K) Ckt-2 (carrying 118MW) was connected at other bus and feeding Alusteng. 220kV Wagoor-Ziankote(J&K) Ckt-1 was not in service. iii) As reported, 220 kV Wagoor(PG)-Ziankote(J&K) (POD K) Ckt-2 tripped on B-N phase to earth fault with distance of 21.32km from Wagoor(PG) end. iv) As per DR at Amargah(PG), fault current was approx. 5.16kA from Wagoor(PG) end. v) As per PMU at Amargah(PG), B-N phase to earth fault is observed with fault clearing time of 160ms. vi) As per SCADA, change in demand of approx. 100MW is observed in J&K control area. But as reported by SLDC J&K, load loss of 60MW occurred in J&K control area.	1) 220 kV Wagoor(PG)-Ziankote(J&K) (POD K) Ckt-2

20.Details of Grid Events during the Month of August 2023



Northern Region

Sl No.	Category of Grid Event (GI for 2/ GD-1 to GD-3)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
30	GI-1	Jammu & Kashmir	25-Aug-2023 13:19	25-Aug-2023 15:02	01:43	0	260	0.000	0.373	63215	69747	i) 220/132kV Ziankote S/s have two bus at 220kV side i.e., main bus & reserve bus. ii) During antecedent condition, 220kV Ziankote was operating in bus split mode via. 220kV Amargarh(INDIGRID) -Ziankote(JK) D/C was feeding Ziankote load. 220 KV Amargarh(Indigrid)-Ziankote(JK) (POD JK) Ckt-1 & 2 were 145MW each. iii) As reported, 220kV Amargarh(INDIGRID) -Ziankote(JK) ckt-1 tripped on B-N phase to earth fault with distance of 11.94km from Amargarh end; fault sensed in zone-1. iv) At the same time, 220kV Amargarh(INDIGRID) -Ziankote(JK) ckt-2 also tripped due to overloading occurred. Hence, load of Ziankote affected due to tripping. v) As per PMU at Amargarh, B-N phase to earth fault is observed with fault clearing time of 80ms. vi) As per SCADA, change in demand of approx. 260MW is observed in J&K control area.	1) 220 KV Amargarh(Indigrid)-Ziankote(JK) (POD JK) Ckt-1 2) 220 KV Amargarh(Indigrid)-Ziankote(JK) (POD JK) Ckt-2
31	GD-1	Rajasthan	28-Aug-2023 05:17	28-Aug-2023 10:23	05:06	1610	0	2.948	0.000	54613	69723	i) During antecedent condition, Rajasthan state wind generation was approx. 2888MW and 220kV Akal-Mada ckt was carrying approx. 240MW wind generation. ii) As reported, at 05:17hrs, 220kV Akal-Mada ckt tripped. Y-phase jumper found broken in yard at 220 kV GSS Mada. iii) As per PMU at Jodhpur(RS), Y-B phase to phase fault with delayed clearance of ~360msec is observed. iv) With the tripping of 220kV Akal-Mada ckt, complete wind generation at Mada lost (220kV Mada S/s blackout). At the same time, wind generation at other connected wind plants (Ithu, Jaijaya, Tejwa, Mulana etc.) also dropped to zero. No line tripping except 220kV Akal-Mada ckt reported and recorded in SDE during the event. v) As per SCADA, total drop in Rajasthan wind generation was approx. 1610MW. Almost ~1200MW RE generation recovered within 5mins.	1) 220 KV Akal-Mada (RS) Ckt
32	GD-1	Jammu & Kashmir	28-Aug-2023 06:09	28-Aug-2023 09:20	03:11	450	100	0.829	0.160	54261	62391	i) Baglihar HEP comprises of Baglihar Stage-1 (150MW Unit-1,2&3) and Baglihar Stage-2 (150MW Unit-4,5&6). Power of Baglihar stage-1 HEP evacuates through 400kV Baglihar-Kishenpur ckt-1 & 2 and power of Baglihar stage-2 HEP evacuates through 400kV Baglihar-Wanpoh ckt & 400kV Baglihar-Kishenpur ckt-3. ii) During antecedent condition, 400kV Baglihar-Kishenpur ckt-1,2&3 and 400kV Baglihar-Wanpoh ckt were carrying 223MW, 221MW, 235MW & 210MW respectively. iii) As reported, at 06:09hrs, 400 KV Baglihar(JK)-Kishenpur(PG) (POD JK) Ckt-2 tripped on Y-N phase to earth fault after unsuccessful A/R operation as fault was of permanent nature. iv) Fault was in Z-1(4.5km) from Kishenpur end and fault current was Iy=17kA. v) As per PMU at Kishenpur(PG), Y-N phase to earth fault with unsuccessful A/R operation and delayed clearance of fault in 200msec is observed. At the same time, 400 KV Baglihar(JK)-Kishenpur(PG) (POD JK) Ckt-1 also tripped from Baglihar end only. vi) With the tripping of 400 KV Baglihar(JK)-Kishenpur(PG) (POD JK) Ckt-1&2, all three running unit, 150MW Unit-1,2&3 (carrying total ~450MW) tripped due to loss of evacuation path leading to complete blackout of Baglihar Stage-1(J&K). vii) As per SCADA, change in demand of approx. 100MW is observed in J&K control area and loss in generation of approx. 450MW at Baglihar HEP.	1) 400 KV Baglihar(JK)-Kishenpur(PG) (POD JK) Ckt-1 2) 400 KV Baglihar(JK)-Kishenpur(PG) (POD JK) Ckt-2
33	GI-2	Rajasthan	28-Aug-2023 11:52	01-Sep-2023 18:38	06:46	2095	0	3.294	0.000	63608	66398	i) As reported, at 11:52hrs on 28th August, 2023, 400kV Bhadla(RS)-Bikaner(RS) Ckt-1 tripped on R-Y phase to phase fault with fault distance of 157.6km from Bikaner(RS). As per information received from SLDC Rajasthan, conductor snapped in line near 400kV level of Bhadla(RS). (Exact location of conductor snapping need to be shared) ii) As per DR at Bikaner(RS) end of 400kV Bhadla(RS)-Bikaner(RS) Ckt-1, fault was sensed in zone-2; fault current was 3.299kA and 3.723kA in R and Y phase respectively from Bikaner(RS) end and fault clearing time was ~70ms. iii) As per SCADA, change in NR total solar generation of approx. 2095MW is observed at 11:52hrs. iv) As per PMU at Bhadla(PG), R-Y phase to phase fault is observed with fault clearance time of 80 ms at 11:52hrs.	1) 400kV Bhadla(RS)-Bikaner(RS) Ckt-1
34	GI-2	Rajasthan	28-Aug-2023 12:05	01-Sep-2023 18:38	06:33	1880	0	3.000	0.000	62663	66556	i) As reported, at 12:05hrs, 400kV Bhadla(RS)-Bikaner(RS) Ckt-2 tripped on Y-B phase to phase fault with fault distance of 148.9km from Bikaner(RS). As per information received from SLDC Rajasthan, conductor snapped in line near 400kV level of Bhadla(RS). (Exact location of conductor snapping need to be shared) ii) As per DR at Bikaner(RS) end of 400kV Bhadla(RS)-Bikaner(RS) Ckt-2, fault was sensed in zone-1; fault current was 3.472kA and 4.467kA in Y and B phase respectively from Bikaner(RS) end and fault clearing time was ~50ms. iii) As per SCADA SOC, 400kV Bhadla(RS)-Bikaner(RS) Ckt-1 also tripped during the same time. (Exact reason yet to be shared) iv) As per SCADA, change in NR total solar generation of approx. 1880MW is observed at 12:05hrs. v) As per PMU at Bhadla(PG), Y-B phase to phase fault is observed with fault clearance time of 80 ms at 12:05hrs.	1) 400kV Bhadla(RS)-Bikaner(RS) Ckt-2
35	GD-1	Uttarakhand	29-Aug-2023 10:44	29-Aug-2023 11:36	00:52	0	181	0.000	0.258	65934	70385	i) 220kV Roorkee(PTCUL) is connected with 400/220kV Roorkee(PG) through 220 KV Roorkee(PG)-Roorkee(UK) (PTCUL) Ckt. ii) During antecedent condition, 220 KV Roorkee(PG)-Roorkee(UK) (PTCUL) Ckt was carrying ~181MW. This was the only source available for 220kV Roorkee(PTCUL). iii) As reported, at 10:43:30hrs, 220 KV Roorkee(PG)-Roorkee(UK) (PTCUL) Ckt tripped on R-Y fault from Roorkee(PG) end only leading to complete blackout at 220kV Roorkee(PTCUL). Distance protection relay at Roorkee(PG) end sensed fault in Z-3 with distance approx. 19.3km (219.3%), fault currents were IIR=4.26kA and IY=3.9kA. iv) As per PMU at Roorkee(PG) and DR of the line at Roorkee(PG) end, R-N fault which late converted into R-Y-N fault with delayed clearance of ~1240msec is observed. v) With the tripping of 220 KV Roorkee(PG)-Roorkee(UK) (PTCUL) Ckt, supply to 220kV Roorkee(PTCUL) lost. vi) As per SLDC-Uttarakhand, load loss of approx. 181MW occurred in Uttarakhand control area.	1) 220 KV Roorkee(PG)-Roorkee(UK) (PTCUL) Ckt-1
36	GI-1	Delhi	30-Aug-2023 12:50	30-Aug-2023 12:53	00:03	0	160	0.000	0.218	68910	73548	i) 220kV Pappankalan(Dwarka2) have feeding from 400/220kV Bannauli(DTL) and 400/220kV Dwarka(DTL). ii) During antecedent condition, 220kV Pappankalan(Dwarka2) was running in split mode. 220 KV Bannauli-Pappankalan(Dwarka2) ckt-1 was under emergency shutdown, 220 KV Bannauli-Pappankalan(Dwarka2) ckt-2 was carrying approx. 155MW, feeding load through 220/66kV 100MVA ICT-2 & 160MVA ICT-4 and 220kV Dwarka-Pappankalan ckt-1&2 was feeding through 220/66kV 100MVA ICT-1 & 160MVA ICT-3. iii) As reported, at 12:50 hrs, 220 KV Bannauli-Pappankalan(Dwarka2) ckt-2 tripped on Y-B phase to phase fault. Line tripped on differential protection operation. iv) Approx. 160MW load affected due to tripping of 220 KV Bannauli-Pappankalan(Dwarka2) ckt-2. At 12:53hrs, load was restored by closing bus coupler at 220kV Pappankalan. v) As per PMU at Bannauli(PG), Y-B phase to phase fault is observed with fault clearing time of 120 ms. vi) As reported by SLDC-Delhi, load loss of approx. 160MW is occurred in Delhi control area.	1) 220 KV Bannauli-Pappankalan(Dwarka2) ckt-2
37	GD-1	Delhi	30-Aug-2023 11:52	30-Aug-2023 11:55	00:03	0	80	0.000	0.108	69396	74057	i) 220kV Masjid Moth(DTL) have feeding from 400/220kV Tuglakabad and 400/220kV Maharambagh and 220kV Okhla(DTL) have feeding from 400/220kV Tuglakabad and 220kV Badliapur. ii) During antecedent condition, 220kV Maharambagh-Masjid Moth ckt-1&2 were not in service and 220kV Tuglakabad-Masjid Moth ckt-1 (carrying 34MW) & ckt-2 (carrying 81MW) were running in split mode. 220kV Okhla was connected to Tuglakabad and Badliapur. iii) As reported, at 11:52 hrs, 220 KV Tuglakabad-Okhla ckt-1 tripped on B-N phase to earth fault, fault distance was ~3.3km from Tuglakabad end. At the same time, 220kV Tuglakabad-Masjid Moth ckt-1 also tripped leading to complete blackout of 220kV Masjid Moth(DTL) S/s. iv) Approx. 80MW load affected at 220kV Masjid Moth. At 11:55hrs, bus coupler was closed and load was restored through 220kV Tuglakabad-Masjid Moth ckt-2. Further at 12:15hrs, 220kV Tuglakabad-Masjid Moth ckt-1 also restored. No load affected at 220kV Okhla. v) As per PMU at Badliapur(PG), B-N phase to earth fault is observed with fault clearing time of 120 ms. vi) As reported by SLDC-Delhi, load loss of approx. 90MW is occurred in Delhi control area.	1) 220 KV Tuglakabad-Masjid Moth (DTL) Ckt-1 2) 220 KV Tuglakabad-Okhla (DTL) Ckt-1

20.Details of Grid Events during the Month of August 2023



Western Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GI-1	WR	06-Aug-23 12:11	06-Aug-23 13:34	01:23	280	-	0.005	-	59837	51273	At 12:11 Hrs/ 06-08-2023, 220/33 kV Ostro-ICT-1 tripped due to opening of LV jumper. At the same time, 220/33 kV Ostro-ICT-2 tripped on overcurrent protection operation. Generation loss of 280 MW occurred at 220 kV Ostro (Renew Power) wind power plant due to the event.	Tripping of 1. 220 kV/33 kV Ostro-ICT-1 & 2
2	GI-2	WR	06-Aug-23 21:12	06-Aug-23 22:35	01:23	-	-	-	-	68922	51686	At 21:12 Hrs/ 06-08-2023, 400 kV Korba (NTPC)-Bus-3 tripped on LBB protection during withdrawal of Korba (NTPC)-unit-7 (500 MW) on Boiler Tube Leakage. During opening of 400 kV Generator-7 breaker (GCB), R and Y phase poles opened immediately but due to B-phase pole delayed opening, LBB operated. 400 kV Korba-Raipur-4, 400 kV Korba- Birsinghpur-2 and 400 kV Korba-Vindhyachal-2 tripped along with 400kV Korba (NTPC)-Bus-3. No generation loss occurred due to the event.	Tripping of 1. 400 kV Korba (NTPC)-Bus-3 2. 400 kV Korba-Raipur-4 3. 400 kV Korba- Birsinghpur-2 4. 400 kV Korba-Vindhyachal-2
3	GD-1	WR	08-Aug-23 13:32	08-Aug-23 22:07	08:35	260	-	0.004	-	66815	55820	At 13:32 Hrs/ 08-08-2023, : 220 kV Naranpar-Bhuj line tripped on B-E fault. As informed by site line was tripped by miscreants due to ROW issue. Generation loss of 260 MW occurred at 220 kV Narnapar (GIWEL) wind power plant due to loss of evacuation path.	Tripping of 1. 220 kV Naranpar-Bhuj
4	GD-1	WR	11-Aug-23 20:42	11-Aug-23 21:46	01:04	-	88	-	0.001	75267	59990	At 20:42hrs/ 11-08-2023, B-phase CT of 220KV Asoj-Jambuva-1 blasted at Jhambuva substation, after 535 msec R-phase CT of 220KV Asoj-Jambuva-2 blasted at Jhambuva substationand and fire erupted in switchyard leading to busbar protection operation in Bus-1 and Bus-2, leading to blackout of Jambuva substation. Load loss of around 88MW was reported due to the event.	Tripping of- 1. 220kv Asoj-Jambuva-1&2 2. 220kv Jambuva-Karamsad-1&2 3. 220kv Jambuva-Jhagadiya 4. 220kv Jambuva-Haldarwa 5. 220kv Jambuva-Achalliya-3&4 6. 220kv Jambuva-Gotri-1&2 7. 220kv Jambuva-Vadodara-1&2 8. 220/66kv Jambuva-ICT-1&2 9. 220/132kv Jambuva-ICT-1,2&3 10. 220kv Jambuva-Bus-1&2
5	GD-1	WR	13-Aug-23 13:07	13-Aug-23 18:30	05:23	250	-	0.004	-	71053	61132	At 13:07 Hrs/ 13-08-2023,220 kV Naranpar-Bhuj line tripped on B-E fault.Generation loss of 250 MW occurred at 220 kV Narnapar (GIWEL) wind power plant due to loss of evacuation path.	Tripping of 1. 220 kV Naranpar-Bhuj
6	GD-1	WR	14-Aug-23 04:09	14-Aug-23 04:31	00:22	253	-	0.004	-	68173	56215	At 04:09 Hrs/ 14-08-2023,220 kV Bhuj-Gadhsisa line tripped on Y-E fault.Generation loss of 253 MW occurred at 220 kV Gadhsisa (Renew Power) wind power plant due to loss of evacuation path.	Tripping of 1. 220 kV Bhuj-Gadhsisa
7	GD-1	WR	14-Aug-23 05:57	14-Aug-23 07:17	01:20	-	1271	-	0.022	70211	58247	At 05:56:53/ 14-08-2023, 220 kV Bhilai-Bemetra tripped on over current protection operation (maloperation), leading to overloading of 220 kV Bhatapara-Suhela and 220 kV DSPM-Suhela. At 05:57:06, 220 kV DSPM-Suhela tripped on over current protection operation. Due to delayed opening of Y-phase at Suhela, LBB protection operated and instead of only 220 kV Suhela-Bus-1, Bus-2 also tripped due to wrong isolator selector switch status of DSPM line (Both the 89A & 89B status was closed), leading to blackout of 220 kV Suhela substation. Also complete outage (blackout) occurred at Paraswani, Mungeli, Gendpur, Bemetara and 132 kV downstream substations. Load loss of 1271 MW occurred at Suhela, Paraswani, Mungeli, Gendpur, Bemetara areas due to the above tripping.	Tripping of 1. 220 kV Bhilai-Bemetra 2. 220 kV Bhatapara-Suhela-1,2&3 3. 220 kV DSPM-Suhela 4. 220 kV Suhela-Bemetra-1&2 5. 220 kV Suhela-Paraswani-1&2 6. 220 kV Suhela-Banari 7. 220 kV Suhela-Bus-1&2
8	GD-1	WR	15-Aug-23 04:35	16-Aug-23 01:26	20:51	135	-	0.002	-	69219	56625	At 04:35 Hrs/ 15-08-2023, 220 kV Bhuj-Vadva-1 tripped on R-E fault. Generation loss of 135 MW occurred at 220 kV Vadva (GIWEL) wind power plant due to loss of evacuation path.	Tripping of 1. 220 kV Bhuj-Vadva-1

20.Details of Grid Events during the Month of August 2023



Western Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
9	GI-1	WR	16-Aug-23 21:33	16-Aug-23 21:53	00:20	-	-	-	-	73804	65515	At 09:33 Hrs/ 16-08-2023, while first time charging of 220 kV Kalwa-Pawne-1, bus bar protection operated in 220 kV Kalwa-Bus-2 resulting in tripping of 220 kV Kalwa-Bus-2 all connected elements.No load loss occurred during the event.	Tripping of 1. 220 kV Kalwa-Bus-2 2. 220 kV Borivali-Kalwa-1 3. 400/220 kV Kalwa-ICT-1&2 4. 220 kV Kalwa-Colorchem-1 5. 220 kV Kalwa-Mulund-2
10	GD-1	WR	16-Aug-23 10:59	16-Aug-23 11:25	00:26	-	350	-	0.005	77689	66700	At 10:47 hrs/ 16-08-2023, 220 kV Sachin-ichhapore-1 tripped on R-E fault due to R phase wave trap got damaged at Sachin end. At the same time 220 kV Sachin-GSEG-1 tripped on reflected earth fault. Prior to the event 220 kV Sachin-Vav was under planned shutdown. At 10:59 hrs, 220 kV Sachin-Navsari-1 tripped on R-Y fault and substation became dark. Load loss of 350 MW occurred due to the event.	Tripping of 1. 220 kV Sachin-ichhapore-1 2. 220 kV Sachin-GSEG-1 3. 220 kV Sachin-Navsari-1
11	GD-1	WR	19-Aug-23 17:57	19-Aug-23 19:00	01:03	1350	-	0.018	-	74687	61077	At 17:57 Hrs/ 19-08-2023, 400 kV SSP-Bus-1&2 tripped on LBB protection operation of Bus-Coupler. Bus Coupler was in open condition and LBB operated due to maloperation of M-2 relay. Even though bus coupler was in open condition, Status of Bus coupler R phase of M-2 relay was showing "closed" and contact of timer relay of LBB was short. This led to LBB operation. Generation loss of 1350 MW occurred at SSP hydro power plant due to the above event.	Tripping of 1. 400 kV SSP-Bus-1&2 2. 400 kV SSP-Dhule-1&2 3. 400 kV SSP-Rajgarh-1&2 4. 400 kV SSP-Asoj-1 5. 400 kV SSP - Kasor 6. 400/220 kV SSP-ICT-1&2 7. SSP Unit-1,2,3,4,5&6
12	GD-1	WR	21-Aug-23 04:18	22-Aug-23 20:02	15:44	143	-	0.002	-	68699	52806	At 04:18 Hrs/ 21-08-2023,220 kV Bhuj-Vadva-1 tripped on R-E fault due to faulty insulator at Tower location 181. Generation loss of 143 MW occurred at 220 kV Vadva (GIWEL II) wind power plant due to loss of evacuation path.	Tripping of 1. 220 kV Bhuj-Vadva-1

20.Details of Grid Events during the Month of August 2023
Southern Region



Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t. Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid		Brief details of the event (pre fault and post fault system conditions)	Name of Elements (Tripped/Manually opened)
	(GI for 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-1	Pondicherry	05-Aug-23 11:57	05-Aug-23 12:58	01hr 1min	0	132	0.00%	0.24%	52061	55929	Complete Outage of 230kV/110kV Villianur SS of Pondicherry: During antecedent conditions, 230kV Neyveli TS-2 Villianur line was under idle charged condition from Neyveli TS-2. As per the reports submitted, the triggering incident was B-N fault in 230kV Pondicherry Villianur line. Tripping of the only connected line resulted in complete outage of 230kV/110kV Villianur SS.	1. 230kV Pondicherry Villianur line
2	GD-1	Pondicherry	05-Aug-23 14:10	05-Aug-23 14:41	31mins	0	138	0.00%	0.25%	50579	54229	Complete Outage of 230kV/110kV Villianur SS of Pondicherry: During antecedent conditions, 230kV Pondicherry Villianur line was under idle charged condition. As per the reports submitted, the triggering incident was B-N fault in 230kV Neyveli TS-2 Villianur line. Tripping of the only connected line resulted in complete outage of 230kV/110kV Villianur SS.	1. 230kV Neyveli TS-2 Villianur line
3	GD-1	Telangana	08-Aug-23 15:47	08-Aug-23 21:28	5hrs 41mins	0	0	0.00%	0.00%	47268	57507	Complete Outage of 765kV/400kV Warangal_WKTL SS: During antecedent conditions, 400kV Warangal Warangal_WKTL line-1 was under outage. 765kV Bus and lines were not in charged condition. As per the reports submitted, the triggering incident was RY-N fault in 400kV Warangal Warangal_WKTL Line-2. Tripping of the only connected line resulted in a complete outage of 765kV/400kV Warangal_WKTL SS.	1.400kV Warangal Warangal_WKTL line-2
4	GD-1	Karnataka	09-Aug-23 13:36	09-Aug-23 13:55	19mins	60	0	0.12%	0.00%	48891	59182	Complete Outage of 220kV Varahi PH of KPCL: 220kV Varahi PH is operating with a single bus scheme. As per the reports submitted, the triggering incident was 220kV Bus fault at Varahi PH. Due to non-operation of BBP, the fault was cleared at remote ends on operation of Zone-2 protection. Tripping of all the connected lines resulted in complete outage of 220kV Varahi PH.	1. 220kV Varahi Shimoga Line-1, 2, & 3 1. 220kV Varahi Kemar Line-1& 2
5	GD-1	Karnataka	12-Aug-23 11:38	12-Aug-23 11:59	21mins	0	42	0.00%	0.08%	49112	55203	Complete Outage of 220kV Kodalalli PH, 220kV Kadra PH of KPCL and 220kV/110kV Karwar SS of KPTCL: During antecedent conditions, 220kV Kaiga Kadra and 220kV Kaiga Kodalalli were under outage. 220kV Kodalalli PH, 220kV Kadra PH and 220kV/110kV Karwar SS were being radially fed from 220kV Nagheri PH. As per the reports submitted, the triggering incident was the tripping of 220kV Nagheri Kodalalli Line-1 and 220kV Nagheri Kodalalli Line-2 on Earth fault protection at Nagheri end. Tripping of both lines led to complete outage of 220kV Kodalalli PH, 220kV Kadra PH and 220kV/110kV Karwar SS .	1. 220kV Nagheri Kodalalli Line-1&2
6	GD-1	Tamil Nadu	13-Aug-23 14:31	13-Aug-23 14:54	23mins	70	0	0.15%	0.00%	46998	53079	Complete Outage of 230kV JSW_Vilathikulam Wind: As per the reports submitted, the 230kV TTGS JSW_Vilathikulam_Wind line tripped only at JSW_Vilathikulam end on distance protection operation during VT fuse failure. Tripping of the only connected line resulted in complete outage of 230kV JSW_Vilathikulam Wind.	230kV TTGS JSW_Vilathikulam_Wind
7	GD-1	Karnataka	23-Aug-23 15:50	23-Aug-23 16:28	38mins	8	358	0.02%	0.60%	48306	59707	Complete Outage of 220kV/110kV Ranebennur SS, 220kV/33kV Sarjan_Suzlon_Wind_Guttur, 220kV/66kV Davanagere SS, 220kV/33kV Suzlon_Wind_Honnali, and 220kV/66kV Benikere SS of KPTCL : As per the information received, the triggering incident was failure of R-phase CT of 220kV Guttur Ranebennur line at Guttur end. This resulted in the operation of 220kV Bus-2 BBP at 400kV/220kV Guttur SS and all the elements connected to 220kV Bus-2 got tripped. This in turn resulted in the complete loss of supply to 220kV Sarjan_Suzlon_Wind_Guttur and 220kV/110kV Ranebennur SS since both SS were only connected to 220kV Bus-2 at 400kV/220kV Guttur SS. After the tripping of 220kV Guttur Davanagere line-1 and 2 on 220kV Bus-2 BBP operation, 220kV Guttur Davanagere line-3 which was connected to 220kV Bus-1 also got tripped on operation of overcurrent protection. This resulted in complete outage of 220kV/66kV Davanagere SS which in turn led to the de-energization of 220kV Bus-2 at 220kV/66kV Honnali SS. Due to this, there was complete loss of supply at 220kV/66kV Benikere SS, and 220kV/33kV Suzlon_Wind_Honnali.	1. 220kV Guttur-Guttur SAS line-2 2. 220kV Guttur-Davanagere line-1, 2, & 3 3. 400/220kV Guttur-ICT-2 4. 220kV Guttur-Ranebennur 5. 220kV Guttur-Chitradurga 6. 220kV Guttur-Haveri line-1& 2 7. 220kV Guttur-Neelagunda 8. 220kV Guttur-Sarjan Wind
8	GD-1	Karnataka	31-Aug-23 22:51	31-Aug-23 23:01	10mins	0	113	0.00%	0.25%	44658	45542	Complete Outage of 220kV/66kV Khodays SS, and 220kV/66kV Subramanyapura SS of KPTCL : During antecedent conditions, 220kV Subramanyapura - Peenya line was under outage. Triggering incident was RN fault in 220kV Somanahally - Khodays line. This resulted in complete loss of supply at 220kV/66kV Khodays SS and 220kV/66kV Subramanyapura SS since these stations were radially fed from Somanahalli Station.	1. 220kV Somanahalli-Khodays
9	GI-1	Karnataka	09-Aug-23 06:02	09-Aug-23 06:34	32mins	200	0	0.55%	0.00%	36688	48230	Tripping of 220kV Bus-1 of 220kV Alamatti Generating station of KPCL: During antecedent conditions, 220kV Alamatti Generating station was operating with split bus condition at 220kV level. 220kV Alamatti Bagewadi Line-1, 220kV Alamatti Bagalkot Line-1 and Unit-4,5 and 6 are connected to 220kV Bus-1. As per the reports submitted, the triggering incident was R-N fault in 220kV Alamatti Bagewadi Line-1. At the same time, 220kV Alamatti Bagalkot Line-1 tripped at Bagalkot end. Tripping of both lines led to loss of evacuation path for the Unit-4,5&6 and they tripped on over frequency protection. This led to de-energisation of 220kV Bus-1 at Alamatti Generating station. Subsequently, Unit-1,2&3 connected to 220kV Bus-2 also tripped.	1. 220kV Alamatti Bagewadi Line-1 2. 220kV Alamatti Bagalkot Line-1 3. Alamatti Unit-1,2,3,4,5 & 6

20.Details of Grid Events during the Month of August 2023
Southern Region



Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t. Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid		Brief details of the event (pre fault and post fault system conditions)	Name of Elements (Tripped/Manually opened)
	(GI for 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
10	GI-1	Telangana	10-Aug-23 16:42	10-Aug-23 19:49	03hrs 07mins	0	0	0.00%	0.00%	46075	53408	Tripping of 220kV Bus-1 of 220kV Nagarjun Sagar Generating Station of TSGENCO: As per the reports submitted, the triggering incident was maloperation of LBB in 220kV Nagarjun Sagar Tallapalli Line-1 which was under LC at Nagarjun Sagar end during testing works. Immediately all elements connected to 220kV Nagarjun Sagar Bus-1 tripped.	1. 220kV Nagarjun Sagar Srisaillam Line-1 2. 220kV/110kV 100MVA PTR-1 at Nagarjun Sagar
11	GI-1	Karnataka	10-Aug-23 11:48	10-Aug-23 16:14	04hrs 26mins	0	0	0.00%	0.00%	49644	58898	Tripping of 220kV Bus-1 of 400kV/220kV Munirabad SS of PGCIL SR-1: During antecedent conditions, at 400kV/220kV Munirabad SS, main circuit breaker of 220kV Munirabad Lingapur line-2 was bypassed and the line was charged through Bus Coupler by connecting to 220kV Bus-1. The triggering incident was R-N fault in 220kV Munirabad Lingapur line-2 and the bus coupler at Munirabad end tripped. Since this is the only line connected to Bus-1 at Munirabad, this resulted in the de-energization of 220kV Bus-1 of 400kV/220kV Munirabad SS.	1. 220kV Munirabad Lingapur line-2
12	GI-2	Andhra Pradesh	10-Aug-23 18:46	11-Aug-23 06:45	11hrs 59mins	0	0	0.00%	0.00%	43043	48992	Tripping of 400kV Bus-1 of 400kV HNPCI SS: As per the reports submitted, the triggering incident was failure of a Y-phase Bus-1 isolator. Immediately, 400kV Bus-1 BBP operated and all the main circuit breakers connected to the Bus-1 tripped. At the same time, 400kV Maradam Kalpakkam line-1 tripped only at Maradam end due to SOTF maloperation.	1. 400kV Maradam Kalpakkam line-1
13	GI-2	Karnataka	11-Aug-23 05:19	11-Aug-23 07:51	02hrs 32mins	0	0	0.00%	0.00%	37699	45054	Tripping of 400kV Bus-1 of 400kV/220kV Kaiga APS of NPCIL: 400kV/220kV Kaiga APS is operating with one and half breaker scheme at 400kV level. As per the reports submitted, the triggering incident was Main CB LBB maloperation of 400kV/220kV Kaiga ICT-1 which was under LC. Immediately all the Main CBs connected to 400kV Bus-1 tripped causing the de-energisation of 400kV Bus-1 at Kaiga APS.	Nil
14	GI-2	Tamil Nadu	11-Aug-23 17:53	11-Aug-23 23:16	05hrs 23mins	0	0	0.00%	0.00%	40972	50325	Tripping of 400kV Bus-1 of 400kV/230kV NNTPP : 400kV/230kV NNTPP is operating with Double Bus with Bus Coupler scheme at 400kV level. As per the reports submitted, the triggering incident was R-N fault in 400kV Bus-1 at 400kV/220kV NNTPP. Immediately, BBP operated and all the elements connected to the 400kV Bus-1 tripped leading to the de-energisation of the Bus.	1. 400kV NNTPP Kalivendapattu Line-1 2. 400kV/230kV NNTPP ICT-1
15	GI-1	Karnataka	15-Aug-23 02:06	15-Aug-23 07:22	05hrs 16mins	0	0	0.00%	0.00%	39930	43465	Tripping of 220kV Bus-1 of 400kV/220kV Munirabad SS of PGCIL SR-1: During antecedent conditions, at 400kV/220kV Munirabad SS, main circuit breaker of 220kV Munirabad Lingapur line-2 was bypassed and the line was charged through Bus Coupler by connecting to 220kV Bus-1. The triggering incident was tripping of 220kV Munirabad Lingapur line-2 at Munirabad end and the bus coupler at Munirabad end tripped. Since this is the only line connected to Bus-1 at Munirabad, this resulted in the de-energization of 220kV Bus-1 of 400kV/220kV Munirabad SS.	1. 220kV Munirabad Lingapur line-2
16	GI-1	Karnataka	22-Aug-23 22:53	23-Aug-23 01:25	02 hrs 32 mins	0	0	0.00%	0.00%	43233	49169	Tripping of 220kV Bus-1 of 400kV/220kV Munirabad SS of PGCIL SR-1: During antecedent conditions, at 400kV/220kV Munirabad SS, main circuit breaker of 220kV Munirabad Lingapur line-2 was bypassed and the line was charged through Bus Coupler by connecting to 220kV Bus-1. The triggering incident was R-N fault in 220kV Munirabad Lingapur line-2 and the bus coupler at Munirabad end tripped. Since this is the only line connected to Bus-1 at Munirabad, this resulted in the de-energization of 220kV Bus-1 of 400kV/220kV Munirabad SS.	1. 220kV Munirabad Lingapur line-2
17	GI-1	Kerala	25-Aug-23 10:58	25-Aug-23 11:05	7mins	0	216	0.00%	0.31%	52758	69350	Tripping of 220kV Bus-1 of 220kV/110kV Pothencode SS of KSEB: During relay testing of 220kV/110kV 200MVA Transformer-3 at Pothencode which was under LC, BBP of Bus-1 operated resulting in the tripping of the elements connected to 220kV Bus-1 at 220kV/110kV Pothencode SS. At the same time, 220kV/110kV 200MVA Transformer-2 which was connected to 220kV Bus-2 got tripped on operation of overload protection.	1. 220kV Pothencode Edamon line-1 2. 220kV Pothencode Trivandrum line-1&3 3. 220kV Pothencode Kattakada line-1 4. 220kV/110kV 200MVA Transformer-1& 2 at Pothencode
18	GI-1	Andhra Pradesh	26-Aug-23 06:55	26-Aug-23 07:55	1 hr	0	0	0.00%	0.00%	4224	53390	Tripping of 220kV Bus-1 of 220kV Vizag Switching Station of APTRANSCO: The triggering incident was the failure of Y-ph pilot SRC insulator of jack bus dropper connecting to Bus isolators-I & II of 220kV VSS-MRS-I feeder bay at 220kV VSS end leading to the operation of BBP of Bus-1 at VSS and tripping of all the elements connected to 220kV Bus-1 at VSS. At the same time, 220kV VSS PGCIL line-2 corresponding to 400kV/220kV Gazuwaka ICT-2 which was connected to 220kV Bus-2 also got tripped during this event and the same needs review.	1. 220kV VSS-Gajuwaka 2. 220kV VSS-MRS-1 3. 220kV VSS- Kalapaka-1 4. 220kV VSS-PGCIL-2& 3 (500MVA ICT-2& 3) 5. 220kV VSS-Parawada-1 6. 220kV VSS-Pendurthy-1

20.Details of Grid Events during the Month of August 2023
Southern Region



Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t. Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid		Brief details of the event (pre fault and post fault system conditions)	Name of Elements (Tripped/Manually opened)
	(GI for 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
19	GI-1	Karnataka	30-Aug-23 03:05	30-Aug-23 04:48	01 hr 43 mins	0	0	0.00%	0.00%	39850	45168	Tripping of 220kV Bus-1 of 400kV/220kV Munirabad SS of PGCIL SR-1: During antecedent conditions, at 400kV/220kV Munirabad SS, main circuit breaker of 220kV Munirabad Lingapur line-2 was bypassed and the line was charged through Bus Coupler by connecting to 220kV Bus-1.The triggering incident was tripping of 220kV Munirabad Lingapur line-2 only at the Munirabad end due to distance protection overreach. Since this is the only line connected to Bus-1 at Munirabad, this resulted in the de-energization of 220kV Bus-1 of 400kV/220kV Munirabad SS.	1. 220kV Munirabad Lingapur line-2

20.Details of Grid Events during the Month of August 2023



Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1 or 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-1	Motipur	15.08.2023 14:31	15.08.2023 14:46	00:15	0	121	0.00%	0.49%	28844	24909	At 14:31 Hrs, 220 kV Motipur-MTPS-2 tripped due to B-Earth fault, however, breaker at Motipur didn't open and LB8 operated. As reported, isolator status of 220 kV Darbhanga (DMTCL)-Motipur-1 at Motipur end was showing connected to both bus. Consequently, both 220 kV Bus at Motipur tripped and Motipur S/s became dead. 121 MW load loss reported at Motipur, Muzaffarpur, Chakia.	220 kV Motipur-MTPS D/c 220 kV Motipur-Darbhanga (DMTCL) D/c 220 kV Motipur-Mushari D/c 220 kV Motipur-Sitamarhi D/c
2	GI-2	Adhunik (APNRL)	17.08.2023 12:18	17.08.2023 18:43	06:25	490	0	1.70%	0.00%	28822	23932	At 12:18 Hrs on 17.08.2023, 2*270 MW U#1 & U#2 at APNRL tripped, leading to load loss of around 490 MW. As reported, GT of both units tripped on E/f. There was a resistive fault in 400 kV Chaibasa-Kharagpur line which persisted for around 2.5 seconds. Both units at APNRL tripped during this instance.	2*270 MW U#1 & U#2 at APNRL 400 kV Chaibasa-Kharagpur-1

20.Details of Grid Events during the Month of August 2023													
North-East Region													
Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM:SS)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the		Antecedent Generation/Load in the Regional Grid		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(G1 for 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD 1	Serchip, Lunglei, Melriat(MI) and Lungmual areas of Mizoram Power System	01-Aug-23 12:25	01-Aug-23 12:38	00:13:00	0	29	0.00%	1.07%	2689	2713	Serchip, Lunglei, Melriat(MI) and Lungmual areas of Mizoram Power System were connected with the rest of NER grid through 132 kV Zuangtui -Serchip line. 132 kV Aizawl-Lungmual line was under planned shutdown from 07:54 Hrs on 01.08.2023. At 12:25 Hrs on 01.08.2023, 132 kV Zuangtui -Serchip line tripped. Due to tripping of this element, Serchip, Lunglei, Melriat(MI) and Lungmual areas of Mizoram Power System got separated from the rest of NER Grid and subsequently collapsed due to no source available in these areas. Power supply was extended to Serchip, Lunglei, Melriat(MI) and Lungmual areas of Mizoram Power System by charging 132 kV Zuangtui-Serchip line at 12:38 Hrs on 01.08.2023.	132 kV Zuangtui -Serchip line
2	GD 1	Meluri, Kiphire areas and Likimro HEP of Nagaland Power System	01-Aug-23 19:14	01-Aug-23 19:26	00:12:00	21	8	0.60%	0.23%	3491	3447	Meluri, Kiphire areas and Likimro HEP of Nagaland Power System were connected with the rest of NER grid through 132 kV Kohima-Meluri line. At 19:14 Hrs on 01.08.2023, 132 kV Kohima-Meluri line tripped. Due to tripping of this element, Meluri, Kiphire areas and Likimro HEP of Nagaland Power System got separated from the rest of NER Grid and subsequently collapsed due to load generation mismatch in these areas. Power supply was extended to Meluri, Kiphire areas and Likimro HEP of Nagaland Power System by charging 132 kV Kohima-Meluri line at 19:26 Hrs on 01.08.2023.	132 kV Kohima-Meluri line
3	GD 1	Meluri, Kiphire areas and Likimro HEP of Nagaland Power System	02-Aug-23 12:30	02-Aug-23 12:37	00:07:00	23	5	0.91%	0.17%	2522	2861	Meluri, Kiphire areas and Likimro HEP of Nagaland Power System were connected with the rest of NER grid through 132 kV Kohima-Meluri line. At 12:30 Hrs on 02.08.2023, 132 kV Kohima-Meluri line tripped. Due to tripping of this element, Meluri, Kiphire areas and Likimro HEP of Nagaland Power System got separated from the rest of NER Grid and subsequently collapsed due to load generation mismatch in these areas. Power supply was extended to Meluri, Kiphire areas and Likimro HEP of Nagaland Power System by charging 132 kV Kohima-Meluri line at 12:37 Hrs on 02.06.2023.	132 kV Kohima-Meluri line
4	GD 1	Dimapur(NL) area of Nagaland Power System	02-Aug-23 16:35	02-Aug-23 17:02	00:27:00	0	85	0.00%	2.93%	2722	2903	Dimapur(NL) area of Nagaland Power System was connected with the rest of NER grid through 132 kV Dimapur (PG) - Dimapur (DoP, Nagaland) D/C lines. At 16:35 Hrs on 02.08.2023, 132 kV Dimapur (PG) - Dimapur (DoP, Nagaland) D/C lines tripped. Due to tripping of this element, Dimapur(NL) area of Nagaland Power System got separated from the rest of NER Grid and subsequently collapsed due to no source available in this area. Power supply was extended to Dimapur(NL) area of Nagaland Power System by charging 132 kV Dimapur (PG) - Dimapur (DoP, Nagaland) 1 line at 17:02 Hrs on 02.08.2023.	132 kV Dimapur (PG) - Dimapur (DoP, Nagaland) D/C lines
5	GD 1	Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System	02-Aug-23 21:52	02-Aug-23 22:21	00:29:00	18	20	0.54%	0.67%	3315	2995	Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System were connected with the rest of NER grid through 132 kV Balipara - Tenga line. At 21:52 Hrs on 02.08.2023, 132 kV Balipara - Tenga line tripped. Due to tripping of this element, Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System got separated from the rest of NER Grid and subsequently collapsed due to load generation mismatch in these areas. Power supply was extended to Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System by charging 132 kV Balipara - Tenga line at 22:21 Hrs on 02.08.2023.	132 kV Balipara - Tenga line
6	GD 1	New Umtru Generating Station of Meghalaya Power System	03-Aug-23 16:47	03-Aug-23 17:32	00:45	36	0	1%	0%	2922	2934	New Umtru Generating Station of Meghalaya Power System was connected with the rest of NER grid through 132 kV EPIP II - New Umtru & 132 kV Umtru - New Umtru lines. At 16:47 Hrs on 03.08.2023,132 kV EPIP II - New Umtru & 132 kV Umtru - New Umtru lines tripped. Due to tripping of these elements, New Umtru Generating Station of Meghalaya Power System got separated from the rest of NER Grid and subsequently collapsed due to loss of evacuation path. Power supply was extended to New Umtru Generating Station of Meghalaya Power System by charging 132 kV EPIP II - New Umtru line at 17:32 Hrs on 03.08.2023.	132 kV EPIP II - New Umtru & 132 kV Umtru - New Umtru lines
7	GD 1	Daporizo, Basar & Along areas of Arunachal Pradesh Power System	04-Aug-23 23:02	05-Aug-23 00:36	01:34	0	21	0%	1%	3257	2864	Daporizo, Basar & Along areas of Arunachal Pradesh Power System were connected with the rest of NER Grid through 132 kV Daporijo -Ziro and 132 kV Along - Pasighat lines. At 23:02 Hrs on 04.08.2023, 132 kV Daporijo -Ziro and 132 kV Along - Pasighat lines tripped. Due to tripping of these elements, Daporizo, Basar & Along areas of Arunachal Pradesh Power System got separated from the rest of NER Grid and subsequently collapsed due to no source available in these areas. Power supply was extended to Daporizo, Basar & Along areas of Arunachal Pradesh Power System by charging 132 kV Along - Pasighat Line at 00:36 Hrs of 05.08.2023.	132 kV Daporijo -Ziro and 132 kV Along - Pasighat lines

20.Details of Grid Events during the Month of August 2023													
North-East Region													
Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM:SS)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the		Antecedent Generation/Load in the Regional Grid		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(G1 1or 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
8	GD 1	Jawaharnagar area of Assam Power System	07-Aug-23 09:32	07-Aug-23 10:08	00:36:00	0	28	0.00%	0.99%	2180	2828	Jawaharnagar area of Assam Power System was connected with the rest of NER Grid through 220 kV Samaguri-Jawaharnagar line. 220 kV Sarusajai-Jawaharnagar line was under planned shutdown. At 09:32 Hrs on 07.08.2023, 220 kV Samaguri-Jawaharnagar line tripped. Due to tripping of this element, Jawaharnagar area of Assam Power System got separated from the rest of NER Grid and subsequently collapsed due to no source available in this area. Power supply was extended to the Jawaharnagar area of Assam Power System by charging 220 kV Sarusajai-Jawaharnagar line at 10:08 Hrs of 07.08.2023.	220 kV Samaguri-Jawaharnagar line
9	GD 1	Dhemaji & Silapathar areas of Assam Power System	08-Aug-23 08:39	08-Aug-23 08:56	00:17:00	0	27	0.00%	1.12%	3472	2411	Dhemaji & Silapathar areas of Assam Power System were connected with the rest of NER Grid through 132 kV North Lakhimpur - Dhemaji line. At 08:39 Hrs on 08.08.2023, 132 kV North Lakhimpur - Dhemaji line tripped. Due to tripping of this element, Dhemaji & Silapathar areas of Assam Power System got separated from the rest of NER Grid and subsequently collapsed due to no source available in these areas. Power supply was extended to the Dhemaji & Silapathar areas of Assam Power System by charging 132 kV North Lakhimpur - Dhemaji line at 08:56 Hrs of 08.08.2023.	132 kV North Lakhimpur - Dhemaji line
10	GD 1	Basar and Along areas of Arunachal Pradesh Power System	08-Aug-23 13:18	08-Aug-23 16:02	02:44:00	0	11	0.00%	0.37%	2604	2947	Basar and Along areas of Arunachal Pradesh Power System were connected with the rest of NER Grid through 132 kV Along-Pasighat and 132 kV Along-Daporijo lines. At 13:18 Hrs on 08.08.2023, 132 kV Along-Pasighat and 132 kV Along-Daporijo lines tripped. Due to tripping of these elements, Basar and Along areas of Arunachal Pradesh Power System were separated from the rest of NER Grid and subsequently collapsed due to no source available in these areas. Power supply was extended to Along area of Arunachal Pradesh Power System by charging 132 kV Along - Pasighat line at 16:02 Hrs on 08.08.2023 and then power supply was extended to Basar area of Arunachal Pradesh Power System by charging 132 kV Along - Basar line at 16:30 Hrs on 08.08.2023.	132 kV Along-Pasighat and 132 kV Along-Daporijo lines
11	GD 1	Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System	08-Aug-23 20:59	08-Aug-23 22:03	01:04:00	24	22	0.79%	0.66%	3036	3314	Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System were connected with the rest of NER grid through 132 kV Balipara - Tenga line. At 20:59 Hrs on 08.08.2023, 132 kV Balipara - Tenga line tripped. Due to tripping of this element, Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System got separated from the rest of NER Grid and subsequently collapsed due to load generation mismatch in these areas. Power supply was extended to Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System by charging 132 kV Balipara - Tenga line at 22:03 Hrs on 08.08.2023.	132 kV Balipara - Tenga line
12	GD 1	Boko area and Boko Solar Power Plant of Assam Power System	18-Aug-23 09:32	18-Aug-23 11:25	01:53	24	20	1%	1%	3044	2606	Boko area and Boko Solar Power Plant of Assam Power System were connected with the rest of NER Grid through 220 kV Agia - Boko and 220 kV Azara - Boko lines. At 09:32 Hrs on 18.08.2023, 220 kV Agia - Boko and 220 kV Azara - Boko lines tripped. Due to tripping of these elements, Boko area and Boko Solar Power Plant of Assam Power System were separated from the rest of NER Grid and subsequently collapsed due to load generation mismatch in these areas. Power supply was extended to Boko area and Boko Solar Power Plant of Assam Power System by charging 220 kV Azara - Boko line at 11:25 Hrs on 18.08.2023.	220 kV Agia - Boko and 220 kV Azara - Boko lines
13	GD 1	Meluri, Kiphire areas and Likimro HEP of Nagaland Power System	18-Aug-23 18:51	18-Aug-23 20:00	01:09	16	12	0%	0%	3540	3391	Meluri, Kiphire areas and Likimro HEP of Nagaland Power System were connected with the rest of NER Grid through 132 kV Kohima-Meluri line. At 18:51 Hrs on 18.08.2023, 132 kV Kohima-Meluri line tripped. Due to tripping of this element, Meluri, Kiphire areas and Likimro HEP of Nagaland Power System got separated from the rest of NER Grid and subsequently collapsed due to load generation mismatch in these areas. Power supply was extended to Meluri, Kiphire areas and Likimro HEP of Nagaland Power System by charging 66 kV Kiphire-Tuensang line at 20:00 Hrs on 18.08.2023. 132 kV Kohima - Meluri line was charged at 16:13 Hrs on 22.08.2023	132 kV Kohima-Meluri line
14	GD 1	Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System	21-Aug-23 19:27	21-Aug-23 19:49	00:22	22.5	25.5	1%	1%	3638	3025	Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System were connected with rest of grid through 132 kV Balipara - Tenga line. At 19:27 Hrs on 21.08.2023, 132 kV Balipara - Tenga line tripped. Due to tripping of this element, Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System got separated from the rest of NER Grid and subsequently collapsed due to load generation mismatch in these areas. Power supply was extended to Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System by charging 132 kV Balipara - Tenga line at 19:49 Hrs on 21.08.2023.	132 kV Balipara - Tenga line

20.Details of Grid Events during the Month of August 2023															
North-East Region															
Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM:SS)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the		Antecedent Generation/Load in the Regional Grid		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped		
	(G1 to 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)				
15	GD 1	Chapakhowa area of Assam Power System and Pasighat, Roing, Tezu, Namsai areas of Arunachal Pradesh Power System	26-Aug-23 18:03	26-Aug-23 19:00	00:57	0	19	0%	1%	3512	2985	Chapakhowa area of Assam Power System and Pasighat, Roing, Tezu, Namsai areas of Arunachal Pradesh Power System were connected with rest of grid through 132 kV Rupai - Chapakhowa line. 132 kV Along- Pasighat line was under emergency shutdown since 16:19 Hrs on 26.08.2023 due to tower collapse. At 18:03 Hrs on 26.08.2023, 132 kV Rupai - Chapakhowa line tripped. Due to tripping of this element, Chapakhowa area of Assam Power System and Pasighat, Roing, Tezu, Namsai areas of Arunachal Pradesh Power System got separated from the rest of NER Grid and subsequently collapsed due to no source available in these areas. 132 kV Rupai - Chapakhowa line was declared faulty at 19:00 Hrs on 26.08.2023. Power supply was extended to Chapakhowa area of Assam Power System by charging 132 kV Rupai - Chapakhowa line at 10:33 Hrs on 27.08.2023. Power supply was extended to Pasighat, Roing, Tezu and Namsai areas of Arunachal Pradesh Power System by charging 132 kV Roing - Chapakhowa 1 line at 11:00 Hrs on 27.08.2023.	132 kV Rupai - Chapakhowa line		
16	GD 1	Chapakhowa area of Assam Power System and Basar, Along, Pasighat, Roing, Tezu, Namsai areas of Arunachal Pradesh Power System	29-Aug-23 09:14	29-Aug-23 09:59	00:45	0	22	0%	1%	3316	2355	Chapakhowa area of Assam Power System and Basar, Along, Pasighat, Roing, Tezu, Namsai areas of Arunachal Pradesh Power System were connected with rest of grid through 132 kV Rupai - Chapakhowa line. 132 kV Daporijo - Basar line was declared faulty since 05:13 Hrs on 27.08.2023. At 09:14 Hrs on 29.08.2023, 132 kV Rupai - Chapakhowa line tripped. Due to tripping of this element, Chapakhowa area of Assam Power System and Basar, Along, Pasighat, Roing, Tezu, Namsai areas of Arunachal Pradesh Power System got separated from the rest of NER Grid and subsequently collapsed due to no source available in these areas. Power supply was extended to Chapakhowa area of Assam Power System and Basar, Along, Pasighat, Roing, Tezu, Namsai areas of Arunachal Pradesh Power System by charging 132 kV Rupai - Chapakhowa line at 09:59 Hrs on 29.08.2023	132 kV Rupai - Chapakhowa line		
17	GD 1	Zuangtui, Saitual, Vankal, Serchhip, Lunglei and Khawzawl areas and Vankal Solar Power Plant of Mizoram Power System	29-Aug-23 11:49	29-Aug-23 13:10	01:21	18	19	1%	1%	3246	2478	Zuangtui, Saitual, Vankal, Serchhip, Lunglei and Khawzawl areas and Vankal Solar Power Plant of Mizoram Power System were connected with the rest of NER grid through 132 kV Melriat(PG) - Zuangtui line. 132 kV Melriat-Lunglei line was under shutdown to control overloading of 132kV Aizawl-Lungmual line At 11:49 Hrs on 29.08.2023, 132 kV Melriat(PG) - Zuangtui line tripped. Due to tripping of this element, Zuangtui, Saitual, Vankal, Serchhip, Lunglei and Khawzawl areas and Vankal Solar Power Plant of Mizoram Power System got separated from the rest of NER Grid and subsequently collapsed due to load generation mismatch in these areas Power supply was extended to Zuangtui, Saitual, Vankal, Serchhip, Lunglei and Khawzawl areas and Vankal Solar Power Plant of Mizoram Power System by charging 132 kV Melriat(PG) - Zuangtui line at 13:10 Hrs on 29.08.2023.	132 kV Melriat(PG) - Zuangtui line		
18	GI-II	Assam	06-Aug-23 00:42	06-Aug-23 02:30	01:48	228	0	7%	0%	3211	2763	BgTPP Unit 2 tripped at 00:42 Hrs on 06.08.2023 due to tripping of Unit Auxiliary Transformer - 2 on Buchholz protection. Revision done from Block No. 11 on 06.08.2023.	BgTPP Unit 2		
19	GI-II	Assam	09-Aug-23 16:40	09-Aug-23 18:30	01:50	228	0	7%	0%	3334	2747	BgTPP Unit 2 tripped at 16:40 Hrs on 09.08.2023 due to low Primary air header pressure. Revision done from Block No. 75 on 09.08.2023.	BgTPP Unit 2		
20	GI-II	Assam	19-Aug-23 12:16	19-Aug-23 14:00	01:44	228	0	9%	0%	2563	2588	BgTPP Unit 2 tripped at 12:16 Hrs on 19.08.2023 due to Flame failure. Revision done from Block No. 57 on 19.08.2023	BgTPP Unit 2		
21	GI-I	Assam	20-Aug-23 01:42	20-Aug-23 03:30	01:48	49	0	2%	0%	3113	2909	Kopili Unit 4 tripped at 01:42 Hrs on 20.08.2023 due to PRV main pipeline burst. Revision done from Block No. 15 on 20.08.2024	Kopili Unit 4		
22	GI-I	Assam	24-Aug-23 17:11	24-Aug-23 19:00	01:49	49	0	2%	0%	3263	2728	Kopili Unit 4 tripped at 17:11 Hrs on 24.08.2023 due to Shear Pin Broken. Revision done from Block No. 77 on 24.08.2024	Kopili Unit 4		

21. NEW ELEMENTS COMMISSIONED* IN AUGUST 2023							
COMMISSIONING OF NEW GENERATING UNITS							
REGION	S.NO.	ENTITY	UNIT NAME / LOCATION	ADD. CAPACITY (MW)	UNIT NO.	INS. CAPACITY (MW)	DATE®
NR	1	THAR SURYA	Thar Surya1 Bikaner(Solar)/Rajasthan	9	-	300	26-08-2023
WR	2	ALFANAR NETRA VAYU	Alfanar Netra Vayu(Wind)/Gujarat	24.7	I	121.5	04-08-2023
	3	ADANI WIND ENERGY KUTCHH FOUR LTD	Adani Wind Energy Kutchh Four Ltd(Wind)/Gujarat	23.1	I	157.5	25-08-2023
SR	4	JSW RENEW TWO ENERGY LIMITED	JSW Renew Two(Wind)/Tamilnadu	27	-	197.1	30-08-2023
	®RE (Solar & Wind generation added capacity FTC is in phases. Date mentioned is the date by which complete (Added) capacity						
COMMISSIONING OF NEW ICTS							
REGION	S.NO.	ENTITY	SUB-STATION	VOLTAGE (kV)	ICT NO.	CAPACITY (MVA)	DATE
SR	1	KSEB	Kottayam	400/220	I	315	17-08-2023
	2	PGCIL	TTGS	400/220	V	500	30-08-2023
NER	3	AEGCL	Moran	132/33	I	31.5	09-08-2023
COMMISSIONING OF NEW TRANSMISSION LINES							
REGION	S.NO.	ENTITY	LINE NAME	CKT NO.	VOLTAGE (kV)	DATE	
NR	1	RRVPNL	400kV Bhadla-Bikaner	I	400	18-08-2023	
	2	RRVPNL	400kV Bhadla-Bikaner	II	400	18-08-2023	
SR	3	TSTRANSO	400kV Yedula-Narlapur	II	400	30-08-2023	
	4	MUML & NEEPCO	13 kV North Lakhimpur-Pare	-	132	01-08-2023	
LILO OF TRANSMISSION LINES							
REGION	S.NO.	ENTITY	LINE NAME (LILOed LINE)	LILO AT	VOLTAGE (kV)	DATE	
NER	1	NER-II Transmission Limited	132kV Biswanath Chariali-Gohpur (132 kV Biswanath Chariali-Itanagar II)	Gohpur	132	11-08-2023	
	2	NER-II Transmission Limited	132kV Itanagar-Gohpur (132 kV Biswanath Chariali-Itanagar II)	Gohpur	132	12-08-2023	
COMMISSIONING OF BUS/LINE REACTORS							
REGION	S.NO.	ENTITY	SUB-STATION / LINE (@SUB-STATION)	VOLTAGE (kV)	CAPACITY (MVAR)	DATE	
NR	1	UPPTCL	Bus Reactor-I@Panki	400	125	09-08-2023	
	2	UPPTCL	400kV Unnao-Bareilly Ckt-I@Bareilly	400	63	11-08-2023	
	3	OCBTL,UPPTCL	400kV Jaunpur- Obra C@Jaunpur	400	50	15-08-2023	
ER	4	WBSETCL	Bus Reactor-II@Durgapur	400	125	31-08-2023	
COMMISSIONING OF HVDC/FACTS DEVICE/SYSTEM							
REGION	S.NO.	NAME	SUB-STATION / CONSTITUENT	RATINGS	VOLTAGE (kV)	DATE	
*Includes first time charging (FTC) as well							

22. Voltage Profile

विद्युत विभव रूपरेखा माह - अगस्त 2023

VOLTAGE PROFILE - AUGUST 2023

Date of reporting: 05-Sep-23

क्र.स. Sl. No.	क्षेत्र REGION	उपकेंद्र SUBSTATION	VOLTAGE < V(lower)* (V=380,728 kV)	V(lower) < VOLTAGE < V(upper)*	VOLTAGE > V(upper)* (V=420,800 kV)	Voltage Deviation Index (%age of time voltage is outside range)	Number of hours voltage was outside IEGC band during month	उच्चतम (कि.वो.) Maximum(kV)	निम्नतम(कि.वो.) Minimum(kV)	औसत (कि.वो.) Average(kV)
1	पूर्वी क्षेत्र ER	अंगल ANGUL	100%	0%	0%	0%	0	799	743	773
2		दार्लिपाली DARLIPALI	0%	100%	0%	0%	0	793	761	778
3		गया GAYA	0%	100%	0%	0%	0	792	761	779
4		जेरत JEERAT	0%	100%	0%	0%	0	795	739	763
5		झारसगुड़ा JHARSUGUDA	0%	100%	0%	0%	3	803	769	787
6		मिदनापुर MEDINIPUR	0%	100%	0%	0%	0	792	750	770
7		रांची RANCHI	0%	100%	0%	0%	0	796	766	781
8		सासाराम SASARAM	0%	100%	0%	0%	0	782	744	765
1	उत्तरी क्षेत्र NR	आगरा AGRA	0%	100%	0%	0%	0	799	756	777
2		आगरा (फतेहाबाद) AGRA (FATEHABAD)	0%	100%	0%	0%	0	796	744	768
3		अजमेर AJMER	0%	100%	0%	0%	1	803	750	776
4		अलीगढ़ ALIGARH	0%	100%	0%	0%	0	796	746	772
5		अनपरा सी ANPARA-C	0%	100%	0%	0%	0	780	757	768
6		अनपरा डी ANPARA-D	0%	100%	0%	0%	0	778	755	766
7		अंता ANTA	0%	100%	0%	0%	0	804	759	778
8		बालिया BALLIA	0%	100%	0%	0%	0	795	752	772
9		बारा BARA	0%	100%	0%	0%	0	783	759	770
10		भादला BHADLA	0%	100%	0%	0%	0	792	743	772
11		भादला-2 BHADLA-2	0%	100%	0%	0%	0	797	751	775
12		भिवानी BHIWANI	0%	100%	0%	0%	0	798	750	775
13		बिकानेर BIKANER	0%	100%	0%	0%	0	798	748	773
14		बरैली BAREILLY	0%	99%	1%	1%	5	807	745	776
15		चित्तौड़गढ़ CHITTORGARH	0%	99%	1%	1%	5	806	748	781
16		फतेहगढ़-2 FATEHGARH-2	0%	100%	0%	0%	0	795	743	773
17		फतेहपुर FATEHPUR	0%	100%	0%	0%	0	792	743	769
18		ग्रेटर नोएडा GREATER NOIDA	0%	100%	0%	0%	0	800	743	773
19		हापड़ HAPUR	0%	100%	0%	0%	1	807	733	768
20		जवाहरपुर JAWAHARPUR	0%	100%	0%	0%	1	801	752	780
21		झाटिकरा JHATIKARA	0%	100%	0%	0%	0	793	747	770
22		कानपुर जेआइएस KANPUR GIS	0%	100%	0%	0%	0	789	751	772
23		खैतरी KHETRI	0%	100%	0%	0%	0	797	746	773
24		कोटेश्वर KOTESHWAR	0%	100%	0%	0%	0	798	725	769
25		ललितपुर LALITPUR	0%	100%	0%	0%	0	781	742	758
26		लखनऊ LUCKNOW	0%	100%	0%	0%	0	797	744	772
27		मैनपुरी MAINPURI	0%	100%	0%	0%	0	798	750	776
28		मेरठ MEERUT	0%	100%	0%	0%	0	800	744	775
29		मोवा MOGA	0%	100%	0%	0%	0	789	748	768
30		ओबरा सी OBRA C	0%	100%	0%	0%	0	779	752	764
31		उरई ORAI	0%	100%	0%	0%	1	802	765	784
32		फागी PHAGI	0%	100%	0%	0%	0	805	755	777
33		उन्नाव UNNAO	0%	100%	0%	0%	0	790	741	763
34		वाराणसी VARANASI	0%	100%	0%	0%	0	794	761	779
1	पश्चिमी क्षेत्र WR	अकोला AKOLA	0%	100%	0%	0%	0	792	753	776
2		औरंगाबाद AURANGABAD	0%	100%	0%	0%	0	799	742	777
3		भोपाल (बीडीटीसीएल) BHOPAL (BDTCL)	0%	100%	0%	0%	0	787	751	772
4		भुज BHUJ	0%	100%	0%	0%	4	806	749	778
5		भुज-2 BHUJ-2	0%	100%	0%	0%	0	798	744	772
6		बिलासपुर BILASPUR	0%	100%	0%	0%	0	792	762	778
7		बीना BINA	0%	100%	0%	0%	0	800	765	781
8		बनसकंठा BANASKANTHA	0%	100%	0%	0%	3	810	754	784
9		चापा CHAMPA	0%	94%	6%	6%	44	808	762	789
10		धुल (बीडीटीसीएल) DHULE (BDTCL)	0%	100%	0%	0%	0	798	753	777
11		धर्मजयगढ़ DHARAMJAIGARH	0%	100%	0%	0%	0	793	764	779
12		रायपुर प्रोडिंग RAIPUR POOLING	0%	100%	0%	0%	0	793	765	783
13		एकतुनी EKTUNI	0%	100%	0%	0%	0	794	746	773
14		गदरवाड़ा GADARWARA	0%	100%	0%	0%	1	802	769	785
15		ग्वालियर GWALIOR	0%	100%	0%	0%	1	803	747	782
16		इंदौर INDORE	0%	100%	0%	0%	0	786	750	772
17		जबलपुर JABALPUR	0%	100%	0%	0%	1	801	775	787
18		खडवा KHANDWA	0%	100%	0%	0%	0	789	752	775
19		कोरडी KORADI	0%	100%	0%	0%	0	781	749	767
20		लकाडिया LAKADIYA	0%	98%	2%	2%	14	809	752	783
21		रायगढ़ प्रोडिंग RAIGARH POOLING	0%	100%	0%	0%	0	801	769	786
22		पड़घं PADGHE	0%	98%	2%	2%	12	812	745	781
23		परली PARLI	0%	99%	1%	1%	6	804	747	784
24		पुणे PUNE	0%	98%	2%	2%	15	812	739	779
25		राजनंदगांव RAJNANDGAON	0%	97%	3%	3%	22	808	769	791
26		सासन SASAN	0%	100%	0%	0%	0	792	770	780
27		सातना SATNA	0%	100%	0%	0%	0	800	772	785
28		सेवनी SEONI	0%	100%	0%	0%	0	797	760	781
29		सीपट SIPAT	0%	100%	0%	0%	0	792	764	779
30		सोलापुर SOLAPUR	0%	98%	2%	2%	15	805	748	785
31		तिरुई TIRORA	0%	100%	0%	0%	0	778	749	764
32		तामनार TAMNAR	0%	100%	0%	0%	0	799	768	784
33		वडोदरा VADODARA	0%	100%	0%	0%	3	804	747	779
34		विंध्याचल प्रोडिंग VINDHYACHAL PS	0%	100%	0%	0%	0	795	774	783
35		वर्धा WARDHA	0%	100%	0%	0%	0	802	746	780
36		वरौरा WARORA	0%	100%	0%	0%	2	806	756	785
1	दक्षिणी क्षेत्र SR	कडपा CUDDAPAH	0%	92%	8%	8%	55	818	754	785
2		चिल्कुरीपेट CHILAKALURIPETA	0%	99%	1%	1%	7	816	735	779
3		कुरुन कुरुन KURNOOL	0%	100%	0%	0%	0	801	736	774
4		महेश्वर MAHESWARAM	0%	97%	3%	3%	20	812	738	780
5		निजामाबाद NIZAMABAD	0%	93%	7%	7%	47	812	735	784
6		नेल्लूर प्रोडिंग NELLORE PS	0%	100%	0%	0%	0	800	741	769
7		रायचूर RAICHUR	0%	100%	0%	0%	1	804	741	778
8		श्रीकाकुलम SRIKAKULAM	0%	96%	4%	4%	27	810	739	783
9		तिरुवलम THIRUVALEM	0%	99%	1%	1%	7	809	740	772
10		वेमगिरी VEMAGIRI	0%	95%	5%	5%	37	812	738	782
1	पूर्वोत्तर क्षेत्र NER	बिस्वनाथ चौराहा BISWANATH CHARIALI (400 kV)	0%	100%	0%	0%	0	416	399	407
2		बोंगाईगांव BONGAIGAON (400 kV)	0%	100%	0%	0%	0	412	400	406
3		बोंगाईगांव टीपीएस BONGAIGAON TPS (400 kV)	0%	100%	0%	0%	0	416	403	410
4		इम्फाल IMPHAL (400 kV)	0%	100%	0%	0%	0	419	396	405
5		बर्निहाट BYRNHAT (400 kV)	0%	100%	0%	0%	0	418	404	411
6		कामेंग KAMENG (400 kV)	0%	100%	0%	0%	0	410	396	402
7		अज़ारा AZARA (400 kV)	0%	100%	0%	0%	0	398	390	395
8		मिसा MISA (400 kV)	0%	100%	0%	0%	0	411	394	402
9		न्यू मरियानी NEW MARIANI (400 kV)	0%	100%	0%	0%	0	415	396	406
10		न्यू कोहिमा NEW KOHIMA (400 kV)	0%	100%	0%	0%	0	415	383	399
11		पालाटाना PALATANA (400 kV)	0%	100%	0%	0%	0	412	355	407
12		पुबकेचनबारी PK BARI (400 kV)	0%	100%	0%	0%	0	412	387	403
13		रंगानादी RANGANADI (400 kV)	0%	100%	0%	0%	0	418	404	410
14		सिलचर SILCHAR (400 kV)	0%	100%	0%	0%	0	415	396	406
15		सूर्ययामानिनगर SURJYAMANINAGAR (400 kV)	0%	100%	0%	0%	0	411	395	404
16		थोबाल THOUBAL (400 kV)	0%	100%	0%	0%	0	411	388	399

All listed stations are 765 kV stations unless otherwise mentioned
*Percentage is calculated w.r.t. Time of one month.

23.List of Outages of Elements monitored by NLDC for the month of August-2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
Inter Regional Elements										
1	220kV Korba(East) - Budhipadar Ckt-III	Line	WR,ER	CSPTCL/GRIDCO	TS	01-Aug-2023 00:00	Tripped due to s/s blackout,Earth wire fallen on 220 kV Korba East-Budhipdar 2 & 220 kV Korba East-Raigarh(D/C tower)	14-Aug-2023 17:48	329:48:00	1
2	220kV Ponda - Ambewadi Ckt-I	Line	WR,SR	GOA/KPTCL	MO	01-Aug-2023 00:00	Line IDle charged from Ambewadi End	05-Aug-2023 07:40	103:40:00	0
3	220KV-MALANPUR-AURIYA-1	Line	WR,NR	MP	SC	01-Aug-2023 00:00	for modification/shifting work at Loc. No. 40 to 51 due to Construction of Bundelkhand expressway.	01-Aug-2023 19:16	19:16:00	0
4	220KV-MEHGAON-AURIYA-1	Line	WR,NR	MP	SC	01-Aug-2023 00:00	for modification/shifting work at Loc. No. 40 to 51 due to Construction of Bundelkhand expressway.	01-Aug-2023 19:06	19:06	0
5	220KV-MEHGAON-AURIYA-1	Line	WR,NR	MP	SC	01-Aug-2023 00:00	for modification/shifting work at Loc. No. 40 to 51 due to Construction of Bundelkhand expressway.	01-Aug-2023 19:05	19:05:00	0
6	+/- 800kV HVDC Champa - Kurukshetra Pole-II	HVDC	WR,NR	POWERGRID	TS	01-Aug-2023 07:51	blocked due to faulty card in hvdc control	01-Aug-2023 10:17	02:26:00	1
7	+/- 800kV HVDC Champa - Kurukshetra Pole-IV	HVDC	WR,NR	POWERGRID	TS	01-Aug-2023 07:51	Tzone protection operated in pole 2 at kurukshetra end	01-Aug-2023 08:29	00:38:00	1
8	800kV HVDC AGRA- ALIPURDUAR-III	HVDC	NR,ER		TS	02-Aug-2023 15:08	due to suspected earth fault	02-Aug-2023 16:03	00:55:00	1
9	220kV Korba(East) - Budhipadar Ckt-III	Line	WR,ER	CSPTCL/GRIDCO	TS	02-Aug-2023 23:46	Tripped from Budhipadar end only (Line on hold from Korba end), CB PD operated at Budipadar	03-Aug-2023 02:49	03:03:00	2
10	220kV Korba(East) - Budhipadar Ckt-III	Line	WR,ER	CSPTCL/GRIDCO	TS	03-Aug-2023 02:51	Tripped from Budhipadar end only with AR Block indication.	03-Aug-2023 08:03	05:12:00	3
11	400KV-NAUBATPUR(BH)-BALIA-1	Line	ER,NR	ER-I	SO	03-Aug-2023 09:52	STRINGING WORK OF OPGW AND REMOVAL OF AVIATION GLOBES	03-Aug-2023 20:30	10:38:00	0
12	400KV-NAUBATPUR(BH)-BALIA-1	Line	ER,NR	ER-I	SO	04-Aug-2023 08:41	STRINGING WORK OF OPGW AND REMOVAL OF AVIATION GLOBES	04-Aug-2023 20:28	11:47:00	0
13	220kV Malanpur - Auraiya Ckt-I	Line	WR,NR	MPPTCL/UPPCL	TL	05-Aug-2023 05:12	R phase fault	05-Aug-2023 09:12	04:00:00	1
14	400KV-NAUBATPUR(BH)-BALIA-1	Line	ER,NR	ER-I	SO	05-Aug-2023 09:20	STRINGING WORK OF OPGW AND REMOVAL OF AVIATION GLOBES	05-Aug-2023 20:52	11:32:00	0
15	400KV-NAUBATPUR(BH)-BALIA-1	Line	ER,NR	ER-I	SO	06-Aug-2023 08:30	STRINGING WORK OF OPGW AND REMOVAL OF AVIATION GLOBES	06-Aug-2023 17:27	08:57:00	0
16	132kV Rihand - Garwah Ckt-I	Line	ER,NR	UPPCL/JSEB	TL	06-Aug-2023 17:01	B phase fault.	06-Aug-2023 20:34	03:33:00	1
17	400KV-BIHARSARIFF(PG)-BALIA-2	Line	ER,NR	ER-I	SO	07-Aug-2023 10:03	FLASHED INSULATOR REPLACEMENT WORK	07-Aug-2023 20:55	10:52:00	0
18	132KV-SHEOPUR-KHANDAR-2	Line	WR,NR	MP	SO	07-Aug-2023 10:06	FOR LINE MAINTENANCE WORK	07-Aug-2023 19:42	09:36:00	0
19	400kV Kolhapur - Kudgi Ckt-I	Line	WR,SR	POWERGRID	SO	07-Aug-2023 14:29	work of conductor repairing & spacer tightening	07-Aug-2023 19:04	04:35:00	0
20	400kV Kolhapur - Kudgi Ckt-II	Line	WR,SR	POWERGRID	SO	07-Aug-2023 14:33	work of conductor repairing & spacer tightening	07-Aug-2023 19:07	04:34:00	0
21	765kV Solapur - Raichur Ckt-II	Line	WR,SR	POWERGRID	SO	08-Aug-2023 10:06	B-Phase Insulator replacement work at Tower No: 198	08-Aug-2023 19:09	09:03:00	0
22	220KV-MALANPUR-AURIYA-1	Line	WR,NR	MP	SO	08-Aug-2023 12:14	FOR LINE MAINTENANCE WORK	08-Aug-2023 19:09	06:55:00	0
23	132kV Sahupuri - Karmanasa Ckt-I	Line	ER,NR	UPPCL/BSPHCL	SE	08-Aug-2023 14:50	Oil Leakage in CT Y phase at Sahupuri(UP).	08-Aug-2023 17:01	02:11:00	0
24	+/- 800kV HVDC Raigarh - Pugalur Pole-II	HVDC	WR,SR	POWERGRID	SE	08-Aug-2023 20:34	hot spot is observed in R-phase clamp of the BPI going to AC PLC filter of Pole-2	09-Aug-2023 22:37	26:03:00	0
25	+/- 205kV HVDC Bhadravati Pole-II	HVDC	WR,SR	POWERGRID	SO	09-Aug-2023 11:11	"To replace 2 Nos. of thyristor/gate card in 1. Pole-2 WEST "Y" Phase in valve YDLV	10-Aug-2023 00:30	13:19:00	0
26	+/- 800kV HVDC Champa - Kurukshetra Pole-III	HVDC	WR,NR	POWERGRID	TS	09-Aug-2023 19:02	due to fault in 5008 card in hvdc control	09-Aug-2023 21:37	02:35:00	1
27	220kV Alipurduar - Salakati Ckt-I	Line	ER,NER	POWERGRID	SO	10-Aug-2023 09:42	Replacement of severely damaged TLA at loc 292 caused due to lightening	10-Aug-2023 18:39	08:57:00	0
28	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-II	HVDC	WR,NR	Adani Trans Ind Ltd	TL	11-Aug-2023 13:51	Due DC line fault	11-Aug-2023 15:12	01:21:00	1
29	220kV Ponda - Ambewadi Ckt-I	Line	WR,SR	GOA/KPTCL	MO	13-Aug-2023 06:49	Previously Anti theft charged	13-Aug-2023 07:10	00:21:00	0
30	220kV Xeldom - Ambewadi Ckt-I	Line	WR,SR	GOA/KPTCL	TL	13-Aug-2023 15:11	C-N fault, Zone 1 Distance 20.58 km Fault current-- 1.184 KA	13-Aug-2023 15:46	00:35:00	1
31	220kV Ponda - Ambewadi Ckt-I	Line	WR,SR	GOA/KPTCL	MO	13-Aug-2023 19:17	Goa intends to normalise its system by opening the 220 KV circuit breaker of Ambewadi-Ponda line at 220KV Ponda Ss	26-Aug-2023 07:08	299:51:00	0

NLDC Outage report of Month August 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
32	765kV Satna - Orai Ckt-I	Line	WR,NR	POWERGRID	TL	15-Aug-2023 13:33	Satna:- B-N fault, 5.455KA, 138KM Orai:- B-N fault, 3.97KA, 144.8KM	15-Aug-2023 14:26	00:53:00	1
33	400KV-SHUJALPUR-RAPP-1	Line	NR,WR	POWERGRID	SO	16-Aug-2023 11:28	Line terminal equipment works and L/R amp works at Shujalpur.	16-Aug-2023 23:18	11:50:00	0
34	765kV Gaya - Balia Ckt-I	Line	ER,NR	POWERGRID	TS	16-Aug-2023 16:41	broken jumper dropper between bay 707 and 708 of B phase	16-Aug-2023 23:45	07:04:00	1
35	220kV Raigarh - Budhipadar Ckt-I	Line	WR,ER	POWERGRID/G RIDCO	TL	16-Aug-2023 16:54	Rph to ground fault at Raigarh end., PLCC carrier command was not received at Raigarh end owing to tripping of line at Raigarh end in Z2 fault.	16-Aug-2023 18:32	01:38:00	1
36	400KV-KANSARI-BHINMAL-1	Line	NR,WR	POWERGRID	SO	17-Aug-2023 13:21	REF Relay Retrofitting work.	17-Aug-2023 23:43	10:22:00	0
37	400KV-KANSARI-KANKROLI-1	Line	NR,WR	POWERGRID	SO	19-Aug-2023 10:42	REF Relay Retrofitting work.	19-Aug-2023 20:25	09:43:00	0
38	400KV-PATNA-BALIA-2	Line	ER,NR	ER-I	SC	20-Aug-2023 07:58	TOWER ERECTION WORK	20-Aug-2023 20:18	12:20:00	0
39	400KV-PATNA-BALIA-2	Line	ER,NR	ER-I	SC	21-Aug-2023 08:15	TOWER ERECTION WORK	21-Aug-2023 20:34	12:19:00	0
40	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-II	HVDC	WR,NR	Adani Trans Ind Ltd	TL	21-Aug-2023 10:36	Due DC line fault	21-Aug-2023 15:56	05:20:00	2
41	220KV-MUDSHINGI-CHIKKODI-II-1	Line	WR,SR	MSLDC	SO	21-Aug-2023 13:10	Maintenance work	21-Aug-2023 18:33	05:23:00	0
42	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-I	HVDC	WR,NR	Adani Trans Ind Ltd	TL	21-Aug-2023 14:24	Due to transient fault in Electrode Line	21-Aug-2023 16:35	02:11:00	1
43	765kV Jabalpur - Orai Ckt-II	Line	WR,NR	POWERGRID	SO	22-Aug-2023 10:10	Relay TMU Card is faulty. To rectify the issue We have decided to replace the relay with spare relay available.	22-Aug-2023 12:05	01:55:00	0
44	220kV Mehgaon - Auraiya Ckt-I	Line	WR,NR	MPPTCL/UPPCL	TL	22-Aug-2023 19:24	Current Phase-A : 2.353 KAm, Phase-B : 184 Amp, Phase-C : 409 Amp	23-Aug-2023 23:18	27:54:00	1
45	220kV Xeldom - Ambewadi Ckt-I	Line	WR,SR	GOA/KPTCL	TL	23-Aug-2023 13:34	Bph-Earth, ZONE 2.	23-Aug-2023 14:09	00:35:00	2
46	765kV Gwalior - Agra Ckt-II	Line	WR,NR	POWERGRID	SE	23-Aug-2023 14:21	for attending broken polymer insulator at loc. No. 25	23-Aug-2023 18:54	04:33:00	0
47	+/- 800kV HVDC Champa - Kurukshetra Pole-II	HVDC	WR,NR	POWERGRID	TS	24-Aug-2023 13:47	Pole-2 blocked on Pole DC differential protection(due to mal function of DCCT)	24-Aug-2023 19:36	05:49:00	2
48	+/- 800kV HVDC Champa - Kurukshetra Pole-IV	HVDC	WR,NR	POWERGRID	TS	24-Aug-2023 13:47	Pole-4 blocked on Cat B protection	24-Aug-2023 15:16	01:29:00	2
49	400 KV BHINMAL-ZERDA (PG) CKT-1	Line	NR,WR	POWERGRID	SO	24-Aug-2023 16:41	For bypass WR-NR Inter- Regional Corridor / 400 KV Zerda- Bhinmal and 400 KV Bhinmal Kankroli line through jumper arrangement (temporary) at Loc. No. 02 of 400 KV D/C Zerda-Bhinmal- Kankroli LILO line vide note E-654054.	24-Aug-2023 22:28	05:47:00	0
50	+/- 800kV HVDC Champa - Kurukshetra Pole-I	HVDC	WR,NR	POWERGRID	TS	24-Aug-2023 17:47	Tripped on DCCT Chasis Mal Function	24-Aug-2023 19:45	01:58:00	1
51	800KV HVDC AGRA-BNC Pole-I	HVDC	NR,NER	POWERGRID	SE	25-Aug-2023 11:50	For checking water leakage in valve cooling system	26-Aug-2023 18:21	30:31:00	0
52	400KV-BIHARSARIFF(PG)-VARANASI-2	Line	ER,NR	ER-I	SO	25-Aug-2023 12:03	FLASHED INSULATOR REPLACEMENT WORK	25-Aug-2023 20:24	08:21:00	0
53	400kV Bhadravati - Ramagundam Ckt-II	Line	WR,SR	POWERGRID	MO	25-Aug-2023 12:21	For HVDC Bhadravati Bypass Black start Mock drill exercise	25-Aug-2023 13:48	01:27:00	0
54	+/- 205kV HVDC Bhadravati Pole-I	HVDC	WR,SR	POWERGRID	MO	25-Aug-2023 13:01	HVDC Mock drill exercise	25-Aug-2023 16:04	03:03:00	0
55	+/- 205kV HVDC Bhadravati Pole-II	HVDC	WR,SR	POWERGRID	MO	25-Aug-2023 13:01	HVDC Mock drill exercise	25-Aug-2023 16:16	03:15:00	0
56	400kV Bhadravati - Ramagundam Ckt-I	Line	WR,SR	POWERGRID	MO	25-Aug-2023 13:10	black start mock drill exercise	25-Aug-2023 16:59	03:49:00	0
57	400kV Bhadravati - Ramagundam Ckt-II	Line	WR,SR	POWERGRID	MO	25-Aug-2023 14:20	black start mock drill	25-Aug-2023 14:59	00:39:00	0
58	400KV-BIHARSARIFF(PG)-VARANASI-1	Line	ER,NR	ER-I	SO	26-Aug-2023 10:20	FLASHED INSULATOR REPLACEMENT WORK	26-Aug-2023 20:05	09:45:00	0
59	220kV Ponda - Ambewadi Ckt-I	Line	WR,SR	GOA/KPTCL	MO	26-Aug-2023 19:33	To keep the line idle charge from Ambewadi	27-Aug-2023 06:47	11:14:00	0
60	220kV Xeldom - Ambewadi Ckt-I	Line	WR,SR	GOA/KPTCL	TL	27-Aug-2023 09:00	From Ambewadi end ZONE 1 C-N Fault current- 362.8 KA Distance - 36.5 km	27-Aug-2023 10:00	01:00:00	3
61	220kV Ponda - Ambewadi Ckt-I	Line	WR,SR	GOA/KPTCL	MO	27-Aug-2023 19:51	In Idle charge condition (Opened form Ponda end)	28-Aug-2023 06:56	11:05:00	0
62	220kV Xeldom - Ambewadi Ckt-I	Line	WR,SR	GOA/KPTCL	TS	28-Aug-2023 10:43	Hand tripped due to heavy arching	28-Aug-2023 11:45	01:02:00	4
63	220kV Ponda - Ambewadi Ckt-I	Line	WR,SR	GOA/KPTCL	SO	28-Aug-2023 15:57	for replacement of deteriorated 220kV BUS Jumps	28-Aug-2023 22:03	06:06:00	0

NLDC Outage report of Month August 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
64	220kV Xeldom - Ambewadi Ckt-I	Line	WR,SR	GOA/KPTCL	SO	28-Aug-2023 16:00	for replacement of deteriorated 220kV BUS Jumps	28-Aug-2023 20:44	04:44:00	4
65	400kV Patna - Balia Ckt-II	Line	ER,NR	POWERGRID	TL	28-Aug-2023 17:46	DUE TO Y-B FAULT .PATNA (SITE)-M1- FD-57.04KM, FC- ly-9.2KA, lb-9.2KA	28-Aug-2023 20:22	02:36:00	1
66	765KV-DHARAMJAYGARH-RANCHI-1	Line	WR,ER	POWERGRID WR1	SO	29-Aug-2023 07:34	FOR REPLACEMENT OF EXISTING E/W WITH OPGW UNDER Western Region communication strengthening scheme.	30-Aug-2023 21:07	37:33:00	0
67	+/- 205kV HVDC Bhadravati Pole-II	HVDC	WR,SR	POWERGRID	SO	29-Aug-2023 08:14	To attend Thyristors redundancy lost	29-Aug-2023 20:52	12:38:00	0
68	400kV Patna - Balia Ckt-II	Line	ER,NR	POWERGRID	SE	29-Aug-2023 11:26	Hotspot attending in Y Phase line isolator	29-Aug-2023 18:40	07:14:00	1
69	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-II	HVDC	WR,NR	Adani Trans Ind Ltd	SE	29-Aug-2023 11:28	for removal of traction machine stuck in earth wire between tower no. 290 to 291,	29-Aug-2023 16:04	04:36:00	2
70	220kV Ponda - Ambewadi Ckt-I	Line	WR,SR	GOA/KPTCL	MO	30-Aug-2023 06:25	Power Regulation	30-Aug-2023 07:03	00:38:00	0
71	220kV Ponda - Ambewadi Ckt-I	Line	WR,SR	GOA/KPTCL	MO	30-Aug-2023 19:03	To control loading	01-Sep-2023 00:00	28:57:00	0
72	HVDC 500KV GAZUWAKA POLE 2	HVDC	SR,ER	pgsr1_sd	MO	31-Aug-2023 10:49	hvdc mock drill of jeypore-gazuwaka pole-2	31-Aug-2023 15:28	04:39:00	0
73	400kV Jeypore - Gajuwaka Ckt-II	Line	ER,SR	POWERGRID	MO	31-Aug-2023 11:18	HVDC mock drill of Jeypore Gazuwaka Pole-2	31-Aug-2023 12:39	01:21:00	0
74	220kV Xeldom - Ambewadi Ckt-I	Line	WR,SR	GOA/KPTCL	SE	31-Aug-2023 11:54	to attend severe red hot was observed on the Circuit breaker terminal pad	31-Aug-2023 15:01	03:07:00	4
75	220kV Raigarh - Budhipadar Ckt-I	Line	WR,ER	POWERGRID/G RIDCO	TL	31-Aug-2023 12:25	Tripped due to Y-G fault	31-Aug-2023 21:11	08:46:00	2

Transnational Elements

1	400kV Alipurduar - Jigmeling Ckt-II	Line	ER,BHUTAN	POWERGRID/B HUTAN	MO	01-Aug-2023 00:00	Line opened on voltage regulation	22-Aug-2023 20:11	524:11:00	0
2	132kV Tanakpur - Mahendernagar Ckt-I	Line	NR,NEPAL	NHPC/NEPAL	TL	08-Aug-2023 12:53	Tripped on earth fault	09-Aug-2023 01:31	12:38:00	1
3	132KV Surajpura-Ramnagar circuit	Line	ER,NEPAL		ME	01-Aug-2023 09:40	Manually switched off due to a man climbed on tower near Khatori Village	01-Aug-2023 16:30	06:50:00	0
4	132KV Surajpura-Ramnagar circuit	Line	ER,NEPAL		ME	04-Aug-2023 18:35	Manually switched off due to a man climbed on tower near Khatori Village	04-Aug-2023 21:20	02:45:00	0
5	132kV Rangia - Motanga Ckt-I	Line	NER,BHUTAN	AEGCL/BHUTAN	SE	05-Aug-2023 05:29	for rectification of hotspot of 132 kV Bus Sectional Isolator.	05-Aug-2023 08:53	03:24:00	0
6	400KV HVDC BHERAMARA Pole-I	HVDC	ER,INDIA/BANGLADESH	POWERGRID	TS	07-Aug-2023 09:49	Tripped - During software updating station control.	07-Aug-2023 10:23	00:34:00	1
7	400KV HVDC BHERAMARA Pole-II	HVDC	ER,INDIA/BANGLADESH	POWERGRID	TS	07-Aug-2023 09:49	Tripped - During software updating station control.	07-Aug-2023 10:23	00:34:00	1
8	400kV Behrampore - Behramara Ckt-III	Line	ER,BANGLADESH	POWERGRID/BANGLADESH	TL	10-Aug-2023 17:57	Due to R-Phase Zone -1 fault M1: R-Ph Zone-1, FD: 72km, FC:3.02 kA from Berhampore End	11-Aug-2023 02:28	08:31:00	1
9	400KV Alipurduar - Jigmeling (via Punstangchu) Ckt-II	Line	ER,BHUTAN	POWERGRID/B HUTAN	TS	15-Aug-2023 14:04	DT Received,RYB trip.	15-Aug-2023 14:45	00:41:00	1
10	400kV Alipurduar - Jigmeling Ckt-I	Line	ER,BHUTAN	POWERGRID/B HUTAN	TS	15-Aug-2023 14:04	DT Received, RYB trip.	15-Aug-2023 14:42	00:38:00	1
11	132KV-SURAJMANI NAGAR-COMILLA(BANGLADESH)-1	Line	NER,BANGLADESH	POWERGRID1	SO	25-Aug-2023 08:33	BUS SIDE ISOLATOR REALIGNMENT WORK, LA BASE INSULATOR MODIFICATION	25-Aug-2023 17:38	09:05:00	0
12	132kV Kataiya - Kusaha	Line	ER,NEPAL	BSEB/NEPAL	TL	26-Aug-2023 20:22	Tripped on distance protection relay	27-Aug-2023 16:07	19:45:00	1
13	400kV Binaguri -Tala Ckt-I	Line	ER,BHUTAN	POWERGRID/THEP	TL	28-Aug-2023 02:15	R-Phase to ground fault at THP end.	28-Aug-2023 02:54	00:39:00	1

Northern Region Elements

1	765 KV BHADLA_2 (PG)-FATEHGARH_II(PG) (PFTL) CKT-2	Line	NR	POWERGRID	SO	01-Aug-2023 00:00	For ladder logic and interlock checking for spare reactor commissioning	01-Aug-2023 02:33	02:33:00	0
2	765kV AJMER - CHITTORGARH Ckt-II	Line	NR	POWERGRID	MO	01-Aug-2023 00:00	Voltage Regulation	01-Aug-2023 09:20	09:20:00	0

NLDC Outage report of Month August 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
3	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	01-Aug-2023 00:00	Voltage Regulation	01-Aug-2023 08:30	08:30:00	0
4	765kV FATEHPUR - AGRA Ckt-II	Line	NR	POWERGRID	MO	01-Aug-2023 00:00	Voltage Regulation	02-Aug-2023 20:22	44:22:00	0
5	765kV ORAI - ALIGARH Ckt-II	Line	NR	POWERGRID	MO	01-Aug-2023 00:00	Voltage Regulation	06-Aug-2023 22:14	142:14:00	0
6	765kV PHAGI - BHIWANI Ckt-I	Line	NR	RRVPNL/PG	MO	01-Aug-2023 00:00	Voltage Regulation	01-Aug-2023 09:47	09:47:00	0
7	765kV Varanasi - Vindhyachal PS Ckt-I	Line	NR	PVTSL	SE	01-Aug-2023 05:52	for attending the hot spot on 718-89A R Ph Isolator at vindhyachal	01-Aug-2023 09:51	03:59:00	0
8	240MVAR LR(S) of 765kV Khetri Ckt-II at Jhatikara	Line Reactor	NR	POWERGRID NR	SE	01-Aug-2023 16:14	To attend Oil leakage	01-Aug-2023 17:43	01:29:00	0
9	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	01-Aug-2023 17:28	Voltage Regulation	02-Aug-2023 08:10	14:42:00	0
10	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	01-Aug-2023 17:50	Voltage Regulation	02-Aug-2023 09:19	15:29:00	0
11	765kV PHAGI - BHIWANI Ckt-I	Line	NR	RRVPNL/PG	MO	01-Aug-2023 18:29	Voltage Regulation	02-Aug-2023 10:48	16:19:00	0
12	765/400 KV 1000 MVA ICT 1 AT UNNAO(UP)	ICT	NR	STU	SO	02-Aug-2023 10:20	For Replacement of CT Switching Relay in 400kV Side by M/S GE T & D.	02-Aug-2023 17:09	06:49:00	0
13	765/400kV 1500MVA ICT-IV at Jhatikara	ICT	NR	POWERGRID	SE	02-Aug-2023 16:37	to attend Hotspot (temperature 175 degC) on dropper jumper at 400kV side of ICT-4.	02-Aug-2023 21:56	05:19:00	0
14	765kV AJMER - CHITTORGARH Ckt-I	Line	NR	POWERGRID	MO	02-Aug-2023 16:56	Voltage Regulation	04-Aug-2023 10:14	41:18:00	0
15	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	02-Aug-2023 18:06	Manually opened due to High Voltage	03-Aug-2023 09:27	15:21:00	0
16	765/400 KV 1500 MVA ICT 1 AT FATEHGARH_II(PG)	ICT	NR	POWERGRID	SO	02-Aug-2023 18:17	Commissioning of ICT with Spare ICT Bank & CSD Fine tuning works	03-Aug-2023 01:21	07:04:00	0
17	765kV PHAGI - BHIWANI Ckt-I	Line	NR	RRVPNL/PG	MO	02-Aug-2023 18:30	Manually opened due to High Voltage	03-Aug-2023 11:06	16:36:00	0
18	765kV BHADLA - BIKANER Ckt-I	Line	NR	POWERGRID	SE	02-Aug-2023 19:28	to attend hotspot in Y-Phase Line isolator contact at Bikaner PG end.	02-Aug-2023 23:52	04:24:00	0
19	765/400kV 1000MVA ICT-I at Bhiwani	ICT	NR	POWERGRID	SO	02-Aug-2023 22:13	high temperature of the dropper near the 89T isolator of LV side	03-Aug-2023 04:26	06:13:00	0
20	765/400 KV 1000 MVA ICT 1 AT UNNAO(UP)	ICT	NR	STU	SO	03-Aug-2023 09:43	For Replacement of CT Switching Relay in 400kV Side by M/S GE T & D.	03-Aug-2023 21:49	12:06:00	0
21	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	03-Aug-2023 17:14	Voltage Regulation	04-Aug-2023 08:59	15:45:00	0
22	765kV PHAGI - BHIWANI Ckt-II	Line	NR	RRVPNL/PG	MO	03-Aug-2023 18:08	taken out on over voltage	04-Aug-2023 10:46	16:38:00	0
23	765/400kV 1000MVA ICT-I at Unnao	ICT	NR	UPPCL	TS	04-Aug-2023 01:36	Due to REF operated	04-Aug-2023 17:29	15:53:00	1
24	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	04-Aug-2023 16:45	Voltage Regulation	05-Aug-2023 09:24	16:39:00	0
25	765kV AJMER - CHITTORGARH Ckt-II	Line	NR	POWERGRID	MO	04-Aug-2023 17:02	Voltage Regulation	05-Aug-2023 09:27	16:25:00	0
26	765kV PHAGI - BHIWANI Ckt-II	Line	NR	RRVPNL/PG	MO	04-Aug-2023 17:13	Voltage Regulation	05-Aug-2023 07:25	14:12:00	0
27	765/400 KV 1500 MVA ICT 4 AT FATEHGARH_II(PG)	ICT	NR	POWERGRID	SO	04-Aug-2023 18:06	For LBB testing of LV side Tie bay 429 for commissioning works of STATCOM Main bay 430	05-Aug-2023 01:43	07:37:00	0
28	765/400 KV 1500 MVA ICT 3 AT BIKANER(PG)	ICT	NR	POWERGRID	SO	04-Aug-2023 18:31	CSD Fine tuning work & ICT3 YPhase Radiator replacemenmt work	05-Aug-2023 04:43	10:12:00	0
29	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	04-Aug-2023 18:53	Voltage Regulation	05-Aug-2023 08:51	13:58:00	0
30	765 KV PHAGI(RS)-BHIWANI(PG) (PG) CKT-1	Line	NR	POWERGRID	SO	05-Aug-2023 08:20	for rectification/ tightening of towers of 765kV Phagi-Bhiwani Ckt-1	05-Aug-2023 22:59	14:39:00	0
31	765/400 KV 1000 MVA ICT 2 AT UNNAO(UP)	ICT	NR	STU	SO	05-Aug-2023 09:58	Work for Upgradation of Differential Relay(P-643,87TB Main-2) software By M/S GE T&D including testing after upgra	05-Aug-2023 16:58	07:00:00	0

NLDC Outage report of Month August 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
32	765/400 KV 1500 MVA ICT 2 AT FATEHPUR(PG)	ICT	NR	POWERGRID	SO	05-Aug-2023 10:03	for AMP works	06-Aug-2023 00:59	14:56:00	0
33	765kV Bikaner - Bhadla II Ckt-II	Line	NR	POWERGRID	TL	05-Aug-2023 16:11	Tripped only from Bikaner end due to DT received from Bhadla-II	05-Aug-2023 16:49	00:38:00	1
34	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	05-Aug-2023 16:42	Voltage Regulation	06-Aug-2023 08:56	16:14:00	0
35	765kV AJMER - CHITTORGARH Ckt-I	Line	NR	POWERGRID	MO	05-Aug-2023 17:03	Voltage Regulation	06-Aug-2023 09:55	16:52:00	0
36	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	05-Aug-2023 18:05	Voltage Regulation	06-Aug-2023 09:30	15:25:00	0
37	765/400 KV 1500 MVA ICT 3 AT BIKANER(PG)	ICT	NR	POWERGRID	SO	05-Aug-2023 18:22	CSD Fine tuning work & ICT3 YPhase Radiator replacemenmt work	06-Aug-2023 04:23	10:01:00	0
38	765kV FATEHPUR - AGRA Ckt-I	Line	NR	POWERGRID	MO	06-Aug-2023 04:12	Voltage Regulation	07-Aug-2023 10:37	30:25:00	0
39	765 KV PHAGI(RS)-BHIWANI(PG) (PG) CKT-1	Line	NR	POWERGRID	SO	06-Aug-2023 08:04	for rectification/ tightening of towers of 765kV Phagi-Bhiwani Ckt-1	06-Aug-2023 21:52	13:48:00	0
40	765/21 kV 825 MVA GT I at Lalitpur(LPG)	ICT	NR	POWERGRID NR	SO	06-Aug-2023 10:38	Half Yearly Maintenance preventive checking and strengthen monsoon protection to improve unit reliability (Unit is already out)	07-Aug-2023 13:44	27:06:00	0
41	765kV AJMER - CHITTORGARH Ckt-II	Line	NR	POWERGRID	MO	06-Aug-2023 17:03	Voltage Regulation	07-Aug-2023 09:24	16:21:00	0
42	765/400 KV 1500 MVA ICT 3 AT BIKANER(PG)	ICT	NR	POWERGRID	SO	06-Aug-2023 18:06	CSD Fine tuning work & ICT3 YPhase Radiator replacemenmt work	07-Aug-2023 02:26	08:20:00	0
43	+/- 500kV HVDC BALIA - BHIWADI Pole-II	HVDC	NR	POWERGRID	TS	06-Aug-2023 18:28	Transient fault . Pole tripped due to Emergency Off received at Bhiwadi end from Ballia end.	06-Aug-2023 23:12	04:44:00	1
44	765kV PHAGI - BHIWANI Ckt-I	Line	NR	RRVPNL/PG	MO	06-Aug-2023 21:52	Voltage Regulation	07-Aug-2023 07:40	09:48:00	0
45	765kV ORAI - ALIGARH Ckt-I	Line	NR	POWERGRID	MO	07-Aug-2023 02:57	Voltage Regulation	08-Aug-2023 09:45	30:48:00	0
46	765 KV PHAGI(RS)-BHIWANI(PG) (PG) CKT-1	Line	NR	POWERGRID	SO	07-Aug-2023 07:40	for rectification/ tightening of towers of 765kV Phagi-Bhiwani Ckt-1	07-Aug-2023 20:57	13:17:00	0
47	765/400 KV 1500 MVA ICT 1 AT FATEHPUR(PG)	ICT	NR	POWERGRID	SO	07-Aug-2023 10:47	for AMP works	07-Aug-2023 18:53	08:06:00	0
48	765kV PHAGI - BHIWANI Ckt-I	Line	NR	RRVPNL/PG	MO	07-Aug-2023 20:57	Voltage Regulation	08-Aug-2023 11:20	14:23:00	0
49	765kV AJMER - CHITTORGARH Ckt-I	Line	NR	POWERGRID	MO	07-Aug-2023 21:48	Voltage Regulation	08-Aug-2023 10:31	12:43:00	0
50	765kV FATEHPUR - AGRA Ckt-II	Line	NR	POWERGRID	MO	08-Aug-2023 04:20	Voltage Regulation	11-Aug-2023 12:37	80:17:00	0
51	765kV ORAI - ALIGARH Ckt-II	Line	NR	POWERGRID	SO	08-Aug-2023 10:46	for replacement of broken suspension string at Location No.: D-97	08-Aug-2023 18:00	07:14:00	0
52	765/400 kV 1500MVA ICT-II at Fatehpur	ICT	NR	POWERGRID	SE	08-Aug-2023 11:22	To attend Hot-spot	08-Aug-2023 13:17	01:55:00	0
53	765kV AJMER - CHITTORGARH Ckt-II	Line	NR	POWERGRID	MO	08-Aug-2023 17:06	Taken out on over voltage	09-Aug-2023 09:20	16:14:00	0
54	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	08-Aug-2023 17:19	Taken out on over voltage	09-Aug-2023 08:59	15:40:00	0
55	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	08-Aug-2023 18:10	Taken out on over voltage	09-Aug-2023 08:30	14:20:00	0
56	765/400 KV 1500 MVA ICT 3 AT MEERUT(PG)	ICT	NR	POWERGRID	SO	09-Aug-2023 09:40	for AMP works	09-Aug-2023 19:55	10:15:00	0
57	+/- 500kV HVDC BALIA - BHIWADI Pole-II	HVDC	NR	POWERGRID	SO	09-Aug-2023 11:41	replacement of damaged & heavily polluted CLR polymer insulators	09-Aug-2023 19:53	08:12:00	1
58	765kV AJMER - CHITTORGARH Ckt-I	Line	NR	POWERGRID	MO	09-Aug-2023 17:05	Taken out on over voltage	10-Aug-2023 09:22	16:17:00	0
59	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	09-Aug-2023 17:07	Taken out on over voltage	10-Aug-2023 08:34	15:27:00	0

NLDC Outage report of Month August 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
60	765kV PHAGI - BHIWANI Ckt-I	Line	NR	RRVPNL/PG	MO	09-Aug-2023 17:22	Taken out on over voltage	10-Aug-2023 09:31	16:09:00	0
61	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	09-Aug-2023 17:37	Voltage Regulation	10-Aug-2023 08:39	15:02:00	0
62	240 MVAR BUS REACTOR NO 1 AT 765KV PHAGI(RS)	Bus Reactor	NR	SLDC	SO	10-Aug-2023 11:06	Quarterly Maintenance	10-Aug-2023 20:34	09:28:00	0
63	765kV AGRA - JHATIKARA Ckt-I	Line	NR	POWERGRID	SE	10-Aug-2023 13:08	attend hotspot on Y-phase isolator dropper jumper of the reactor.	10-Aug-2023 14:28	01:20:00	0
64	765kV AJMER - CHITTORGARH Ckt-II	Line	NR	POWERGRID	MO	10-Aug-2023 16:22	Voltage Regulation	11-Aug-2023 11:35	19:13:00	0
65	765kV PHAGI - BHIWANI Ckt-II	Line	NR	RRVPNL/PG	MO	10-Aug-2023 17:55	Voltage Regulation	11-Aug-2023 09:51	15:56:00	0
66	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	10-Aug-2023 18:01	Voltage Regulation	11-Aug-2023 08:32	14:31:00	0
67	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	10-Aug-2023 18:08	Voltage Regulation	11-Aug-2023 08:51	14:43:00	0
68	765kV AJMER - CHITTORGARH Ckt-I	Line	NR	POWERGRID	MO	11-Aug-2023 16:53	Taken out on over voltage	12-Aug-2023 09:21	16:28:00	0
69	765/400kV 1500MVA ICT-II at Jhatikara	ICT	NR	POWERGRID	SE	11-Aug-2023 17:19	To attend hotspot observed in dropper/jumper of 400KV side.	11-Aug-2023 22:20	05:01:00	0
70	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	11-Aug-2023 17:24	Taken out on over voltage	12-Aug-2023 08:41	15:17:00	0
71	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	11-Aug-2023 18:21	Taken out on over voltage	12-Aug-2023 08:50	14:29:00	0
72	765/400kV 1000MVA ICT-II at Bhiwani	ICT	NR	POWERGRID	SE	11-Aug-2023 18:54	To attend hotspot in jumper of 400kV side near the bus and dropper side of the main and tie bay of ICT-2	12-Aug-2023 03:30	08:36:00	0
73	765/400 KV 1500 MVA ICT 1 AT AGRA(PG)	ICT	NR	POWERGRID	SO	12-Aug-2023 09:30	for AMP work.	12-Aug-2023 20:06	10:36:00	0
74	765kV AJMER - CHITTORGARH Ckt-II	Line	NR	POWERGRID	MO	12-Aug-2023 16:30	Voltage Regulation	13-Aug-2023 09:45	17:15:00	0
75	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	12-Aug-2023 16:49	Voltage Regulation	13-Aug-2023 08:38	15:49:00	0
76	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	12-Aug-2023 18:11	Voltage Regulation	13-Aug-2023 08:57	14:46:00	0
77	765kV AJMER - CHITTORGARH Ckt-II	Line	NR	POWERGRID	TL	13-Aug-2023 09:45	Tripped due to BCU issue at Chittorgarh end.	13-Aug-2023 10:28	00:43:00	1
78	765kV AJMER - CHITTORGARH Ckt-I	Line	NR	POWERGRID	MO	13-Aug-2023 16:01	Voltage Regulation	14-Aug-2023 09:44	17:43:00	0
79	765kV FATEHPUR - AGRA Ckt-I	Line	NR	POWERGRID	MO	13-Aug-2023 16:24	Voltage Regulation	14-Aug-2023 10:59	18:35:00	0
80	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	13-Aug-2023 16:54	Voltage Regulation	14-Aug-2023 08:48	15:54:00	0
81	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	13-Aug-2023 17:33	Voltage Regulation	14-Aug-2023 09:09	15:36:00	0
82	765kV AJMER - CHITTORGARH Ckt-II	Line	NR	POWERGRID	MO	14-Aug-2023 16:15	Voltage Regulation	15-Aug-2023 09:38	17:23:00	1
83	765kV FATEHPUR - AGRA Ckt-II	Line	NR	POWERGRID	MO	14-Aug-2023 16:25	Voltage Regulation	15-Aug-2023 21:27	29:02:00	0
84	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	14-Aug-2023 17:57	Voltage Regulation	15-Aug-2023 08:50	14:53:00	0
85	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	14-Aug-2023 18:03	Voltage Regulation	15-Aug-2023 06:20	12:17:00	0
86	765kV OBRA C - UNNAO	Line	NR	UPPTCL	SO	15-Aug-2023 05:45	hot point found at Obra-C Unnao line (over the Wave trap) B-phase	15-Aug-2023 11:01	05:16:00	0
87	765kV KOTESHWAR - MEERUT Ckt-II	Line	NR	POWERGRID	SE	15-Aug-2023 10:06	to remove the hanging ropes and clear the preparation from TN-216 to TN-217	15-Aug-2023 12:45	02:39:00	0
88	765kV AJMER - CHITTORGARH Ckt-I	Line	NR	POWERGRID	MO	15-Aug-2023 16:39	Voltage Regulation	16-Aug-2023 09:07	16:28:00	0

NLDC Outage report of Month August 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
89	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	15-Aug-2023 18:12	Voltage Regulation	16-Aug-2023 08:16	14:04:00	0
90	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	15-Aug-2023 18:14	Voltage Regulation	16-Aug-2023 07:46	13:32:00	0
91	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	16-Aug-2023 17:13	Taken out on over voltage	17-Aug-2023 09:46	16:33:00	0
92	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	16-Aug-2023 17:34	Taken out on over voltage	17-Aug-2023 09:07	15:33:00	0
93	765kV PHAGI - BHIWANI Ckt-II	Line	NR	RRVPNL/PG	MO	16-Aug-2023 18:24	Taken out on over voltage	17-Aug-2023 09:38	15:14:00	0
94	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	17-Aug-2023 17:14	Voltage Regulation	18-Aug-2023 08:42	15:28:00	0
95	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	17-Aug-2023 17:24	Voltage Regulation	18-Aug-2023 09:07	15:43:00	0
96	765kV AJMER - CHITTORGARH Ckt-II	Line	NR	POWERGRID	MO	18-Aug-2023 16:48	Voltage Regulation	19-Aug-2023 09:45	16:57:00	1
97	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	18-Aug-2023 17:42	Voltage Regulation	19-Aug-2023 09:07	15:25:00	0
98	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	18-Aug-2023 17:44	Voltage Regulation	19-Aug-2023 09:15	15:31:00	0
99	765kV FATEHPUR - AGRA Ckt-I	Line	NR	POWERGRID	MO	19-Aug-2023 04:04	Voltage Regulation	21-Aug-2023 09:50	53:46:00	0
100	765/220kV 315MVA ICT-II at Lalitpur	ICT	NR	LPCL	SO	19-Aug-2023 04:25	to carry out oil filtration work	19-Aug-2023 20:01	15:36:00	0
101	765kV AJMER - CHITTORGARH Ckt-I	Line	NR	POWERGRID	MO	19-Aug-2023 16:31	Voltage Regulation	20-Aug-2023 10:39	18:08:00	0
102	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	19-Aug-2023 17:39	Voltage Regulation	20-Aug-2023 09:24	15:45:00	0
103	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	19-Aug-2023 19:32	Voltage Regulation	20-Aug-2023 09:15	13:43:00	0
104	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	20-Aug-2023 16:19	Voltage Regulation	21-Aug-2023 08:48	16:29:00	0
105	765kV AJMER - CHITTORGARH Ckt-II	Line	NR	POWERGRID	MO	20-Aug-2023 16:21	Voltage Regulation	21-Aug-2023 09:24	17:03:00	1
106	765kV PHAGI - BHIWANI Ckt-II	Line	NR	RRVPNL/PG	MO	20-Aug-2023 16:40	Voltage Regulation	21-Aug-2023 09:38	16:58:00	0
107	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	20-Aug-2023 17:29	Voltage Regulation	21-Aug-2023 08:57	15:28:00	0
108	765kV AJMER - CHITTORGARH Ckt-I	Line	NR	POWERGRID	MO	21-Aug-2023 16:03	Voltage Regulation	22-Aug-2023 09:38	17:35:00	0
109	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	21-Aug-2023 17:04	Voltage Regulation	22-Aug-2023 08:39	15:35:00	0
110	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	21-Aug-2023 18:28	Voltage Regulation	22-Aug-2023 09:04	14:36:00	0
111	765kV FATEHPUR - AGRA Ckt-II	Line	NR	POWERGRID	MO	22-Aug-2023 07:34	Voltage Regulation	22-Aug-2023 11:10	03:36:00	0
112	765kV AJMER - CHITTORGARH Ckt-II	Line	NR	POWERGRID	MO	22-Aug-2023 17:22	Voltage Regulation	23-Aug-2023 09:28	16:06:00	1
113	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	22-Aug-2023 19:03	Voltage Regulation	23-Aug-2023 08:17	13:14:00	0
114	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	22-Aug-2023 19:25	Voltage Regulation	23-Aug-2023 08:58	13:33:00	0
115	765kV FATEHPUR - AGRA Ckt-I	Line	NR	POWERGRID	MO	23-Aug-2023 03:14	Voltage Regulation	26-Aug-2023 11:19	80:05:00	0
116	765kV ORAI - ALIGARH Ckt-I	Line	NR	POWERGRID	MO	23-Aug-2023 03:30	Voltage Regulation	02-Sep-2023 10:21	246:51:00	0

NLDC Outage report of Month August 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
117	765kV AJMER - CHITTORGARH Ckt-I	Line	NR	POWERGRID	MO	23-Aug-2023 17:24	Voltage Regulation	24-Aug-2023 09:36	16:12:00	0
118	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	23-Aug-2023 17:26	Voltage Regulation	24-Aug-2023 09:06	15:40:00	0
119	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	23-Aug-2023 17:30	Voltage Regulation	24-Aug-2023 08:18	14:48:00	0
120	765kV PHAGI - BHIWANI Ckt-I	Line	NR	RRVPNL/PG	MO	23-Aug-2023 17:51	Voltage Regulation	24-Aug-2023 09:53	16:02:00	0
121	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	24-Aug-2023 17:20	Voltage Regulation	25-Aug-2023 08:19	14:59:00	0
122	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	24-Aug-2023 17:25	Voltage Regulation	25-Aug-2023 08:55	15:30:00	0
123	765kV PHAGI - BHIWANI Ckt-I	Line	NR	RRVPNL/PG	MO	24-Aug-2023 18:01	Voltage Regulation	25-Aug-2023 09:50	15:49:00	0
124	765kV AJMER - CHITTORGARH Ckt-II	Line	NR	POWERGRID	MO	25-Aug-2023 04:07	Voltage Regulation	25-Aug-2023 09:41	05:34:00	1
125	765/400kV 1500MVA ICT-I at Hapur	ICT	NR	UPPTCL	TS	25-Aug-2023 08:41	PRV protection of R phase	25-Aug-2023 11:39	02:58:00	1
126	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	25-Aug-2023 17:10	Voltage Regulation	26-Aug-2023 09:18	16:08:00	0
127	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	25-Aug-2023 17:13	Voltage Regulation	26-Aug-2023 08:30	15:17:00	0
128	765kV AJMER - CHITTORGARH Ckt-II	Line	NR	POWERGRID	MO	25-Aug-2023 21:40	Voltage Regulation	26-Aug-2023 09:39	11:59:00	1
129	765kV AJMER - CHITTORGARH Ckt-I	Line	NR	POWERGRID	MO	26-Aug-2023 17:05	Voltage Regulation	27-Aug-2023 08:28	15:23:00	0
130	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	26-Aug-2023 17:16	Voltage Regulation	27-Aug-2023 09:17	16:01:00	0
131	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	26-Aug-2023 18:24	Voltage Regulation	27-Aug-2023 08:09	13:45:00	0
132	765kV PHAGI - BHIWANI Ckt-I	Line	NR	RRVPNL/PG	MO	26-Aug-2023 18:53	Voltage Regulation	27-Aug-2023 10:23	15:30:00	0
133	765kV AJMER - CHITTORGARH Ckt-I	Line	NR	POWERGRID	MO	27-Aug-2023 16:33	Voltage Regulation	28-Aug-2023 09:28	16:55:00	0
134	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	27-Aug-2023 16:47	Voltage Regulation	28-Aug-2023 09:09	16:22:00	0
135	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	27-Aug-2023 17:52	Voltage Regulation	28-Aug-2023 09:02	15:10:00	0
136	765kV PHAGI - BHIWANI Ckt-II	Line	NR	RRVPNL/PG	MO	27-Aug-2023 18:15	Voltage Regulation	28-Aug-2023 08:30	14:15:00	0
137	765kV AJMER - CHITTORGARH Ckt-II	Line	NR	POWERGRID	MO	28-Aug-2023 16:46	Voltage Regulation	29-Aug-2023 10:15	17:29:00	1
138	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	28-Aug-2023 17:12	Voltage Regulation	29-Aug-2023 09:30	16:18:00	0
139	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	28-Aug-2023 17:37	Voltage Regulation	29-Aug-2023 09:11	15:34:00	0
140	765/400 KV 1500 MVA ICT 1 AT BAREILLY_2(PG)	ICT	NR	POWERGRID	SO	29-Aug-2023 09:59	for AMP work	29-Aug-2023 18:52	08:53:00	0
141	765/400 KV 1500 MVA ICT 1 AT VARANASI(PG)	ICT	NR	POWERGRID	SO	29-Aug-2023 10:27	for AMP and WTI/OTI, Scheme Modification works	29-Aug-2023 20:16	09:49:00	0
142	765kV AJMER - CHITTORGARH Ckt-I	Line	NR	POWERGRID	MO	29-Aug-2023 16:37	Voltage Regulation	30-Aug-2023 09:25	16:48:00	0
143	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	29-Aug-2023 16:55	Voltage Regulation	30-Aug-2023 09:04	16:09:00	0
144	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	29-Aug-2023 17:59	Voltage Regulation	30-Aug-2023 08:50	14:51:00	0

NLDC Outage report of Month August 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
145	765/400 KV 1500 MVA ICT 2 AT BAREILLY_2(PG)	ICT	NR	POWERGRID	SO	30-Aug-2023 09:50	for AMP work.	30-Aug-2023 20:00	10:10:00	0
146	765/400 KV 1000 MVA ICT 3 AT BHIWANI(PG)	ICT	NR	POWERGRID	SO	30-Aug-2023 15:57	for the charging of B-Phase unit and taking out spare unit	31-Aug-2023 01:38	09:41:00	0
147	765KV AJMER - CHITTORGARH Ckt-II	Line	NR	POWERGRID	MO	30-Aug-2023 16:53	Voltage Regulation	31-Aug-2023 08:45	15:52:00	1
148	765kv Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	30-Aug-2023 19:10	Voltage Regulation	31-Aug-2023 08:02	12:52:00	0
149	765KV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	30-Aug-2023 19:44	Voltage Regulation	31-Aug-2023 08:34	12:50:00	0
150	765KV PHAGI - BHIWANI Ckt-I	Line	NR	RRVPNL/PG	MO	30-Aug-2023 19:45	Voltage Regulation	31-Aug-2023 09:40	13:55:00	0
151	765KV AJMER - CHITTORGARH Ckt-I	Line	NR	POWERGRID	MO	31-Aug-2023 16:37	Voltage Regulation	01-Sep-2023 09:17	16:40:00	0
152	765/400KV 1500MVA ICT-III at Jhatikara	ICT	NR	POWERGRID	SE	31-Aug-2023 16:44	Hotspot observed in 400KV Isolator 89T, B phase of 400KV side of the ICT	31-Aug-2023 19:29	02:45:00	0
153	765KV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	31-Aug-2023 17:23	Voltage Regulation	01-Sep-2023 08:24	15:01:00	0
154	765KV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	31-Aug-2023 17:58	Voltage Regulation	01-Sep-2023 08:49	14:51:00	0

Western Region Elements

1	765KV AURANGABAD - SOLAPUR Ckt-II	Line	WR	POWERGRID	MO	01-Aug-2023 00:00	Voltage Regulation	10-Aug-2023 10:02	226:02:00	0
2	765KV DHARAMJAYGARH - JABALPUR PS Ckt-III	Line	WR	POWERGRID	MO	01-Aug-2023 00:00	Voltage Regulation	24-Aug-2023 10:28	562:28:00	0
3	765KV Lakadia -Vadodara Ckt-I	Line	WR	STERLITE	MO	01-Aug-2023 00:00	Voltage Regulation	02-Aug-2023 15:12	39:12:00	0
4	765KV RAIPUR-PS(DURG) - CHAMPA PS Ckt-II	Line	WR	POWERGRID	MO	01-Aug-2023 00:00	Voltage Regulation	10-Aug-2023 10:02	226:02:00	0
5	765KV WARDHA - AURANGABAD Ckt-II	Line	WR	POWERGRID	MO	01-Aug-2023 00:00	Voltage Regulation	24-Aug-2023 07:19	559:19:00	0
6	765KV-JABALPUR-GADARWARA-2	Line	WR	NTPC	SO	02-Aug-2023 09:06	Line CT and CVT testing , Relay testing	02-Aug-2023 20:14	11:08:00	0
7	765KV-JABALPUR-GADARWARA-2 L/R@ GADARWARA - 765KV	Line Reactor	WR	NTPC	SO	02-Aug-2023 09:06	Annual PM and monsoon preparation. Leakage attend from PRV-1	02-Aug-2023 20:14	11:08:00	0
8	765KV/400KV TIRODA-ICT-1	ICT	WR	APML	SO	02-Aug-2023 09:43	Annual Maintenance of Transformer.	03-Aug-2023 20:12	34:29:00	0
9	765/400kv 1500MVA ICT-I at BILASPUR	ICT	WR	POWERGRID	SE	02-Aug-2023 12:36	To attend the hot spot of 177 degree C on 401-89T Rph isolator of 765/400kv ICT#1.	02-Aug-2023 15:21	02:45:00	0
10	765KV/400KV BILASPUR-ICT-2	ICT	WR	POWERGRID WR1	SO	02-Aug-2023 15:57	For spare ICT change over	03-Aug-2023 00:40	08:43:00	0
11	240MVAR LR(S) of 765kv Bina - Jabalpur PS Ckt-III at Jabalpur	Line Reactor	WR	POWERGRID	TS	02-Aug-2023 17:12	Fault details: Jabalpur: 21.66KM/16.6KA Bina: 210.6KM/3.06KA	02-Aug-2023 18:38	01:26:00	1
12	765KV Lakadia -Vadodara Ckt-II	Line	WR	STERLITE	MO	02-Aug-2023 22:01	Voltage Regulation	07-Aug-2023 10:50	108:49:00	0
13	240MVAR LR(S) of 765kv Banaskantha-Lakadia Ckt-I at Banaskantha	Line Reactor	WR	POWERGRID	TS	03-Aug-2023 21:52	Due to CSD malfunction	03-Aug-2023 23:42	01:50:00	1
14	330MVAR 765kv Bus Reactor-I at WARORA	Bus Reactor	WR	PWTL-PG	SO	04-Aug-2023 10:30	FOR SPARE CHANGEOVER WORK	04-Aug-2023 15:54	05:24:00	0
15	765KV-SIPAT-BILASPUR-3	Line	WR	NTPC_SIPAT	SO	07-Aug-2023 09:54	For Testing of Line CT, CVT LA, Isolators, PM of MB's , tightness checking, Alignment checking,Relay testing	09-Aug-2023 19:40	57:46:00	0
16	JABALPUR - 765KV B/R 2	Bus Reactor	WR	POWERGRID	SO	07-Aug-2023 10:04	FOR AMP WORK.	07-Aug-2023 19:26	09:22:00	0
17	765KV/400KV INDORE-ICT-1	ICT	WR	POWERGRID	SO	07-Aug-2023 10:11	FOR ROTATION OF SPARE ICT BEFORE 6 MONTHS. DIA TO BE KEPT OPEN.	07-Aug-2023 15:18	05:07:00	0
18	765KV-RAIPUR-PS (DURG)-RAJNANDGAON-RRWTL-1	Line	WR	RRWTL	SO	07-Aug-2023 11:06	For Equipment Operation Check.	07-Aug-2023 11:46	00:40:00	0

NLDC Outage report of Month August 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
19	765kV DHARAMJAYGARH - CHAMPA PS Ckt-II	Line	WR	POWERGRID	TS	07-Aug-2023 17:52	Due to DT receipt from Dharamjaygarh end	07-Aug-2023 19:59	02:07:00	1
20	765KV-RAIPUR-PS (DURG)-RAINANDGAON-RRWTL-2	Line	WR	RRWTL	SO	08-Aug-2023 10:55	For Equipment Operation Check.	08-Aug-2023 13:09	02:14:00	0
21	765KV/400KV EKTUNI-ICT-1	ICT	WR	MSLDC	SO	08-Aug-2023 16:09	Diagnostic testing	09-Aug-2023 01:19	09:10:00	0
22	RAINANDGAON-RRWTL - 765KV B/R 1	Bus Reactor	WR	RRWTL	SO	09-Aug-2023 10:35	For Equipment Operation Check.	09-Aug-2023 11:00	00:25:00	0
23	765kV Lakadia - Banaskantha Ckt-I	Line	WR	Adani Trans Ind Ltd	MO	10-Aug-2023 02:49	Voltage Regulation	19-Aug-2023 10:47	223:58:00	0
24	765kV AURANGABAD - SOLAPUR Ckt-I	Line	WR	POWERGRID	SE	10-Aug-2023 10:15	to attend Jumper Sub Conductor Cut Rectification at Loc No:253 Yph	10-Aug-2023 22:10	11:55:00	0
25	765KV-RAIPUR-PS (DURG)-CHAMPA-2	Line	WR	POWERGRID WR1	SO	10-Aug-2023 10:37	Line reactor Spare change over at Durg end.CEA clearance is already taken.	10-Aug-2023 16:50	06:13:00	0
26	765KV-RAIPUR-PS (DURG)-CHAMPA-2 L/R@ RAIPUR-PS (DURG)	Line Reactor	WR	POWERGRID WR1	SO	10-Aug-2023 10:37	Line reactor Spare change over at Durg end.	01-Sep-2023 00:00	517:23:00	0
27	765kV RAIPUR-PS(DURG) - CHAMPA PS Ckt-II	Line	WR	POWERGRID	MO	10-Aug-2023 16:50	Voltage Regulation	28-Aug-2023 10:57	426:07:00	0
28	765kV AURANGABAD - SOLAPUR Ckt-I	Line	WR	POWERGRID	MO	10-Aug-2023 22:11	Voltage Regulation	11-Aug-2023 10:15	12:04:00	0
29	765KV/21KV TIRODA-GT-4	ICT	WR	APML	SO	13-Aug-2023 01:40	Annual Maintenance & Testing Transformer. Annual maintenance of main bay and tie bay equipments.	01-Sep-2023 00:00	454:20:00	0
30	765KV/400KV SOLAPUR-ICT-2	ICT	WR	POWERGRID WR1	SO	16-Aug-2023 09:01	765kV ICT#2 AMP Works at 765kV Solapur Substation	16-Aug-2023 19:01	10:00:00	0
31	765KV-BILASPUR-DHARAMJAYGARH-1	Line	WR	POWERGRID WR1	SO	18-Aug-2023 09:07	Line equipments tightness & LR amp works	18-Aug-2023 21:21	12:14:00	0
32	765KV-BILASPUR-DHARAMJAYGARH-1 L/R@ BILASPUR - DHARAMJAYGARH	Line Reactor	WR	POWERGRID WR1	SO	18-Aug-2023 09:07	Line reactor AMP works	18-Aug-2023 21:21	12:14:00	0
33	765KV-BHUJ-II-LAKADIA-1	Line	WR	POWERGRID	SO	18-Aug-2023 12:32	For spare L/R changover with Rph at Bhuj-II end. Due date 21.08.2023.	18-Aug-2023 17:27	04:55:00	0
34	765KV-BHUJ-II-LAKADIA-1 L/R@ BHUJ-II - 765KV	Line Reactor	WR	POWERGRID	SO	18-Aug-2023 12:32	For spare L/R changover with Rph at Bhuj-II end. Due date 21.08.2023	18-Aug-2023 17:27	04:55:00	0
35	765KV/400KV JABALPUR-PS-ICT-1	ICT	WR	POWERGRID	SO	19-Aug-2023 10:22	For TRANSFORMER & TERMINAL EQUIPMENT AMP work & B-phase unit shall also be taken into service (Due date 22.08.2023).	19-Aug-2023 19:20	08:58:00	0
36	765KV Lakadia -Vadodara Ckt-II	Line	WR	STERLITE	MO	19-Aug-2023 21:37	Voltage Regulation	23-Aug-2023 10:46	85:09:00	0
37	765KV-SATNA-VINDHYACHAL(PS)-1	Line	WR	POWERGRID	SO	20-Aug-2023 10:05	For Switching of Y-ph with Spare L/R at Satna end (For taking spare in Service). (Due date 30.08.2023)	20-Aug-2023 16:27	06:22:00	0
38	765KV-SATNA-VINDHYACHAL(PS)-1 L/R@ SATNA - 765KV	Line Reactor	WR	POWERGRID	SO	20-Aug-2023 10:05	For Switching of Y-ph L/R with Spare L/R (For taking spare in Service).(Due date 30.08.2023)	20-Aug-2023 16:27	06:22:00	0
39	765KV-AKOLA (2)-EKTUNI-1	Line	WR	MEGPTCL	SO	20-Aug-2023 16:58	As per grid guideline, Line outage required with Line Reactor for spare reactor changeover at Ektuni SS. Non-switchable Reactor at Ektuni SS Last changeover date-25.07.2022	20-Aug-2023 22:12	05:14:00	0
40	765/400kV 1500 MVA ICT-I at Lakadiya	ICT	WR	Adani Trans Ind Ltd	SO	21-Aug-2023 10:22	Annual maintenace of ICT-1 and bay equipments. ICT-1, R-ph will be taken into service instead of Spare ICT as per CEA Regulations.Last changeover date 14-03-2023.	21-Aug-2023 22:29	12:07:00	0
41	765KV-JABALPUR-GADARWARA-1	Line	WR	POWERGRID	SO	21-Aug-2023 11:10	FOR AMP WORK OF LINE TERMINAL EQUIPMENT AND LINE AMP WORKS.	21-Aug-2023 19:59	08:49:00	0
42	765KV/400KV BINA-ICT-2	ICT	WR	POWERGRID	SO	21-Aug-2023 11:11	For taking Y-ph ICT-2 unit in service in place of Spare ICT unit.Last date of spare changeover is 24.02.2023.	21-Aug-2023 17:24	06:13:00	0
43	240 MVAR LR ON 765 kV AKOLA (2)-KORADI-III-II @ KORADI-III	Line Reactor	WR		TS	21-Aug-2023 11:45	To differential protection operated at Koradi- III SS	21-Aug-2023 18:10	06:25:00	1
44	765KV-SEONI-WARDHA-2	Line	WR	POWERGRID WR1	SO	22-Aug-2023 09:19	for taking out spare reactor unit at Seoni end.,Please note Spare Reactor unit is in service in place of Rph unit at Seoni end in aforesaid line since 4th May 2023	22-Aug-2023 22:12	12:53:00	0
45	WARDHA - 765KV B/R 1	Bus Reactor	WR	POWERGRID WR1	SO	23-Aug-2023 09:40	For taking Spare into Service	23-Aug-2023 20:45	11:05:00	0
46	WARORA-PG - 765KV B/R 1	Bus Reactor	WR	POWERGRID WR1	SO	23-Aug-2023 11:12	FOR SPARE CHANGEOVER WORK	23-Aug-2023 17:20	06:08:00	0
47	765KV Lakadia -Vadodara Ckt-I	Line	WR	STERLITE	MO	23-Aug-2023 20:18	Voltage Regulation	26-Aug-2023 18:41	70:23:00	0

NLDC Outage report of Month August 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
48	765KV DHARAMJAYGARH - JABALPUR PS Ckt-III	Line	WR	POWERGRID	TS	24-Aug-2023 10:28	R-Phase LA failed at JABALPUR(Pooling) while charing	26-Aug-2023 11:00	48:32:00	1
49	330MVAR L/R of Lakhdiya-1 at 765KV Vadodara S/S	Line Reactor	WR	POWERGRID WR	TS	24-Aug-2023 15:38	Differential protection operated	26-Aug-2023 18:41	51:03:00	1
50	330MVAR L/R of Lakhdiya-1 at 765KV Vadodara S/S	Line Reactor	WR	POWERGRID WR	TS	24-Aug-2023 15:43	Differential protection operated	24-Aug-2023 20:17	04:34:00	2
51	765kv WARDHA - AURANGABAD Ckt-IV	Line	WR	POWERGRID	MO	24-Aug-2023 22:55	Voltage Regulation	01-Sep-2023 00:00	169:05:00	0
52	765KV-SEONI-WARDHA-1	Line	WR	POWERGRID WR1	SO	25-Aug-2023 10:18	Line Bay AMP works.	25-Aug-2023 21:06	10:48:00	0
53	765KV DHARAMJAYGARH - JABALPUR PS Ckt-III	Line	WR	POWERGRID	TV	26-Aug-2023 11:00	tripped on O/V	28-Aug-2023 09:54	46:54:00	2
54	765KV Lakadia -Vadodara Ckt-II	Line	WR	STERLITE	MO	26-Aug-2023 22:17	Voltage Regulation	28-Aug-2023 12:11	37:54:00	0
55	765/440kV 1500MVA ICT-III at WARDHA	ICT	WR	POWERGRID	SO	28-Aug-2023 10:48	For Taking Spare out of service	28-Aug-2023 19:14	08:26:00	0
56	765KV-RAIGARH-PS-CHAMPA-1	Line	WR	POWERGRID WR1	SO	28-Aug-2023 11:41	For AMP of LTE at Champa end. Dia to be kept open. AR in non auto mode of 765KV-RAIGARH-PS-CHAMPA-2	29-Aug-2023 22:49	35:08:00	0
57	765KV Lakadia -Vadodara Ckt-I	Line	WR	STERLITE	MO	29-Aug-2023 00:45	Voltage Regulation	29-Aug-2023 10:59	10:14:00	0
58	765KV/400KV SATNA-ICT-1	ICT	WR	POWERGRID	SO	29-Aug-2023 09:27	For Busbar and LBB Testing of Main Bay 403. Simultaneous outage of 400KV Bus # 2, 765/400KV ICT # 1 and 400KV Satna-JP Nigrie #1 is required and Dia to be kept open at both ends/sides.	29-Aug-2023 21:42	12:15:00	0
59	CHAMPA - 765KV B/R 1	Bus Reactor	WR	POWERGRID WR1	SO	29-Aug-2023 09:49	For AMP works.	29-Aug-2023 20:01	10:12:00	0
60	765KV-JABALPUR-GADARWARA-2	Line	WR	POWERGRID	SO	29-Aug-2023 10:07	FOR AMP WORK OF LINE TERMINAL EQUIPMENT AND LINE AMP WORKS.	29-Aug-2023 19:47	09:40:00	0
61	765KV Lakadia -Vadodara Ckt-II	Line	WR	STERLITE	MO	30-Aug-2023 01:31	Voltage Regulation	31-Aug-2023 10:40	33:09:00	0
62	765KV/400KV WARDHA-ICT-1	ICT	WR	POWERGRID WR1	SO	30-Aug-2023 10:23	For Transformer Amp works	31-Aug-2023 20:43	34:20:00	0

Eastern Region Elements

1	765 kV ANGUL - JHARSUGUDA Ckt-IV	Line	ER	POWERGRID	MO	01-Aug-2023 00:00	Taken out on over voltage.	09-Aug-2023 12:59	204:59:00	0
2	HVDC PUSAULI BACK TO BACK	HVDC	ER		TS	01-Aug-2023 00:00	Tripped on loss of Minimum filter(CWC-13& CWC-14 filter banks got tripped due to bird strike in North side Filter Bank).Tripped on 19:10 Hrs (31.07.23).	13-Aug-2023 03:04	291:04:00	1
3	765kv NEW RANCHI - MEDINIPUR Ckt-II	Line	ER	POWERGRID/P MJTL	TL	01-Aug-2023 00:01	New ranchi-Z1 Y-N FC-8.84kA FD-34.83km Medinipur- Z1 Y-N FC-3.47kA FD-174.1km	01-Aug-2023 16:15	16:14:00	1
4	330MVAR 765KV B/R-2 AT MEDINIPUR	Bus Reactor	ER	ER-II	SO	10-Aug-2023 08:07	PRV Modification	10-Aug-2023 14:28	06:21:00	0
5	765 kV ANGUL - JHARSUGUDA Ckt-III	Line	ER	POWERGRID	MO	10-Aug-2023 22:22	Voltage Regulation	31-Aug-2023 09:13	490:51:00	0
6	330MVAR 765KV B/R-1 AT MEDINIPUR	Bus Reactor	ER	ER-II	SO	11-Aug-2023 08:26	PRV Modification	11-Aug-2023 13:09	04:43:00	0
7	765KV/400KV 1500 MVA ICT 2 AT ANGUL	ICT	ER	PG (ODISHA PROJECT)	SO	14-Aug-2023 10:49	Spare rotation	14-Aug-2023 17:51	07:02:00	0
8	765KV/400KV 1500 MVA ICT 2 AT MEDINIPUR	ICT	ER	ER-II	SO	18-Aug-2023 09:02	PRV MODIFICATION	18-Aug-2023 19:58	10:56:00	0
9	765KV/400KV 1500 MVA ICT 1 AT NEW JEERAT	ICT	ER	ER-II	SO	19-Aug-2023 10:27	Goose file upgradation work (BCU) for interlock rectification of Isolator and Earth switch	19-Aug-2023 16:47	06:20:00	0
10	240MVAR SWITCHABLE L/R OF 765KV-MEDINIPUR-NEW	Line Reactor	ER	ER-II	SO	21-Aug-2023 10:45	6 MONTHS CHANGE OVER OF LINE REACTOR SPARE PHASE	21-Aug-2023 19:43	08:58:00	0
11	765KV-MEDINIPUR-NEW JEERAT-2	Line	ER	ER-II	SO	21-Aug-2023 10:45	6 MONTHS CHANGE OVER OF LINE REACTOR SPARE PHASE	21-Aug-2023 19:43	08:58:00	0
12	240MVAR 765KV B/R-2 AT JHARSUGUDA	Bus Reactor	ER	PG (ODISHA PROJECT)	SO	22-Aug-2023 09:21	Protection scheme modification work	22-Aug-2023 17:31	08:10:00	0
13	330MVAR 765KV B/R-2 AT NEW JEERAT	Bus Reactor	ER	ER-II	SO	25-Aug-2023 09:40	WTI & OTI MODIFICATION	25-Aug-2023 18:16	08:36:00	0

NLDC Outage report of Month August 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
14	765KV/400KV 1500 MVA ICT 1 AT MEDINIPUR	ICT	ER	ER-II	SO	25-Aug-2023 09:44	PRV MODIFICATION	25-Aug-2023 16:10	06:26:00	0
15	765KV-MEDINIPUR-NEW JEERAT-1	Line	ER	ER-II	SO	26-Aug-2023 09:36	REPLACEMENT OF DEFECTIVE INSULATOR DUE TO LIGHTENING	26-Aug-2023 19:31	09:55:00	0
16	765KV-ANGUL-JHARSUGUDA-3	Line	ER	PG (ODISHA PROJECT)	SO	31-Aug-2023 09:13	Maintenance and Protection scheme modification work	31-Aug-2023 19:29	10:16:00	0
17	400KV-RANCHI-SIPAT-2	Line	ER	ER-I	SO	31-Aug-2023 09:19	CT REPLACEMENT WORKS	01-Sep-2023 21:45	36:26:00	0
18	240MVAR NON-SWITCHABLE L/R OF 765KV-ANGUL-JHA	Line Reactor	ER	PG (ODISHA PROJECT)	SO	31-Aug-2023 09:28	maintenance and protection scheme modification work	31-Aug-2023 19:29	10:01:00	0
19	240MVAR SWITCHABLE L/R OF 765KV-ANGUL-JHARSUG	Line Reactor	ER	PG (ODISHA PROJECT)	SO	31-Aug-2023 09:29	maintenance and protection scheme modification work	31-Aug-2023 19:29	10:00:00	0
20	765 kV ANGUL - JHARSUGUDA Ckt-IV	Line	ER	POWERGRID	MO	31-Aug-2023 19:44	Voltage Regulation	01-Sep-2023 00:00	04:16:00	0
Southern Region Elements										
1	765 kV-KURNOOL_(PG)-MAHESHWARAM_PG-I	Line	SR	POWERGRID SR	TL	01-Aug-2023 00:00	Tripped on R-N Fault at 11:04Hrs (29.07.23) during charging, damaged insulator along with fittings.	03-Aug-2023 17:13	65:13:00	1
2	765kv CUDDAPAH - THIRUVALAM Ckt-II	Line	SR	POWERGRID	MO	01-Aug-2023 00:00	Voltage Regulation	03-Aug-2023 08:08	56:08:00	0
3	765kv KURNOOL - CUDDAPAH Ckt-II	Line	SR	POWERGRID	MO	01-Aug-2023 00:00	Voltage Regulation	08-Aug-2023 09:58	177:58:00	0
4	765KV NIZAMABAD - MAHESHWARAM Ckt-II	Line	SR	POWERGRID	MO	01-Aug-2023 00:00	taken out on over voltage	03-Aug-2023 08:44	56:44:00	0
5	765KV VEMAGIRI - CHILAKALURIPETA Ckt-I	Line	SR	POWERGRID	MO	01-Aug-2023 00:00	Voltage Regulation	02-Aug-2023 11:06	35:06:00	0
6	765KV KURNOOL - CUDDAPAH Ckt-II	Line	SR	POWERGRID	MO	08-Aug-2023 20:00	line kept after tripping on over voltage.	16-Aug-2023 10:01	182:01:00	0
7	765kv CHILAKALURIPETA - CUDDAPAH Ckt-I	Line	SR	POWERGRID	SE	02-Aug-2023 11:15	SF6 leakage noise observed in C'peta Line-1 Line isolator(71589L) Module	02-Aug-2023 20:14	08:59:00	0
8	765KV CHILAKALURIPETA - CUDDAPAH Ckt-I	Line	SR	POWERGRID	MO	02-Aug-2023 20:14	Voltage Regulation	03-Aug-2023 08:19	12:05:00	0
9	765KV VEMAGIRI - CHILAKALURIPETA Ckt-II	Line	SR	POWERGRID	MO	03-Aug-2023 13:34	Voltage Regulation	09-Aug-2023 17:06	147:32:00	0
10	765KV NIZAMABAD - MAHESHWARAM Ckt-II	Line	SR	POWERGRID	MO	04-Aug-2023 16:23	Voltage Regulation	09-Aug-2023 14:37	118:14:00	0
11	765/400 KV ICT-1 at Warangal	ICT	SR	Adani Trans Ind Ltd	TS	08-Aug-2023 15:47	Due to power supply failure to ICT	09-Aug-2023 22:24	30:37:00	1
12	765KV KURNOOL - CUDDAPAH Ckt-II	Line	SR	POWERGRID	TV	08-Aug-2023 19:54	Tripped on O/V.	08-Aug-2023 20:00	00:06:00	1
13	+/- 320KV PUGALUR - THRISSUR Pole-I	HVDC	SR	POWERGRID	SO	08-Aug-2023 22:08	CWC PLC fault (trip by equipments) at Thrissur HVDC station	09-Aug-2023 23:10	25:02:00	0
14	765/400 KV ICT-2 at warangal	ICT	SR	Adani Trans Ind Ltd	TS	09-Aug-2023 11:32	Tripped on Transformer differential protection	09-Aug-2023 22:00	10:28:00	1
15	765KV CHILAKALURIPETA - CUDDAPAH Ckt-II	Line	SR	POWERGRID	MO	09-Aug-2023 18:31	Voltage Regulation	01-Sep-2023 00:00	533:29:00	0
16	765 kV-KURNOOL_(PG)-MAHESHWARAM_PG-II	Line	SR	POWERGRID	MO	09-Aug-2023 21:10	Voltage Regulation	25-Aug-2023 08:35	371:25:00	0
17	765KV NIZAMABAD - MAHESHWARAM Ckt-I	Line	SR	POWERGRID	MO	10-Aug-2023 19:58	Voltage Regulation	16-Aug-2023 10:17	134:19:00	0
18	765KV VEMAGIRI - CHILAKALURIPETA Ckt-I	Line	SR	POWERGRID	MO	12-Aug-2023 20:00	Voltage Regulation	16-Aug-2023 09:39	85:39:00	0
19	765KV NIZAMABAD - MAHESHWARAM Ckt-II	Line	SR	POWERGRID	MO	17-Aug-2023 18:36	Voltage Regulation	25-Aug-2023 12:25	185:49:00	0
20	765KV/400KV NPS-ICT-3	ICT	SR	pgsr1_sd	SO	18-Aug-2023 08:12	AMP Works	18-Aug-2023 20:05	11:53:00	0
21	765 kV-KURNOOL_(PG)-NPS-II	Line	SR	POWERGRID	SE	22-Aug-2023 12:16	Hotsport observed in R-ph reactor isolator at kurnool ss	22-Aug-2023 16:15	03:59:00	0

NLDC Outage report of Month August 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
22	765KV-KURNOOL_PG-RAICHUR_PG-2	Line	SR	pgsr1_sd	SO	25-Aug-2023 09:04	AMP Works	25-Aug-2023 19:23	10:19:00	0
23	765/400 KV ICT-2 at warangal	ICT	SR	POWERGRID SR	SE	25-Aug-2023 12:42	hotspot in isolator	25-Aug-2023 14:59	02:17:00	1
24	765KV NIZAMABAD - MAHESHWARAM Ckt-I	Line	SR	POWERGRID	MO	25-Aug-2023 17:06	Voltage Regulation	29-Aug-2023 09:15	88:09:00	0
25	765 KV-KURNOOL_(PG)-MAHESHWARAM_PG-I	Line	SR	POWERGRID SR	MO	26-Aug-2023 18:19	Voltage Regulation	29-Aug-2023 09:25	63:06:00	1
26	765kV VEMAGIRI - CHILAKALURIPETA Ckt-II	Line	SR	POWERGRID	TS	28-Aug-2023 11:47	DT receipt at Vemagiri end	28-Aug-2023 12:23	00:36:00	1
27	240MVAR LR(S) of 765kV Ariyalur Ckt-I at Thiruvalam	Line Reactor	SR	TN/POWERGRID	SO	28-Aug-2023 13:51	for carry out the cable termination from DTPC, PLCC to Relay panel	01-Sep-2023 00:00	82:09:00	0
28	765kV NIZAMABAD - MAHESHWARAM Ckt-II	Line	SR	POWERGRID	MO	29-Aug-2023 18:41	Voltage Regulation	12-Sep-2023 11:49	329:08:00	0
29	765 KV-KURNOOL_(PG)-MAHESHWARAM_PG-II	Line	SR	POWERGRID SR	MO	29-Aug-2023 22:07	Voltage Regulation	02-Sep-2023 11:27	85:20:00	0

North Eastern Region Elements

Nil

	TL= Tripping due to Line Fault
	TS= Tripping due to S/S Fault
	MO= Opened due to system constraints
	TV= Tripped on Overvoltage
	SC= Planned Shutdown for construction activities
	SO= Planned Shutdown for O&M activities
	SE= Emergency Shutdown
	TP= Protection Maloperation
	ME= Miscellaneous outage

24. ALL TIME HIGHEST

31-08-2023

	Maximum Demand Met during the day (MW)	Demand Met during Evening Peak hrs(MW)	Energy Met (MU)	Hydro Gen. (MU)	Wind Gen. (MU)	Solar Gen. (MU)
NR	81097 18-08-2023 @14:41	76072 23-06-2023	1777 18-08-2023	443 01-08-2023	86 07-08-2023	147 10-05-2023
WR	71708 31-08-2023 @11:03	64447 29-08-2023	1539 18-04-2023	167 18-12-2014	273 07-08-2023	70.69 12-05-2023
SR	64314 15-03-2023	52366 18-04-2023	1329 19-04-2023	208 31-08-2018	298 21-07-2023	142.7 21-03-2023
ER	29641 28-07-2023	28579 18-04-2023	639 08-06-2023	157 14-09-2022	-	7 23-03-2023
NER	3603 17-08-2022	3510 12-08-2022	70 01-08-2023	41 29-08-2023	-	2 22-06-2022
All India	236598 31-08-2023 @12:11	215592 28-08-2023	5125 31-08-2023	877 30-08-2022	611 02-08-2023	351 10-05-2023
Regions	States	Max. Demand Met during the day (MW)		Energy Consumption (MU)		
			As on date		As on date	
NR	Punjab	15237	23-06-2023	343.5	24-06-2023	
	Haryana	12692	18-08-2023 @14:00	273.1	18-08-2023	
	Rajasthan	17148	18-08-2023 @14:00	351.8	18-08-2023	
	Delhi	7770	29-06-2022	153.5	28-06-2022	
	UP	28553	25-07-2023	577.5	24-07-2023	
	Uttarakhand	2594	14-06-2022	55.8	17-06-2023	
	HP	2071	06-01-2023	40.7	22-08-2023	
	J&K(UT) and Ladakh(UT)	3636	29-06-2023	65.4	20-01-2023	
	Chandigarh	426	08-07-2021	8.4	08-07-2021	
Railways NR ISTS		-	-	-	-	
WR	Chhattisgarh	5827	28-08-2023 @23:00	133.5	28-08-2023	
	Gujarat	22972	31-08-2023 @14:00	470.5	29-08-2023	
	MP	17238	13-01-2023	329.3	10-01-2023	
	Maharashtra	28846	14-04-2022	636.1	21-06-2023	
	Goa	776	07-06-2023	17.1	08-06-2023	
	DD & DNH	1327	17-08-2023 @16:00	30.9	10-08-2023	
	AMNSIL	977	18-08-2021	21.0	31-05-2022	
Balco	-	-	-	-		
SR	Andhra Pradesh*	12900	17-06-2023	263.8	16-06-2023	
	Telangana*	15497	30-03-2023	303.4	03-03-2023	
	Karnataka	16950	25-08-2023 @11:00	309.5	20-04-2023	
	Kerala	5024	18-04-2023	103.3	19-04-2023	
	Tamil Nadu	19387	20-04-2023	415.4	20-04-2023	
	Pondy	512	17-05-2023	11.6	18-05-2023	
ER	Bihar	7578	27-07-2023	161.3	28-07-2023	
	DVC	3751	18-04-2023	81.2	22-04-2022	
	Jharkhand	1923	16-06-2023	43.3	17-06-2023	
	Odisha	7192	19-04-2023	145.5	25-09-2022	
	West Bengal	11868	18-04-2023	245.7	18-04-2023	
	Sikkim	137	03-02-2022	2.5	28-01-2020	
	Railways ER ISTS	-	-	-	-	
NER	Arunachal Pradesh	172	31-05-2023	3.1	18-08-2023	
	Assam	2413	31-07-2023	48.1	01-08-2023	
	Manipur	258	31-01-2022	3.7	10-02-2022	
	Meghalaya	415	09-02-2022	7.8	31-01-2022	
	Mizoram	157	16-01-2023	2.3	18-01-2023	
	Nagaland	178	11-08-2023 @16:14	3.14	29-07-2023	
	Tripura	370	07-06-2023	7.0	06-06-2023	
*SR	Andhra Pradesh (Undivided)	13162	23-03-2014	284.8	22-03-2014	

25.System Reliability Indices Report for the month of August 2023

Percentage (%) of times ATC was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	9	2.25	0.30
2	ER-NR	0	0.00	0.00
3	Import of NR	0	0.00	0.00
4	NEW-SR	5	1.25	0.17
5	NER Import	0	0.00	0.00

Percentage(%) of times (N-1) Criteria was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	0	0.00	0.00
2	ER-NR	0	0.00	0.00
3	Import of NR	0	0.00	0.00
4	NEW-SR	1	0.25	0.03
4	NER Import	0	0.00	0.00

Remarks: Flows crossing Total Transfer Capability (TTC) on interregional corridors has been worked out as a proxy for (N-1) violation.



POWER SYSTEM OPERATION CORPORATION LIMITED

पावर सिस्टम ऑपरेशन कारपोरेशन लिमिटेड

NATIONAL LOAD DESPATCH CENTRE – राष्ट्रीय भार प्रेषण केन्द्र

First floor, B-9, Qutab Institutional Area,
Katwaria Sarai, New Delhi-110016.
