



ग्रीड कंट्रोलर ऑफ इंडिया लिमिटेड
(भारत सरकार का उद्यम)
GRID CONTROLLER OF INDIA LIMITED
(A Government of India Enterprise)



[formerly Power System Operation Corporation Limited (POSOCO)]
राष्ट्रीय भार प्रेषण केन्द्र / **National Load Despatch Centre**

कार्यालय : बी-9, प्रथम एवं द्वितीय तल, कुतुब इंस्टीट्यूशनल एरिया, कटवारिया सराय, नई दिल्ली - 110016
Office : 1st and 2nd Floor, B-9, Qutab Institutional Area, Katwaria Sarai, New Delhi -110016
CIN : U40105DL2009GOI188682, Website : www.grid-india.in, E-mail : gridindiacc@grid-india.in, Tel.: 011- 42785855

संदर्भ संख्या: - GRID-INDIA/NLDC/MR/

दिनांक: 26.03.2024

सेवा में,

वितरण सूची के अनुसार

विषय:- निष्पादन रिपोर्ट – फ़रवरी 2024

महोदय,

आई०ई०जी०सी०-2010 के प्रावधान के अनुसार, फ़रवरी 2024 माह की अखिल भारतीय प्रणाली की निष्पादन रिपोर्ट संलग्न है।

धन्यवाद

भवदीय

(सुरजीत बनर्जी)

मुख्य महाप्रबन्धक (प्रणाली प्रचालन)

(रा०भा०प्रे०के०)

संलग्नक: मासिक प्रणाली रिपोर्ट

वितरण सूची Distribution List

- 1 सचिव, के.वि.नि.आ. तीसरा एवं चौथा तल, चंद्रलोक भवन, 36, जनपथ, नई दिल्ली-110001
Secretary, CERC, 3rd & 4th Floor, Chanderlok Building, 36, Janpath, New Delhi-110001
- 2 मुख्य अभियंता (जी एम), के.वि.प्रा., सेवा भवन, आर. के. पुरम, नई दिल्ली-110066
Chief Engineer (GM), CEA, Sewa Bhavan, R.K.Puram, New Delhi-110066
- 3 सदस्य सचिव, उ. क्षेत्र. वि. स., 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली - 110016
Member Secretary, NRPC, 18/A, SJSS Marg, Katwaria Sarai, New Delhi-110016
- 4 सदस्य सचिव, प. क्षेत्र. वि. स., एफ-3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई - 400093
Member Secretary, WRPC, F-3, MIDC Area, Andheri (East), Mumbai-400093
- 5 सदस्य सचिव, द. क्षेत्र. वि. स., 29, रेस कोर्स क्रॉस रोड, बंगलूरु - 560009
Member Secretary, SRPC, 29, Race Course Cross Road, Bangalore-560009
- 6 सदस्य सचिव, पू. क्षेत्र. वि. स., 14, गोल्फ क्लब रोड, कोलकाता - 700033
Member Secretary, ERPC, 14, Golf Club Road, Kolkata-700033
- 7 सदस्य सचिव, उ. पू. क्षेत्र. वि. स., मेघालय राज्य आवासीय वित्त सहकारी समिति लिमिटेड भवन, नॉग्रिम हिल्स, शिलोंग - 793003
Member Secretary, NERPC, Meghalaya State Housing Finance Cooperative Society Ltd. Building, Nongrim Hills, Shillong -793003
- 8 मुख्य अभियंता, राष्ट्रीय विद्युत समिति, एनआरपीसी भवन, तृतीय तल, 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली - 110016
Chief Engineer, National Power Committee, NRPC Building, 3rd floor, 18/A, SJSS Marg, Katwaria Sarai, New Delhi-110016
- 9 कार्यपालक निदेशक, पू. क्षेत्र. भा. प्रे. के., 14, गोल्फ क्लब रोड, कोलकाता - 700033
Executive Director, ERLDC, 14, Golf Club Road, Kolkata-700033
- 10 कार्यपालक निदेशक, प. क्षेत्र. भा. प्रे. के., एफ-3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई - 400093
Executive Director, WRLDC, F-3, MIDC Area, Andheri (East), Mumbai-400093
- 11 कार्यपालक निदेशक, उ. क्षेत्र. भा. प्रे. के., 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली - 110016
Executive Director, NRLDC, 18/A, SJSS Marg, Katwaria Sarai, New Delhi-110016
- 12 कार्यपालक निदेशक, द. क्षेत्र. भा. प्रे. के., 29, रेस कोर्स क्रॉस रोड, बंगलूरु - 560009
Executive Director, SRLDC, 29, Race Course Cross Road, Bangalore-560009
- 13 मुख्य महाप्रबंधक, पू. क्षेत्र. भा. प्रे. के., डोंगतिह, लोअर नॉग्रह, लापलंग, शिलोंग- 793006
Chief General Manager, NERLDC, Dongtiah, Lower Nongrah, Laplang, Shillong-793006



ग्रिड-इंडिया
GRID-INDIA

GRID CONTROLLER OF INDIA LIMITED

Formerly Power System Operation Corporation Limited

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड

NATIONAL LOAD DESPATCH CENTRE –राष्ट्रीय भार प्रेषण केन्द्र

मासिक ऑपरेशन रिपोर्ट

Monthly
Operation Report



फरवरी 2024

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड
राष्ट्रीय भार प्रेषण केंद्र, नई दिल्ली

GRID CONTROLLER OF INDIA LIMITED

Formerly Power System Operation Corporation Limited

NATIONAL LOAD DESPATCH CENTRE, NEW DELHI



ग्रिड-इंडिया
GRID-INDIA

माह फ़रवरी 2024 के लिए प्रचालन निष्पादन रिपोर्ट
OPERATIONAL PERFORMANCE REPORT FOR THE
MONTH OF FEBRUARY-2024


पृष्ठसूची CONTENTS

1	माह फरवरी 2024 की सारांश रिपोर्ट Summary of report for the month of FEBRUARY 2024	1-5
2	क्षेत्रवार स्थापित विद्युत क्षमता Region wise Installed Capacity	6
3	राष्ट्रीय स्तर पर सांध्यकालीन शिखर मांगपूर्ति Peak demand met at National level	7-8
4	राष्ट्रीय स्तर पर विद्युत ऊर्जा खपत Energy consumption at National level	9-10
5	फ्रिक्वेंसी रूपरेखा Frequency profile	11-12
6	राष्ट्रीय स्तर पर जल विद्युत ऊर्जा उत्पादन Hydro generation at National level	13-14
7	राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन Wind generation at National level	15
8	राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन Solar generation at National level	16
9	राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग पूर्ति Daily maximum demand met at National level	17
10	23 फरवरी के माँग एवं उत्पादन प्लॉट(अधिकतम मांग पूर्ति)व माँग का डाटा (15 मिनट अंतराल) Demand and generation plots for 23-FEBRUARY (Max Demand Met) and Demand data (15-minute interval)	18-22
11	ऊर्जा आपूर्ति की वास्तविक स्थिति Actual power supply position	23
12	ऊर्जा आवश्यकता एवं आपूर्ति की पिछले वर्ष माह फरवरी 2023 से तुलना Energy requirement and met comparison with FEBRUARY 2023	24
13	शिखर मांग आवश्यकता एवं आपूर्ति की पिछले वर्ष माह फरवरी 2023 से तुलना Peak demand requirement and met comparison with FEBRUARY 2023	25


14	क्षेत्रीय स्तर पर शिड्यूल एवं ड्रावल Schedule & drawal at regional level	26
15	अंतर क्षेत्रीय विनिमय Inter-regional exchanges	27-36
16	अंतर राष्ट्रीय विद्युत विनिमय Inter-national exchanges	37-39
17	एसटीओए (द्विपक्षीय एवं सामूहिक) एवं यू आइ का ब्यौरा Bilateral and collective short-term open access & UI details	40
18	पावर मार्केट की सूचना Power market information	41-47
19	अक्षय ऊर्जा प्रमाण पत्र प्रक्रिया Renewable energy certificate mechanism	48-50
20	मुख्य घटनाएँ एवं डिस्टर्बेंस Important events/disturbances	51-57
21	नए कमीशंड पारेषण तत्व New elements commissioned	58
22	विभव रूपरेखा Voltage profile	59
23	अब तक उच्चतम (मांग व ऊर्जा) आँकड़े : माह फरवरी 2024 तक All Time Highest (Demand & Energy) figures: Till FEBRUARY 2024	60
24	फरवरी 2024 के लिए सिस्टम रिलाइबिलिटी सूचकांक System Reliability Indices for FEBRUARY 2024	61

1. SUMMARY OF REPORT FOR THE MONTH OF FEBRUARY-2024


EVENING PEAK HOUR (at 1900hrs) DEMAND MET AT NATIONAL LEVEL (MW)

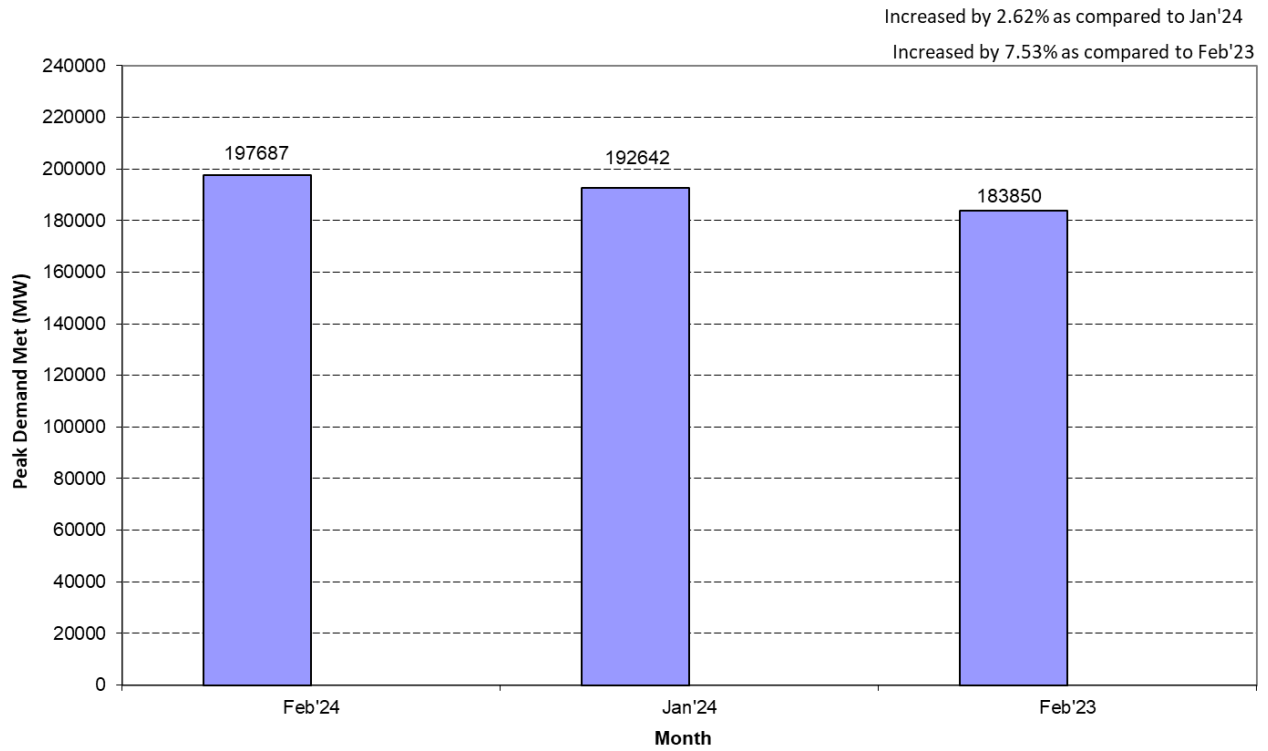


Frequency within IEGC Band

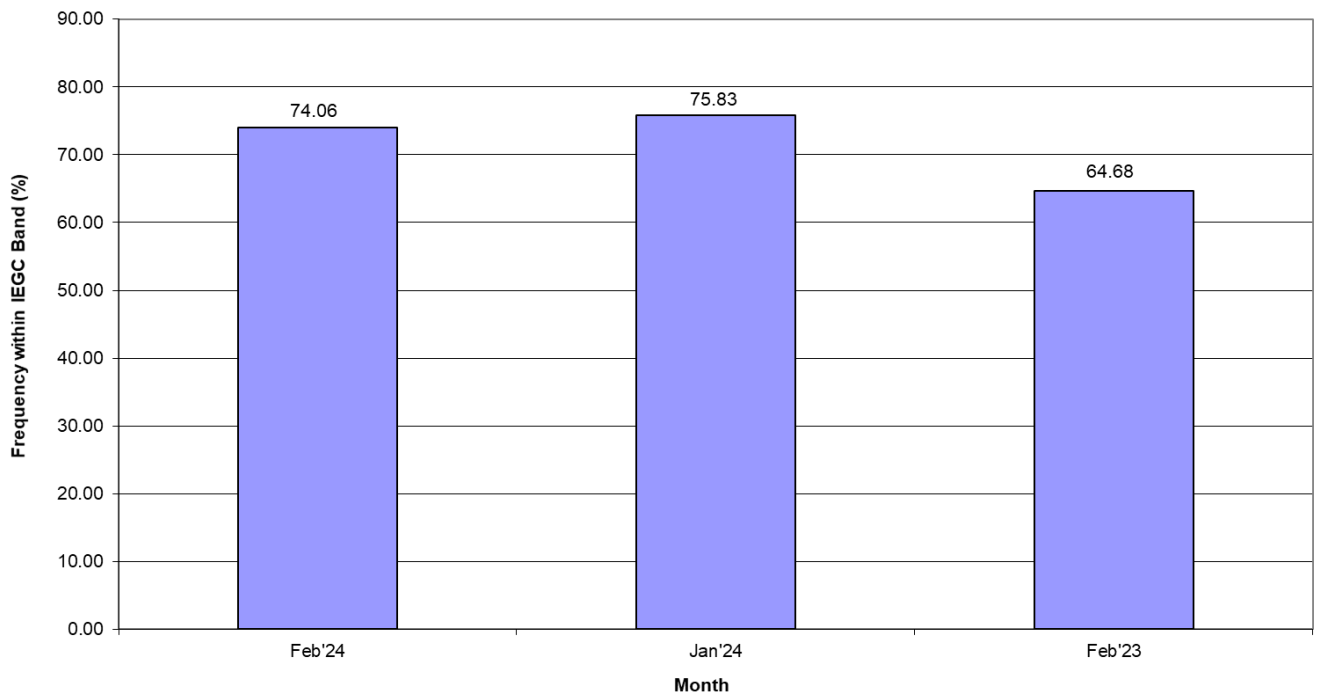


ENERGY MET AT NATIONAL LEVEL (MU)

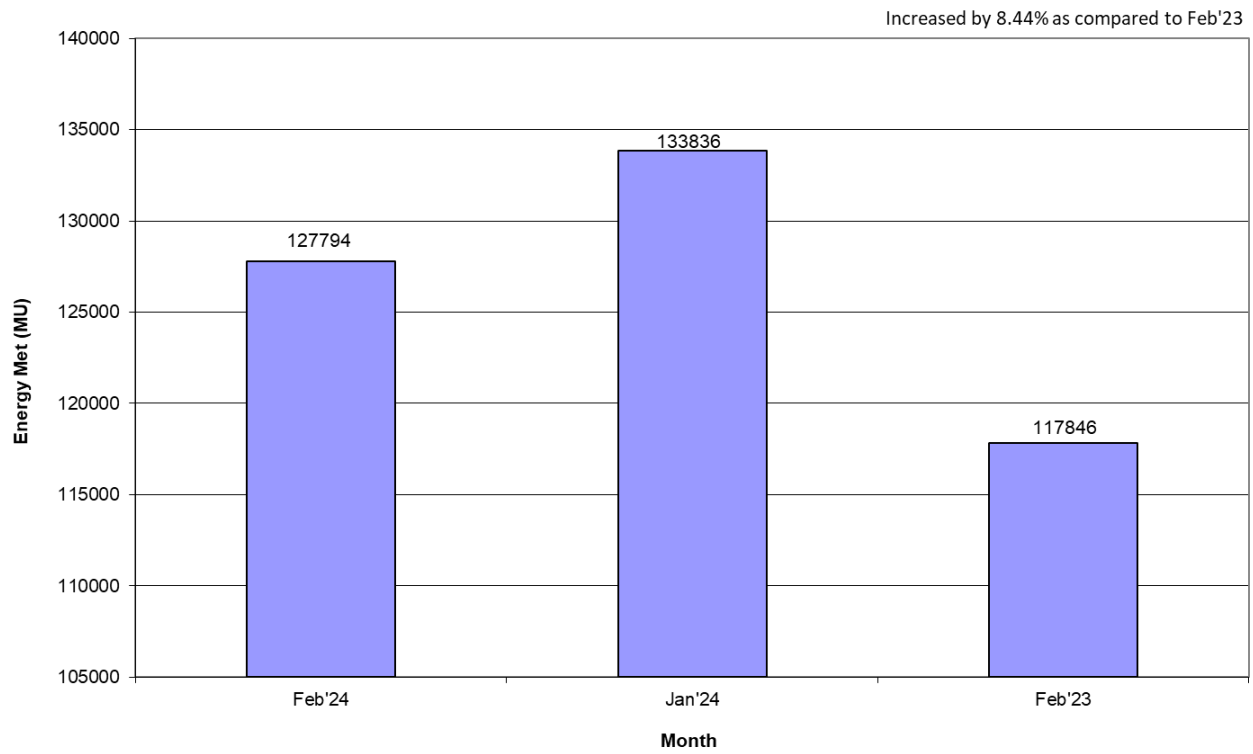


AVERAGE ENERGY MET AT NATIONAL LEVEL (MU/Day)

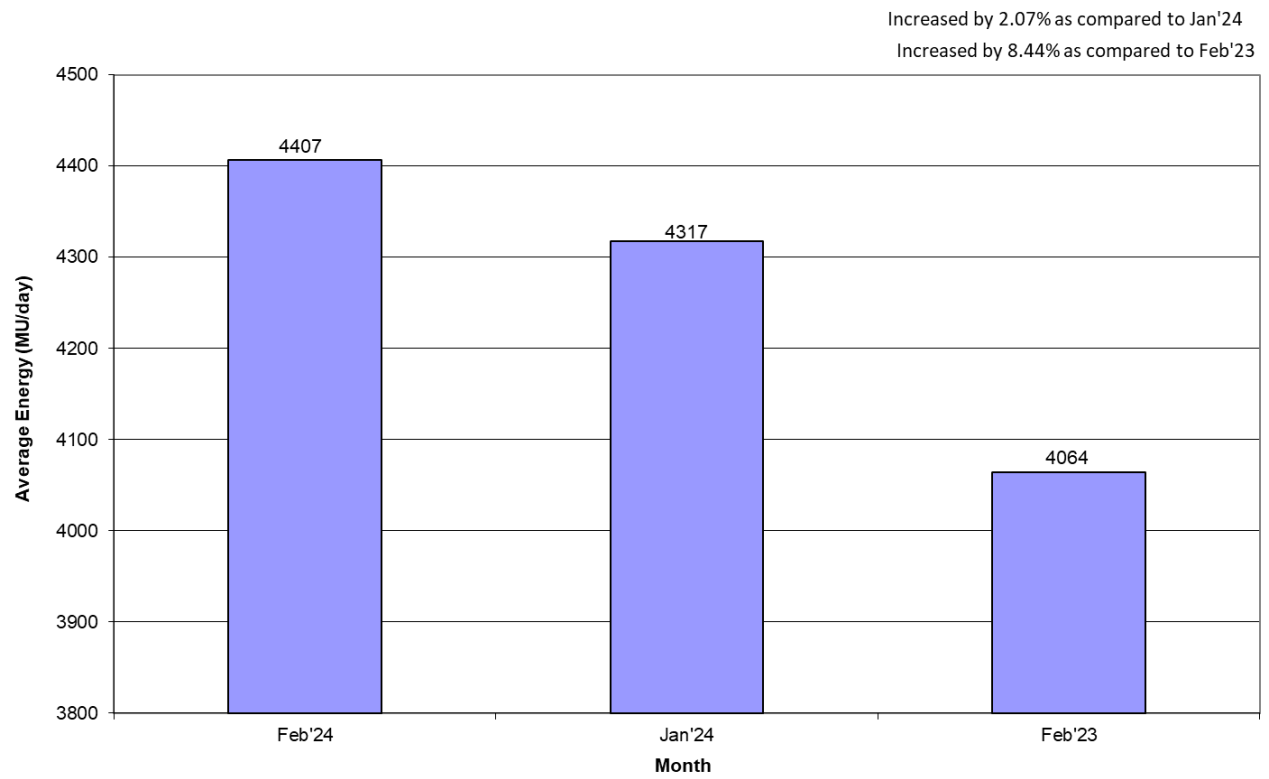


HYDRO GENERATION AT NATIONAL LEVEL (MU)

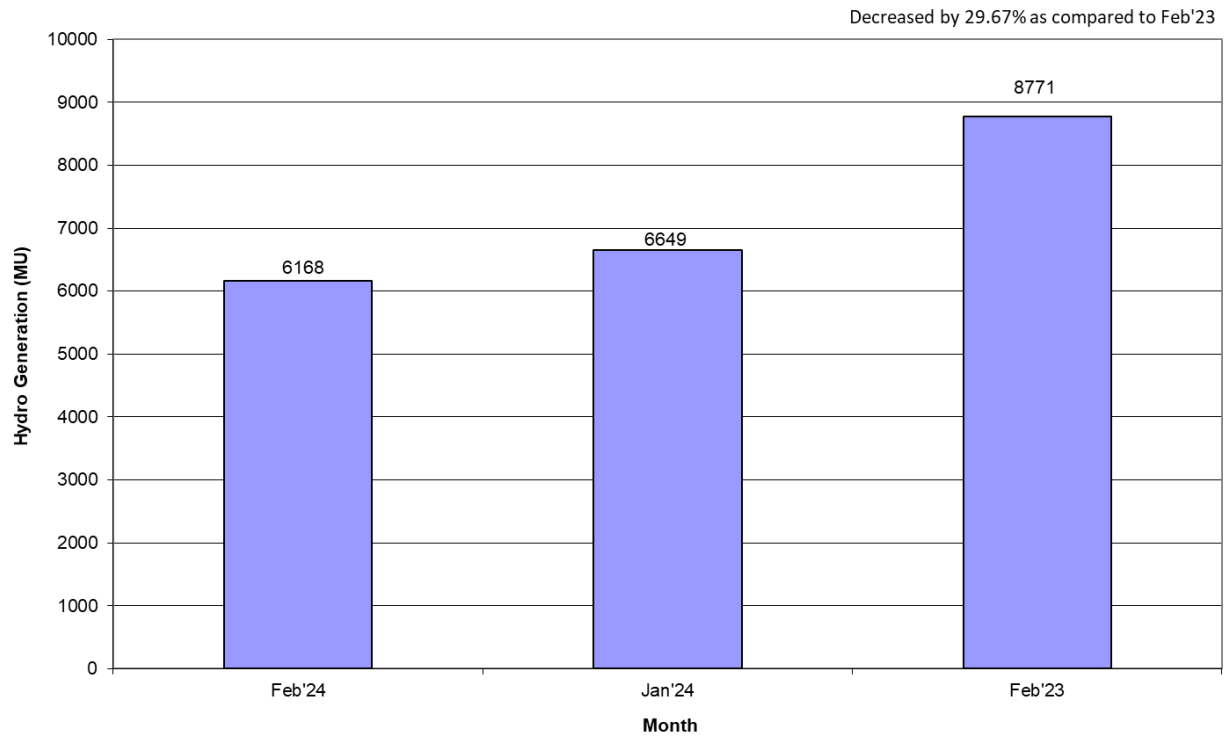


AVERAGE HYDRO GENERATION AT NATIONAL LEVEL (MU/Day)

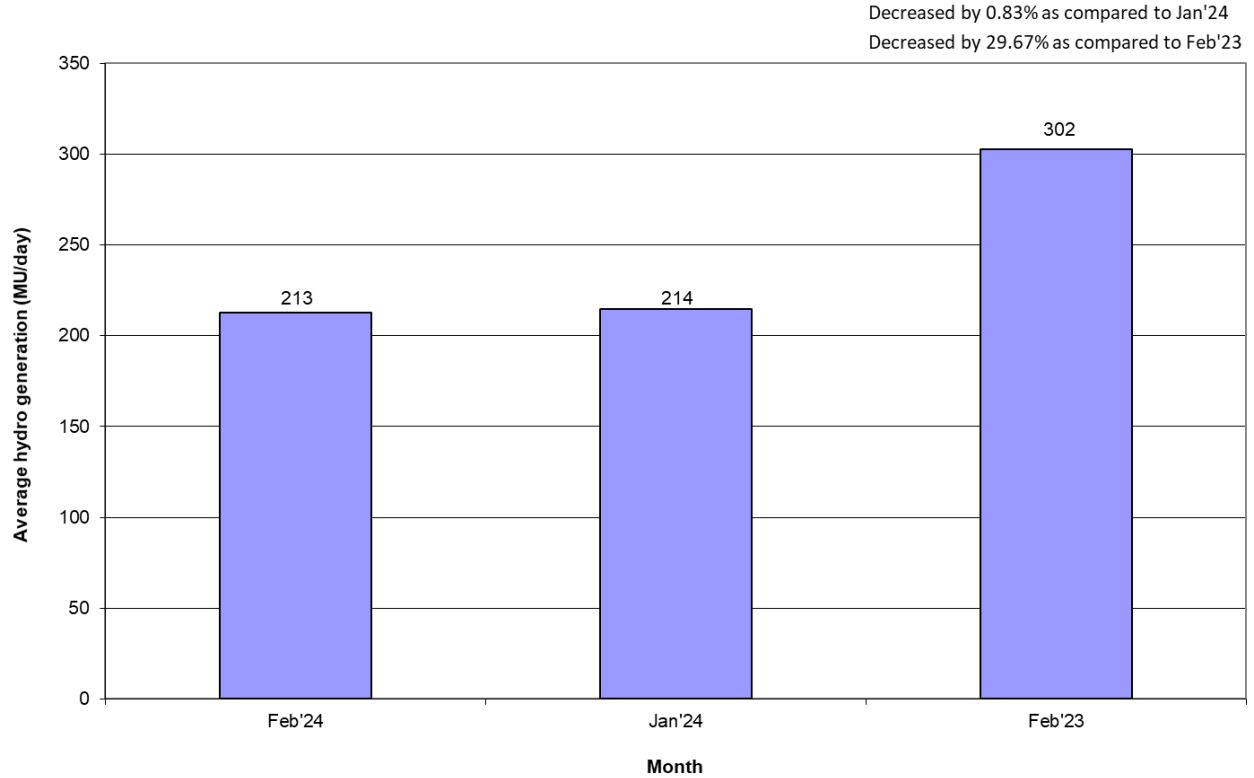


WIND GENERATION AT NATIONAL LEVEL (MU)

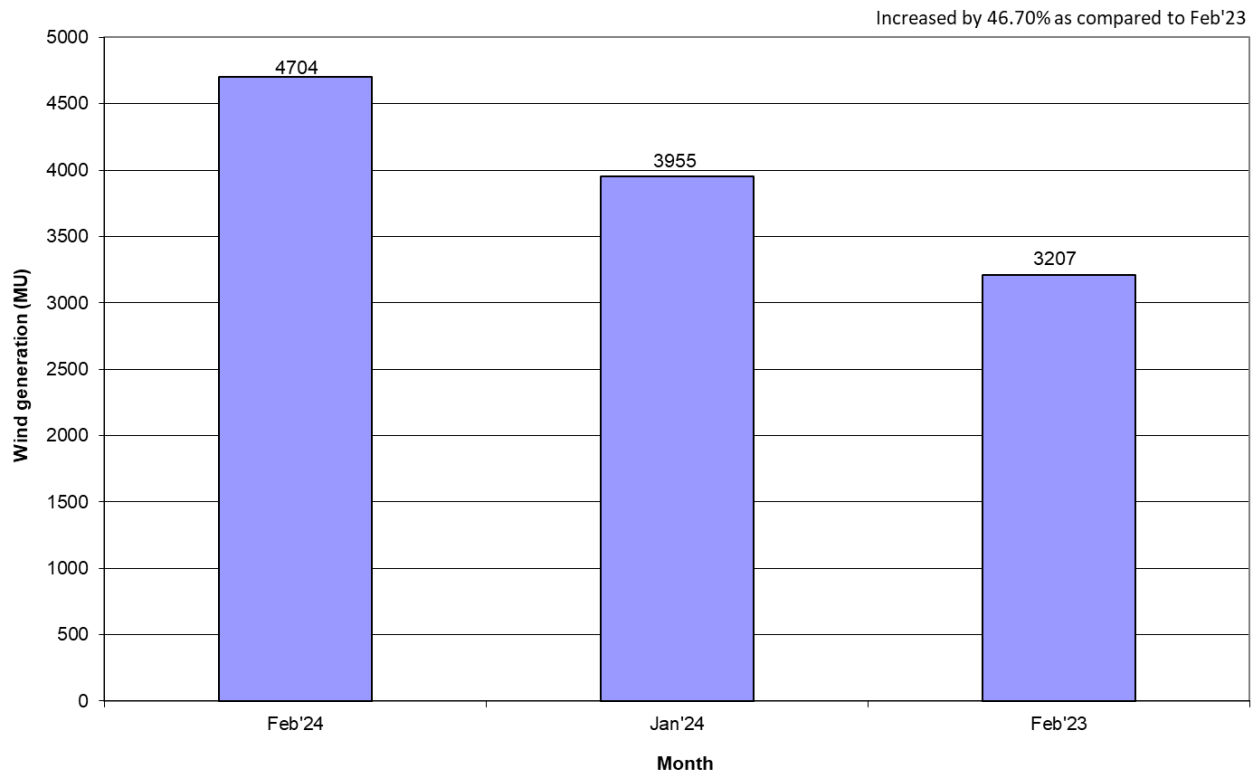


AVERAGE WIND GENERATION AT NATIONAL LEVEL (MU/Day)

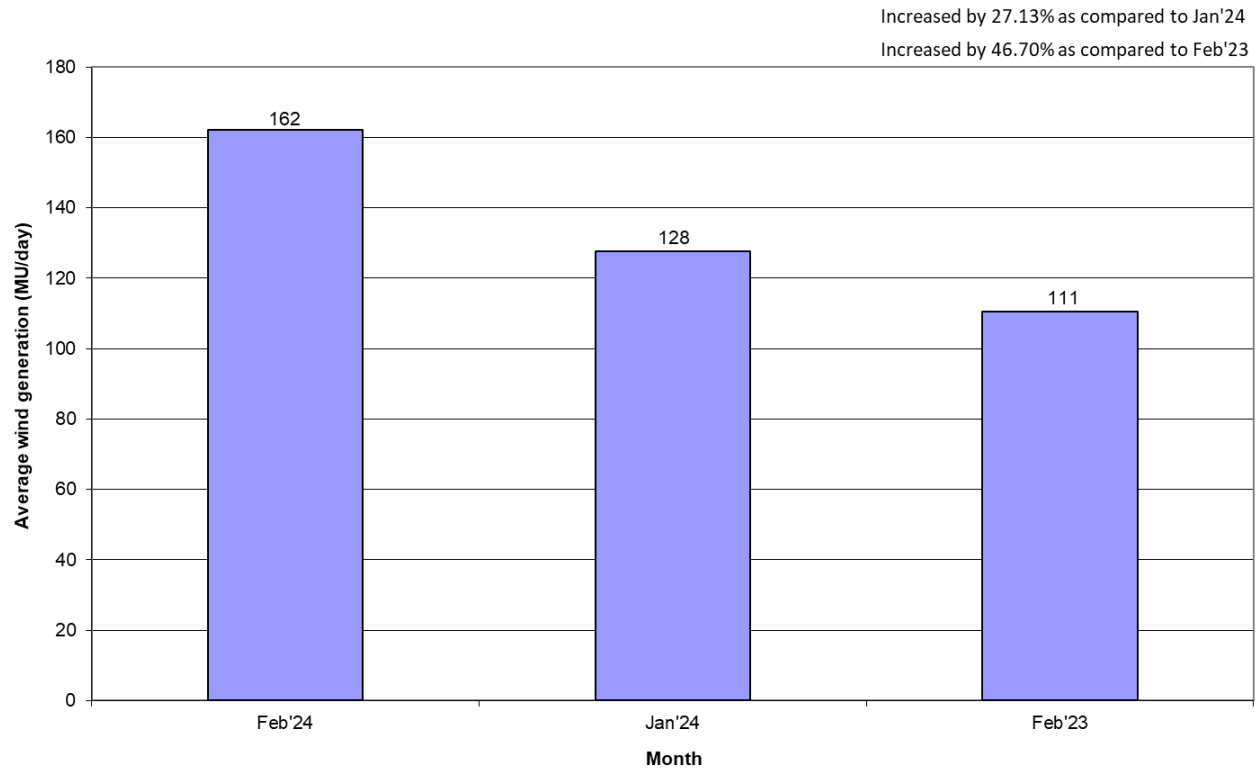

SOLAR GENERATION AT NATIONAL LEVEL (MU)

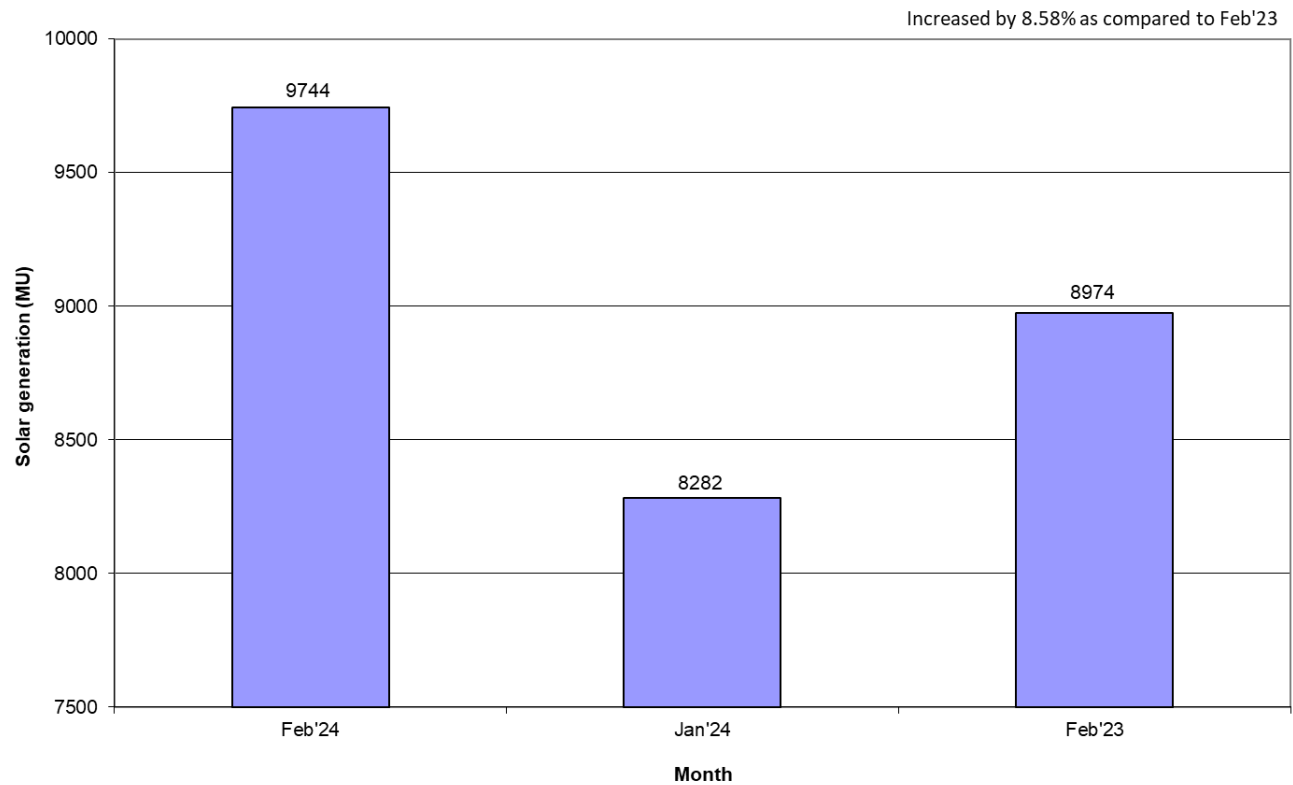

AVERAGE SOLAR GENERATION AT NATIONAL LEVEL (MU/Day)

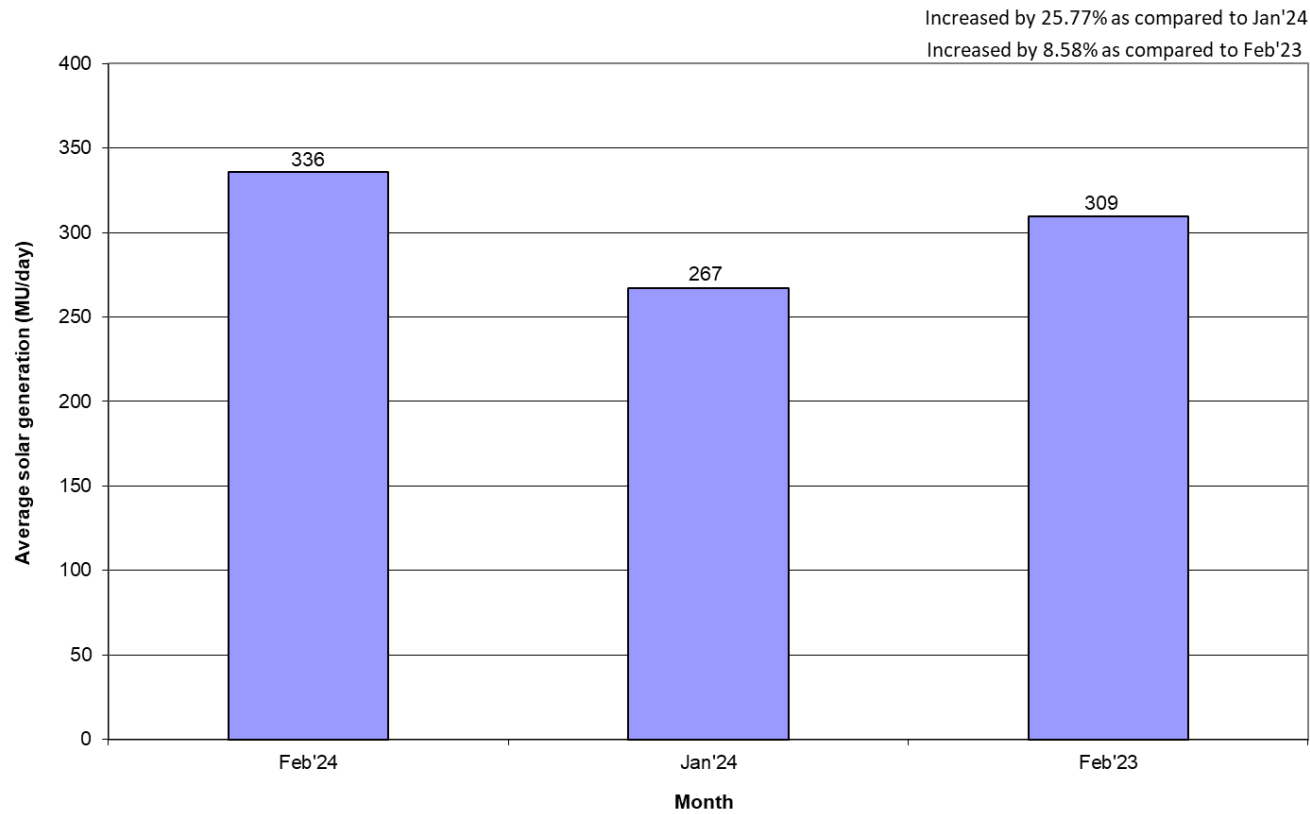

2. ALL INDIA REGIONWISE INSTALLED CAPACITY

As on 29.02.2024
(All figures are in MW)

S No	Region	THERMAL					NUCLEAR	HYDRO	RES @ MNRE	GRAND TOTAL
		COAL	LIGNITE	GAS	DIESEL	TOTAL				
1	NR	56951	1580	5995	0	64526	1620	20830	36276	123252
2	WR	74663	1400	10806	0	86869	2540	7563	44186	141158
3	SR	49894	3640	6492	434	60460	3320	11827	53579	129186
4	ER	28512	0	80	0	28592	0	4764	1914	35271
5	NER	949	0	1665	36	2650	0	1944	575	5169
6	ISLANDS	0	0	0	120	120	0	0	40	160
	ALL INDIA	210969	6620	25038	589	243217	7480	46928	136570	434195

Remarks: Data from CEA website

3. राष्ट्रीय स्तर पर संध्याकालीन शिखर विद्युत मांग पूर्ति
EVENING PEAK HOUR DEMAND MET AT NATIONAL LEVEL


माह: फरवरी 2024 MONTH:- FEB 2024

सभी आंकड़े मेगावाट मे All figures in MW

दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
1-Feb-24	55532	62157	47830	20990	2604	189113
2-Feb-24	56781	61962	48331	21123	2514	190711
3-Feb-24	57075	62270	47387	21086	2572	190390
4-Feb-24	43147	59111	43230	20371	2536	168395
5-Feb-24	55227	63232	46315	20039	2528	187341
6-Feb-24	55879	63379	46740	20727	2651	189376
7-Feb-24	57003	63009	50577	20342	2689	193620
8-Feb-24	55006	62959	50269	20301	2704	191239
9-Feb-24	53802	62464	49601	20674	2674	189215
10-Feb-24	55971	62491	49133	21111	2644	191350
11-Feb-24	52963	58265	44153	20516	2546	178443
12-Feb-24	54698	61334	49045	21233	2658	188968
13-Feb-24	54771	61523	47661	20594	2673	187222
14-Feb-24	54468	61534	49940	21063	2657	189662
15-Feb-24	54572	62873	49847	21166	2666	191124
16-Feb-24	54353	62580	49457	21483	2634	190507
17-Feb-24	53807	63080	49765	21156	2576	190384
18-Feb-24	49875	59423	44972	20668	2528	177466
19-Feb-24	52560	63752	50527	21706	2722	191267
20-Feb-24	52375	64113	51202	21354	2464	191508
21-Feb-24	52879	63056	51372	21653	2406	191366
22-Feb-24	59324	63082	51487	21327	2467	197687
23-Feb-24	53305	62672	51890	21662	2518	192047
24-Feb-24	53884	62251	50465	21613	2614	190827
25-Feb-24	51230	59255	46305	20639	2570	179999
26-Feb-24	52452	61234	50821	21671	2600	188778
27-Feb-24	53067	60430	51253	20501	2775	188026
28-Feb-24	53564	62571	51108	21908	2712	191863
29-Feb-24	53400	63566	51744	21679	2718	193107
उच्चतम MAXIMUM	59324	64113	51890	21908	2775	197687
निम्नतम MINIMUM	43147	58265	43230	20039	2406	168395
औसत AVERAGE	53896	62056	49049	21047	2608	188655
अब तक का उच्चतम All Time Max.	76274	65518	52366	28579	3510	215592
दिनांक Date	04.09.23	13.10.23	18.04.23	18.04.23	12.08.22	28.08.23

नोट : सभी आंकड़े 1900 बजे की मांगपूर्ति पर आधारित है ।
 Note: The above figures correspond to value at 1900 Hrs

EVENING PEAK HOUR DEMAND(at 1900hrs)MET DURING THE MONTH OF FEBRUARY 2024

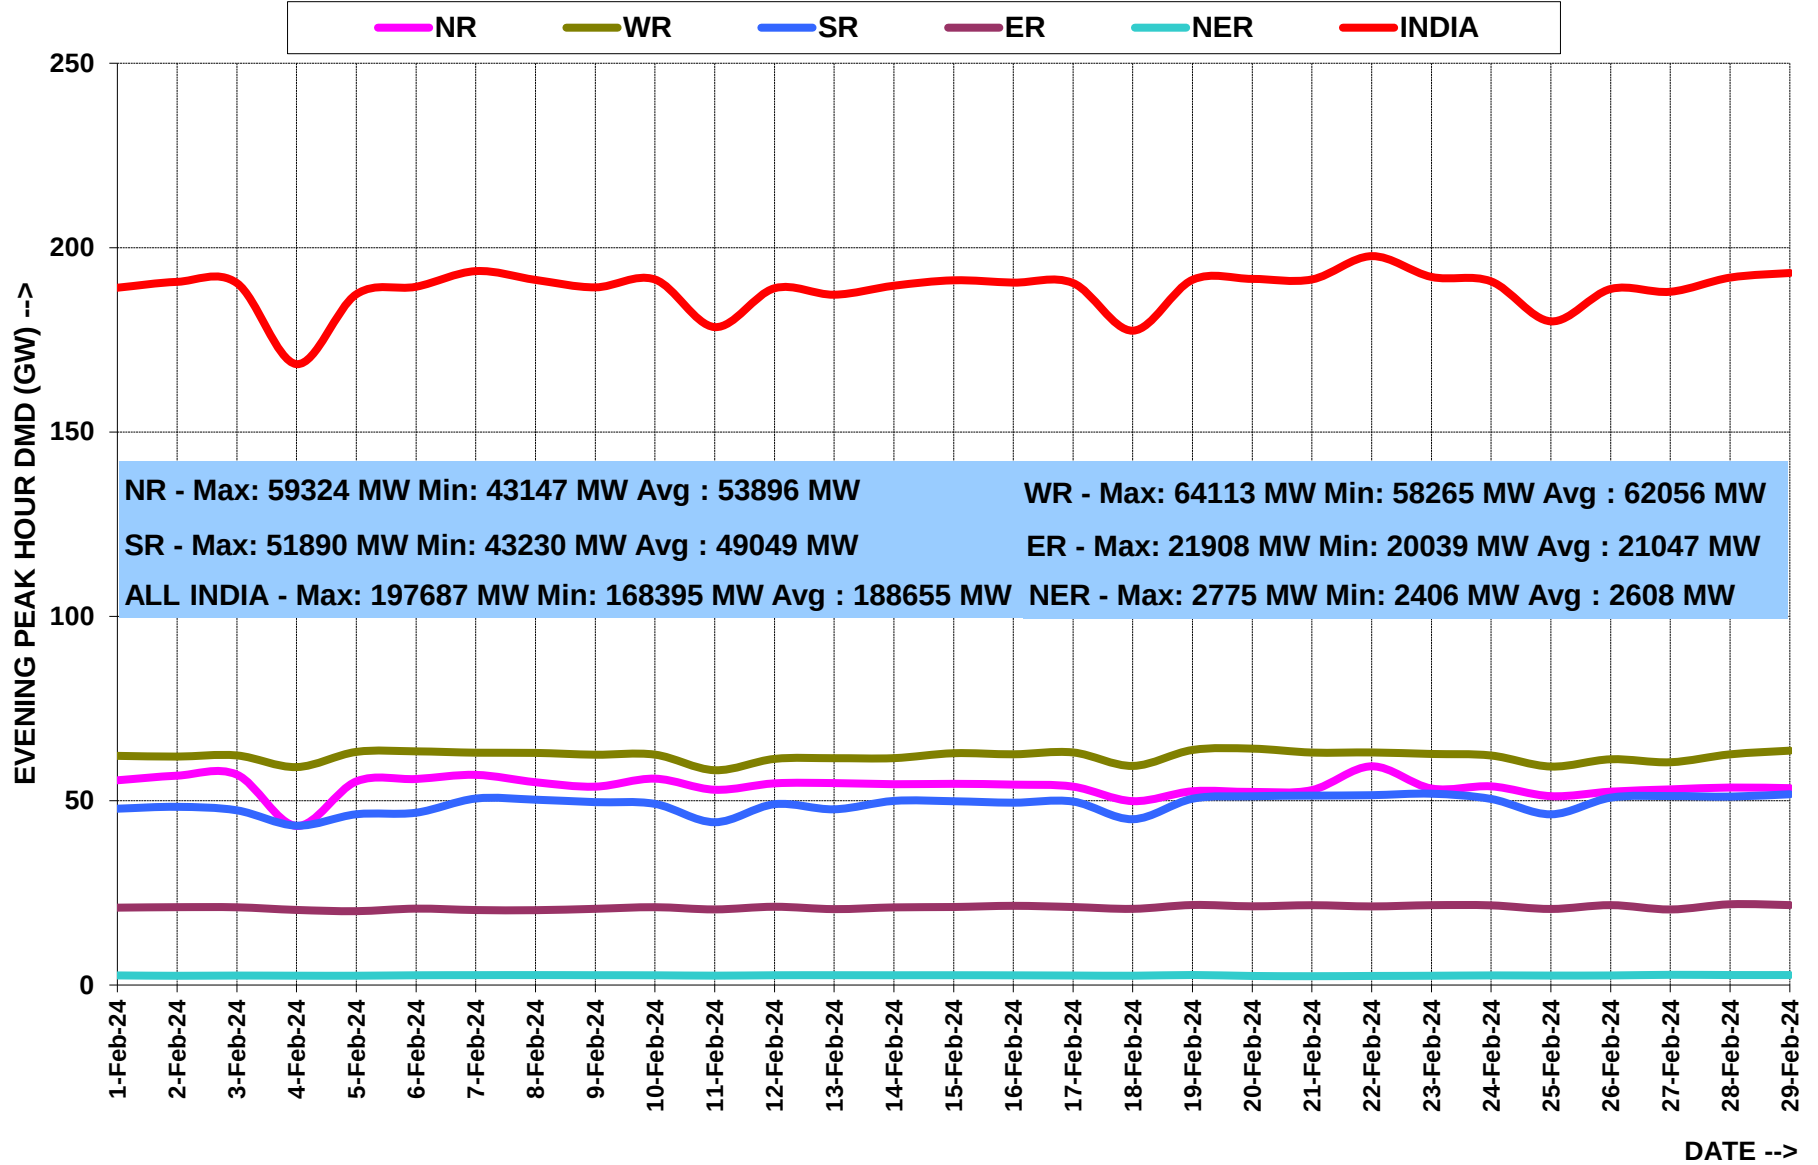


4. राष्ट्रीय स्तर पर विद्युत ऊर्जा आपूर्ति ENERGY MET AT NATIONAL LEVEL

माह: फरवरी 2024 MONTH:- FEB 2024

सभी आंकड़े मिलियन यूनिट में All figures in MU

दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Feb-24	1113	1488	1230	440	49	4320
02-Feb-24	1188	1497	1246	442	48	4421
03-Feb-24	1183	1491	1231	440	46	4392
04-Feb-24	1082	1460	1159	427	48	4176
05-Feb-24	1097	1495	1223	434	48	4298
06-Feb-24	1152	1524	1249	448	49	4421
07-Feb-24	1168	1523	1260	442	49	4443
08-Feb-24	1163	1516	1270	444	49	4441
09-Feb-24	1182	1510	1274	449	49	4463
10-Feb-24	1185	1499	1256	444	48	4432
11-Feb-24	1154	1444	1182	433	48	4261
12-Feb-24	1180	1471	1222	441	49	4362
13-Feb-24	1188	1487	1264	441	49	4428
14-Feb-24	1189	1479	1274	443	49	4434
15-Feb-24	1185	1489	1277	445	49	4445
16-Feb-24	1196	1502	1277	449	49	4474
17-Feb-24	1178	1507	1264	449	49	4447
18-Feb-24	1112	1467	1201	438	47	4264
19-Feb-24	1076	1490	1268	453	49	4337
20-Feb-24	1101	1514	1300	460	49	4424
21-Feb-24	1117	1504	1307	457	48	4434
22-Feb-24	1151	1495	1318	457	48	4468
23-Feb-24	1193	1492	1335	459	48	4526
24-Feb-24	1187	1479	1328	459	49	4502
25-Feb-24	1167	1435	1242	440	48	4331
26-Feb-24	1178	1471	1287	450	51	4437
27-Feb-24	1164	1464	1320	457	49	4455
28-Feb-24	1159	1454	1327	459	50	4449
29-Feb-24	1163	1495	1333	468	49	4508
कुल TOTAL	33552	43141	36723	12969	1409	127794
उच्चतम MAXIMUM	1196	1524	1335	468	51	4526
निम्नतम MINIMUM	1076	1435	1159	427	46	4176
औसत AVERAGE	1157	1488	1266	447	49	4407
संचयी 2023-24 Cumulative 2023-24	440190	469898	380833	171446	18237	1480604
अब तक का उच्चतम All Time Max.	1796	1618	1335	639	72	5224
दिनांक Date	04.09.23	02.09.23	23.02.24	08.06.23	15.09.23	02.09.23

ENERGY MET DURING THE MONTH OF FEBRUARY' 2024

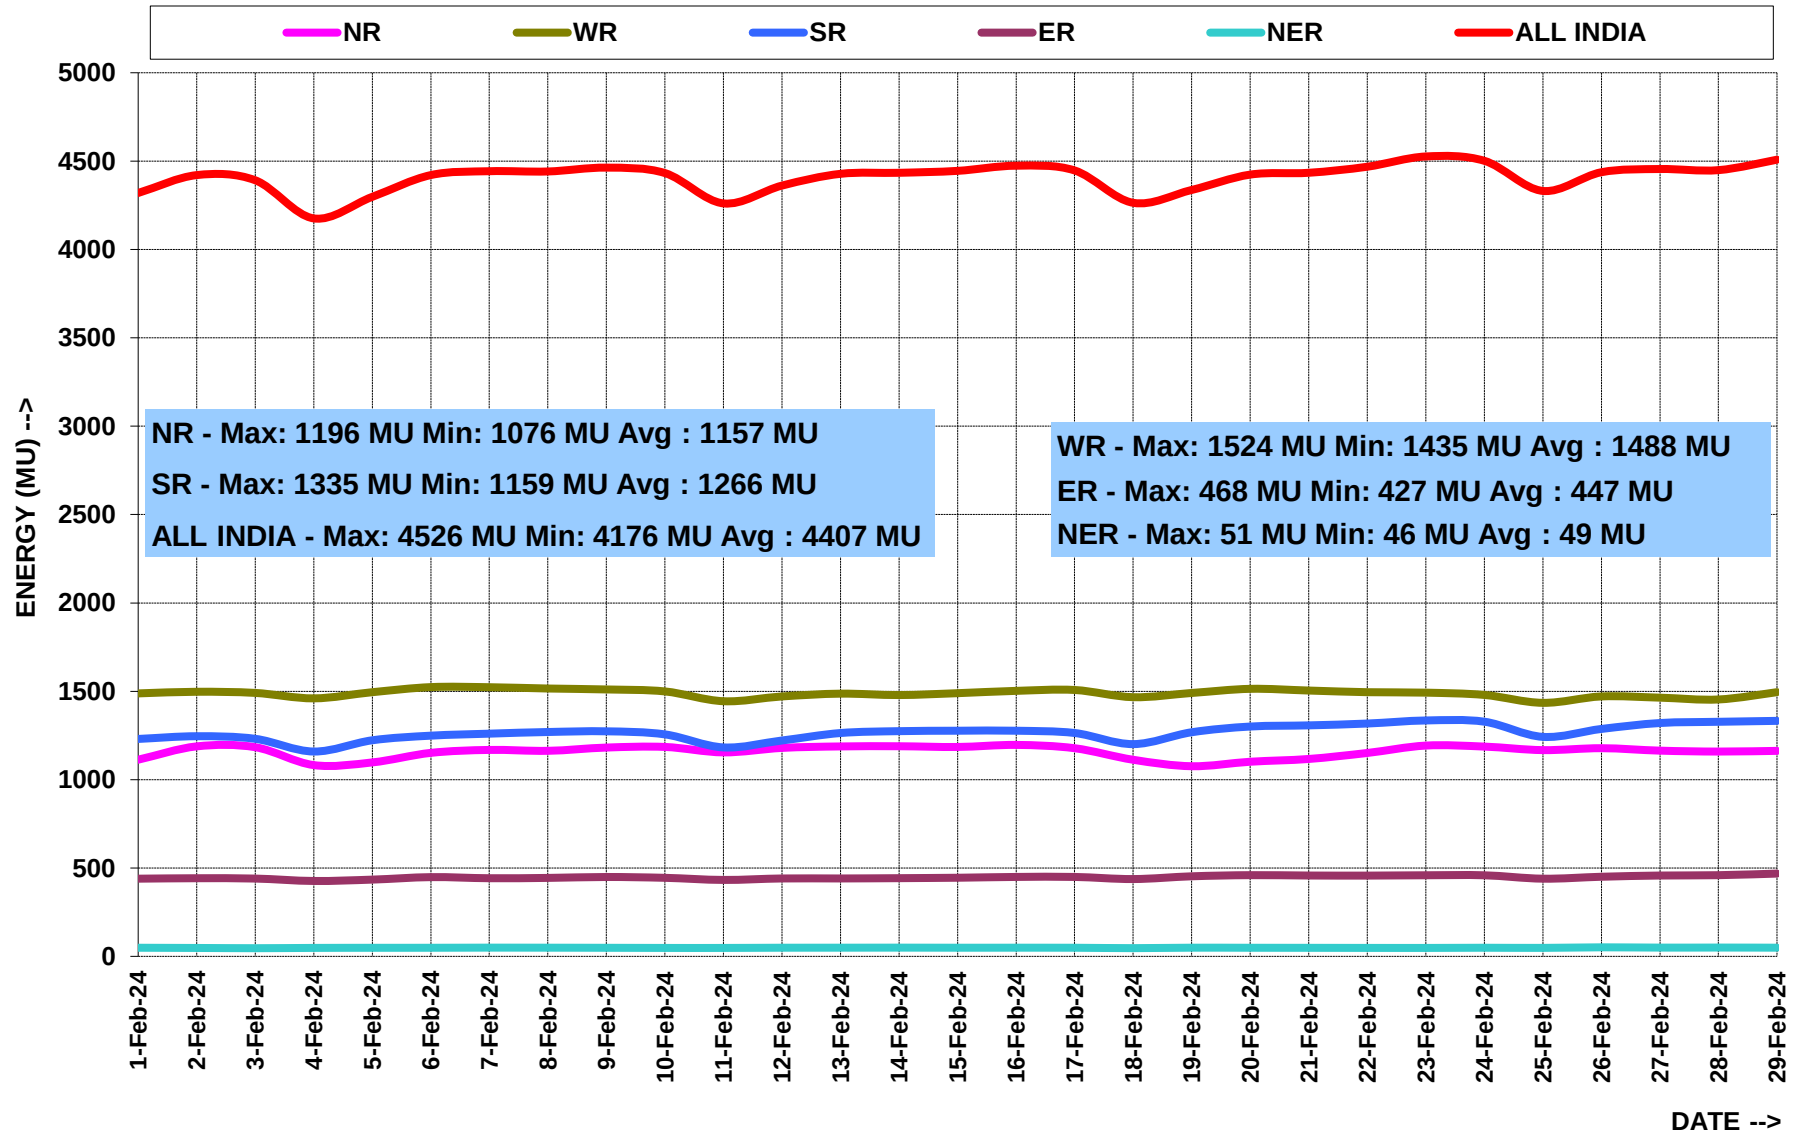

5. वर्ष 2023-24 के लिए आवृत्ति रूपरेखा FREQUENCY PROFILE FOR YEAR 2023-24

राष्ट्रीय ग्रिड NATIONAL GRID								
फ्रीक्वेंसी रूपरेखा (Hz)			<49.9	49.9-50.05	>50.05	उच्चतम फ्रीक्वेंसी	निम्नतम फ्रीक्वेंसी	औसत फ्रीक्वेंसी
% समय	Apr-23	All India Grid	10.54	67.90	21.56	50.33	49.49	49.99
	May-23	All India Grid	9.83	68.48	21.69	50.43	49.48	49.99
	Jun-23	All India Grid	6.47	67.82	25.71	50.41	49.51	50.01
	Jul-23	All India Grid	4.60	74.96	20.44	50.23	49.76	50.01
	Aug-23	All India Grid	7.08	77.28	15.63	50.20	49.74	50.00
	Sep-23	All India Grid	5.26	77.90	16.84	50.21	49.77	50.00
	Oct-23	All India Grid	8.87	74.42	16.71	50.21	49.71	49.99
	Nov-23	All India Grid	6.83	74.36	18.81	50.26	49.73	50.00
	Dec-23	All India Grid	7.83	75.21	16.96	50.26	49.71	49.99
	Jan-24	All India Grid	6.80	75.83	17.37	50.25	49.73	50.00
	Feb-24	All India Grid	6.24	74.06	19.70	50.26	49.74	50.00
	2023-24 (upto Feb)	All India Grid	7.31	73.49	19.20	50.43	49.48	50.00

5.1 फरवरी 2024 के लिए आवृत्ति रूपरेखा FREQUENCY PROFILE FOR FEBRUARY 2024

फ्रिक्वेंसी रूपरेखा (Hz)		<49.9	49.9-50.05	>50.05	उच्चतम फ्रिक्वेंसी	निम्नतम फ्रिक्वेंसी	औसत फ्रिक्वेंसी	एफ़.वी.आई.
% समय	01-Feb-24	4.02	72.04	23.95	50.35	49.72	50.01	0.04
	02-Feb-24	6.68	74.77	18.55	50.24	49.65	50.00	0.05
	03-Feb-24	12.97	69.72	17.30	50.24	49.72	49.99	0.05
	04-Feb-24	10.20	70.02	19.78	50.30	49.70	49.99	0.07
	05-Feb-24	5.45	60.50	34.05	50.27	49.77	50.02	0.06
	06-Feb-24	6.30	77.75	15.95	50.19	49.66	49.99	0.04
	07-Feb-24	3.10	75.44	21.46	50.30	49.80	50.01	0.04
	08-Feb-24	5.94	73.84	20.22	50.23	49.77	50.00	0.04
	09-Feb-24	7.81	74.66	17.52	50.18	49.73	49.99	0.04
	10-Feb-24	2.42	79.53	18.06	50.28	49.83	50.00	0.03
	11-Feb-24	2.18	82.87	14.95	50.25	49.85	50.00	0.03
	12-Feb-24	6.50	71.12	22.37	50.27	49.71	50.01	0.05
	13-Feb-24	4.39	71.40	24.21	50.23	49.77	50.01	0.04
	14-Feb-24	2.94	76.04	21.02	50.25	49.74	50.01	0.04
	15-Feb-24	3.75	72.49	23.76	50.27	49.75	50.01	0.04
	16-Feb-24	3.32	79.50	17.18	50.23	49.79	50.00	0.03
	17-Feb-24	10.17	72.86	16.97	50.30	49.76	49.99	0.05
	18-Feb-24	8.89	65.01	26.10	50.32	49.57	50.01	0.08
	19-Feb-24	7.71	62.62	29.68	50.31	49.68	50.01	0.07
	20-Feb-24	17.25	73.18	9.57	50.20	49.62	49.96	0.07
	21-Feb-24	9.79	78.39	11.82	50.23	49.78	49.99	0.04
	22-Feb-24	6.23	80.53	13.24	50.20	49.71	49.99	0.04
	23-Feb-24	9.47	79.02	11.52	50.22	49.78	49.99	0.04
	24-Feb-24	8.28	73.23	18.50	50.21	49.75	50.00	0.04
	25-Feb-24	3.51	75.20	21.30	50.33	49.75	50.01	0.04
	26-Feb-24	4.68	70.37	24.95	50.27	49.73	50.01	0.05
	27-Feb-24	1.56	79.56	18.88	50.23	49.85	50.01	0.03
	28-Feb-24	2.62	78.75	18.63	50.25	49.82	50.01	0.03
	29-Feb-24	2.80	77.40	19.80	50.27	49.82	50.01	0.04


6.राष्ट्रीय स्तर पर जल विद्युत उत्पादन
HYDRO GENERATION AT NATIONAL LEVEL

माह: फरवरी 2024 MONTH:- FEB 2024

सभी आंकड़े मिलियन यूनिट में All figures in MU

दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Feb-24	94	40	48	22	9	213
02-Feb-24	93	40	57	24	9	224
03-Feb-24	94	42	60	23	9	227
04-Feb-24	92	35	37	19	8	190
05-Feb-24	95	35	51	22	8	211
06-Feb-24	92	47	55	23	10	226
07-Feb-24	93	47	50	22	9	220
08-Feb-24	92	38	50	21	8	210
09-Feb-24	94	44	50	22	9	219
10-Feb-24	95	41	44	21	9	210
11-Feb-24	95	29	32	20	8	183
12-Feb-24	96	47	46	24	8	222
13-Feb-24	95	41	44	23	8	211
14-Feb-24	95	41	41	21	8	206
15-Feb-24	97	37	40	20	8	202
16-Feb-24	98	39	35	20	8	200
17-Feb-24	99	34	43	21	7	204
18-Feb-24	98	29	33	18	7	186
19-Feb-24	111	32	44	17	8	213
20-Feb-24	122	31	56	18	10	237
21-Feb-24	120	32	53	20	9	234
22-Feb-24	112	34	58	24	7	236
23-Feb-24	112	32	62	21	9	237
24-Feb-24	110	31	62	19	7	229
25-Feb-24	110	23	41	12	8	194
26-Feb-24	113	27	40	18	8	207
27-Feb-24	110	23	44	19	8	203
28-Feb-24	106	25	49	20	8	209
29-Feb-24	107	26	48	18	7	207
कुल TOTAL	2940	1023	1373	593	239	6168
उच्चतम MAXIMUM	122	47	62	24	10	237
निम्नतम MINIMUM	92	23	32	12	7	183
औसत AVERAGE	101	35	47	20	8	213
संचयी 2023-24 Cumulative 2023-24	72393	15935	20018	22037	6391	136774
अब तक का उच्चतम All Time Max.	443	167	208	157	41	877
दिनांक Date	01.08.23	18.12.14	31.08.18	14.09.22	29.08.23	30.08.22

HYDRO ENERGY DURING THE MONTH OF FEBRUARY' 2024

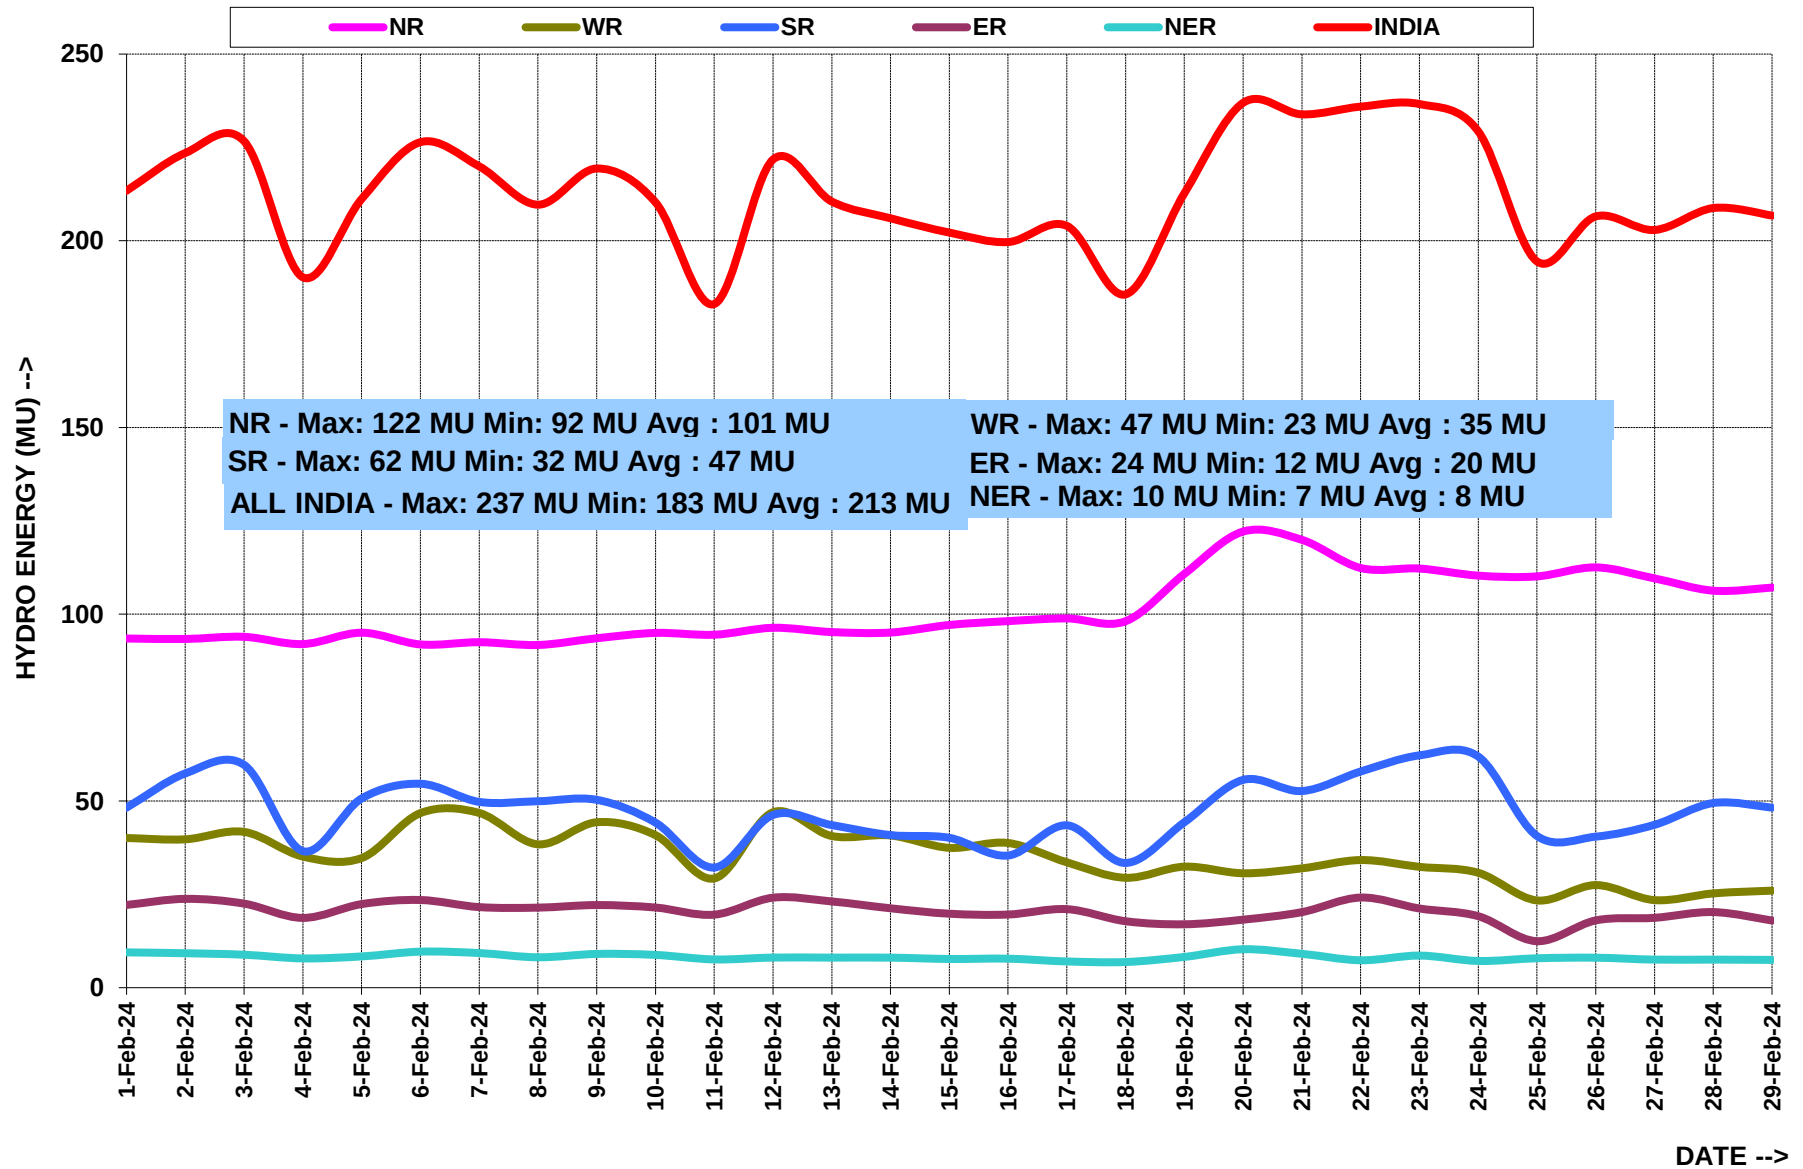

7. राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन
WIND GENERATION AT NATIONAL LEVEL

माह: फरवरी 2024 MONTH:- FEB 2024

सभी आंकड़े मिलियन यूनिट में All figures in MU

दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Feb-24	4	38	29	-----	-----	72
02-Feb-24	18	25	21	-----	-----	65
03-Feb-24	12	28	40	-----	-----	80
04-Feb-24	5	45	56	-----	-----	106
05-Feb-24	7	23	50	-----	-----	80
06-Feb-24	20	26	59	-----	-----	105
07-Feb-24	26	68	44	-----	-----	138
08-Feb-24	11	123	41	-----	-----	175
09-Feb-24	5	63	59	-----	-----	127
10-Feb-24	13	70	91	-----	-----	173
11-Feb-24	21	82	92	-----	-----	195
12-Feb-24	25	71	88	-----	-----	184
13-Feb-24	20	66	79	-----	-----	165
14-Feb-24	12	93	79	-----	-----	184
15-Feb-24	10	118	82	-----	-----	211
16-Feb-24	11	126	110	-----	-----	247
17-Feb-24	6	78	75	-----	-----	159
18-Feb-24	50	62	62	-----	-----	174
19-Feb-24	68	146	62	-----	-----	276
20-Feb-24	14	89	42	-----	-----	145
21-Feb-24	13	119	30	-----	-----	162
22-Feb-24	14	85	35	-----	-----	134
23-Feb-24	11	78	40	-----	-----	129
24-Feb-24	11	62	32	-----	-----	104
25-Feb-24	18	90	52	-----	-----	160
26-Feb-24	31	131	118	-----	-----	280
27-Feb-24	48	146	102	-----	-----	296
28-Feb-24	24	107	75	-----	-----	205
29-Feb-24	20	74	82	-----	-----	176
कुल TOTAL	547	2333	1825	-----	-----	4704
उच्चतम MAXIMUM	68	146	118	-----	-----	296
निम्नतम MINIMUM	4	23	21	-----	-----	65
औसत AVERAGE	19	80	63	-----	-----	162
संचयी 2023-24 Cumulative 2023-24	7740	34381	33586	-----	-----	75707
अब तक का उच्चतम All Time Max.	86	273	298	-----	-----	611
दिनांक Date	07.08.23	07.08.23	21.07.23	-----	-----	02.08.23

***Source:** As reported by SLDCs. Limited visibility of embedded wind generator data.

8. राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन
SOLAR GENERATION AT NATIONAL LEVEL

माह: फरवरी 2024 MONTH:- FEB 2024

सभी आंकड़े मिलियन यूनिट में All figures in MU

दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Feb-24	123	65	116	2.4	0.8	307
02-Feb-24	109	66	118	2.3	0.6	295
03-Feb-24	68	65	112	2.8	0.7	249
04-Feb-24	67	62	125	2.9	1.0	257
05-Feb-24	125	63	127	5.7	0.7	321
06-Feb-24	124	64	132	5.4	0.5	325
07-Feb-24	119	64	133	5.3	0.6	322
08-Feb-24	136	70	129	6.0	1.0	342
09-Feb-24	150	76	133	3.0	1.2	362
10-Feb-24	149	73	127	2.9	1.1	354
11-Feb-24	145	71	125	2.8	1.3	345
12-Feb-24	99	65	134	2.5	1.2	301
13-Feb-24	110	59	135	5.5	1.1	312
14-Feb-24	134	71	127	5.0	1.0	339
15-Feb-24	144	69	137	5.1	0.8	355
16-Feb-24	140	71	140	5.8	1.2	357
17-Feb-24	146	73	142	5.5	1.0	367
18-Feb-24	131	76	138	3.0	0.9	349
19-Feb-24	126	77	135	3.2	1.0	343
20-Feb-24	138	79	128	2.8	0.6	348
21-Feb-24	136	77	129	5.9	0.8	349
22-Feb-24	143	74	137	5.6	0.4	359
23-Feb-24	154	83	137	2.2	0.7	378
24-Feb-24	155	83	121	3.2	1.2	364
25-Feb-24	140	78	118	2.8	0.5	340
26-Feb-24	101	58	130	2.5	1.3	293
27-Feb-24	141	68	137	2.7	1.2	350
28-Feb-24	158	78	141	2.9	1.2	381
29-Feb-24	155	78	138	6.3	1.0	379
कुल TOTAL	3766	2054	3783	114	26	9744
उच्चतम MAXIMUM	158	83	142	6	1	381
निम्नतम MINIMUM	67	58	112	2	0	249
औसत AVERAGE	130	71	130	4	1	336
संचयी 2023-24 Cumulative 2023-24	39970	18694	37172	1112	322.2	97168
अब तक का उच्चतम All Time Max.	158	83	143	6.7	2.4	381
दिनांक Date	28.02.24	23.02.24	21.03.23	23.03.23	22.06.22	28.02.24

***Source:** RLDCs for solar connected to ISTs; SLDCs for embedded solar. Limited visibility of embedded solar data.

9. राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग पूर्ति
DAILY MAXIMUM DEMAND MET AT NATIONAL LEVEL

माह: फरवरी 2024 MONTH:- FEB 2024

सभी आंकड़े मेगावाट में All figures in MW


दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL	विभिन्नता फैक्टर Diversity Factor*
01-Feb-24	57339	73753	61371	21908	2675	211794	1.025
02-Feb-24	62054	73376	61170	21834	2587	218600	1.011
03-Feb-24	59214	74014	60021	22068	2649	214106	1.018
04-Feb-24	56729	73410	57136	21660	2640	206344	1.025
05-Feb-24	58420	74114	60649	21988	2589	214108	1.017
06-Feb-24	59499	73757	61097	22024	2696	215684	1.016
07-Feb-24	59668	74453	61627	21737	2711	216413	1.017
08-Feb-24	60756	73726	62404	21785	2814	217272	1.019
09-Feb-24	62185	73074	62941	21643	2696	220140	1.011
10-Feb-24	61973	72968	61373	21910	2843	216992	1.019
11-Feb-24	60225	70460	58053	21892	2613	210290	1.014
12-Feb-24	61376	72168	62032	22075	2751	217018	1.016
13-Feb-24	61464	73231	62565	21424	2776	218065	1.016
14-Feb-24	63160	72357	63234	21830	2812	220547	1.013
15-Feb-24	62197	72876	62585	22067	2821	219502	1.014
16-Feb-24	63806	72863	63192	21881	2789	221986	1.011
17-Feb-24	61936	72871	62106	21980	2809	218656	1.014
18-Feb-24	59794	71247	59251	21034	2560	211372	1.012
19-Feb-24	56573	72907	63204	22338	2789	213775	1.019
20-Feb-24	58006	72544	64211	22913	2806	216812	1.017
21-Feb-24	57525	72474	64298	22508	2696	215966	1.016
22-Feb-24	58868	71971	64993	22236	2510	217388	1.015
23-Feb-24	62601	72153	65828	22330	2687	222003	1.016
24-Feb-24	61041	71101	65698	23690	2727	219478	1.022
25-Feb-24	62009	69224	60376	21866	2625	214554	1.007
26-Feb-24	61459	71632	63604	23044	2728	219480	1.014
27-Feb-24	61894	70281	64831	22461	2776	219272	1.014
28-Feb-24	62155	68788	65434	22704	2776	218553	1.015
29-Feb-24	60975	70350	65063	22692	2824	218040	1.018
उच्चतम MAXIMUM	63806	74453	65828	23690	2843	222003	1.025
निम्नतम MINIMUM	56573	68788	57136	21034	2510	206344	1.007
औसत AVERAGE	60514	72350	62426	22121	2716	216697	1.016
अब तक का उच्चतम All Time Max.	81220	74799	65828	29641	3712	239978	
दिनांक Date	04.09.23	29.01.24	23.02.24	28.07.23	04.09.23	01.09.23	

* Diversity factor = (Sum of regional max demands) / All India max demand


नोट : यह आंकड़े एनएलडीसी स्काडा प्रणाली में दर्ज दैनिक अधिकतम मांगपूर्ति दर्शाते हैं ।

Note: The above figures denote daily maximum demand met recorded in NLDC SCADA.


10. DEMAND AND GENERATION PLOTS FOR 23 FEBRUARY (MAXIMUM DEMAND MET)

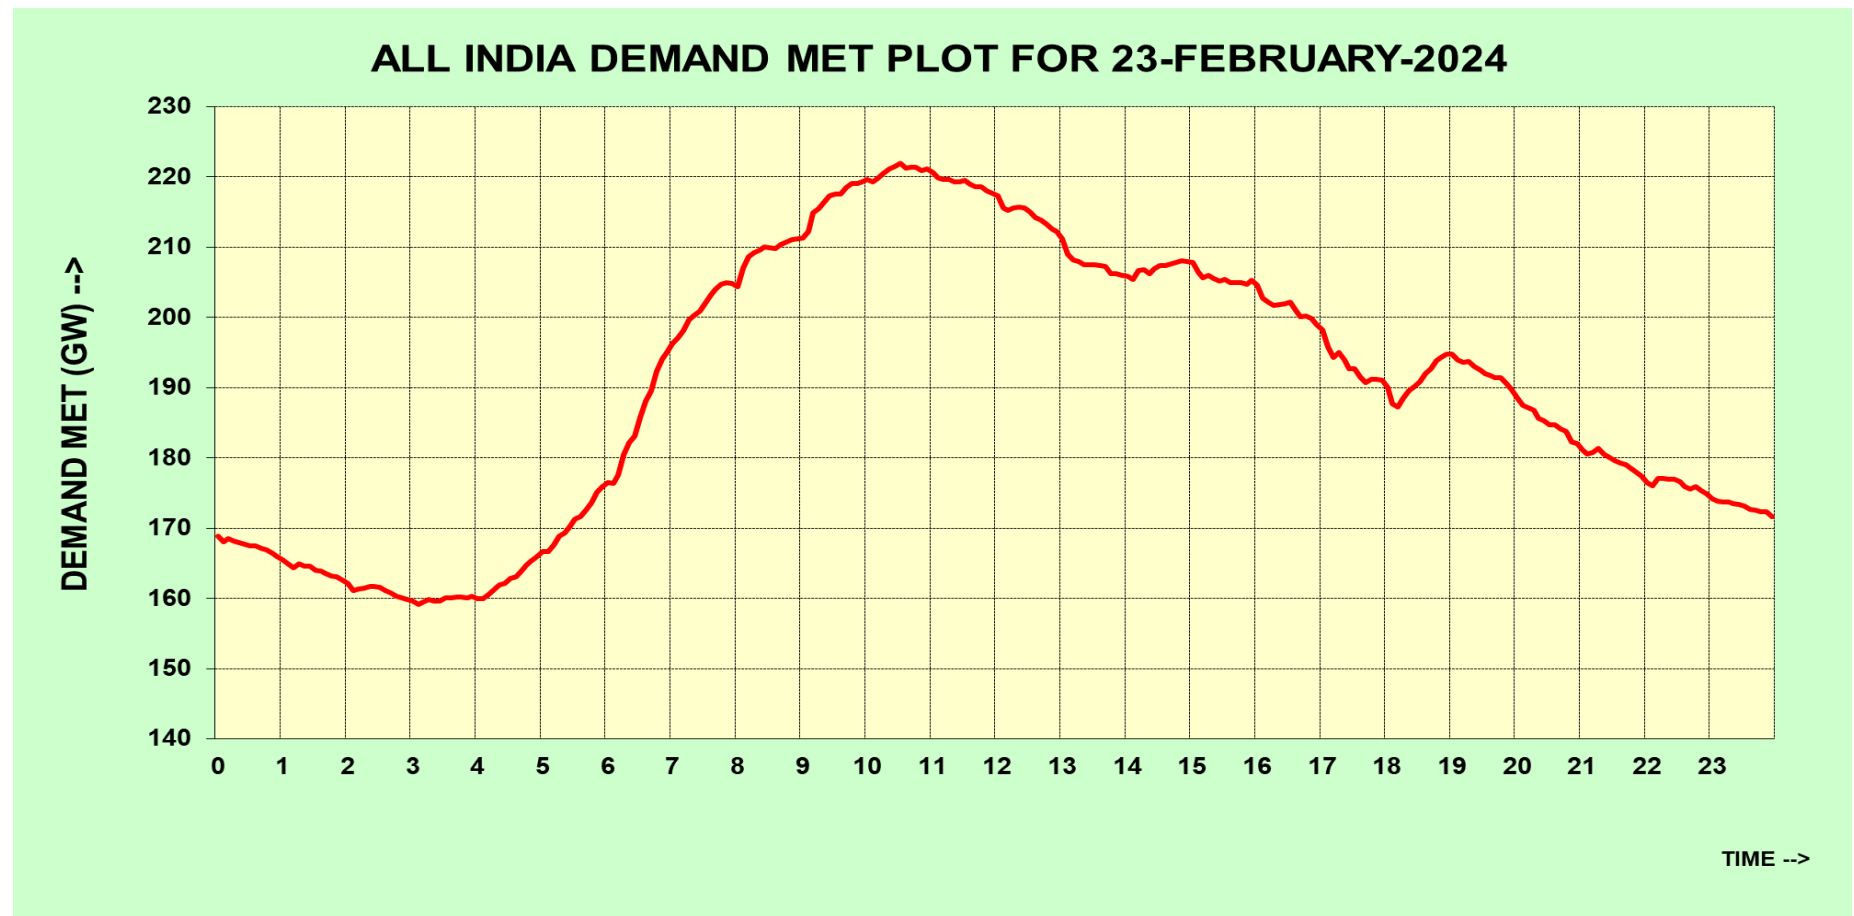


REGIONAL DEMAND MET PLOT FOR 23-FEBRUARY-2024

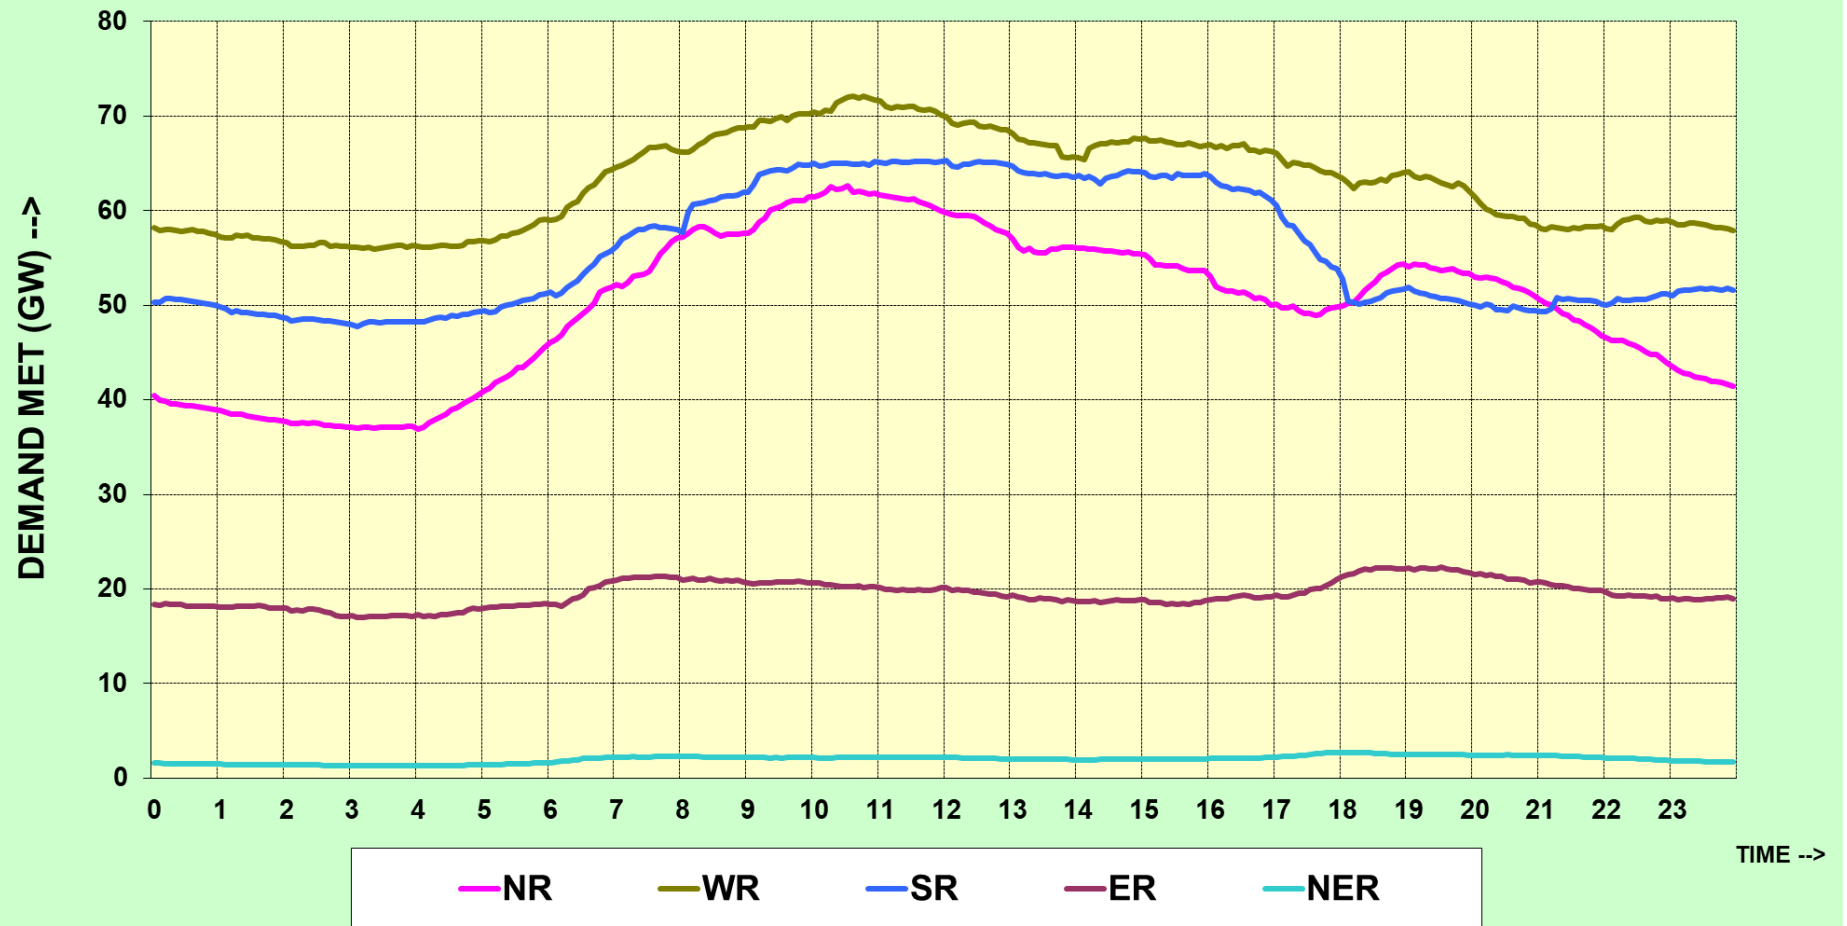

ALL INDIA GENERATION PLOT FOR 23-FEBRUARY-2024

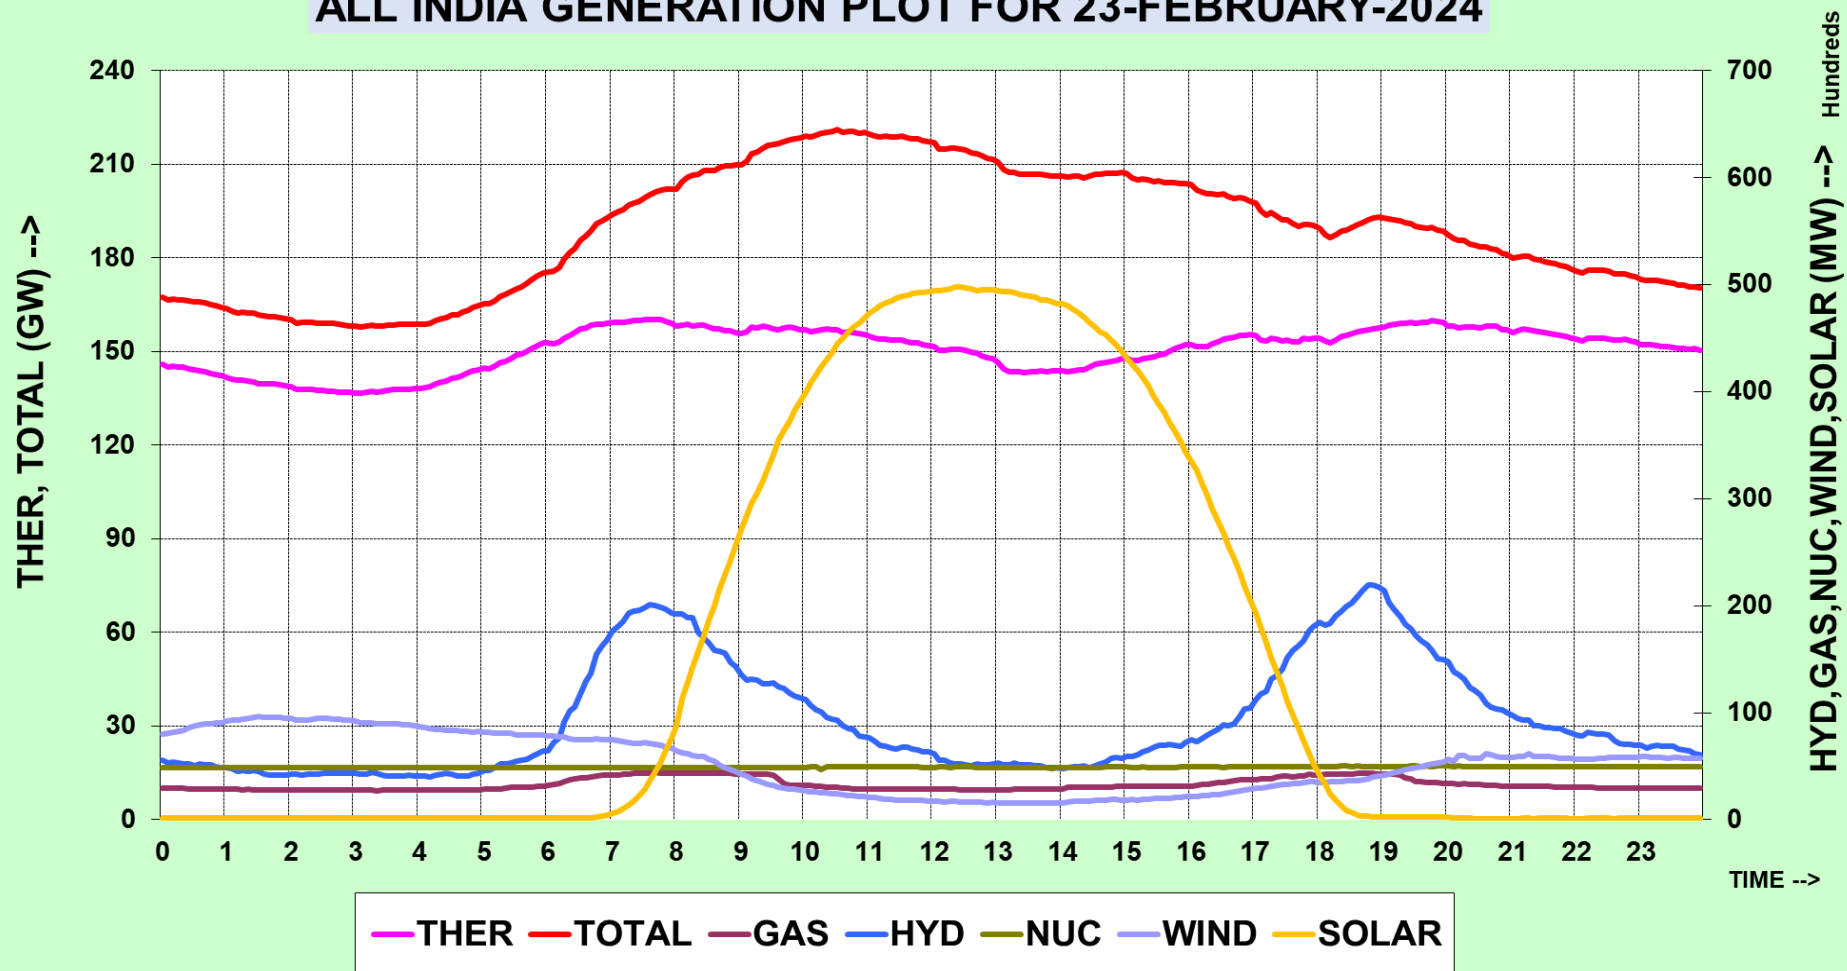

All India Fuel-wise Generation Patterns for 23-FEBRUARY-2024

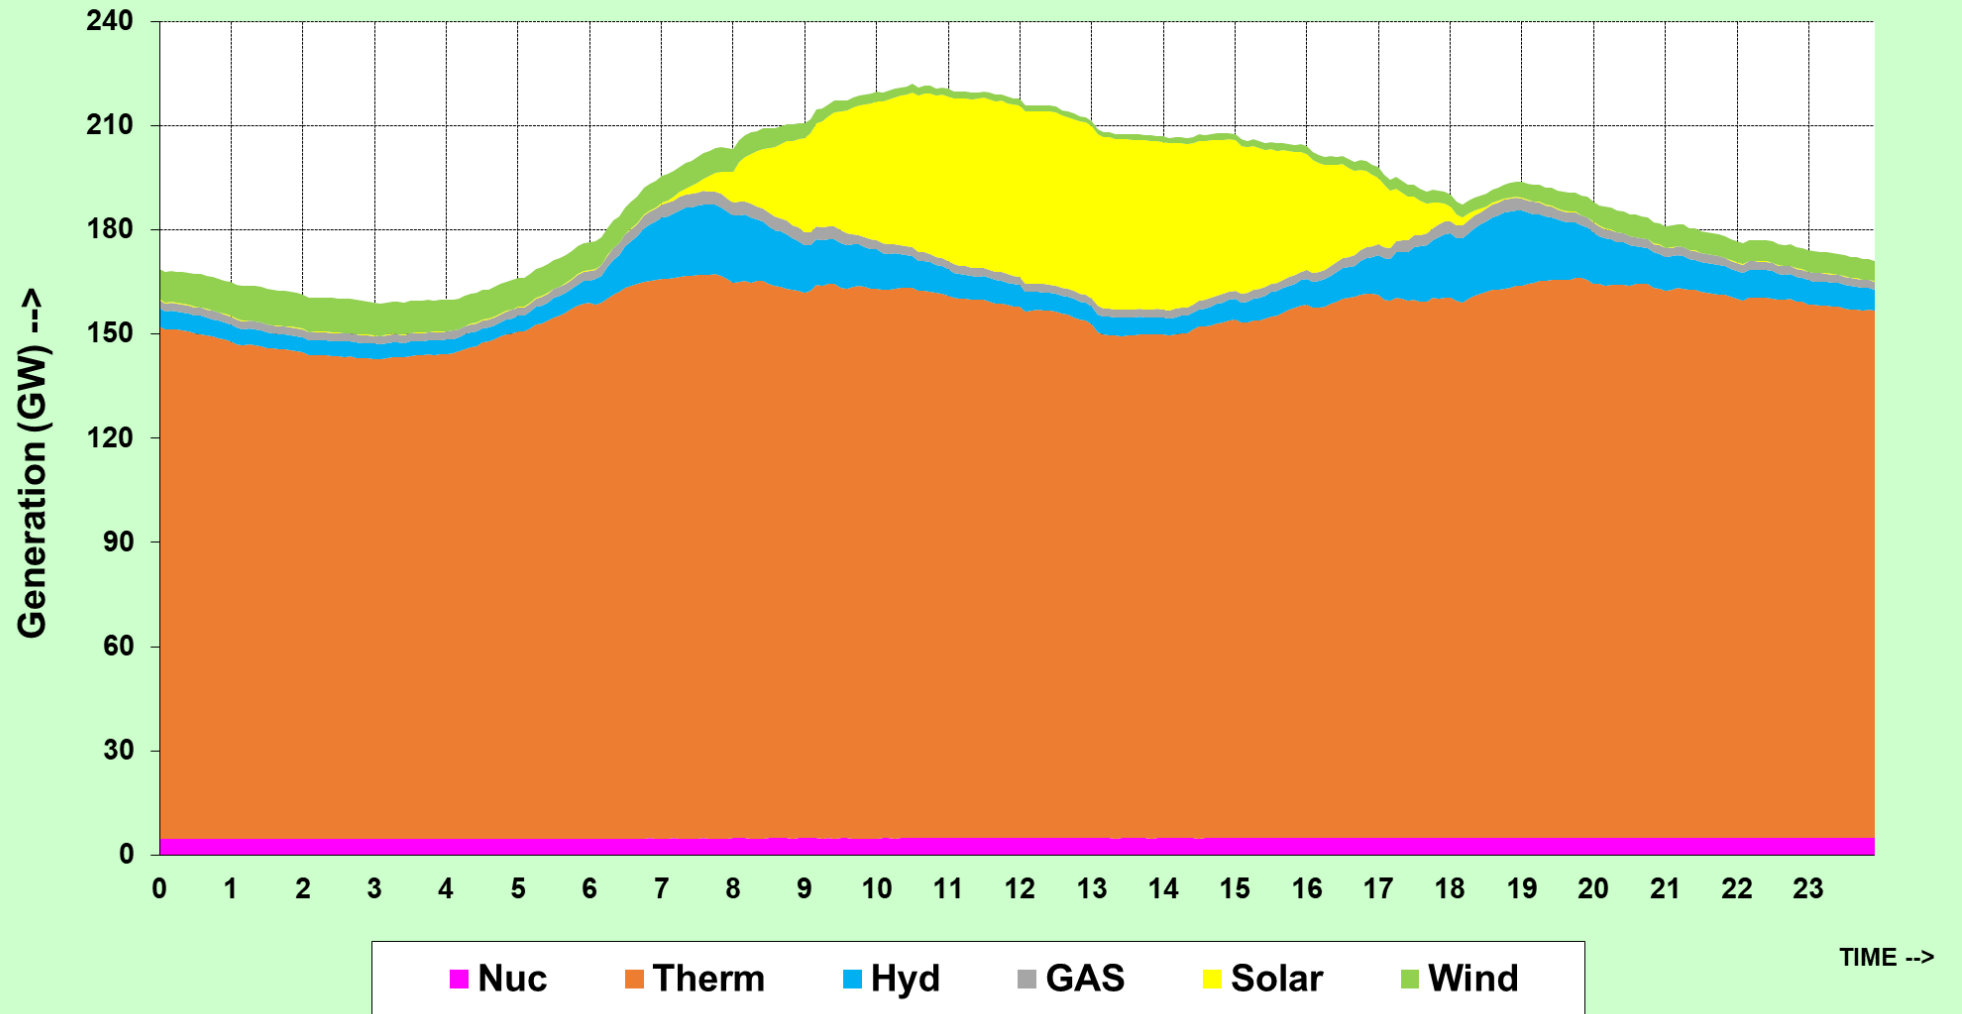

23 फ़रवरी 2024 (अधिकतम माँग) की आल इंडिया माँग आपूर्ति
ALL INDIA DEMAND MET FOR 23 FEBRUARY 2024 (MAXIMUM DEMAND*)

Time (hrs)	All India Demand (MW)		Time (hrs)	All India Demand (MW)
00:05	168052		12:05	215579
00:20	167972		12:20	215684
00:35	167461		12:35	214262
00:50	166423		12:50	212605
01:05	164953		13:05	209019
01:20	164591		13:20	207558
01:35	163894		13:35	207448
01:50	163115		13:50	206276
02:05	161165		14:05	205465
02:20	161653		14:20	206262
02:35	161145		14:35	207359
02:50	160031		14:50	208035
03:05	159200		15:05	206476
03:20	159626		15:20	205585
03:35	160060		15:35	204952
03:50	160113		15:50	204746
04:05	159935		16:05	202751
04:20	161872		16:20	201864
04:35	163095		16:35	201005
04:50	165399		16:50	199877
05:05	166678		17:05	195801
05:20	169320		17:20	193980
05:35	171646		17:35	191591
05:50	175063		17:50	191146
06:05	176404		18:05	187721
06:20	182142		18:20	189596
06:35	188051		18:35	192057
06:50	194115		18:50	194357
07:05	197137		19:05	193997
07:20	200312		19:20	192995
07:35	203219		19:35	191771
07:50	204927		19:50	190593
08:05	206991		20:05	187450
08:20	209587		20:20	185636
08:35	209835		20:35	184683
08:50	211135		20:50	182338
09:05	212255		21:05	180557
09:20	216406		21:20	180564
09:35	217609		21:35	179242
09:50	219071		21:50	178033
10:05	219267		22:05	176019
10:20	221180		22:20	177016
10:35	221317		22:35	175920
10:50	220916		22:50	175294
11:05	219835		23:05	173836
11:20	219359		23:20	173494
11:35	218953		23:35	172696
11:50	218042		23:50	172335
Maximum Demand of 222003 MW met@10:30 hrs (from 1 min. interval SCADA DATA)				

* 15 minute interval SCADA DATA of instantaneous demand

11. ACTUAL POWER SUPPLY POSITION - FEBRUARY 2024

REGION	STATE	Requirement/Availability in MU/DAY			Requirement/Availability in MU				Peak Demand/Peak Met in MW			
		Requirement	Energy met	Surplus(+)/Deficit(-)	Requirement	Energy met	Surplus(+)/Deficit(-)	% Shortage	Requirement	Peak Demand Met	Surplus(+)/Deficit(-)	% Shortage
NR	Chandigarh	4	4	0.0	116	116	0	0.0	304	304	0	0.0
	Delhi	75	75	0.0	2176	2176	0	0.0	5406	5406	0	0.0
	Haryana	147	147	-0.6	4273	4255	-19	-0.4	8868	8868	0	0.0
	Himachal Pradesh	36	36	-0.1	1035	1031	-4	-0.4	2133	2133	0	0.0
	J&K(UT) and Ladakh(UT)	59	58	-1.0	1703	1672	-30	-1.8	3071	3071	0	0.0
	Punjab	156	156	0.0	4518	4518	0	0.0	10307	10307	0	0.0
	Rajasthan	316	316	-0.1	9161	9157	-4	0.0	17867	17867	0	0.0
	Uttar Pradesh	320	320	0.0	9292	9291	-1	0.0	20346	19726	-620	-3.0
	Uttarakhand	43	42	-0.2	1236	1231	-5	-0.4	2523	2328	-195	-7.7
	Railway	4	4	0.0	104	104	0	0.0	201	201	0	0.0
	NFL	0	0	0.0	2	2	0	0.0	4	4	0	0.0
	TOTAL	1159	1157	-2.2	33616	33554	-63	-0.2	63481	63481	0	0.0
WR	Gujarat	406	406	0.0	11786	11786	0	0.0	21248	21248	0	0.0
	Madhya Pradesh	298	296	-1.5	8635	8591	-44	-0.5	16998	16992	-6	0.0
	Chhattisgarh	119	119	-0.1	3457	3453	-4	-0.1	5819	5813	-6	-0.1
	Maharashtra	592	592	0.0	17182	17182	0	0.0	28969	28969	0	0.0
	Goa	13	13	0.0	378	378	0	0.0	749	749	0	0.0
	DNHDDPDCL	29	29	0.0	843	843	0	0.0	1304	1304	0	0.0
	AMNSIL	19	19	0.0	547	547	0	0.0	926	926	0	0.0
	BALCO	12	12	0.0	361	361	0	0.0	525	525	0	0.0
	TOTAL	1489	1488	-1.6	43189	43141	-48	-0.1	74397	73830	-567	-0.8
SR	Andhra Pradesh	230	230	0.0	6658	6658	0	0.0	12216	12216	0	0.0
	Telangana	274	275	0.4	7957	7968	11	0.1	13828.825	13810	-19	-0.1
	Karnataka	304	304	0.4	8812	8823	11	0.1	16632	16632	0	0.0
	Kerala	89	89	0.1	2583	2587	4	0.1	4841	4841	0	0.0
	Tamil Nadu	359	359	0.5	10404	10419	14	0.1	17044.81	17035	-10	-0.1
	Puducherry	9	9	0.0	269	269	0	0.2	453	453	0	0.0
	TOTAL	1265	1266	1.4	36683	36723	40	0.1	65840	65820	-20	0.0
ER	Bihar	89	88	-0.3	2575	2566	-9	-0.4	5190	5190	0	0.0
	Jharkhand	36	35	-1.5	1051	1008	-43	-4.1	1756	1756	0	0.0
	DVC	71	71	0.0	2052	2052	0	0.0	3291	3291	0	0.0
	Odisha	104	104	0.0	3029	3029	0	0.0	5421	5421	0	0.0
	West Bengal	151	151	0.0	4374	4374	0	0.0	7522	7522	0	0.0
	Sikkim	2	2	0.0	57	57	0	0.0	128	128	0	0.0
	Railways_ER ISTS	0	0	0.0	4	4	0	0.0	23	23	0	0.0
	TOTAL	453	451	-1.8	13142	13090	-52	-0.4	23650	23650	0	0.0
NER	Arunachal Pradesh	3	3	0.0	89	89	0	0.0	186	186	0	0.0
	Assam	28	28	-0.4	817	804	-13	-1.5	1634	1634	0	0.0
	Manipur	3	3	-0.2	91	86	-4	-4.9	252	235	-17	-6.7
	Meghalaya	6	6	0.0	188	188	0	0.0	399	399	0	0.0
	Mizoram	2	2	0.0	64	64	0	0.0	155	155	0	0.0
	Nagaland	2	2	0.0	69	69	0	0.0	156	156	0	0.0
	Tripura	4	4	0.0	109	109	0	0.0	261	261	0	0.0
	TOTAL	49	49	-0.6	1428	1410	-17	-1.2	2861	2861	0	0.0
ALL INDIA		4416	4411	-4.8	128058	127919	-140	-0.1				

NOTE: BASED ON THE DATA FURNISHED BY ENTITIES ON DAILY BASIS

12. ENERGY COMPARISON OF FEBRUARY 2024 vs FEBRUARY 2023

REGION	STATE	Energy Requirement (MU)					Energy Met (MU)				
		Feb-23	Feb-24	Difference	% Change	Average MU/day for Feb-24	Feb-23	Feb-24	Difference	% Change	Average MU/day for Feb-24
NR	Chandigarh	97	116	19	19	4	97	116	19	19	4
	Delhi	1903	2176	273	14	75	1903	2176	273	14	75
	Haryana	3945	4273	328	8	147	3929	4255	326	8	147
	Himachal Pradesh	906	1035	129	14	36	902	1031	129	14	36
	J&K(UT) and Ladakh(UT)	1669	1703	34	2	59	1665	1672	8	0	58
	Punjab	4240	4518	278	7	156	4198	4518	320	8	156
	Rajasthan	8570	9161	591	7	316	8325	9157	832	10	316
	Uttar Pradesh	9053	9292	239	3	320	9033	9291	259	3	320
	Uttarakhand	1133	1236	104	9	43	1111	1231	120	11	42
	Railway/NFL	87	106	19	22	4	87	106	19	22	4
	TOTAL	31603	33616	2013	6	1159	31249	33554	2304	7	1157
WR	Gujarat	10973	11786	812	7	406	10973	11786	812	7	406
	Madhya Pradesh	8419	8635	216	3	298	8394	8591	197	2	296
	Chhattisgarh	3156	3457	301	10	119	3147	3453	306	10	119
	Maharashtra	15703	17182	1479	9	592	15702	17182	1479	9	592
	Goa	389	378	-10	-3	13	388	378	-10	-3	13
	DNHDDPDCL	793	843	51	6	29	793	843	51	6	29
	AMNSIL	498	547	49	10	19	498	547	49	10	19
	BALCO	345	361	16	5	12	345	361	16	5	12
	TOTAL	40275	43189	2914	7	1489	40241	43141	2900	7	1488
SR	Andhra Pradesh	6203	6658	455	7	230	6185	6658	473	8	230
	Telangana	7514	7957	443	6	274	7493	7968	475	6	275
	Karnataka	7539	8812	1273	17	304	7517	8823	1306	17	304
	Kerala	2241	2583	343	15	89	2233	2587	354	16	89
	Tamil Nadu	8956	10404	1449	16	359	8926	10419	1492	17	359
	Puducherry	242	269	27	11	9	241	269	28	12	9
	TOTAL	32694	36683	3989	12	1265	32595	36723	4128	13	1266
ER	Bihar	2496	2575	79	3	89	2477	2566	89	4	88
	Jharkhand	850	1051	202	24	36	780	1008	228	29	35
	DVC	2095	2052	-43	-2	71	2095	2052	-43	-2	71
	Odisha	2987	3029	42	1	104	2987	3029	42	1	104
	West Bengal	4142	4374	232	6	151	4141	4374	233	6	151
	Sikkim	52	57	5	9	2	52	57	5	9	2
	Railways_ER ISTS		4	-	-	0		4	-	-	0
	TOTAL	12620	13142	522	4	453	12531	13090	559	4	451
NER	Arunachal Pradesh	77	89	12	15	3	77	89	12	15	3
	Assam	751	817	66	9	28	744	804	60	8	28
	Manipur	84	91	7	8	3	83	86	3	4	3
	Meghalaya	188	188	0	0	6	188	188	0	0	6
	Mizoram	55	64	9	16	2	55	64	9	16	2
	Nagaland	59	69	10	16	2	59	69	10	16	2
	Tripura	109	109	1	1	4	109	109	1	1	4
	TOTAL	1323	1428	104	8	49	1316	1410	94	7	49
ALL INDIA		118516	128058	9542	8	4416	117932	127919	9987	8	4411

13. DEMAND COMPARISON OF FEBRUARY 2024 vs FEBRUARY 2023

REGION	STATE	Peak Requirement (MW)				Peak Met (MW)			
		Feb-23	Feb-24	Difference	% Change	Feb-23	Feb-24	Difference	% Change
NR	Chandigarh	295	304	9	3.1	295	304	9	3.1
	Delhi	4667	5406	739	15.8	4667	5406	739	15.8
	Haryana	8570	8868	298	3.5	8570	8868	298	3.5
	Himachal Pradesh	1977	2133	156	7.9	1977	2133	156	7.9
	J&K(UT) and Ladakh(UT)	3044	3071	27	0.9	3044	3071	27	0.9
	Punjab	8864	10307	1443	16.3	8864	10307	1443	16.3
	Rajasthan	16754	17867	1113	6.6	16754	17867	1113	6.6
	Uttar Pradesh	18602	20346	1744	9.4	18602	19726	1124	6.0
	Uttarakhand	2368	2523	155	6.5	2218	2328	110	5.0
	Railway/NFL	172	205	33	19.2	172	205	33	19.2
WR	Gujarat	19185	21248	2063	11	19185	21248	2063	10.8
	Madhya Pradesh	15875	16998	1123	7	15858	16992	1134	7.2
	Chhattisgarh	5326	5819	493	9	5326	5813	487	9.1
	Maharashtra	28519	28969	450	2	28499	28969	470	1.6
	Goa	689	749	60	9	688	749	61	8.9
	DNHDDPDCL	1278	1304	26	2.0	1278	1304	26	2.0
	AMNSIL	861	926	65	7.6	861	926	65	7.6
	BALCO	527	525	-2	-0.4	527	525	-2	-0.4
SR	Andhra Pradesh	11980	12216	236	2.0	11980	12216	236	2.0
	Telangana	14812	13829	-983	-6.6	14794	13810	-984	-6.7
	Karnataka	15543	16632	1089	7.0	15543	16632	1089	7.0
	Kerala	4214	4841	627	14.9	4210	4841	631	15.0
	Tamil Nadu	16783	17045	262	1.6	16783	17035	252	1.5
	Puducherry	413	453	40	9.7	413	453	40	9.7
ER	Bihar	5326	5190	-136	-2.5	4857	5190	333	6.9
	Jharkhand	1915	1756	-159	-8.3	1561	1756	195	12.5
	DVC	3481	3291	-190	-5.5	3481	3291	-190	-5.5
	Odisha	5538	5421	-117	-2.1	5538	5421	-117	-2.1
	West Bengal	7630	7522	-108	-1.4	7630	7522	-108	-1.4
	Sikkim	122	128	6	4.9	122	128	6	4.9
	Railways_ER ISTS*		23	23	-		23	23	-
NER	Arunachal Pradesh	159	186	27	17.0	159	186	27	17.0
	Assam	1572	1634	62	3.9	1572	1634	62	3.9
	Manipur	225	252	27	12.0	225	235	10	4.4
	Meghalaya	394	399	5	1.3	394	399	5	1.3
	Mizoram	139	155	16	11.5	139	155	16	11.5
	Nagaland	148	156	8	5.4	148	156	8	5.4
	Tripura	252	261	9	3.6	252	261	9	3.6

14. SCHEDULE AND DRAWAL OF CONSTITUENTS - FEBRUARY 2024

REGION	STATE	SCHEDULE (MU)	ACTUAL DRAWAL (MU)	Over drawal(+)/ Under Drawal(-) (MU)	% OD/UD	SCHEDULE (MU/DAY)	ACTUAL DRAWAL (MU/DAY)	Over drawal(+)/ Under Drawal(-) (MU/DAY)
NR	Chandigarh	120.00	118.83	-1.17	-0.97	4.14	4.10	-0.04
	Delhi	1860.44	1844.85	-15.59	-0.84	64.15	63.62	-0.54
	Haryana	2821.47	2792.34	-29.13	-1.03	97.29	96.29	-1.00
	Himachal Pradesh	893.84	908.40	14.56	1.63	30.82	31.32	0.50
	J&K(UT) and Ladakh(UT)	1562.53	1558.96	-3.57	-0.23	53.88	53.76	-0.12
	Punjab	1872.28	1832.11	-40.17	-2.15	64.56	63.18	-1.39
	Rajasthan	3142.05	3040.07	-101.98	-3.25	108.35	104.83	-3.52
	Uttar Pradesh	2371.63	2343.20	-28.43	-1.20	81.78	80.80	-0.98
	Uttarakhand	910.53	913.10	2.57	0.28	31.40	31.49	0.09
	Railway	102.26	104.19	1.93	1.89	3.53	3.59	0.07
	NFL	2.09	2.05	-0.04	-2.10	0.07	0.07	0.00
	Total	15659.12	15458.10	-201.02	-1.28	539.97	533.04	-6.93
WR	Gujarat	4446.49	4423.96	-22.53	-0.51	153.33	152.55	-0.78
	Madhya Pradesh	5350.68	5261.79	-88.89	-1.66	184.51	181.44	-3.07
	Chhattisgarh	1636.94	1616.64	-20.30	-1.24	56.45	55.75	-0.70
	Maharashtra	5280.54	5218.46	-62.08	-1.18	182.09	179.95	-2.14
	Goa	395.87	372.73	-23.14	-5.84	13.65	12.85	-0.80
	DNHDDPDCL	844.74	843.20	-1.54	-0.18	29.13	29.08	-0.05
	AMNSIL	255.51	257.78	2.27	0.89	8.81	8.89	0.08
	BALCO*	362.09	361.33	-0.76	-0.21	12.49	12.46	-0.03
	Total	18572.86	18355.90	-216.96	-1.17	640.44	632.96	-7.48
SR	Andhra Pradesh	2476.03	2456.15	-19.88	-0.80	85.38	84.69	-0.69
	Telangana	4105.12	4094.88	-10.24	-0.25	141.56	141.20	-0.35
	Karnataka	3975.35	3973.94	-1.41	-0.04	137.08	137.03	-0.05
	Kerala	2064.22	2100.17	35.95	1.74	71.18	72.42	1.24
	Tamil Nadu	5352.22	5342.38	-9.84	-0.18	184.56	184.22	-0.34
	Puducherry	261.70	255.01	-6.69	-2.56	9.02	8.79	-0.23
	Goa (SR)	62.90	62.32	-0.58	-0.92	2.17	2.15	-0.02
	Total	18297.54	18284.85	-12.69	-0.07	630.95	630.51	-0.44
ER	Bihar	2254.28	2231.92	-22.36	-0.99	77.73	76.96	-0.77
	Jharkhand	647.40	646.14	-1.25	-0.19	22.32	22.28	-0.04
	DVC	-1369.95	-1357.40	12.55	-0.92	-47.24	-46.81	0.43
	Odisha	643.79	600.04	-43.75	-6.80	22.20	20.69	-1.51
	West Bengal	589.10	532.03	-57.07	-9.69	20.31	18.35	-1.97
	Sikkim	56.83	57.02	0.19	0.33	1.96	1.97	0.01
	Railways_ER ISTS*	4.14	4.12	-0.02	-0.41	0.14	0.14	0.00
	Total	2825.60	2713.88	-111.72	-3.95	97.43	93.58	-3.85
NER	Arunachal Pradesh	82.60	86.64	4.04	4.89	2.85	2.99	0.14
	Assam	636.16	652.91	16.75	2.63	21.94	22.51	0.58
	Manipur	85.83	86.43	0.60	0.70	2.96	2.98	0.02
	Meghalaya	158.96	154.51	-4.45	-2.80	5.48	5.33	-0.15
	Mizoram	49.14	46.58	-2.56	-5.21	1.69	1.61	-0.09
	Nagaland	69.02	66.90	-2.12	-3.07	2.38	2.31	-0.07
	Tripura	100.90	97.17	-3.73	-3.70	3.48	3.35	-0.13
	Total	1182.61	1191.14	8.53	0.72	40.78	41.07	0.29
All India Total		56537.73	56003.87	-533.86	-0.94	1949.58	1931.17	-18.41

15. INTER REGIONAL EXCHANGES 2023-24 (All figures in MU)												
	Apr'23	May'23	June'23	July'23	Aug'23	Sep'23	Oct'23	Nov'23	Dec'23	Jan'24	Feb'24	Fin. Year 2023-24
Name of Line												
Import of NR from WR (WR-NR)												
WR - NR 765 kV Gwalior - Agra 2x5/C	635.95	996.71	863.68	972.77	772.12	902.82	479.75	675.87	1109.33	1292.73	685.48	9387.21
WR-NR 765 kV Gwalior - Phagi 2x5/C	553.05	453.93	342.56	671.61	397.70	687.31	582.69	906.94	1039.97	857.36	683.53	7176.65
WR-NR 765 kV Jabalpur-Orai D/C	430.29	804.53	778.33	964.77	658.94	991.15	602.03	622.44	986.15	1084.38	544.06	8467.07
WR-NR 765 kV Satna-Orai	505.37	598.85	574.83	615.77	543.29	593.66	548.69	623.24	692.79	691.06	560.49	6548.04
WR-NR 765 kV Gwalior-Orai	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
WR - NR HVDC Champa - Kurukshetra	804.26	1126.68	2069.11	2235.18	1955.13	2230.56	739.22	674.04	450.87	1556.24	1385.18	15226.47
WR - NR HVDC Vindhyachal	0.49	3.23	3.13	94.78	21.55	7.26	50.51	28.33	18.10	26.05	0.00	253.43
WR - NR 400 kV Zerda Kankroli	0.00	0.00	1.48	15.36	13.10	8.58	0.00	1.30	3.11	9.71	1.89	54.53
WR - NR 400 kV Zerda Bhinmal	0.00	0.00	0.00	12.54	13.56	23.81	0.34	3.28	11.42	20.30	0.35	85.60
WR - NR 400 kV RAPP C - Shujalpur D/C	2.28	31.04	16.05	164.49	80.51	147.53	18.12	25.82	78.97	145.10	15.75	725.66
WR - NR 220 kV Bhanpura - Ranpur	9.67	65.53	68.13	70.02	74.29	61.03	65.71	43.01	33.94	38.18	5.64	535.15
WR - NR 220 kV Bhanpura - Modak	0.00	0.00	0.00	0.00	0.00	38.00	62.92	72.56	72.98	34.77	11.48	292.71
WR - NR 220 kV Auraiya - Malanpur/Mehgaon	0.00	0.15	0.00	0.00	0.00	0.00	0.00	0.00	0.71	0.00	0.00	0.86
WR - NR 400 kV Vindhyachal-Rihand D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.47	0.00	0.47
WR - NR HVDC Mundra - Mohindergarh	132.55	340.75	234.27	124.89	667.23	827.57	920.93	511.53	563.55	931.29	547.02	5801.58
WR-NR 765 kV Banaskata-Chittorgarh D/C	0.00	3.26	16.02	169.31	260.02	66.60	0.00	4.54	27.97	46.56	22.32	616.60
WR-NR 765 kV Varanasi-Vindhyachal	1030.05	1663.34	1854.30	1854.38	1551.38	1697.01	1174.50	1049.13	1321.93	1485.20	629.64	15310.86
Total WR - NR	4103.96	6088.00	6821.89	7965.87	7008.82	8282.89	5245.41	5242.03	6411.79	8219.40	5092.83	70482.89
Export of NR to WR (NR-WR)												
NR - WR 765 kV Gwalior - Agra 2x5/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
NR - WR 765 kV Gwalior - Phagi 2x5/C	0.00	5.41	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	5.41
NR - WR 765 kV Jabalpur-Orai D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
NR - WR 765 kV Satna-Orai	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
NR - WR 765 kV Gwalior-Orai	440.87	385.11	301.32	367.88	368.83	385.80	399.85	459.18	533.25	500.66	435.25	4578.00
NR - WR HVDC Champa - Kurukshetra	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
NR - WR HVDC Vindhyachal	289.83	273.88	267.04	184.43	225.73	180.86	26.34	219.10	161.65	131.32	230.46	2190.64
NR - WR 400 kV Zerda Kankroli	185.75	94.43	108.34	24.78	31.17	41.36	96.48	75.31	44.39	13.91	39.18	755.10
NR - WR 400 kV Zerda Bhinmal	282.42	181.64	200.56	73.76	74.62	64.65	158.50	60.27	38.76	19.27	89.32	1243.77
NR - WR 400 kV RAPP C - Shujalpur D/C	85.74	45.64	45.64	0.00	3.36	0.00	46.93	23.25	0.00	0.00	88.00	338.56
NR - WR 220 kV Bhanpura - Ranpur	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	27.59	27.59
NR - WR 220 kV Bhanpura - Modak	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	11.30	2.66	13.96
NR - WR 220 kV Auraiya - Malanpur/Mehgaon	56.56	28.58	50.82	47.16	97.78	68.03	111.08	74.65	30.32	32.76	65.50	663.24
NR-WR 400 kV Rihand-Vindhyachal D/C	644.30	672.49	642.32	664.33	653.25	658.85	669.33	655.41	657.92	560.83	319.58	6798.61
NR - WR HVDC Mundra - Mohindergarh	243.86	54.36	36.25	94.16	0.00	0.00	0.00	0.00	0.00	0.00	0.00	428.63
NR - WR 765 kV Banaskata-Chittorgarh D/C	976.83	428.19	421.52	94.53	51.63	180.84	597.81	524.56	292.98	164.35	222.27	3955.51
NR-WR 765 kV Varanasi-Vindhyachal	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Total NR - WR	3206.16	2169.73	2073.81	1551.03	1506.37	1580.39	2106.32	2091.73	1759.27	1434.40	1519.81	20999.02

	Apr'23	May'23	June'23	July'23	Aug'23	Sep'23	Oct'23	Nov'23	Dec'23	Jan'24	Feb'24	Fin. Year 2023-24
Name of Line												
Import of NR from ER (ER-NR)												
ER - NR 765 kV Sasaram - Fatehpur	166.02	114.36	82.57	74.16	131.29	131.20	192.41	301.01	254.85	260.73	320.01	2028.61
ER - NR 765 kV Gaya - Varanasi 2*5/C	224.56	107.46	28.46	47.20	75.64	115.88	182.55	439.13	474.87	419.93	546.17	2661.85
ER - NR 765 kV Gaya - Balia	246.38	335.46	321.28	300.74	224.31	332.43	250.12	325.32	373.66	432.02	272.37	3414.09
ER - NR HVDC Alipurduar - Agra	0.00	0.00	375.05	784.99	444.13	750.81	497.43	168.00	0.00	1.34	0.00	3021.75
ER-NR 400 kV Patna - Balia D/C	219.16	246.32	242.35	242.23	300.66	262.01	203.70	186.43	90.17	338.23	443.37	2774.63
ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	127.03	223.63	277.35	376.44	415.21	330.20	255.04	312.10	270.56	284.40	179.74	3051.70
ER - NR 400 kV Biharshariff - Balia D/C	22.11	72.32	102.97	92.77	101.30	90.47	56.79	138.97	145.18	163.30	59.71	1045.89
ER - NR 400 kV Motihari - Gorakhpur D/C	156.88	188.70	180.09	228.59	251.16	190.46	142.10	216.07	233.85	268.64	240.45	2296.99
ER - NR 400 kV Biharshariff - Varanasi D/C	67.56	47.21	34.66	24.65	44.14	47.88	63.00	164.47	171.28	183.46	181.32	1029.63
ER - NR 400 kV Sasaram -Varanasi	74.99	38.68	46.09	55.64	28.71	57.56	16.47	4.09	2.63	7.91	5.60	338.37
ER - NR 400 kV Sasaram -Allahabad	51.91	33.39	21.29	28.77	17.25	52.61	27.20	32.87	36.28	31.03	25.33	357.93
ER - NR 220 kV Sahupuri-Karamnasa	78.64	82.22	82.32	43.45	51.19	29.26	36.16	53.46	34.10	44.57	40.86	576.23
ER - NR 132 kV Sahupuri - Karamnasa	1.92	0.00	0.96	1.12	0.96	2.02	3.28	5.11	1.62	1.44	3.84	22.27
ER - NR 132 kV 132 kV Rihand - Nagar Untari	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
ER - NR 132 kV Rihand - Garhwa	0.46	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.18	0.00	0.00	0.64
ER-NR 400 kV Naubatpur - Balia D/C	211.13	243.59	239.56	236.53	300.12	264.57	198.04	328.08	343.58	353.99	156.20	2875.39
Total ER-NR	1648.75	1733.34	2035.00	2537.28	2386.07	2657.36	2124.29	2675.11	2432.81	2790.99	2474.97	25495.97
Import of NR from NER (NER-NR)												
NER-NR HVDC Biswanath Chariali - Agra	0.00	0.00	153.62	339.28	465.76	447.38	470.05	190.40	0.00	0.00	0.00	2066.49
Total NER - NR	0.00	0.00	153.62	339.28	465.76	447.38	470.05	190.40	0.00	0.00	0.00	2066.49
Export of NR to ER (NR-ER)												
NR - ER 765 kV Sasaram - Fatehpur	0.00	2.65	7.74	3.45	0.00	4.62	0.00	0.00	0.00	0.00	0.00	18.46
NR - ER 765 kV Gaya - Varanasi 2*5/C	0.30	38.74	102.98	45.94	11.70	32.51	8.41	1.45	0.00	0.00	0.00	242.03
NR - ER 765 kV Gaya - Balia	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
NR - ER HVDC Alipurduar - Agra	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
NR - ER 400 kV Patna - Balia 2xD/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
NR - ER 400 kV Muzaffarpur - Gorakhpur D/C	3.47	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	3.47
NR - ER 400 kV Biharshariff - Balia D/C	17.15	4.18	13.06	0.00	0.00	3.12	4.14	0.75	0.00	0.00	0.61	43.01
ER - NR 400 kV Motihari - Gorakhpur D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
NR - ER 400 kV Biharshariff - Varanasi D/C	2.90	7.31	20.53	10.39	0.22	12.39	4.69	0.00	0.00	0.00	0.00	58.43
NR - ER 400 kV Sasaram -Varanasi	0.00	0.00	0.00	0.00	1.67	0.00	0.85	5.47	4.05	3.29	2.61	17.94
NR - ER 400 kV Sasaram -Allahabad	2.25	0.00	0.00	0.82	2.28	0.00	0.23	0.00	0.00	0.24	0.72	6.54
NR - ER 220 kV Sahupuri-Karamnasa	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
NR - ER 132 kV Sahupuri - Karamnasa	0.01	0.96	0.48	0.96	0.00	0.58	0.48	0.00	1.44	0.96	1.44	7.31
NR - ER 132 kV 132 kV Rihand - Nagar Untari	1.74	2.20	1.08	3.37	2.39	3.46	1.80	2.75	0.00	1.23	0.20	20.22
ER - NR 132 kV Rihand - Garhwa	10.23	8.48	19.67	18.35	14.38	11.19	11.51	8.39	4.64	12.89	13.67	133.40
NR-ER 400 kV Balia- Naubatpur D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Total NR - ER	38.05	64.52	165.54	83.28	32.64	67.87	32.11	18.81	10.13	18.61	19.25	550.81
Export of NR to NER (NER-NR)												
NR-NER HVDC Biswanath Chariali - Agra	261.93	291.71	104.47	0.00	0.00	0.00	0.00	257.02	0.00	486.81	502.32	1904.26
Total NR - NER	261.93	291.71	104.47	0.00	0.00	0.00	0.00	257.02	0.00	486.81	502.32	1904.26

	Apr'23	May'23	June'23	July'23	Aug'23	Sep'23	Oct'23	Nov'23	Dec'23	Jan'24	Feb'24	Fin. Year 2023-24
Name of Line												
Export of WR to ER (WR-ER)												
WR - ER 765 kV Ranchi - Dharamjaygarh 2x5/C	139.81	504.96	673.15	734.00	331.39	537.29	228.34	42.77	55.89	144.01	12.73	3404.34
WR - ER 765 kV Dharamjaygarh - Jharsuguda 2xD/C	652.31	469.82	490.99	593.61	768.89	177.22	238.94	52.91	224.71	96.99	168.60	3934.99
WR - ER 765 kV Durg - Jharsuguda D/C	0.00	0.64	1.75	26.78	7.42	1.32	0.00	0.00	0.00	0.00	0.00	37.91
WR - ER 400 kV Sipat - Ranchi D/C	15.97	93.84	118.29	133.75	52.57	87.51	30.29	8.20	13.05	16.97	0.75	571.20
WR - ER 400 kV Raigarh - Jharsuguda 2xD/C	0.44	6.23	8.79	6.26	28.69	11.41	0.82	0.78	0.99	0.01	0.00	64.42
WR - ER 220 kV Korba - Budhipadar D/C	36.08	80.04	73.19	22.96	28.75	29.18	26.25	36.70	47.92	14.51	10.54	406.12
WR - ER 220 kV Raigarh - Budhipadar	0.15	0.57	1.17	0.00	0.35	0.34	0.00	0.08	2.74	0.06	0.00	5.46
Total WR - ER	844.75	1156.11	1367.33	1517.34	1218.07	844.29	524.64	141.44	345.30	272.55	192.63	8424.45
Import of WR from ER (ER - WR)												
ER - WR 765 kV Ranchi - Dharamjaygarh 2x5/C	144.10	11.95	15.57	10.81	83.69	14.84	62.72	294.10	166.96	114.80	421.37	1340.92
ER - WR 765 kV Dharamjaygarh - Jharsuguda 2XD/C	25.46	58.29	33.08	15.65	2.33	214.83	131.20	338.83	241.82	386.37	174.98	1622.84
ER - WR 765 kV Durg - Jharsuguda D/C	394.08	204.42	148.02	71.84	73.64	163.98	298.15	464.99	456.27	465.79	397.81	3138.99
ER - WR 400 kV Sipat - Ranchi D/C	55.56	5.71	9.07	7.22	29.65	8.91	40.59	105.31	60.55	61.48	151.92	535.96
ER - WR 400 kV Raigarh - Jharsuguda 2xD/C	248.78	148.94	125.69	125.00	127.87	110.94	267.35	221.93	208.02	310.82	371.43	2266.77
ER - WR 220 kV Korba - Budhipadar D/C	1.45	0.00	0.14	6.23	1.99	1.46	3.18	3.22	2.35	33.09	17.42	70.52
ER - WR 220 kV Raigarh - Budhipadar	55.98	38.46	41.41	66.29	74.76	49.37	81.54	41.32	24.30	48.09	73.44	594.95
Total ER - WR	925.41	467.76	372.98	303.04	393.92	564.32	884.73	1469.71	1160.27	1420.43	1608.37	9570.95
Export of ER to NER (ER - NER)												
ER - NER 400 kV Binaguri - Bongaigaon D/C	6.99	16.15	105.81	142.19	71.19	215.10	134.98	60.68	0.64	4.12	6.09	763.94
ER - NER 400 kV Alipurduar - Bongaigaon D/C	4.62	34.31	135.94	83.03	84.82	161.59	95.15	85.48	0.00	1.71	2.63	689.27
ER - NER 220 kV Birpara - Salakati D/C	0.54	3.12	31.19	37.25	25.19	47.94	25.71	15.50	0.00	0.38	0.45	187.26
Total ER - NER	12.16	53.58	272.93	262.48	181.20	424.63	255.83	161.66	0.64	6.20	9.16	1640.46
Import of ER from NER (NER - ER)												
NER - ER 400 kV Binaguri - Bongaigaon D/C	52.83	40.19	37.75	2.10	10.62	0.07	5.53	48.07	75.32	53.10	17.90	343.49
NER - ER 400 kV Alipurduar - Bongaigaon D/C	182.37	135.22	72.81	20.59	29.76	3.08	23.52	172.08	294.27	231.86	141.39	1306.95
NER - ER 220 kV Birpara - Salakati D/C	34.59	31.32	10.78	0.62	2.83	0.14	2.65	38.72	64.62	39.51	27.84	253.61
Total NER - ER	269.78	206.73	121.33	23.31	43.22	3.29	31.70	258.87	434.22	324.47	187.14	1904.06
Export of ER to SR (ER - SR)												
ER - SR HVDC Gazuwaka	375.93	395.23	208.61	178.44	321.36	201.99	378.26	352.24	239.96	240.59	353.34	3245.94
ER - SR HVDC Talchar - Kolar	1233.20	1204.28	984.75	977.61	1284.58	1076.42	1294.48	1214.02	1257.33	611.06	993.37	12131.09
ER - SR 765 kV Angul- Srikakulam D/C	1683.42	1561.33	1412.42	1184.37	1380.27	1160.32	1534.32	1466.97	1513.04	1468.02	1655.15	16019.65
Total ER - SR	3292.55	3160.85	2605.77	2340.42	2986.21	2438.74	3207.06	3033.23	3010.33	2319.67	3001.86	31396.69
Import of ER from SR (SR - ER)												
SR - ER HVDC Gazuwaka	0.00	0.00	55.34	114.11	32.48	0.00	0.00	6.03	0.00	0.00	0.00	207.97
SR - ER HVDC Talchar - Kolar	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.01
SR - ER 765 kV Angul- Srikakulam D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Total SR - ER	0.00	0.00	55.34	114.11	32.48	0.00	0.00	6.03	0.00	0.00	0.00	207.97

	Apr'23	May'23	June'23	July'23	Aug'23	Sep'23	Oct'23	Nov'23	Dec'23	Jan'24	Feb'24	Fin. Year 2023-24
Name of Line												
Export of WR to SR (WR-SR)												
WR - SR HVDC Bhadrawati	544.41	411.52	171.68	139.64	464.81	222.80	593.89	435.49	593.74	438.40	511.83	4528.22
WR - SR 765 kV Sholapur - Raichur 2x5/C	417.69	222.76	146.07	83.93	451.70	125.10	226.89	116.70	185.60	358.47	476.22	2811.13
WR - SR 765 kV Wardha - Nizamabad D/C	1323.51	873.44	1018.25	852.05	1313.80	864.24	1099.04	930.66	873.02	1038.49	181.65	10368.15
WR - SR 400KV Kolhapur-Kudgi D/C	0.00	0.00	0.00	0.00	0.06	0.00	0.00	0.00	0.00	0.03	0.00	0.09
WR-SR HVDC Raigarh-Pugalur	3004.35	1791.86	1182.91	885.62	2135.69	1450.16	2583.88	1858.37	1697.06	1365.48	2307.50	20262.87
WR-SR 220kV Xeldem - Ambewadi S/C	77.16	70.18	68.17	61.74	68.61	67.55	69.49	67.29	61.47	59.32	64.33	735.30
WR-SR 220kV Ponda - Ambewadi S/C	0.29	1.54	0.28	0.16	5.23	0.04	0.08	0.97	0.04	1.38	1.26	11.26
WR-SR 765 kV Warora - Warangal D/C	-	-	-	-	-	-	-	-	-	1060.47	1296.17	2356.64
Total WR - SR	5367.41	3371.30	2587.37	2023.14	4439.89	2729.89	4573.27	3409.48	3410.93	4322.03	4838.96	41073.65
Import of WR from SR (SR - WR)												
SR - WR HVDC Bhadrawati	4.11	25.09	178.09	308.60	10.36	114.86	0.00	0.00	0.00	0.00	0.00	641.13
SR - WR 765 kV Raichur - Sholapur 2x5/C	29.13	205.27	344.82	478.51	54.56	420.76	215.80	334.15	175.90	151.44	64.99	2475.32
SR - WR 765 kV Wardha - Nizamabad D/C	0.00	3.90	0.32	18.33	0.00	19.87	0.03	0.89	0.00	0.53	0.05	43.93
SR - WR 400KV Kolhapur-Kudgi D/C	623.59	719.30	784.98	796.02	623.43	850.54	765.68	701.36	642.95	615.99	577.88	7701.73
SR-WR HVDC Pugalur-Raigarh	0.00	3.73	14.87	16.65	0.00	0.09	0.00	0.00	0.00	0.00	0.00	35.33
WR-SR 220kV Ambewadi - Xeldem S/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
WR-SR 220kV Ambewadi-Ponda S/C	0.00	0.00	0.01	0.00	0.01	0.01	0.02	0.01	0.02	0.02	0.00	0.10
SR-WR 765 kV Warangal - Warora D/C	-	-	-	-	-	-	-	-	-	0.26	0.00	0.26
Total SR - WR	656.84	957.30	1323.09	1618.10	688.36	1406.13	981.53	1036.41	818.88	768.24	642.92	10897.80
TOTAL ALL INDIA	20628	19721	20060	20679	21383	21447	20437	19992	19795	22384	20090	226615
*In case of mutiple ckt / DC pole year corres. to the commissioning of final element												

Date	15.1 Import-Export of NR with WR during February 2024																	
	Import of NR from WR (WR-NR)																	
	WR - NR 765 kV Gwalior - Agra 2x5/C	WR-NR 765 kV Gwalior-Phagi 2x5/C	WR-NR 765 kV Jabalpur- Orai D/C	WR-NR 765 kV Satna- Orai	WR-NR 765 kV Gwalior-Orai	WR - NR HVDC Champa- Kurukshetra	WR - NR HVDC Vindhyachal	WR - NR 400 kV Zerda- Kankroli	WR - NR 400 kV Zerda- Bhinmal	WR-NR 400 kV RAPP C - Shujalpur D/C	WR - NR 220 kV Bhanpura - Ranpur	WR - NR 220 kV Bhanpura - Modak	WR - NR 220 kV Auraiya - Malanpur / Mehgaon	WR-NR 400 kV Rihand Vindhyachal D/C	WR - NR HVDC Mundra - M'garh	WR - NR 765 kV Banaskata - Chittorgarh D/C	WR-NR 765 kV Varanasi- Vindhyachal	Total WR - NR
1-Feb-24	14.89	24.64	17.13	16.57	0.00	82.90	0.00	0.00	0.00	0.00	0.86	0.00	0.00	0.00	15.72	0.00	26.30	199.01
2-Feb-24	26.57	26.64	19.67	20.45	0.00	72.02	0.00	0.00	0.00	0.57	1.46	0.00	0.00	0.00	14.89	0.00	33.10	215.37
3-Feb-24	29.91	34.40	21.69	22.69	0.00	69.77	0.00	0.00	0.00	3.97	1.42	1.30	0.00	0.00	12.18	0.00	32.30	229.63
4-Feb-24	28.20	31.13	27.35	18.78	0.00	56.91	0.00	0.00	0.00	2.46	1.35	0.73	0.00	0.00	12.18	0.00	32.72	211.81
5-Feb-24	24.77	27.39	28.77	18.88	0.00	46.98	0.00	0.00	0.00	0.00	0.18	0.92	0.00	0.00	12.18	0.00	29.08	189.15
6-Feb-24	22.86	29.34	23.68	17.28	0.00	51.40	0.00	0.00	0.00	0.32	0.00	0.92	0.00	0.00	16.40	0.00	24.20	186.40
7-Feb-24	22.48	26.41	20.92	18.28	0.00	47.24	0.00	0.00	0.00	0.00	0.00	0.99	0.00	0.00	28.79	0.00	20.02	185.13
8-Feb-24	22.68	21.26	16.98	18.65	0.00	50.41	0.00	0.07	0.00	0.00	0.00	1.24	0.00	0.00	19.82	1.16	22.55	174.82
9-Feb-24	22.01	23.80	16.77	17.57	0.00	71.89	0.00	0.00	0.00	0.00	0.00	0.66	0.00	0.00	12.18	0.00	18.50	183.38
10-Feb-24	26.48	27.39	21.75	18.64	0.00	70.93	0.00	0.00	0.00	1.14	0.00	1.15	0.00	0.00	12.18	0.00	21.19	200.85
11-Feb-24	27.94	26.88	21.37	20.58	0.00	47.87	0.00	0.00	0.00	1.32	0.00	1.17	0.00	0.00	10.96	0.00	28.95	187.04
12-Feb-24	33.95	34.03	29.37	21.13	0.00	54.10	0.00	0.00	0.00	3.61	0.37	1.06	0.00	0.00	7.36	0.00	32.95	217.93
13-Feb-24	30.85	30.87	24.95	20.15	0.00	46.58	0.00	0.00	0.00	2.36	0.00	0.00	0.00	0.00	10.99	0.00	30.00	196.75
14-Feb-24	27.74	21.68	19.92	18.92	0.00	44.20	0.00	0.24	0.00	0.00	0.00	0.41	0.00	0.00	20.26	1.96	29.20	184.53
15-Feb-24	27.22	19.99	19.60	18.85	0.00	47.41	0.00	0.58	0.00	0.00	0.00	0.07	0.00	0.00	24.23	1.74	24.91	184.60
16-Feb-24	27.40	20.89	19.60	19.10	0.00	48.75	0.00	1.00	0.35	0.00	0.00	0.10	0.00	0.00	21.13	4.91	23.00	186.23
17-Feb-24	26.40	27.97	20.60	19.60	0.00	59.29	0.00	0.00	0.00	0.00	0.00	0.13	0.00	0.00	22.91	0.00	22.70	199.60
18-Feb-24	20.90	21.60	15.62	18.16	0.00	47.24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	18.00	0.00	20.44	161.96
19-Feb-24	20.49	10.24	9.29	16.66	0.00	36.01	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	21.80	6.34	20.29	141.12
20-Feb-24	15.76	20.97	11.69	17.38	0.00	24.20	0.00	0.00	0.00	0.00	0.00	0.18	0.00	0.00	27.22	0.00	11.65	129.05
21-Feb-24	14.95	18.15	4.82	18.51	0.00	28.90	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	24.23	0.00	7.98	117.54
22-Feb-24	15.34	21.84	11.92	18.62	0.00	31.58	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	22.86	0.00	0.76	122.92
23-Feb-24	20.05	19.80	14.67	19.88	0.00	35.84	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	22.18	0.00	3.23	135.65
24-Feb-24	18.47	22.96	15.91	21.27	0.00	36.08	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	18.54	0.00	6.76	139.99
25-Feb-24	22.58	23.08	17.91	20.52	0.00	35.02	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	17.55	0.00	12.85	149.51
26-Feb-24	26.40	23.16	20.44	20.89	0.00	34.86	0.00	0.00	0.00	0.00	0.00	0.38	0.00	0.00	23.91	1.34	17.93	169.31
27-Feb-24	23.38	11.98	15.73	20.07	0.00	36.06	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	28.71	4.87	24.85	165.65
28-Feb-24	22.10	15.31	16.21	21.13	0.00	35.77	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	26.68	0.00	24.76	161.96
29-Feb-24	22.71	19.73	19.73	21.28	0.00	34.97	0.00	0.00	0.00	0.00	0.00	0.07	0.00	0.00	20.98	0.00	26.47	165.94
Total	685.48	683.53	544.06	560.49	0.00	1385.18	0.00	1.89	0.35	15.75	5.64	11.48	0.00	0.00	547.02	22.32	629.64	5092.83
Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day																		

Date	15.1 Import-Export of NR with WR during February 2024																	
	Export of NR to WR (NR- WR)																	
	NR - WR 765 kV Gwalior - Agra 2xS/C	NR-WR 765 kV Gwalior- Phagi 2xS/C	NR-WR 765 kV Jabalpur- Orai D/C	NR-WR 765 kV Satna- Orai	NR-WR 765 kV Gwalior-Orai	NR - WR HVDC Champa- Kurukshetra	NR - WR HVDC Vindhyachal	NR - WR 400 kV Zerd- Kankroli	NR - WR 400 kV Zerd- Bhinmal	NR-WR 400 kV RAPP C- Shujalpur D/C	WR - NR 220 kV Bhanpura - Ranpur	WR - NR 220 kV Bhanpura - Modak	NR - WR 220 kV Auraiya - Malanpur / Mehgaon	NR-WR 400 kV Rihand- Vindhyachal D/C	NR - WR HVDC Mundra - M'garh	NR - WR 765 kV Banaskata - Chittorgarh D/C	NR-WR 765 kV Varanasi- Vindhyachal	Total NR - WR
1-Feb-24	0.00	0.00	0.00	0.00	16.10	0.00	9.23	2.24	3.75	1.24	0.00	0.85	2.85	11.07	0.00	17.87	0.00	65.20
2-Feb-24	0.00	0.00	0.00	0.00	14.90	0.00	12.12	1.58	2.89	0.00	0.00	0.38	2.04	11.14	0.00	14.50	0.00	59.55
3-Feb-24	0.00	0.00	0.00	0.00	15.34	0.00	6.67	0.95	0.45	0.00	0.00	0.00	1.72	11.15	0.00	11.91	0.00	48.19
4-Feb-24	0.00	0.00	0.00	0.00	17.68	0.00	3.60	1.02	0.49	0.00	0.00	0.00	1.69	11.14	0.00	9.21	0.00	44.83
5-Feb-24	0.00	0.00	0.00	0.00	13.48	0.00	7.23	2.95	4.95	0.60	0.00	0.00	1.65	10.91	0.00	20.87	0.00	62.64
6-Feb-24	0.00	0.00	0.00	0.00	17.35	0.00	7.31	2.64	4.76	0.00	0.96	0.00	1.78	11.05	0.00	19.74	0.00	65.59
7-Feb-24	0.00	0.00	0.00	0.00	16.75	0.00	7.26	1.90	3.98	1.13	0.48	0.00	2.10	11.10	0.00	12.34	0.00	57.04
8-Feb-24	0.00	0.00	0.00	0.00	14.17	0.00	7.28	0.00	0.32	1.90	0.22	0.00	2.01	11.10	0.00	0.00	0.00	37.00
9-Feb-24	0.00	0.00	0.00	0.00	15.89	0.00	7.26	1.28	2.45	0.94	0.90	0.00	2.71	11.27	0.00	11.45	0.00	54.15
10-Feb-24	0.00	0.00	0.00	0.00	17.75	0.00	7.26	1.15	2.20	0.00	0.24	0.00	2.03	11.10	0.00	11.11	0.00	52.84
11-Feb-24	0.00	0.00	0.00	0.00	15.78	0.00	7.27	1.90	2.90	0.00	0.39	0.00	2.07	11.08	0.00	8.77	0.00	50.16
12-Feb-24	0.00	0.00	0.00	0.00	17.82	0.00	11.77	0.80	1.45	0.00	0.00	0.00	2.16	11.08	0.00	5.67	0.00	50.75
13-Feb-24	0.00	0.00	0.00	0.00	17.79	0.00	9.93	0.85	1.52	0.00	1.60	0.03	2.10	10.75	0.00	4.95	0.00	49.52
14-Feb-24	0.00	0.00	0.00	0.00	15.42	0.00	6.12	0.00	0.20	0.28	1.12	0.00	2.28	11.08	0.00	0.00	0.00	36.50
15-Feb-24	0.00	0.00	0.00	0.00	14.60	0.00	6.00	0.00	0.30	3.96	0.53	0.00	2.18	11.01	0.00	0.00	0.00	38.58
16-Feb-24	0.00	0.00	0.00	0.00	15.48	0.00	6.14	0.00	0.00	5.54	0.63	0.00	1.01	11.14	0.00	0.00	0.00	39.94
17-Feb-24	0.00	0.00	0.00	0.00	17.36	0.00	6.06	0.46	1.51	4.37	1.51	0.00	2.20	11.20	0.00	3.28	0.00	47.95
18-Feb-24	0.00	0.00	0.00	0.00	15.22	0.00	6.15	1.09	6.10	6.89	1.64	0.03	2.50	11.00	0.00	4.26	0.00	54.88
19-Feb-24	0.00	0.00	0.00	0.00	14.09	0.00	6.05	1.08	6.45	9.05	1.54	0.09	2.51	10.41	0.00	0.00	0.00	51.27
20-Feb-24	0.00	0.00	0.00	0.00	16.21	0.00	6.49	2.51	4.62	7.62	1.28	0.00	3.01	11.26	0.00	12.31	0.00	65.31
21-Feb-24	0.00	0.00	0.00	0.00	13.41	0.00	11.63	1.55	3.25	6.89	1.70	0.08	2.85	11.12	0.00	3.53	0.00	56.01
22-Feb-24	0.00	0.00	0.00	0.00	13.16	0.00	12.14	2.32	4.62	6.31	1.94	0.29	2.68	11.16	0.00	12.18	0.00	66.80
23-Feb-24	0.00	0.00	0.00	0.00	12.42	0.00	7.70	1.30	3.85	6.52	1.95	0.02	2.87	11.06	0.00	6.66	0.00	54.35
24-Feb-24	0.00	0.00	0.00	0.00	13.84	0.00	4.84	2.01	5.74	6.64	1.69	0.06	2.90	10.95	0.00	12.86	0.00	61.53
25-Feb-24	0.00	0.00	0.00	0.00	13.51	0.00	5.08	1.54	3.79	5.30	1.07	0.35	2.51	10.91	0.00	8.32	0.00	52.38
26-Feb-24	0.00	0.00	0.00	0.00	13.88	0.00	6.04	0.76	2.14	3.68	1.02	0.00	2.21	10.85	0.00	0.00	0.00	40.58
27-Feb-24	0.00	0.00	0.00	0.00	11.21	0.00	11.59	1.13	5.56	4.74	1.94	0.35	2.27	10.79	0.00	0.00	0.00	49.58
28-Feb-24	0.00	0.00	0.00	0.00	11.77	0.00	12.11	1.75	3.92	3.01	1.75	0.13	2.28	10.85	0.00	2.05	0.00	49.62
29-Feb-24	0.00	0.00	0.00	0.00	12.87	0.00	12.13	2.42	5.16	1.39	1.49	0.00	2.33	10.85	0.00	8.43	0.00	57.07
Total	0.00	0.00	0.00	0.00	435.25	0.00	230.46	39.18	89.32	88.00	27.59	2.66	65.50	319.58	0.00	222.27	0.00	1519.81
Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day																		

Date	15.2 Import-Export of NR with ER & NER during February 2024																		
	Import of NR from ER (ER-NR)																	Import of NR from NER (NER-NR)	
	ER - NR 765 kV Sasaram - Fatehpur	ER - NR 765 kV Gaya - Varanasi 2*s/C	ER - NR 765 kV Gaya Ballia	ER - NR HVDC Alipurduar - Agra	ER-NR 400 kV Patna - Ballia D/C	ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	ER - NR 400 kV Biharshariff - Ballia D/C	ER - NR 400 kV Motihari - Gorakhpur D/C	ER - NR 400 kV Biharshariff - Varanasi D/C	ER-NR 400 kV Sasaram - Varanasi	ER-NR 400 kV Sasaram - Allahabad	ER - NR 220 kV Sahupuri - Karamnasa	ER - NR 132 kV Sahupuri - Karamnasa	ER - NR 132 kV Rihand - Nagar Untari	NR - ER 132 kV Rihand - Garhwa	ER-NR 400 kV Naubatpur - Ballia D/C	Total ER - NR	NER-NR HVDC Biswanath Chariali - Agra	Total NER-NR
1-Feb-24	8.60	11.76	8.30		6.44	3.70	2.09	5.30	5.70	0.60	0.51	1.25			0.00	5.80	60.05	0.00	0.00
2-Feb-24	7.53	17.40	11.50		11.76	7.50	3.85	4.81	6.71	-0.12	1.11		2.05		0.00	7.38	81.48	0.00	0.00
3-Feb-24	11.70	20.94	12.86		14.70	9.34	5.71	10.47	6.80	0.00	1.20	1.97	0.48		0.00	5.56	101.73	0.00	0.00
4-Feb-24	8.90	15.15	11.21		12.95	7.23	3.52	9.04	4.51	0.24	0.51	1.45			0.00	6.02	80.73	0.00	0.00
5-Feb-24	9.68	13.69	10.74		11.39	7.31	3.60	8.55	4.34	0.44	0.60	1.20	0.00		0.00	5.65	77.19	0.00	0.00
6-Feb-24	10.24	17.92	10.38		12.22	7.20	3.38	8.58	5.62	0.22	0.96	1.68			0.00	5.32	83.72	0.00	0.00
7-Feb-24	11.02	17.22	8.62		18.24	6.08	1.19	8.92	5.16	0.13	0.96	1.32			0.00	4.19	83.05	0.00	0.00
8-Feb-24	9.61	16.10	8.27		12.75	4.86	0.40	7.80	3.30	0.31	0.91	1.20			0.00	3.65	69.16	0.00	0.00
9-Feb-24	10.20	16.13	7.65		11.70	4.32	0.67	7.50	4.90	0.50	0.50	1.28			0.00	3.60	68.95	0.00	0.00
10-Feb-24	10.88	20.11	5.84		8.93	5.28	0.40	7.91	4.89	0.39	0.79	1.25	0.00		0.00	4.36	71.03	0.00	0.00
11-Feb-24	9.24	13.88	8.83		12.94	5.70	0.32	8.71	3.95	0.19	0.92	1.41			0.00	4.09	70.18	0.00	0.00
12-Feb-24	10.49	17.75	8.25		13.80	6.98	1.61	7.97	4.98	0.09	1.20	1.40	0.48		0.00	4.22	79.22	0.00	0.00
13-Feb-24	10.85	16.53	9.24		15.33	5.31	1.30	8.14	5.08	0.05	1.02	1.45			0.00	4.84	79.14	0.00	0.00
14-Feb-24	9.72	15.25	10.16		16.32	3.92	2.25	7.36	5.12	0.30	0.73	1.48	0.48		0.00	5.32	78.41	0.00	0.00
15-Feb-24	9.90	17.55	9.35		15.20	4.36	1.17	7.44	5.00	0.20	0.92	1.40			0.00	4.50	76.99	0.00	0.00
16-Feb-24	11.00	18.90	9.65		14.66	6.20	2.01	8.40	6.20	0.19	0.91	1.42			0.00	4.96	84.50	0.00	0.00
17-Feb-24	11.42	19.05	9.10		15.40	6.40	2.98	8.43	5.97	0.18	0.91	1.50	0.00		0.00	4.83	86.17	0.00	0.00
18-Feb-24	10.80	18.32	8.75		14.69	6.17	2.50	7.83	5.30	0.31	0.90	1.55			0.00	4.65	81.77	0.00	0.00
19-Feb-24	8.12	14.24	7.92		12.73	4.13	0.00	4.94	3.81	0.42	0.76	1.41			0.00	3.81	62.29	0.00	0.00
20-Feb-24	11.84	20.42	8.42		15.96	6.19	3.32	6.41	9.82	0.28	0.64	1.52		0.00	0.00	6.48	91.30	0.00	0.00
21-Feb-24	13.55	22.36	8.01		20.08	5.75	1.49	9.35	8.15	0.00	1.14	1.60		0.00	0.00	6.55	98.03	0.00	0.00
22-Feb-24	13.92	23.80	8.64		20.84	5.80	1.52	9.20	9.40	0.38	0.72	1.54			0.00	6.72	102.48	0.00	0.00
23-Feb-24	13.95	24.15	9.19		19.02	5.96	1.35	9.77	8.45	0.14	0.73	1.38			0.00	6.37	100.46	0.00	0.00
24-Feb-24	14.12	28.69	9.22		19.95	8.49	2.01	10.63	7.78	0.16	1.13	1.55			0.00	6.56	110.29	0.00	0.00
25-Feb-24	15.28	27.32	11.02		23.32	8.33	3.25	10.73	9.66	0.00	1.40	1.65	0.00		0.00	6.63	118.59	0.00	0.00
26-Feb-24	12.90	25.55	11.62		18.39	8.23	2.96	9.80	9.50	0.00	0.00	1.62	0.00		0.00	6.18	106.75	0.00	0.00
27-Feb-24	11.52	18.41	9.75		16.16	5.95	1.61	8.83	6.51	0.00	1.02	1.35	0.35		0.00	5.45	86.91	0.00	0.00
28-Feb-24	11.21	17.88	9.76		17.68	6.44	1.76	9.01	6.96	0.00	0.88	1.38	0.00		0.00	5.66	88.62	0.00	0.00
29-Feb-24	11.82	19.70	10.12		19.82	6.61	1.49	8.62	7.75	0.00	1.35	1.65	0.00		0.00	6.85	95.78	0.00	0.00
Total	320.01	546.17	272.37	0.00	443.37	179.74	59.71	240.45	181.32	5.60	25.33	40.86	3.84	0.00	0.00	156.20	2474.97	0.00	0.00
Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day																			

Date	15.2 Import-Export of NR with ER & NER during February 2024																		
	Export of NR to ER (NR- ER)																	Export of NR to NER (NR-NER)	
	NR - ER 765 kV Sasaram - Fatehpur	NR - ER 765 kV Gaya - Varanasi 2*s/C	NR - ER 765 kV Gaya Balia	NR - ER HVDC Alipurduar - Agra	NR-ER 400 kV Patna - Balia D/C	NR - ER 400 kV Muzaffarpur - Gorakhpur D/C	NR - ER 400 kV Biharshariff - Balia D/C	NR - ER 400 kV Motihari - Gorakhpur D/C	NR - ER 400 kV Biharshariff - Varanasi D/C	NR-ER 400 kV Sasaram - Varanasi	NR-ER 400 kV Sasaram - Allahabad	NR - ER 220 kV Sahupuri - Karamnasa	NR - ER 132 kV Sahupuri - Karamnasa	NR - ER 132 kV Rihand -Nagar Untari	NR - ER 132 kV Rihand - Garhwa	NR-ER 400 kV Balia- Naubatpur D/C	Total NR -ER	NR-NER HVDC Biswanath Chariali - Agra	Total NR-NER
1-Feb-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.54	0.00	0.54	17.73	17.73
2-Feb-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00		0.63	0.00	0.63	17.85	17.85
3-Feb-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.12	0.00	0.00	0.00		0.60	0.00	0.72	17.53	17.53
4-Feb-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.52	0.00	0.52	17.56	17.56
5-Feb-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.48		0.32	0.00	0.80	17.12	17.12
6-Feb-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.52	0.00	0.52	16.72	16.72
7-Feb-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.52	0.00	0.52	16.84	16.84
8-Feb-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.50	0.00	0.50	17.21	17.21
9-Feb-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.51	0.00	0.51	18.15	18.15
10-Feb-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.52	0.00	0.52	17.04	17.04
11-Feb-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.54	0.00	0.54	18.04	18.04
12-Feb-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.51	0.00	0.51	18.59	18.59
13-Feb-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.40	0.00	0.40	15.32	15.32
14-Feb-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.36	0.00	0.36	16.90	16.90
15-Feb-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.30	0.00	0.30	16.92	16.92
16-Feb-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.40	0.00	0.40	17.63	17.63
17-Feb-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.48		0.49	0.00	0.97	17.77	17.77
18-Feb-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.58	0.00	0.58	17.49	17.49
19-Feb-24	0.00	0.00	0.00		0.00	0.00	0.61	0.00	0.00	0.00	0.00	0.00			0.49	0.00	1.10	17.29	17.29
20-Feb-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.10	0.46	0.00	0.56	18.53	18.53
21-Feb-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.13	0.00	0.00		0.10	0.47	0.00	0.70	17.06	17.06
22-Feb-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.43	0.00	0.43	17.18	17.18
23-Feb-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.45	0.00	0.45	17.35	17.35
24-Feb-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.45	0.00	0.45	17.65	17.65
25-Feb-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.23	0.00	0.00	0.00		0.48	0.00	0.71	17.82	17.82
26-Feb-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.67	0.72	0.00	0.00		0.49	0.00	1.88	17.45	17.45
27-Feb-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.51	0.00	0.00	0.00		0.37	0.00	0.88	17.75	17.75
28-Feb-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.62	0.00	0.00	0.00		0.39	0.00	1.01	16.81	16.81
29-Feb-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.33	0.00	0.00	0.48		0.43	0.00	1.24	15.02	15.02
Total	0.00	0.00	0.00	0.00	0.00	0.00	0.61	0.00	0.00	2.61	0.72	0.00	1.44	0.20	13.67	0.00	19.25	502.32	502.32
Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day																			

Date	15.3 Import and Export of ER with WR & NER during February 2024																							
	Export of WR to ER (WR-ER)								Import of WR from ER (ER - WR)								Export of ER to NER (ER-NER)				Import of ER from NER (NER-ER)			
	WR - ER 765 kV Dharamjaygarh - Ranchi 2x5/C	WR - ER 765 kV Dharamjaygarh - Jharsuguda Q/C	WR - ER 765 kV Durg - Jharsuguda D/C	WR - ER 400 kV Sipat - Ranchi D/C	WR - ER 400 kV Raigarh - Jharsuguda-2xD/C	WR - ER 220 kV Korba - Budhipadar D/C	WR - ER 220 kV Raigarh - Budhipadar	Total WR - ER	ER - WR 765 kV Dharamjaygarh - Ranchi 2x5/C	ER-WR 765 kV Dharamjaygarh - Jharsuguda D/C	ER-WR 765 kV Durg - Jharsuguda D/C	ER - WR 400 kV Sipat - Ranchi D/C	ER - WR 400 kV Raigarh - Jharsuguda-2xD/C	ER - WR 220 kV Korba - Budhipadar D/C	ER - WR 220 kV Raipara - Budhipadar	Total ER - WR	ER - NER 400 kV Binaguri - Bongaigaon D/C	ER - NER 400 kV Alipurduar - Bongaigaon D/C	ER - NER 220 kV Birpara - Salakati D/C	Total ER - NER	NER - ER 400 kV Binaguri - Bongaigaon D/C	NER - ER 400 kV Alipurduar - Bongaigaon 2xD/C	NER - ER 220 kV Birpara - Salakati D/C	Total NER - ER
1-Feb-24	0.4	0.6	0.0	0.0	0.0	0.0	0.0	0.97	12.3	21.8	15.9	5.4	13.3	1.8	2.6	73.15	0.26	0.03	0.03	0.32	0.60	4.23	0.73	5.56
2-Feb-24	0.2	0.2	0.0	0.0	0.0	0.0	0.0	0.42	11.7	21.4	15.4	4.4	13.1	1.6	3.0	70.46	0.01	0.01	0.01	0.03	0.17	5.25	0.91	6.33
3-Feb-24	0.2	0.0	0.0	0.0	0.0	0.0	0.0	0.22	11.2	25.6	16.3	4.5	14.0	1.2	3.1	75.87	0.00	0.00	0.00	0.00	0.00	7.68	1.45	9.13
4-Feb-24	2.1	0.1	0.0	0.2	0.0	0.4	0.0	2.85	7.5	16.3	13.1	2.6	13.3	0.6	2.1	55.40	0.03	0.00	0.00	0.03	0.82	5.08	0.92	6.81
5-Feb-24	0.4	0.0	0.0	0.0	0.0	0.2	0.0	0.61	6.6	12.7	13.4	3.1	13.8	1.0	2.5	53.08	0.25	0.00	0.00	0.25	0.79	4.66	0.89	6.34
6-Feb-24	0.3	0.1	0.0	0.0	0.0	0.1	0.0	0.52	7.9	11.6	13.5	3.6	14.4	0.8	2.2	53.89	0.24	0.00	0.00	0.24	1.11	5.64	1.05	7.80
7-Feb-24	0.2	0.1	0.0	0.0	0.0	0.1	0.0	0.43	11.6	12.5	13.9	4.4	14.4	0.8	2.2	59.75	0.29	0.04	0.01	0.34	1.02	5.07	1.09	7.18
8-Feb-24	0.3	1.5	0.0	0.0	0.0	0.7	0.0	2.57	11.2	5.1	12.7	4.1	12.7	0.5	1.9	48.06	0.37	0.02	0.01	0.40	0.65	3.99	0.75	5.39
9-Feb-24	0.5	1.4	0.0	0.0	0.0	0.7	0.0	2.71	13.0	8.2	13.1	4.4	12.3	0.3	2.0	53.38	0.03	0.00	0.01	0.04	0.31	5.84	1.08	7.23
10-Feb-24	0.3	1.8	0.0	0.0	0.0	0.5	0.0	2.62	9.8	5.8	11.6	3.8	11.9	0.5	2.1	45.44	0.00	0.05	0.01	0.06	0.00	6.08	1.29	7.37
11-Feb-24	1.8	3.9	0.0	0.2	0.0	0.7	0.0	6.60	6.2	1.7	9.9	2.6	11.5	0.3	2.2	34.30	0.28	0.07	0.00	0.35	0.75	4.40	1.02	6.18
12-Feb-24	2.5	4.3	0.0	0.1	0.0	0.6	0.0	7.56	2.9	4.0	10.3	2.2	11.4	0.4	1.5	32.58	0.16	0.05	0.01	0.22	0.63	4.57	1.14	6.34
13-Feb-24	2.6	6.1	0.0	0.1	0.0	0.9	0.0	9.64	3.4	1.5	10.0	2.5	12.2	0.2	1.4	31.09	0.15	0.01	0.00	0.16	0.60	4.47	1.13	6.20
14-Feb-24	0.4	7.1	0.0	0.0	0.0	1.3	0.0	8.85	6.7	1.7	10.0	2.6	10.0	0.0	1.8	32.80	0.27	0.02	0.00	0.30	0.61	3.78	1.07	5.46
15-Feb-24	0.2	4.9	0.0	0.0	0.0	0.8	0.0	5.91	12.5	1.1	11.2	4.0	10.7	0.1	2.5	42.12	0.36	0.13	0.03	0.51	0.40	3.27	0.90	4.57
16-Feb-24	0.0	3.9	0.0	0.0	0.0	0.2	0.0	4.10	14.6	2.8	12.3	4.9	12.7	0.5	3.0	50.76	0.05	0.16	0.02	0.23	0.12	3.80	0.90	4.82
17-Feb-24	0.0	5.9	0.0	0.0	0.0	0.1	0.0	6.09	17.5	1.1	12.9	6.0	13.5	0.6	3.2	54.80	0.01	0.05	0.00	0.06	0.00	4.02	1.12	5.15
18-Feb-24	0.0	5.2	0.0	0.0	0.0	0.1	0.0	5.33	19.9	2.1	12.4	6.1	13.5	0.5	3.1	57.61	0.22	0.03	0.00	0.25	0.77	4.83	1.34	6.94
19-Feb-24	0.3	9.5	0.0	0.0	0.0	0.2	0.0	10.06	14.5	0.6	12.1	5.1	13.5	0.5	2.9	49.25	0.34	0.12	0.02	0.48	0.59	3.89	0.65	5.13
20-Feb-24	0.0	9.8	0.0	0.0	0.0	0.0	0.0	9.80	20.8	1.2	13.6	7.3	15.7	0.8	3.0	62.43	0.28	0.03	0.02	0.32	1.04	5.30	0.99	7.33
21-Feb-24	0.0	3.8	0.0	0.0	0.0	0.2	0.0	3.92	25.8	1.8	14.1	7.9	14.7	0.4	2.9	67.59	0.11	0.00	0.00	0.11	1.26	6.43	0.83	8.51
22-Feb-24	0.0	16.9	0.0	0.0	0.0	0.0	0.0	16.92	23.2	0.4	11.5	7.9	12.8	0.8	2.8	59.36	0.52	0.52	0.00	1.04	1.19	5.34	0.77	7.30
23-Feb-24	0.0	15.0	0.0	0.0	0.0	0.3	0.0	15.32	21.3	0.5	12.1	7.8	11.7	0.5	2.6	56.59	0.00	0.45	0.09	0.55	0.40	6.03	1.14	7.56
24-Feb-24	0.0	12.4	0.0	0.0	0.0	0.1	0.0	12.47	27.6	3.2	14.8	9.6	14.6	0.7	3.0	73.56	0.00	0.00	0.00	0.00	0.18	5.70	1.12	7.00
25-Feb-24	0.0	9.0	0.0	0.0	0.0	0.1	0.0	9.05	25.4	4.1	19.4	8.9	14.5	0.4	2.7	75.46	0.12	0.14	0.01	0.26	0.78	4.62	0.91	6.31
26-Feb-24	0.0	14.1	0.0	0.0	0.0	0.0	0.0	14.12	20.3	3.2	22.6	7.9	14.7	1.0	3.0	72.77	0.65	0.43	0.06	1.15	0.33	2.57	0.57	3.47
27-Feb-24	0.0	13.5	0.0	0.0	0.0	0.8	0.0	14.28	18.7	0.5	21.3	6.2	11.0	0.3	2.7	60.72	0.56	0.20	0.06	0.83	0.67	3.85	0.60	5.12
28-Feb-24	0.0	8.8	0.0	0.0	0.0	0.7	0.0	9.41	19.5	1.6	14.5	6.5	9.7	0.2	2.9	54.94	0.32	0.05	0.04	0.41	1.01	5.17	0.72	6.90
29-Feb-24	0.0	8.8	0.0	0.0	0.0	0.5	0.0	9.30	17.9	0.9	13.9	5.8	9.9	0.2	2.7	51.18	0.20	0.00	0.01	0.21	1.10	5.85	0.77	7.72
Total	12.73	168.60	0.00	0.75	0.00	10.54	0.00	192.63	421.37	174.98	397.81	151.92	371.43	17.42	73.44	1608.37	6.09	2.63	0.45	9.16	17.90	141.39	27.84	187.14

Date	15.4 Import and Export of SR with ER & WR during February 2024																									
	Export of ER to SR (ER - SR)				Import of ER from SR (SR - ER)				Export of WR to SR (WR-SR)								Import of WR from SR (SR - WR)									
	ER - SR HVDC Gazuwaka	ER - SR HVDC Talchar -Kolar	ER-SR 765 kV Angul- Srikakulam D/C	Total ER - SR	SR - ER HVDC Gazuwaka	SR - ER HVDC Talchar -	SR-ER 765 kV Angul- Srikakulam D/C	Total SR - ER	WR - SR HVDC Bhadrawati	WR - SR 765 kV Sholapur - Raichur 2x5/C	WR-SR 765 kV Wardha - Nizamabad D/C	WR-SR 400KV Kolhapur-Kudgi D/C	WR-SR HVDC Raigarh- Puglur	WR-SR 220kV Xeldem - Ambewadi S/C	WR-SR 220kV Ponda - Ambewadi S/C	WR-SR 765 kV Warora - Warangal D/C	Total WR - SR	SR - WR HVDC Bhadrawati	SR - WR 765 kV Raichur Sholapur 2x5/C	SR-WR 765 kV Wardha Nizamabad D/C	SR-WR 400KV Kolhapur-Kudgi D/C	SR-WR HVDC Raigarh- Puglur	WR-SR 220kV Xeldem - Ambewadi S/C	WR-SR 220kV Ponda - Ambewadi S/C	SR-WR 765 kV Warangal - Warora D/C	Total SR - WR
1-Feb-24	11.30	0.00	57.88	69.18	0.00	0.00	0.00	0.00	20.26	24.50	42.17	0.00	87.11	1.96	0.00	45.10	221.10	0.00	0.97	0.00	15.43	0.00	0.00	0.00	0.00	16.40
2-Feb-24	11.30	0.00	57.25	68.55	0.00	0.00	0.00	0.00	18.73	25.21	43.42	0.00	91.02	1.97	0.00	44.66	225.01	0.00	0.65	0.00	15.21	0.00	0.00	0.00	0.00	15.86
3-Feb-24	11.34	0.21	54.98	66.53	0.00	0.00	0.00	0.00	12.13	19.88	35.66	0.00	84.92	2.07	0.00	40.85	195.51	0.00	1.20	0.05	17.36	0.00	0.00	0.00	0.00	18.61
4-Feb-24	11.35	30.04	50.13	91.52	0.00	0.00	0.00	0.00	11.37	10.12	33.03	0.00	57.06	2.10	0.00	34.51	148.19	0.00	5.17	0.00	21.01	0.00	0.00	0.00	0.00	26.18
5-Feb-24	11.23	34.84	53.46	99.53	0.00	0.00	0.00	0.00	20.41	14.64	27.37	0.00	66.91	2.19	0.00	38.60	170.12	0.00	1.98	0.00	19.61	0.00	0.00	0.00	0.00	21.59
6-Feb-24	10.97	40.45	53.36	104.78	0.00	0.00	0.00	0.00	22.16	12.31	0.00	0.00	61.28	2.21	0.00	37.29	135.25	0.00	2.48	0.00	20.68	0.00	0.00	0.00	0.00	23.16
7-Feb-24	11.01	38.44	52.75	102.20	0.00	0.00	0.00	0.00	22.44	11.73	0.00	0.00	88.77	2.28	0.00	35.79	161.01	0.00	5.13	0.00	20.83	0.00	0.00	0.00	0.00	25.96
8-Feb-24	11.00	37.47	53.72	102.19	0.00	0.00	0.00	0.00	17.51	16.06	0.00	0.00	84.00	2.31	0.00	40.70	160.58	0.00	2.55	0.00	18.78	0.00	0.00	0.00	0.00	21.33
9-Feb-24	10.97	30.13	52.68	93.78	0.00	0.00	0.00	0.00	13.27	14.70	0.00	0.00	64.79	2.37	0.00	39.48	134.61	0.00	3.35	0.00	20.10	0.00	0.00	0.00	0.00	23.45
10-Feb-24	11.09	33.74	52.17	97.00	0.00	0.00	0.00	0.00	15.00	10.96	0.00	0.00	61.83	2.31	0.00	37.36	127.46	0.00	4.38	0.00	20.17	0.00	0.00	0.00	0.00	24.55
11-Feb-24	11.10	30.12	52.74	93.96	0.00	0.00	0.00	0.00	16.53	8.93	0.00	0.00	53.01	2.20	0.00	36.52	117.19	0.00	5.40	0.00	20.47	0.00	0.00	0.00	0.00	25.87
12-Feb-24	10.77	33.95	52.48	97.20	0.00	0.00	0.00	0.00	13.97	10.60	0.00	0.00	43.61	2.23	0.00	36.05	106.46	0.00	5.60	0.00	22.77	0.00	0.00	0.00	0.00	28.37
13-Feb-24	8.72	45.45	49.97	104.14	0.00	0.00	0.00	0.00	16.80	8.08	0.00	0.00	58.93	2.25	0.00	37.64	123.70	0.00	3.50	0.00	24.02	0.00	0.00	0.00	0.00	27.52
14-Feb-24	8.71	45.25	51.93	105.89	0.00	0.00	0.00	0.00	19.81	8.13	0.00	0.00	83.55	2.19	0.00	38.54	152.22	0.00	3.87	0.00	23.44	0.00	0.00	0.00	0.00	27.31
15-Feb-24	8.73	39.21	56.35	104.29	0.00	0.00	0.00	0.00	16.76	11.76	0.00	0.00	80.21	2.30	0.00	43.66	154.69	0.00	2.44	0.00	23.28	0.00	0.00	0.00	0.00	25.72
16-Feb-24	8.73	31.89	57.48	98.10	0.00	0.00	0.00	0.00	17.51	12.48	0.00	0.00	69.75	2.27	0.00	43.34	145.35	0.00	4.07	0.00	23.43	0.00	0.00	0.00	0.00	27.50
17-Feb-24	8.72	37.93	60.16	106.81	0.00	0.00	0.00	0.00	16.94	16.60	0.00	0.00	49.83	2.34	0.00	45.29	131.00	0.00	2.31	0.00	21.98	0.00	0.00	0.00	0.00	24.29
18-Feb-24	13.61	36.74	54.18	104.53	0.00	0.00	0.00	0.00	19.18	12.02	0.00	0.00	69.78	2.30	0.00	42.65	145.93	0.00	1.32	0.00	20.29	0.00	0.00	0.00	0.00	21.61
19-Feb-24	14.88	37.29	59.37	111.54	0.00	0.00	0.00	0.00	19.41	17.44	0.00	0.00	84.22	2.42	0.00	50.40	173.89	0.00	0.28	0.00	17.58	0.00	0.00	0.00	0.00	17.86
20-Feb-24	14.88	41.05	62.53	118.46	0.00	0.00	0.00	0.00	17.20	20.32	0.00	0.00	86.20	2.41	0.00	51.28	177.41	0.00	0.78	0.00	18.38	0.00	0.00	0.00	0.00	19.16
21-Feb-24	14.83	41.98	60.20	117.01	0.00	0.00	0.00	0.00	21.50	20.90	0.00	0.00	120.40	2.21	0.00	49.93	214.94	0.00	0.18	0.00	19.49	0.00	0.00	0.00	0.00	19.67
22-Feb-24	14.70	41.14	61.49	117.33	0.00	0.00	0.00	0.00	13.80	23.95	0.00	0.00	90.48	2.14	0.00	52.99	183.36	0.00	0.00	0.00	20.05	0.00	0.00	0.00	0.00	20.05
23-Feb-24	14.71	43.66	63.89	122.26	0.00	0.00	0.00	0.00	11.98	23.90	0.00	0.00	95.55	2.07	0.00	54.28	187.78	0.00	0.97	0.00	19.79	0.00	0.00	0.00	0.00	20.76
24-Feb-24	14.87	36.46	70.29	121.62	0.00	0.00	0.00	0.00	19.96	31.41	0.00	0.00	107.72	2.10	0.00	60.41	221.60	0.00	0.00	0.00	15.82	0.00	0.00	0.00	0.00	15.82
25-Feb-24	14.99	43.48	60.41	118.88	0.00	0.00	0.00	0.00	20.07	18.90	0.00	0.00	96.10	2.04	1.17	49.87	188.15	0.00	1.30	0.00	15.53	0.00	0.00	0.00	0.00	16.83
26-Feb-24	14.71	35.32	64.94	114.97	0.00	0.00	0.00	0.00	13.21	23.13	0.00	0.00	72.37	2.03	0.09	55.91	166.74	0.00	0.67	0.00	18.22	0.00	0.00	0.00	0.00	18.89
27-Feb-24	14.71	41.46	61.08	117.25	0.00	0.00	0.00	0.00	21.85	15.73	0.00	0.00	100.40	2.36	0.00	51.66	192.00	0.00	0.93	0.00	21.36	0.00	0.00	0.00	0.00	22.29
28-Feb-24	14.71	42.23	58.94	115.88	0.00	0.00	0.00	0.00	24.15	16.47	0.00	0.00	101.87	2.29	0.00	51.10	195.88	0.00	0.96	0.00	20.16	0.00	0.00	0.00	0.00	21.12
29-Feb-24	14.70	43.44	58.34	116.48	0.00	0.00	0.00	0.00	17.92	15.36	0.00	0.00	95.83	2.41	0.00	50.31	181.83	0.00	2.55	0.00	22.64	0.00	0.00	0.00	0.00	25.19
TOTAL	353.34	993.37	1655.15	3001.86	0.00	0.00	0.00	0.00	511.83	476.22	181.65	0.00	2307.50	64.33	1.26	1296.17	4838.96	0.00	64.99	0.05	577.88	0.00	0.00	0.00	0.00	642.92

16. भूटान , नेपाल, बांग्लादेश एवं म्यान्मार के साथ अंतरराष्ट्रीय विद्युत विनिमय

अप्रैल 2023 से मार्च 2024 April 2023 to March 2024

अंतरराष्ट्रीय विद्युत विनिमय [भारत 'से निर्यात' 'को आयात']
Transnational Exchange ('Export from'/'Import to' India)

माह MONTH	भूटान BHUTAN		नेपाल NEPAL		बांग्लादेश BANGLADESH		म्यान्मार MYANMAR	
	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)
अप्रैल 2023 APR'23	19.40	41.40	357.99	0.00	687.30	0.00	0.73	0.00
मई 2023 MAY'23	2.27	117.99	271.80	0.34	775.10	0.00	0.61	0.00
जून 2023 JUN'23	0.00	626.15	80.00	88.86	743.92	0.00	0.77	0.00
जुलाई 2023 JUL'23	0.00	1291.66	0.00	223.72	780.77	0.00	1.02	0.00
अगस्त 2023 AUG'23	0.00	1244.52	0.00	281.61	767.79	0.00	0.94	0.00
सितंबर 2023 SEP'23	0.00	924.25	0.00	323.59	754.88	0.00	0.77	0.00
अक्टूबर 2023 OCT'23	0.00	588.64	0.00	460.97	755.92	0.00	0.84	0.00
नवंबर 2023 NOV'23	51.41	36.77	0.00	271.72	628.24	0.00	0.72	0.00
दिसम्बर 2023 DEC'23	212.51	0.00	88.76	5.09	593.51	0.00	0.70	0.00
जनवरी 2024 JAN'24	287.94	0.00	271.79	0.00	601.77	0.00	0.65	0.00
फरवरी 2024 FEB'24	312.87	0.00	368.61	0.00	593.99	0.00	0.60	0.00
कुल Total	886.41	4871.38	1438.94	1655.89	7683.19	0.00	8.35	0.00

* Based on daily operational data

Date	16.1 Import from neighbouring countries during February 2024													
	(All figures in MU)													
	Import from Bhutan								Import from Bangladesh		Import from Nepal			Import from Myanmar
	400 kV Tala-Binaguri I,II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurdwār D/C*	400 kV Jigmeling-Alipurdwār D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-Feb-24	0.00	0.00	0.00	0.00	0.00	0.00	0.25	0.00	0.00	0.00	0.00	0.00	0.00	0.00
2-Feb-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
3-Feb-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
4-Feb-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
5-Feb-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
6-Feb-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
7-Feb-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
8-Feb-24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
9-Feb-24	0.00	0.00	0.00	0.00	0.00	0.00	0.11	0.00	0.00	0.00	0.00	0.00	0.00	0.00
10-Feb-24	0.00	0.00	0.00	0.00	0.00	0.00	0.17	0.00	0.00	0.00	0.00	0.00	0.00	0.00
11-Feb-24	0.00	0.00	0.00	0.00	0.00	0.00	0.21	0.00	0.00	0.00	0.00	0.00	0.00	0.00
12-Feb-24	1.16	0.00	0.00	0.00	0.00	0.00	0.25	0.00	0.00	0.00	0.00	0.00	0.00	0.00
13-Feb-24	1.36	0.00	0.00	0.00	0.00	0.00	0.36	0.00	0.00	0.00	0.00	0.00	0.00	0.00
14-Feb-24	0.00	0.00	0.00	0.00	0.00	0.00	0.27	0.00	0.00	0.00	0.00	0.00	0.00	0.00
15-Feb-24	0.00	0.00	0.00	0.00	0.00	0.00	0.23	0.00	0.00	0.00	0.00	0.00	0.00	0.00
16-Feb-24	0.00	0.00	0.00	0.00	0.00	0.00	0.19	0.00	0.00	0.00	0.00	0.00	0.00	0.00
17-Feb-24	0.00	0.00	0.00	0.00	0.00	0.00	0.20	0.00	0.00	0.00	0.00	0.00	0.00	0.00
18-Feb-24	0.00	0.00	0.00	0.00	0.00	0.00	0.12	0.00	0.00	0.00	0.00	0.00	0.00	0.00
19-Feb-24	0.00	0.00	0.00	0.00	0.00	0.00	0.21	0.00	0.00	0.00	0.00	0.00	0.00	0.00
20-Feb-24	0.00	0.00	0.00	0.00	0.00	0.00	0.29	0.00	0.00	0.00	0.00	0.00	0.00	0.00
21-Feb-24	0.00	0.00	0.00	0.00	0.00	0.00	0.29	0.00	0.00	0.00	0.00	0.00	0.00	0.00
22-Feb-24	0.00	0.00	0.00	0.00	0.00	0.00	0.26	0.00	0.00	0.00	0.00	0.00	0.00	0.00
23-Feb-24	0.00	0.00	0.00	0.00	0.00	0.00	0.22	0.00	0.00	0.00	0.00	0.00	0.00	0.00
24-Feb-24	0.00	0.00	0.00	0.00	0.00	0.00	0.29	0.00	0.00	0.00	0.00	0.00	0.00	0.00
25-Feb-24	0.00	0.00	0.00	0.00	0.00	0.00	0.25	0.00	0.00	0.00	0.00	0.00	0.00	0.00
26-Feb-24	0.00	0.00	0.00	0.00	0.00	0.00	0.32	0.00	0.00	0.00	0.00	0.00	0.00	0.00
27-Feb-24	0.00	0.00	0.00	0.00	0.00	0.00	0.39	0.00	0.00	0.00	0.00	0.00	0.00	0.00
28-Feb-24	0.00	0.00	0.00	0.00	0.00	0.00	0.39	0.00	0.00	0.00	0.00	0.00	0.00	0.00
29-Feb-24	0.00	0.00	0.00	0.00	0.00	0.00	0.32	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Total	2.52	0.00	0.00	0.00	0.00	0.00	5.59	0.00	0.00	0.00	0.00	0.00	0.00	0.00

Based on SEM/Energy meter data for links where available (*Mangdechu generation receipt at APD through a bypassed arrangement at 400kV Punatsanchu station)

Date	16.2 Export to neighbouring countries during February 2024 (All figures in MU)													
	Export to Bhutan								Export to Bangladesh		Export to Nepal			Export to Myanmar
	400 kV Tala-Binaguri I, II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurwar D/C*	400 kV Jigmeling-Alipurwar D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-Feb-24	0.55	1.47	2.04	1.20	0.49	2.94	0.00	0.52	18.52	2.61	1.50	8.65	0.55	0.02
2-Feb-24	0.33	1.25	2.09	1.22	0.00	2.87	0.10	0.45	17.38	2.33	1.44	8.83	0.81	0.02
3-Feb-24	0.64	1.55	2.49	1.34	0.00	2.66	0.04	0.50	18.53	2.48	1.37	7.97	0.78	0.02
4-Feb-24	0.52	1.41	2.19	1.23	0.00	2.78	0.30	0.45	19.53	2.50	1.53	9.20	1.58	0.02
5-Feb-24	0.65	1.69	2.82	1.18	0.00	3.12	0.30	0.46	19.41	2.68	1.45	8.89	1.17	0.02
6-Feb-24	0.78	1.81	2.93	1.28	0.00	3.12	0.16	0.47	19.37	2.66	1.49	8.54	1.79	0.02
7-Feb-24	0.88	1.90	2.87	1.23	0.00	3.07	0.09	0.46	19.30	2.74	1.41	8.55	1.11	0.03
8-Feb-24	0.95	1.97	2.89	1.25	0.00	3.15	0.23	0.42	19.28	2.65	1.48	8.80	1.38	0.02
9-Feb-24	0.83	1.87	3.13	1.22	0.00	3.32	0.00	0.53	17.94	2.36	1.45	8.98	1.46	0.02
10-Feb-24	1.20	2.25	3.65	1.36	0.00	2.46	0.00	0.44	18.64	2.50	1.40	7.92	1.12	0.02
11-Feb-24	1.15	2.23	3.67	1.47	0.00	2.59	0.00	0.40	20.23	2.54	1.49	9.03	1.70	0.02
12-Feb-24	0.00	4.00	3.96	1.88	0.00	2.75	0.00	0.42	18.54	2.51	1.39	8.46	1.27	0.02
13-Feb-24	0.00	4.05	4.06	1.75	0.00	2.66	0.00	0.40	18.48	2.39	1.42	8.70	1.80	0.02
14-Feb-24	1.21	2.29	4.82	1.18	0.00	1.68	0.00	0.28	18.59	2.57	1.55	9.41	2.23	0.02
15-Feb-24	1.23	2.41	4.47	1.04	0.00	2.23	0.00	0.32	18.45	2.56	1.41	9.04	1.74	0.03
16-Feb-24	1.29	2.38	3.88	1.12	0.51	1.48	0.00	0.32	17.96	2.07	1.55	8.86	1.86	0.02
17-Feb-24	0.28	1.02	5.61	0.70	1.13	1.65	0.00	0.45	16.84	2.22	1.49	8.37	2.07	0.02
18-Feb-24	0.00	0.68	6.06	0.80	1.09	1.68	0.00	0.49	12.85	2.30	1.49	8.94	2.38	0.02
19-Feb-24	1.07	2.13	3.65	1.41	1.03	1.50	0.00	0.40	19.01	2.27	1.49	8.74	2.60	0.03
20-Feb-24	1.05	2.09	3.71	1.36	1.12	1.63	0.00	0.39	19.52	2.33	1.50	8.72	2.11	0.02
21-Feb-24	1.24	2.22	3.52	1.44	1.11	1.64	0.00	0.50	17.95	2.15	1.50	8.91	1.26	0.02
22-Feb-24	1.10	2.09	3.47	1.40	0.99	1.43	0.00	0.44	19.02	2.34	1.46	8.59	1.78	0.02
23-Feb-24	0.90	1.91	3.44	1.38	0.79	1.80	0.00	0.46	18.43	2.42	1.46	8.44	1.91	0.02
24-Feb-24	0.96	1.96	3.47	1.40	0.00	2.80	0.00	0.47	18.81	2.48	1.47	8.03	1.26	0.02
25-Feb-24	0.82	1.84	3.46	1.34	0.00	2.68	0.00	0.44	19.51	2.47	1.45	9.24	1.90	0.02
26-Feb-24	0.90	1.88	3.80	0.86	0.00	2.79	0.00	0.39	13.86	2.23	1.52	9.00	2.67	0.02
27-Feb-24	1.10	2.18	3.92	1.23	1.04	2.17	0.00	0.41	9.84	2.63	1.46	9.59	2.56	0.02
28-Feb-24	1.09	2.14	4.09	1.16	2.83	0.00	0.00	0.41	14.75	2.63	1.49	9.32	2.51	0.01
29-Feb-24	1.71	2.71	3.88	1.57	3.09	0.00	0.00	0.42	19.66	2.64	1.49	9.19	2.62	0.00
Total	24.42	59.38	104.06	37.01	15.24	64.66	1.22	12.51	520.20	71.25	42.63	254.90	49.96	0.60

Based on SEM/Energy meter data for links where available (*Mangdechhu generation receipt at APD through a bypassed arrangement at 400kV Punatsanchu station)

17. एसटीओए (द्विपक्षीय एवं सामूहिक) एवं डी एस एम बिलिंग का ब्योरा – फ़रवरी 2024

STOA (BILATERAL AND COLLECTIVE) & DSM BILLING DETAILS - FEBRUARY

2024 द्विपक्षीय एसटीओए BILATERAL SHORT TERM OPEN ACCESS

फ़रवरी 2024	FEBRUARY 2024	Apr'23- Feb'24
नोडल क्षेत्र.भा.प्रे.के. का नाम Name of Nodal RLDC	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Energy Approved(MU)
ऊ. क्षेत्र. NR	206	626
प.क्ष. WR	370	399
द.क्ष. SR	484	1098
पू.क्ष. ER	157	183
पूर्वांतर क्षेत्र. NER	124	49
कुल TOTAL	1341	2355

एसटीओए SHORT TERM OPEN ACCESS

	सामूहिक एसटीओए Collective STOA	द्विपक्षीय एसटीओए Bilateral STOA
माह MONTH	क्रेताओं / विक्रेताओं की सं. NO. of Buyers/Sellers	अनुमोदित ऊर्जा (मि.यु.) Approved Energy (MU)
अप्रैल 2023 Apr'23	5580	6941
मई 2023 May'23	5798	6626
जून 2023 Jun'23	5783	6966
जुलाई 2023 Jul'23	6428	6719
अगस्त 2023 Aug'23	5954	6805
सितंबर 2023 Sep'23	6440	6506
अक्टूबर 2023 Oct'23	6571	7388
नवंबर 2023 Nov'23	7848	7741
दिसम्बर 2023 Dec'23	8441	7397
जनवरी 2024 Jan'24	9045	8184
फ़रवरी 2024 Feb'24	8419	7349
कुल TOTAL	76307	78622

मासिक डी एस एम बिलिंग का ब्योरा* 2023-24
MONTHLY DSM BILLING DETAILS* 2023-24

अनंतिम आँकड़े
Provisional data
subject to change

करोड़ रु. में (RS. IN CRORES)

क्षेत्र REGION →	उत्तरी क्षेत्र NORTH	पश्चिमी क्षेत्र WEST	दक्षिणी क्षेत्र SOUTH	पूर्वी क्षेत्र EAST	पूर्वांतर क्षेत्र NORTH EAST
सप्ताह WEEK ↓					
29.01.24 to 04.02.24	126.54	243.62	163.68	---	78.12
05.02.24 to 11.02.24	120.12	182.45	185.30	---	70.07
12.02.24 to 18.02.24	90.00	181.24	223.38	---	64.07
19.02.24 to 25.02.24	113.28	202.26	252.23	---	63.55
26.02.24 to 03.03.24	76.55	151.71	182.52	---	53.26

* Amount shown is Payable to DSM pool ^Provisional Data

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL) पावर एक्स्चेंज के माध्यम से विनिमय – माह:- फ़रवरी 2024 EXCHANGES THROUGH POWER EXCHANGES - FEBRUARY 2024				
क्र. सं. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
1	AD HYDRO POWER LIMITED	उत्तरी क्षेत्र NR	10.37	0.00
2	ADANI SOLAR ENERGY JAISALMER TWO PRIVATE LIMITED(Project-2)		17.64	0.00
3	ADANI SOLAR ENERGY JODHPUR TWO LIMITED		9.82	0.00
4	ADANI SOLAR ENERGY RJ TWO PRIVATE LIMITED		10.38	0.00
5	ADANI SOLAR ENERGY RJ TWO PRIVATE LIMITED (infirm)		0.71	0.00
6	Adept Renewable Technologies Private Limited		11.27	0.00
7	Amp Energy Green Six Private Limited		18.03	0.00
8	Amplus Ages Private Limited		17.83	0.00
9	Budhil HEP (Greenko Budhil Hydro Power Pvt. Ltd.)		0.47	0.00
10	Chandigarh (UT)		14.05	7.33
11	Delhi		208.19	79.88
12	Grian Energy Private Limited		17.62	0.00
13	Haryana		31.00	302.67
14	Himachal Pradesh		61.76	47.46
15	IGSTPS JHAJJAR		1.43	0.00
16	Jammu Kashmir		29.31	537.55
17	KARCHAM WANGTOO HYDRO ELECTRIC PLANT.		15.20	0.00
18	NEPAL ELECTRICITY AUTHORITY TANAKPUR		0.00	35.31
19	NTPC Dadri Stage I		5.18	0.00
20	NTPC Dadri Stage II		1.79	0.00
21	NTPC Rihand stage I		6.77	0.00
22	NTPC Rihand stage II		6.78	0.00
23	NTPC Rihand stage III		4.72	0.00
24	NTPC Singrauli		6.58	0.00
25	NTPC Tanda Stage II		7.87	0.00
26	NTPC Unchahar Stage I		0.86	0.00
27	NTPC Unchahar Stage II		1.61	0.00
28	NTPC Unchahar Stage III		0.89	0.00
29	NTPC Unchahar Stage IV		0.08	0.00
30	North Central Railway Prayagraj		0.00	25.69
31	Onevolt Energy Private Limited		17.36	0.00
32	Punjab		3.82	1075.71
33	RENEW SURYA AAYAN PRIVATE LIMITED		18.87	0.00
34	RENEW SURYA PRATAP PRIVATE LIMITED		30.04	0.00
35	RENEW SURYA ROSHNI PRIVATE LIMITED-Fatehgarh-III PS		1.52	0.00
36	RENEW SURYA VIHAAN PRIVATE LIMITED		15.50	0.00
37	Rajasthan		608.31	67.59
38	ReNew Surya Ravi Private Limited		44.25	0.00
39	SHREE CEMENT LIMITED TPS		24.48	0.00
40	Sainj HEP		4.81	0.00
41	Singoli Bhatwari HEP		5.82	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL) पावर एक्स्चेंज के माध्यम से विनिमय – माह:- फ़रवरी 2024 EXCHANGES THROUGH POWER EXCHANGES - FEBRUARY 2024				
क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
42	Sorang HEP (Himachal Sorang Power Pvt. Ltd.))		5.57	0.00
43	Transition Energy Services Private Limited		5.27	0.00
44	Uttar Pradesh		923.96	412.70
45	Uttarakhand		21.11	169.85

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL) पावर एक्स्चेंज के माध्यम से विनिमय – माह:- फ़रवरी 2024 EXCHANGES THROUGH POWER EXCHANGES - FEBRUARY 2024				
क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
46	ACB (INDIA) LIMITED	पश्चिमी क्षेत्र WR	67.63	0.28
47	ADANI RENEWABLE ENERGY HOLDING FOUR LIMITED		46.31	0.00
48	ADANI WIND ENERGY KUTCHH FOUR Ltd. Nakhatrana		58.34	0.00
49	Adani Power Limited - Raigarh TPP		185.17	4.25
50	Adani Power Limited-Raipur TPP		331.19	0.94
51	ArcelorMittal Nippon Steel India Limited		0.00	86.75
52	BHARAT ALUMINIUM COMPANY LTD		14.20	0.00
53	BHARAT ALUMINIUM COMPANY LTD (Bulk Consumer)		0.00	12.95
54	CONTINUUM POWER TRADING (TN) PRIVATE LIMITED		11.17	0.00
55	Chhattisgarh		181.13	36.03
56	D B Power Limited		235.24	0.00
57	DGEN MEGA POWER PROJECT		11.96	0.00
58	DHARIWAL STU OTH		11.34	0.00
59	Daman and Diu - Dadra and Nagar Haveli		1.12	165.37
60	Dhariwal ISTS		8.39	1.37
61	GMR Warora Energy Limited		18.00	0.00
62	Goa WR		3.11	32.40
63	Gujarat		190.73	712.19
64	INOX GREEN ENERGY SERVICES LIMITED		1.33	0.00
65	Jaypee Nigrie Super Thermal Power Plant		60.08	0.00
66	Jhabua Power Limited		27.31	4.17
67	Jindal Power Limited, Stage-1		106.84	0.36
68	Jindal Power Limited, Stage-2		239.95	0.00
69	Jindal Steel & Power Ltd , DCPP		121.24	1.62
70	MAHAN ENERGEN LIMITED.		269.02	1.84
71	MB POWER (MADHYA PRADESH) LIMITED		48.65	2.46
72	Madhya Pradesh		211.91	191.33
73	Maharashtra		104.68	240.81
74	Maruti Clean Coal and Power Limited		7.38	0.34
75	NPCIL KAKRAPAR ATOMIC POWER STATION UNIT 4 INFIRM		9.80	0.00
76	NREL-Dayapar Wind		5.16	0.00
77	NTPC Gadawara		3.51	0.00
78	NTPC Jhanor Gandhar GPS		0.00	0.83
79	NTPC Kawas GPS		0.00	0.67
80	NTPC Korba Stage I &II		0.40	0.00
81	NTPC Korba Stage III		0.77	0.00
82	NTPC Lara Stage I		0.50	0.00
83	NTPC Mouda Stage I		2.65	0.00
84	NTPC Mouda Stage II		4.88	0.00
85	NTPC SAIL POWER COMPANY LIMITED		0.01	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- फ़रवरी 2024
EXCHANGES THROUGH POWER EXCHANGES - FEBRUARY 2024

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
86	NTPC Sipat Stage I		1.86	0.00
87	NTPC Sipat Stage II		2.21	0.00
88	NTPC Solapur		5.04	0.00
89	NTPC Vindhyachal Stage I		1.53	0.00
90	NTPC Vindhyachal Stage II		1.19	0.00
91	NTPC Vindhyachal Stage III		1.63	0.00
92	NTPC Vindhyachal Stage IV		2.10	0.00
93	NTPC Vindhyachal Stage V		0.14	0.00
94	NTPC khargone		4.51	0.00
95	R.K.M POWERGEN PRIVATE LIMITED		27.81	0.00
96	Ratnagiri Gas & Power Private Limited		0.00	0.97
97	SKS Power Generation Chhattisgarh Limited		12.50	18.20
98	Sasan Power Limited		6.20	0.00
99	TRN ENERGY PRIVATE LIMITED		22.78	0.00
100	The Tata Power Co Ltd (MTPS)		11.81	0.00
101	WIND FIVE RENERGY LIMITED		7.94	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- फ़रवरी 2024
EXCHANGES THROUGH POWER EXCHANGES - FEBRUARY 2024

क्र. सं. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
102	Andhra Pradesh	दक्षिणी क्षेत्र SR	110.25	322.16
103	Ayana Renewable Power Six Private Limited		7.62	0.00
104	COASTAL ENERGEN PRIVATE LIMITED		1.32	0.00
105	Goa SR		0.28	11.61
106	IL&FS TAMIL NADU POWER COMPANY LIMITED		1.67	0.00
107	JSW RENEW ENERGY LIMITED		1.40	0.00
108	JSW RENEW ENERGY TWO LIMITED		1.52	0.00
109	Karnataka		0.15	167.61
110	Kerala		7.11	331.94
111	NLC INDIA LIMITED NEYVELI NEW THERMAL POWER STATION		3.05	0.00
112	NLC INDIA LIMITED THERMAL POWER STATION I EXPANSION		1.16	0.00
113	NLC INDIA LIMITED THERMAL POWER STATION II EXPANSION		0.01	0.00
114	NLC INDIA LIMITED THERMAL POWER STATION II STAGE II		0.07	0.00
115	NTPC KUDGI		2.34	0.00
116	NTPC Ramagundam Stage I &II		4.44	0.00
117	NTPC Ramagundam Stage III		1.56	0.00
118	NTPC Simhadri Stage I		0.64	0.00
119	NTPC Simhadri Stage II		1.60	0.00
120	NTPC Talcher Super Thermal Power Station Stage II		3.51	0.00
121	NTPC Telangana		0.52	0.00
122	OSTRO KANNADA POWER PRIVATE LIMITED		16.16	0.00
123	Pondicherry UT		47.63	0.14
124	RENEW SURYA OJAS PRIVATE LIMITED-Wind		12.73	0.00
125	RENEW SURYA ROSHNI PRIVATE LIMITED Koppal PS		11.89	0.00
126	Ramagundam Floating solar		8.14	0.00
127	SEIL ENERGY INDIA LIMITED		30.17	0.00
128	SEIL Energy India Limited Project II		44.07	0.00
129	SIMHAPURI ENERGY LIMITED		17.78	9.11
130	Simhadri FSP 15 MW		2.14	0.00
131	Simhadri Floating solar (10 MW)		1.44	0.00
132	Tamil Nadu		72.61	486.42
133	Telangana		237.93	799.44

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- फ़रवरी 2024
EXCHANGES THROUGH POWER EXCHANGES - FEBRUARY 2024

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
134	ADHUNIK POWER & NATURAL RESOURCES LIMITED	पूर्वी क्षेत्र ER	0.55	0.00
135	Bihar		477.52	5.59
136	Damodar Valley Corporation		31.38	30.95
137	Druk Green Power Corporation Limited (DGPCL-Bhutan)		0.00	352.15
138	GMR KAMALANGA ENERGY LTD-CTU		0.26	0.00
139	IND BARATH ENERGY UTKAL LIMITED		55.39	1.52
140	Jharkhand		79.43	20.88
141	Jindal India Thermal Power Limited		127.93	0.00
142	KANTI BIJLEE UTPADAN NIGAM LIMITED		0.23	0.00
143	Kabeli B-1 Hydro Power Project NEPAL ELECTRICITY AUTHORITY		0.05	0.00
144	NABINAGAR POWER GENERATING COMPANY LIMITED		147.84	0.00
145	NEA Nepal Solu Khola (Dudhkoshi) Hydropower Project		0.44	0.00
146	NEA Nepal Upper Dordi A Hydropower Project		0.05	0.00
147	NEPAL ELECTRICITY AUTHORITY MUZAFFARPUR		0.00	247.51
148	NTPC BARH Stage I		12.81	0.00
149	NTPC BARH Stage II		11.23	0.00
150	NTPC Darlipali		0.72	0.00
151	NTPC Farakka stage I		26.87	0.00
152	NTPC Kahalgaon stage I		8.03	0.00
153	NTPC Kahalgaon stage II		13.70	0.00
154	NTPC North Karanpura STPS		0.47	0.00
155	NTPC North Karanpura STPS infirm (UNIT # 2)		88.87	0.00
156	NTPC Talcher Stage I		0.31	0.00
157	Odisha		408.24	60.75
158	Sikkim		6.94	1.55
159	Tashiding HEP, Shiga Energy Private Limited		0.05	0.00
160	West Bengal		189.49	98.65

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- फ़रवरी 2024
EXCHANGES THROUGH POWER EXCHANGES - FEBRUARY 2024

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
161	AGARTALA GAS BASED POWER STATION	पूर्वोत्तर क्षेत्र NER	0.00	0.00
162	ASSAM GAS BASED POWER STATION		0.63	0.00
163	Arunachal Pradesh		0.05	14.39
164	Assam		10.12	58.84
165	Bongaigaon Thermal Power Station NTPC		1.11	0.00
166	Doyang HPS, NEEPCO		0.04	0.00
167	KAMENG HYDRO POWER STATION		7.72	0.00
168	Kopili Power Station NEEPCO		0.29	0.00
169	Manipur		5.74	8.08
170	Meghalaya		2.56	36.96
171	Nagaland		4.61	4.10
172	Palatana Plant		1.87	0.00
173	Pare Hydro Power Station		0.00	0.00
174	Tripura		13.19	0.57
Total			7349	7349

19. INFORMATION ABOUT RENEWABLE ENERGY
CERTIFICATE MECHANISM

MONTH : FEBRUARY 2024

RE Source & Unit wise break up (01.02.2024-29.02.2024)

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	1	1	0	0
2	Urban or Municipal Waste	0	0	0	0
3	Solar Thermal	0	0	0	0
4	Solar PV	25	11	15	4
5	Small Hydro	100	1	59	1
6	Others	0	0	0	0
7	Geothermal	0	0	0	0
8	Biomass	0	0	0	0
9	Bio-fuel cogeneration	0	0	0	0
	Total	126	13	74	5

RECs Issued (01.02.2024-29.02.2024)

Sr.No.	Non Solar	Solar	Total
1	884955	112682	997637

Redemption of REC (01.02.2024-29.02.2024)

Sr.No.	Non Solar	Solar	Total
1	887419	19914	907333

19. INFORMATION ABOUT RENEWABLE ENERGY
CERTIFICATE MECHANISM
MONTH : FEBRUARY 2024

RE Source & Unit wise break up (Apr'23-Feb'24)

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	419	25	522	28
2	Urban or Municipal Waste	0	0	0	0
3	Solar Thermal	0	0	0	0
4	Solar PV	349	66	283	14
5	Small Hydro	201	9	101	8
6	Others	0	0	0	0
7	Geothermal	0	0	0	0
8	Biomass	5	1	5	1
9	Bio-fuel cogeneration	8	2	23	5
	Total	982	103	934	56

RECs Issued (Apr'23-Feb'24)

Sr.No.	Non Solar	Solar	Total
1	22687331	1027920	23715251

Redemption of REC (Apr'23-Feb'24)

Sr.No.	Non Solar	Solar	Total
1	9260747	733714	9994461

19. INFORMATION ABOUT RENEWABLE ENERGY
CERTIFICATE MECHANISM

MONTH : FEBRUARY 2024

RE Source & Unit wise break up Since Inception to Feb'24

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	3132	530	2975	530
2	Urban or Municipal Waste	0	0	0	0
3	Solar Thermal	0	0	0	0
4	Solar PV	1618	558	1468	479
5	Small Hydro	845	42	757	43
6	Others	4	2	3	1
7	Geothermal	0	0	0	0
8	Biomass	402	37	378	35
9	Bio-fuel cogeneration	823	91	383	55
	Total	6824	1260	5964	1143

RECs Issued since Inception to Feb'24

Sr.No.	Non Solar	Solar	Total
1	110567471	13438658	124006129

Redemption of REC since Inception to Feb'24

Sr.No.	Non Solar	Solar	Total
1	76788932	12362102	89151034

REC Closing balance as on 29.02.2024

Sr.No.	Non Solar	Solar	Total
1	33778539	1076556	34855095

Details of Grid Events during the Month of February 2024 in Northern Region

Sl No.	Category of Grid Event (GI for GI-2/ GD-1 to GD-5)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (H:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t. Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GI-2	Jammu and Kashmir	01-02-2024 01:20	01-02-2024 06:07	04:47	25	0	0.089	0.000	28144	33714	i) As per SCADA SOE, PMU and information received from constituents the sequence of event is as follows: a. At 01:19:18.711hrs, CB of 80MVAR Bus reactor at 400kV Samba(PG) opened. b. At 01:20:31.160 hrs, R-N phase to earth fault is observed as per PMU at Amargah(INDIGRID) (exact reason and location of fault yet to be shared). c. As per PMU, voltage increased to 1.1 p.u. and over-voltage trip command picked-up. However although voltage reduced to 1.075 p.u. after fault but over-voltage trip command didn't get reset (drop-off to pick-up ratio may be reviewed) and after 5 secs. at 01:20:36:160 hrs, 400 KV Ur_1(NH)-Amargah (INDIGRID) Ckt-2 (as per PMU, voltage reached upto ~1.1 p.u. at the time of tripping) tripped on over-voltage. At the same time, active power generation of 60MW Unit-4 at Ur_2(NH) reduced from 63MW to 38MW. ii) As per PMU at Amargah(INDIGRID), R-N phase to earth fault with fault clearing time of 120ms is observed at 01:20hrs. iii) As per SCADA, generation loss of approx. 25MW occurred at Ur_2(NH) at 01:20hrs.	1) 400 KV Ur_1(NH)-Amargah (INDIGRID) (INDIGRID) Ckt-2
2	GD-1	Jammu and Kashmir	01-02-2024 01:50	01-02-2024 02:56	01:06	51	600	0.184	1.837	27750	32660	i) As per SCADA SOE, PMU and information received from constituents the sequence of event is as follows: a. At 01:49:13 hrs, 400 KV Ur_2(NH) Ur_1(NH) (PG) Ckt and 400 KV Ur_2(NH) Wagora (PG) Ckt also tripped on over-voltage. b. This led to tripping of 60MW Unit-4 at Ur_2(NH) (generating ~38MW and absorbing ~32MVA) due to loss of evacuation path. Complete blackout occurred at 400KV Ur_2(NH). c. At 01:50:04 hrs, 400 KV Ur_1(NH)-Amargah(INDIGRID) (INDIGRID) Ckt-1 (As per DR at Amargah end, voltage reached upto ~1.13 p.u. and as per PMU voltage reached upto ~1.17 p.u.), also tripped on over-voltage. d. This led to tripping of 120MW Unit-1 at Ur_1(NH) (generating ~13MW and absorbing ~48MVA) due to loss of evacuation path. Complete blackout occurred at 400KV Ur_1(NH). e. Due to tripping of 120MW Unit-1 at Ur_1(NH) and 60MW Unit-4 at Ur_2(NH) MVAR support lost and voltage further increased. f. After this all other 400KV lines from Amargah(INDIGRID) tripped on over-voltage and supply to 220KV lines also lost which led to complete blackout at 400/220KV Amargah(INDIGRID). g. During the same time, 400KV Kisherpur(PG) Chamera_2(NH) (PG) Ckt and 400 KV Duhast(NH)-Kisherpur(PG) (PG) Ckt-1 also tripped on over-voltage. h. At the same time, 220KV Drass(PG)-Alusteng Ckt also tripped on over-voltage. Power was coming from Alusteng through 220KV Drass(PG)-Alusteng Ckt and it was going to Kargil through 220KV Drass(PG)-Kargil Ckt. Due to tripping of 220KV Drass(PG)-Alusteng Ckt, supply to 220KV Drass(PG) Kargil Ckt lost and complete blackout occurred at 220/66kV Drass(PG). ii) As per SCADA SOE, 220KV Baitasul(NH)-Jassore(HF) Ckt also tripped at the same time (exact reason yet to be shared). iii) As per SCADA, load loss of approx. 600MW is observed in Jammu and Kashmir control area. iv) As per SCADA, generation loss of approx. 38MW occurred at Ur_2(NH) and approx. 13MW occurred at Ur_1(NH) at 01:50hrs.	1) 400 KV Amargah(INDIGRID)-Samba(PG) (INDIGRID) Ckt-1 2) 400 KV Amargah(INDIGRID)-Samba(PG) (INDIGRID) Ckt-2 3) 400 KV Amargah(INDIGRID)-Wagora(PG) (INDIGRID) Ckt-1 4) 400 KV Amargah(INDIGRID)-Wagora(PG) (INDIGRID) Ckt-2 5) 220 KV Amargah(INDIGRID)-Delina(PG) (PG) Ckt-1 6) 220 KV Amargah(INDIGRID)-Delina(PG) (PG) Ckt-2 7) 220 KV Amargah(INDIGRID)-Zankote(PG) (PG) Ckt-1 8) 220 KV Amargah(INDIGRID)-Zankote(PG) (PG) Ckt-2 9) 400 KV Ur_1(NH)-Amargah(INDIGRID) (INDIGRID) Ckt-1 10) 400 KV Ur_1(NH)-Ur_2(NH) (PG) Ckt 11) 400 KV Ur_2(NH)-Wagora (PG) Ckt 12) 120MW Unit-1 at Ur_1(NH) 13) 60MW Unit-4 at Ur_2(NH) 14) 400KV Kisherpur(PG)-Chamera_2(NH) (PG) Ckt 15) 400 KV Duhast(NH)-Kisherpur(PG) (PG) Ckt-1 16) 220KV Baitasul(NH)-Jassore(HF) Ckt 17) 220KV Drass(PG)-Alusteng Ckt
3	GD-1	Punjab	01-02-2024 08:30	01-02-2024 11:21	02:51	0	30	0.000	0.060	44749	50280	i) As reported, at 08:30hrs, bus-bar protection of 220KV Bus 1 at Jamalpur(BB) operated (exact reason, nature and location of fault yet to be shared). ii) Due to bus bar protection operation, all the elements connected to 220KV Bus-1 at Jamalpur(BB) tripped and 220KV Bus-1 at Jamalpur(BB) became dead (Bus-wise arrangement of elements yet to be shared). iii) As reported, 220 KV Bhakra_R-Jamapur (BB) Ckt-1 tripped on Y-N phase to earth fault with fault current of 2.031 kA and fault distance of 66.32km from Bhakra_R(BB); zone-1 distance protection operated at Bhakra_R(BB) end. iv) As per DR of main-1 relay of 220 KV Jalandhar(end)-Jamapur (BB) Ckt-1, Y-N phase to earth fault with fault current of 2.515kA and fault clearing time of 53ms is observed. As per DR of main-2 relay of 220 KV Jalandhar(end)-Jamapur (BB) Ckt-1, B-N phase to earth fault with fault current of 3.358kA and fault clearing time of 70ms is observed; zone-1 distance protection operated at Jalandhar end. (Phase sequence issue is observed in main-2 relay). v) As per PMU at Bhakra_R(BB), Y-N phase to earth fault is observed with fault clearing time of 120ms. vi) As per SCADA, load loss of approx. 30 MW is observed in Punjab control area.	1) 220KV Bus 1 at Jamalpur(BB) 2) 220 KV Jalandhar-Jamapur (BB) Ckt-1 3) 220 KV Bhakra_R-Jamapur (BB) Ckt-1 4) 220 KV Gangwal-Jamapur (BB) Ckt-1 5) 220/66kV 100 MVA ICT-1 at Jamalpur(BB)M 6) 220/66kV 160 MVA ICT-3 at Jamalpur(BB)M 7) 220/132kV 100 MVA ICT-1 at Jamalpur(BB)M
4	GD-1	Himachal Pradesh	02-02-2024 15:27	02-02-2024 16:30	01:03	0	785	0.000	1.616	44573	48586	i) As reported, at 15:27 hrs, 220KV Baddi(HF)-Pinjore(HF) (HPPTCL) Ckt-1 & 2 tripped on R-Y phase to phase fault; zone-1 distance protection operated at Pinjore end. (Exact reason, nature and location of fault yet to be shared). ii) Due to tripping of aforementioned lines, 220 KV Baddi-Kunhar(HF) Ckt-1 & 2, 220 KV Baddi-Upper Nangal(HF) Ckt, 220 KV Baddi-Madhala(HF) Ckt and 220 KV Baddi-Northman(HF) Ckt tripped due to over-loading and 220/66kV Baddi(HF) S/s became dead. iii) During the same time, 220 KV Madhala-Upper Nangal(HF) Ckt, 220 KV Bhabha-Kunhar(HF) Ckt and 220 KV Jeori-Kunhar(HF) Ckt also tripped on over-loading. iv) Further, at 15:34 hrs, all 133kV lines from Kunhar(HF) tripped on over-loading and 220/132kV Kunhar(HF) S/s became dead. v) As per PMU, R-Y phase to phase fault is observed with delayed fault clearing time of 400ms. vi) As per SCADA, total change in demand of approx. 785MW in HP control area is observed.	1) 220KV Baddi(HF)-Pinjore(HF) (HPPTCL) Ckt-1 2) 220KV Baddi(HF)-Pinjore(HF) (HPPTCL) Ckt-2 3) 220 KV Baddi-Kunhar(HF) Ckt-1 4) 220 KV Baddi-Kunhar(HF) Ckt-2 5) 220 KV Baddi-Upper Nangal(HF) Ckt 6) 220 KV Baddi-Madhala(HF) Ckt 7) 220 KV Baddi-Wardthman(HF) Ckt 8) 220 KV Madhala-Upper Nangal(HF) Ckt 9) 220 KV Bhabha-Kunhar(HF) Ckt 10) 220 KV Jeori-Kunhar(HF) Ckt
5	GI-2	Uttar Pradesh	05-02-2024 23:58	06-02-2024 00:53	00:55	0	170	0.000	0.447	30345	38002	i) During antecedent condition, 400/220KV 500MVA ICT-2, 220/132kV 160MVA ICT-3 and 4 at Rasra(UP) was carrying approx. 180MW, 30MW and 30MW respectively. 400/220KV 500MVA ICT-1 at Rasra(UP) was not in service. ii) As reported, at 23:58 hrs, bus bar protection operated at both the 220KV buses of 400/220/132kV Rasra(UP) indicating flag "Low gas pressure zone-1". iii) Due to this, all 220KV cts and 400/220KV ICT-2 and 220/132kV ICT-3 & 4 tripped and both the 220KV buses at Rasra(UP) became dead. iv) During inspection, low gas pressure was not found in GIS physically and the flag was reset. It seems that the relay mal-operated due to which this tripping occurred. v) As per PMU at Balia(PG), no fault is observed in the system. vi) As per SCADA, load loss of approx. 170MW is observed in UP control area.	1) 400/220KV 500MVA ICT-2 at Rasra(UP) 2) 220/132kV 160MVA ICT-3 at Rasra(UP) 3) 220/132kV 160MVA ICT-4 at Rasra(UP) 4) 220KV Rasra-Rasra_220(UP) Ckt 5) 220KV Rasra-Bhadural(UP) Ckt-1 6) 220KV Rasra-Bhadural(UP) Ckt-2 7) 220KV Rasra-Ghazipur(UP) Ckt
6	GD-1	Delhi	06-02-2024 10:10	06-02-2024 11:24	01:14	477	587	0.957	0.989	49866	59355	i) During antecedent condition, 400KV interconnectors 41952 and 42352 between 400KV Buses at Bawana(DTL) and 400KV Buses at Bawana(CGTB)(PGCL) were in off position. 400/220KV 315MVA ICT-1, A, S & 6 were connected to Bawana(CGTB)(PGCL) and 315 MVA ICT-2 & 3 were connected to Bawana(DTL). 216 MW Bawana GPS - UNIT 2 (GT-2) & 4 (GT-4) and 253.6 MW Bawana GPS - UNIT 5 (STG-1) & 6 (STG-2) were generating approx. 145MW, 154MW, 88MW and 50MW respectively. 216 MW Bawana GPS - UNIT 1 (GT-1) & 3 (GT-3) were in back-charged condition for meeting the station auxiliary supply. ii) As reported, at around 10:10 hrs, heavy sparking and flash over were observed in 400 KV switchyard of CGT Bawana. On inspection it was found that Y - phase drop down jumper of bay 413 (400 KV Bawana CGT(B)(PGCL)-Bahadurgah(PG) (PG) Ckt) snapped from Jack Bus and fell on the support structure which led to fault in 400 KV Bawana CGT(B)(PGCL) - Bus 2. iii) Since, the Bus Bar Protection was out of service, both 400 KV Bawana CGT(B)(PGCL)-Bhiwani(PG) (PG) Ckt and 400 KV Bawana CGT(B)(PGCL)-Bahadurgah(PG) (PG) Ckt sensed the fault in 24 (reverse zone) and tripped after a time interval of 560ms from Bawana end. Although the fault was on Bus-2, yet both the line sensed the fault since the CB was in closed position. iv) During antecedent condition, 220 KV Mandola(PG)-Narela(DV) (DTL) Ckt-1 & 2, 220 KV DSOC-Narela(DV) (DTL) Ckt-1 & 2 and 220/66kV 100MVA ICT-1, 2 & 3 at Narela(DTL) were connected to 220KV Bus-1 at Narela(DTL) and 220 KV Panipat(BB)-Narela(DV) (DTL) Ckt-1, 2 & 3 and 220 KV Rohtak Road-Narela(DV) (DTL) Ckt-1 & 2 were connected to 220KV Bus-2 at Narela(DTL). 220KV Bus coupler was in off position. v) As reported, at 10:29 Hrs, bus bar protection operated at 220KV Bus-1 at Narela(DTL) as PG clamp of B-phase conductor of Bus-1 got damaged creating bus fault on B-ph near ICT 2 bay. vi) Due to operation of bus-bar protection, all the elements connected to 220KV Bus-1 at Narela(DTL) tripped and Bus-1 became dead. vii) As reported by SDC Dehi, the load of 220KV Narela S/s, Bhalwa 2, Badi, IFC Narela, A-7 Narela, A.L.R. Kham Pur, DSOC Narela-I got affected. viii) As per PMU, R-B phase to phase fault with fault clearing time of 120ms is observed. ix) As per SCADA, change in demand of approx. 270MW is observed in Delhi control area, but as reported by SDC Dehi, load loss of approx. 126MW is observed which was normalized within 35 minutes. x) As reported, at 11:04hrs, load was normalized on 220KV Bus-2 at Narela(DTL).	1) 400 KV Bawana CGT(B)(PGCL)-Bhiwani(PG) (PG) Ckt 2) 400 KV Bawana CGT(B)(PGCL)-Bahadurgah(PG) (PG) Ckt 3) 216 MW Bawana GPS - UNIT 2 (GT-2) 4) 216 MW Bawana GPS - UNIT 4 (GT-4) 5) 253.6 MW Bawana GPS - UNIT 5 (STG-1) 6) 253.6 MW Bawana GPS - UNIT 6 (STG-2) 7) 400/220KV 315MVA ICT-1 at Bawana(DV) 8) 400/220KV 315MVA ICT-4 at Bawana(DV) 9) 400/220KV 315MVA ICT-5 at Bawana(DV) 10) 400/220KV 315MVA ICT-6 at Bawana(DV)
7	GI-1	Delhi	06-02-2024 10:29	06-02-2024 11:04	00:35	0	126	0.000	0.213	50745	59286	i) 220/66kV Narela(DTL) has double main bus scheme. ii) During antecedent condition, 220 KV Mandola(PG)-Narela(DV) (DTL) Ckt-1 & 2, 220 KV DSOC-Narela(DV) (DTL) Ckt-1 & 2 and 220/66kV 100MVA ICT-1, 2 & 3 at Narela(DTL) were connected to 220KV Bus-1 at Narela(DTL) and 220 KV Panipat(BB)-Narela(DV) (DTL) Ckt-1, 2 & 3 and 220 KV Rohtak Road-Narela(DV) (DTL) Ckt-1 & 2 were connected to 220KV Bus-2 at Narela(DTL). 220KV Bus coupler was in off position. iii) As reported, at 10:29 Hrs, bus bar protection operated at 220KV Bus-1 at Narela(DTL) as PG clamp of B-phase conductor of Bus-1 got damaged creating bus fault on B-ph near ICT 2 bay. iv) Due to operation of bus-bar protection, all the elements connected to 220KV Bus-1 at Narela(DTL) tripped and Bus-1 became dead. v) As reported by SDC Dehi, the load of 220KV Narela S/s, Bhalwa 2, Badi, IFC Narela, A-7 Narela, A.L.R. Kham Pur, DSOC Narela-I got affected. vi) As per PMU, R-B phase to phase fault with fault clearing time of 120ms is observed. vii) As per SCADA, change in demand of approx. 270MW is observed in Delhi control area, but as reported by SDC Dehi, load loss of approx. 126MW is observed which was normalized within 35 minutes. viii) As reported, at 11:04hrs, load was normalized on 220KV Bus-2 at Narela(DTL).	1) 220 KV Mandola(PG)-Narela(DV) (DTL) Ckt-1 2) 220 KV Mandola(PG)-Narela(DV) (DTL) Ckt-2 3) 220 KV DSOC-Narela(DV) (DTL) Ckt-1 4) 220 KV DSOC-Narela(DV) (DTL) Ckt-2 5) 220/66kV 100MVA ICT-1 at Narela(DTL) 6) 220/66kV 100MVA ICT-2 at Narela(DTL) 7) 220/66kV 100MVA ICT-3 at Narela(DTL) 8) 220KV Bus-1 at Narela(DTL)
8	GD-1	Himachal Pradesh	08-02-2024 10:41	08-02-2024 10:59	00:18	0	525	0.000	0.901	49687	58261	i) During antecedent condition, as per SCADA, power was flowing towards Kunhar through 220 KV Bhabha-Kunhar(HF) Ckt and 220 KV Baddi-Kunhar(HF) Ckt-1 & 2 carrying approx. 143MW, 115MW and 115MW. Approx. 31MW was going from Kunhar to Jeori through 220 KV Jeori-Kunhar(HF) Ckt and 220/132kV 100MVA ICT-1 & 2 at Kunhar(HF) were carrying approx. 170MW each. Bus coupler was in off position at 220KV Baddi(HF). ii) As reported, at 10:41 hrs, 220 KV Bhabha-Kunhar(HF) Ckt tripped on B-N phase to earth fault. (Exact reason, nature and location of fault yet to be shared). iii) Due to tripping of this line, 220 KV Baddi-Kunhar(HF) Ckt-1 & 2 and 220 KV Jeori-Kunhar(HF) Ckt tripped due to over-loading and 220/66kV Kunhar(HF) S/s became dead. iv) During this time, 220 KV Baddi-Upper Nangal(HF) Ckt, 220 KV Baddi-Madhala(HF) Ckt and 220 KV Baddi-Wardthman(HF) Ckt also tripped due to over-loading and 220KV Bus-1 at Baddi(HF) became dead. v) As per SCADA SOE, 220/66kV 31.5MVA ICT-1 at Jeori(HF) tripped during the same time. (Exact reason yet to be shared). vi) As per PMU, B-N phase to earth fault is observed with fault clearing time of 80ms. vii) As per SCADA, change in demand of approx. 525MW in HP control area is observed.	1) 220 KV Bhabha-Kunhar(HF) Ckt 2) 220 KV Jeori-Kunhar(HF) Ckt 3) 220 KV Baddi-Kunhar(HF) Ckt-1 4) 220 KV Baddi-Kunhar(HF) Ckt-2 5) 220 KV Baddi-Upper Nangal(HF) Ckt 6) 220 KV Baddi-Madhala(HF) Ckt 7) 220 KV Baddi-Wardthman(HF) Ckt

Details of Grid Events during the Month of February 2024 in Northern Region

Sl No.	Category of Grid Event (GI for GI-2/GD-1 to GD-5)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (H:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t. Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
9	GD-1	Haryana	08-02-2024 16:22	08-02-2024 16:45	00:23	547	160	1.214	0.343	45045	46699	i) During antecedent condition, 220kV DCRTPP-Rampur Ckt-1 was under construction (ILO) in place of DCRTPP-Abdulpur Ckt and 220kV DCRTPP-Rampur Ckt-2 was under shutdown. 220kV DCRTPP(HS)-Jorah(HR) ckt-1 & 2, 220kV DCRTPP(HS)-Bakana(HR) ckt-1 & 2 and 220kV DCRTPP(HS)-Unisapur(HR) ckt-1 & 2 were carrying approx. 188MW, 183MW, 47MW, 56MW, 30MW and 31MW respectively. ii) As reported, at 16:12hrs, 220kV DCRTPP(HR)-Jorah(HR) ckt-2 tripped due to snapping of R-ph jumper at tower location no. 8. Simultaneously, 220kV DCRTPP(HR)-Jorah(HR) ckt-1 tripped on over-loading. iii) After this, load shifted to remaining four ckt. 220kV DCRTPP(HR)-Bakana(HR) ckt-1 & 2 and 220kV DCRTPP(HS)-Unisapur(HR) ckt-1 & 2 were carrying approx. 192MW, 202MW, 74MW and 74MW respectively. Power was flowing from 220kV DCRTPP(HR) to Bakana(HR) through 220kV DCRTPP(HS)-Bakana(HR) D/C to Salempur(HR) through 220kV Bakana(HR) Salempur(HR) D/C and 220kV DCRTPP(HR) to Unisapur(HR) through 220kV DCRTPP(HS)-Unisapur(HR) D/C to Kamal(HR) through 220kV Unisapur(HR)-Kamal(HR) S/C. iv) As further reported, at 16:22hrs, 220kV Kamal(HR)-Unisapur(HR) ckt (carrying ~123MW) tripped on transient fault (exact nature and location of fault yet to be shared). v) After this, 220kV DCRTPP(HR)-Bakana(HR) ckt-1 & 2 and 220kV Bakana(HR) Salempur(HR) ckt-1 & 2 were carrying approx. 253MW, 263MW, 239MW and 233MW respectively. vi) During the same time, 220kV Salempur(HR)-Bakana(HR) ckt-2 also tripped due to breaking of 1-ph conductor at tower location no. 83. vii) Due to this tripping, DCRTPP(HS)-Bakana(HR) ckt-1 & 2, 220kV Bakana(HR) Salempur(HR) ckt-1 & 2 and 220kV DCRTPP(HS)-Unisapur(HR) ckt-1 & 2 tripped on over-loading. Complete blackout occurred at 220kV Bakana(HR) and Unisapur(HR) S/s. viii) Due to tripping of all the evacuating lines a DCRTPP, 300 MW DCRTPP (Yamuna Nagar) - UNIT 1 & 2 also tripped and complete blackout occurred at 220kV DCRTPP(HR) S/s. ix) As per PMU at Abdulpur(PG), R-ph phase to phase fault is observed with fault clearing time of 80ms. x) As per SCADA, load loss of approx. 160 MW in Haryana control area and generation loss of approx. 547 MW at 220kV DCRTPP Yamunanagar(HR) are observed. xi) Supply at 220kV DCRTPP(HR) and Unisapur(HR) was restored within 23 minutes and Supply at Bakana(HR) was restored within 30 minutes.	1) 220kV DCRTPP(HR)-Jorah(HR) ckt-2 2) 220kV DCRTPP(HR)-Jorah(HR) ckt-1 3) 220kV Kamal(HR)-Unisapur(HR) ckt 4) 220kV Salempur(HR)-Bakana(HR) ckt-2 5) 220kV DCRTPP(HS)-Unisapur(HR) ckt-1 6) 220kV DCRTPP(HS)-Unisapur(HR) ckt-2 7) 220kV Salempur(HR)-Bakana(HR) ckt-1 8) 220kV DCRTPP(HR)-Bakana(HR) ckt-1 9) 220kV DCRTPP(HR)-Bakana(HR) ckt-2 10) 300 MW DCRTPP (Yamuna Nagar) - UNIT 1 11) 300 MW DCRTPP (Yamuna Nagar) - UNIT 2
10	GD-1	Rajasthan	14-02-2024 09:49	14-02-2024 18:23	08:34	45	0	0.089	0.000	50457	62135	i) Generation of 220kV AHEJAL PSS-3 RE stations evacuates through 220 KV Adani RenewPark_SL_FGARH_FBTL (AREPR) - AHEJAL PSS 3 HB_FGRAH_FBTL (AHEJAL) (AREPR) Ckt. During antecedent condition, AHEJAL PSS 3 RE station was generating approx. 45MW as per SCADA. ii) As reported, at 09:49hrs, 220 KV Adani RenewPark_SL_FGARH_FBTL (AREPR) AHEJAL PSS 3 HB_FGRAH_FBTL (AHEJAL) (AREPR) Ckt tripped on mal-operation of relay leading to Bay-20A CB trip (exact reason yet to be shared). iii) As per PMU at AHEJAL, R-B phase to phase fault is observed with fault clearing time of 80ms. Voltage dropped to ~0.91 p.u. during the fault. iv) As per PMU, due to tripping of 220kV AHEJAL PSS-3 line, RE (wind) generation (~45MW) of the RE station lost due to loss of evacuation path.	1) 220 KV Adani RenewPark_SL_FGARH_FBTL (AREPR) AHEJAL PSS 3 HB_FGRAH_FBTL (AHEJAL) (AREPR) Ckt
11	GD-1	Himachal Pradesh	16-02-2024 11:30	16-02-2024 11:36	00:06	40	400	0.073	0.645	54781	62049	i) During antecedent condition, as per SCADA, power was flowing towards Kunihar through 220kV Jeori-Kunihar(HP) Ckt, 220 KV Wangtoo-Bhabha-Kunihar(HP) ckt (T-connection) and 220 KV Baddi-Kunihar(HP) Ckt-1 & 2 carrying approx. 91MW, 99MW, 57MW and 58MW. 220/132kV 80/100MVA ICT-1 & 2 at Kunihar(HP) were carrying approx. 150MW each. Bus coupler was in off position at 220kV Baddi(HP). ii) As reported, at 11:30 hrs, 220kV Jeori-Kunihar(HP) Ckt tripped from Jeori end on R-N phase to earth fault with fault current of 1.537kA and fault distance of 9.76m from Jeori end. (Exact reason of fault yet to be shared). At the same time, 220kV Jeori-Bhabha(HP) Ckt also tripped on the same fault resulting into blackout at 220/66kV Jeori(HP) S/s. iii) On inspection it was found that a stone crusher office was laying internet cable near Bayal below tower no. 110 span, due to which 220kV Jeori-Kunihar(HP) Ckt came in induction zone of the line and the line tripped. It was also reported that a person got injured due to same and notice by concerned office was served to the defaulting party. iv) As further reported, bus coupler was in on position at that time at Bhabha(HP). Hence fault was sensed by 220 KV Wangtoo-Bhabha-Kunihar(HP) ckt (T-connection) and line tripped from Wangtoo end. v) Due to tripping of these two lines, 220 KV Baddi-Kunihar(HP) Ckt-1 & 2 tripped due to over-loading and 220/66kV Kunihar(HP) S/s became dead. vi) During this time, 220 KV Baddi-Upper Nangal(HP) Ckt, 220 KV Baddi-Madhala(HP) Ckt and 220 KV Baddi-Wardthman(HP) Ckt also tripped due to over-loading and 220kV Bus-1 at Baddi(HP) became dead. vii) As per SCADA SOE, 220/66kV 31.5MVA ICT-1 at Jeori(HP) and 220/11kV 3X13MVA ICT-2 at Mori(HP) tripped during the same time. (Exact reason yet to be shared) viii) As per PMU, R-N phase to earth fault is observed with delayed fault clearing time of 560ms. ix) As per SCADA, change in demand of approx. 510MW and change in generation of approx. 50MW in HP control area is observed. But as reported by, SDC-HP, load loss of ~400MW (320MW at Kunihar feeding load of Solan and Shimla) and generation loss of ~400MW (20MW in Bhabha and 20MW in Giri) occurred in HP control area.	1) 220 KV Bhabha-Kunihar(HP) ckt 2) 220 KV Jeori-Kunihar(HP) Ckt 3) 220 KV Baddi-Kunihar(HP) Ckt-1 4) 220 KV Baddi-Kunihar(HP) Ckt-2 5) 220 KV Baddi-Upper Nangal(HP) Ckt 6) 220 KV Baddi-Madhala(HP) Ckt 7) 220 KV Baddi-Wardthman(HP) Ckt 8) 220 KV Jeori-Bhabha(HP) Ckt
12	GD-1	Jammu and Kashmir	19-02-2024 19:19	19-02-2024 20:20	01:01	0	260	0.000	0.485	41035	53652	i) 220/66kV Drass(PG) have double main bus arrangement at 220kV side. ii) During antecedent condition, approx. 25MW power was coming from Alusteng to Drass and approx. 23MW power was going out from Drass to Kargil. iii) As reported, at 19:19 hrs, 220 KV Alusteng-Drass (PG) Ckt tripped on R-N phase to earth fault with distance of 96km from Drass end. iv) Due to this tripping supply to 220 KV Drass (PG) Kargil Ckt was lost and blackout occurred at 220/66kV Drass(PG) S/s. v) As per PMU at Amarghar, R-N phase to earth fault is observed with fault clearing time of 280ms. vi) As per SCADA, change in demand of approx. 260MW is observed in J&K control area.	1) 220 KV Alusteng-Drass (PG) Ckt
13	GD-1	Himachal Pradesh	20-02-2024 17:32	20-02-2024 19:41	02:09	0	45	0.000	0.091	45200	49340	i) During antecedent condition, no generation was there at Baraisal(NH). ii) As reported, at 17:32hrs, 220 KV Baraisal(NH)-Pong (BB)(PG) ckt tripped on 3-phase to earth fault (zone-2 distance protection operated at Pong(BB)) end with fault distance of 76.55km and fault current of I_r=7.602kA, I_p=3.122kA and I_b=3.293kA from Pong(BB) end. iii) During the same time, 220 KV Baraisal(NH)-Jessore (HP)(PG) Ckt also tripped on 3-phase to earth fault (fault sensed in zone-2 at Jessore(HP)) end with fault distance of 54.22km and fault current of I_r=5.513kA, I_p=2.77kA and I_b=2.56kA from Jessore(HP) end. iv) As per DR of 220 KV Baraisal(NH) end-Jessore(HP) (PG) Ckt, R-B double phase to earth fault is observed with fault current of I_r=2.845kA and I_b=3.093kA from Baraisal(NH) end. Fault sensed in zone-1 at Baraisal(NH) end. Fault clearing time was approx. 54ms. v) As per PMU at Jalandhar(PG), 3-phase to earth fault is observed with fault clearing time of 80ms. vi) As per SCADA, load loss of approx. 45MW is observed in HP control area.	1) 220 KV Baraisal(NH)-Pong (BB)(PG) ckt 2) 220 KV Baraisal(NH)-Jessore (HP)(PG) ckt
14	GI-2	Uttar Pradesh	20-02-2024 21:47	20-02-2024 22:51	01:04	0	0	0.000	0.000	35580	44516	i) 765/400/220kV Unnao(UP) has double main and transfer bus scheme at 400kV level. ii) During antecedent condition, 400 KV Agra-Unnao (UP) Ckt, 400 KV Unnao-Lucknow (UP) Ckt, 400 KV Bareilly-Unnao (UP) Ckt-2, 400 KV Unnao(UPI)-Jehta_Hardoi Road (UP) (PG) Ckt 2, 400/220 KV 315 MVA ICT 1 at Unnao(UP), 765/400 KV 1000 MVA ICT 2 and 3 at Unnao(UP) were connected to 400KV Bus 1 at Unnao(UP) and rest of the elements were connected to 400KV Bus 2 at Unnao(UP). iii) As per SCADA, 400/220 KV 315 MVA ICT 1 at Unnao(UP), 765/400 KV 1000 MVA ICT 2 and 3 at Unnao(UP) were carrying approx. 151MW, 518MW and 535MW respectively. iv) As reported, at 21:47 hrs, LBB operated due to fault at Main Ckt of 400 KV Bareilly-Unnao (UP) Ckt-2. Hence all the elements connected to 400KV Bus 1 at Unnao(UP) tripped and 400KV Bus 1 at Unnao(UP) became dead. v) As per DR of 400 KV Bareilly-Unnao (UP) Ckt-2, R-N phase to earth fault is observed with fault current of 6.135kA from Unnao(UP) and 2.197kA from Bareilly(UP). Fault was sensed in zone-1 at Unnao(UP) end. Fault was cleared within 280ms from Unnao(UP) end and 130ms from Bareilly(UP) end. vi) As per PMU at Unnao(UP), R-ph phase to earth fault is observed with fault clearing time of 280ms. vii) As per SCADA, no change in demand is observed in UP control area.	1) 400 KV Agra-Unnao (UP) Ckt 2) 400 KV Unnao-Lucknow (UP) Ckt 3) 400 KV Bareilly-Unnao (UP) Ckt-2 4) 400 KV Unnao(UP)-Jehta_Hardoi Road (UP) (PG) Ckt-2 5) 400/220 KV 315 MVA ICT 1 at Unnao(UP) 6) 765/400 KV 1000 MVA ICT 2 at Unnao(UP) 7) 765/400 KV 1000 MVA ICT 3 at Unnao(UP) 8) 400KV Bus 1 at Unnao(UP)
15	GD-1	Jammu and Kashmir	21-02-2024 10:00	21-02-2024 11:50	01:50	0	115	0.000	0.205	49115	56164	i) 220/66kV Drass(PG) have double main bus arrangement at 220kV side. ii) During antecedent condition, approx. 47MW power was coming from Alusteng to Drass and approx. 45MW power was going out from Drass to Kargil. iii) As reported, at 10:00 hrs, 220 KV Alusteng-Drass (PG) Ckt tripped on R-N phase to earth fault with fault current of 2kA and 2.2kA from Alusteng end in R and B phases respectively and fault distance of 63km from Alusteng end and 48km from Drass end. iv) Due to this tripping supply to 220 KV Drass (PG)-Kargil Ckt was lost and blackout occurred at 220/66kV Drass(PG) S/s. v) As per PMU at Amarghar, R-B phase to phase fault is observed with fault clearing time of 80ms. vi) As per SCADA, change in demand of approx. 115MW is observed in J&K control area.	1) 220 KV Alusteng-Drass (PG) Ckt
16	GD-1	Punjab	24-02-2024 10:31	24-02-2024 12:03	01:32	123	70	0.231	0.116	53134	60108	i) During antecedent condition, 220 KV Ludhiana(PG)-Dandhari Kalan(PS) Ckt was not in service. 126MW Unit-3 at Bhakra(BBMB) was generating approx. 126MW. ii) As reported, at 10:31hrs, 1-phase jumper (exact location yet to be shared) of 220 KV Lathon Kalan(PS)-Dandhari Kalan(PS) (PSTCL) Ckt snapped. CB didn't open from Dandhari Kalan end, due to which 220 KV Jamalpur(BB)-Dandhari Kalan(PS) (PSTCL) Ckt-1 & 2 tripped from Jamalpur(BB) end on back-up earth fault protection operation. iii) As 220 KV Ludhiana(PG)-Dandhari Kalan(PS) Ckt was not in service and 220 KV Lathon Kalan(PS)-Dandhari Kalan(PS) (PSTCL) Ckt, 220 KV Jamalpur(BB)-Dandhari Kalan(PS) (PSTCL) Ckt-1 & 2 already tripped, hence complete blackout occurred at 220kV Dandhari Kalan(PS) S/s. iv) During the same time, as per DR, bus bar protection (zone-2) operated at 220kV Bus 1 at Jamalpur(BB) (exact reason yet to be shared) and all other elements connected to Bus-3 tripped and Bus-3 became dead (Bus-wise arrangement of elements yet to be shared). v) As per SCADA SOE, 126MW Unit-3 at Bhakra(BBMB) tripped during the same time (exact reason yet to be shared). vi) As per PMU at Jalandhar(PG), no fault is observed in the system. vii) As per SCADA, generation loss of approx. 123 MW is observed at Bhakra(BBMB). viii) As per SCADA, load loss of approx. 70 MW is observed in Punjab control area.	1) 220 KV Lathon Kalan(PS)-Dandhari Kalan(PS) (PSTCL) Ckt 2) 220 KV Gangwal-Jamalpur (BB) Ckt-2 3) 220 KV Jamalpur(BB)-Sangrur(PS) (BB) Ckt-2 4) 220 KV Jamalpur(BB)-Dandhari Kalan(PS) (PSTCL) Ckt-1 5) 220 KV Jamalpur(BB)-Dandhari Kalan(PS) (PSTCL) Ckt-2 6) 220KV Bus 3 at Bhakra(BB) 7) 126MW Unit-3 at Bhakra(BB)
17	GI-2	Rajasthan	25-02-2024 12:55	25-02-2024 14:08	01:13	1890	545	3.714	0.942	50888	57861	i) During antecedent condition, MVA power flows of 400/220 KV 500 MVA ICT 1, 2 & 3 at Bhadla(RS) were 417MVA, 452MVA and 454MVA respectively as per SCADA. ii) As reported, at 12:55hrs, 400/220 KV 500 MVA ICT 1 at Bhadla(RS) tripped due to burning of isolator (exact reason, nature and location of fault yet to be shared) iii) Due to this tripping, 400/220 KV 500 MVA ICT 2 & 3 at Bhadla(RS) got overloaded and tripped due to over-current protection operation. iv) As per PMU at Bikaner(PG), R-ph phase to phase fault converted to 3-phase fault is observed with delayed fault clearance time of 880 ms. v) As per SCADA, change in demand of approx. 545MW is observed in Rajasthan control area. vi) As per SCADA, change in NR total solar generation of approx. 3495MW is observed.	1) 400/220 KV 500 MVA ICT 1 at Bhadla(RS) 2) 400/220 KV 500 MVA ICT 2 at Bhadla(RS) 3) 400/220 KV 500 MVA ICT 3 at Bhadla(RS)

Details of Grid Events during the Month of February 2024 in Northern Region



Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
18	GD-1	Uttar Pradesh	27-02-2024 13:57	27-02-2024 14:11	00:14	580	0	1.199	0.000	48368	52560	i) During antecedent condition, 500MW Anpara-D TPS Unit-1&2 were generating approx. 285MW & 295MW respectively and evacuating from 765kV Anpara_D-Obra_C ckt carrying approx 582MW. ii) As reported, at 13:57hrs, R-N phase to earth fault occurred on 765kV Anpara_D-Obra_C ckt. Fault distance was ~18.5km from Obra_C end, 2-1 from Obra_C end and 2-2 from Anpara_D end. On this fault, 765kV Anpara_D-Obra_C ckt tripped from both ends however, delayed clearance occurred at Anpara_D end. iii) At the same time, 765 kV Anpara_C(LAN)-Anpara_D(LUP) (LUP) Ckt-1 tripped from Anpara_C end and 400 KV Anpara-Anpara_D (LUP) Ckt-1&2 tripped from Anpara end on O/C E/F protection operation. Protection setting of O/C E/F protection in these lines need to be reviewed. iv) With the tripping of aforementioned lines, 500MW Unit-1&2 at Anpara_D TPS tripped due to loss of evacuation path. v) As per PMU at Anpara TPS, R-N phase to earth fault with delayed clearance of 480ms is observed. vi) As per SCADA, loss of generation of approx. 580MW is observed at Anpara_D TPS in UP control area.	1) 765 KV Anpara_D(LUP) - Bus 1 2) 765 KV Anpara_D(LUP) - Bus 2 3) 765/400 KV 1000 MVA ICT 1 at Anpara_D(LUP) 4) 765 KV Obra_C_TPS-Anpara_D (LUP) ckt 5) 765 KV Anpara_C(LAN)-Anpara_D(LUP) (LUP) Ckt-1 6) 500 MW Anpara-D TPS - UNIT 1 7) 500 MW Anpara-D TPS - UNIT 2 8) 400 KV Anpara-Anpara_D (LUP) Ckt-1 9) 400 KV Anpara-Anpara_D (LUP) Ckt-2
19	GI-2	Rajasthan	28-02-2024 06:58	28-02-2024 07:38	00:40	0	680	0.000	1.314	42410	51769	i) During antecedent condition, 220 KV Bassi(PG)-Dausa(RS) (PG) Ckt-1 & 2 were carrying approx. 205MW towards Dausa and 400/220 KV 315 MVA ICT 1 & 2 at Hindaun(RS) were carrying approx. 257MW & 238MW respectively. ii) As reported, at 06:58hrs, 220 KV Bassi(PG)-Dausa(RS) (PG) Ckt-1 tripped due to snapping of B-ph dropper conductor at Dausa end. Due to tripping of 220 KV Bassi(PG)-Dausa(RS) (PG) Ckt-1, loading of 220kV Anta-Sakarpura ckt and 220 KV Bassi(PG)-Dausa(RS) (PG) Ckt-2 increased. Further, 220kV Anta-Sakarpura ckt and 220 KV Bassi(PG)-Dausa(RS) (PG) Ckt-2 also tripped from Sakarpura and Dausa end respectively due to overloading. Exact details of protection operation yet to be received. iii) Due to tripping of aforementioned lines, load of Dausa now started drawing power from Hinduan leading to overloading of 400/220KV ICTs at Hinduan and ICT-1&2 at Hindaun tripped on over current protection operation. iv) As per PMU at Bassi(PG), no fault in system is observed. v) As per SCADA, change in demand of approx. 680MW is observed in Rajasthan control area.	1) 220 KV Bassi(PG)-Dausa(RS) (PG) Ckt-1 2) 220 KV Bassi(PG)-Dausa(RS) (PG) Ckt-2 3) 220 KV Anta(NT)-Sakarpura(RS) (RS) Ckt-1 4) 400/220 KV 315 MVA ICT 1 at Hindaun(RS) 5) 400/220 KV 315 MVA ICT 2 at Hindaun(RS)
20	GI-2	Rajasthan	28-02-2024 18:16	28-02-2024 20:35	02:19	200	0	0.487	0.000	41038	50247	i) During antecedent condition, 250MW Suratgarh TPS Unit-3,4&5 were generating approx. 153MW, 203MW & 205MW respectively. 400/220KV ICT-2 was under shutdown and 250MW Unit-6 was not in service. ii) As reported, at 18:16hrs, Bus bar protection of 400kV Bus-2 at Suratgarh TPS operated. Event occurred during renovation work of protection system of ICT-2. During investigation, LBB cable of ICT-2 coming to bus bar panel was found earth. Due to operation of bus bar protection of 400kV Bus-2 at Suratgarh, 400 KV Suratgarh SCTPS(RVUN)-Suratgarh(RS) (RS) Ckt-2, 400 KV Suratgarh(RVUN)-Ratangarh(RS) (RS) Ckt-1 and 250 MW Suratgarh TPS - UNIT 4 tripped. All these elements were connected to 400kV Bus-2 at Suratgarh S/S. iii) As per PMU at Bikaner2(PG), no fault in system is observed. iv) As per SCADA, loss of generation of approx. 200MW is observed at Suratgarh TPS due to tripping of 250MW Suratgarh TPS Unit-4 in Rajasthan control area.	1) 400 KV Suratgarh SCTPS(RVUN)-Suratgarh(RS) (RS) Ckt-2 2) 400 KV Suratgarh(RVUN)-Ratangarh(RS) (RS) Ckt-1 3) 250 MW Suratgarh TPS - UNIT 4

Details of Grid Events during the Month of February 2024 in Western Region



Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t. Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI for GI-2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GI-1	WR	13:22 / 02-02-2024	14:26 / 02-02-2024	01:04	-	26	-	0.04%	73800	68305	At 13:22 Hrs / 02-02-2024, Flashover of Y-phase Potential Transformer of 220 kV Kharghar-Bus-1 resulted in tripping of 220 kV Kharghar-Bus-1 and all connected elements on busbar protection operation. Load loss of around 26 MW occurred due to the event.	Tripping of following elements: 1. 220 kV Kharghar-Bus-1 2. 220 kV Kharghar-Uran-1 3. 220 kV Kharghar-Panvel 4. 220 kV Kharghar-Sonikhar 5. 220 kV Kharghar-Bornell(M)-1 6. 400/220 kV 315 MVA Kharghar ICT-3 7. 220 kV Bhuj-Gadhisa
2	GD-1	WR	20:01 / 04-02-2024	02:05 / 05-02-2024	06:04	29	-	0.04%	-	68384	58109	At 20:01 Hrs / 04-02-2024, 220 kV Bhuj-Gadhisa and 220 kV Bhuj-Baranda tripped on Y-E fault and B-E fault respectively due to falling of conductor on gantry at Bhuj End. Generation loss of 24 MW and 5 MW reported at Baranda (ASPL) and Gadhisa (Renew AP2) Wind Power Plants respectively.	Tripping of following elements: 1. 220 kV Bhuj-Baranda 2. 220 kV Bhuj-Gadhisa
3	GD-1	WR	18:01 / 05-02-2024	19:55 / 05-02-2024	01:54	6	-	0.01%	-	75788	66658	At 18:01 Hrs / 05-02-2024, 220 kV Bhuj-Kotda Madh tripped on B-E fault from Kotda Madh end only, auto recloser successfully operated from Bhuj end. Generation loss of 6 MW occurred at Kotda Madh (Alfanar) wind power plant due to loss of evacuation path.	Tripping of following elements: 1. 220 kV Kotda Madh-Bhuj
4	GD-1	WR	09:41 / 06-02-2024	10:04 / 06-02-2024	00:23	-	500	-	0.69%	78442	72530	At 09:41 Hrs / 06-02-2024, Flashover in B-phase bus side isolator of 400 kV Gandhar-Hazira-2 at Gandhar end resulted in bus bar protection operation at 400 kV Gandhar-Bus-1 and tripping of all connected elements. 400 kV Hazira-Bus-1&2 also tripped as 400 kV Gandhar-Hazira-1 was already under planned shutdown since 09:07 hrs / 06.02.2024. Load loss of around 500 MW occurred at Hazira (BANGSI) due to loss of evacuation path.	Tripping of following elements: 1. 400 kV Gandhar-Hazira-1&2 2. 400/220 kV Hazira-ICT-1 & 2 3. 220 kV Bhuj-Gadhisa
5	GD-1	WR	18:10 / 07-02-2024	19:28 / 07-02-2024	01:18	115	-	0.16%	-	72368	65000	At 18:10 Hrs / 07-02-2024, 220 kV Bhuj-Gadhisa tripped on R-E fault from Gadhisa end only and auto recloser successful at Bhuj end. Generation loss of 115 MW occurred at Gadhisa (Renew Power) wind power plant due to loss of evacuation path.	Tripping of following elements: 1. 220 kV Bhuj-Gadhisa
6	GD-1	WR	02:26 / 10-02-2024	03:24 / 10-02-2024	00:58	-	-	-	-	61355	54686	At 02:26 Hrs / 10-02-2024, 220 kV Tilarani-Halkarni and 220 kV Tilarani-Amona tripped on distance protection operation from remote ends due to fault in 33 kV Kanur feeder connected to Halkarni. No load loss / generation loss occurred due to the event.	Tripping of following elements: 1. 220 kV Tilarani-Halkarni 2. 220 kV Tilarani-Amona
7	GD-1	WR	15:28 / 12-02-2024	22:37 / 19-02-2024	175:09	0	-	0.00%	-	72348	68302	At 15:28 Hrs / 12-02-2024, 400 kV Vav-Bus-1 and 400 kV Vav-Kosamba were already under forced outage from 14-11-2023 due to problem in GIS module. Due to outage of 400 kV Vav-Bus-1, 400 kV Vav-Tharad and 400 kV Vav-Nasari were disconnected from the system. No load loss / generation loss occurred due to the event.	Tripping of following elements: 1. 400 kV Vav-Tharad 2. 400 kV Vav-Nasari
8	GD-1	WR	18:38 / 12-02-2024	22:07 / 12-02-2024	03:29	5	-	0.01%	-	68384	58109	At 20:01 Hrs / 12-02-2024, 220 kV Baranda-Bhuj tripped on B-E fault. On patrolling it was found that tripping was done by some local villagers by throwing foreign object on line near tower number 231. Generation loss of around 5 MW occurred reported at Baranda (ASPL) Wind Power Plant due to loss of evacuation path.	Tripping of following elements: 1. 220 kV Bhuj-Baranda
9	GD-1	WR	19:09 / 13-02-2024	00:38 / 14-02-2024	05:29	36.26	-	0.05%	-	73007	64860	At 19:09 Hrs / 13-02-2024, 220 kV Baranda-Bhuj tripped on B-E fault. On patrolling it was found that tripping was done by some local villagers by throwing foreign object on line near tower number 238. Generation loss of around 36.26 MW occurred reported at Baranda (ASPL) Wind Power Plant due to loss of evacuation path.	Tripping of following elements: 1. 220 kV Bhuj-Baranda
10	GD-1	WR	19:15 / 14-02-2024	01:11 / 15-02-2024	05:56	78.24	-	0.11%	-	73908	64020	At 19:15 Hrs / 14-02-2024, 220 kV Baranda-Bhuj tripped on B-E fault. On patrolling it was found that tripping was done by some local villagers by throwing foreign object on line near tower number 260. Generation loss of around 78.24 MW occurred reported at Baranda (ASPL) Wind Power Plant due to loss of evacuation path.	Tripping of following elements: 1. 220 kV Bhuj-Baranda
11	GD-1	WR	18:48 / 15-02-2024	21:37 / 15-02-2024	02:49	47.5	-	0.06%	-	74058	65280	At 18:48 Hrs / 15-02-2024, 220 kV Baranda-Bhuj tripped on B-E fault. On patrolling it was found that tripping was done by some local villagers by throwing foreign object on line near tower number 260. Generation loss of around 47.5 MW occurred reported at Baranda (ASPL) Wind Power Plant due to loss of evacuation path.	Tripping of following elements: 1. 220 kV Bhuj-Baranda
12	GI-1	WR	14:21 / 19-02-2024	18:10 / 19-02-2024	03:49	49.1	-	0.07%	-	68439	62866	At 14:21 Hrs / 19-02-2024, Failure of B-phase suspension disc insulator string of 220 kV Rajgarh(MP)-Rajgarh(PG)-1 bay at Rajgarh(MP) caused in flashover from gantry to conductor resulting in busbar protection operation of 220 kV Rajgarh(MP)-Bus-1 and tripping of all connected elements. Generation loss of 49.1 MW occurred at Clean Wind Power due to the event.	Tripping of following elements: 1. 220 kV Rajgarh(MP)-Bus-1 2. 220 kV Rajgarh(MP)-Rajgarh(PG)-1 3. 220 kV Rajgarh(MP)-Clean Wind Power 4. 220/132 kV Rajgarh(MP)-ICT-2 (160 MVA)
13	GD-1	WR	12:09 / 24-02-2024	16:41 / 24-02-2024	04:32	-	400	-	0.58%	75696	68566	At 12:09 Hrs / 24-02-2024, 220 kV Siltara-Main Bus Potential Transformer cable was short circuited resulting in tripping of 220 kV Siltara-Chardehi, 220 kV Siltara-Rata, 220 kV Urita-Siltara, 220 kV Siltara-Rajpur(PG), 220 kV Siltara-Main Bus became dead due to these trippings (Bus bar protection not operated). Generation loss of 400 MW occurred at Siltara due to the event.	Tripping of following elements: 1. 220 kV Siltara-Chardehi 2. 220 kV Siltara-Rata 3. 220 kV Urita-Siltara 4. 220 kV Siltara-Rajpur(PG) 5. 220 kV Siltara-Main Bus
14	GI-1	WR	04:57 / 25-02-2024	06:20 / 25-02-2024	01:23	-	-	-	-	73006	66947	At 04:57 Hrs / 25-02-2024, Busbar protection operation in 220 kV Kansari-Bus-2 resulted in tripping of 220 kV Kansari-Bus-2 and all connected elements. On inspection it is suspected that the fault might have occurred due to bird coming near to the gantry. No load loss occurred due to the event.	Tripping of following elements: 1. 220 kV Kansari-Bus-2 2. 220 kV Kansari-Tharad 3. 220 kV Kansari-Thaver-2 4. 220 kV Kansari-Deodar-2 5. 220 kV Kansari-Jangral-2 6. 220 kV Kansari-Palampur-2 7. 400/220 kV Kansari-ICT-1&4 (315 MVA) 8. 220/66 kV Kansari-ICT-2 (100 MVA) 9. 220/66 kV Kansari-ICT-3 (160 MVA)
15	GI-1	WR	12:11 / 25-02-2024	13:17 / 25-02-2024	01:06	47	-	0.06%	-	76406	69412	At 12:11 Hrs / 25-02-2024, 220/33 kV Kotda Madh-ICT-1&2 tripped on under voltage protection operation for fault in 33 kV Feeders. On checking the relay settings it was observed that the Time setting for under voltage protection was neither coordinated with LVRT settings of WFGs. Generation loss of 47 MW occurred at Kotda Madh(Alfanar) due to the event.	Tripping of following elements: 1. 220/33 kV Kotda Madh-ICT-1&2
16	GD-1	WR	11:16 / 26-02-2024	12:28 / 26-02-2024	01:12	434	-	0.56%	-	78149	71043	At 11:16 Hrs / 26-02-2024, 400 kV Tannar-TRN Energy-1&2 tripped from TRN Energy end only on receipt of Direct Trip (DT). On inspection no fault or abnormality found in line or Tannar end. Generation loss of 434 MW occurred at TRN Energy due to loss of evacuation path.	Tripping of following elements: 1. 400 kV Tannar-TRN Energy-1&2 2. TRN Unit-1&2 (300 MW)

Details of Grid Events during the Month of February 2024 in Southern Region



Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (H:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-1	Tamil Nadu	03-02-2024 19:22	05-02-2024 10:06	14:44	0	0	0.00%	0.00%	43266	46525	Complete outage of 765kV Ariyalur and 765kV NCPS of TANTRANSOCO. 765kV Ariyalur and 765kV NCPS are being radially fed from 765kV Ariyalur-Thiruvalem-2. The triggering incident is the tripping of 765kV Ariyalur-Thiruvalem-2 at Thiruvalem end on the operation of over-voltage protection and DT was sent to the remote end. From the DR at Thiruvalem end, voltages observed are Vr – 66.62V, Vy – 58.43V, Vb – 36.11V which is 105% of rated voltage. Since 765kV Ariyalur and 765kV NCPS are being radially fed from 765kV Ariyalur-Thiruvalem-2 tripping of this line led to a complete outage of 765kV Ariyalur and 765kV NCPS.	1. 765kV Ariyalur Thiruvalem Line-2
2	GD-1	Karnataka	22-02-2024 14:18	22-02-2024 14:53	0:35	0	710	0.00%	1.14%	52763	62448	Complete outage of 220kV Kadur, Arasikere, Bettedevarakere, Shiraloppa and tripping of Bus-2 at Honnali, KB Cross and 400kV Bus-1 and Bus-2 at Talaguppa of KPTEL. In the antecedent conditions, 220kV Kadur, Arasikere, Bettedevarakere, Shiraloppa and Bus-2 at Honnali, KB Cross were radially connected to 220kV Shimoga SS. The triggering incident is the R-N fault in 220kV Shimoga-Anthrasanahalli line. After which 400/220kV ICTs at Talaguppa and 220kV Hassan Shimoga loading increased and crossed the pick-up current for 400/220kV Talavanna ICTs of 450A and tripped in around 80s and subsequently 220kV Shimoga-Hassan tripped at Shimoga end. PSB observed and tripped on ZL. With this tripping, Complete outage of 220kV/66kV Davanagere SS, 220kV/66kV Hosadurga SS, 220kV/66kV Benikere SS and Tripping of 220kV Bus-1 of 220kV/66kV Honnali SS of KPTEL. During the antecedent conditions 220kV/66kV Davanagere SS, 220kV/66kV Hosadurga SS, 220kV/66kV Benikere SS and 220kV Bus-1 of 220kV/66kV Honnali SS were being radially fed through 400kV/220kV Guttur SS through 220kV Guttur-Davanagere-1,2 and 3 lines of which line-2 was under forced outage. The triggering incident is the tripping of 220kV Guttur.	1. 220kV Shimoga-Anthrasanahalli 2. 220kV Shimoga-Hassan 3. 400/220kV Talaguppa ICT-1 4. 400/220kV Talavanna ICT-3
3	GD-1	Karnataka	23-02-2024 14:10	23-02-2024 14:54	0:44	0	181	0.00%	0.29%	54025	63381	Complete outage of 220kV/66kV Davanagere SS, 220kV/66kV Hosadurga SS, 220kV/66kV Benikere SS and Tripping of 220kV Bus-1 of 220kV/66kV Honnali SS of KPTEL. During the antecedent conditions 220kV/66kV Davanagere SS, 220kV/66kV Hosadurga SS, 220kV/66kV Benikere SS and 220kV Bus-1 of 220kV/66kV Honnali SS were being radially fed through 400kV/220kV Guttur SS through 220kV Guttur-Davanagere-1,2 and 3 lines of which line-2 was under forced outage. The triggering incident is the tripping of 220kV Guttur.	1. 220kV Guttur-Davanagere-1&3
4	GD-1	Karnataka	24-02-2024 06:52	24-02-2024 11:52	5:00	118	0	0.30%	0.00%	39436	54735	Complete Outage of 220kV Kadra PH of KPTEL and 220kV/110kV Karwar SS of KPTEL. During antecedent conditions, 220kV Kaiga Kadra and 220kV Kaiga Kodasaly were under outage. 220kV Kadra PH and 220kV/110kV Karwar SS were being radially fed through 220kV Kadra Kodasali line. As per the reports submitted, the triggering incident was an R-N fault in 220kV Kadra Kodasali line. Tripping of this line led to a complete outage of 20kV Kadra PH and 220kV/110kV Karwar SS.	1. 220kV Kadra Kodasali
5	GI-1	Karnataka	07-02-2024 13:14	07-02-2024 14:15	1:01	0	49	0.00%	0.08%	52454	58574	Tripping of 220kV Bus-1 of 220kV/66kV Chintamani SS of KPTEL: As per the reports submitted, the triggering incident was 220kV Bus-1 BBP maloperation causing all the lines connected to 220kV Bus-1 to trip.	1. 220kV Kolar Chintamani Line-1 2. 220kV Chintamani Srinivasapura Line-2 3. 220kV/66kV Chintamani Auto Transformer-1
6	GI-2	Andhra Pradesh	14-02-2024 06:58	14-02-2024 10:16	3:18	0	0	0.00%	0.00%	42948	56288	Tripping of 400kV Bus-1 of 400kV/220kV Kalpakka SS of APTRANSCO. As per the reports submitted, the triggering incident was isolator failure in 400kV Kalpakka Simhadri Line-4 at Kalpakka SS causing a R-N fault in 400kV Bus-1. Immediately, BBP operated and all the elements connected to the Bus-1 tripped.	1. 400kV Kalpakka-Simhadri-4 2. 400kV Hinduja-Kalpakka-1 3. 400/220kV ICT-1 at Kalpakka
7	GI-1	Telangana	27-02-2024 17:32	28-02-2024 21:06	3:34	0	0	0.00%	0.00%	43952	55879	Tripping of 220kV Bus-2 of 220kV KTPS station of TSGENCO: As per the reports submitted, the triggering incident was LBB maloperation in 220kV KTPS Nunna line which is connected to 220kV Bus-2 at the KTPS end. Immediately all the elements connected to Bus-2 tripped.	1. 220kV KTPS Nunna 2. 220kV KTPS BG Kothuru 3. 220kV KTPS Manuguru Line-2

Details of Grid Events during the Month of February 2024 in Eastern Region



Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-1	Dhanbad	16.02.2024 09:15	16.02.2024 11:52	02:37	0	90	0.00%	0.43%	30046	20809	At 09:15 Hrs on 16.02.2024, Bus Bar protection of both bus operated (due to Shorting of B-Phase MB#2 and Y-Phase MB#1 due to some foreign element) at 220/132 kV Dhanbad S/S which led to total power failure at 220/132 kV Dhanbad (DVC) S/S. Around 90 MW load loss occurred. 220kV Dhanbad Bus normalized through 220 kV Dhanbad-Giridih ckt#1 at 11:52 hrs.	220 kV Main Bus-1 & 2 at Dhanbad 220 kV Maithon-Dhanbad D/c 220 kV Giridih-Dhanbad D/c 220 kV CTPS B-Dhanbad D/c 2*220/132 kV ATR at Dhanbad

Details of Grid Events during the Month of February 2024 in North Eastern Region



Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI Ior GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD I	Churachandpur and Thanlon areas of Manipur power system	01-02-2024 22:47	01-02-2024 23:25	00:38:00	0	8	0.00%	0.40%	1518	1983	Churachandpur and Thanlon areas of Manipur Power system was connected with the rest of the grid by 132 kV Ningthoukhong-Churachandpur II line. 132 kV Ningthoukhong-Churachandpur I line is under outage since 13/01/2024. Also, 132 kV Churachandpur-Kachiching & 132 kV Churachandpur-Elangkangpokpi lines are out since 08/06/2023. At 22:47 hrs of 01/02/2024, 132 kV Ningthoukhong-Churachandpur II line tripped and Churachandpur and Thanlon areas of Manipur Power system got separated from rest of the grid due to no source available in this area. Power was extended to Churachandpur and Thanlon areas of Manipur Power system by charging 132 kV Ningthoukhong-Churachandpur II line at 23:25 Hrs of 01/02/2024.	132 kV Ningthoukhong-Churachandpur II
2	GD I	Churachandpur and Thanlon areas of Manipur power system	02-02-2024 01:37	02-02-2024 06:45	05:08:00	0	5	0.00%	0.33%	1181	1506	Churachandpur and Thanlon areas of Manipur Power system was connected with the rest of the grid by 132 kV Ningthoukhong-Churachandpur II line. 132 kV Ningthoukhong-Churachandpur I line is under outage since 13/01/2024. Also, 132 kV Churachandpur-Kachiching & 132 kV Churachandpur-Elangkangpokpi lines are out since 08/06/2023. At 01:37 hrs of 02/02/2024, 132 kV Ningthoukhong-Churachandpur II line tripped and Churachandpur and Thanlon areas of Manipur Power system got separated from rest of the grid due to no source available in this area. Power was extended to Churachandpur and Thanlon areas of Manipur Power system by charging 132 kV Ningthoukhong-Churachandpur II line at Hrs of 02/02/2024.	132 kV Ningthoukhong-Churachandpur II
3	GD I	Ningthoukhong, Churachandpur and Thanlon areas of Manipur power system	02-02-2024 10:05	02-02-2024 10:32	00:27:00	0	18	0.00%	0.84%	1649	2135	Ningthoukhong, Churachandpur and Thanlon areas of Manipur Power system was connected with the rest of the grid by 132 kV Loktak-Ningthoukhong, 132 kV Imphal(PG)-Ningthoukhong and 132 kV Ningthoukhong-Churachandpur II lines. 132 kV Ningthoukhong-Churachandpur I line is under outage since 13/01/2024. Also, 132 kV Churachandpur-Kachiching & 132 kV Churachandpur-Elangkangpokpi lines are out since 08/06/2023. At 10:05 hrs of 02/02/2024, 132 kV Loktak-Ningthoukhong & 132 kV Imphal(PG)-Ningthoukhong lines tripped and Ningthoukhong, Churachandpur and Thanlon areas of Manipur Power system got separated from rest of the grid due to no source available in this area. Power was extended to Ningthoukhong, Churachandpur and Thanlon areas of Manipur Power system by charging 132 kV Imphal(PG)-Ningthoukhong line at 10:32 Hrs of 02/02/2024.	132 kV Loktak-Ningthoukhong & 132 kV Imphal(PG)-Ningthoukhong lines
4	GD I	Ningthoukhong, Churachandpur and Thanlon areas of Manipur power system	02-02-2024 18:44	02-02-2024 19:16	00:32:00	0	19	0.00%	0.76%	2821	2492	Ningthoukhong, Churachandpur and Thanlon areas of Manipur Power system was connected with the rest of the grid by 132 kV Loktak-Ningthoukhong, 132 kV Imphal(PG)-Ningthoukhong and 132 kV Ningthoukhong-Churachandpur II lines. 132 kV Ningthoukhong-Churachandpur I line is under outage since 13/01/2024. Also, 132 kV Churachandpur-Kachiching & 132 kV Churachandpur-Elangkangpokpi lines are out since 08/06/2023. At 18:44 hrs of 02/02/2024, 132 kV Loktak-Ningthoukhong & 132 kV Imphal(PG)-Ningthoukhong lines tripped and Ningthoukhong, Churachandpur and Thanlon areas of Manipur Power system got separated from rest of the grid due to no source available in this area. Power was extended to Ningthoukhong, Churachandpur and Thanlon areas of Manipur Power system by charging 132 kV Imphal(PG)-Ningthoukhong line at 19:16 Hrs of 02/02/2024.	132 kV Loktak-Ningthoukhong & 132 kV Imphal(PG)-Ningthoukhong lines
5	GD I	Churachandpur and Thanlon areas of Manipur power system	08-02-2024 12:57	08-02-2024 15:09	02:12:00	0	7	0.00%	0.34%	1470	2033	Churachandpur and Thanlon areas of Manipur Power system was connected with the rest of the grid by 132 kV Ningthoukhong-Churachandpur II line. 132 kV Ningthoukhong-Churachandpur I line is under outage since 13/01/2024. Also, 132 kV Churachandpur-Kachiching & 132 kV Churachandpur-Elangkangpokpi lines are out since 08/06/2023. At 12:57 hrs of 08/02/2024, 132 kV Ningthoukhong-Churachandpur II line tripped and Churachandpur and Thanlon areas of Manipur Power system got separated from rest of the grid due to no source available in this area. Power was extended to Churachandpur and Thanlon areas of Manipur Power system by charging 132 kV Ningthoukhong-Churachandpur II line at 15:09 Hrs of 08/02/2024.	132 kV Ningthoukhong-Churachandpur II
6	GD 1	Churachandpur and Thanlon area of Manipur power system	21-02-2024 06:57	21-02-2024 07:31	00:34:00	0	2	0.00%	0.09%	1680	2202	Due to the outage of 132 kV Churachandpur-Kachiching, 132 kV Churachandpur-Elangkangpokpi and 132 kV Ningthoukhong-Churachandpur I line, Churachandpur and Thanlon area of Manipur radially connected with rest of the grid with through 132 kV Ningthoukhong-Churachandpur II line. At 06:57 Hrs of 21.02.2024, 132 kV Ningthoukhong-Churachandpur II line tripped resulted into the blackout of the Churachandpur and Thanlon area of Manipur power system. Power was extended to 132 kV Churachandpur S/S by charging 132 kV Ningthoukhong-Churachandpur II Line at 07:31 Hrs of 21-02-2024.	132 kV Ningthoukhong-Churachandpur II
7	GD 1	Kolasib, Turiel and Bairabi areas of Mizoram Power System	22-02-2024 13:47	22-02-2024 16:23	02:36:00	0	5	0.00%	0.27%	1254	1861	Kolasib, Turiel and Bairabi areas of Mizoram Power System were connected with rest of NER Grid through 132 kV Badarpur-Kolasib line and 132 kV Aizawl-Kolasib line. At 13:47 Hrs of 22-02-2024, 132 kV Badarpur-Kolasib and 132 kV Aizawl-Kolasib tripped. Due to tripping of this element, Kolasib, Turiel and Bairabi areas of Mizoram Power System were isolated from NER Grid and collapsed due to no source available in these areas. Power was extended to Kolasib, Turiel and Bairabi areas of Mizoram Power System by charging 132 kV Aizawl-Kolasib line at 16:23 Hrs, subsequently 132 kV Badarpur-Kolasib line at 16:24 Hrs of 22.02.2024.	132 kV Badarpur-Kolasib & 132 kV Aizawl-Kolasib
8	GD 1	Karong area of Manipur Power System	28-02-2024 20:40	28-02-2024 21:56	01:16:00	0	15.8	0.00%	0.64%	2499	2455	132 kV Karong Substation of Manipur Power System was connected with rest of NER Grid via 132kV Karong-Kohima and 132 kV Karong-Imphal (Yurembam) lines. At 20:40 Hrs of 28.02.2024, 132kV Karong-Kohima and 132 kV Karong-Imphal (Yurembam) lines tripped. Due to tripping of these elements, Karong area of Manipur Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Karong area of Manipur Power System by charging 132kV Karong-Kohima at 21:56 Hrs of 28.02.2024.	132kV Karong-Kohima & 132 kV Karong-Imphal (Yurembam)
9	GI 2	AGBPP	23-02-2024 06:31	-	-	223	0	13.43%	0.00%	1660	2065	AGBPP U-7 (i.e. STG-1) under tripped condition since 12-02-2024 due to cooling water system failure (Under Planned shutdown from 00:07 Hrs of 13.02.2024). As reported from AGBPP, at 06:31 Hrs station transformer tripped which lead to tripping all gas compressors and subsequently tripped all available units (U1, U2, U3, U4, U5, U6, U7 & U9). Restoration time of various units are as follows:- Unit 1 : 23-02-2024 16:22 Hrs Unit 2 : 23-02-2024 08:56 Hrs Unit 3 : 23-02-2024 09:54 Hrs Unit 4 : 23-02-2024 09:37 Hrs	All available Units

21. NEW ELEMENTS COMMISSIONED* IN FEBRUARY 2024							
COMMISSIONING OF NEW GENERATING UNITS							
REGION	S.NO.	ENTITY	UNIT NAME / LOCATION	ADD. CAPACITY (MW)	UNIT NO.	INS. CAPACITY (MW)	DATE®
NR	1	Azure Power Maple Private Limited (APMPL)	Azure Power Maple Private Limited(Solar)/Rajasthan	24	-	300	01-02-2024
	2	ADANI SOLAR ENRGY RJ TWO PRIVATE LIMITED	Adani Solar Energy RJ Two Private Limited(Solar)/Rajasthan	59.95	-	165	04-02-2024
	3	ADEPT RENEWABLE TECHNOLOGY PVT LTD	Adept Renewable Technology Pvt Ltd(Solar)/Rajasthan	110	-	110	06-02-2024
	4	RENEW SURYA AAYAN PRIVATE LIMITED	Renew Surya Aayan Private Limited(Solar)/Rajasthan	193	-	290	08-02-2024
	5	RENEW SURYA AAYAN PRIVATE LIMITED	Renew Surya Aayan Private Limited(Solar)/Rajasthan	48.25	-	290	08-02-2024
	6	TRANSITION ENERGY SERVICES PRIVATE LIMITED	Transition Energy Services Private Limited(Solar)/Rajasthan	60	-	84.4	08-02-2024
	7	TRANSITION ENERGY SERVICES PRIVATE LIMITED	Transition Energy Services Private Limited(Solar)/Rajasthan	24.4	-	84.4	08-02-2024
	8	RENEW SURYA ROSHNI PRIVATE LIMITED	Renew Surya Roshni Private Limited(Solar+BESS)/Rajasthan	95	-	380	19-02-2024
	9	RENEW SURYA ROSHNI PRIVATE LIMITED	Renew Surya Roshni Private Limited(Solar+BESS)/Rajasthan	95	-	380	20-02-2024
	10	RENEW SURYA AAYAN PRIVATE LIMITED	Renew Surya Aayan Private Limited(Solar)/Rajasthan	48.75	-	290	22-02-2024
	11	ADANI SOLAR ENERGY RJ TWO PRIVATE LIMITED	Adani Solar Energy RJ Two Private Limited(Solar)/Rajasthan	52.5	-	165	24-02-2024
	12	RENEW SURYA ROSHNI PRIVATE LIMITED	Renew Surya Roshni Private Limited(Solar+BESS)/Rajasthan	95	-	380	27-02-2024
	13	ADANI SOLAR ENERGY RJ TWO PRIVATE LIMITED	Adani Solar Energy RJ Two Private Limited(Solar)/Rajasthan	52.55	-	165	29-02-2024
WR	14	ADANI WIND ENERGY KUTCHHH FOUR LTD	Adani Wind Energy Kutchh Four Ltd(Wind),Gujarat	14.7	I	203.7	16-02-2024
	15	APRAVAA ENERGY PRIVATE LIMITED (AEPL)	Apravaa Energy Private Limited (Solar)/Gujarat	25.2	I	163.8	29-02-2024
	16	NPCIL	NPCIL(Nuclear)/Gujarat	700	IV	700	20-02-2024
SR	17	RSRPL	RSRPL(Wind)/Karnataka	34.65	LOT-VI	256.41	05-02-2024
	18	JSW RENEW	JSW Renew(Wind)/Tamilnadu	13.5	-	245.7	08-02-2024
	19	JSW	JSW(Wind)/Tamilnadu	5.4	LOT-I	5.4	23-02-2024
	20	JSW	JSW(Wind)/Tamilnadu	32.4	LOT-II	37.8	10-02-2024
	21	JSW	JSW(Wind)/Tamilnadu	8.1	LOT-III	67.5	21-02-2024
	22	RSOPL	RSOPL(Wind)/Karnataka	183.645	LOT-I	183.645	19-02-2024
	23	RSOPL	RSOPL(Wind)/Karnataka	41.58	LOT-II	225.225	22-02-2024
	24	NTPC	NTPC(Thermal)/Telangana	800	II	1600	28-02-2024
®RE (Solar & Wind generation added capacity FTC is in phases. Date mentioned is the date by which complete (Added) capacity							
COMMISSIONING OF NEW ICTs							
REGION	S.NO.	ENTITY	SUB-STATION	VOLTAGE (kV)	ICT NO.	CAPACITY (MVA)	DATE
NR	1	UPPTCL	Orai	400/220/33	II	315	08-02-2024
	2	POWERGRID	Fatehgarh, II	765/400	I	1500	22-02-2024
	3	UPPTCL	Sahupuri	400/220/33	I	500	24-02-2024
WR	4	KBTL Khavda Bhuj Transmission Limited	Khavda PS1	765/400	I	1500	12-02-2024
SR	5	TS TRANSCO	Dichpally	400/220	IV	500	24-02-2024
	6	TANTRANSCO	NCPS	765/400	II	1500	02-02-2024
	7	TANTRANSCO	NCPS	765/400	III	1500	02-02-2024
NER	8	AEGLCL	Sishupam	132/33	I	50	09-02-2024
	9	AEGLCL	Behiating	132/33	II	25	29-02-2024
	10	AEGLCL	GMC	132/33	I	50	27-02-2024
COMMISSIONING OF NEW TRANSMISSION LINES							
REGION	S.NO.	ENTITY	LINE NAME	CKT NO.	VOLTAGE (kV)	DATE	
NR	1	GTL	765kV Hapur-Rampur_PRSTL	I	765	24-02-2024	
	2	WUPPTCL	765kV Mainpuri-Hapur	I	765	27-02-2024	
WR	3	Kallam TL (Indigrd)	400kV Parli-Kallam	I	400	11-02-2024	
	4	Kallam TL (Indigrd)	400kV Kallam-Pune GIS	I	400	11-02-2024	
	5	Kallam TL (Indigrd)	400kV Parli-Kallam	II	400	12-02-2024	
	6	Kallam TL (Indigrd)	400kV Kallam-Pune GIS	II	400	12-02-2024	
	7	KBTL Khavda Bhuj Transmission Limited	765 kV Khavda PS-4-Bhuj	II	765	17-02-2024	
	8	Rajgarh Transmission Ltd (RTL)	400kV Pachora PS-Bhopal BDTCL	I	400	23-02-2024	
	9	Rajgarh Transmission Ltd (RTL)	400kV Pachora PS-Bhopal BDTCL	II	400	24-02-2024	
SR	10	POWERGRID	400kV Ariyalur-NNTTP	I	400	08-02-2024	
	11	POWERGRID	400kV-Ariyalur-NNTTP	II	400	07-02-2024	
LILO OF TRANSMISSION LINES							
REGION	S.NO.	ENTITY	LINE NAME (LILOed LINE)	LILO AT	VOLTAGE (kV)	DATE	
SR	1	TANTRANSCO	Ariyalur-kalvendapattu-II (Kalvendapattu - Pugulur D/C)	Ariyalur	400	12-02-2024	
	2	TANTRANSCO	Ariyalur-kalvendapattu-I (Kalvendapattu - Pugulur D/C)	Ariyalur	400	12-02-2024	
	3	TANTRANSCO	Ariyalur-pugulur-II (Kalvendapattu - Pugulur D/C)	Ariyalur	400	10-02-2024	
	4	TANTRANSCO	Ariyalur-pugulur-I (Kalvendapattu - Pugulur D/C)	Ariyalur	400	10-02-2024	
ER	5	POWERGRID	Patna-Balia-III (Bypassing Balia-Naubatpur-I & Patna-Naubatpur-I)	-	400	06-02-2024	
COMMISSIONING OF BUS/LINE REACTORS							
REGION	S.NO.	ENTITY	SUB-STATION / LINE (@SUB-STATION)	VOLTAGE (kV)	CAPACITY (MVAR)	DATE	
NR	1	GTL	Hapur-Rampur @Hapur	765	330	24-02-2024	
	2	WUPPTCL	Mainpuri-Hapur@Mainpuri	765	189	24-02-2024	
WR	3	Kallam TL (Indigrd)	Kallam PS-Pune GIS-I@Kallam	400	50	11-02-2024	
	4	Kallam TL (Indigrd)	Kallam PS-Pune GIS-II@Kallam	400	50	12-02-2024	
	5	Rajgarh Transmission Ltd (RTL)	Pachora PS-Bhopal BDTCL-I@Pachora	400	80	23-02-2024	
	6	Rajgarh Transmission Ltd (RTL)	Pachora PS-Bhopal BDTCL-II@Pachora	400	80	24-02-2024	
	7	Khavda Bhuj Transmission Limited(KBTL)	Bus Reactor-I@ Khavda PSI	765	330	16-02-2024	
	8	Rajgarh Transmission Ltd (RTL)	Bus Reactor-I@Pachora PS	400	125	28-02-2024	
SR	9	TANTRANSCO	Thiruvallam-Ariyalur-I@Ariyalur	765	240	12-02-2024	
NER	10	POWERGRID	Balipara -BNC-II@Balipara	400	63	07-02-2024	
COMMISSIONING OF HVDC/FACTS DEVICE/SYSTEM							
REGION	S.NO.	ELEMENT NAME	SUB-STATION / CONSTITUENT	RATINGS	VOLTAGE (kV)	DATE	
WR	1	SVG	Khavda PSS1(AREH4L)	50	33	17-02-2024	
	2	SVG	Khavda PSS1(AREH4L)	50	33	17-02-2024	
	3	SVG	Khavda PSS1(AREH4L)	50	33	17-02-2024	
	4	SVG	Khavda PSS1(AREH4L)	50	33	17-02-2024	
*Includes first time charging (FTC) as well							

*Includes first time charging (FTC) as well

Voltage Profile

विद्युत विभव रूपरेखा माह - फरवरी 2024

VOLTAGE PROFILE - FEBRUARY 2024

Date of reporting: 05-Mar-24

क्र.स. Sl. No.	क्षेत्र REGION	उपकेंद्र SUBSTATION	VOLTAGE < V(lower)* (V=380,728 kV)	V(lower) < VOLTAGE < V(upper)*	VOLTAGE > V(upper)* (V=420,800 kV)	Voltage Deviation Index (%age of time voltage is outside range)	Number of hours voltage was outside IECG band during month	उच्चतम (कि. वो.) Maximum(kV)	निम्नतम(कि. वो.) Minimum(kV)	औसत (कि. वो.) Average(kV)
1	पूर्वी क्षेत्र ER	अंगुल ANGUL	0%	100%	0%	0%	0	799	749	777
2		दार्लिपली DURLIPALI	0%	100%	0%	0%	0	795	762	777
3		गया GAYA	0%	100%	0%	0%	0	789	750	769
4		जैरत JEERAT	0%	100%	0%	0%	0	783	736	760
5		झारसुगुडा JHARSUGUDA	0%	100%	0%	0%	2	804	765	785
6		मिदनापुर MEDINIPUR	0%	100%	0%	0%	0	783	748	766
7		रांची RANCHI	0%	100%	0%	0%	0	791	759	778
8		सासाराम SASARAM	0%	100%	0%	0%	0	779	727	759
1	उत्तरी क्षेत्र NR	आगरा AGRA	0%	100%	0%	0%	0	803	745	779
2		आगरा (फतेहाबाद) AGRA (FATEHABAD)	0%	100%	0%	0%	0	795	732	773
3		अजमेर AJMER	0%	100%	0%	0%	1	804	748	778
4		अलीगढ़ ALIGARH	0%	100%	0%	0%	0	797	740	774
5		अनपरा सी ANPARA-C	0%	100%	0%	0%	0	782	755	768
6		अनपरा डी ANPARA-D	0%	100%	0%	0%	0	780	754	766
7		अंता ANTA	0%	100%	0%	0%	0	797	751	777
8		बालिया BALLIA	0%	100%	0%	0%	0	789	742	767
9		बारा BARA	0%	100%	0%	0%	0	784	749	769
10		भाड़ला BHADLA	0%	100%	0%	0%	0	793	739	772
11		भाड़ला-2 BHADLA-2	0%	100%	0%	0%	0	800	748	775
12		भिवानी BHIWANI	0%	100%	0%	0%	1	802	746	780
13		बिकानेर BIKANER	0%	100%	0%	0%	0	798	744	774
14		बरौली BAREILLY	0%	99%	1%	1%	9	809	733	777
15		चित्तौड़गढ़ CHITTORGARH	0%	100%	0%	0%	1	803	750	779
16		फतेहगढ़-2 FATEHGARH-2	0%	100%	0%	0%	0	795	739	775
17		फतेहपुर FATEHPUR	0%	100%	0%	0%	0	801	740	770
18		ग्रेटर नोएडा GREATER NOIDA	0%	100%	0%	0%	2	802	744	781
19		हापड़ HAPUR	0%	98%	2%	2%	11	806	739	780
20		जावहरपुर JAWAHARPUR	0%	100%	0%	0%	0	797	737	776
21		झाटिकुरा JHATIKARA	0%	100%	0%	0%	0	797	743	776
22		कानपुर जीआरएस KANPUR GIS	0%	100%	0%	0%	0	795	742	773
23		खेतवा KHETWA	0%	100%	0%	0%	0	803	741	777
24		कोटेश्वर KOTESHWAR	0%	100%	0%	0%	0	802	736	774
25		लालितपुर LALITPUR	0%	100%	0%	0%	0	773	732	760
26		लखनऊ LUCKNOW	0%	100%	0%	0%	0	798	744	771
27		मैनपुरी MAINPURI	0%	100%	0%	0%	0	798	731	774
28		मेरठ MEERUT	0%	100%	0%	0%	2	806	739	779
29		मेरठ(UP) MEERUT (UP)	0%	100%	0%	0%	2	803	740	778
30		मोगा MOGA	0%	100%	0%	0%	0	805	733	769
31		ओबरा सी OBRA C	0%	100%	0%	0%	3	810	747	761
32		उरई ORAI	0%	98%	2%	2%	13	807	753	786
33		फागी PHAGI	0%	100%	0%	0%	1	801	744	778
34		रामपुर RAMPUR	0%	99%	0%	1%	4	808	717	767
35		उन्नाव UNNAO	0%	100%	0%	0%	0	793	735	762
36		वाराणसी VARANASI	0%	100%	0%	0%	0	793	752	775
1	पश्चिमी क्षेत्र WR	अकोला AKOLA	0%	100%	0%	0%	0	792	750	772
2		औरंगाबाद AURANGABAD	0%	100%	0%	0%	0	799	750	777
3		भोपाल (बीडीटीसीएल) BHOPAL (BDTCL)	0%	100%	0%	0%	0	795	745	772
4		भुज BHUJ	0%	100%	0%	0%	0	794	748	775
5		भुज-2 BHUJ-II	0%	100%	0%	0%	0	787	745	769
6		बिलासपुर BILASPUR	0%	100%	0%	0%	0	785	752	767
7		बीना BINA	0%	100%	0%	0%	0	797	754	781
8		बनसकंठा BANASKANTHA	0%	100%	0%	0%	0	800	754	782
9		चांपा CHAMPA	0%	100%	0%	0%	0	802	765	784
10		धुल (बीडीटीसीएल) DHULE (BDTCL)	0%	100%	0%	0%	0	796	746	774
11		धर्मजगढ़ DHARAMJAGARH	0%	100%	0%	0%	0	788	754	770
12		रायपुर पूलिंग RAIPUR POOLING	0%	100%	0%	0%	0	794	758	776
13		एकतुनी EKTUNI	0%	100%	0%	0%	0	792	744	770
14		गदरवाड़ा GADARWARA	0%	100%	0%	0%	0	802	764	784
15		ग्वालियर GWALIOR	0%	99%	1%	1%	5	807	747	783
16		इंदौर INDORE	0%	100%	0%	0%	0	794	747	773
17		जबलपुर JABALPUR	0%	100%	0%	0%	0	801	760	787
18		खड़वा KHANDWA	0%	100%	0%	0%	0	796	750	774
19		कोरडी KORADI	0%	100%	0%	0%	0	782	752	768
20		लाकाडिया LAKADIVA	0%	100%	0%	0%	0	795	754	777
21		रायगढ़ पूलिंग RAIGARH POOLING	0%	100%	0%	0%	0	795	766	782
22		पडुछे PADGHE	0%	100%	0%	0%	0	805	737	777
23		परली PARLI	0%	100%	0%	0%	1	803	755	782
24		पुणे PUNE	0%	100%	0%	0%	1	807	734	778
25		राजनन्दगांव RAJNANDGAON	0%	100%	0%	0%	2	805	760	782
26		सासन SASAN	0%	100%	0%	0%	0	789	761	778
27		सतना SATNA	0%	100%	0%	0%	0	798	760	784
28		सिवनी SEONI	0%	100%	0%	0%	0	795	750	772
29		सोपट SIPAT	0%	100%	0%	0%	0	785	755	768
30		सोलापुर SOLAPUR	0%	99%	1%	1%	4	805	758	784
31		तिरोड़ा TIRODA	0%	100%	0%	0%	0	776	753	765
32		तामनार TAMNAR	0%	100%	0%	0%	0	792	764	780
33		वडोदरा VADODARA	0%	100%	0%	0%	0	803	735	774
34		विंध्याचल पूलिंग VINDHYACHAL PS	0%	100%	0%	0%	0	794	765	782
35		वधा WARDHA	0%	100%	0%	0%	1	804	753	779
36		वरारार WARORA	0%	100%	0%	0%	0	802	749	780
1	दक्षिणी क्षेत्र SR	अरियलूर ARIYALUR	0%	100%	0%	0%	0	799	729	769
2		कडपा CUDDAPAH	0%	93%	7%	7%	46	812	746	784
3		चिल्कुरीपेट CHILAKALURIPETA	0%	94%	6%	6%	39	813	742	783
4		कन्नूल KURNOOL	0%	100%	0%	0%	0	800	742	772
5		महेश्वर MAHESWARAM	0%	93%	7%	7%	50	813	745	782
6		निज़ामाबाद NIZAMABAD	0%	87%	13%	13%	91	816	745	785
7		नेल्लूर पूलिंग NELLORE PS	0%	100%	0%	0%	0	798	747	773
8		नॉर्थ चेन्नै पूलिंग NORTH CHENNAI PS	0%	85%	15%	15%	102	817	741	788
9		रायचूर RAICHUR	0%	100%	0%	0%	1	805	748	776
10		श्रीकाकुलम SRIKAKULAM	0%	96%	4%	4%	29	811	744	783
11		थिरुवल्लम THIRUVALEM	0%	100%	0%	0%	1	810	739	774
12		वेमगिरि VEMAGIRI	0%	94%	6%	6%	44	813	746	784
13		वारंगल WARANGAL	0%	95%	5%	5%	34	811	744	783
1	पूर्वोत्तर क्षेत्र NER	बिस्वनाथ चरिआल बिसवानाथ चारिआल (400 kV)	0%	100%	0%	0%	0	415	393	403
2		बोंगाईगांव BONGAIGAON (400 kV)	0%	100%	0%	0%	0	418	398	407
3		बोंगाईगांव टीपीएस BONGAIGAON TPS (400 kV)	0%	100%	0%	0%	0	420	399	409
4		इम्फाल IMPHAL (400 kV)	0%	100%	0%	0%	0	417	392	405
5		बर्निहाट BYRNHAT (400 kV)	0%	100%	0%	0%	1	421	402	411
6		कामेंग KAMENG (400 kV)	0%	100%	0%	0%	0	414	392	403
7		अज़ारा AZARA (400 kV)	0%	100%	0%	0%	0	411	393	403
8		मिसा MISA (400 kV)	0%	100%	0%	0%	0	413	392	402
9		न्यू मारियानो NEW MARIANI (400 kV)	0%	100%	0%	0%	0	418	394	406
10		न्यू कोहिमा NEW KOHIMA (400 kV)	0%	100%	0%	0%	0	422	395	407
11		पालाताना PALATANA (400 kV)	0%	100%	0%	0%	0	413	401	407
12		प्रबोक्चनबारी PK BARI (400 kV)	0%	100%	0%	0%	0	413	391	402
13		रंगानादी RANGANADI (400 kV)	0%	99%	1%	1%	4	422	392	410
14		सिलचर SILCHAR (400 kV)	0%	100%	0%	0%	0	418	397	408
15		सूर्ययामोनिनगर SURJYAMANINAGAR (400 kV)	0%	100%	0%	0%	0	411	393	402
16		थोबाल THOUBAL (400 kV)	0%	100%	0%	0%	0	414	385	402

All listed stations are 765 kV stations unless otherwise mentioned

*Percentage is calculated w.r.t. Time of one month.

23.ALL TIME HIGHEST

29-02-2024

	Maximum Demand Met during the day (MW)	Demand Met during Evening Peak hrs(MW)	Energy Met (MU)	Hydro Gen. (MU)	Wind Gen. (MU)	Solar Gen. (MU)
NR	81220 04-09-2023	76274 04-09-2023	1796 04-09-2023	443 01-08-2023	86 07-08-2023	158 28-02-2024
WR	74799 29-01-2024	65518 13-10-2023	1618 02-09-2023	167 18-12-2014	273 07-08-2023	83.44 23-02-2024
SR	65828 23-02-2024	52366 18-04-2023	1335 23-02-2024	208 31-08-2018	298 21-07-2023	142.7 21-03-2023
ER	29641 28-07-2023	28579 18-04-2023	639 08-06-2023	157 14-09-2022	-	7 23-03-2023
NER	3712 04-09-2023	3510 12-08-2022	72 15-09-2023	41 29-08-2023	-	2 22-06-2022
All India	239978 01-09-2023	215592 28-08-2023	5224 02-09-2023	877 30-08-2022	611 02-08-2023	381 28-02-2024
Regions	States	Max. Demand Met during the day (MW)		Energy Consumption (MU)		
			As on date		As on date	
NR	Punjab	15237	23-06-2023	343.5	24-06-2023	
	Haryana	12692	18-08-2023	273.1	18-08-2023	
	Rajasthan	17949	20-01-2024	371.6	04-09-2023	
	Delhi	7770	29-06-2022	153.5	28-06-2022	
	UP	28553	25-07-2023	580.0	03-09-2023	
	Uttarakhand	2594	14-06-2022	55.8	17-06-2023	
	HP	2235	20-01-2024	40.7	22-08-2023	
	J&K(UT) and Ladakh(UT)	3636	29-06-2023	66.8	26-01-2024	
	Chandigarh	426	08-07-2021	8.4	08-07-2021	
Railways NR ISTS	-	-	-	-		
WR	Chhattisgarh	5832	02-09-2023	133.5	28-08-2023	
	Gujarat	24544	01-09-2023	511.6	02-09-2023	
	MP	17819	29-12-2023	335.9	10-11-2023	
	Maharashtra	28969	07-02-2024	636.1	21-06-2023	
	Goa	776	07-06-2023	17.1	08-06-2023	
	DD & DNH	1327	17-08-2023	30.9	10-08-2023	
	AMNSIL	1083	10-01-2024	21.0	31-05-2022	
Balco	-	-	-	-		
SR	Andhra Pradesh*	13084	28-02-2024	263.8	16-06-2023	
	Telangana*	15497	30-03-2023	303.4	03-03-2023	
	Karnataka	16950	25-08-2023	320.9	29-02-2024	
	Kerala	5024	18-04-2023	103.3	19-04-2023	
	Tamil Nadu	19387	20-04-2023	415.4	20-04-2023	
	Pondy	512	17-05-2023	11.6	18-05-2023	
ER	Bihar	7578	27-07-2023	161.3	28-07-2023	
	DVC	3751	18-04-2023	81.2	22-04-2022	
	Jharkhand	1923	16-06-2023	43.3	17-06-2023	
	Odisha	7192	19-04-2023	145.5	25-09-2022	
	West Bengal	11868	18-04-2023	245.7	18-04-2023	
	Sikkim	137	03-02-2022	2.5	28-01-2020	
	Railways ER ISTS	-	-	-	-	
NER	Arunachal Pradesh	186	10-02-2024	3.3	08-02-2024	
	Assam	2498	16-09-2023	50.0	15-09-2023	
	Manipur	258	31-01-2022	3.7	10-02-2022	
	Meghalaya	415	09-02-2022	7.8	31-01-2022	
	Mizoram	162	27-01-2024	2.5	27-01-2024	
	Nagaland	179	28-09-2023	3.29	05-09-2023	
	Tripura	370	07-06-2023	7.0	06-06-2023	
*SR	Andhra Pradesh (Undivided)	13162	23-03-2014	284.8	22-03-2014	

24.System Reliability Indices Report for the month of February 2024

Percentage (%) of times ATC was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	0	0.00	0.00
2	ER-NR	1	0.25	0.04
3	Import of NR	0	0.00	0.00
4	NEW-SR	0	0.00	0.00
5	NER Import	0	0.00	0.00

Percentage(%) of times (N-1) Criteria was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	0	0.00	0.00
2	ER-NR	0	0.00	0.00
3	Import of NR	0	0.00	0.00
4	NEW-SR	0	0.00	0.00
4	NER Import	0	0.00	0.00

Remarks: Flows crossing Total Transfer Capability (TTC) on interregional corridors has been worked out as a proxy for (N-1) violation.



POWER SYSTEM OPERATION CORPORATION LIMITED

पावर सिस्टम ऑपरेशन कारपोरेशन लिमिटेड

NATIONAL LOAD DESPATCH CENTRE – राष्ट्रीय भार प्रेषण केन्द्र

First floor, B-9, Qutab Institutional Area,
Katwaria Sarai, New Delhi-110016.
