

कार्यालय : बी-9, प्रथम एवं द्वितीय तल, कुतुब इंस्टीट्यूशनल एरिया, कटवारिया सराय, नई दिल्ली - 110016
Office : 1st and 2nd Floor, B-9, Qutab Institutional Area, Katwaria Sarai, New Delhi -110016
CIN : U40105DL2009GOI188682, Website : www.grid-india.in, E-mail : gridindiacc@grid-india.in, Tel.: 011- 42785855

संदर्भ संख्या : - GRID-INDIA/NLDC/MR/

दिनांक : 22.06.2023

सेवा में,

वितरण सूची के अनुसार

विषय:- निष्पादन रिपोर्ट – मई 2023

महोदय,

आई०ई०जी०सी०-2010 के प्रावधान के अनुसार, मई 2023 माह की अखिल भारतीय प्रणाली की निष्पादन रिपोर्ट संलग्न है।

धन्यवाद

भवदीय



(सुरजीत बनर्जी)

मुख्य महाप्रबन्धक (प्रणाली प्रचालन)

(रा०भा०प्रे०के०)

संलग्नक : मासिक प्रणाली रिपोर्ट

वितरण सूची Distribution List

- 1 सचिव, के.वि.नि.आ. तीसरा एवं चौथा तल, चंद्रलोक भवन, 36, जनपथ, नई दिल्ली-110001
Secretary, CERC, 3rd & 4th Floor, Chanderlok Building, 36, Janpath, New Delhi-110001
- 2 मुख्य अभियंता (जी एम), के.वि.प्रा., सेवा भवन, आर. के. पुरम, नई दिल्ली-110066
Chief Engineer (GM), CEA, Sewa Bhavan, R.K.Puram, New Delhi-110066
- 3 सदस्य सचिव, उ. क्षेत्र. वि. स., 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली - 110016
Member Secretary, NRPC, 18/A, SJSS Marg, Katwaria Sarai, New Delhi-110016
- 4 सदस्य सचिव, प. क्षेत्र. वि. स., एफ-3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई - 400093
Member Secretary, WRPC, F-3, MIDC Area, Andheri (East), Mumbai-400093
- 5 सदस्य सचिव, द. क्षेत्र. वि. स., 29, रेस कोर्स क्रॉस रोड, बंगलूरु - 560009
Member Secretary, SRPC, 29, Race Course Cross Road, Bangalore-560009
- 6 सदस्य सचिव, पू. क्षेत्र. वि. स., 14, गोल्फ क्लब रोड, कोलकाता - 700033
Member Secretary, ERPC, 14, Golf Club Road, Kolkata-700033
- 7 सदस्य सचिव, उ. पू. क्षेत्र. वि. स., मेघालय राज्य आवासीय वित्त सहकारी समिति लिमिटेड भवन, नॉग्रिम हिल्स, शिलोंग - 793003
Member Secretary, NERPC, Meghalaya State Housing Finance Cooperative Society Ltd. Building, Nongrim Hills, Shillong -793003
- 8 मुख्य अभियंता, राष्ट्रीय विद्युत समिति, एनआरपीसी भवन, तृतीय तल, 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली - 110016
Chief Engineer, National Power Committee, NRPC Building, 3rd floor, 18/A, SJSS Marg, Katwaria Sarai, New Delhi-110016
- 9 कार्यपालक निदेशक, पू. क्षेत्र. भा. प्रे. के., 14, गोल्फ क्लब रोड, कोलकाता - 700033
Executive Director, ERLDC, 14, Golf Club Road, Kolkata-700033
- 10 कार्यपालक निदेशक, प. क्षेत्र. भा. प्रे. के., एफ-3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई - 400093
Executive Director, WRLDC, F-3, MIDC Area, Andheri (East), Mumbai-400093
- 11 कार्यपालक निदेशक, उ. क्षेत्र. भा. प्रे. के., 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली - 110016
Executive Director, NRPC, 18/A, SJSS Marg, Katwaria Sarai, New Delhi-110016
- 12 कार्यपालक निदेशक, द. क्षेत्र. भा. प्रे. के., 29, रेस कोर्स क्रॉस रोड, बंगलूरु - 560009
Executive Director, SRLDC, 29, Race Course Cross Road, Bangalore-560009
- 13 कार्यपालक निदेशक, पू. क्षेत्र. भा. प्रे. के., डोंगतिह, लोअर नॉग्रह, लापलंग, शिलोंग- 793006
Executive Director, NERLDC, Dongtieh, Lower Nongrah, Laplang, Shillong-793006



ग्रिड-इंडिया
GRID-INDIA

GRID CONTROLLER OF INDIA LIMITED

Formerly Power System Operation Corporation Limited

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड

NATIONAL LOAD DESPATCH CENTRE –राष्ट्रीय भार प्रेषण केन्द्र

मासिक ऑपरेशन रिपोर्ट

Monthly
Operation Report



मई 2023

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड
राष्ट्रीय भार प्रेषण केंद्र, नई दिल्ली

GRID CONTROLLER OF INDIA LIMITED

Formerly Power System Operation Corporation Limited

NATIONAL LOAD DESPATCH CENTRE, NEW DELHI



ग्रिड-इंडिया
GRID-INDIA

माह मई 2023 के लिए प्रचालन निष्पादन रिपोर्ट

OPERATIONAL PERFORMANCE REPORT FOR THE
MONTH OF MAY-2023


पृष्ठसूची CONTENTS

1	माह मई 2023 की सारांश रिपोर्ट Summary of report for the month of MAY 2023	1-5
2	क्षेत्रवार स्थापित विद्युत क्षमता Region wise Installed Capacity	6
3	राष्ट्रीय स्तर पर सांध्यकालीन शिखर मांगपूर्ति Peak demand met at National level	7-8
4	राष्ट्रीय स्तर पर विद्युत ऊर्जा खपत Energy consumption at National level	9-10
5	फ्रिक्वेंसी रूपरेखा Frequency profile	11-12
6	राष्ट्रीय स्तर पर जल विद्युत ऊर्जा उत्पादन Hydro generation at National level	13-14
7	राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन Wind generation at National level	15
8	राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन Solar generation at National level	16
9	राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग पूर्ति Daily maximum demand met at National level	17
10	23 मई के माँग एवं उत्पादन प्लॉट (अधिकतम मांग पूर्ति) व माँग का डाटा (15 मिनट अंतराल) Demand and generation plots for 23-MAY (Max Demand Met) and Demand data (15-minute interval)	18-22
11	ऊर्जा आपूर्ति की वास्तविक स्थिति Actual power supply position	23
12	ऊर्जा आवश्यकता एवं आपूर्ति की पिछले वर्ष माह मई 2022 से तुलना Energy requirement and met comparison with MAY 2022	24
13	शिखर मांग आवश्यकता एवं आपूर्ति की पिछले वर्ष माह मई 2022 से तुलना Peak demand requirement and met comparison with MAY 2022	25


14	क्षेत्रीय स्तर पर शिड्यूल एवं ड्रावल Schedule & drawal at regional level	26
15	अंतर क्षेत्रीय विनिमय Inter-regional exchanges	27-36
16	अंतर राष्ट्रीय विद्युत विनिमय Inter-national exchanges	37-39
17	एसटीओए (द्विपक्षीय एवं सामूहिक) एवं यू आइ का ब्यौरा Bilateral and collective short-term open access & UI details	40
18	पावर मार्केट की सूचना Power market information	41-44
19	अक्षय ऊर्जा प्रमाण पत्र प्रक्रिया Renewable energy certificate mechanism	45-47
20	मुख्य घटनाएँ एवं डिस्टर्बेंस Important events/disturbances	48-62
21	नए कमीशंड पारेषण तत्व New elements commissioned	63
22	विभव रूपरेखा Voltage profile	64
23	मई 2023 के दौरान रा. भा. प्रे. के. द्वारा निगरानी में तत्वों के आउटेज की सूची List of outage of elements monitored by NLDC for the month of MAY 2023	65-81
24	अब तक उच्चतम (मांग व ऊर्जा) आँकड़े : माह मई 2023 तक All Time Highest (Demand & Energy) figures: Till MAY 2023	82
25	मई 2023 के लिए सिस्टम रिलाइबिलिटी सूचकांक System Reliability Indices for MAY 2023	83

1. SUMMARY OF REPORT FOR THE MONTH OF MAY-2023

EVENING PEAK HOUR (at 2000hrs) DEMAND MET AT NATIONAL LEVEL (MW)

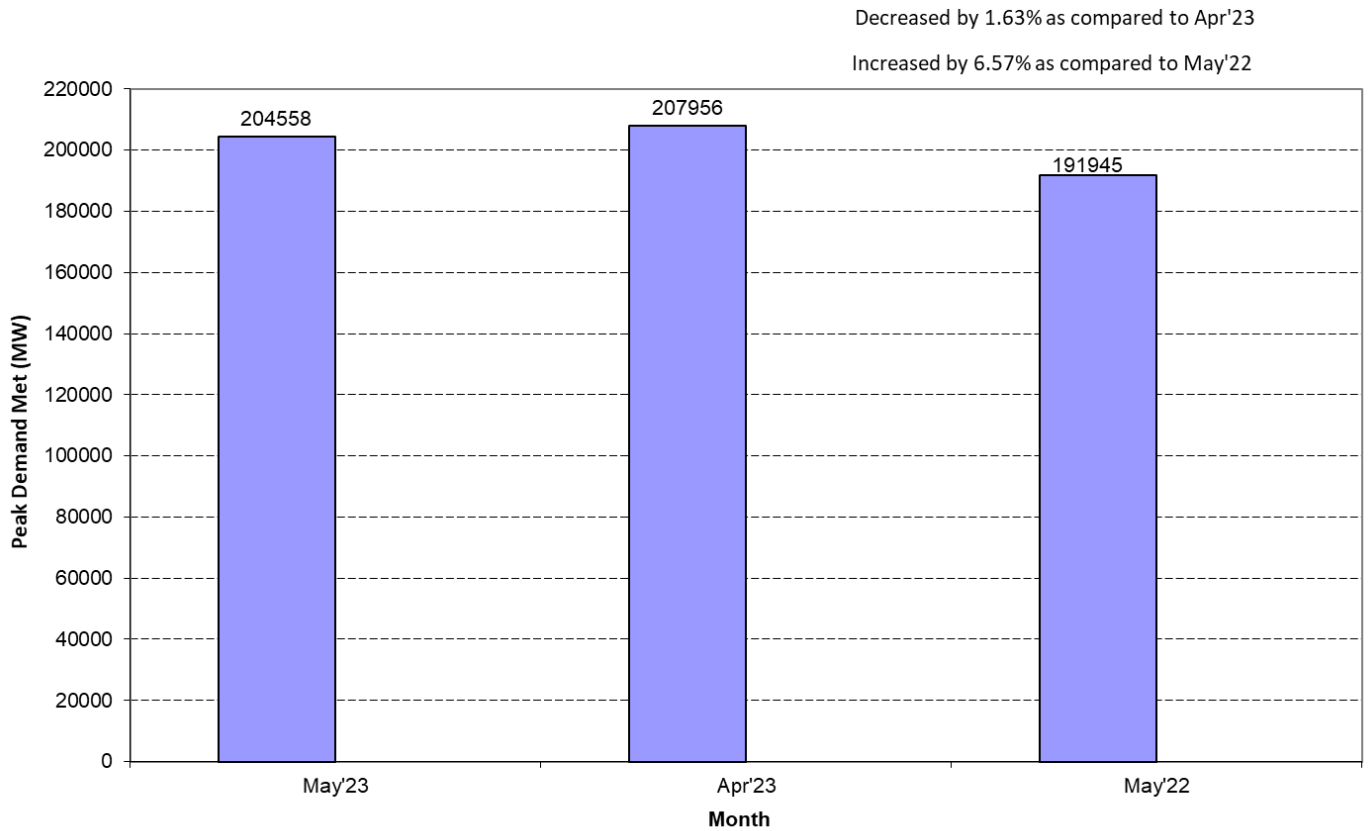


Frequency within IEGC Band

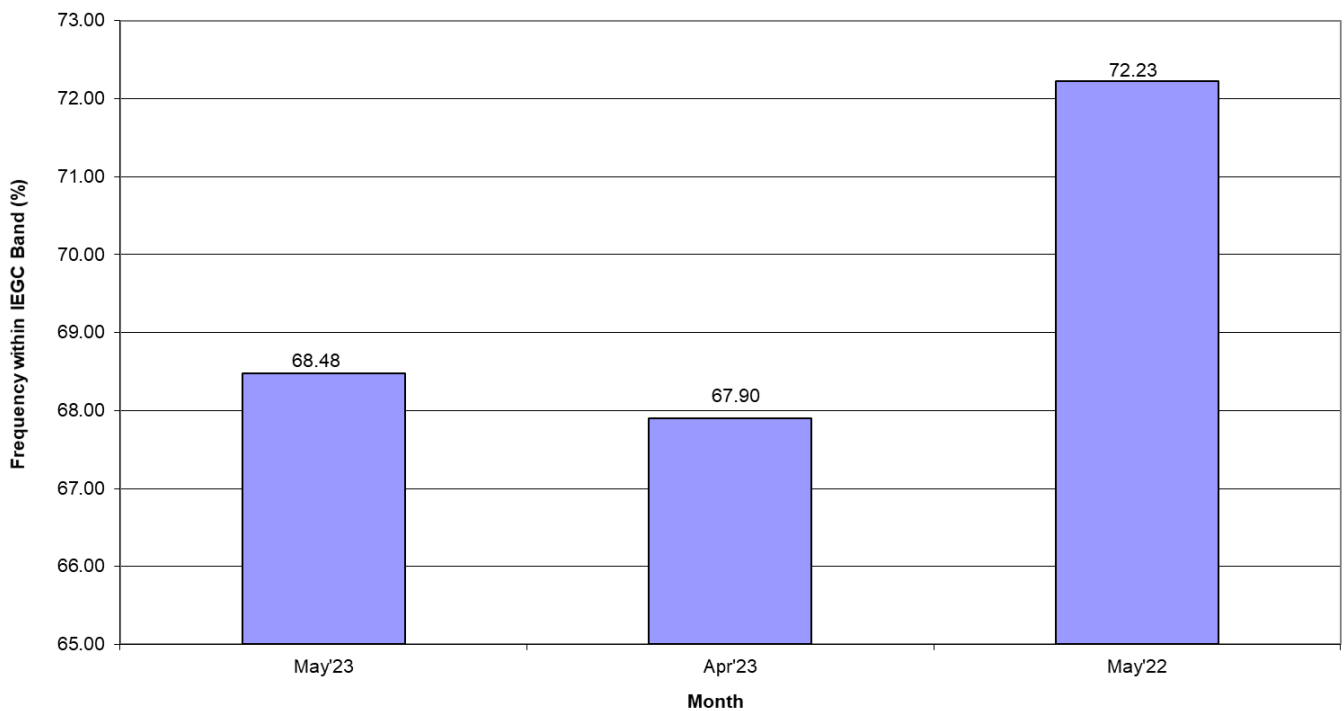

ENERGY MET AT NATIONAL LEVEL (MU)


Increased by 3.84% as compared to Apr'23

Decreased by 0.36% as compared to May'22

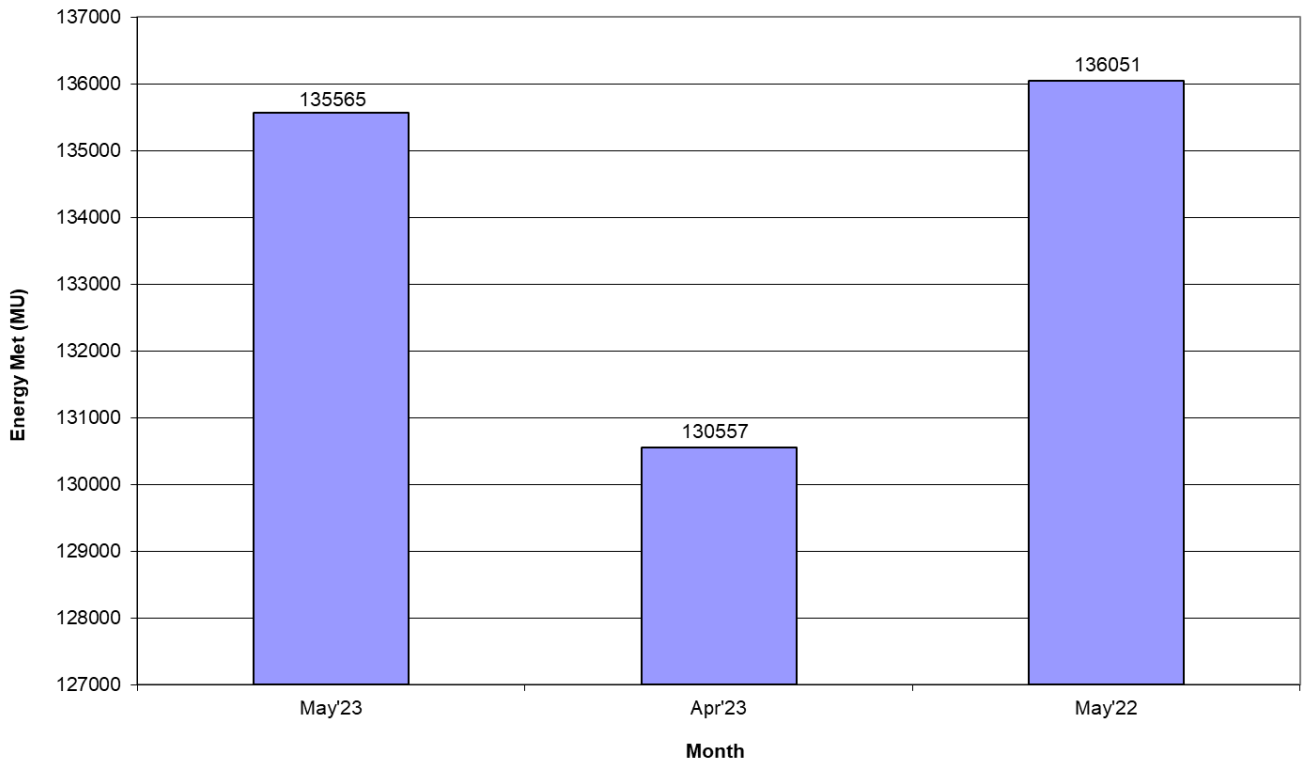


AVERAGE ENERGY MET AT NATIONAL LEVEL (MU/Day)

Decreased by 0.36% as compared to May'22

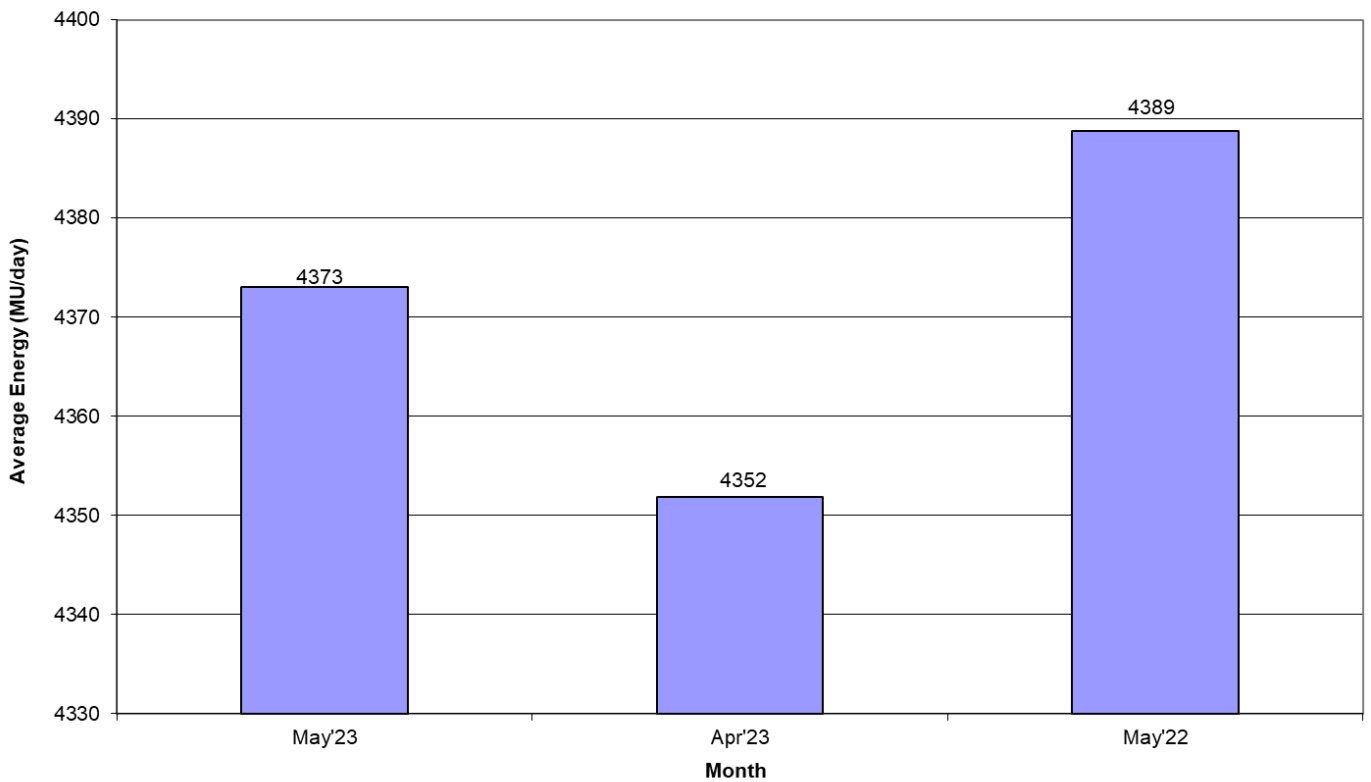


HYDRO GENERATION AT NATIONAL LEVEL (MU)

Increased by 29.70% as compared to Apr'23
Decreased by 11.95% as compared to May'22

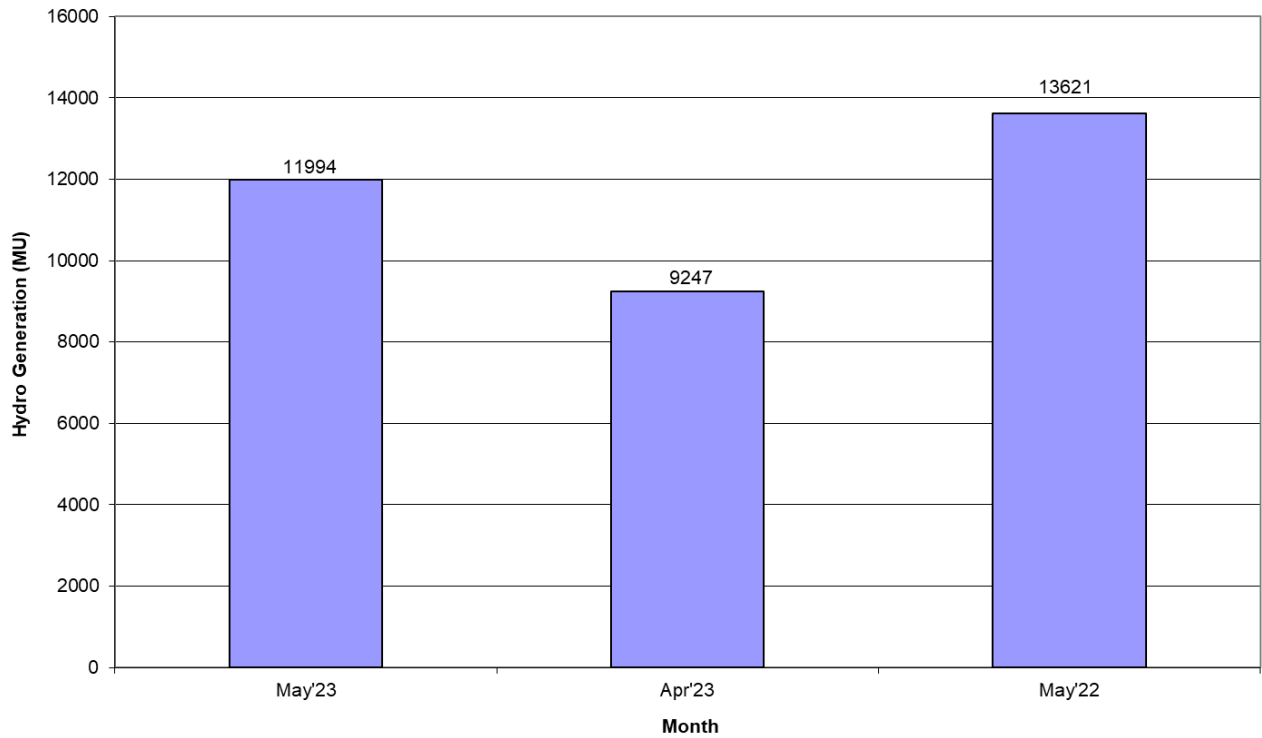


AVERAGE HYDRO GENERATION AT NATIONAL LEVEL (MU/Day)

Decreased by 11.95% as compared to May'22

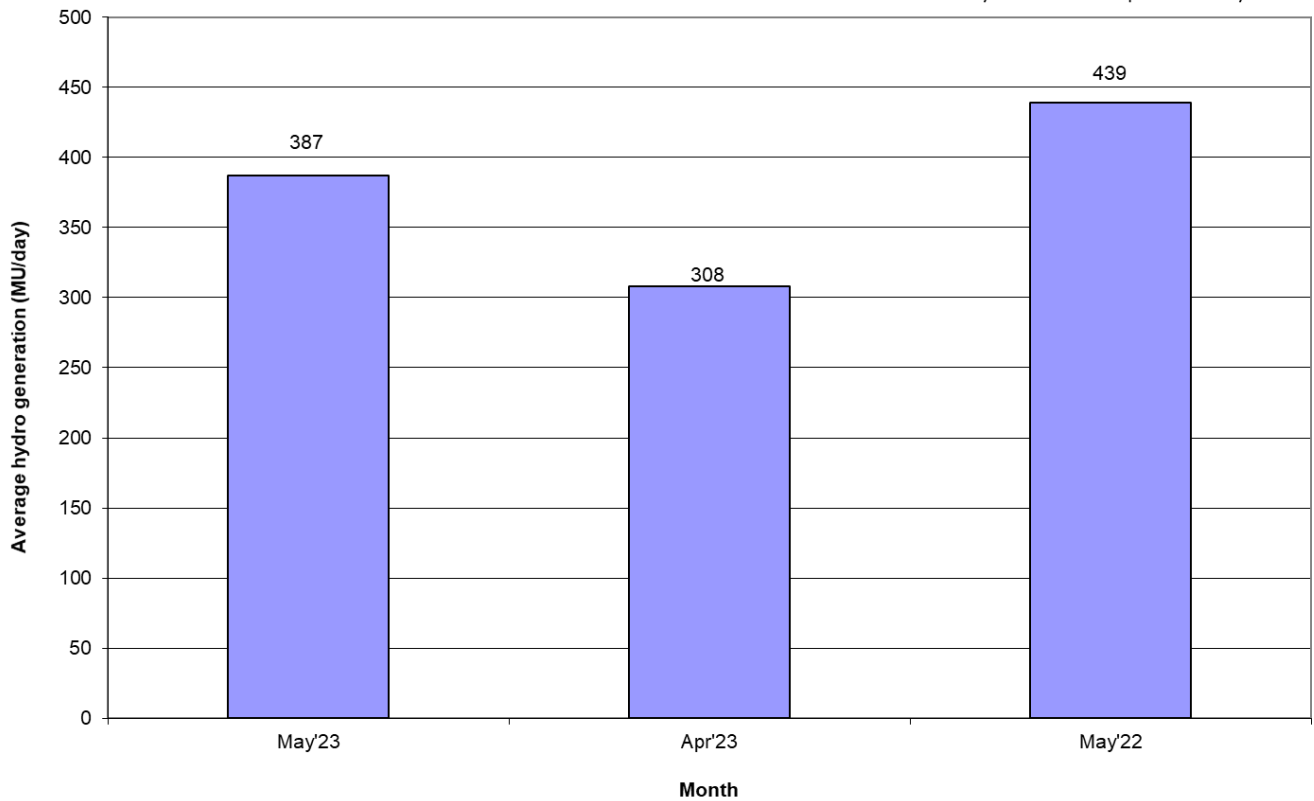


WIND GENERATION AT NATIONAL LEVEL (MU)

Increased by 63.67% as compared to Apr'23
Decreased by 30.64% as compared to May'22

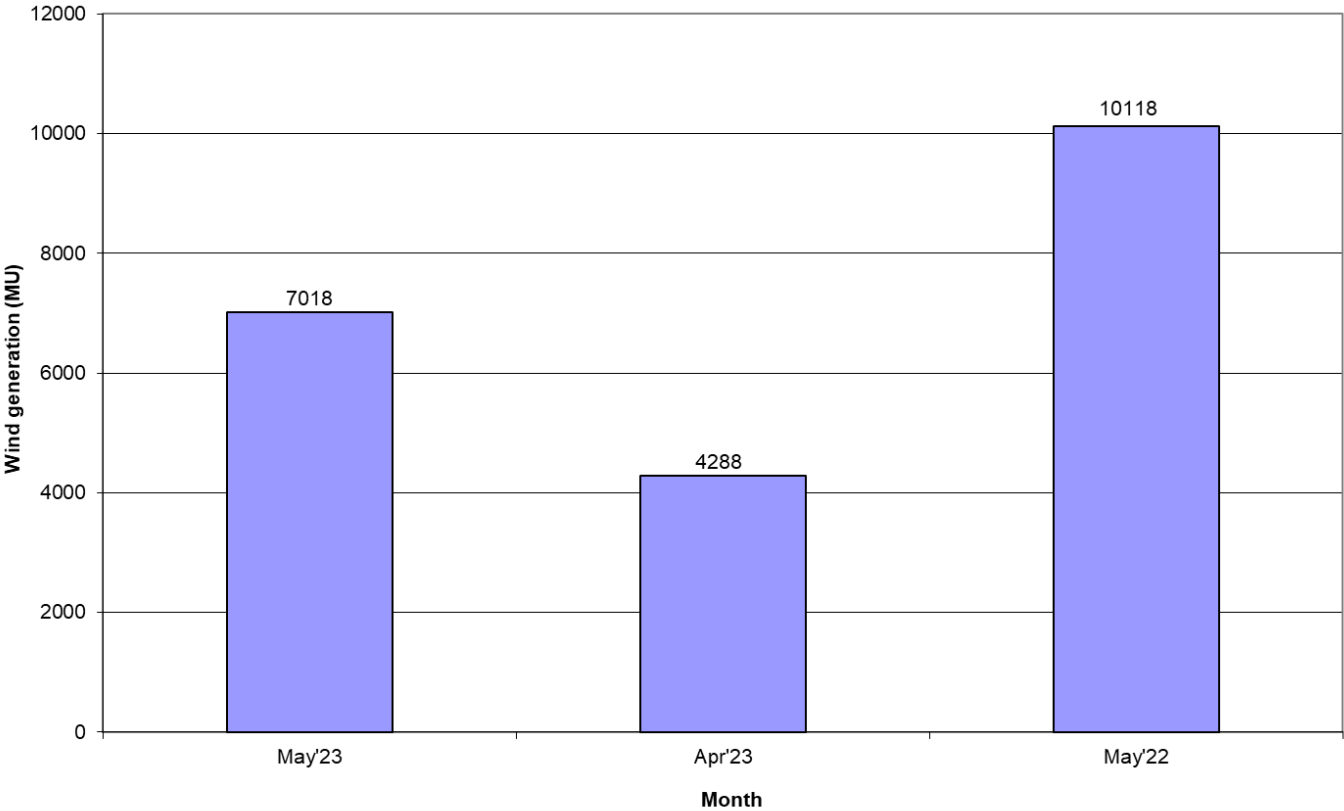

AVERAGE WIND GENERATION AT NATIONAL LEVEL (MU/Day)


Decreased by 30.64% as compared to May'22

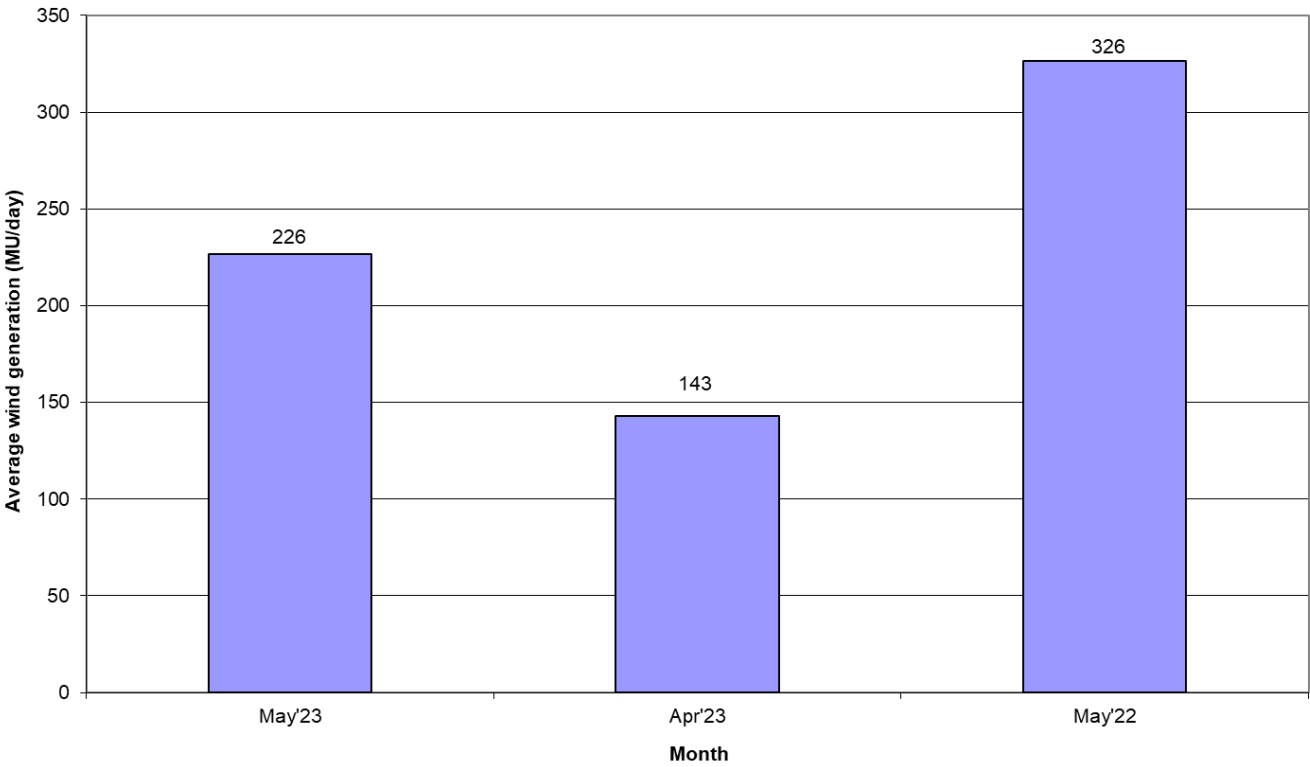

SOLAR GENERATION AT NATIONAL LEVEL (MU)


Increased by 3.19% as compared to Apr'23

Increased by 23.81% as compared to May'22

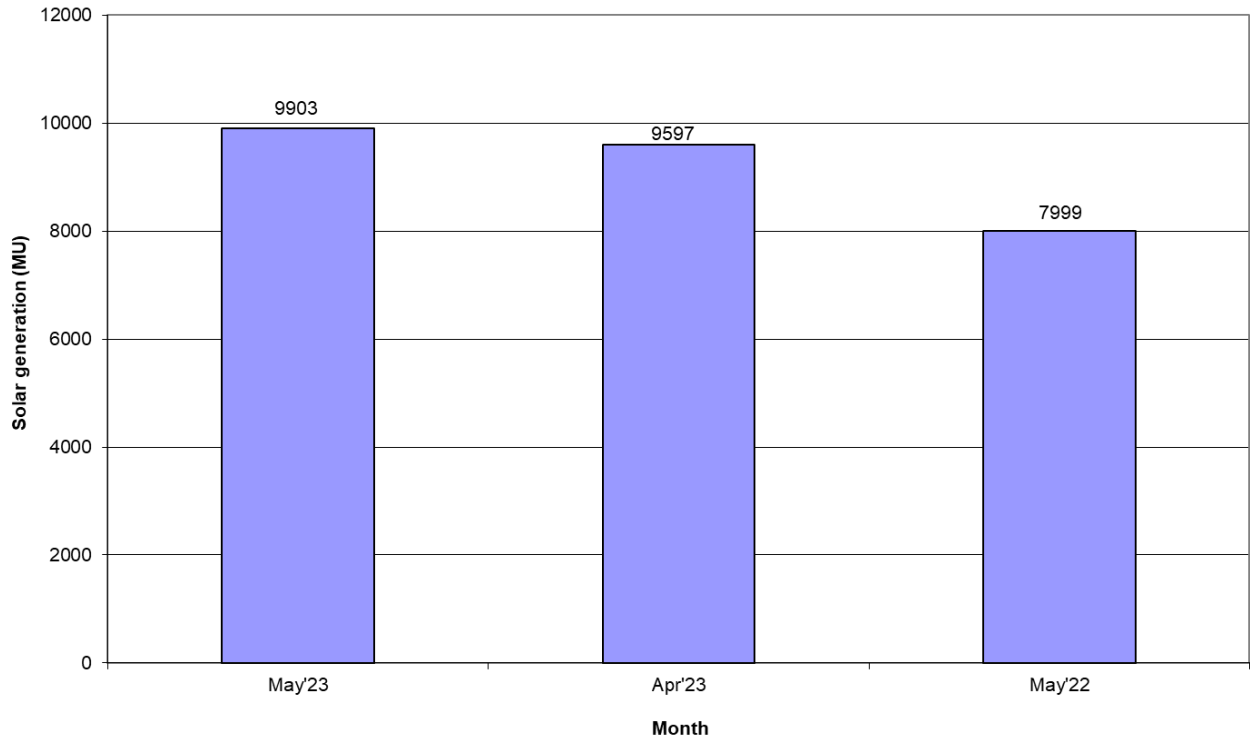

AVERAGE SOLAR GENERATION AT NATIONAL LEVEL (MU/Day)

Increased by 23.81% as compared to May'22

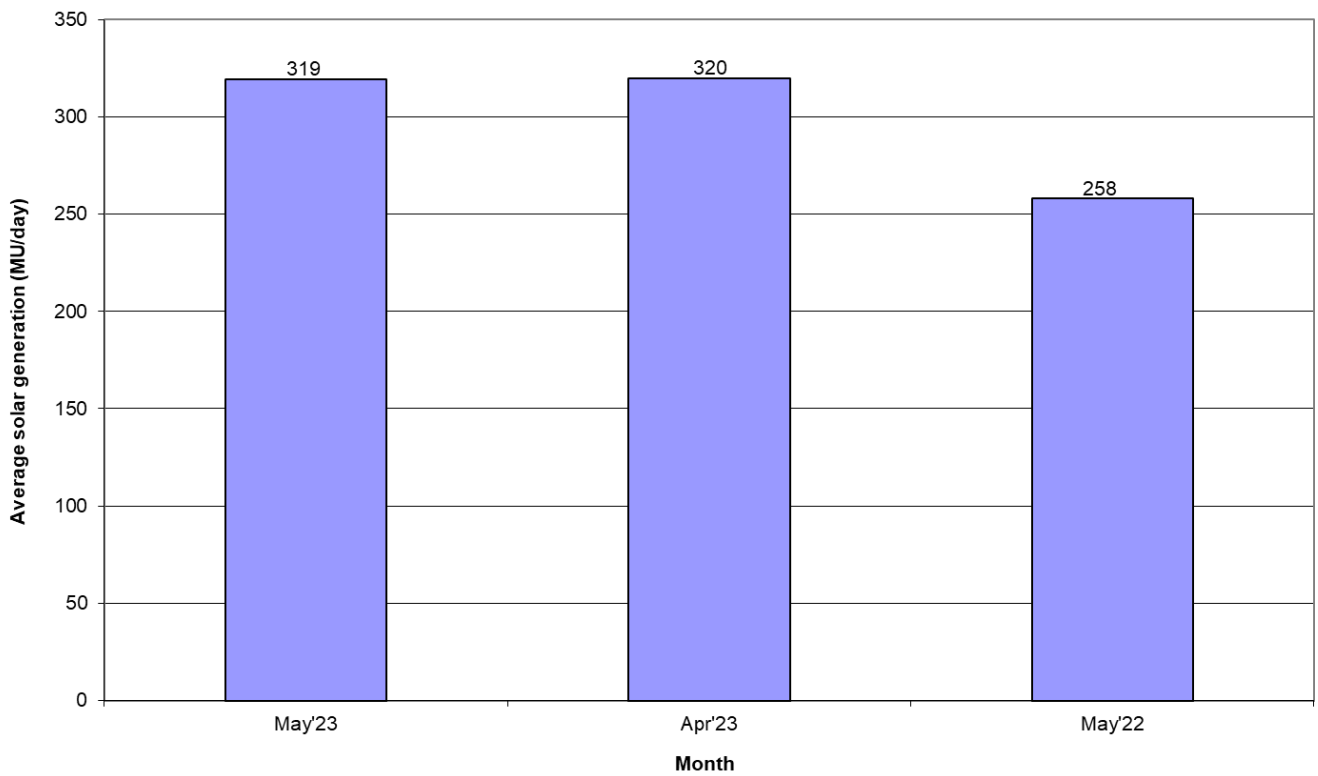

2. ALL INDIA REGIONWISE INSTALLED CAPACITY

As on 31.05.2023
(All figures are in MW)

S No	Region	THERMAL					NUCLEAR	HYDRO	RES @ MNRE	GRAND TOTAL
		COAL	LIGNITE	GAS	DIESEL	TOTAL				
1	NR	55458	1580	5781	0	62819	1620	20752	33157	118347
2	WR	74463	1400	10806	0	86669	1840	7563	40390	136462
3	SR	47005	3640	6492	434	57571	3320	11827	50779	123498
4	ER	27700	0	80	0	27780	0	4764	1854	34398
5	NER	610	0	1665	36	2311	0	1944	550	4805
6	ISLANDS	0	0	0	120	120	0	0	38	158
	ALL INDIA	205235	6620	24824	589	237269	6780	46850	126769	417668

Remarks: Data from CEA website

3. राष्ट्रीय स्तर पर संध्याकालीन शिखर विद्युत मांग पूर्ति
EVENING PEAK HOUR DEMAND MET AT NATIONAL LEVEL

माह: मई 2023 MONTH:- MAY 2023


सभी आंकड़े मेगावाट में All figures in MW

दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
1-May-23	42496	50421	39946	20660	2567	156090
2-May-23	46199	53187	44384	22647	2571	168988
3-May-23	44121	54140	44703	22418	2693	168075
4-May-23	49776	54968	45230	22769	2718	175461
5-May-23	52753	56530	44854	24432	2681	181250
6-May-23	53244	57453	44136	24683	2895	182411
7-May-23	52877	55148	40873	24311	2937	176146
8-May-23	55343	59319	45067	25341	2943	188013
9-May-23	57155	60250	45070	26122	3058	191655
10-May-23	58763	61029	45941	25989	2805	194527
11-May-23	59520	61600	46027	26146	2956	196249
12-May-23	61733	61521	47338	26575	3040	200207
13-May-23	61861	61725	46690	25689	3098	199063
14-May-23	56203	58739	45158	25760	2435	188295
15-May-23	63282	62277	49972	21996	2890	200417
16-May-23	64257	61514	50706	24519	2271	203267
17-May-23	61292	61517	50329	23855	2642	199635
18-May-23	62448	62829	50661	22847	2720	201505
19-May-23	64117	61433	50219	22255	2808	200832
20-May-23	65328	62216	48310	25628	2678	204160
21-May-23	65236	58595	42813	24923	2444	194011
22-May-23	68209	61184	46719	25582	2864	204558
23-May-23	63301	63142	48358	21965	2554	199320
24-May-23	58560	62910	48618	24787	2834	197709
25-May-23	52496	62485	47563	19348	3109	185001
26-May-23	57028	61233	47714	19404	3001	188380
27-May-23	54919	59394	49193	24141	2726	190373
28-May-23	52883	55179	43809	23834	2961	178666
29-May-23	53624	58745	48842	25098	3020	189329
30-May-23	53358	59786	45858	25841	3343	188186
31-May-23	54832	61074	47138	26131	3424	192599
उच्चतम MAXIMUM	68209	63142	50706	26575	3424	204558
निम्नतम MINIMUM	42496	50421	39946	19348	2271	156090
औसत AVERAGE	57007	59405	46524	24055	2829	189819
अब तक का उच्चतम All Time Max.	71909	63593	52366	28579	3510	207956
दिनांक Date	09.09.22	18.04.23	18.04.23	18.04.23	12.08.22	18.04.23

नोट : सभी आंकड़े 2000 बजे की मांगपूर्ति पर आधारित है।

Note: The above figures correspond to value at 2000 Hrs

EVENING PEAK HOUR DEMAND(at 2000hrs)MET DURING THE MONTH OF MAY 2023

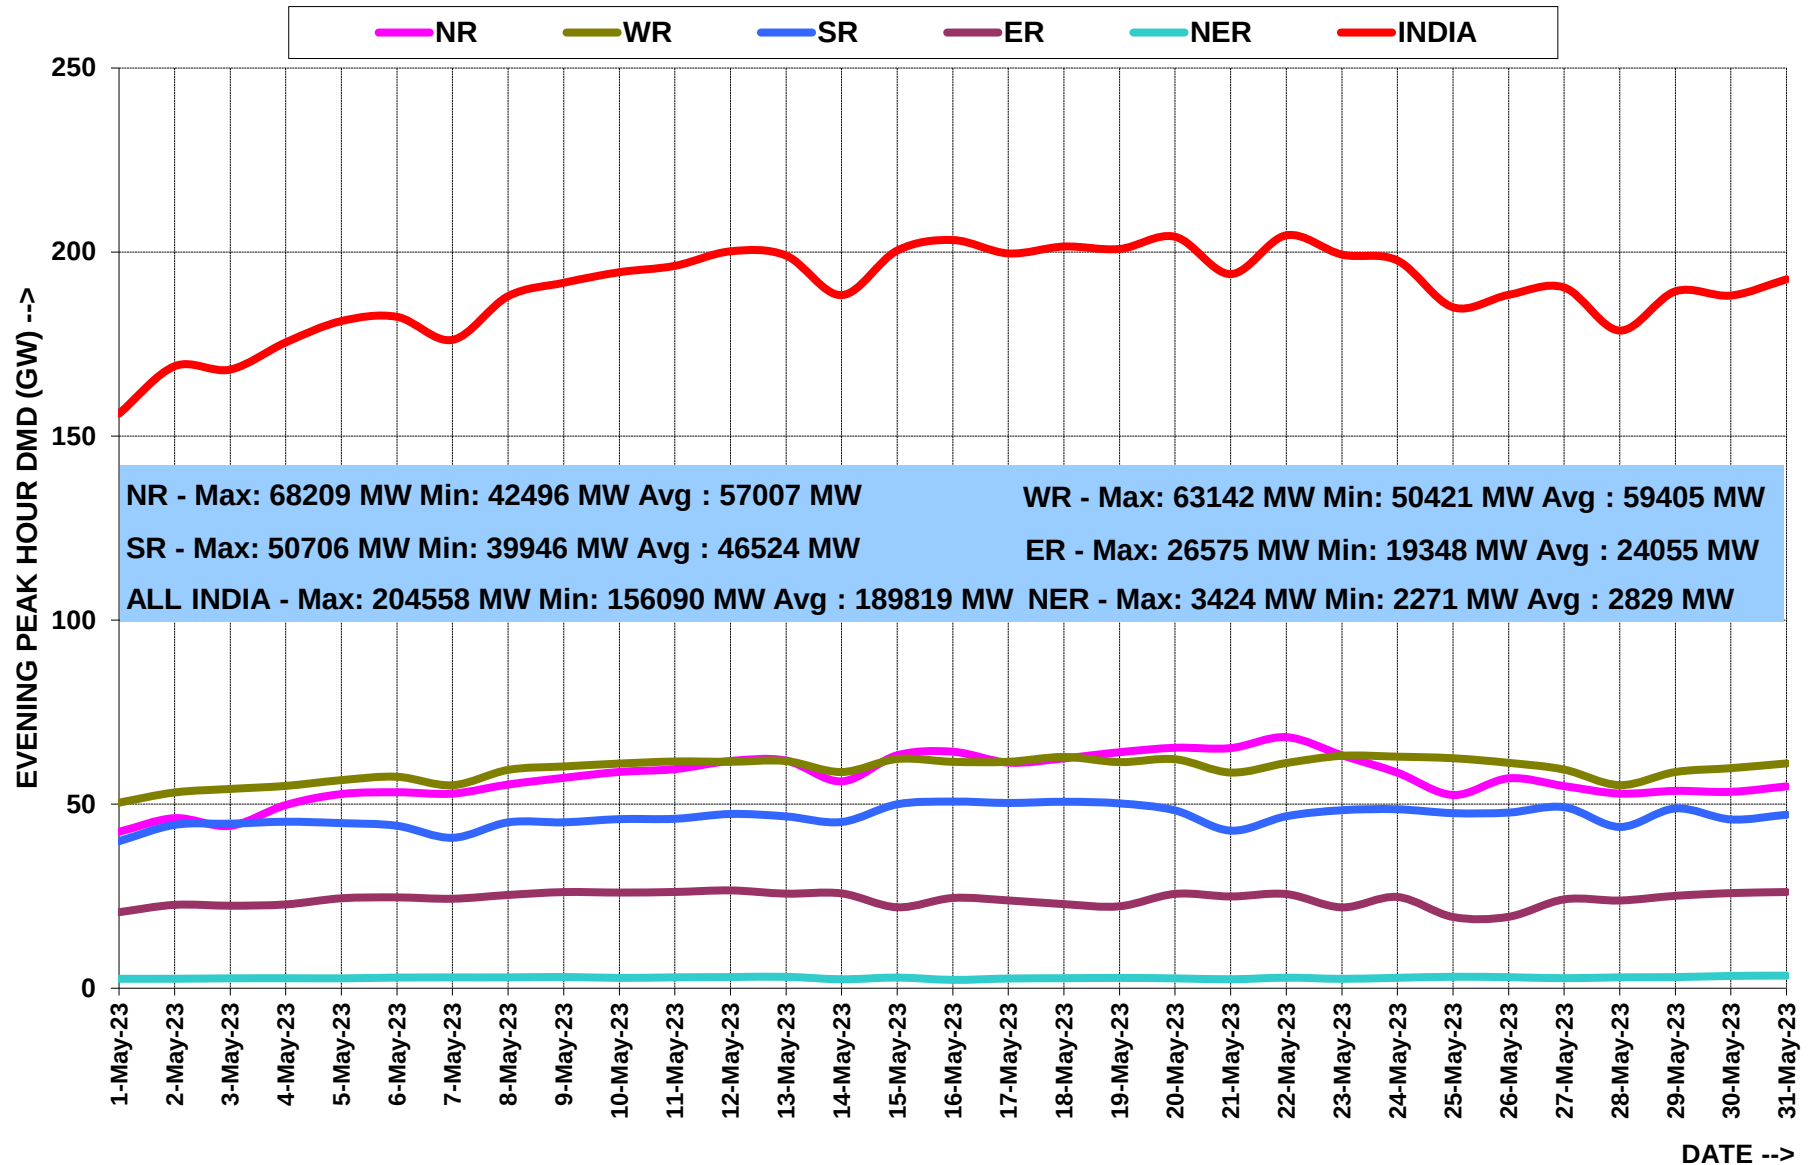


4. राष्ट्रीय स्तर पर विद्युत ऊर्जा आपूर्ति ENERGY MET AT NATIONAL LEVEL

माह: मई 2023 MONTH:- MAY 2023

सभी आंकड़े मिलियन यूनिट में All figures in MU

दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-May-23	979	1198	926	453	49	3605
02-May-23	991	1236	959	472	50	3707
03-May-23	1004	1246	1001	502	51	3804
04-May-23	1019	1267	1024	492	49	3851
05-May-23	1113	1293	1032	514	51	4003
06-May-23	1156	1345	1020	535	53	4109
07-May-23	1125	1325	945	549	53	3998
08-May-23	1202	1397	1012	572	52	4236
09-May-23	1275	1423	1030	591	57	4376
10-May-23	1281	1436	1043	590	56	4406
11-May-23	1322	1465	1071	593	57	4508
12-May-23	1378	1467	1085	594	57	4581
13-May-23	1403	1471	1093	594	58	4619
14-May-23	1326	1427	1054	577	48	4433
15-May-23	1381	1474	1154	537	49	4596
16-May-23	1398	1481	1199	546	45	4669
17-May-23	1466	1477	1229	561	44	4778
18-May-23	1271	1493	1242	532	47	4585
19-May-23	1429	1491	1239	544	51	4753
20-May-23	1467	1495	1214	561	50	4787
21-May-23	1463	1433	1098	562	46	4602
22-May-23	1544	1472	1109	560	49	4735
23-May-23	1559	1498	1158	533	52	4799
24-May-23	1332	1504	1170	533	50	4588
25-May-23	1220	1484	1166	523	55	4448
26-May-23	1148	1448	1165	484	49	4294
27-May-23	1139	1442	1175	490	50	4297
28-May-23	1152	1379	1115	519	53	4218
29-May-23	1187	1367	1181	564	58	4357
30-May-23	1179	1411	1135	594	64	4382
31-May-23	1186	1443	1135	610	67	4441
कुल TOTAL	39095	43788	34179	16882	1621	135565
उच्चतम MAXIMUM	1559	1504	1242	610	67	4799
निम्नतम MINIMUM	979	1198	926	453	44	3605
औसत AVERAGE	1261	1413	1103	545	52	4373
संचयी 2023-24 Cumulative 2023-24	72507	86435	71121	32957	3101	266121
अब तक का उच्चतम All Time Max.	1737	1539	1329	631	69	4836
दिनांक Date	28.06.22	18.04.23	19.04.23	18.04.23	15.07.22	18.04.23

ENERGY MET DURING THE MONTH OF MAY' 2023

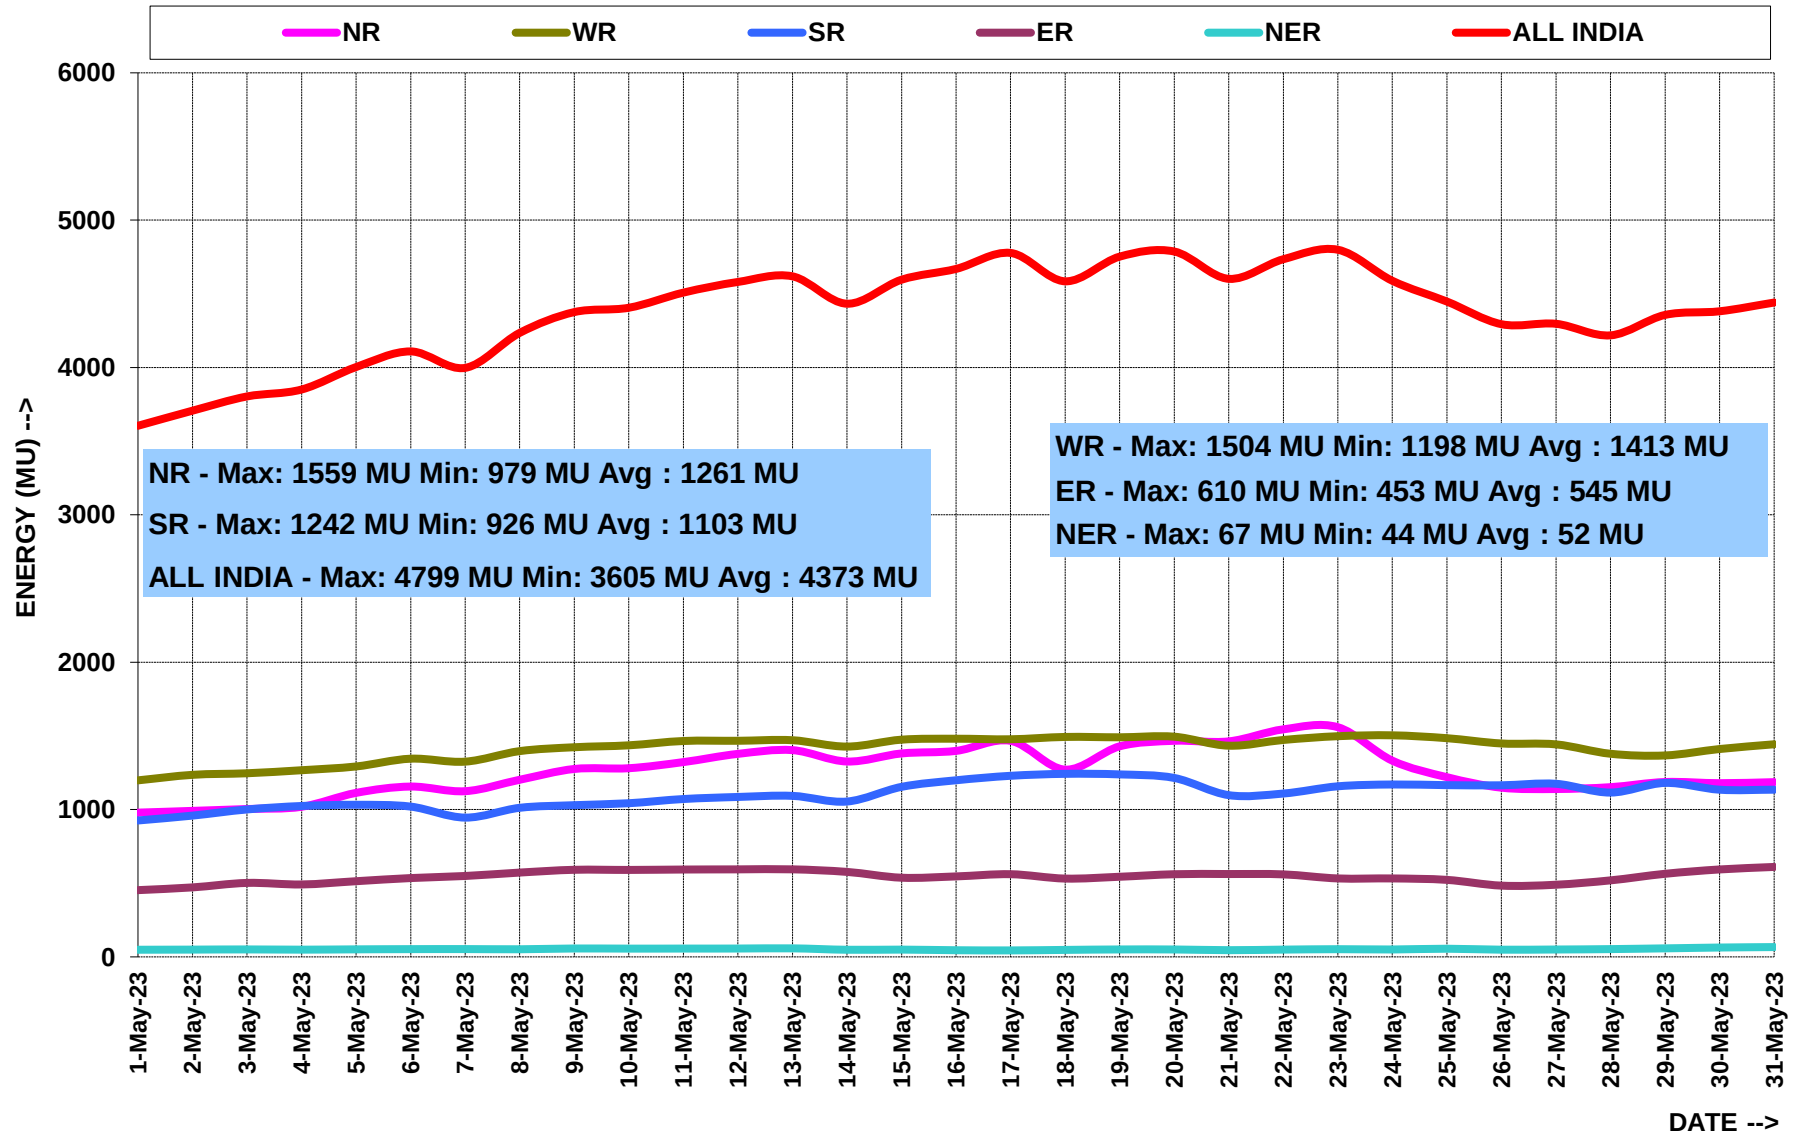

5. वर्ष 2023-24 के लिए आवृत्ति रूपरेखा FREQUENCY PROFILE FOR YEAR 2023-24

राष्ट्रीय ग्रीड NATIONAL GRID								
फ्रिक्वेंसी रूपरेखा (Hz)			<49.9	49.9-50.05	>50.05	उच्चतम फ्रिक्वेंसी	निम्नतम फ्रिक्वेंसी	औसत फ्रिक्वेंसी
% समय	Apr-23	All India Grid	10.54	67.90	21.56	50.33	49.49	49.99
	May-23	All India Grid	9.83	68.48	21.69	50.43	49.48	49.99
	2023-24 (upto May)	All India Grid	10.18	68.20	21.62	50.43	49.48	49.99

5.1 मई 2023 के लिए आवृत्ति रूपरेखा FREQUENCY PROFILE FOR MAY 2023

फ्रिक्वेंसी रूपरेखा (Hz)		<49.9	49.9-50.05	>50.05	उच्चतम फ्रिक्वेंसी	निम्नतम फ्रिक्वेंसी	औसत फ्रिक्वेंसी	एफ़.वी.आई.
% समय	01-May-23	17.47	63.83	18.70	50.30	49.65	49.98	0.08
	02-May-23	9.31	65.56	25.14	50.31	49.78	50.00	0.06
	03-May-23	8.33	77.12	14.55	50.20	49.73	49.99	0.04
	04-May-23	6.93	73.03	20.03	50.17	49.66	50.00	0.05
	05-May-23	9.91	72.74	17.35	50.23	49.77	49.99	0.05
	06-May-23	9.51	71.94	18.54	50.17	49.62	49.99	0.05
	07-May-23	6.82	74.97	18.22	50.28	49.78	49.99	0.04
	08-May-23	10.94	72.66	16.40	50.18	49.76	49.99	0.05
	09-May-23	5.97	76.26	17.77	50.19	49.77	50.00	0.03
	10-May-23	3.77	72.78	23.45	50.26	49.74	50.01	0.04
	11-May-23	7.44	69.77	22.79	50.25	49.71	50.00	0.05
	12-May-23	11.86	70.64	17.50	50.24	49.79	49.98	0.05
	13-May-23	12.00	78.00	10.00	50.18	49.78	49.97	0.05
	14-May-23	6.39	64.24	29.38	50.23	49.70	50.01	0.06
	15-May-23	5.74	64.26	30.00	50.31	49.48	50.02	0.08
	16-May-23	9.79	71.78	18.43	50.40	49.67	49.99	0.06
	17-May-23	9.98	73.43	16.60	50.21	49.75	49.99	0.05
	18-May-23	17.55	62.55	19.91	50.43	49.61	49.98	0.11
	19-May-23	5.60	68.25	26.15	50.27	49.78	50.01	0.05
	20-May-23	6.15	73.90	19.95	50.34	49.76	50.00	0.05
	21-May-23	6.15	74.26	19.59	50.19	49.80	50.00	0.04
	22-May-23	14.47	66.25	19.28	50.26	49.65	49.98	0.08
	23-May-23	1.77	59.27	38.96	50.28	49.78	50.03	0.06
	24-May-23	6.12	69.62	24.26	50.24	49.80	50.00	0.04
	25-May-23	5.76	68.34	25.89	50.30	49.75	50.01	0.06
	26-May-23	12.21	66.77	21.02	50.29	49.69	49.99	0.06
	27-May-23	20.34	59.66	20.00	50.32	49.64	49.97	0.10
	28-May-23	18.98	65.52	15.50	50.20	49.53	49.97	0.10
	29-May-23	23.99	61.74	14.27	50.17	49.65	49.96	0.09
	30-May-23	11.03	50.65	38.32	50.31	49.58	50.01	0.10
	31-May-23	2.50	63.10	34.40	50.28	49.84	50.03	0.04


6.राष्ट्रीय स्तर पर जल विद्युत उत्पादन
HYDRO GENERATION AT NATIONAL LEVEL

माह: मई 2023 MONTH:- MAY 2023

सभी आंकड़े मिलियन यूनिट में All figures in MU

दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-May-23	179	16	50	55	14	315
02-May-23	192	15	66	58	15	346
03-May-23	201	16	67	44	12	340
04-May-23	205	14	73	42	11	345
05-May-23	206	22	77	47	11	364
06-May-23	194	40	65	46	12	358
07-May-23	187	27	61	63	11	349
08-May-23	190	33	68	55	12	359
09-May-23	181	43	67	62	11	363
10-May-23	174	39	61	58	10	342
11-May-23	181	30	60	53	9	333
12-May-23	195	31	61	47	8	342
13-May-23	213	23	61	45	8	350
14-May-23	213	17	51	52	8	341
15-May-23	211	23	69	54	8	365
16-May-23	209	30	82	52	8	381
17-May-23	216	45	89	48	9	407
18-May-23	219	44	83	60	11	417
19-May-23	215	48	79	52	14	409
20-May-23	227	43	68	70	17	425
21-May-23	237	31	62	55	13	398
22-May-23	259	30	64	47	14	415
23-May-23	276	36	60	55	12	438
24-May-23	281	36	59	47	11	434
25-May-23	270	28	54	63	11	426
26-May-23	262	46	61	77	12	459
27-May-23	250	46	74	75	18	465
28-May-23	236	38	75	65	14	427
29-May-23	233	48	84	64	10	439
30-May-23	235	52	61	58	10	417
31-May-23	250	48	56	60	10	424
कुल TOTAL	6798	1041	2070	1731	354	11994
उच्चतम MAXIMUM	281	52	89	77	18	465
निम्नतम MINIMUM	174	14	50	42	8	315
औसत AVERAGE	219	34	67	56	11	387
संचयी 2023-24 Cumulative 2023-24	11348	2095	4191	2950	657	21241
अब तक का उच्चतम All Time Max.	409	167	208	157	41	877
दिनांक Date	22.08.22	18.12.14	31.08.18	14.09.22	01.08.22	30.08.22

HYDRO ENERGY DURING THE MONTH OF MAY' 2023

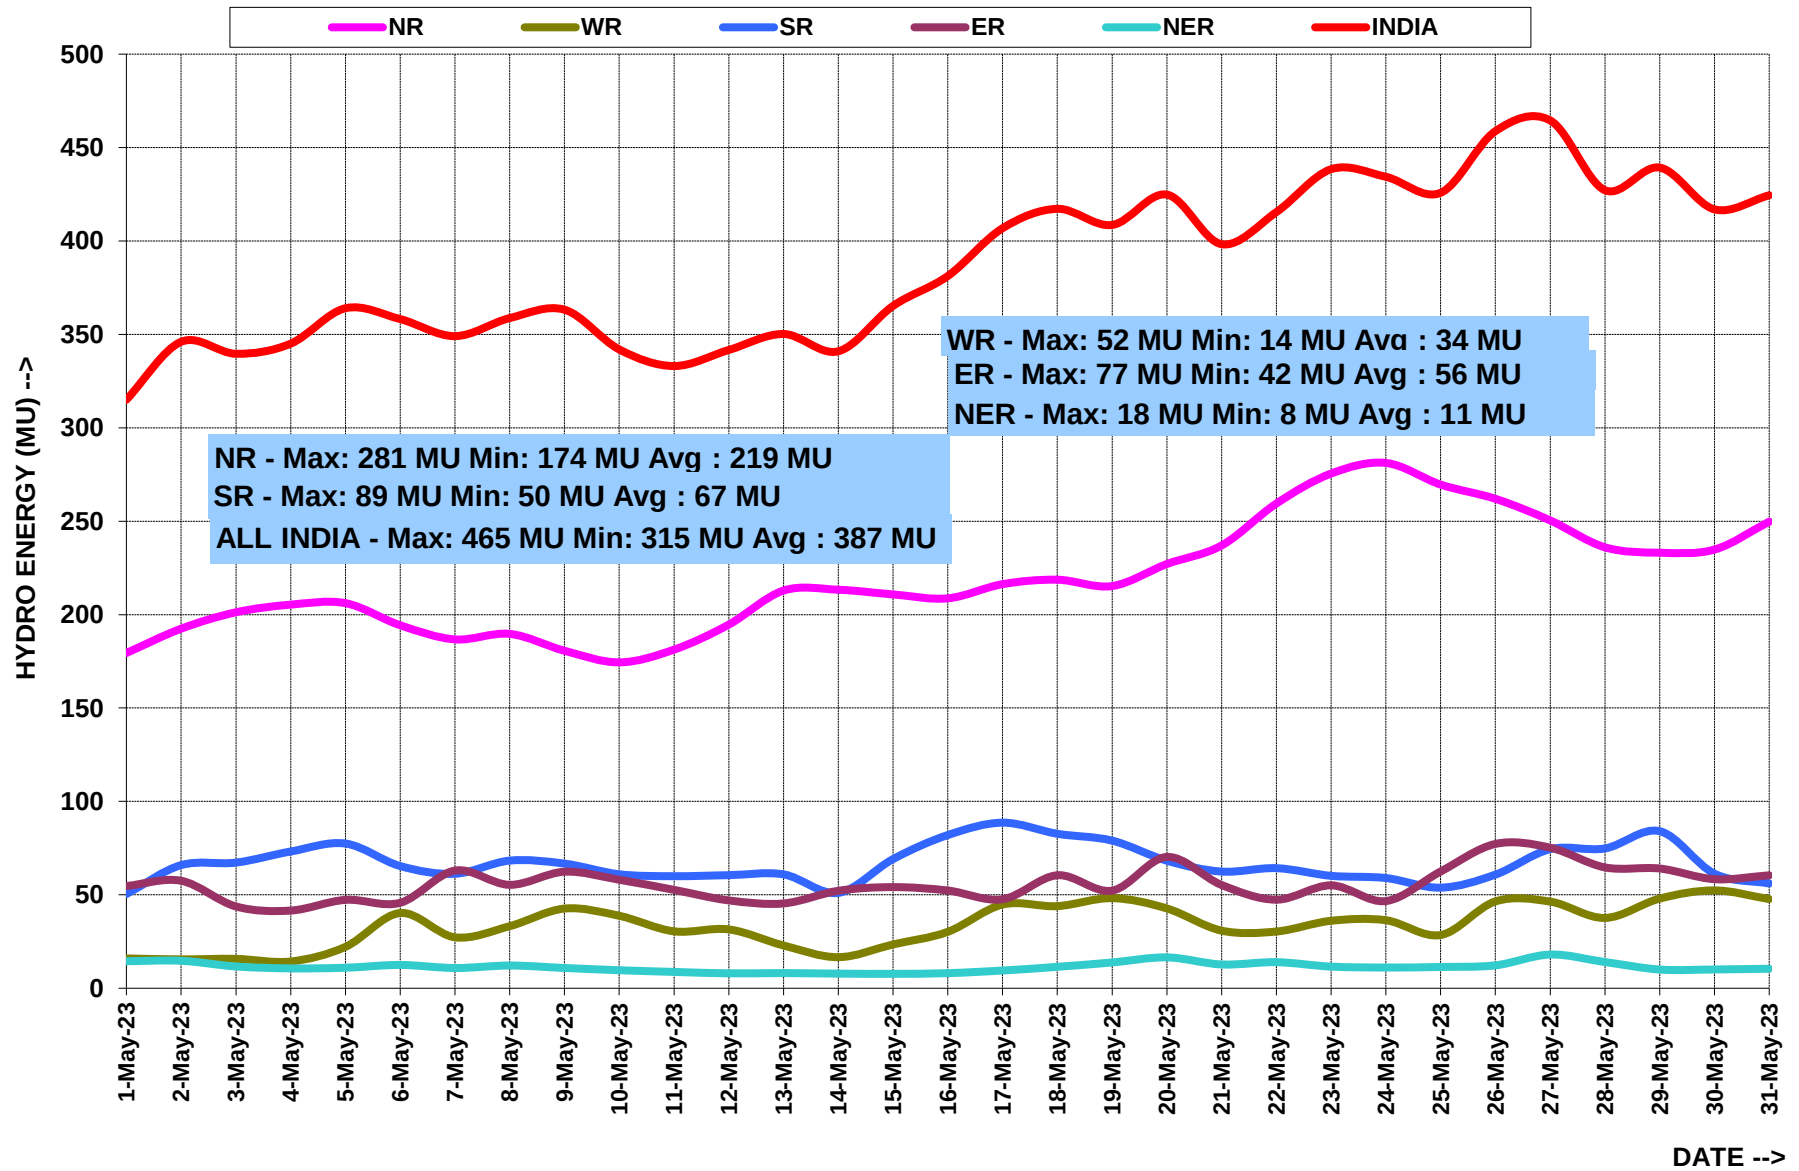

7. राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन
WIND GENERATION AT NATIONAL LEVEL

माह: मई 2023 MONTH:- MAY 2023

सभी आंकड़े मिलियन यूनिट में All figures in MU

दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-May-23	5	50	30	-----	-----	86
02-May-23	8	63	29	-----	-----	99
03-May-23	5	59	41	-----	-----	105
04-May-23	14	55	27	-----	-----	96
05-May-23	17	56	35	-----	-----	108
06-May-23	16	59	46	-----	-----	120
07-May-23	29	77	42	-----	-----	147
08-May-23	25	81	36	-----	-----	142
09-May-23	18	60	37	-----	-----	114
10-May-23	16	60	27	-----	-----	104
11-May-23	4	89	64	-----	-----	158
12-May-23	26	118	105	-----	-----	249
13-May-23	35	155	165	-----	-----	354
14-May-23	31	183	166	-----	-----	379
15-May-23	68	206	144	-----	-----	419
16-May-23	50	188	89	-----	-----	327
17-May-23	55	157	51	-----	-----	263
18-May-23	10	146	52	-----	-----	208
19-May-23	13	102	74	-----	-----	189
20-May-23	45	123	81	-----	-----	249
21-May-23	65	132	70	-----	-----	267
22-May-23	59	135	45	-----	-----	238
23-May-23	44	156	51	-----	-----	250
24-May-23	48	202	100	-----	-----	351
25-May-23	65	233	144	-----	-----	443
26-May-23	56	246	152	-----	-----	454
27-May-23	42	230	99	-----	-----	371
28-May-23	32	178	74	-----	-----	283
29-May-23	19	82	34	-----	-----	135
30-May-23	17	73	46	-----	-----	137
31-May-23	14	106	53	-----	-----	172
कुल TOTAL	950	3860	2207	-----	-----	7018
उच्चतम MAXIMUM	68	246	166	-----	-----	454
निम्नतम MINIMUM	4	50	27	-----	-----	86
औसत AVERAGE	31	125	71	-----	-----	226
संचयी 2023-24 Cumulative 2023-24	1598	6386	3322	-----	-----	11305
अब तक का उच्चतम All Time Max.	78	272	297	-----	-----	555
दिनांक Date	09.06.22	22.05.22	12.07.22	-----	-----	22.05.22

*Source: As reported by SLDCs. Limited visibility of embedded wind generator data.

8. राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन
SOLAR GENERATION AT NATIONAL LEVEL

माह: मई 2023 MONTH:- MAY 2023

सभी आंकड़े मिलियन यूनिट में All figures in MU

दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-May-23	125	55	104	4.5	1.2	289
02-May-23	129	57	97	5.1	1.2	289
03-May-23	137	55	104	2.9	0.9	300
04-May-23	135	60	111	2.8	0.7	309
05-May-23	140	60	93	2.7	1.0	296
06-May-23	132	60	114	2.8	1.1	310
07-May-23	135	63	94	5.4	1.4	299
08-May-23	145	63	113	2.9	1.2	324
09-May-23	145	67	119	5.3	1.3	337
10-May-23	147	70	126	6.2	1.2	351
11-May-23	145	70	119	3.4	1.3	339
12-May-23	143	71	118	3.2	1.1	336
13-May-23	133	69	119	2.9	1.1	325
14-May-23	127	68	133	2.8	0.5	332
15-May-23	120	67	138	5.7	1.0	331
16-May-23	131	66	136	5.3	0.9	339
17-May-23	137	67	133	5.6	0.7	343
18-May-23	134	67	131	6.0	0.7	339
19-May-23	139	66	122	2.7	0.9	331
20-May-23	141	65	116	2.2	1.1	324
21-May-23	140	65	116	2.3	1.0	324
22-May-23	144	68	121	2.4	1.0	335
23-May-23	134	65	126	4.8	1.1	330
24-May-23	128	65	128	5.3	0.7	327
25-May-23	131	65	124	5.1	1.2	326
26-May-23	130	64	128	5.5	1.0	328
27-May-23	118	66	130	3.5	0.9	318
28-May-23	85	62	123	3.6	1.3	274
29-May-23	125	60	114	3.0	1.5	303
30-May-23	95	62	99	2.9	1.4	260
31-May-23	137	68	124	2.8	1.4	333
कुल TOTAL	4085	1994	3670	122	33	9903
उच्चतम MAXIMUM	147	71	138	6	1	351
निम्नतम MINIMUM	85	55	93	2	0	260
औसत AVERAGE	132	64	118	4	1	319
संचयी 2023-24 Cumulative 2023-24	8039	3854	7305	239	63.2	19500
अब तक का उच्चतम All Time Max.	147	71	143	7	2.4	351
दिनांक Date	10.05.23	12.05.23	21.03.23	23.03.23	22.06.22	10.05.23

*Source: RLDCs for solar connected to ISTS; SLDCs for embedded solar. Limited visibility of embedded solar data.

9. राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग पूर्ति
DAILY MAXIMUM DEMAND MET AT NATIONAL LEVEL

माह: मई 2023 MONTH:- MAY 2023

सभी आंकड़े मेगावाट में All figures in MW


दिनांक Date	ऊत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL	विभिन्नता फैक्टर Diversity Factor*
01-May-23	45847	52166	42168	21134	2644	159720	1.027
02-May-23	48236	56712	45503	22958	2597	173208	1.016
03-May-23	47159	56477	45760	22642	2712	172050	1.016
04-May-23	51290	57574	47616	23080	2717	178915	1.019
05-May-23	53612	59283	48257	24480	2854	184356	1.022
06-May-23	53891	60710	47187	25193	2981	185602	1.023
07-May-23	53111	58842	41849	26218	2957	180377	1.014
08-May-23	56138	64448	47857	26581	2992	191660	1.033
09-May-23	57874	64677	48390	27163	3197	196276	1.026
10-May-23	59313	65450	48177	27105	2812	198388	1.023
11-May-23	60808	67054	49984	27235	3132	202891	1.026
12-May-23	62766	66721	51211	27402	3136	207191	1.020
13-May-23	63697	66298	51421	27110	3216	208181	1.017
14-May-23	61564	64711	47873	26367	2461	199382	1.018
15-May-23	63511	67695	54676	25590	2923	212421	1.009
16-May-23	64645	67555	55920	25851	2557	215113	1.007
17-May-23	66838	68011	58369	26592	2672	221076	1.006
18-May-23	62941	68789	59501	24683	2822	213893	1.023
19-May-23	64614	68809	59107	25620	2941	218030	1.014
20-May-23	68261	68500	58366	26777	2859	217155	1.035
21-May-23	68456	65106	51371	26893	2476	207935	1.031
22-May-23	69729	68657	54614	26927	2979	220974	1.009
23-May-23	72920	69633	54954	26075	2633	221347	1.022
24-May-23	61589	68227	55081	25578	2892	210952	1.011
25-May-23	56201	67605	55704	25189	3168	204585	1.016
26-May-23	57572	65317	55312	23400	3090	196387	1.042
27-May-23	55413	65047	55688	24273	2765	194797	1.043
28-May-23	53475	63095	51662	24755	3001	190900	1.027
29-May-23	54461	64556	57580	26511	3282	201431	1.025
30-May-23	54227	63775	52904	27111	3380	196231	1.026
31-May-23	54939	66745	54138	27768	3452	201708	1.026
उच्चतम MAXIMUM	72920	69633	59501	27768	3452	221347	1.043
निम्नतम MINIMUM	45847	52166	41849	21134	2461	159720	1.006
औसत AVERAGE	58874	64460	51877	25621	2913	199456	1.022
अब तक का उच्चतम All Time Max.	77091	71321	64314	29302	3596	221347	
दिनांक Date	28.06.22	27.12.22	15.03.23	19.04.23	17.08.22	23.05.23	

* Diversity factor = (Sum of regional max demands) / All India max demand


नोट : यह आंकड़े एनएलडीसी स्काडा प्रणाली में दर्ज दैनिक अधिकतम मांगपूर्ति दर्शाते हैं ।

Note: The above figures denote daily maximum demand met recorded in NLDC SCADA.


10. DEMAND AND GENERATION PLOTS FOR 23 MAY (MAXIMUM DEMAND MET)

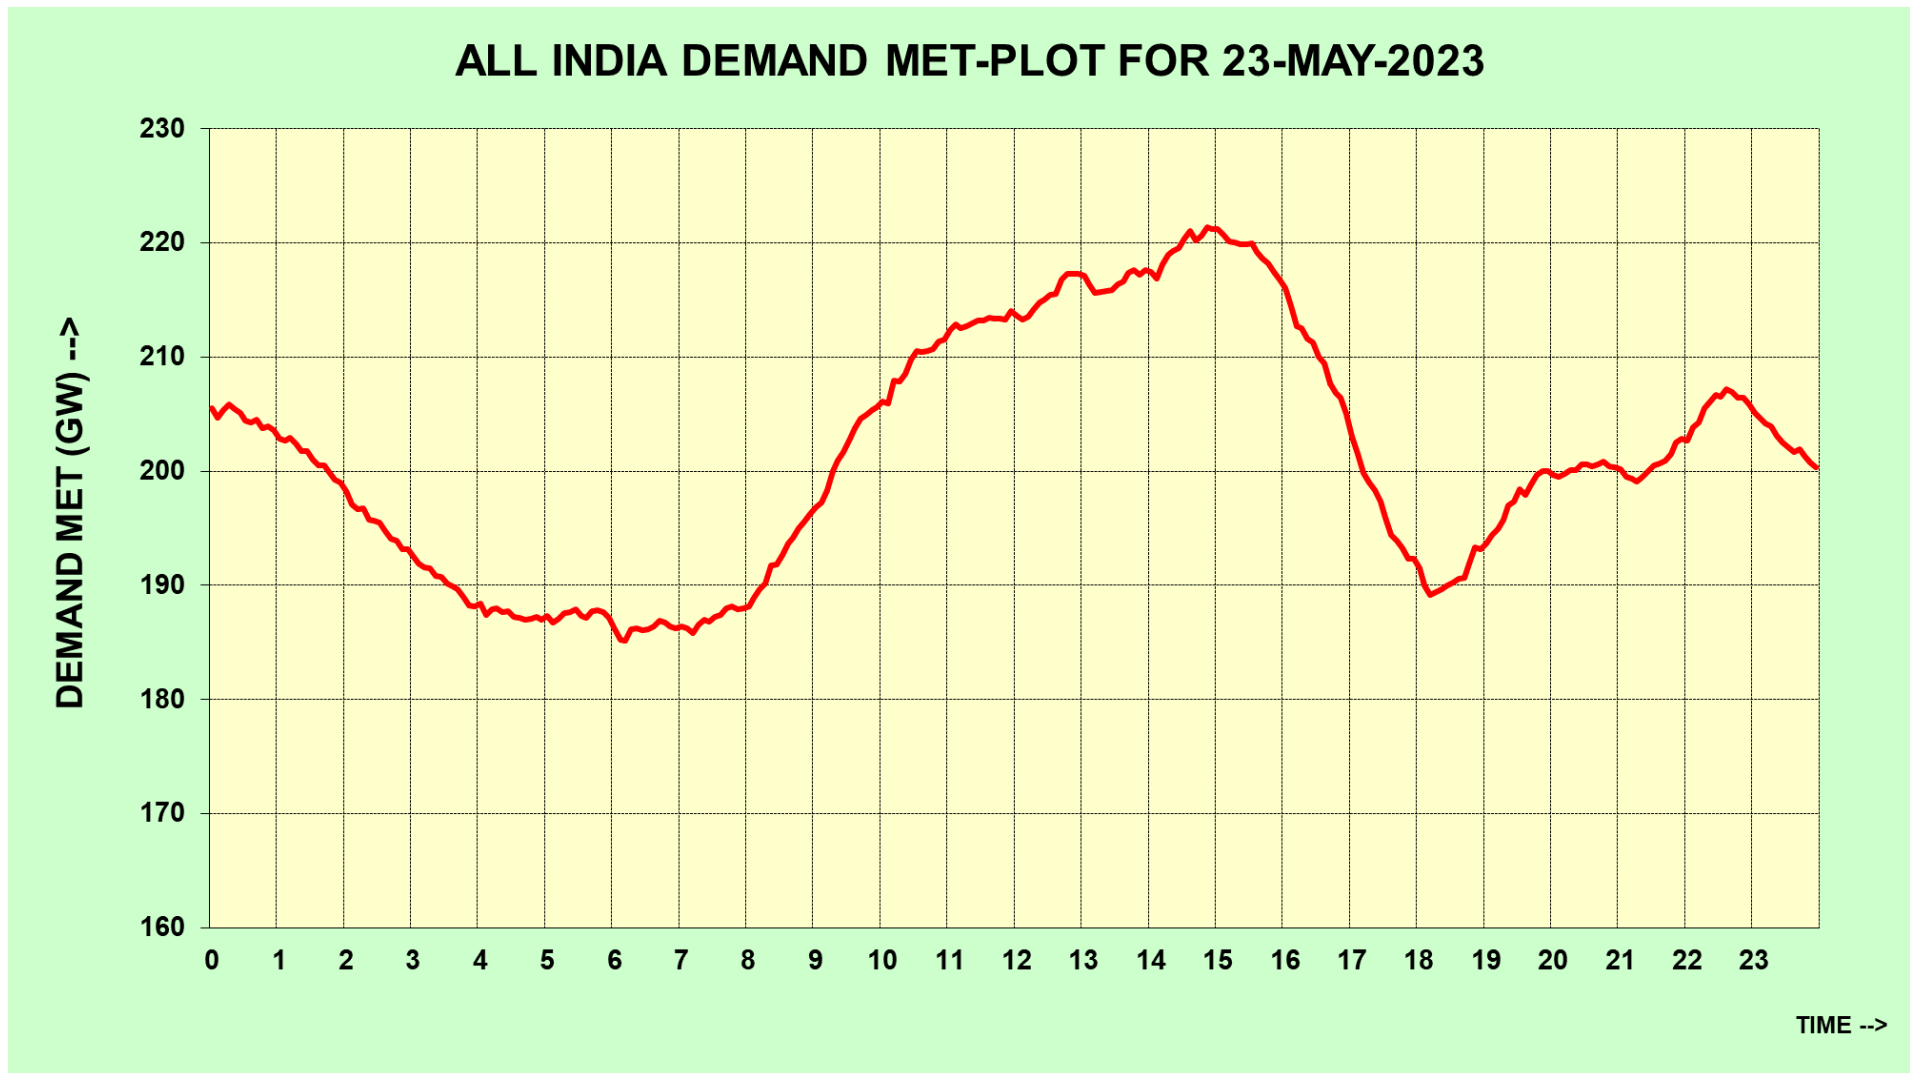


REGIONAL DEMAND MET-PLOT FOR 23-MAY-2023

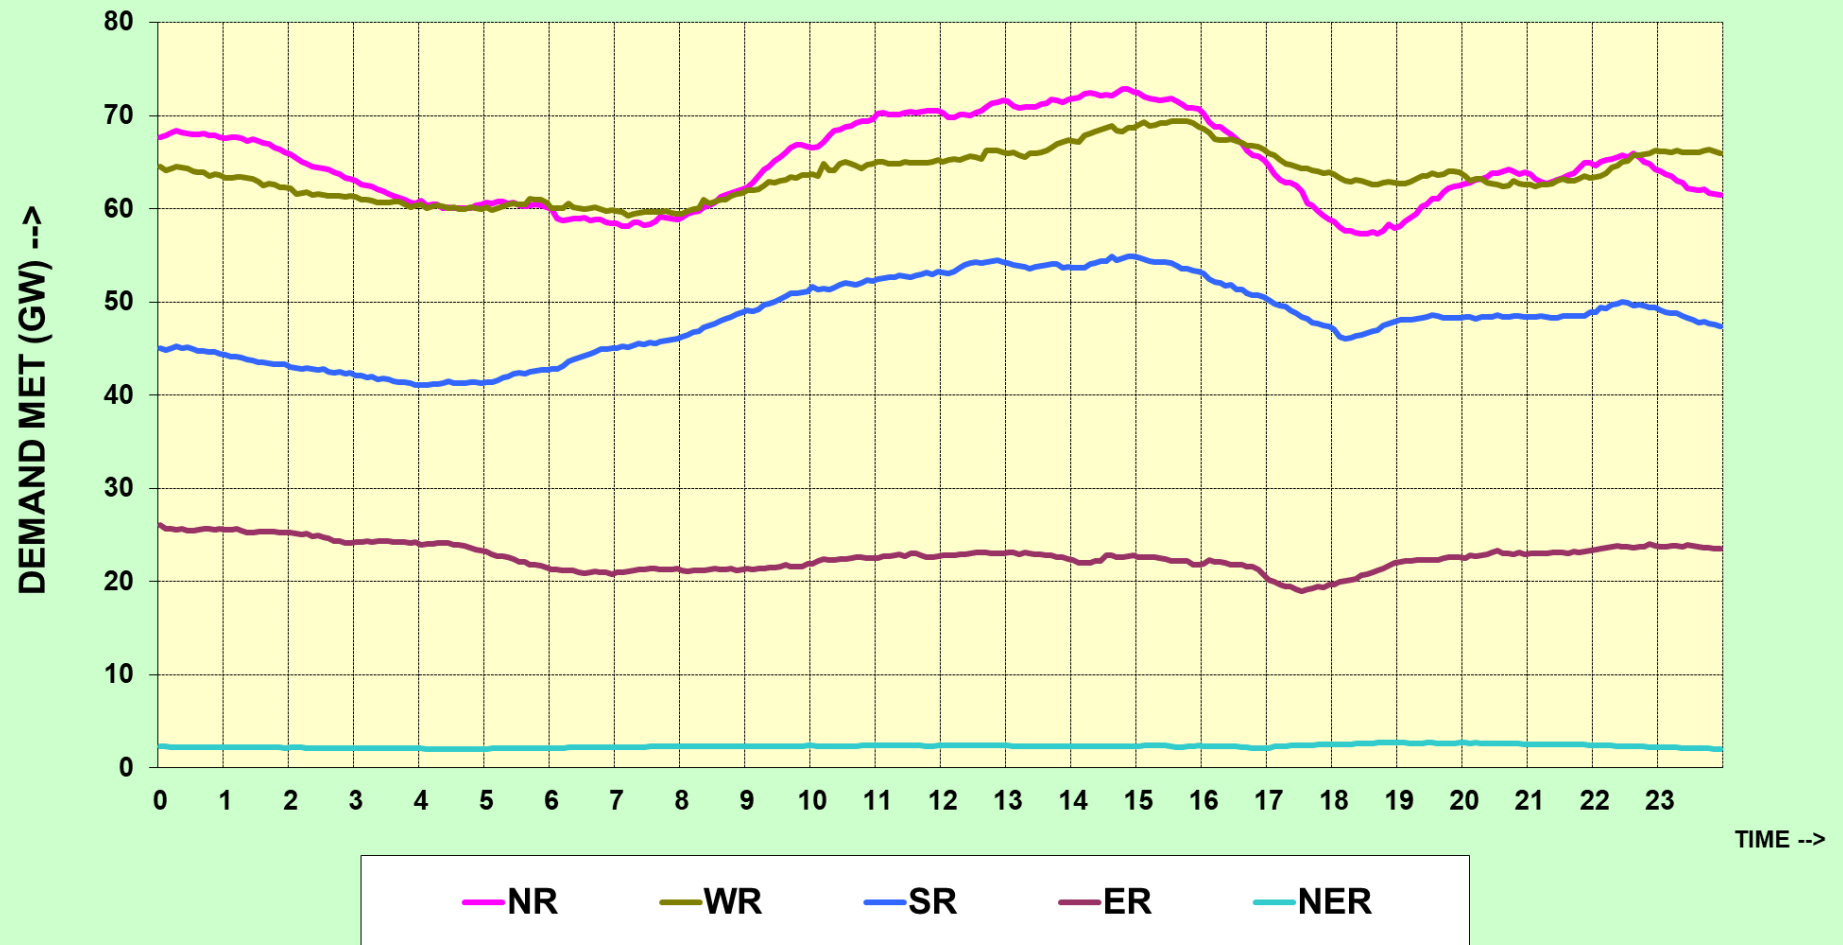

ALL INDIA GENERATION PLOT FOR 23-MAY-2023

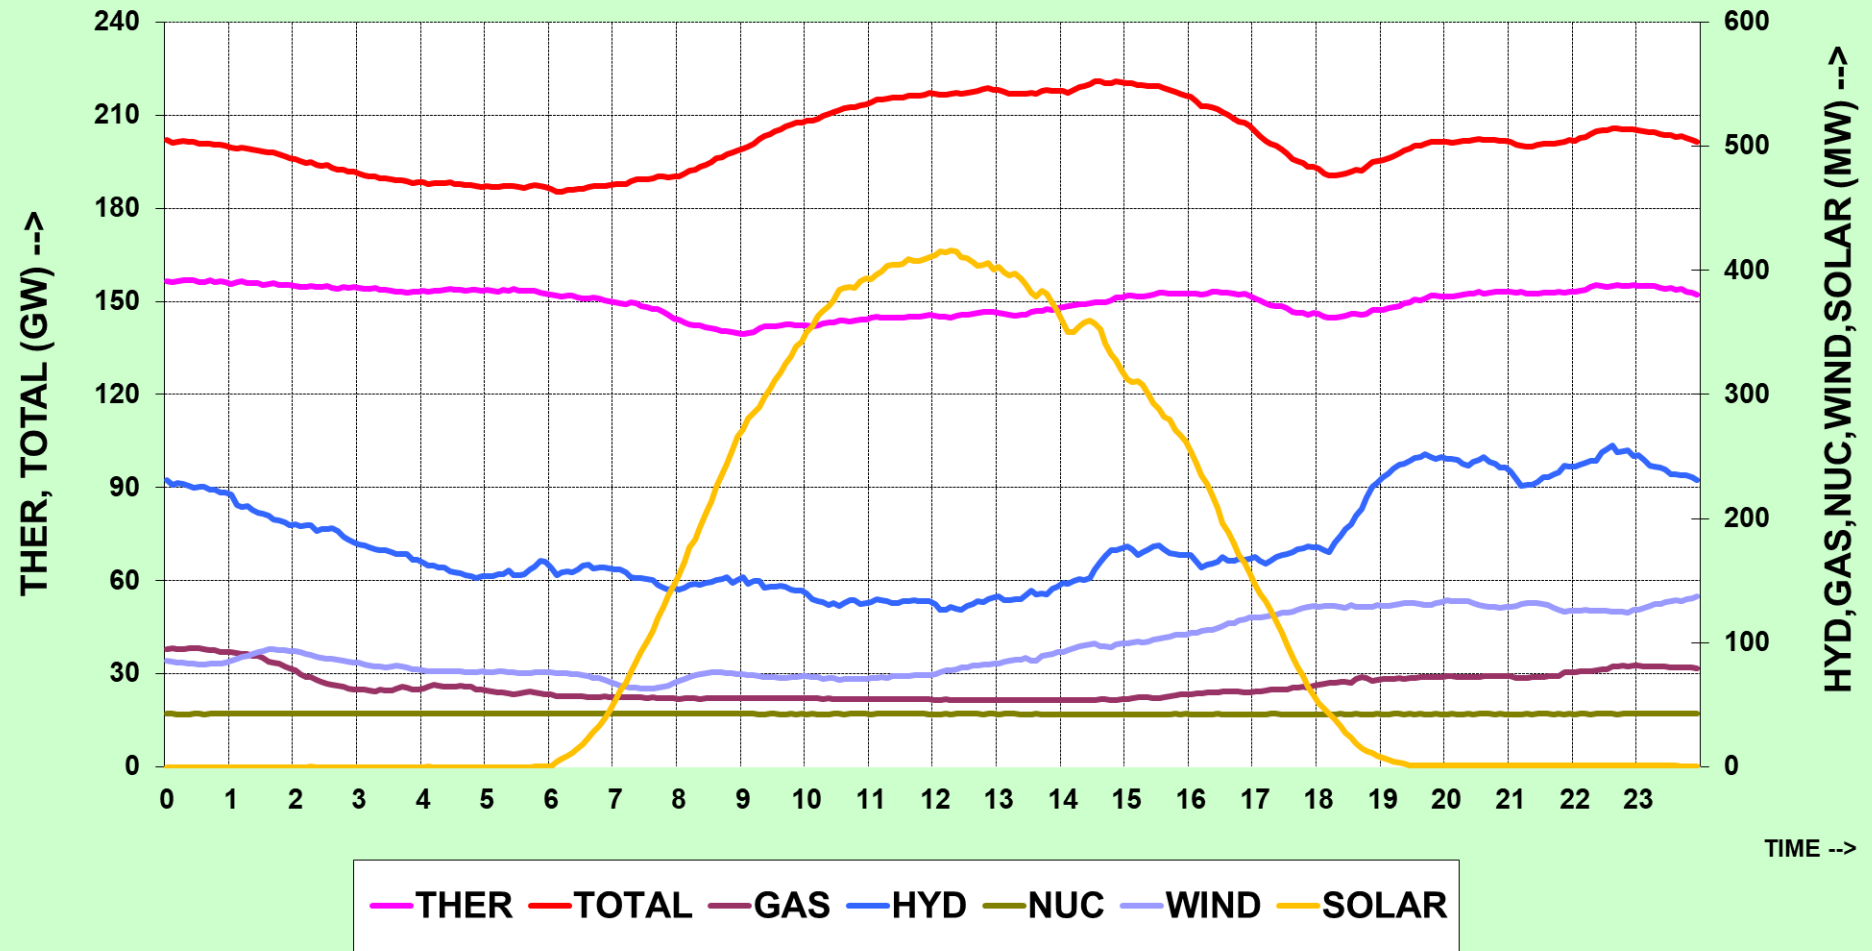

All India Fuel-wise Generation Patterns for 23-MAY-2023

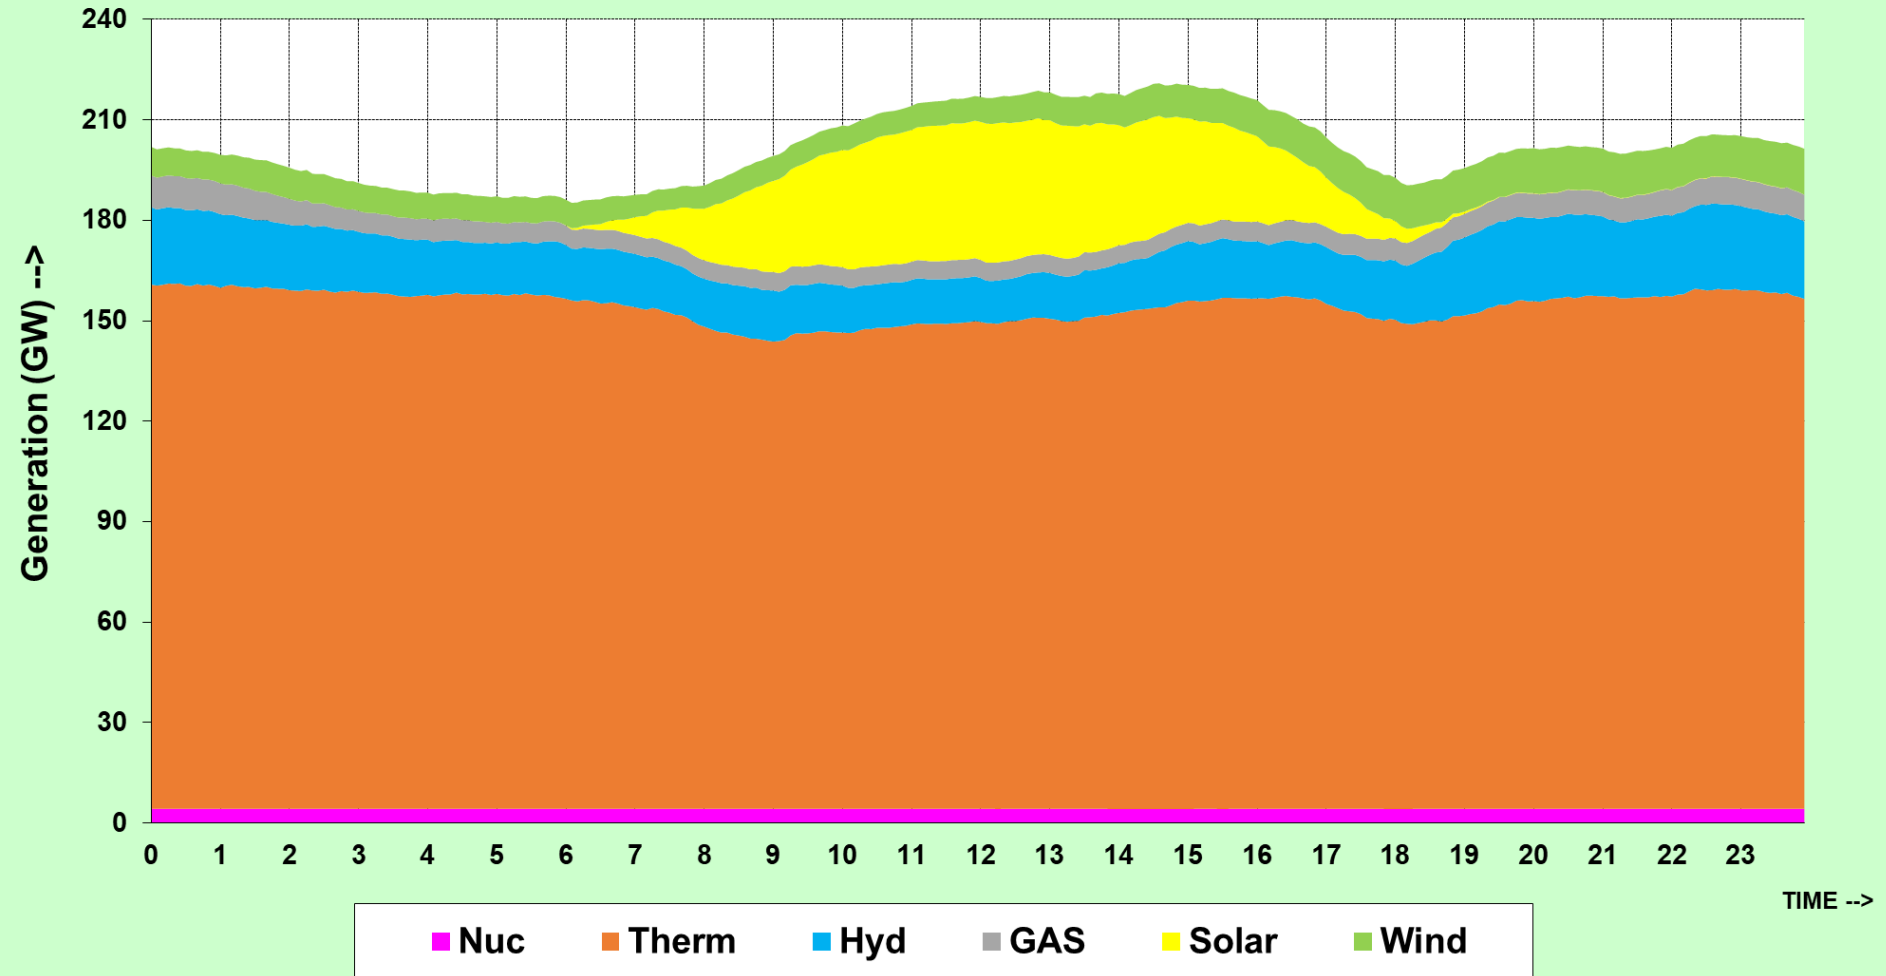

23 मई 2023 (अधिकतम माँग) की आल इंडिया माँग आपूर्ति
ALL INDIA DEMAND MET FOR 23 MAY 2023 (MAXIMUM DEMAND*)

Time (hrs)	All India Demand (MW)		Time (hrs)	All India Demand (MW)
00:05	204660		12:05	213243
00:20	205447		12:20	214774
00:35	204235		12:35	215514
00:50	203917		12:50	217322
01:05	202721		13:05	216370
01:20	201759		13:20	215792
01:35	200535		13:35	216640
01:50	199283		13:50	217224
02:05	197067		14:05	216871
02:20	195737		14:20	219271
02:35	194764		14:35	221010
02:50	193138		14:50	221347
03:05	191905		15:05	220757
03:20	190794		15:20	219883
03:35	189877		15:35	219213
03:50	188226		15:50	217469
04:05	187400		16:05	214464
04:20	187626		16:20	211604
04:35	187173		16:35	209421
04:50	187213		16:50	206410
05:05	186748		17:05	201483
05:20	187632		17:20	198329
05:35	187120		17:35	194447
05:50	187684		17:50	192358
06:05	185226		18:05	189967
06:20	186231		18:20	189676
06:35	186421		18:35	190607
06:50	186370		18:50	193294
07:05	186249		19:05	194394
07:20	186979		19:20	196970
07:35	187385		19:35	197939
07:50	187908		19:50	199977
08:05	188904		20:05	199536
08:20	191734		20:20	200125
08:35	193683		20:35	200431
08:50	195560		20:50	200408
09:05	197272		21:05	199497
09:20	200920		21:20	199496
09:35	203748		21:35	200677
09:50	205370		21:50	202528
10:05	205934		22:05	203832
10:20	208492		22:20	206099
10:35	210455		22:35	207153
10:50	211334		22:50	206439
11:05	212830		23:05	204646
11:20	212973		23:20	203113
11:35	213472		23:35	201651
11:50	213315		23:50	200774
Maximum Demand of 221347 MW met@14:50 hrs (from 1 min. interval SCADA DATA)				

* 15 minute interval SCADA DATA of instantaneous demand

11. ACTUAL POWER SUPPLY POSITION - MAY 2023

REGION	STATE	Requirement/Availability in MU/DAY			Requirement/Availability in MU				Peak Demand/Peak Met in MW			
		Requirement	Energy met	Surplus(+)/ Deficit(-)	Requirement	Energy met	Surplus(+)/ Deficit(-)	% Shortage	Requirement	Peak Demand Met	Surplus(+)/ Deficit(-)	% Shortage
NR	Chandigarh	5	5	0.0	154	154	0	0.0	321	321	0	0.0
	Delhi	101	101	0.0	3121	3120	0	0.0	6916	6916	0	0.0
	Haryana	165	164	-0.5	5113	5098	-15	-0.3	10020	10020	0	0.0
	Himachal Pradesh	29	29	-0.1	909	906	-3	-0.4	1702	1702	0	0.0
	J&K(UT) and Ladakh(UT)	55	55	-0.4	1720	1709	-12	-0.7	2823	2823	0	0.0
	Punjab	170	170	0.0	5278	5278	0	0.0	11940	11940	0	0.0
	Rajasthan	266	265	-0.7	8231	8210	-22	-0.3	16470	16470	0	0.0
	Uttar Pradesh	427	425	-1.2	13225	13187	-38	-0.3	26386	26166	-220	-0.8
	Uttarakhand	43	43	-0.1	1345	1342	-4	-0.3	2415	2415	0	0.0
	Railway	3	3	0.0	102	102	0	0.0	177	178	1	0.4
	NFL	0	0	0.0	2	2	0	0.0	19	19	0	0.0
	TOTAL	1265	1261	-3.0	39200	39106	-94	-0.2	72625	72625	0	0.0
WR	Gujarat	427	427	0.0	13231	13231	0	0.0	21340	21310	-30	-0.1
	Madhya Pradesh	239	239	0.0	7418	7418	0	0.0	12286	12286	0	0.0
	Chhattisgarh	104	104	0.0	3212	3212	0	0.0	4905	4901	-3	-0.1
	Maharashtra	570	569	-0.4	17663	17650	-13	-0.1	28160	28121	-39	-0.1
	Goa	15	15	0.0	476	475	-1	-0.2	755	755	0	0.0
	DNHDDPDCL	28	28	0.0	876	876	0	0.0	1265	1265	0	0.0
	AMNSIL	18	18	0.0	546	546	0	0.0	897	897	0	0.0
	BALCO*	12	12	0.0	384	384	0	0.0	522	522	0	0.0
	TOTAL	1413	1413	-0.5	43806	43792	-14	0.0	68767	68671	-96	-0.1
SR	Andhra Pradesh	223	222	-1.8	6926	6870	-56	-0.8	12653	12653	0	0.0
	Telangana	186	184	-2.1	5756	5691	-65	-1.1	9886	9867	-19	-0.2
	Karnataka	246	244	-2.1	7624	7559	-65	-0.9	15111	15111	0	0.0
	Kerala	92	92	-0.7	2867	2846	-21	-0.7	4862	4862	0	0.0
	Tamil Nadu	354	352	-2.7	10982	10897	-85	-0.8	18658	18658	0	0.0
	Puducherry	10	10	-0.1	318	316	-2	-0.8	512	512	0	0.0
	TOTAL	1112	1103	-9.5	34473	34179	-294	-0.9	59560	59532	-28	0.0
ER	Bihar	121	120	-1.7	3763	3710	-53	-1.4	6657	6657	0	0.0
	Jharkhand	36	34	-2.0	1106	1045	-61	-5.5	1839	1839	0	0.0
	DVC	76	76	0.0	2342	2342	0	0.0	3751	3751	0	0.0
	Odisha	120	120	0.0	3729	3729	0	0.0	6940	6940	0	0.0
	West Bengal	194	194	0.0	6005	6005	0	0.0	11105	11105	0	0.0
	Sikkim	1	1	0.0	45	45	0	0.0	104	104	0	0.0
	Railways_ER ISTS*	0	0	0.0	4	4	0	0.0	19	19	0	0.0
	TOTAL	548	545	-3.7	16996	16882	-114	-0.7	28791	27761	-1030	-3.6
NER	Arunachal Pradesh	3	3	0.0	78	78	0	0.0	165	165	0	0.0
	Assam	33	33	-0.1	1033	1029	-3	-0.3	2219	2219	0	0.0
	Manipur	2	2	0.0	73	73	0	0.0	193	193	0	0.0
	Meghalaya	6	5	-1.2	195	156	-39	-19.8	353	332	-21	-5.9
	Mizoram	2	2	0.0	54	54	0	0.0	122	122	0	0.0
	Nagaland	2	2	0.0	75	75	0	0.0	152	152	0	0.0
	Tripura	5	5	0.0	164	164	0	0.0	345	345	0	0.0
	TOTAL	54	53	-1.4	1671	1629	-42	-2.5	3477	3453	-24	-0.7
ALL INDIA		4392	4374	-18.0	136146	135587	-558	-0.4				

* BALCO has been added as new entity wef 20.12.2022

NOTE: BASED ON THE DATA FURNISHED BY ENTITIES ON DAILY BASIS

12. ENERGY COMPARISON OF MAY 2023 vs MAY 2022

REGION	STATE	Energy Requirement (MU)					Energy Met (MU)				
		May-22	May-23	Difference	% Change	Average MU/day for May-23	May-22	May-23	Difference	% Change	Average MU/day for May-23
NR	Chandigarh	183	154	-30	-16	5	183	154	-30	-16	5
	Delhi	3738	3121	-618	-17	101	3738	3120	-618	-17	101
	Haryana	5692	5113	-580	-10	165	5641	5098	-543	-10	164
	Himachal Pradesh	1004	909	-95	-9	29	1003	906	-97	-10	29
	J&K(UT) and Ladakh(UT)	1578	1720	143	9	55	1546	1709	163	11	55
	Punjab	6345	5278	-1067	-17	170	6331	5278	-1053	-17	170
	Rajasthan	9068	8231	-837	-9	266	8954	8210	-745	-8	265
	Uttar Pradesh	14175	13225	-951	-7	427	14084	13187	-897	-6	425
	Uttarakhand	1401	1345	-55	-4	43	1393	1342	-51	-4	43
	Railway/NFL	91	103	12	14	3	91	103	12	14	3
	TOTAL	43277	39200	-4077	-9	1265	42964	39106	-3858	-9	1261
WR	Gujarat	13310	13231	-79	-1	427	13310	13231	-79	-1	427
	Madhya Pradesh	8195	7418	-777	-9	239	8102	7418	-683	-8	239
	Chhattisgarh	3253	3212	-41	-1	104	3252	3212	-40	-1	104
	Maharashtra	18147	17663	-484	-3	570	18147	17650	-497	-3	569
	Goa	444	476	32	7	15	444	475	31	7	15
	DNHDDPDCL	847	876	29	3	28	847	876	29	3	28
	AMNSIL	595	546	-49	-8	18	595	546	-49	-8	18
	BALCO*		384	-	-	12		384	-	-	12
	TOTAL	44790	43806	-984	-2	1413	44696	43792	-904	-2	1413
SR	Andhra Pradesh	6062	6926	863	14	223	6062	6870	808	13	222
	Telangana	5748	5756	8	0	186	5748	5691	-57	-1	184
	Karnataka	6220	7624	1404	23	246	6219	7559	1340	22	244
	Kerala	2359	2867	508	22	92	2359	2846	487	21	92
	Tamil Nadu	10459	10982	523	5	354	10458	10897	439	4	352
	Puducherry	280	318	38	14	10	280	316	36	13	10
	TOTAL	31128	34473	3345	11	1112	31125	34179	3054	10	1103
ER	Bihar	3555	3763	208	6	121	3500	3710	210	6	120
	Jharkhand	1036	1106	70	7	36	979	1045	66	7	34
	DVC	2587	2342	-245	-9	76	2587	2342	-245	-9	76
	Odisha	3841	3729	-111	-3	120	3836	3729	-107	-3	120
	West Bengal	5368	6005	637	12	194	5354	6005	651	12	194
	Sikkim	47	45	-1	-3	1	47	45	-1	-3	1
	Railways_ER ISTS*		4	-	-	0		4	-	-	0
	TOTAL	16433	16996	563	3	548	16303	16882	578	4	545
NER	Arunachal Pradesh	78	78	0	0	3	78	78	0	0	3
	Assam	956	1033	76	8	33	956	1029	73	8	33
	Manipur	75	73	-2	-3	2	75	73	-2	-3	2
	Meghalaya	170	195	25	15	6	167	156	-11	-6	5
	Mizoram	53	54	1	3	2	53	54	1	3	2
	Nagaland	72	75	3	4	2	72	75	3	4	2
	Tripura	213	164	-49	-23	5	213	164	-49	-23	5
	TOTAL	1617	1671	54	3	54	1614	1629	15	1	53
ALL INDIA		137246	136146	-1100	-1	4392	136703	135587	-1116	-1	4374

* BALCO has been added as new entity wef 20.12.2022

13. DEMAND COMPARISON OF MAY 2023 vs MAY 2022

REGION	STATE	Peak Requirement (MW)				Peak Met (MW)			
		May-22	May-23	Difference	% Change	May-22	May-23	Difference	% Change
NR	Chandigarh	372	321	-51	-13.7	372	321	-51	-13.7
	Delhi	7070	6916	-154	-2.2	7070	6916	-154	-2.2
	Haryana	10052	10020	-32	-0.3	10052	10020	-32	-0.3
	Himachal Pradesh	1644	1702	58	3.5	1644	1702	58	3.5
	J&K(UT) and Ladakh(UT)	2825	2823	-2	-0.1	2825	2823	-2	-0.1
	Punjab	10886	11940	1054	9.7	10886	11940	1054	9.7
	Rajasthan	15949	16470	521	3.3	15898	16470	572	3.6
	Uttar Pradesh	25046	26386	1340	5.4	25046	26166	1120	4.5
	Uttarakhand	2354	2415	61	2.6	2354	2415	61	2.6
	Railway/NFL	20	196	176	869.5	20	197	177	873.3
WR	Gujarat	20769	21340	571	3	20769	21310	541	2.6
	Madhya Pradesh	12541	12286	-255	-2	12480	12286	-194	-1.6
	Chhattisgarh	4975	4905	-70	-1	4975	4901	-74	-1.5
	Maharashtra	27969	28160	192	1	27969	28121	153	0.5
	Goa	711	755	44	6	711	755	44	6.2
	DNHDDPDCL	1252	1265	13	1.0	1252	1265	13	1.0
	AMNSIL	935	897	-38	-4.1	935	897	-38	-4.1
	BALCO*		522	-	-		522	-	-
SR	Andhra Pradesh	11218	12653	1435	12.8	11218	12653	1435	12.8
	Telangana	10519	9886	-633	-6.0	10519	9867	-652	-6.2
	Karnataka	12260	15111	2851	23.3	12260	15111	2851	23.3
	Kerala	4190	4862	672	16.0	4182	4862	680	16.3
	Tamil Nadu	16906	18658	1752	10.4	16906	18658	1752	10.4
	Puducherry	482	512	30	6.2	482	512	30	6.2
ER	Bihar	6405	6657	252	3.9	6040	6657	617	10.2
	Jharkhand	1775	1839	64	3.6	1544	1839	295	19.1
	DVC	3665	3751	86	2.3	3459	3751	292	8.4
	Odisha	6267	6940	673	10.7	6267	6940	673	10.7
	West Bengal	9225	11105	1880	20.4	9215	11105	1890	20.5
	Sikkim	113	104	-9	-8.0	113	104	-9	-8.0
	Railways_ER ISTS*		19	19	-		19	19	-
NER	Arunachal Pradesh	142	165	23	16.0	137	165	28	20.2
	Assam	2146	2219	73	3.4	2082	2219	137	6.6
	Manipur	197	193	-4	-2.0	195	193	-2	-0.9
	Meghalaya	343	353	11	3.1	343	332	-10	-3.0
	Mizoram	117	122	5	4.4	117	122	5	4.4
	Nagaland	145	152	7	4.7	145	152	7	4.7
	Tripura	303	345	42	13.7	303	345	42	13.7

* BALCO has been added as new entity wef 20.12.2022

14. SCHEDULE AND DRAWAL OF CONSTITUENTS - MAY 2023

REGION	STATE	SCHEDULE (MU)	ACTUAL DRAWAL (MU)	Over drawal(+)/ Under Drawal(-) (MU)	% OD/UD	SCHEDULE (MU/DAY)	ACTUAL DRAWAL (MU/DAY)	Over drawal(+)/ Under Drawal(-) (MU/DAY)
NR	Chandigarh	155.37	157.09	1.72	1.11	5.01	5.07	0.06
	Delhi	2929.93	2865.34	-64.59	-2.20	94.51	92.43	-2.08
	Haryana	3606.09	3541.39	-64.71	-1.79	116.33	114.24	-2.09
	Himachal Pradesh	220.83	226.37	5.54	2.51	7.12	7.30	0.18
	J&K(UT) and Ladakh(UT)	1106.43	1087.35	-19.08	-1.72	35.69	35.08	-0.62
	Punjab	2354.42	2281.58	-72.84	-3.09	75.95	73.60	-2.35
	Rajasthan	2167.33	2025.32	-142.01	-6.55	69.91	65.33	-4.58
	Uttar Pradesh	5601.10	5600.70	-0.40	-0.01	180.68	180.67	-0.01
	Uttarakhand	770.41	758.22	-12.19	-1.58	24.85	24.46	-0.39
	Railway	99.83	101.50	1.67	1.67	3.22	3.27	0.05
	NFL	2.17	1.85	-0.32	-14.84	0.07	0.06	-0.01
	Total	19013.91	18646.70	-367.21	-1.93	613.35	601.51	-11.85
WR	Gujarat	5917.16	5895.13	-22.03	-0.37	190.88	190.17	-0.71
	Madhya Pradesh	4040.00	3937.53	-102.47	-2.54	130.32	127.02	-3.31
	Chhattisgarh	1353.46	1307.85	-45.61	-3.37	43.66	42.19	-1.47
	Maharashtra	6523.73	6514.04	-9.69	-0.15	210.44	210.13	-0.31
	Goa	468.53	463.76	-4.77	-1.02	15.11	14.96	-0.15
	DNHDDPDCL	888.82	875.85	-12.97	-1.46	28.67	28.25	-0.42
	AMNSIL	299.38	299.29	-0.09	-0.03	9.66	9.65	0.00
	BALCO*	385.55	383.97	-1.58	-0.41	12.44	12.39	-0.05
	Total	19876.63	19677.41	-199.22	-1.00	641.18	634.76	-6.43
SR	Andhra Pradesh	2288.51	2306.48	17.97	0.79	73.82	74.40	0.58
	Telangana	1767.89	1771.42	3.53	0.20	57.03	57.14	0.11
	Karnataka	2579.33	2574.92	-4.41	-0.17	83.20	83.06	-0.14
	Kerala	2067.08	2067.86	0.78	0.04	66.68	66.71	0.03
	Tamil Nadu	6206.66	6185.22	-21.44	-0.35	200.21	199.52	-0.69
	Puducherry	304.53	294.40	-10.13	-3.33	9.82	9.50	-0.33
	Goa (SR)	69.93	71.39	1.46	2.09	2.26	2.30	0.05
	Total	15283.93	15271.69	-12.24	-0.08	493.03	492.64	-0.39
ER	Bihar	3451.53	3406.17	-45.36	-1.31	111.34	109.88	-1.46
	Jharkhand	864.93	866.68	1.75	0.20	27.90	27.96	0.06
	DVC	-1302.77	-1291.61	11.16	-0.86	-42.02	-41.66	0.36
	Odisha	1539.64	1519.92	-19.72	-1.28	49.67	49.03	-0.64
	West Bengal	2072.67	1972.11	-100.56	-4.85	66.86	63.62	-3.24
	Sikkim	40.44	42.46	2.02	5.00	1.30	1.37	0.07
	Railways_ER ISTS*	6.29	2.37	-3.92	-62.33	0.20	0.08	-0.13
	Total	6672.73	6518.09	-154.64	-2.32	215.25	210.26	-4.99
NER	Arunachal Pradesh	81.85	75.33	-6.52	-7.97	2.64	2.43	-0.21
	Assam	826.46	833.88	7.42	0.90	26.66	26.90	0.24
	Manipur	76.49	73.03	-3.47	-4.53	2.47	2.36	-0.11
	Meghalaya	107.21	108.59	1.38	1.29	3.46	3.50	0.04
	Mizoram	55.03	50.10	-4.94	-8.97	1.78	1.62	-0.16
	Nagaland	74.92	71.34	-3.58	-4.77	2.42	2.30	-0.12
	Tripura	166.24	176.01	9.78	5.88	5.36	5.68	0.32
	Total	1388.20	1388.28	0.08	0.01	44.78	44.78	0.00
All India Total		62235.40	61502.18	-733.22	-1.18	2007.59	1983.94	-23.65

* BALCO has been added as new entity wef 20.12.2022

15. INTER REGIONAL EXCHANGES 2023-24

(All figures in MU)

	Apr'23	May'23	Fin. Year 2023-24
Name of Line			
Import of NR from WR (WR-NR)			
WR - NR 765 kV Gwalior - Agra 2xS/C	635.95	996.71	1632.66
WR-NR 765 kV Gwalior - Phagi 2xS/C	553.05	453.93	1006.98
WR-NR 765 kV Jabalpur-Orai D/C	430.29	804.53	1234.82
WR-NR 765 kV Satna-Orai	505.37	598.85	1104.22
WR-NR 765 kV Gwalior-Orai	0.00	0.00	0.00
WR - NR HVDC Champa - Kurukshetra	804.26	1126.68	1930.94
WR - NR HVDC Vindhyachal	0.49	3.23	3.72
WR - NR 400 kV Zerda Kankroli	0.00	0.00	0.00
WR - NR 400 kV Zerda Bhinmal	0.00	0.00	0.00
WR - NR 400 kV RAPP C - Shujalpur D/C	2.28	31.04	33.32
WR - NR 220 kV Bhanpura - Ranpur	9.67	65.53	75.20
WR - NR 220 kV Bhanpura - Modak	0.00	0.00	0.00
WR - NR 220 kV Auraiya - Malanpur/Mehgaon	0.00	0.15	0.15
WR - NR 400 kV Vindhyachal-Rihand D/C	0.00	0.00	0.00
WR - NR HVDC Mundra - Mohindergarh	132.55	340.75	473.30
WR-NR 765 kV Banaskata-Chittorgarh D/C	0.00	3.26	3.26
WR-NR 765 kV Varanasi-Vindhyachal	1030.05	1663.34	2693.39
Total WR - NR	4103.96	6088.00	10191.96
Export of NR to WR (NR-WR)			
NR - WR 765 kV Gwalior - Agra 2xS/C	0.00	0.00	0.00
NR - WR 765 kV Gwalior - Phagi 2xS/C	0.00	5.41	5.41
NR - WR 765 kV Jabalpur-Orai D/C	0.00	0.00	0.00
NR - WR 765 kV Satna-Orai	0.00	0.00	0.00
NR - WR 765 kV Gwalior-Orai	440.87	385.11	825.98
NR - WR HVDC Champa- Kurukshetra	0.00	0.00	0.00
NR - WR HVDC Vindhyachal	289.83	273.88	563.71
NR - WR 400 kV Zerda Kankroli	185.75	94.43	280.18
NR - WR 400 kV Zerda Bhinmal	282.42	181.64	464.06
NR - WR 400 kV RAPP C - Shujalpur D/C	85.74	45.64	131.38
NR - WR 220 kV Bhanpura - Ranpur	0.00	0.00	0.00
NR - WR 220 kV Bhanpura - Modak	0.00	0.00	0.00
NR - WR 220 kV Auraiya - Malanpur/Mehgaon	56.56	28.58	85.14
NR-WR 400 kV Rihand-Vindhyachal D/C	644.30	672.49	1316.79
NR - WR HVDC Mundra - Mohindergarh	243.86	54.36	298.22
NR - WR 765 kV Banaskata-Chittorgarh D/C	976.83	428.19	1405.02
NR-WR 765 kV Varanasi-Vindhyachal	0.00	0.00	0.00
Total NR - WR	3206.16	2169.73	5375.89

	Apr'23	May'23	Fin. Year 2023-24
Name of Line			
Import of NR from ER (ER-NR)			
ER - NR 765 kV Sasaram - Fatehpur	166.02	114.36	280.38
ER - NR 765 kV Gaya - Varanasi 2*S/C	224.56	107.46	332.02
ER - NR 765 kV Gaya - Balia	246.38	335.46	581.84
ER - NR HVDC Alipurduar - Agra	0.00	0.00	0.00
ER-NR 400 kV Patna - Balia D/C	219.16	246.32	465.48
ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	127.03	223.63	350.66
ER - NR 400 kV Biharshariff - Balia D/C	22.11	72.32	94.43
ER - NR 400 kV Motihari - Gorakhpur D/C	156.88	188.70	345.58
ER - NR 400 kV Biharshariff - Varanasi D/C	67.56	47.21	114.77
ER - NR 400 kV Sasaram -Varanasi	74.99	38.68	113.67
ER - NR 400 kV Sasaram -Allahabad	51.91	33.39	85.30
ER - NR 220 kV Sahupuri-Karamnasa	78.64	82.22	160.86
ER - NR 132 kV Sahupuri - Karamnasa	1.92	0.00	1.92
ER - NR 132 kV 132 kV Rihand - Nagar Untari	0.00	0.00	0.00
ER - NR 132 kV Rihand - Garhwa	0.46	0.00	0.46
ER-NR 400 kV Naubatpur - Balia D/C	211.13	243.59	454.72
Total ER-NR	1648.75	1733.34	3382.09
Import of NR from NER (NER-NR)			
NER-NR HVDC Biswanath Chariali - Agra	0.00	0.00	0.00
Total NER - NR	0.00	0.00	0.00
Export of NR to ER (NR-ER)			
NR - ER 765 kV Sasaram - Fatehpur	0.00	2.65	2.65
NR - ER 765 kV Gaya - Varanasi 2*S/C	0.30	38.74	39.04
NR - ER 765 kV Gaya - Balia	0.00	0.00	0.00
NR - ER HVDC Alipurduar - Agra	0.00	0.00	0.00
NR - ER 400 kV Patna - Balia 2xD/C	0.00	0.00	0.00
NR - ER 400 kV Muzaffarpur - Gorakhpur D/C	3.47	0.00	3.47
NR - ER 400 kV Biharshariff - Balia D/C	17.15	4.18	21.33
ER - NR 400 kV Motihari - Gorakhpur D/C	0.00	0.00	0.00
NR - ER 400 kV Biharshariff - Varanasi D/C	2.90	7.31	10.21
NR - ER 400 kV Sasaram -Varanasi	0.00	0.00	0.00
NR - ER 400 kV Sasaram -Allahabad	2.25	0.00	2.25
NR - ER 220 kV Sahupuri-Karamnasa	0.00	0.00	0.00
NR - ER 132 kV Sahupuri - Karamnasa	0.01	0.96	0.97
NR - ER 132 kV 132 kV Rihand - Nagar Untari	1.74	2.20	3.94
ER - NR 132 kV Rihand - Garhwa	10.23	8.48	18.71
NR-ER 400 kV Balia- Naubatpur D/C	0.00	0.00	0.00
Total NR - ER	38.05	64.52	102.57
Export of NR to NER (NER-NR)			
NR-NER HVDC Biswanath Chariali - Agra	261.93	291.71	553.64
Total NR - NER	261.93	291.71	553.64

	Apr'23	May'23	Fin. Year 2023-24
Name of Line			
Export of WR to ER (WR-ER)			
WR - ER 765 kV Ranchi - Dharamjaygarh 2xS/C	139.81	504.96	644.77
WR - ER 765 kV Dharamjaygarh - Jharsuguda 2xD/C	652.31	469.82	1122.13
WR - ER 765 kV Durg - Jharsuguda D/C	0.00	0.64	0.64
WR - ER 400 kV Sipat - Ranchi D/C	15.97	93.84	109.81
WR - ER 400 kV Raigarh - Jharsuguda 2xD/C	0.44	6.23	6.67
WR - ER 220 kV Korba - Budhipadar D/C	36.08	80.04	116.12
WR - ER 220 kV Raigarh - Budhipadar	0.15	0.57	0.72
Total WR - ER	844.75	1156.11	2000.86
Import of WR from ER (ER - WR)			
ER - WR 765 kV Ranchi - Dharamjaygarh 2xS/C	144.10	11.95	156.05
ER - WR 765 kV Dharamjaygarh - Jharsuguda 2XD/C	25.46	58.29	83.76
ER - WR 765 kV Durg - Jharsuguda D/C	394.08	204.42	598.50
ER - WR 400 kV Sipat - Ranchi D/C	55.56	5.71	61.27
ER - WR 400 kV Raigarh - Jharsuguda 2xD/C	248.78	148.94	397.71
ER - WR 220 kV Korba - Budhipadar D/C	1.45	0.00	1.45
ER - WR 220 kV Raigarh - Budhipadar	55.98	38.46	94.44
Total ER - WR	925.41	467.76	1393.18
Export of ER to NER (ER - NER)			
ER - NER 400 kV Binaguri - Bongaigaon D/C	6.99	16.15	23.14
ER - NER 400 kV Alipurduar - Bongaigaon D/C	4.62	34.31	38.93
ER - NER 220 kV Birpara - Salakati D/C	0.54	3.12	3.66
Total ER - NER	12.16	53.58	65.73
Import of ER from NER (NER - ER)			
NER - ER 400 kV Binaguri - Bongaigaon D/C	52.83	40.19	93.02
NER - ER 400 kV Alipurduar - Bongaigaon D/C	182.37	135.22	317.58
NER - ER 220 kV Birpara - Salakati D/C	34.59	31.32	65.90
Total NER - ER	269.78	206.73	476.51
Export of ER to SR (ER - SR)			
ER - SR HVDC Gazuwaka	375.93	395.23	771.16
ER - SR HVDC Talchar - Kolar	1233.20	1204.28	2437.48
ER - SR 765 kV Angul- Srikakulam D/C	1683.42	1561.33	3244.75
Total ER - SR	3292.55	3160.85	6453.40
Import of ER from SR (SR - ER)			
SR - ER HVDC Gazuwaka	0.00	0.00	0.00
SR - ER HVDC Talchar - Kolar	0.00	0.00	0.00
SR - ER 765 kV Angul- Srikakulam D/C	0.00	0.00	0.00
Total SR - ER	0.00	0.00	0.00

	Apr'23	May'23	Fin. Year 2023-24
Name of Line			
Export of WR to SR (WR-SR)			
WR - SR HVDC Bhadrawati	544.41	411.52	955.94
WR - SR 765 kV Sholapur - Raichur 2xS/C	417.69	222.76	640.45
WR - SR 765 kV Wardha - Nizamabad D/C	1323.51	873.44	2196.95
WR - SR 400KV Kolhapur-Kudgi D/C	0.00	0.00	0.00
WR-SR HVDC Raigarh-Pugalur	3004.35	1791.86	4796.20
WR-SR 220kV Xeldem - Ambewadi S/C	77.16	70.18	147.34
WR-SR 220kV Ponda - Ambewadi S/C	0.29	1.54	1.83
Total WR - SR	5367.41	3371.30	8738.71
Import of WR from SR (SR - WR)			
SR - WR HVDC Bhadrawati	4.11	25.09	29.21
SR - WR 765 kV Raichur - Sholapur 2xS/C	29.13	205.27	234.40
SR - WR 765 kV Wardha - Nizamabad D/C	0.00	3.90	3.90
SR - WR 400KV Kolhapur-Kudgi D/C	623.59	719.30	1342.89
SR-WR HVDC Pugalur-Raigarh	0.00	3.73	3.73
WR-SR 220kV Ambewadi - Xeldem S/C	0.00	0.00	0.00
WR-SR 220kV Ambewadi-Ponda S/C	0.00	0.00	0.00
Total SR - WR	656.84	957.30	1614.13
TOTAL ALL INDIA	20628	19721	40349

*In case of mutiple ckt / DC pole year corres. to the commissioning of final element

Date	15.1 Import-Export of NR with WR during May 2023																	
	Import of NR from WR (WR-NR)																	
	WR - NR 765 kV Gwalior - Agra 2x5/C	WR-NR 765 kV Gwalior-Phagi 2x5/C	WR-NR 765 kV Jabalpur- Orai D/C	WR-NR 765 kV Satna- Orai	WR-NR 765 kV Gwalior-Orai	WR - NR HVDC Champa- Kurukshetra	WR - NR HVDC Vindhyachal	WR - NR 400 kV Zerda- Kankroli	WR - NR 400 kV Zerda- Bhinmal	WR-NR 400 kV RAPP C - Shujalpur D/C	WR - NR 220 kV Bhanpura - Ranpur	WR - NR 220 kV Bhanpura - Modak	WR - NR 220 kV Auraiya - Malanpur / Mehgaon	WR-NR 400 kV Rihand Vindhyachal D/C	WR - NR HVDC Mundra - M'garh	WR -NR 765 kV Banaskata - Chittorgarh D/C	WR-NR 765 kV Varanasi- Vindhyachal	Total WR - NR
1-May-23	37.68	18.41	24.57	18.24	0.00	23.21	0.00	0.00	0.00	0.74	1.59		0.00	0.00	0.00	0.00	42.46	166.90
2-May-23	36.83	20.89	23.30	19.07	0.00	24.30	0.00	0.00	0.00	0.28	1.68		0.00	0.00	0.00	0.00	44.69	171.04
3-May-23	33.35	18.36	23.06	18.21	0.00	23.32	0.00	0.00	0.00	0.00	1.70		0.00	0.00	0.00	0.00	48.18	166.18
4-May-23	31.70	22.08	22.46	17.60	0.00	23.16	0.00	0.00	0.00	0.69	1.78		0.00	0.00	0.00	0.00	43.01	162.48
5-May-23	32.40	21.30	22.04	17.84	0.00	23.39	0.00	0.00	0.00	0.95	2.01		0.00	0.00	0.00	0.00	51.58	171.51
6-May-23	38.98	23.95	28.14	18.85	0.00	14.27	0.00	0.00	0.00	2.66	2.07		0.00	0.00	0.00	0.00	53.63	182.55
7-May-23	29.78	14.54	19.52	16.69	0.00	28.69	0.00	0.00	0.00	0.00	2.16		0.00	0.00	0.00	0.00	55.08	166.46
8-May-23	34.24	15.24	25.02	19.88	0.00	37.34	0.00	0.00	0.00	0.00	2.39		0.00	0.00	0.00	0.00	56.23	190.34
9-May-23	37.29	20.80	32.40	21.27	0.00	48.26	0.53	0.00	0.00	2.97	2.30		0.00	0.00	7.35	0.00	55.89	229.06
10-May-23	33.79	20.27	33.93	20.66	0.00	46.89	2.24	0.00	0.00	1.56	2.20		0.00	0.00	7.45	0.00	54.90	223.89
11-May-23	32.72	18.28	29.83	19.84	0.00	46.50	0.00	0.00	0.00	1.92	2.17		0.00	0.00	16.94	0.00	56.47	224.67
12-May-23	35.36	18.29	34.61	22.17	0.00	66.61	0.00	0.00	0.00	2.64	2.64		0.00	0.00	24.21	0.00	64.23	270.76
13-May-23	46.03	25.55	42.26	22.78	0.00	18.41	0.00	0.00	0.00	6.41	2.62		0.00	0.00	33.34	0.00	62.07	259.47
14-May-23	45.89	20.17	45.36	21.62	0.00	0.67	0.00	0.00	0.00	5.08	2.71		0.15	0.00	17.06	3.26	67.62	229.59
15-May-23	34.30	11.70	29.37	20.53	0.00	35.55	0.00	0.00	0.00	0.00	2.55		0.00	0.00	18.14	0.00	55.25	207.39
16-May-23	27.77	8.13	22.66	19.58	0.00	64.89	0.00	0.00	0.00	0.00	2.59		0.00	0.00	14.72	0.00	51.31	211.65
17-May-23	25.46	8.89	19.66	18.97	0.00	77.28	0.00	0.00	0.00	0.00	2.76		0.00	0.00	19.40	0.00	46.07	218.49
18-May-23	20.89	12.46	16.52	17.65	0.00	14.55	0.00	0.00	0.00	0.00	2.43		0.00	0.00	19.40	0.00	46.27	150.17
19-May-23	33.58	24.00	36.28	20.64	0.00	17.11	0.00	0.00	0.00	2.25	2.26		0.00	0.00	19.40	0.00	57.57	213.09
20-May-23	33.34	19.21	33.30	21.57	0.00	18.59	0.00	0.00	0.00	1.35	2.36		0.00	0.00	19.40	0.00	56.07	205.19
21-May-23	35.42	15.37	33.14	19.90	0.00	34.84	0.00	0.00	0.00	1.33	2.10		0.00	0.00	12.31	0.00	64.91	219.32
22-May-23	33.54	14.25	31.27	20.26	0.00	61.02	0.00	0.00	0.00	0.15	2.34		0.00	0.00	7.35	0.00	60.24	230.42
23-May-23	32.74	12.83	27.62	20.81	0.00	90.42	0.00	0.00	0.00	0.00	2.33		0.00	0.00	7.35	0.00	56.53	250.63
24-May-23	23.45	3.40	19.37	18.68	0.00	58.50	0.46	0.00	0.00	0.00	2.22		0.00	0.00	7.34	0.00	60.24	193.66
25-May-23	23.27	0.00	17.07	16.59	0.00	20.86	0.00	0.00	0.00	0.00	1.91		0.00	0.00	10.32	0.00	57.90	147.92
26-May-23	30.69	0.00	15.39	15.78	0.00	23.74	0.00	0.00	0.00	0.00	1.80		0.00	0.00	11.20	0.00	45.91	144.51
27-May-23	24.96	4.41	15.33	18.13	0.00	28.53	0.00	0.00	0.00	0.00	0.73		0.00	0.00	12.84	0.00	41.60	146.53
28-May-23	36.76	13.00	26.84	20.32	0.00	31.18	0.00	0.00	0.00	0.06	1.90		0.00	0.00	15.69	0.00	45.84	191.59
29-May-23	32.01	15.10	20.21	19.41	0.00	45.10	0.00	0.00	0.00	0.00	1.79		0.00	0.00	6.66	0.00	51.30	191.58
30-May-23	21.74	9.40	21.60	18.91	0.00	43.40	0.00	0.00	0.00	0.00	1.75		0.00	0.00	17.41	0.00	49.44	183.65
31-May-23	20.75	3.65	12.40	16.40	0.00	36.10	0.00	0.00	0.00	0.00	1.69		0.00	0.00	15.47	0.00	60.85	167.31
Total	996.71	453.93	804.53	598.85	0.00	1126.68	3.23	0.00	0.00	31.04	65.53	0.00	0.15	0.00	340.75	3.26	1663.34	6088.00
Disclaimer:- Blank entry if the line under outage/shutdown on corrsponding day																		

Date	15.1 Import-Export of NR with WR during May 2023																	
	Export of NR to WR (NR- WR)																	
	NR - WR 765 kV Gwalior - Agra 2x5/C	NR-WR 765 kV Gwalior-Phagi 2x5/C	NR-WR 765 kV Jabalpur- Orai D/C	NR-WR 765 kV Satna- Orai	NR-WR 765 kV Gwalior-Orai	NR - WR HVDC Champa- Kurukshetra	NR - WR HVDC Vindhyachal	NR - WR 400 kV Zerda- Kankrol	NR - WR 400 kV Zerda- Bhinmal	NR-WR 400 kV RAPP C - Shujalpur D/C	WR - NR 220 kV Bhanpura - Ranpur	WR - NR 220 kV Bhanpura - Modak	NR - WR 220 kV Auraiya - Malanpur / Mehgaon	NR-WR 400 kV Rihand- Vindhyachal D/C	NR - WR HVDC Mundra - M'garh	NR - WR 765 kV Banaskata - Chittorgarh D/C	NR-WR 765 kV Varanasi- Vindhyachal	Total NR - WR
1-May-23	0.00	0.00	0.00	0.00	14.68	0.00	12.17	4.69	6.41	0.00	0.00		0.31	18.47	7.19	23.63	0.00	87.55
2-May-23	0.00	0.00	0.00	0.00	15.12	0.00	9.34	4.11	7.07	0.00	0.00		0.38	21.12	7.14	21.62	0.00	85.90
3-May-23	0.00	0.00	0.00	0.00	14.55	0.00	6.08	4.65	6.91	0.74	0.00		0.38	22.19	7.19	21.06	0.00	83.75
4-May-23	0.00	0.00	0.00	0.00	15.22	0.00	6.11	4.53	6.52	0.00	0.00		0.70	21.88	7.20	22.77	0.00	84.93
5-May-23	0.00	0.00	0.00	0.00	16.63	0.00	6.10	4.08	6.01	0.00	0.00		0.63	22.17	7.23	21.01	0.00	83.86
6-May-23	0.00	0.00	0.00	0.00	18.01	0.00	6.08	3.11	4.30	0.00	0.00		0.36	22.06	7.22	14.82	0.00	75.96
7-May-23	0.00	0.00	0.00	0.00	15.39	0.00	6.09	4.17	6.61	1.71	0.00		0.97	21.43	7.24	19.67	0.00	83.28
8-May-23	0.00	0.00	0.00	0.00	13.48	0.00	6.11	3.29	5.08	0.02	0.00		0.61	22.08	3.95	14.55	0.00	69.17
9-May-23	0.00	0.00	0.00	0.00	11.80	0.00	5.12	2.58	3.26	0.00	0.00		0.64	21.97	0.00	13.14	0.00	58.51
10-May-23	0.00	0.00	0.00	0.00	12.80	0.00	1.37	2.60	3.57	0.00	0.00		0.82	22.10	0.00	14.41	0.00	57.67
11-May-23	0.00	0.00	0.00	0.00	11.74	0.00	3.93	1.80	2.20	0.00	0.00		0.59	21.80	0.00	9.79	0.00	51.85
12-May-23	0.00	0.00	0.00	0.00	12.65	0.00	6.10	1.43	3.10	0.00	0.00		0.69	22.08	0.00	4.20	0.00	50.25
13-May-23	0.00	0.00	0.00	0.00	13.04	0.00	6.10	1.55	3.55	0.00	0.00		0.15	22.23	0.00	3.76	0.00	50.38
14-May-23	0.00	0.00	0.00	0.00	10.79	0.00	2.94	0.32	1.87	0.00	0.00		0.00	20.87	0.00	0.00	0.00	36.79
15-May-23	0.00	0.00	0.00	0.00	8.69	0.00	6.52	2.69	8.71	1.50	0.00		0.41	21.16	0.00	3.95	0.00	53.63
16-May-23	0.00	0.00	0.00	0.00	8.69	0.00	12.17	2.50	6.04	2.75	0.00		1.29	22.11	0.00	7.55	0.00	63.10
17-May-23	0.00	0.00	0.00	0.00	9.26	0.00	12.11	2.81	6.26	2.45	0.00		1.60	22.06	0.00	9.97	0.00	66.52
18-May-23	0.00	0.00	0.00	0.00	11.54	0.00	12.18	2.72	2.93	2.39	0.00		2.67	22.20	0.00	16.58	0.00	73.21
19-May-23	0.00	0.00	0.00	0.00	13.93	0.00	12.20	2.53	3.02	0.00	0.00		1.94	21.98	0.00	15.33	0.00	70.93
20-May-23	0.00	0.00	0.00	0.00	12.61	0.00	12.14	2.53	5.74	0.00	0.00		1.84	22.02	0.00	12.63	0.00	69.51
21-May-23	0.00	0.00	0.00	0.00	11.14	0.00	12.13	2.97	7.85	0.00	0.00		0.56	22.40	0.00	12.06	0.00	69.11
22-May-23	0.00	0.00	0.00	0.00	10.48	0.00	12.16	2.01	5.77	0.00	0.00		1.39	22.03	0.00	7.09	0.00	60.93
23-May-23	0.00	0.00	0.00	0.00	10.22	0.00	12.18	0.29	2.15	0.96	0.00		1.84	21.78	0.00	4.78	0.00	54.20
24-May-23	0.00	0.00	0.00	0.00	8.78	0.00	6.64	2.13	4.90	3.91	0.00		2.01	22.01	0.00	8.74	0.00	59.12
25-May-23	0.00	1.66	0.00	0.00	9.18	0.00	11.58	3.76	10.01	7.01	0.00		1.04	21.86	0.00	11.39	0.00	77.49
26-May-23	0.00	3.75	0.00	0.00	10.61	0.00	9.74	3.75	8.92	4.40	0.00		0.36	19.11	0.00	11.59	0.00	72.23
27-May-23	0.00	0.00	0.00	0.00	12.29	0.00	9.86	1.25	5.67	2.76	0.00		0.76	20.42	0.00	9.97	0.00	62.98
28-May-23	0.00	0.00	0.00	0.00	15.45	0.00	12.14	2.55	5.74	0.00	0.00		0.07	22.53	0.00	7.15	0.00	65.63
29-May-23	0.00	0.00	0.00	0.00	14.70	0.00	12.18	5.59	11.71	3.99	0.00		0.79	22.27	0.00	25.92	0.00	97.15
30-May-23	0.00	0.00	0.00	0.00	10.07	0.00	12.15	5.40	10.01	4.39	0.00		0.85	22.16	0.00	27.41	0.00	92.44
31-May-23	0.00	0.00	0.00	0.00	11.57	0.00	12.16	6.04	9.75	6.66	0.00		1.93	21.94	0.00	31.65	0.00	101.70
Total	0.00	5.41	0.00	0.00	385.11	0.00	273.88	94.43	181.64	45.64	0.00	0.00	28.58	672.49	54.36	428.19	0.00	2169.73
Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day																		

Date	15.2 Import-Export of NR with ER & NER during May 2023																		
	Import of NR from ER (ER-NR)																	Import of NR from NER (NER-NR)	
	ER - NR 765 kV Sasaram - Fatehpur	ER - NR 765 kV Gaya - Varanasi 2*5/C	ER - NR 765 kV Gaya Ballia	ER - NR HVDC Alipurduar - Agra	ER-NR 400 kV Patna - Ballia D/C	ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	ER - NR 400 kV Biharsharif - Ballia D/C	ER - NR 400 kV Motihari - Gorakhpur D/C	ER - NR 400 kV Biharsharif - Varanasi D/C	ER-NR 400 kV Sasaram - Varanasi	ER-NR 400 kV Sasaram - Allahabad	ER - NR 220 kV Sahupuri - Karamnasa	ER - NR 132 kV Sahupuri - Karamnasa	ER - NR 132 kV Rihand - Nagar Untari	NR - ER 132 kV Rihand - Garhwa	ER-NR 400 kV Naubatpur - Ballia D/C	Total ER - NR	NER-NR HVDC Biswanath Chariali - Agra	Total NER-NR
1-May-23	5.19	8.16	9.79		10.15	12.83	3.26	8.14	2.45	0.38	1.97	2.40			0.00	8.34	73.06	0.00	0.00
2-May-23	5.81	6.71	9.10		5.41	9.46	0.72	6.81	2.74	0.44	1.92	2.04			0.00	5.37	56.53	0.00	0.00
3-May-23	5.13	5.36	10.71		6.02	7.33	0.87	5.34	2.29	0.73	1.51	2.27	0.00		0.00	5.88	53.44	0.00	0.00
4-May-23	4.90	6.01	9.86		7.31	6.58	0.54	7.18	2.17	0.83	1.44	2.14		0.00		7.37	56.33	0.00	0.00
5-May-23	5.82	6.60	10.64		9.10	7.82	1.36	9.02	2.70	1.08	1.20	2.20		0.00		9.31	66.85	0.00	0.00
6-May-23	5.39	7.74	12.52		8.73	6.53	0.75	7.68	2.30	1.14	1.14	2.72		0.00	0.00	8.90	65.54	0.00	0.00
7-May-23	3.16	2.48	11.37		8.72	7.44	1.79	7.44	0.57	1.84	0.56	2.90			0.00	8.87	57.14	0.00	0.00
8-May-23	3.65	3.22	11.79		7.25	5.87	0.89	6.33	0.37	1.79	0.61	2.90			0.00	7.21	51.88	0.00	0.00
9-May-23	3.38	4.00	11.56		5.98	4.79	0.00	5.61	0.81	2.04	0.26	3.09				5.79	47.31	0.00	0.00
10-May-23	2.42	3.39	10.82		5.58	3.69	0.00	4.92	0.76	1.90	0.47	2.92	0.00	0.00		5.24	42.11	0.00	0.00
11-May-23	2.04	3.18	12.32		7.05	2.10	0.17	4.09	0.89	1.58	0.72	0.08		0.00		6.93	41.15	0.00	0.00
12-May-23	1.00	0.52	12.19		6.71	1.21	0.00	3.77	0.00	1.32	1.02	2.62	0.00	0.00		6.46	36.82	0.00	0.00
13-May-23	2.71	6.20	14.40		7.72	3.62	0.48	5.21	2.00	0.87	1.50	2.97				7.57	55.25	0.00	0.00
14-May-23	1.85	2.67	15.26		8.59	6.64	2.94	6.28	0.67	0.69	1.66	2.86	0.00		0.00	8.55	58.66	0.00	0.00
15-May-23	3.04	3.83	13.28		11.16	10.40	5.96	8.24	2.10	1.40	0.93	3.10	0.00		0.00	11.38	74.82	0.00	0.00
16-May-23	3.65	3.90	12.21		11.59	8.07	5.09	7.13	1.99	1.05	1.29	3.05	0.00	0.00		11.68	70.70	0.00	0.00
17-May-23	3.77	3.65	11.23		8.04	7.95	2.79	6.70	1.07	1.42	0.80	2.98		0.00		7.78	58.18	0.00	0.00
18-May-23	2.84	2.71	8.84		5.87	9.39	3.77	5.25	1.45	1.65	0.72	3.02	0.00	0.00	0.00	5.50	51.01	0.00	0.00
19-May-23	5.05	6.94	13.34		10.43	11.70	5.91	7.30	3.52	1.29	1.10	3.10			0.00	10.53	80.21	0.00	0.00
20-May-23	7.00	8.06	13.65		11.06	13.17	6.67	7.63	3.74	1.21	1.15	3.73			0.00	11.34	88.41	0.00	0.00
21-May-23	5.04	1.68	11.57		11.01	11.25	4.35	7.70	1.67	1.32	1.05	3.88			0.00	11.18	71.70	0.00	0.00
22-May-23	3.36	3.16	12.36		10.80	9.01	3.52	7.01	1.52	1.54	0.92	3.70	0.00		0.00	11.02	67.92	0.00	0.00
23-May-23	2.87	4.77	11.85		12.44	10.44	6.16	8.06	3.36	1.32	1.14	3.77			0.00	13.06	79.24	0.00	0.00
24-May-23	1.24	0.00	7.53		6.96	4.53	1.74	4.70	0.00	1.54	0.69	2.99			0.00	6.86	38.78	0.00	0.00
25-May-23	1.89	0.00	6.44		4.93	4.85	0.15	4.50	0.00	1.89	0.44	2.68	0.00		0.00	4.57	32.34	0.00	0.00
26-May-23	4.56	0.70	6.52		6.81	10.39	2.93	6.32	2.22	0.99	1.32	2.51	0.00		0.00	6.73	52.00	0.00	0.00
27-May-23	6.84	1.82	6.93		7.23	10.52	3.14	6.44	1.75	0.53	1.75	0.07			0.00	7.30	54.32	0.00	0.00
28-May-23	5.99	0.00	11.01		8.69	8.70	4.36	5.38	2.10	0.32	1.70	2.20		0.00		8.90	59.35	0.00	0.00
29-May-23	4.66	0.00	9.23		6.10	4.86	2.01	3.79	0.00	1.40	0.99	2.43			0.00	5.88	41.35	0.00	0.00
30-May-23	0.11	0.00	8.51		4.71	2.42	0.00	3.52	0.00	1.47	0.84	2.64		0.00	0.00	4.47	28.69	0.00	0.00
31-May-23	0.00	0.00	8.63		4.17	0.07	0.00	1.21	0.00	1.71	0.58	2.26			0.00	3.62	22.25	0.00	0.00
Total	114.36	107.46	335.46	0.00	246.32	223.63	72.32	188.70	47.21	38.68	33.39	82.22	0.00	0.00	0.00	243.59	1733.34	0.00	0.00
Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day																			

Date	15.2 Import-Export of NR with ER & NER during May 2023																		
	Export of NR to ER (NR- ER)																	Export of NR to NER (NR-NER)	
	NR - ER 765 kV Sasaram - Fatehpur	NR - ER 765 kV Gaya - Varanasi 2*/S/C	NR - ER 765 kV Gaya Balia	NR - ER HVDC Alipurduar - Agra	NR-ER 400 kV Patna - Balia D/C	NR - ER 400 kV Muzaffarpur - Gorakhpur D/C	NR - ER 400 kV Biharshariff - Balia D/C	NR - ER 400 kV Motihari - Gorakhpur D/C	NR - ER 400 kV Biharshariff - Varanasi D/C	NR-ER 400 kV Sasaram - Varanasi	NR-ER 400 kV Sasaram - Allahabad	NR - ER 220 kV Sahupuri- Karamnasa	NR - ER 132 kV Sahupuri - Karamnasa	NR - ER 132 kV Rihand - Nagar Untari	NR - ER 132 kV Rihand - Garhwa	NR-ER 400 kV Balia- Naubatpur D/C	Total NR -ER	NR-NER HVDC Biswanath Chariali - Agra	Total NR-NER
1-May-23	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.38	0.00	0.38	10.44	10.44
2-May-23	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.38	0.00	0.38	7.26	7.26
3-May-23	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.41	0.00	0.41	10.95	10.95
4-May-23	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.26		0.00	0.26	6.72	6.72
5-May-23	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.36		0.00	0.36	7.19	7.19
6-May-23	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.00	0.36	0.00	0.36	7.30	7.30
7-May-23	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.42	0.00	0.42	6.77	6.77
8-May-23	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.25	0.00	0.25	11.27	11.27
9-May-23	0.00	0.00	0.00		0.00	0.00	0.38	0.00	0.00	0.00	0.00	0.00				0.00	0.38	11.12	11.12
10-May-23	0.00	0.00	0.00		0.00	0.00	0.73	0.00	0.00	0.00	0.00	0.00	0.48	0.07		0.00	1.28	7.20	7.20
11-May-23	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.08		0.00	0.08	7.12	7.12
12-May-23	0.00	0.00	0.00		0.00	0.00	0.05	0.00	0.02	0.00	0.00	0.00	0.00	0.07		0.00	0.14	7.63	7.63
13-May-23	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00				0.00	0.00	7.07	7.07
14-May-23	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.38	0.00	0.38	6.89	6.89
15-May-23	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.42	0.00	0.42	11.82	11.82
16-May-23	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.48	0.07		0.00	0.55	10.77	10.77
17-May-23	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.07		0.00	0.07	11.50	11.50
18-May-23	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.52	0.00	0.00	0.52	11.82	11.82
19-May-23	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.41	0.00	0.41	12.30	12.30
20-May-23	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.41	0.00	0.41	11.86	11.86
21-May-23	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.40	0.00	0.40	12.63	12.63
22-May-23	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.35	0.00	0.35	10.60	10.60
23-May-23	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.40	0.00	0.40	10.18	10.18
24-May-23	0.00	4.04	0.00		0.00	0.00	0.00	0.00	0.54	0.00	0.00	0.00			0.39	0.00	4.97	10.90	10.90
25-May-23	0.00	5.10	0.00		0.00	0.00	0.00	0.00	1.03	0.00	0.00	0.00	0.00		0.37	0.00	6.50	9.74	9.74
26-May-23	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.21	0.00	0.21	13.67	13.67
27-May-23	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.39	0.00	0.39	4.40	4.40
28-May-23	0.00	1.10	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00		0.70		0.00	1.80	9.68	9.68
29-May-23	0.00	7.46	0.00		0.00	0.00	0.00	0.00	0.14	0.00	0.00	0.00			0.68	0.00	8.28	8.40	8.40
30-May-23	0.00	7.43	0.00		0.00	0.00	1.50	0.00	1.56	0.00	0.00	0.00		0.00	0.80	0.00	11.29	7.02	7.02
31-May-23	2.65	13.61	0.00		0.00	0.00	1.52	0.00	4.02	0.00	0.00	0.00			0.67	0.00	22.47	9.49	9.49
Total	2.65	38.74	0.00	0.00	0.00	0.00	4.18	0.00	7.31	0.00	0.00	0.00	0.96	2.20	8.48	0.00	64.52	291.71	291.71
Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day																			

Date	15.3 Import and Export of ER with WR & NER during May 2023																							
	Export of WR to ER (WR-ER)								Import of WR from ER (ER - WR)								Export of ER to NER (ER-NER)				Import of ER from NER (NER-ER)			
	WR - ER 765 kV Dharamjaygarh - Ranchi 2x5/C	WR - ER 765 kV Dharamjaygarh - Jharsuguda Q/C	WR - ER 765 kV Durg - Jharsuguda D/C	WR - ER 400 kV Sipat - Ranchi D/C	WR - ER 400 kV Raigarh - Jharsuguda-2x5/C	WR - ER 220 kV Korba - Budhipadar D/C	WR - ER 220 kV Raigarh - Budhipadar	Total WR - ER	ER - WR 765 kV Dharamjaygarh - Ranchi 2x5/C	ER-WR 765 kV Dharamjaygarh - Jharsuguda D/C	ER-WR 765 kV Durg - Jharsuguda D/C	ER - WR 400 kV Sipat - Ranchi D/C	ER - WR 400 kV Raigarh - Jharsuguda-2x5/C	ER - WR 220 kV Korba - Budhipadar D/C	ER - WR 220 kV Raigarh - Budhipadar	Total ER - WR	ER - NER 400 kV Binaguri - Bongaigaon D/C	ER - NER 400 kV Alipurduar - Bongaigaon D/C	ER - NER 220 kV Birpara - Salakati D/C	Total ER - NER	NER - ER 400 kV Binaguri - Bongaigaon D/C	NER - ER 400 kV Alipurduar - Bongaigaon 2x5/C	NER - ER 220 kV Birpara - Salakati D/C	Total NER - ER
1-May-23	5.9	11.4	0.0	1.4	0.0	3.1	0.0	21.79	1.7	2.7	7.6	0.6	7.3	0.0	1.3	21.18	0.00	0.01	0.00	0.01	1.99	7.01	1.64	10.64
2-May-23	7.1	11.4	0.0	1.6	0.0	3.0	0.0	22.99	1.2	2.2	8.4	0.4	7.2	0.0	1.8	21.11	0.00	0.00	0.00	0.00	1.83	4.93	1.44	8.20
3-May-23	10.2	10.2	0.0	2.0	0.0	2.7	0.0	25.10	0.0	2.7	9.4	0.1	6.5	0.0	1.7	20.43	0.10	0.05	0.00	0.15	1.65	5.82	1.66	9.13
4-May-23	11.0	10.9	0.0	1.6	0.0	1.9	0.0	25.31	0.0	0.7	9.3	0.1	6.2	0.0	1.3	17.60	0.87	1.84	0.20	2.90	0.73	3.02	0.58	4.33
5-May-23	7.7	4.6	0.0	1.5	0.0	2.0	0.0	15.72	0.7	2.2	9.2	0.4	5.4	0.0	1.1	19.07	0.46	0.77	0.11	1.34	0.56	2.53	0.48	3.57
6-May-23	15.3	9.1	0.0	2.1	0.0	1.4	0.0	28.02	0.0	2.8	9.0	0.0	7.0	0.0	1.3	20.05	0.26	0.20	0.01	0.47	0.59	3.06	0.75	4.40
7-May-23	15.0	12.4	0.0	2.6	0.1	1.6	0.0	31.76	0.2	1.4	8.4	0.2	6.5	0.0	1.0	17.63	0.53	1.19	0.09	1.81	0.50	1.82	0.49	2.81
8-May-23	20.0	12.7	0.0	3.3	0.0	1.6	0.0	37.53	0.0	2.0	7.7	0.0	5.7	0.0	1.3	16.62	0.02	0.00	0.00	0.02	1.37	5.34	1.12	7.83
9-May-23	23.0	11.0	0.0	4.0	0.0	1.5	0.0	39.43	0.0	3.5	6.7	0.0	5.3	0.0	0.9	16.50	0.44	0.55	0.01	1.01	0.76	2.78	0.76	4.29
10-May-23	26.3	14.9	0.0	4.5	0.0	1.5	0.0	47.16	0.0	1.0	5.1	0.0	5.4	0.0	1.2	12.64	1.11	2.73	0.22	4.06	0.25	1.17	0.32	1.74
11-May-23	28.2	9.1	0.0	5.4	0.2	1.2	0.0	44.07	0.0	4.4	5.3	0.0	4.2	0.0	1.0	14.96	1.33	2.88	0.20	4.41	0.16	1.05	0.38	1.59
12-May-23	29.6	9.7	0.0	6.3	0.4	2.4	0.0	48.32	0.0	3.8	5.0	0.0	2.6	0.0	1.1	12.46	1.72	3.51	0.10	5.32	0.00	0.06	0.16	0.22
13-May-23	33.2	15.5	0.0	6.4	0.1	2.5	0.0	57.72	0.0	4.8	4.4	0.0	4.4	0.0	1.3	14.95	1.87	3.73	0.21	5.80	0.00	0.08	0.19	0.27
14-May-23	31.0	22.7	0.6	6.6	0.6	2.5	0.1	64.07	0.0	3.9	3.2	0.0	2.7	0.0	0.9	10.75	0.55	0.89	0.00	1.44	0.25	1.57	0.79	2.61
15-May-23	14.0	22.0	0.0	3.0	1.3	3.3	0.1	43.66	0.9	0.5	4.0	0.4	1.4	0.0	1.1	8.20	0.12	0.10	0.00	0.22	0.85	3.54	1.12	5.51
16-May-23	3.8	7.9	0.0	1.0	0.3	3.2	0.0	16.17	1.4	3.7	6.9	0.5	2.4	0.0	1.6	16.41	0.12	0.19	0.00	0.32	1.70	5.58	1.58	8.86
17-May-23	4.0	6.0	0.0	1.2	0.0	2.5	0.0	13.78	1.0	3.4	7.5	0.2	4.0	0.0	1.7	17.80	0.00	0.00	0.00	0.00	3.35	11.00	2.21	16.56
18-May-23	6.1	28.5	0.0	1.2	0.0	1.9	0.0	37.65	1.0	0.2	5.9	0.3	6.2	0.0	1.5	15.11	0.00	0.00	0.00	0.00	2.52	8.50	1.71	12.73
19-May-23	14.7	29.1	0.0	2.2	0.0	1.6	0.0	47.75	0.0	0.5	6.0	0.0	6.7	0.0	0.9	14.14	0.00	0.00	0.00	0.00	2.93	9.93	1.43	14.29
20-May-23	17.2	21.0	0.0	3.5	0.0	2.9	0.0	44.54	0.2	1.4	6.4	0.2	5.8	0.0	0.9	15.00	0.00	0.00	0.00	0.00	3.29	10.41	1.32	15.02
21-May-23	21.8	18.4	0.0	4.3	0.4	3.6	0.0	48.45	0.0	0.7	4.7	0.0	3.7	0.0	0.6	9.72	0.00	0.00	0.00	0.00	3.15	9.90	1.82	14.87
22-May-23	24.1	18.6	0.0	4.4	0.2	2.9	0.0	50.19	0.0	0.3	4.6	0.0	4.2	0.0	0.8	9.91	0.01	0.00	0.00	0.01	2.20	7.75	1.56	11.51
23-May-23	13.9	13.5	0.0	2.0	0.0	2.2	0.0	31.62	1.2	0.4	6.7	0.6	5.4	0.0	1.4	15.66	0.08	0.04	0.00	0.12	1.24	4.31	1.36	6.90
24-May-23	15.9	17.8	0.0	2.8	0.3	2.5	0.0	39.33	0.0	0.6	6.0	0.1	3.8	0.0	1.1	11.55	0.21	0.23	0.00	0.44	1.29	3.27	1.36	5.93
25-May-23	17.4	20.5	0.0	3.2	0.5	3.0	0.1	44.63	0.0	1.1	6.4	0.1	5.4	0.0	1.1	14.15	0.98	2.42	0.26	3.66	0.47	1.69	0.58	2.74
26-May-23	10.2	28.2	0.1	1.7	0.1	3.1	0.1	43.37	0.0	0.0	4.9	0.2	5.1	0.0	1.1	11.25	0.05	0.34	0.01	0.41	2.29	6.34	1.47	10.10
27-May-23	7.5	21.2	0.0	1.5	0.7	4.0	0.0	34.98	1.6	0.0	5.8	0.9	3.4	0.0	1.2	12.91	0.00	0.00	0.00	0.00	1.93	5.07	1.11	8.11
28-May-23	9.9	7.2	0.0	2.1	0.3	4.1	0.0	23.60	0.9	1.4	6.8	0.3	2.9	0.0	1.3	13.59	0.15	0.18	0.00	0.33	2.00	6.10	1.28	9.37
29-May-23	13.4	8.8	0.0	2.5	0.5	3.4	0.0	28.59	0.0	3.3	8.1	0.1	3.5	0.0	1.6	16.66	0.40	0.73	0.01	1.14	0.36	1.55	0.55	2.46
30-May-23	20.4	14.2	0.0	3.2	0.0	3.6	0.0	41.36	0.0	2.1	8.0	0.0	4.8	0.0	1.5	16.45	2.12	5.60	0.43	8.15	0.00	0.02	0.06	0.09
31-May-23	27.3	21.4	0.0	4.9	0.3	3.5	0.0	57.45	0.0	0.5	7.0	0.0	4.0	0.0	1.8	13.30	2.63	6.16	1.25	10.04	0.00	0.00	0.00	0.00
Total	504.96	469.82	0.64	93.84	6.23	80.04	0.57	1156.11	11.95	58.29	204.42	5.71	148.94	0.00	38.46	467.76	16.15	34.31	3.12	53.58	40.19	135.22	31.32	206.73

Date	15.4 Import and Export of SR with ER & WR during May 2023																							
	Export of ER to SR (ER - SR)				Import of ER from SR (SR - ER)				Export of WR to SR (WR-SR)								Import of WR from SR (SR - WR)							
	ER - SR HVDC Gazuwaka	ER - SR HVDC Talchar -Kolar	ER-SR 765 kV Angul- Srikakulam D/C	Total ER - SR	SR - ER HVDC Gazuwaka	SR - ER HVDC Talchar -	SR-ER 765 kV Angul- Srikakulam D/C	Total SR - ER	WR - SR HVDC Bhadravati	WR - SR 765 kV Sholapur - Raichur 2x5/C	WR-SR 765 kV Wardha - Nizamabad D/C	WR-SR 400kV Kolhapur-Kudgi/ D/C	WR-SR HVDC Raigarh- Puglur	WR-SR 220kV/ Xeldem - Ambewadi S/C	WR-SR 220kV/ Ponda - Ambewadi S/C	Total WR - SR	SR - WR HVDC Bhadravati	SR - WR 765 kV Raichur - Sholapur 2x5/C	SR-WR 765 kV Wardha - Nizamabad D/C	SR-WR 400kV/ Kolhapur- Kudgi D/C	SR-WR HVDC Raigarh- Puglur	WR-SR 220kV/ Xeldem - Ambewadi S/C	WR-SR 220kV/ Ponda - Ambewadi S/C	Total SR - WR
1-May-23	12.59	35.97	42.32	90.88	0.00	0.00	0.00	0.00	13.85	3.55	17.63	0.00	41.39	2.49	0.01	78.91	1.71	8.85	1.02	20.91	0.00	0.00	0.00	32.50
2-May-23	12.50	39.68	46.12	98.29	0.00	0.00	0.00	0.00	7.26	3.86	21.29	0.00	41.95	2.61	0.01	76.99	0.00	7.95	0.00	23.02	0.00	0.00	0.00	30.97
3-May-23	12.50	39.67	52.89	105.07	0.00	0.00	0.00	0.00	7.25	5.77	25.95	0.00	26.88	2.44	0.01	68.29	0.00	3.90	0.00	22.57	0.00	0.00	0.00	26.46
4-May-23	12.49	39.66	55.29	107.44	0.00	0.00	0.00	0.00	7.27	5.73	26.22	0.00	17.19	2.26	0.01	58.68	0.00	2.42	0.00	21.95	0.00	0.00	0.00	24.37
5-May-23	12.53	39.66	51.11	103.31	0.00	0.00	0.00	0.00	7.25	2.61	26.10	0.00	53.97	2.23	0.01	92.17	0.00	4.17	0.00	23.96	0.00	0.00	0.00	28.13
6-May-23	12.58	39.67	50.89	103.14	0.00	0.00	0.00	0.00	11.27	2.59	23.40	0.00	33.00	2.25	0.01	72.53	0.00	9.81	0.00	24.58	0.00	0.00	0.00	34.39
7-May-23	12.59	39.67	50.16	102.41	0.00	0.00	0.00	0.00	14.30	3.76	18.96	0.00	33.04	2.15	0.01	72.22	0.00	8.55	0.00	24.84	0.00	0.00	0.00	33.39
8-May-23	12.58	39.67	53.28	105.54	0.00	0.00	0.00	0.00	7.27	5.86	25.08	0.00	35.99	2.38	0.01	76.60	0.00	4.94	0.00	24.58	0.00	0.00	0.00	29.52
9-May-23	12.58	36.90	49.48	98.96	0.00	0.00	0.00	0.00	5.51	5.67	21.50	0.00	39.79	2.27	0.01	74.75	1.64	10.95	0.00	24.68	0.00	0.00	0.00	37.27
10-May-23	12.59	37.44	50.73	100.76	0.00	0.00	0.00	0.00	11.06	5.94	25.84	0.00	22.75	2.47	0.01	68.08	0.00	7.37	0.00	24.03	3.73	0.00	0.00	35.13
11-May-23	12.60	39.99	41.74	94.32	0.00	0.00	0.00	0.00	13.97	0.62	18.30	0.00	33.41	2.52	0.01	68.84	0.00	12.31	0.00	27.90	0.00	0.00	0.00	40.20
12-May-23	12.59	39.69	42.30	94.58	0.00	0.00	0.00	0.00	7.28	4.68	20.93	0.00	27.58	2.54	0.01	63.01	0.00	12.98	0.00	25.25	0.00	0.00	0.00	38.23
13-May-23	12.58	36.59	41.23	90.40	0.00	0.00	0.00	0.00	9.80	0.27	14.37	0.00	20.76	2.55	0.01	47.74	0.00	23.19	1.18	29.40	0.00	0.00	0.00	53.77
14-May-23	12.58	36.37	39.75	88.69	0.00	0.00	0.00	0.00	3.43	3.40	18.01	0.00	29.79	2.44	0.01	57.07	6.17	24.05	1.70	28.77	0.00	0.00	0.00	60.70
15-May-23	12.46	42.68	53.30	108.44	0.00	0.00	0.00	0.00	0.00	10.52	37.96	0.00	56.01	2.48	0.00	106.97	11.39	8.52	0.00	23.35	0.00	0.00	0.00	43.25
16-May-23	12.49	43.99	51.93	108.41	0.00	0.00	0.00	0.00	6.69	9.78	34.96	0.00	94.42	2.55	0.01	148.41	4.18	5.51	0.00	22.50	0.00	0.00	0.00	32.19
17-May-23	12.39	40.90	49.15	102.44	0.00	0.00	0.00	0.00	24.05	11.56	32.09	0.00	121.11	0.65	1.23	190.69	0.00	6.07	0.00	21.97	0.00	0.00	0.00	28.03
18-May-23	12.51	40.88	55.81	109.20	0.00	0.00	0.00	0.00	24.08	17.33	41.20	0.00	109.31	2.44	0.17	194.53	0.00	2.07	0.00	17.45	0.00	0.00	0.00	19.52
19-May-23	12.51	40.85	59.71	113.07	0.00	0.00	0.00	0.00	16.77	14.83	43.20	0.00	61.82	2.65	0.01	139.28	0.00	0.34	0.00	19.04	0.00	0.00	0.00	19.39
20-May-23	12.49	35.42	56.32	104.23	0.00	0.00	0.00	0.00	12.05	9.48	36.14	0.00	66.03	2.58	0.00	126.28	0.00	2.13	0.00	20.02	0.00	0.00	0.00	22.15
21-May-23	12.52	44.10	45.47	102.09	0.00	0.00	0.00	0.00	12.07	1.00	22.33	0.00	48.19	1.30	0.00	84.91	0.00	8.37	0.00	25.19	0.00	0.00	0.00	33.56
22-May-23	12.51	39.63	51.42	103.56	0.00	0.00	0.00	0.00	12.05	11.74	29.67	0.00	47.49	2.44	0.00	103.40	0.00	4.55	0.00	23.14	0.00	0.00	0.00	27.69
23-May-23	12.52	39.63	57.06	109.20	0.00	0.00	0.00	0.00	12.05	15.78	35.58	0.00	48.72	0.77	0.00	112.90	0.00	1.06	0.00	21.49	0.00	0.00	0.00	22.56
24-May-23	12.55	39.63	52.40	104.59	0.00	0.00	0.00	0.00	12.08	6.34	33.36	0.00	71.53	2.63	0.00	125.94	0.00	3.37	0.00	24.32	0.00	0.00	0.00	27.69
25-May-23	12.63	39.68	51.77	104.08	0.00	0.00	0.00	0.00	16.17	6.82	33.89	0.00	77.01	2.57	0.00	136.46	0.00	5.15	0.00	25.49	0.00	0.00	0.00	30.63
26-May-23	12.63	39.71	52.88	105.23	0.00	0.00	0.00	0.00	19.74	9.95	34.96	0.00	68.11	2.50	0.00	135.27	0.00	3.44	0.00	21.94	0.00	0.00	0.00	25.39
27-May-23	12.62	39.71	57.72	110.05	0.00	0.00	0.00	0.00	21.24	13.37	35.88	0.00	87.36	1.49	0.00	159.33	0.00	2.36	0.00	21.55	0.00	0.00	0.00	23.91
28-May-23	13.61	36.85	50.13	100.58	0.00	0.00	0.00	0.00	23.95	6.94	27.27	0.00	103.31	2.55	0.00	164.02	0.00	4.40	0.00	22.78	0.00	0.00	0.00	27.18
29-May-23	16.51	26.42	53.75	96.68	0.00	0.00	0.00	0.00	23.93	10.79	35.58	0.00	121.86	2.68	0.00	194.82	0.00	0.37	0.00	19.77	0.00	0.00	0.00	20.14
30-May-23	14.00	35.03	46.68	95.72	0.00	0.00	0.00	0.00	23.86	4.07	27.02	0.00	83.18	1.59	0.00	139.72	0.00	2.34	0.00	21.19	0.00	0.00	0.00	23.54
31-May-23	12.38	38.52	48.56	99.46	0.00	0.00	0.00	0.00	23.95	8.15	28.79	0.00	68.90	2.69	0.00	132.48	0.00	3.79	0.00	21.67	0.00	0.00	0.00	25.46
TOTAL	395.23	1204.28	1561.33	3160.85	0.00	0.00	0.00	0.00	411.52	222.76	873.44	0.00	1791.86	70.18	1.54	3371.30	25.09	205.27	3.90	719.30	3.73	0.00	0.00	957.30

16. भूटान , नेपाल, बांग्लादेश एवं म्यान्मार के साथ अंतरराष्ट्रीय विद्युत विनिमय

अप्रैल 2023 से मार्च 2024 April 2023 to March 2024

अंतरराष्ट्रीय विद्युत विनिमय [भारत 'से निर्यात'/'को आयात']

Transnational Exchange ('Export from'/'Import to' India)

माह MONTH	भूटान BHUTAN		नेपाल NEPAL		बांग्लादेश BANGLADESH		म्यान्मार MYANMAR	
	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)
अप्रैल 2023 APR'23	19.40	41.40	357.99	0.00	687.30	0.00	0.73	0.00
मई 2023 MAY'23	2.27	114.78	265.04	0.34	750.12	0.00	0.09	0.00
कुल Total	21.67	156.18	623.03	0.34	1437.42	0.00	0.82	0.00

* Based on daily operational data

Date	16.1 Import from neighbouring countries during May 2023													
	(All figures in MU)													
	Import from Bhutan								Import from Bangladesh		Import from Nepal			Import from Myanmar
	400 kV Tala-Binaguri I,II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurwar D/C*	400 kV Jigmeling-Alipurwar D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-May-23	4.92	2.22	0.00	0.00	1.17	1.81	0.50	0.00	0.00	0.00	0.00	0.00	0.00	0.00
2-May-23	7.20	2.30	0.00	0.00	1.20	1.86	0.73	0.00	0.00	0.00	0.00	0.00	0.00	0.00
3-May-23	3.39	0.73	0.00	0.00	0.00	0.09	0.50	0.00	0.00	0.00	0.00	0.00	0.00	0.00
4-May-23	2.82	0.59	0.00	0.00	0.00	0.00	0.49	0.00	0.00	0.00	0.00	0.00	0.00	0.00
5-May-23	2.76	0.80	0.00	0.00	0.22	0.41	0.43	0.00	0.00	0.00	0.00	0.00	0.00	0.00
6-May-23	2.74	0.32	0.00	0.00	0.00	0.00	0.43	0.00	0.00	0.00	0.00	0.00	0.00	0.00
7-May-23	5.38	1.26	0.00	0.00	0.85	1.33	0.69	0.00	0.00	0.00	0.00	0.00	0.00	0.00
8-May-23	4.95	0.61	0.00	0.00	0.30	0.49	0.51	0.00	0.00	0.00	0.00	0.00	0.00	0.00
9-May-23	3.31	1.03	0.00	0.00	0.55	0.87	0.64	0.00	0.00	0.00	0.00	0.00	0.00	0.00
10-May-23	4.62	1.65	0.00	0.00	0.55	0.87	0.57	0.00	0.00	0.00	0.00	0.00	0.00	0.00
11-May-23	2.92	0.80	0.00	0.00	0.00	0.00	0.64	0.00	0.00	0.00	0.00	0.00	0.00	0.00
12-May-23	2.50	0.57	0.00	0.00	0.00	0.00	0.64	0.00	0.00	0.00	0.00	0.00	0.00	0.00
13-May-23	2.05	0.33	0.00	0.00	0.00	0.00	0.71	0.00	0.00	0.00	0.00	0.00	0.00	0.00
14-May-23	2.24	0.49	0.00	0.00	0.07	0.16	0.63	0.00	0.00	0.00	0.00	0.00	0.00	0.00
15-May-23	2.32	1.08	0.00	0.00	0.38	0.60	0.74	0.00	0.00	0.00	0.00	0.00	0.00	0.00
16-May-23	2.06	1.41	0.00	0.00	0.82	1.28	0.73	0.00	0.00	0.00	0.00	0.00	0.00	0.00
17-May-23	2.29	1.44	0.00	0.00	0.33	0.54	0.42	0.00	0.00	0.00	0.00	0.00	0.00	0.00
18-May-23	2.39	1.77	0.00	0.00	0.43	0.72	0.56	0.00	0.00	0.00	0.00	0.00	0.00	0.00
19-May-23	2.75	1.32	0.00	0.00	0.53	0.85	0.83	0.00	0.00	0.00	0.00	0.00	0.00	0.00
20-May-23	2.88	1.03	0.00	0.00	1.21	1.86	0.86	0.00	0.00	0.00	0.00	0.00	0.97	0.00
21-May-23	2.91	0.92	0.00	0.00	1.12	1.72	0.53	0.00	0.00	0.00	0.00	0.00	0.00	0.00
22-May-23	2.47	0.64	0.00	0.00	0.31	0.51	0.56	0.00	0.00	0.00	0.00	0.00	0.00	0.00
23-May-23	4.44	0.30	0.00	0.00	0.64	1.00	0.71	0.00	0.00	0.00	0.00	0.00	0.00	0.00
24-May-23	6.30	0.00	0.00	0.00	0.54	0.86	0.65	0.00	0.00	0.00	0.00	0.00	0.00	0.00
25-May-23	8.17	0.00	0.00	0.00	1.10	1.71	0.83	0.00	0.00	0.00	0.00	0.00	0.00	0.00
26-May-23	10.32	0.00	0.00	0.00	2.25	3.47	0.86	0.02	0.00	0.00	0.00	0.00	0.00	0.00
27-May-23	6.96	1.83	0.00	0.00	2.04	3.12	0.81	0.07	0.00	0.00	0.00	0.34	0.00	0.00
28-May-23	4.94	1.10	0.00	0.00	1.12	1.71	0.88	0.00	0.00	0.00	0.00	0.00	0.00	0.00
29-May-23	3.86	0.91	0.00	0.00	0.67	1.07	0.85	0.00	0.00	0.00	0.00	0.00	0.00	0.00
30-May-23	2.91	0.87	0.00	0.00	0.98	1.49	0.92	0.04	0.00	0.00	0.00	0.00	0.00	0.00
31-May-23	2.86	0.74	0.00	0.00	1.61	2.45	1.12	0.20	0.00	0.00	0.00	0.00	0.00	0.00
Total	122.64	29.07	0.00	0.00	20.98	32.85	20.97	0.33	0.00	0.00	0.00	0.34	0.97	0.00
Based on SEM/Energy meter data for links where available (*Mangdechu generation receipt at APD through a bypassed arrangement at 400kV Punatsanchu station)														

Date	16.2 Export to neighbouring countries during May 2023 (All figures in MU)													
	Export to Bhutan								Export to Bangladesh		Export to Nepal			Export to Myanmar
	400 kV Tala-Binaguri I,II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurwar D/C*	400 kV Jigmeling-Alipurwar D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-May-23	0.00	0.00	1.81	2.53	0.00	0.00	0.00	0.13	22.19	3.20	1.33	3.19	1.18	0.00
2-May-23	0.00	0.00	1.60	2.50	0.00	0.00	0.00	0.11	21.99	3.78	1.23	9.13	1.29	0.03
3-May-23	0.00	0.00	1.58	1.71	0.00	0.00	0.00	0.29	21.83	3.75	1.26	9.37	1.77	0.03
4-May-23	0.00	0.00	1.49	1.16	0.17	0.20	0.00	0.22	22.03	3.49	1.10	8.00	0.30	0.03
5-May-23	0.00	0.00	1.28	1.13	0.00	0.00	0.00	0.12	22.07	3.50	1.41	8.14	0.19	0.00
6-May-23	0.00	0.00	1.34	1.19	0.14	0.20	0.00	0.21	21.76	3.64	1.40	7.83	1.46	0.00
7-May-23	0.00	0.00	0.64	1.02	0.00	0.00	0.00	0.06	21.90	3.67	1.43	9.30	2.32	0.00
8-May-23	0.00	0.00	0.87	0.83	0.00	0.00	0.00	0.21	21.81	3.83	1.50	9.75	2.19	0.00
9-May-23	0.00	0.00	0.81	1.16	0.00	0.00	0.00	0.14	21.66	3.84	1.60	9.94	2.47	0.00
10-May-23	0.00	0.00	0.32	0.86	0.00	0.00	0.00	0.04	21.64	3.88	1.55	9.44	2.19	0.00
11-May-23	0.00	0.00	0.69	1.13	0.04	0.01	0.00	0.13	21.69	3.77	1.59	9.86	2.16	0.00
12-May-23	0.00	0.00	0.93	1.23	0.07	0.06	0.00	0.19	20.77	3.40	1.55	10.24	3.93	0.00
13-May-23	0.00	0.00	1.36	1.27	0.33	0.44	0.00	0.13	21.83	3.12	1.54	10.79	2.47	0.00
14-May-23	0.00	0.00	1.51	1.26	0.00	0.00	0.00	0.19	22.27	3.08	1.49	9.37	1.76	0.00
15-May-23	0.00	0.00	1.46	1.31	0.00	0.00	0.00	0.20	21.71	3.40	1.43	6.30	0.78	0.00
16-May-23	0.00	0.00	1.48	1.39	0.00	0.00	0.00	0.21	17.32	3.59	1.45	7.67	1.89	0.00
17-May-23	0.00	0.00	1.36	0.96	0.00	0.00	0.00	0.39	21.51	2.96	1.46	6.15	0.88	0.00
18-May-23	0.00	0.00	1.45	1.28	0.00	0.00	0.00	0.31	20.15	2.83	1.45	5.43	0.47	0.00
19-May-23	0.00	0.00	1.37	1.39	0.00	0.00	0.00	0.28	21.62	3.01	1.45	4.02	0.74	0.00
20-May-23	0.00	0.00	1.27	1.23	0.00	0.00	0.00	0.11	21.01	3.58	1.20	3.95	0.00	0.00
21-May-23	0.00	0.00	1.51	1.51	0.00	0.00	0.00	0.22	21.45	3.61	1.45	3.48	0.76	0.00
22-May-23	0.00	0.00	1.71	1.57	0.00	0.00	0.00	0.29	21.62	3.26	1.40	4.62	1.60	0.00
23-May-23	0.00	0.00	2.20	2.52	0.00	0.00	0.00	0.18	20.13	3.08	1.28	4.31	0.70	0.00
24-May-23	0.00	0.23	2.33	3.02	0.00	0.00	0.00	0.15	21.52	2.90	1.02	3.71	0.24	0.00
25-May-23	0.00	2.34	1.35	1.72	0.00	0.00	0.00	0.00	22.22	3.17	0.87	4.22	0.00	0.00
26-May-23	0.00	0.47	0.40	1.51	0.00	0.00	0.00	0.00	22.05	2.76	0.74	2.59	0.00	0.00
27-May-23	0.00	0.00	0.30	1.12	0.00	0.00	0.00	0.00	21.79	3.34	0.05	0.00	0.00	0.00
28-May-23	0.00	0.00	0.93	1.28	0.00	0.00	0.00	0.09	22.20	3.57	0.84	1.85	0.33	0.00
29-May-23	0.00	0.00	0.88	1.38	0.00	0.00	0.00	0.10	21.82	3.62	1.41	3.88	1.08	0.00
30-May-23	0.00	0.00	0.74	1.12	0.00	0.00	0.00	0.00	21.74	3.44	1.24	4.28	0.68	0.00
31-May-23	0.00	0.00	0.73	0.92	0.00	0.00	0.00	0.00	21.33	3.58	1.32	4.38	1.07	0.00
Total	0.00	3.04	37.70	44.22	0.76	0.91	0.00	4.70	666.62	105.64	40.04	195.19	36.89	0.09
Based on SEM/Energy meter data for links where available (*Mangdechu generation receipt at APD through a bypassed arrangement at 400kV Punatsanchu station)														

17. एसटीओए (द्विपक्षीय एवं सामूहिक) एवं डी एस एम बिलिंग का ब्योरा – मई 2023

STOA (BILATERAL AND COLLECTIVE) & DSM BILLING DETAILS - MAY 2023

द्विपक्षीय एसटीओए BILATERAL SHORT TERM OPEN ACCESS

मई 2023	MAY 2023		Apr'23-May'23	
नोडल क्षेत्र.भा.प्रे.के. का नाम Name of Nodal RLDC	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Energy Approved(MU)	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Energy Approved (MU)
ऊ. क्षेत्र. NR	972	2629	1761	4119
प.क्ष. WR	1036	2548	1950	5344
द.क्ष. SR	698	2370	1539	6949
पू.क्ष. ER	687	868	1392	1705
पूर्वांचल क्षेत्र. NER	76	3	149	15
कुल TOTAL	3469	8418	6791	18132

एसटीओए SHORT TERM OPEN ACCESS

	सामूहिक एसटीओए Collective STOA		द्विपक्षीय एसटीओए Bilateral STOA	
माह MONTH	क्रेताओं / विक्रेताओं की सं. NO. of Buyers/Sellers	अनुमोदित ऊर्जा (मि.यु.) Approved Energy (MU)	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Approved Energy (MU)
अप्रैल 2023 Apr'23	5580	6941	3322	9714
मई 2023 May'23	5798	6626	3469	8418
कुल TOTAL	11378	13567	6791	18132

* Approved Energy (MU) includes the Real Time Market (RTM) transactions (started from 1st Jun-20) as well, while No. of Buyers/Sellers are excluding RTM transactions.
 ** Approved Energy (MU) includes the Real Time Market (RTM) transactions (started from 1st Jun-20) as well, while No. of Buyers/Sellers are excluding RTM transactions

**मासिक डी एस एम बिलिंग का ब्योरा* 2021-22
MONTHLY DSM BILLING DETAILS* 2021-22**

**अनंतिम आँकड़े
Provisional data
subject to change
करोड़ रु. में (RS. IN CRORES)**

क्षेत्र REGION →	उत्तरी क्षेत्र NORTH	पश्चिमी क्षेत्र WEST	दक्षिणी क्षेत्र SOUTH	पूर्वी क्षेत्र EAST	पूर्वांचल क्षेत्र NORTH EAST
सप्ताह WEEK ↓					
01.05.23 to 07.05.23	91.97	157.54	170.41	137.87	---
08.05.23 to 14.05.23	115.37	174.21	216.96	121.26	---
15.05.23 to 21.05.23	164.78	240.29	254.17	124.48	---
22.05.23 to 28.05.23	98.56	163.04	175.15	85.84	---

* Amount shown is Payable to DSM pool ^Provisional Data

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एच.पी.एक्स.आई.एस.) POWER MARKET INFORMATION (Source IEX & PXIL) पावर एक्चेंज के माध्यम से विनिमय - माह- मई 2023 EXCHANGES THROUGH POWER EXCHANGES - MAY 2023						
क्र. स. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्चेंज के माध्यम से (मि.यू.मै) Through Power Exchange in MU			
			Integrated Day Ahead Market (I-DAM)		Real Time Market (RTM)	
			विक्रय Sale	क्रय Purchase	विक्रय Sale	क्रय Purchase
1	पंजाब Punjab	उत्तरी क्षेत्र NR	74.52	164.26	63.14	79.94
2	हरियाणा Haryana		77.55	84.27	51.53	60.39
3	राजस्थान Rajasthan		66.22	314.96	161.39	265.81
4	दिल्ली Delhi		179.47	13.29	144.46	30.91
5	उत्तर प्रदेश Uttar Pradesh		405.49	240.50	58.68	153.73
6	उत्तराखंड Uttarakhand		65.16	65.49	46.68	10.48
7	हिमाचल प्रदेश Himachal Pradesh		90.32	62.93	115.97	19.87
8	जम्मू और कश्मीर J & K		17.02	254.09	23.02	160.93
9	केन्द्र शासित चंडीगढ़ UT Chandigarh		39.75	0.85	0.21	0.58
10	ए डी हाइड्रो AD Hydro		21.04	0.00	2.85	0.00
11	कन्याम वांगतू Karcham Wangtoo		17.32	0.00	2.06	0.00
12	श्री सीमेंट Shree Cement		2.97	0.00	0.99	0.51
13	नाथपा झाकरी Nathpa Jhakri		0.00	0.00	0.00	0.00
14	लांको बुधिल Lanco Budhil		2.71	0.00	0.62	0.00
15	सिंगरौली Singrauli		0.00	0.00	0.00	0.00
16	दादरी-I Dadri TPS		0.00	0.00	0.00	0.00
17	दादरी-II Dadri stg-II		0.00	0.00	0.00	0.00
18	ऊंचाहार-I Unchahar-I TPS		0.00	0.00	0.00	0.00
19	ऊंचाहार-II Unchahar-II TPS		0.00	0.00	0.00	0.00
20	ऊंचाहार-III Unchahar-III TPS		0.00	0.00	0.00	0.00
21	रिहंद-I Rihand STPS-I		0.00	0.00	0.00	0.00
22	रिहंद-II Rihand STPS-II		0.00	0.00	0.00	0.00
23	रिहंद-III Rihand STPS-III		0.00	0.00	0.00	0.00
24	एपीसीपीएल झुझर APCL Jhajjar		0.00	0.00	0.00	0.00
25	सांज Sainj HEP		15.02	0.00	8.76	0.30
26	दादरी गैस Dadri GPP		0.00	0.00	0.00	0.00
27	औरंगा गैस NTPC Auraiya		0.00	0.00	0.00	0.00
28	अंता गैस NTPC Anta		0.00	0.00	0.00	0.00
29	रामपुर एचईपी RAMPUR HEP		0.00	0.00	0.00	0.00
30	ऊंचाहार-IV UNCHAHAR-IV		0.00	0.00	0.00	0.00
31	एनटीपीसी कोलडाम NTPC KOLDAM		0.00	0.00	0.00	0.00
32	कोटेश्वर Koteswar		0.00	0.00	0.00	0.00
33	टांडा स्टेज-२ Tanda Stg-2		0.00	0.00	0.00	0.00
34	अदानी सौर एनर्जि टू लिमिटेड Adani Solar Energy Jodhpur Two Limited		11.69	0.00	0.00	0.00
35	सिंगोली भटवारी हेप Singoli Bhatwari HEP		17.19	0.00	3.43	0.32
36	रेलवे Railways		0.00	17.96	0.00	3.08
37	दिहरी Tuhri		0.00	0.00	0.00	0.00
38	Renew Solar Energy (Jharkhand Three) Private Limited (RSEJTPL)		0.00	0.00	0.00	0.00
39	सोरंग एच.ई.पी. Sorang HEP, (Himachal Sorang Power Private Ltd)		0.98	0.00	2.62	0.00
40	अदानी संकर ऊर्जा जैसलमेर वन लिमिटेड (सौर) Adani Hybrid Energy Jaisalmer One Limited (Solar)		0.00	0.00	0.00	0.00
41	अदानी संकर ऊर्जा जैसलमेर टू लिमिटेड (सौर) Adani Hybrid Energy Jaisalmer Two Limited (Solar)		0.00	0.00	0.00	0.00
42	अदानी संकर ऊर्जा जैसलमेर थ्री लिमिटेड (सौर) Adani Hybrid Energy Jaisalmer Three Limited (Solar)		0.00	0.00	0.00	0.00
43	अयाना रिन्यूबल पावर वन लिमिटेड Ayana Renewable Power One Private Limited		0.00	0.00	0.00	0.00
44	Adani Hybrid Energy Jaisalmer Four Limited (Solar)अदानी संकर ऊर्जा जैसलमेर चार लिमिटेड (सौर)		0.00	0.00	0.00	0.00
45	रिनीव सोलर ऊर्जा प्राइवेट लिमिटेड Renew Solar Urja private limited		0.00	0.00	0.00	0.00
46	NEA-NR एन ई ए-एन और		0.00	19.41	0.00	0.00
47	रेन्यू सूर्य रीवे प्राइवेट लिमिटेड (सौर) Renew Surya Ravi Private Limited (Solar)		30.33	0.00	0.59	0.00
48	अझरे पावर मपल प्राइवेट लिमिटेड (सौर) Azure Power Maple Pvt Ltd (Solar)		0.00	0.00	0.00	0.00
49	अदानी ग्रीन हाइड्रिड सौर जैसलमेर Adani Green Hybrid Solar Jaisalmer		0.00	0.00	0.00	0.00
50	अदानी ग्रीन हाइड्रिड पवन जैसलमेरAdani Green Hybrid Wind Jaisalmer		0.00	0.00	0.00	0.00
51	अदानी ग्रीन सौर जैसलमेर Adani Green Solar Jaisalmer		0.00	0.00	0.00	0.00
52	ABC Renewable Energy (RJ-01) Private Limited एबीसी नवीकरणीय ऊर्जा (आर.ओ.1) प्राइवेट लिमिटेड		0.00	0.00	0.00	0.00
53	SBSR Power Cleantech Eleven Private Limited एसबीएसआर पावर एलीनटेक लिमिटेड		1.48	0.00	0.00	1.48
54	टनकपुर पावर स्टेशन Tanakpur Power Station		0.00	0.00	0.00	0.00
55	उरी पावर स्टेशन Uri I Power Station		0.00	0.00	0.00	0.00
56	उरी पावर स्टेशन Uri II Power Station		0.00	0.00	0.00	0.00
57	चमेरा पावर स्टेशन Chamera I Power Station		0.00	0.00	0.00	0.00
58	चमेरा पावर स्टेशन Chamera II Power Station		0.00	0.00	0.00	0.00
59	चमेरा पावर स्टेशन Chamera III Power Station		0.00	0.00	0.00	0.00
60	धौलीगंगा पावर स्टेशन Dhauliganga Power Station		0.00	0.00	0.00	0.00
61	दुलहासी पावर स्टेशन Dulhashti Power Station		0.00	0.00	0.00	0.00
62	किसनगंगा पावर स्टेशन Kishanganga Power Station		0.00	0.00	0.00	0.00
63	पार्वती पावर स्टेशन Parbati III Power Station		0.00	0.00	0.00	0.00
64	सेवा पावर स्टेशन Sewa II Power Station		0.00	0.00	0.00	0.00
65	सलाल पावर स्टेशन Salal Power Station		0.00	0.00	0.00	0.00
66	ADANI SOLAR ENERGY JAISALMER ONE PRIVATE LIMITED AHS अदानी सौर ऊर्जा जैसलमेर वन प्राइवेट लिमिटेड ए एच अल		0.00	0.00	0.00	0.00
67	पार्वती ह. ई. प्रोजेक्ट Parbati II HE Project		0.00	0.00	0.00	0.00
68	एनटीपीसी अंता जीपीएस NTPC ANTA GPS RLNG		1.36	0.00	0.30	1.66
69	एनटीपीसी औरंगा जीपीएस NTPC AURAIYA GPS RLNG		1.98	0.00	1.91	3.89
70	एनटीपीसी दादरी जीपीएस NTPC DADRI GPS RLNG		2.64	0.00	2.93	5.57

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एच.पी.एक्स.आई.एस.) POWER MARKET INFORMATION (Source IEX & PXIL) पावर एक्स्चेंज के माध्यम से विनिमय - माह:- मई 2023 EXCHANGES THROUGH POWER EXCHANGES - MAY 2023						
क्र. स. स. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (पि.यू. मे) Through Power Exchange in MU			
			Integrated Day Ahead Market (I-DAM)		Real Time Market (RTM)	
			विक्रय Sale	क्रय Purchase	विक्रय Sale	क्रय Purchase
71	मध्य प्रदेश Madhya Pradesh	पश्चिमी क्षेत्र WR	64.75	39.56	365.97	10.08
72	महाराष्ट्र Maharashtra		49.76	325.50	48.94	204.09
73	गुजरात Gujarat		42.60	698.81	18.94	101.08
74	छत्तीसगढ़ Chhattisgarh		648.40	0.00	118.84	2.37
75	गोवा डब्ल्यू.आर. गोवा WR		34.46	9.65	0.19	1.36
76	जिंदल पावर JINDAL POWER		128.12	0.00	4.42	0.68
77	लान्को Lanco		0.00	0.00	0.00	0.00
78	ए सी बी आई एल ACBIL		33.84	0.00	5.11	0.76
79	जिंदल स्टील JINDAL STEEL		52.32	0.00	5.94	2.64
80	बालको 2 BALCO 2		5.41	0.00	5.71	0.00
81	जीएमआर वरोरा GMR Warora		5.36	0.00	4.57	0.00
82	एस्सर पावर एम पी Essar Power MP Ltd		98.11	0.00	11.10	0.00
83	के एस के महानदी KSK Mahanadi		0.00	0.00	0.00	0.00
84	जिंदल पावर लिमिटेड Jindal Power Ltd. Stg-II		183.80	0.00	9.92	3.01
85	रायगढ़ एनर्जी लिमिटेड Raigarh Energy Ltd.		12.96	0.00	0.80	0.00
86	डी बी पावर DB Power		94.77	0.00	0.32	0.00
87	धारीवाल Dharawal		0.00	0.00	0.00	0.00
88	जेपी निगमी JAYPEE NIGRIE		180.52	0.00	0.57	0.00
89	डीजेन मेगा पावर DGEN Mega power		5.28	0.00	2.37	0.00
90	एम बी पावर MB Power		125.17	0.00	16.23	0.00
91	अदानी पावर स्टेज 3 Adani Power STG3		0.00	0.00	0.00	0.00
92	टोरेंट पावर Torrent Power		0.00	0.00	0.00	0.00
93	मारुती स्टीन कोल पावर Maruti Clean Coal Power		8.85	0.00	3.15	0.92
94	झाबुआ पावर Jhabua Power		7.77	0.00	5.56	0.00
95	विंध्याचल स्टेज-1 Vindhyachal stg-1		0.00	0.00	0.00	0.00
96	विंध्याचल स्टेज-2 Vindhyachal stg-2		0.00	0.00	0.00	0.00
97	विंध्याचल स्टेज-3 Vindhyachal stg-3		0.00	0.00	0.00	0.00
98	विंध्याचल स्टेज-4 Vindhyachal stg-4		0.00	0.00	0.00	0.00
99	विंध्याचल स्टेज-5 Vindhyachal stg-5		0.00	0.00	0.00	0.00
100	मौदा स्टेज-1 Mouda Stg-1		0.00	0.00	0.00	0.00
101	सिपत स्टेज-1 Sipat Stg-1		0.00	0.00	0.00	0.00
102	सिपत स्टेज-2 Sipat Stg-2		0.00	0.00	0.00	0.00
103	सासन Sasan UMPP		0.00	0.00	16.97	0.00
104	भिलाई एनर्जी लिमिटेड NSPCL Bhilai		0.00	0.00	0.00	0.00
105	कोरबा स्टेज-3 Korba Stg 3		0.00	0.00	0.00	0.00
106	टीआरएन एनर्जी TRN Energy		0.00	0.00	30.95	0.00
107	गंधार Gandhar		0.00	0.00	0.00	0.82
108	कोरबा Korba		0.00	0.00	0.00	0.00
109	आर के एम पावर RKM Power		11.76	0.00	44.62	0.00
110	कावास Kawas		0.00	0.00	0.00	0.35
111	मौदा स्टेज-2 Mouda Stg-2		0.00	0.00	0.00	0.00
112	एस के एस पावर SKS Power		57.76	0.00	20.92	2.15
113	एन टी पि सी शोलापुर NTPC Sholapur		0.00	0.00	0.00	0.00
114	एन टी पि सी गदवारा NTPC Gadawara		0.00	0.00	0.00	0.03
115	एन टी पि सी लारा NTPC Lara		0.00	0.00	0.00	0.00
116	रायपुर एनर्जी Raipur Energen		138.20	0.00	8.21	0.00
117	आर्सेलर मितल ArcelorMittal Nippon steel (ESIL)		0.00	44.08	0.00	18.84
118	खरगोन Khargone STPP		0.00	0.00	0.00	0.00
119	कोस्टल गुजरात पावर लिमिटेड Coastal Gujarat Power Limited		0.00	0.00	1.35	0.00
120	कंटीन्यूम पावर ट्रेडिंग Continuum Power Trading (TN) Private Limited		5.38	0.00	1.30	0.00
121	ऑस्ट्रो एनर्जी प्राइवेट लिमिटेड Ostro Energy Private Limited (OEPL)		0.00	0.00	0.00	0.00
122	दामन डीयू/दादरा और नगर हवेली Daman & Diu/Dadar and Nagar Haveli		0.00	125.43	4.13	24.93
123	अदानी विंड एनर्जी Adani Wind Energy Kutchh Five Limited		0.00	0.00	0.00	0.00
124	आर जी पि पि एल RGPEL		0.00	0.13	0.00	0.73
125	Kakrapar Atomic Power Station काकरपर अटॉमिक पावर स्टेशन		0.00	0.00	140.34	0.00
126	BALCO बालको		0.00	9.84	0.00	12.19
127	अदानी विंड एनर्जी कच कोर लिमिटेड नखटरना ADANI WIND ENERGY KUTCHH FOUR Ltd. Nakhatrana		28.65	0.00	0.53	0.00
128	एनटीपीसी ज़नोर गंधार जीपीएस NTPC Jhanor Gandhar GPS RLNG		2.22	0.00	2.27	0.00
129	एनटीपीसी कावास गंधार NTPC Kawas GPS RLNG		2.50	0.00	2.79	0.00
130	रत्नागिरी गैस और पावर प्राइवेट लिमिटेड Ratnagiri Gas and Power Private Limited-LTRLNG		6.06	0.00	2.49	0.00
131	विंड फ़ाव्ड एनर्जी लिमिटेड WIND FIVE RENEGERGY LIMITED		15.81	0.00	0.00	0.00
132	एनटीपीसी ज़नोर गंधार जीपीएस कांम गैस NTPC Jhanor Gandhar GPS COMGAS		0.00	0.00	0.00	0.00
133	धारीवाल एस टी डू DHARIWAL STU OTH		1.85	0.00	0.00	0.00
134	धारीवाल आइ एस टी एस Dharawal ISTS		2.39	0.00	0.00	0.00
135	इनोक्स ग्रीन एनर्जी सर्विसेस लिमिटेड INOX GREEN ENERGY SERVICES LIMITED		3.21	0.00	0.33	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एच पी.एक्स.आई.एस.) POWER MARKET INFORMATION (Source IEX & PXIL) पावर एक्स्चेंज के माध्यम से विनिमय - माह- मई 2023 EXCHANGES THROUGH POWER EXCHANGES - MAY 2023								
क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (पि.यू. मे) Through Power Exchange in MU					
			Integrated Day Ahead Market (I-DAM)		Real Time Market (RTM)		Total (I-DAM+RTM)	
			विक्रय Sale	क्रय Purchase	विक्रय Sale	क्रय Purchase	विक्रय Sale	क्रय Purchase
136	आंध्र प्रदेश Andhra Pradesh	पश्चिमी क्षेत्र SR	34.28	317.93	24.96	176.83	59.24	494.77
137	कर्नाटक Karnataka		61.96	43.74	46.11	100.77	108.07	144.51
138	केरल Kerala		3.25	68.11	14.18	32.01	17.43	100.12
139	तमिलनाडु Tamilnadu		46.52	212.30	11.21	144.73	57.73	357.03
140	पोंडिचेरी Pondicherry		28.09	0.00	11.33	0.06	39.42	0.06
141	गोवा एस और गोa SR		0.00	17.04	0.00	1.30	0.00	18.34
142	तेलंगाना TELANGANA		216.76	143.43	125.20	198.58	341.97	342.01
143	कोस्टल एनर्जेन Costal Energen		16.99	0.00	0.11	0.00	17.09	0.00
144	आई एल और एफ एस IL&FS		15.71	0.00	3.32	0.00	19.03	0.00
145	सिंहद्री स्टेज -2 Simhadri Stg-2		0.00	0.00	0.00	0.00	0.00	0.00
146	एनएलसी इंडिया स्टेशन 1 विस्तार NLC India Station I Expansion		0.00	0.00	0.00	0.00	0.00	0.00
147	एन एल सी स्टेज-1 NLC TPS-II Stg-1		0.00	0.00	0.00	0.00	0.00	0.00
148	एन एल सी स्टेज-2 NLC TPS-II Stg-2		0.00	0.00	0.00	0.00	0.00	0.00
149	रामगुंडम स्टेज-1 Ramagundam Stg-1		0.00	0.00	0.00	0.00	0.00	0.00
150	तलचर स्टेज -2 Talcher Stg-2		0.00	0.00	0.00	0.00	0.00	0.00
151	रामगुंडम स्टेज-3 Ramagundam Stg-3		0.00	0.00	0.00	0.00	0.00	0.00
152	सेम्बकोर्प गायत्री Sembcorp Gayatri		25.61	0.00	7.48	0.00	33.09	0.00
153	वल्लूर Vallur		0.00	0.00	0.00	0.00	0.00	0.00
154	कुदगी NTPC Kudgi		0.00	0.00	0.00	0.00	0.00	0.00
155	सिंहद्री स्टेज -1 Simhadri Stg-1		0.00	0.00	0.00	0.00	0.00	0.00
156	एन एल सी टी पी एस -11 एक्सपन NLC TPS-II Expn		0.00	0.00	0.00	0.00	0.00	0.00
157	एनटीपीएस NTPL		0.00	0.00	4.97	0.00	4.97	0.00
158	नयवेली न्यू थर्मल पावर प्रोजेक्ट Neyveli New Thermal Power Project		0.00	0.00	0.00	0.00	0.00	0.00
159	रामगुंडम फ्लोटिंग सोलर पी वी स्टेशन Ramagundam Floating Solar PV Station		8.71	0.00	0.00	0.00	8.71	0.00
160	सिंहद्री फ्लोटिंग सोलर Simhadri Floating solar		2.06	0.00	0.00	0.00	2.06	0.00
161	सिंहद्री एक्सप्रेसवी 15 एसवी प्रोजेक्ट Simhadri FSP 15 MW Project		3.09	0.00	0.00	0.00	3.09	0.00
162	सेम्बकोर्प एनर्जी इंडिया लिमिटेड Sembcorp energy india limited		13.53	0.00	6.04	0.00	19.56	0.00
163	जे एस डब्ल्यू रिनो एनर्जी टू लिमिटेड JSW RENEW ENERGY TWO LIMITED		0.00	0.00	0.00	0.00	0.00	0.00
164	Ostro Kannada Power Private Limited ओस्ट्रो कन्नड़ पावर प्राइवेट लिमिटेड		14.06	0.00	1.22	0.00	15.28	0.00
165	Simhapuri Energy Limited सिमहापुरी एनर्जी लिमिटेड		3.71	0.00	3.41	0.26	7.11	0.26
166	पश्चिम बंगाल West Bengal	पूर्वी क्षेत्र ER	6.77	498.92	106.22	274.02	112.99	772.94
167	ओडिशा Odisha		40.72	25.52	72.58	105.65	113.30	131.18
168	बिहार Bihar		214.64	2.47	231.65	9.23	446.28	11.70
169	झारखंड Jharkhand		9.74	92.68	18.37	42.05	28.11	134.73
170	सिक्किम Sikkim		14.94	0.00	4.77	5.33	19.71	5.33
171	दामोदर घाटी परियोजना DVC		18.02	18.79	3.26	19.82	21.27	38.61
172	मैथन पावर लिमिटेड Maithon P. Ltd		0.00	0.00	0.00	0.00	0.00	0.00
173	आधुनिक पा. लिमिटेड Adhunik P.Ltd		1.09	0.00	1.08	0.00	2.16	0.00
174	चुजाचेन Chuzachen HEP		5.72	0.00	0.75	0.00	6.47	0.00
175	जीएमआर कामलंगा GMR Kamalanga		0.43	0.00	0.09	0.00	0.52	0.00
176	जिंदल आई पी टी एल JPTL		45.52	0.00	2.83	0.00	48.34	0.00
177	जोरथंग Jorethang		0.00	0.00	0.60	0.00	0.60	0.00
178	फरक्का-I Farakka-I		0.00	0.00	0.00	0.00	0.00	0.00
179	बाढ़-II Barh Stage-II		0.00	0.00	0.16	0.00	0.16	0.00
180	कहलगाँव-II Kahalgaon Stage-II		0.00	0.00	0.00	0.00	0.00	0.00
181	फरक्का Farakka		0.00	0.00	0.00	0.00	0.00	0.00
182	कहलगाँव Kahalgaon		0.00	0.00	0.00	0.00	0.00	0.00
183	तालचर Talcher		0.00	0.00	0.00	0.00	0.00	0.00
184	तीस्ता-III Teesta-III		87.57	0.00	34.66	0.00	122.23	0.00
185	दिक्चु Dikchu HEP		5.66	0.00	9.03	0.00	14.70	0.00
186	ताशिदिंग Tashiding HEP		0.00	0.00	0.01	0.00	0.01	0.00
187	केबीएनएनएल KBUNL		0.00	0.00	0.00	0.00	0.00	0.00
188	दर्रापल्ली Darlipalli		0.00	0.00	0.00	0.00	0.00	0.00
189	नबीनगर NPGC Nabhinagar		0.00	0.00	0.00	0.00	0.00	0.00
190	नेपाल विद्युत प्राधिकरण Nepal Electricity Authority		0.60	139.20	0.00	0.00	0.60	139.20
191	Barh STPS Stage-I बाढ़ एसटीपीएस स्टेज-1		0.00	0.00	0.00	0.00	0.00	0.00
192	NTPC North Karanpura STPS नॉर्थ करनपुरा		0.00	0.00	0.00	0.00	0.00	0.00
193	Druk Green Power Corporation Limited-Bhutan ड्रुक ग्रीन पावर कॉर्पोरेशन लिमिटेड-भूटान		0.00	0.00	0.00	0.00	0.00	0.00
194	NTPC BARH Unit 2 एनटीपीसी बाढ़ 1		0.00	0.00	26.03	0.00	26.03	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एच पी.एक्स.आई.एस.) POWER MARKET INFORMATION (Source IEX & PXIL) पावर एक्स्चेंज के माध्यम से विनिमय - माह: मई 2023 EXCHANGES THROUGH POWER EXCHANGES - MAY 2023								
क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (पि.यु. मे) Through Power Exchange in MU					
			Integrated Day Ahead Market (I-DAM)		Real Time Market (RTM)		Total (I-DAM+RTM)	
			विक्रय Sale	क्रय Purchase	विक्रय Sale	क्रय Purchase	विक्रय Sale	क्रय Purchase
195	अरुणाचल प्रदेश Arunachal Pradesh	पूर्वोत्तर क्षेत्र NER	5.95	1.52	1.41	0.71	7.36	2.23
196	असम Assam		26.86	93.30	17.55	89.47	44.41	182.77
197	मणिपुर Manipur		0.00	0.00	4.41	6.66	4.41	6.66
198	मेघालय Meghalaya		0.29	26.14	0.19	14.56	0.48	40.70
199	मिज़ोरम Mizoram		7.69	0.00	0.00	0.00	7.69	0.00
200	नागालैंड Nagaland		0.48	0.00	0.34	0.00	0.82	0.00
201	त्रिपुरा Tripura		0.00	7.55	3.11	30.03	3.11	37.58
202	अगरतला जीटीपीपी Agartala GTPP_AGO		0.00	0.00	0.00	0.00	0.00	0.00
203	असम जीबीपीपी Assam GBPP_KTO		0.00	0.00	0.27	0.00	0.27	0.00
204	पलताना Palatana		10.90	0.00	12.00	0.00	22.90	0.00
205	Doyang HEP दोंयांग हेप		0.00	0.00	0.00	0.00	0.00	0.00
206	बोंगाईगाँव Bongaigaon TPP		0.38	0.00	0.00	0.00	0.38	0.00
207	कामेंग Kameng HEP		1.06	0.00	17.09	0.00	18.15	0.00
			4200	4200	2426	2426	6626	6626

19. INFORMATION ABOUT RENEWABLE ENERGY
CERTIFICATE MECHANISM

MONTH : MAY 2023

RE Source & Unit wise break up (01.05.2023-31.05.2023)

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	1	1	1	1
2	Urban or Municipal Waste	0	0	0	0
3	Solar Thermal	0	0	0	0
4	Solar PV	50	1	14	1
5	Small Hydro	29	5	22	2
6	Others	0	0	0	0
7	Geothermal	0	0	0	0
8	Biomass	5	1	0	0
9	Bio-fuel cogeneration	0	0	0	0
	Total	85	8	37	4

RECs Issued (01.05.2023-31.05.2023)

Sr.No.	Non Solar	Solar	Total
1	364324	141435	505759

Redemption of REC (01.05.2023-31.05.2023)

Sr.No.	Non Solar	Solar	Total
1	190225	44486	234711

19. INFORMATION ABOUT RENEWABLE ENERGY
CERTIFICATE MECHANISM

MONTH : MAY 2023

RE Source & Unit wise break up (Apr'23-May'23)

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	1	1	102	2
2	Urban or Municipal Waste	0	0	0	0
3	Solar Thermal	0	0	0	0
4	Solar PV	51	2	14	1
5	Small Hydro	29	5	22	2
6	Others	0	0	0	0
7	Geothermal	0	0	0	0
8	Biomass	5	1	0	0
9	Bio-fuel cogeneration	4	1	4	1
	Total	90	10	142	6

RECs Issued (Apr'23-May'23)

Sr.No.	Non Solar	Solar	Total
1	523497	240496	763993

Redemption of REC (Apr'23-May'23)

Sr.No.	Non Solar	Solar	Total
1	478623	132220	610843

19. INFORMATION ABOUT RENEWABLE ENERGY
CERTIFICATE MECHANISM

MONTH : MAY 2023

RE Source & Unit wise break up Since Inception to May'23

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	2759	510	2604	511
2	Urban or Municipal Waste	0	0	0	0
3	Solar Thermal	0	0	0	0
4	Solar PV	1320	494	1199	466
5	Small Hydro	673	38	678	37
6	Others	4	2	3	1
7	Geothermal	0	0	0	0
8	Biomass	402	37	373	34
9	Bio-fuel cogeneration	813	89	373	53
	Total	5971	1170	5230	1102

RECs Issued since Inception to May'23

Sr.No.	Non Solar	Solar	Total
1	88403637	12651234	101054871

Redemption of REC since Inception to May'23

Sr.No.	Non Solar	Solar	Total
1	68006808	11760608	79767416

REC Closing balance as on 31.05.2023

Sr.No.	Non Solar	Solar	Total
1	20396829	890626	21287455

20.Details of Grid Events during the Month of May 2023
Northern Region



Sl.No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (H:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GI-2	Uttar Pradesh	01-May-2023 16:59	01-May-2023 17:51	00:52	0	0	0.000	0.000	34436	37824	i) As reported, at 16:59 hrs, 400 KV Bara(UP)-Meja TPS(MUN) (UP) Ckt-1 tripped on B-N phase to earth fault, fault was in Z-1 from Bara(UP) end, distance was 0.598km from Bara(UP) end. As per DR, line tripped after unsuccessful A/R operation and fault current was approx. 17.9kA. ii) At the same time, 400 KV Bara(UP)-Meja TPS(MUN) (UP) Ckt-2 also tripped from Bara(UP) end only on B-N phase to earth fault. As per DR, fault was in Z-3 from Bara(UP) end, fault current was approx. 3.67kA. iii) As per PMU at Mainpur(PG), B-N phase to earth fault with unsuccessful A/R operation is observed. Fault clearance time was 80 ms. iv) As per SCADA, no load loss/generation loss is observed in UP control area.	1) 400 KV Bara(UP)-Meja TPS(MUN) (UP) Ckt-1 2) 400 KV Bara(UP)-Meja TPS(MUN) (UP) Ckt-2
2	GD-1	Rajasthan	01-May-2023 13:23	01-May-2023 13:41	00:18	1100	0	2.829	0.000	38877	40743	i) As per PMU at Ajmer(PG), at 13:23 hrs, B-N fault phase to ground is observed with fault clearance time of 80 msec. ii) As per SOE, no triggering incident (exact location of fault) identified. iii) After clearance of fault, a sudden rise in voltage from 796kV to 831kV was observed at 765kV Ajmer(PG). iv) As reported, during the same time, 765 KV Ajmer(PG)-Phagi(RS) (PAPT) Ckt-1, 765 KV Fatehgarh, II (PG)-Bhadla(PG) (FBTL) Ckt-1 and 765 KV Ajmer-Bhadla, 2 (PG) Ckt-1 tripped due to over-voltage. v) As per DR, 765 KV Ajmer(PG)-Phagi(RS) (PAPT) Ckt-1 and 765 KV Fatehgarh, II (PG)-Bhadla(PG) (FBTL) Ckt-1 tripped on over-voltage stage-1 operation. 765 KV Ajmer-Bhadla, 2 (PG) Ckt-1 tripped on DT received from Bhadla2(PG) end. vi) During the fault, drop in generation of almost all the RE plants pooled at 765kV Fatehgarh2(PG), Bhadla2(PG), Bhadla2(PG) & Bikaner(PG) is observed. Generation at few of the RE station revived back with the clearance of fault but at some stations partial or no recovery is observed. PMU plots of the MW/MVar and phase voltages of RE plants are attached for the reference. vii) As per SCADA, total NR solar generation drop of approx. 1100MW in Rajasthan RE complex is observed. Solar generation was restored within 2 minutes. viii) As per SCADA, change of approx. 890MW is observed in NR demand.	1) 765 KV Ajmer(PG)-Phagi(RS) (PAPT) Ckt-1 2) 765 KV Fatehgarh, II (PG)-Bhadla(PG) (FBTL) Ckt-1 3) 765 KV Ajmer-Bhadla, 2 (PG) Ckt-1
3	GI-2	Rajasthan	04-May-2023 09:41	04-May-2023 12:31	02:50	0	185	0.000	0.421	41778	43943	i) 400/220kV Ratangarh(Raj) has double main & transfer bus scheme at 220kV side. ii) As reported at 09:41 hrs, R-ph bus jumper of isolator of 220 KV Ratangarh-Badnu (Raj) Ckt broke and created phase to earth bus fault. iii) On this fault, bus bar protection of 220kV Bus-8 operated which led to the tripping of all the elements connected at 220kV Bus-8 at Ratanagrh(Raj). 400/220 KV 315 MVA ICT 2 at Ratangarh(RS) and 220kV feeders to Sikar(PG)-I & II, Ratangarh-I, Khethi-I and Badnu tripped on the bus bar protection operation. iv) As per DR of tripped elements at Ratangarh end, R-N phase to earth fault with delayed clearance in ~240msec is observed, elements tripped on LBB protection operation. v) As per PMU at Sikar(PG), phase to earth fault with delayed clearance in 240msec is observed. vi) As per SCADA, change in load of approx. 185MW is observed in Rajasthan control area.	1) 400/220 KV 315 MVA ICT 2 at Ratangarh(RS) 2) 220 KV Ratangarh(RS)-Sikar(PG) (PG) Ckt-1 3) 220 KV Ratangarh(RS)-Sikar(PG) (PG) Ckt-2 4) 220 KV Ratangarh-Badnu (Raj) Ckt 5) 220 KV Ratangarh-Ratangarh220 (Raj) Ckt-1 6) 220 KV Ratangarh-Khethi (Raj) Ckt-1 7) 220 KV Ratangarh-Sridungargarh (Raj) Ckt-1
4	GI-2	Rajasthan	05-May-2023 12:26	05-May-2023 14:20	01:54	305	0	0.641	0.000	47560	49783	i) During antecedent condition, emergency shutdown of 404 main Bay of 400/220kV 500MVA ICT-7 at Bhadla2(PG) was taken for attending CT emergency alarm. During this work, bus bar protection mal-operated at 400kV Bus 1 at Bhadla2(PG) and Bus-1 became dead. ii) As per SCADA data and CB status, tie CB at 400kV side of 765/400kV 1500MVA ICT-3 and tie CB at 400kV side of 400/220kV 500MVA ICT-6 at Bhadla2(PG) were already in open condition. Hence due to bus bar protection operation as main CB connected to bus-1 opened, 765/400kV 1500MVA ICT-3 and 400/220kV 500MVA ICT-6 at Bhadla2(PG) tripped. Along with this, 400/220kV 500MVA ICT-7 at Bhadla2(PG) also tripped during the same time due to opening of Tie CB (Main CB was already open). iii) Total generation of 220kV Avada Sunrays (ASEPL) was feeding through 400/200kV 500MVA ICT-6 and 7 at Bhadla2(PG) only. Hence tripping of ICT-6 and 7 led to tripping of 220 KV Bhadla2(PG)-ASEPL(P) ckt which eventually resulted in generation loss of 220kV Avada Sunrays (ASEPL). iv) As per PMU at 400kV Bhadla2(PG), no fault is observed in the system. v) As per SCADA, generation loss of approx. 305MW is observed observed in NR Solar generation.	1) 765/400kV 1500MVA ICT-3 at Bhadla2(PG) 2) 400/220kV 500MVA ICT-6 at Bhadla2(PG) 3) 400/220kV 500MVA ICT-7 at Bhadla2(PG) 4) 400kV Bus 1 at Bhadla2(PG) 5) 220 KV Bhadla2(PG) –ASEPL(P) ckt 6) 220/33kV 150MVA ICT-1 at ASEPL(P) 7) 220/33kV 150MVA ICT-2 at ASEPL(P) 8) 220/33kV 150MVA ICT-3 at ASEPL(P)
5	GI-2	Rajasthan	05-May-2023 18:13	05-May-2023 21:05	02:52	0	65	0.000	0.146	36369	44548	i) 400/220kV Heerapura(Raj) has one and half breaker bus scheme. ii) As reported at 18:13 hrs, R-ph CT at 400kV side of 400/220kV 315MVA ICT-4 at Heerapura(Raj) burst followed by damage of R-ph pole of its CB. iii) On this fault, bus bar protection of 400kV Bus-1 at Heerapura(Raj) operated led to the tripping of 400kV Bus 1 at Heerapura(RS). At the same time, 400 KV Basi(PG)-Heerapura(RS) (PG) Ckt-1 & 2, 400/220 KV 250 MVA ICT 2 & 3 and 315MVA ICT 4 at Heerapura(RS) also tripped. iv) As per communication with Heerapura S/s, 400 KV Basi(PG)-Heerapura(RS) (PG) Ckt-1 remained charged from Heerapura end via Tie CB, however, it tripped from Basi end. In case of 400 KV Basi(PG)-Heerapura(RS) (PG) Ckt-2, 400/220kV 250MVA ICT 2&3 at Heerapura, Tie CB at Heerapura end also opened. v) As per PMU at Basi(PG), multiple R-N fault, first at 18:12:58hrs which cleared within 100msec followed by another R-N fault with delayed clearance of 280msec is observed. vi) As per SCADA, change in load of approx. 65MW is observed in Rajasthan control area. vii) As informed by SLDC-Rajasthan, relays at Heerapura(Raj) are of electromagnetic nature. Hence, disturbance recorder files are not available.	1) 400kV Bus 1 at Heerapura(RS) 2) 400 KV Basi(PG)-Heerapura(RS) (PG) Ckt-1 3) 400 KV Basi(PG)-Heerapura(RS) (PG) Ckt-2 4) 400/220 KV 250 MVA ICT 2 at Heerapura(RS) 5) 400/220 KV 250 MVA ICT 3 at Heerapura(RS) 6) 400/220 KV 315 MVA ICT 4 at Heerapura(RS)
6	GI-1	Jammu & Kashmir	05-May-2023 14:58	05-May-2023 15:57	00:59	0	360	0.000	0.743	46362	48474	i) During antecedent condition, active power loading of 220 KV MirBazar(PDD)-NewWanpoh(PG) (PDD JK) Ckt-1 & 2 were 178MW and 177MW respectively. ii) As reported, at 14:58hrs, 220 KV MirBazar(PDD)-NewWanpoh(PG) (PDD JK) Ckt-1 tripped on Y-B phase to phase fault with distance of 1.2 km (22.9%) from NewWanpoh(PG) end. As per telephonic conversation with MirBazar S/s, 220 KV MirBazar(PDD)-NewWanpoh(PG) (PDD JK) Ckt-1 tripped as a tree was leaning on the circuit. iii) As per DR at NewWanpoh(PG) end of 220 KV MirBazar(PDD)-NewWanpoh(PG) (PDD JK) Ckt-1, zone-1 distance protection operated with fault current of 6.7kA and 6.3kA in Y and B-phase respectively. iv) Due to tripping of 220 KV MirBazar(PDD)-NewWanpoh(PG) (PDD JK) Ckt-1, loading on 220 KV MirBazar(PDD)-NewWanpoh(PG) (PDD JK) Ckt-2 increased and line CB at 220kV MirBazar(PDD) end of 220 KV MirBazar(PDD)-NewWanpoh(PG) (PDD JK) Ckt-2 opened due to over-loading, but line remain charged from NewWanpoh(PG) end. v) As per PMU at Kshempur(PG), Y-B phase to phase fault is observed in system with fault clearance time of 80 ms. vi) As per SCADA, load loss of approx. 360MW occurred in J&K control area.	1) 220 KV Mir Bazar(PDD)-NewWanpoh(PG) (PDD JK) Ckt-1 2) 220 KV Mir Bazar(PDD)-NewWanpoh(PG) (PDD JK) Ckt-2
7	GI-1	Rajasthan	08-May-2023 19:11	08-May-2023 22:32	03:21	230	220	0.519	0.409	44284	53815	i) 220/132kV Sakatpura(Raj) S/s have double main & transfer bus scheme. Station is connected with 220kV Kota TPS via 220kV KTPS-Sakatpura ckt-1, 2, 3 & 4. ii) As reported at 19:11 hrs, R & Y ph CT at Sakatpura end of 220kV Sakatpura-Mandalgarh ckt burst and bus fault occurred. iii) As per information received, bus bar protection is not healthy at 220kV Sakatpura S/s and Z-4(reverse) distance protection time delay setting is kept as 160msec. iv) On this bus fault, 220kV line from RAPP_A & Anta(NTPC) tripped in Z-4 distance protection operation at Sakatpura end and 220kV KTPS-Sakatpura ckt-1, 2, 3&4 tripped on distance protection in Z-1 from KTPS end. 220kV KTPS-Kota(PG) ckt-1 also tripped from KTPS end. v) At the same time, 210MW Unit-4 at Kota TPS tripped followed by tripping of 210MW Unit-3 & 5 at 19:15 hrs & 19:21 hrs respectively due to tripping of auxiliary components (boiler, pulveriser etc.) vi) As per PMU at Kota(PG), R-N fault converted into R-Y-N fault with delayed clearance of 240msec is observed. vii) As per SCADA, change in load of approx. 210MW in Rajasthan control area and loss in generation of approx. 230MW at 19:11hrs due to tripping of 210MW unit-4 at KTPS. Further at 19:15hrs, 210MW unit-3 at KTPS tripped followed by tripping of 210MW unit-5 at KTPS 19:21hrs is observed.	1) 220kV Sakatpura-Mandalgarh ckt 2) 220 KV Kota(PG)-KTPS(RVUN) (RS) Ckt-1 3) 220 KV Anta(NT)-Sakatpura(RS) (RS) Ckt-1 4) 220 KV RAPP_A(NTP)-Sakatpura(RS) (RS) Ckt-2 5) 220kV KTPS-Sakatpura ckt-1 6) 220kV KTPS-Sakatpura ckt-2 7) 220kV KTPS-Sakatpura ckt-3 8) 220kV KTPS-Sakatpura ckt-4 9) 210MW Unit-3 at KTPS 10) 210MW Unit-4 at KTPS 11) 210MW Unit-5 at KTPS

20.Details of Grid Events during the Month of May 2023
Northern Region



Sl.No.	Category of Grid Event (GI 1or 2/ GD-1 to GD-5)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (H:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
						Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
8	GD-1	Rajasthan	09-May-2023 12:57	09-May-2023 13:22	00:25	1390	0	2.687	0.000	51736	56171	i) As reported, at 12:57 hrs, 220 KV Bhadia(PG)-ACME Solar(ACM) Ckt-1 tripped on R-N phase to ground fault. Fault distance was 3.3 km from Bhadia(PG) end. During patrolling, it was observed that a tree bush was touching R-phase of the line. ii) After clearance of fault, a sudden rise in voltage from 767kV to 823kV was observed at 765kV Fatehgarh2(PG). iii) Due to this, 765 KV Ajmer-Bhadia_2 (PG) Ckt-1, 765 KV Bhadia_2 (PG)-Fatehgarh_II(PG) (PFTL) Ckt-1 and 765 KV Fatehgarh_II(PG)-Bhadia(PG) (FRTL) Ckt-1 tripped on over-voltage protection operation. iv) As reported, during the same time, 220/33 KV 150 MVA ICT 1 & 2 at AzureMaplePSS SL_BHD_PG (APMPL) and 220/33 kv 150 MVA ICT 1 & 2 at AzurePSS41 SL_BHD_PG (APFOU) also tripped due to over-voltage protection operation. v) As per DR at Bhadia(PG) end of 220 KV Bhadia(PG)-ACME Solar(ACM) (ACME) Ckt-1 tripped on zone-1 distance protection operation on R-N phase to ground fault with fault current of 18kA from Bhadia(PG) end. Unsuccessful A/R operation is observed. vi) As per DR, 765 KV Ajmer-Bhadia_2 (PG) Ckt-1, 765 KV Bhadia_2 (PG)-Fatehgarh_II(PG) (PFTL) Ckt-1 and 765 KV Fatehgarh_II(PG)-Bhadia(PG) (FRTL) Ckt-1 tripped on over-voltage stage-1 operation. vii) During the fault, drop in generation of almost all the RE plants pooled at 765kV Fatehgarh2(PG), Bhadia(PG), Bhadia2(PG) & Bikaner(PG) is observed. Generation at few of the RE station revived back with the clearance of fault but at some stations partial or no recovery is observed. PMU plots of the MW/MVA and phase voltages of RE plants are attached for the reference. viii) As per SCADA, total NR solar generation drop of approx. 1390MW in Rajasthan RE complex is observed.	1) 765 KV Ajmer-Bhadia_2 (PG) Ckt-1 2) 765 KV Bhadia_2 (PG)-Fatehgarh_II(PG) (PFTL) Ckt-1 3) 765 KV Fatehgarh_II(PG)-Bhadia(PG) (FRTL) Ckt-1 4) 220 KV Bhadia(PG)-ACME Solar(ACM) (ACME) Ckt-1 5) 220/33 KV 150 MVA ICT 1 at AzureMaplePSS SL_BHD_PG (APMPL) 6) 220/33 KV 150 MVA ICT 2 at AzureMaplePSS SL_BHD_PG (APMPL) 7) 220/33 KV 150 MVA ICT 1 at AzurePSS41 SL_BHD_PG (APFOU) 8) 220/33 KV 150 MVA ICT 2 at AzurePSS41 SL_BHD_PG (APFOU)
9	GI-1	Rajasthan	09-May-2023 16:46	09-May-2023 20:22	03:36	170	0	0.359	0.000	47395	52613	i) During antecedent condition, 220 KV RAPS_A(NP)-Sakarpura(RS) (RS) Ckt-1, 220 KV RAPS_B(NP)-RAPS_A(NP) (RS) Ckt-1 and 200 MW RAPS-A - UNIT 2 were connected to 220KV Bus-2 at RAPS_A(NP) and rest of the elements were connected to 220KV Bus-1 at RAPS_A(NP). 200 MW RAPS-A - UNIT 2 was generating approx. 170MW. ii) As reported, at 16:46hrs, 220 KV RAPS_A(NP)-Sakarpura(RS) (RS) Ckt-1 tripped on B-N phase to earth fault (Zone-1 distance protection operated at Sakarpura end). Fault distance was 20.97 km and fault current 6.93 kA from Sakarpura(RS). iii) However, RAPS_A(NP) end CB got stuck, hence LBB operated. Due to this, 220 KV RAPS_B(NP)-RAPS_A(NP) (RS) Ckt-1 and 200 MW RAPS-A - UNIT 2 also tripped and 220KV Bus-2 at RAPS_A(NP) became dead. iv) As per PMU at RAPS_A(NP), phase to ground fault is observed in system with delayed fault clearance time of 280 ms. v) As per SCADA, change in generation of approx. 170 MW is observed at RAPS_A(NP).	1) 220 KV RAPS_A(NP)-Sakarpura(RS) (RS) Ckt-1 2) 220 KV RAPS_B(NP)-RAPS_A(NP) (RS) Ckt-1 3) 200 MW RAPS-A - UNIT 2 4) 220KV Bus-2 at RAPS_A(NP)
10	GI-2	Haryana	10-May-2023 22:24	10-May-2023 23:27	01:03	0	0	0.000	0.000	46977	58783	i) During antecedent condition, 800 KV HVDC Kurukshetra(PG) Pole-1, 2, 3 & 4 were carrying 494 MW, 483 MW, 469 MW and 481 MW respectively from Champa to Kurukshetra. ii) As reported at 22:24hrs, "Pole 4 sub-rack 3 Data Invalid" alarm appeared in Pole 4 resulting in Pole 4 lane changeover from lane 2 to lane 1. 800 KV HVDC Kurukshetra(PG) Pole-2 & 4 blocked due to control maloperation of newly installed V6 software after lane changeover at Kurukshetra end. iii) As reported, sequence of events are as follows: # 22:24:49.108 - Pole 4 Subrack 3 D/MR latched Kurukshetra # 22:24:49.108 - Pole 4 lane changed from L2 to L1 due to D/MR in P4 Subrack 3 at Kurukshetra. # 22:24:49.930 - EAPR Active got high in P4 & P3. ("Master Control Power Control moniEAPRActive_PowerLimit" alarm appeared at both ends in Pole 2 & Pole 4) # 22:24:50.340 - Valves of Pole 4 at Champa blocked # 22:24:50.864- Pole 4 at Kurukshetra blocked followed by Power limit alarm in Pole 2 & Pole 4 although minimum filter required were in service. Power limit alarm led to power ramp down in Pole 4 only and Pole 4 got blocked at 22:24:50 hrs. (The reason for ramp down of Power in Pole 4 is not clear.) # 22:24:55.909 - CAT A2 from other end received at Kurukshetra in Pole 4 which is a clear control maloperation as blocked Pole shouldn't initiate any protective sequence after blocking. # 22:24:56.151 - Again CATS from other end received at Kurukshetra in Pole 4 which is again control maloperation as Pole shouldn't initiate any protective sequence after blocking. # 22:24:56.165 - As CAT B sequence trip both parallel Poles, Pole 2 blocked on CAT B initiated by Pole 4 from Champa end. # Complete power was compensated by P1 & P3. iv) As per PMU at Kurukshetra(PG), no fault is observed in the system, but fluctuation in voltage is observed. v) As per SCADA, no load loss is observed in Haryana control area.	1) 800 KV HVDC Kurukshetra(PG) Pole-02 2) 800 KV HVDC Kurukshetra(PG) Pole-04
11	GD-1	Haryana	10-May-2023 16:22	10-May-2023 18:24	02:02	0	130	0.000	0.244	48099	53343	i) As reported, at 16:22hrs, a fire incident is observed in the field near to 220/132KV Mohana(HS) S/s. B-phase of float T/F burnt and AC/DC changeover card got damaged which led to defect in 220V Main DC Charger-1. Due to this, 220 KV Mohana(HV)-Sonitap(PG) (HVPNL) Ckt-1 and 2 tripped. ii) At the same time, 220KV Mohana(HV)-Sampla(HV) Ckt-1 & 2 and 220KV Mohana(HV)-Samalkha(HV) Ckt-1 & 2 also tripped due to non-availability of the DC supply with the operation of Capacitor Trip Device (CTD) in the circuit breakers. Hence, 220/132KV Mohana(HS) S/s became dead. iii) After identifying the fault in 220V DC Charger-1, the complete DC load was put on alternate 220V DC Charger-2. iv) At 16:45 hrs, 220KV Mohana(HV)-Sampla(HV) Ckt-2 was charged and supply to 220KV Mohana was restored. v) As reported by Mohana S/s, no DR was recorded in distance protection relay at 220KV Mohana(HS) end of 220 KV Mohana(HV)-Sonitap(PG) (HVPNL) Ckt-1 and 2 due to DC supply fail. vi) As per DR at Sonitap(PG) end of 220 KV Mohana(HV)-Sonitap(PG) (HVPNL) Ckt-1 & 2, zone-2 distance protection operated at Sonitap end. Fault current was approx. 6kA and 5kA in Y and B-phase in both the circuits. vii) As per PMU at Sonitap(PG), B-N phase to ground fault converted to Y-B-N double phase to ground fault is observed in system with delayed fault clearance time of 360 ms. viii) As per SCADA, load loss of approx. 130MW occurred in Haryana control area.	1) 220 KV Mohana(HV)-Sonitap(PG) (HVPNL) Ckt-1 2) 220 KV Mohana(HV)-Sonitap(PG) (HVPNL) Ckt-2 3) 220KV Mohana(HV)-Sampla(HV) Ckt-1 4) 220KV Mohana(HV)-Sampla(HV) Ckt-2 5) 220KV Mohana(HV)-Samalkha(HV) Ckt-1 6) 220KV Mohana(HV)-Samalkha(HV) Ckt-2
12	GI-1	Rajasthan	11-May-2023 13:37	11-May-2023 13:50	00:13	940	0	1.880	0.000	50003	56300	i) Total generation of 220KV Azure Maple evacuates through 220KV Bhadia(PG)- AzureMaplePSS SL_BHD_PG (APMPL) ckt which is connected to 220/33 kv 150 MVA ICT 1 & 2 at AzureMaplePSS SL_BHD_PG (APMPL). ii) As per PMU at 400KV Bhadia(PG), R-Y phase to phase fault is observed with fault clearing time of 80 ms. Voltage dip of approx. 33.8kV(L-L) is observed at Bhadia(PG). iii) After fault clearance, voltage increased upto 441.4kV(L-L) (1.1035 p.u.). Hence, over voltage (>1.1pu at 765kV & 400kV level at RE Pooling stations) scenario occurred immediately after the fault. iv) As reported by Azure Maple solar plant, at 13:37 hrs, 220/33 kv 150 MVA ICT 1 & 2 at AzureMaplePSS SL_BHD_PG (APMPL) tripped due to over voltage protection operation. v) As per SCADA, generation drop of approx. 940MW is observed in NR Solar generation. vi) As per PMU, due to significant dip in RE generation frequency dropped by 0.17Hz (from 49.95Hz to 49.78Hz). However frequency recovered to 49.98Hz within 1 minute. vii) Almost all the generation revived within 10 minutes except Azure maple which got revived at 13:50 hrs.	1) 220/33 KV 150 MVA ICT 1 at AzureMaplePSS SL_BHD_PG (APMPL) 2) 220/33 KV 150 MVA ICT 2 at AzureMaplePSS SL_BHD_PG (APMPL)
13	GI-1	Rajasthan	13-May-2023 22:04	13-May-2023 23:12	01:08	275	0	0.546	0.000	50400	62238	i) Total generation of 220KV AHEJAL PSS3, AHEJ3L PSS, and AHEJOL PSS were feeding through 220 KV Adani RenewPark_SL_FGARH_FRTL (AREPRL)-AHEJAL PSS 3 HB_FGARH_FRTL (AHEJAL) (AREPRL) Ckt, 220 KV Fatehgarh_II(PG)-AHEJ3L PSS HB_FGARH_PG (AHEJ3L) (AHEJ3L) Ckt and 220 KV Fatehgarh_II(PG)-AHEJOL PSS HB_FGARH_PG (AHEJOL) (AHEJOL) Ckt-1 & 2 respectively. ii) As reported, at 22:04 hrs, 220 KV Adani RenewPark_SL_FGARH_FRTL (AREPRL)-AHEJAL PSS 3 HB_FGARH_FRTL (AHEJAL) (AREPRL) Ckt tripped on Y-N phase to earth fault during very high wind condition. At the same time, 220 KV Fatehgarh_II(PG)-AHEJ3L PSS HB_FGARH_PG (AHEJ3L) (AHEJ3L) Ckt also tripped on B-N phase to earth fault (zone-1 from AHEJ3L end). iii) As reported, at 22:05 hrs, 220 KV Fatehgarh_II(PG)-AHEJOL PSS HB_FGARH_PG (AHEJOL) (AHEJOL) Ckt-1 tripped on B-N phase to earth fault (zone-1 from AHEJOL end). iv) As per PMU and SCADA SOE, the details of event is as follows: # At 22:04:06 hrs: 220 KV Adani RenewPark_SL_FGARH_FRTL (AREPRL)-AHEJAL PSS 3 HB_FGARH_FRTL (AHEJAL) (AREPRL) Ckt tripped. As per PMU, B-N phase to earth fault is observed with fault clearing time of 80 ms. As per PMU, generation loss of approx. 187 MW is observed at AWPSS3. # At 22:04:34 hrs: 220 KV Fatehgarh_II(PG)-AHEJ3L PSS HB_FGARH_PG (AHEJ3L) (AHEJ3L) Ckt tripped. As per PMU, R-N phase to earth fault is observed with fault clearing time of 80 ms. PMU data for generation at AHEJ3L is not available. # At 22:05:18 hrs: 220 KV Fatehgarh_II(PG)-AHEJOL PSS HB_FGARH_PG (AHEJOL) (AHEJOL) Ckt-1 tripped. As per PMU, B-N phase to earth fault is observed with fault clearing time of 120 ms. As per PMU, generation loss of approx. 30 MW is observed at AHEJOL PSS. # At 22:07:20 hrs: As per PMU, B-N phase to earth fault is observed with fault clearing time of 80 ms. v) As per SCADA, generation loss of approx. 275MW is observed in NR wind generation.	1) 220 KV Adani RenewPark_SL_FGARH_FRTL (AREPRL)-AHEJAL PSS 3 HB_FGARH_FRTL (AHEJAL) (AREPRL) Ckt 2) 220 KV Fatehgarh_II(PG)-AHEJ3L PSS HB_FGARH_PG (AHEJ3L) (AHEJ3L) Ckt 3) 220 KV Fatehgarh_II(PG)-AHEJOL PSS HB_FGARH_PG (AHEJOL) (AHEJOL) Ckt-1

20.Details of Grid Events during the Month of May 2023
Northern Region



Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (H:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
14	GD-2	Rajasthan	15-May-2023 11:51	15-May-2023 14:38	02:47	7120	1635	12.505	2.686	56939	60878	i) As reported, at 11:51:55 hrs, 765kV Bhadla-Bikaner ckt-1 tripped on Y-B phase to phase fault during inclement weather condition (wind/dust storm), fault distance was ~111.6km from Bikaner end (line length is ~169km). ii) On this fault during voltage dip, significant dip in RE generation observed. Voltage dipped up to 0.65pu (as per PMU at Fatehgarh2). iii) Due to significant dip in RE generation and de-loading of 765kV EHV lines (as RE generation failed to recover 90% of pre-fault active power within 1 sec and further Inverters tripping on OV, LVRT/HVRT Non-compliant), over voltage (>1.1pu at 765kV & 400kV level at RE Pooling stations) scenario triggered immediately after the fault that led to multiple element tripping in the RE complex. iv) As per PMU & SCADA, total RE generation drop/loss was approx.7120MW (~6410MW ISTS RE generation and ~710MW Rajasthan RE generation). Due to significant dip in RE generation frequency dropped by 0.58Hz (from 49.98Hz to 49.4Hz). v) As frequency hit 49.40Hz, total all India load relief of approx. 4016MW is observed on operation of UFR & df/dt. Load relief of approx. 1635MW observed in NR region (as per details received from states). Region wise summary of load relief along with state wise details of UFR & df/dt operation is attached in Annexure-II. vi) After the fault, following 765 & 400 kV lines in RE complex tripped on high voltage: 765kV Fatehgarh2-Bhadla ckt-1, 765kV Bhadla2-Bikaner ckt-1, 765kV Fatehgarh2-Bhadla2 ckt-1, 765kV Bhadla-Bikaner ckt-2, 400kV Fatehgarh1-Fatehgarh2 ckt-1, 400kV Bhadla-Bhadla2 ckt-1&2, 400kV Bhadla-Bhadla, Raj ckt-1&2, 400kV Bhadla, Raj-Merta ckt, 400kV Bhadla, Raj-Jodhpur ckt, 400kV Bhadla, Raj-Ramgarh ckt-1&2 vii) Multiple 220kV lines dedicated to RE stations also tripped on over voltage during same time. viii) Further at 12:08 hrs, 765kV Fatehgarh2-Bhadla2 ckt-1 was charged.	1) 765kV Bhadla-Bikaner ckt-1 2) 400kV Bikaner-Azures ckt 3) 400kV Fatehgarh1-Fatehgarh2 ckt-1 4) 400kV Bhadla-Bhadla2 ckt-1 5) 400kV Bhadla-Bhadla, Raj ckt-2 6) 765kV Fatehgarh2-Bhadla ckt-1 7) 400kV Bhadla-Bhadla2 ckt-2 8) 400kV Bhadla-Bhadla, Raj ckt-1 9) 765kV Bhadla2-Bikaner ckt-1 10) 765kV Ajmer-Phagi ckt-1 11) 765kV Fatehgarh2-Bhadla2 ckt-1 12) 765kV Bhadla-Bikaner ckt-2 13) 400kV Bhadla, Raj-Merta ckt 14) 400kV Bhadla, Raj-Jodhpur ckt 15) 400kV Bhadla, Raj-Ramgarh ckt-1 16) 400kV Bhadla, Raj-Ramgarh ckt-2
15	GD-1	Rajasthan	15-May-2023 12:16	15-May-2023 15:21	03:05	2700	0	5.321	0.000	50743	59684	i) At 12:16hrs, charging attempt of 765kV Bhadla-Bikaner ckt-2 was taken from Bhadla end however, line didn't hold and over voltage (>1.1pu at 765kV & 400kV level at RE Pooling stations) scenario occurred in RE complex. ii) On this over voltage following 765 & 400 kV lines in RE complex tripped: a. 765kV Bhadla-Fatehgarh2 ckt-2 b. 765kV Bhadla2-Fatehgarh2 ckt-1 c. 400kV Fatehgarh1-AFSP5 ckt-1 & 2 d. 400kV Bhadla2-Kolayat ckt iii) Multiple 220kV lines dedicated to RE stations also tripped on over voltage during same time. iv) With the tripping of 765kV Bhadla-Fatehgarh2 ckt-2 and 400kV Fatehgarh1-AFSP5 ckt-1 & 2, blackout of 765/400/220kV Bhadla (PG) & 400/220kV ADANI Fatehgarh Solar park occurred. v) As per PMU & SCADA, total RE generation drop/loss was approx. 2700MW. Due to dip in RE generation frequency dropped by 0.25Hz (from 49.88Hz to 49.63Hz).	1) 400kV Fatehgarh1-AFSP5 ckt-1 2) 400kV Fatehgarh1-AFSP5 ckt-2 3) 765kV Bhadla-Fatehgarh2 ckt-2 4) 400kV Bhadla2-Kolayat ckt 5) 765kV Bhadla2-Fatehgarh2 ckt-1
16	GI-1	Rajasthan	16-May-2023 15:13	16-May-2023 16:03	00:50	175	0	0.298	0.000	58682	63664	i) During antecedent condition, total generation of 220kV AHEJ3L was evacuating through 220kV Fatehgarh2(PG)-AHEJ3L ckt which was connected to 220/33/33 kV 150 MVA ICT 1 & 2 at AHEJ3L PSS HB_FGRAH_PG (AHEJ3L) carrying approx. 136MW and 148MW respectively. ii) As reported, at 15:13 hrs, 220/33/33 kV 150 MVA ICT 1 at AHEJ3L PSS HB_FGRAH_PG (AHEJ3L) tripped due to operation of transformer protection on LV WTI instrument failure. iii) As per DR/EL, "WTI_LV1_Alarm" is observed and cooling supply failed. iv) As per PMU at 400kV Fatehgarh2(PG), no fault is observed in the system. MW generation drop of approx. 155MW is observed as per PMU at AHEJ3L v) As per SCADA, generation drop of approx. 175MW is observed in NR Solar generation.	1) 220/33/33 kV 150 MVA ICT 1 at AHEJ3L PSS HB_FGRAH_PG (AHEJ3L)
17	GD-1	Haryana	16-May-2023 01:52	16-May-2023 04:23	02:31	0	300	0.000	0.547	43731	54888	i) As reported, at 01:52 hrs, Y-phase PT and R and Y phase breaker poles of 220 kV Ballabgarh(BB)-Badarpur(NT) (BB) Ckt-2 burst at Ballabgarh(BB) end. ii) This resulted in LBB protection operation and all the elements connected to Bus-1 and Bus-2 tripped and 220/66/23kV Ballabgarh(BB) S/s became dead. iii) As per DR of 220 kV Ballabgarh(BB)-Badarpur(NT) Ckt-1, zone-2 distance protection operated at Badarpur(NT) end (Y-B fault, fault current of approx. 6.9kA) and zone-4 distance protection operated at Ballabgarh(BB) end (R-Y-N fault, fault current of approx. 12kA in each phase followed by R-N fault, fault current of approx. 17kA). iv) As per DR of 220kV Bus 1 at Ballabgarh(BB), LBB protection operated (Y-N fault converted to 3-phase fault followed by R-N fault followed by R-Y-N fault were observed) v) As per PMU at Ballabgarh(BB), multiple faults (Y-N fault converted to 3-phase fault followed by R-N fault followed by R-Y-N fault) were observed in system with delayed fault clearing time of 1400 ms. vi) As per SCADA, load loss of approx. 300MW is observed in Haryana control area.	1) 220 kV Ballabgarh(BB)-Badarpur(NT) (BB) Ckt-1 2) 220 kV Ballabgarh(BB)-Badarpur(NT) (BB) Ckt-2 3) 220 kV Ballabgarh-Charkhi Dabri (BB) Ckt-1 4) 220 kV Ballabgarh-Samaypur (BB) Ckt-1 5) 220 kV Ballabgarh-Samaypur (BB) Ckt-2 6) 220 kV Ballabgarh-Samaypur (BB) Ckt-3 7) 220kV Bus 1 at Ballabgarh(BB) 8) 220kV Bus 2 at Ballabgarh(BB) 9) 220/66kV 100MVA ICT1 at Ballabgarh(BB) 10) 220/66kV 100MVA ICT2 at Ballabgarh(BB) 11) 220/66kV 100MVA ICT3 at Ballabgarh(BB)
18	GD-1	Delhi	17-May-2023 12:21	17-May-2023 13:26	01:05	145	500	0.246	0.780	58926	64110	i) As reported, at 12:05 hrs, 220kV Geeta Colony - South wazirabad (DTL) ckt-1 tripped on Y-N phase to earth fault, fault distance was ~3.3km(Z-1) from Geeta Colony end. During line patrolling heavy fire was found under the between tower no 349 to 350 in Jhuggies. R phase bottom conductor found napped and Y phase middle conductor found bulged of 220kV Geeta Colony - South wazirabad (DTL) ckt-1. ii) With the tripping of 220kV Geeta Colony - South wazirabad (DTL) ckt-1, MW loading of 220kV Geeta Colony - South wazirabad (DTL) ckt-2 increased to ~400MW. iii) Further at 12:21hrs, 220kV Geeta Colony - South wazirabad (DTL) ckt-2 tripped on B-N phase to earth fault. iv) With the tripping of 220kV Geeta Colony - South wazirabad (DTL) ckt-1 & 2, GT-2 and STG at Pragati(DTL) (generating approx. 94MW and 51MW respectively during antecedent condition) became islanded and collapsed. v) Complete load of Geeta Colony, IPONVERTIN, RPH and part load of Patparganj and Park street were affected. vi) As per PMU at Mandola(PG), B-N phase to earth fault with unsuccessful A/R is observed with delayed fault clearing time of 240 ms. vii) As per SCADA, load loss of approx. 500MW is observed in Delhi control area and loss of generation of approx. 145MW is observed.	1) 220kV Geeta Colony - South wazirabad (DTL) ckt-1 2) 220kV Geeta Colony - South wazirabad (DTL) ckt-2 3) GT-2 at Pragati(DTL) 4) STG at Pragati(DTL)
19	GD-1	Uttarakhand	17-May-2023 20:25	17-May-2023 21:00	00:35	0	160	0.000	0.258	53580	62112	i) As reported by SIDC Uttarakhand, increase in demand, low generation from hydro power plants of UJVN Ltd., outage of Dhakrani, Dhalpur and Kulhal Power house at 132 kV level in Dehradun area and fluctuations of generation from MB-I & II led to import of more power from Sherpur S/S of PGCL. ii) As per Bus-wise arrangement at Jhagra(UK), 220/132kV 160MVA ICT-2 at Jhagra(UK) and 220 kV Jhagra(UK)-Dehradun(PG) ckt (load on the ckt before tripping was 993 MW) were connected to Bus-A. 220/132kV 160MVA ICT-1 at Jhagra(UK) and 220 kV Jhagra-Vyasi ckt, 220 kV Jhagra-Khodri ckt and 220 Jhagra-IP Harrowala ckt were connected to Bus-B. Both 160 MVA transformers was running in parallel. iii) At 20:25hrs, 220/132kV 160MVA ICT-2 at Jhagra(UK) tripping on over-current protection operation. iv) Due to tripping of 220/132kV 160MVA ICT-2 at Jhagra(UK), entire load shifted to 220/132kV 160MVA ICT-1 at Jhagra(UK) and loaded this transformer up to 775 A resulted into tripping of 220/132kV 160MVA ICT-1 at Jhagra(UK). v) Tripping of both 160 MVA transformers resulted into more import of power from 220/132 kV S/s which led to tripping of 132 kV Rishikesh-Laltappur ckt and 132 kV Bindal-Majra ckt. vi) These trippings further led to tripping of 132 kV Khodri-Dhakrani ckt which resulted in complete supply disturbance in Dehradun area. vii) Supply was restored within 40 minutes in whole area. viii) As per PMU at Dehradun(PG), no fault is observed in the system. ix) As per SCADA, load loss of approx. 160MW is observed in Uttarakhand control area.	1) 220/132kV 160MVA ICT-1 at Jhagra(UK) 2) 220/132kV 160MVA ICT-2 at Jhagra(UK)

20.Details of Grid Events during the Month of May 2023													
Northern Region													
Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HR:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
20	GI-1	Delhi	17-May-2023 14:50	17-May-2023 18:49	03:59	0	110	0.000	0.167	60161	65922	i) During antecedent condition, 220kV Mandola-Narela Ckt-1 & 2 were connected to 220kV Bus-1 feeding the load of 220kV Narela S/s whereas 220kV Panipat-Narela ckt- 1, 2 & 3 were connected to 220kV Bus-2 and feeding the 220kV Narela-Delhi RR (Rohtak road) ckt-1 & 2. 220kV Bus Coupler was in off position at Narela(DV) and 220kV DSIDC - Narela ckt-1 & 2 were on no-load. ii) As reported, at 14:50 hrs, 220 KV Delhi RR(BB)-Narela(DV) (BBMB) Ckt-2 tripped on Y-N phase to earth fault (Zone 1 from Narela end) with fault distance of 15.63km from Delhi RR(BB) end. iii) Further at 15:02 hrs, B-phase jumper of 220 KV Delhi RR(BB)-Narela(DV) (BBMB) Ckt-1 snapped between wavetrap and line isolator. Due to this, 220 KV Delhi RR(BB)-Narela(DV) (BBMB) Ckt-1 tripped on B-N phase to earth fault (Zone 3 from Narela(DV) end) with fault distance of 15.20km from Delhi RR(BB) end. iv) As per DR of 220 KV Delhi RR(BB)-Narela(DV) (end) (BBMB) Ckt-2, fault current was 4.3kA from Narela(DV) end and as per DR of 220 KV Delhi RR(BB)-Narela(DV) (end) (BBMB) Ckt-1, fault current was 8.6kA from Narela(DV) end. v) As per PMU at Dadri Thermal (NT), Y-N phase to earth fault is observed at 14:50 hrs with fault clearing time of 80 ms and B-N phase to earth fault is observed at 15:02 hrs with fault clearing time of 80 ms. vi) As per SCADA, load loss of approx. 110MW is observed in Delhi control area.	1) 220 KV Delhi RR(BB)-Narela(DV) (BBMB) Ckt-2 2) 220 KV Delhi RR(BB)-Narela(DV) (BBMB) Ckt-1
21	GI-2	Haryana	18-May-2023 00:58	18-May-2023 07:21	06:23	0	0	0.000	0.000	46288	54707	i) During antecedent condition, 800 KV HVDC Kurukshetra(PG) Pole-1, 2, 3 & 4 were carrying ~600 MW each from Champa to Kurukshetra. ii) As reported at 00:58hrs, Pole-1 was blocked from Kurukshetra end on emergency due to smoke observed from HV smoothing reactor in DC Yard. Pole 3 at Champa blocked on CAT B protection as Pole-1 failed to isolate (isolation auto sequence failure) at Kurukshetra end. At the same time, Pole-2 & Pole-4 blocked on CAT-B protection operated at Champa end. iii) As reported, sequence of events are as follows: B 00:58:38 hrs: Pole 1 was manually hand tripped from Kurukshetra end as smoke was observed in Pole 1 DC yard. During the event there were continuous AC side disturbances at Kurukshetra end which lead to several commutation failures and further control action at both Champa and Kurukshetra Stations. B 00:59:15 hrs: Due to failure of the parallel sequence of Pole-1 from Pole-3 at Kurukshetra, Pole 1 generated CAT B sequence that resulted in tripping of Pole 3 at both ends. B 00:59:56:30 hrs: After blocking of Pole 1 & Pole 3, system was running with return current through DMR 1 & DMR 2. After few seconds, DMR 2 minor fail alarm also appeared, however fault was of transient nature and got reset after protective sequence initiation. B 00:59:56:907 hrs: Multiple commutation failures were occurring at Kurukshetra end due to persistent heavy thunderstorm and rain (tripping / AR of AC lines). During multiple commutation failure at Kurukshetra end "Instability Detection minor fail" latched in Pole-2 / Lane-1 at Champa end, resulted Pole 2 lane changeover from lane 1 to lane 2 at Champa. At Champa "HV CLD protective sequence" was latched in Pole 2 lane 2 which initiated CAT B sequence and caused the tripping of both Pole 2 & Pole 4. iv) As per PMU at Kurukshetra(PG), no fault is observed in the system, but fluctuation in voltage is observed. v) As per SCADA, no load loss is observed in Haryana control area.	1) 800 KV HVDC Kurukshetra(PG) Pole-01 2) 800 KV HVDC Kurukshetra(PG) Pole-02 3) 800 KV HVDC Kurukshetra(PG) Pole-03 4) 800 KV HVDC Kurukshetra(PG) Pole-04
22	GI-2	Uttar Pradesh	18-May-2023 11:47	18-May-2023 14:27	02:40	470	0	0.871	0.000	53946	56737	i) As reported, shifting of 400 KV Singrauli(NT)-Vindhyachal(PG) (PG) Ckt-1 from Main bus to Transfer bus was being done for relay modernization work. After shifting, LBB of Transfer bus coupler (TBC-2) mal-operated due to issue in wiring. TBC-2 tripped within 50msec and LBB reset. ii) At the same time, 500 MW Singrauli STPS - UNIT 7 also tripped due to shorting of contacts which sent general protection control signal. Both the issues has been resolved. iii) As per PMU at Singrauli(NT), no fault is observed in the system. iv) As per SCADA, no load loss is observed in Uttar Pradesh control area. Change in generation of approx. 470MW is observed at Singrauli(NTPC).	1) 400 KV Singrauli(NT)-Vindhyachal(PG) (PG) Ckt-1 2) 500 MW Singrauli STPS - UNIT 7
23	GI-1	Jammu & Kashmir	20-May-2023 12:22	20-May-2023 13:26	01:04	0	185	0.000	0.289	58638	63970	i) During antecedent condition, active power loading of 220 KV Barri(JK)-Kishenpur(PG) Ckt-1 & 2 were 99MW and 101MW respectively. ii) As reported, at 12:22hrs, 220 KV Barri(JK)-Kishenpur(PG) Ckt-1 tripped on R-B phase to phase fault. iii) As per DR of 220 KV Barri(JK)-Kishenpur(PG) Ckt-1 at Kishenpur end, fault in R & B phase was persisting and line tripped from Kishenpur end on directional earth fault protection operation (back up protection). iv) Due to tripping of 220 KV Barri(JK)-Kishenpur(PG) Ckt-1, loading on 220 KV Barri(JK)-Kishenpur(PG) Ckt-2 increased and line CB at 220kV Barri(PDD JK) end of 220 KV Barri(JK)-Kishenpur(PG) Ckt-2 opened due to over-loading, but line remain charged from Kishenpur(PG) end. v) As per PMU at Kishenpur(PG), R-B phase to phase fault is observed in system with delayed fault clearance time of 840 ms. vi) As per SCADA, load loss of approx. 185MW occurred in J&K control area.	1) 220 KV Barri(JK)-Kishenpur(PG) Ckt-1 2) 220 KV Barri(JK)-Kishenpur(PG) Ckt-2
24	GD-1	Uttarakhand	20-May-2023 16:18	20-May-2023 16:57	00:39	36	20	0.065	0.032	55208	61572	i) During antecedent condition, 33 MW Unit 1 at Singoli Bhatwari HEP was generating 36MW which was evacuating through 220 KV Singoli Bhatwari(Singoli(TUHP))- Srinagar(UK) (PTCU) Ckt-1 & 2, carrying 18MW each. ii) As reported, at 16:18hrs, 220 KV Singoli Bhatwari(Singoli(TUHP))-Srinagar(UK) (PTCU) Ckt-1 tripped on Y-B-N double phase to earth fault with fault distance of 45.11km from Srinagar(UK) end. iii) At the same time, 220 KV Singoli Bhatwari(Singoli(TUHP))-Srinagar(UK) (PTCU) Ckt-2 also tripped on Y-B-N double phase to earth fault with fault distance of 52.79km from Srinagar(UK) end. iv) Due to tripping of both 220 KV Singoli Bhatwari(Singoli(TUHP))-Srinagar(UK) (PTCU) Ckt-1 & 2, 33MW Unit-1 at Singoli Bhatwari HEP tripped due to loss of evacuation path. v) As per DR of 220 KV Singoli Bhatwari(Singoli(TUHP))-Srinagar(UK) (end) (PTCU) Ckt-1, zone-1 distance protection operated at Srinagar(UK) end with fault current of approx. 2.985kA and 2.33kA in Y and B-phase respectively. vi) As per DR of 220 KV Singoli Bhatwari(Singoli(TUHP))-Srinagar(UK) (end) (PTCU) Ckt-2, zone-1 distance protection operated at Srinagar(UK) end with fault current of approx. 1.454kA and 2.48kA in Y and B-phase respectively. vii) As per PMU, Y-B-N double phase to earth fault is observed with fault clearing time of 80ms. viii) As per SCADA, load loss of approx. 20MW is observed in Uttarakhand control area and change in generation of approx. 36MW is observed at Singoli Bhatwari HEP.	1) 220 KV Singoli Bhatwari(Singoli(TUHP))-Srinagar(UK) (PTCU) Ckt-1 2) 220 KV Singoli Bhatwari(Singoli(TUHP))-Srinagar(UK) (PTCU) Ckt-2 3) 33 MW Unit-1 at Singoli Bhatwari HEP
25	GI-1	Jammu and Kashmir	22-May-2023 14:36	22-May-2023 15:19	00:43	0	310	0.000	0.449	62758	69083	i) As reported, at 14:36hrs, 220 KV Bishnah(JK)-Hiranagar(JK) ckt tripped on R-Y phase to phase fault with fault current of 3.92kA and 3.73kA in R and Y-phase respectively. ii) At the same time, 220 KV Samba(PG)-Bishnah(JK) ckt also tripped on R-Y phase to phase fault. iii) As per DR at Samba(PG) end of 220 KV Samba(PG) (end)-Bishnah(JK) (PDD JK) Ckt, zone-3 distance protection operated with fault current of 2.77kA and 2.34kA in R and Y-phase respectively at Samba(PG) end. Fault clearing time was ~840ms. iv) As per PMU at Kishenpur(PG), R-Y phase to phase fault is observed in system with fault clearance time of 840 ms. v) As per SCADA, load loss of approx. 310MW occurred in J&K control area.	1) 220 KV Bishnah(JK)-Hiranagar(JK) ckt 2) 220 KV Samba(PG)-Bishnah(JK) ckt

20.Details of Grid Events during the Month of May 2023

Northern Region



Sl.No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (H:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
26	GI-2	Punjab	24-May-2023 22:12	24-May-2023 22:53	00:41	300	0	0.636	0.000	47149	55608	i) As reported, at 21:31 hrs, 400 KV Dehar(BB)-Panchkula(PG) (PG) Ckt tripped on B-N phase to earth fault (zone-1 from Dehar end). ii) At 21:33 hrs, 400 KV Dehar(BB)-Rajpura(PS) (PG) Ckt tripped on R-N phase to earth fault (zone-2 From Rajpura end) with fault current 3.2kA and distance of 129.0km from Rajpura end. iii) Hence, during antecedent condition, both 400 KV Dehar(BB)-Panchkula(PG) (PG) Ckt and 400 KV Dehar(BB)-Rajpura(PS) (PG) Ckt were already out and total generation of 165MW Unit-4 & 5 at Dehar(BB) of approx. 300MW was evacuating through 400/220 kv 315 MVA ICT 1 at Dehar(BB). iv) Further, as reported, at 22:12 hrs, while charging 400 KV Dehar(BB)-Panchkula(PG) (PG) Ckt from Dehar end, 400/220 kv 315 MVA ICT 1 at Dehar(BB) tripped. Due to this, 165MW Unit-4 & 5 at Dehar(BB) also tripped due to loss of evacuation path. v) As per PMU at Jalandhar(PG), no fault is observed in the system at 22:12hrs. vi) As per SCADA, change in generation of approx. 300MW is observed at Dehar(BBMB) at 22:12 hrs.	1) 400 KV Dehar(BB)-Panchkula(PG) (PG) Ckt 2) 400 KV Dehar(BB)-Rajpura(PS) (PG) Ckt 3) 400/220 kv 315 MVA ICT 1 at Dehar(BB) 4) 165MW Unit-4 at Dehar(BB) 5) 165MW Unit-5 at Dehar(BB)
27	GI-2	Jammu and Kashmir	24-May-2023 15:09	24-May-2023 16:41	01:32	380	0	0.691	0.000	55009	61070	i) During the antecedent condition, 130 MW Dulhasti HPS - UNIT 1, 2 & 3 were generating approx. 380MW in total and total power of 380MW was evacuating through 400KV Dulhasti(NH)-Kishenpur(PG) ckt-1&2. ii) As reported, at 15:09 hrs, UCB (Unit control board) disconnection fault QSD (Quick shutdown) operated from SCADA because of malfunctioning of surge shaft gate opening signal. Due to this, 130 MW Dulhasti HPS - UNIT 1, 2 & 3 tripped. Incorrect signal of surge shaft gate closed generated due to malfunction of contacts. iii) As per PMU at Kishenpur(PG), no fault is observed. iv) As per SCADA, generation loss of approx. 380MW is observed at Dulhasti(NH). v) During investigation, no issue in contacts found.	1) 130 MW Dulhasti HPS - UNIT 1 2) 130 MW Dulhasti HPS - UNIT 2 3) 130 MW Dulhasti HPS - UNIT 3
28	GD-1	Rajasthan	24-May-2023 20:14	24-May-2023 23:40	03:26	0	275	0.000	0.471	48757	58394	i) 400/220KV Jodhpur(RS) has one and half breaker bus scheme at 400KV side. ii) As reported at 20:10 hrs, Isolator of 220 KV Jodhpur to Bilara line and the IPS tube of 400 KV main bus-A got damaged due to heavy storm at 400 KV GSS, Jodhpur. iii) On this fault, Bus bar protection operated at 400V Bus-A (as reported and as verified from DR). iv) As reported, at the same time, all the elements connected to 400V Bus-A & Bus-B tripped and substation became dead. v) As per PMU at Bhadla(PG), R-N phase to earth fault which further converted into three phase fault with delayed clearance of 2080ms is observed. vi) As per DR of 400 KV Jodhpur-Kankani (end) (RS) Ckt-1, at 20:14 hrs, line tripped on R-N phase to earth fault (zone-3 distance protection) with fault current of 1.16kA from Kankani(RS) end and fault clearance time of ~900msec. As reported, fault distance was 211km from Kankani(RS) end. vii) As per DR of 400 KV Kankani(PG) (end)-Jodhpur(RS) (PG) Ckt, at 20:14 hrs, line tripped on R-N phase to earth fault later converted into R-Y fault is observed. Fault current was ~1.38kA from Kankani(PG) end. Fault clearing time was ~1560ms. As reported, fault distance was 187.5km from Kankani(PG) end. viii) As per DR of 400/220 kv 315 MVA ICT 1 & 2 at Jodhpur(RS), ICTs tripped on directional over current protection operation with the delay of approx. ~1300msec. Fault in R-phase which converted into R-Y-B is observed. ix) As per SCADA, change in demand of approx. 275MW in Rajasthan control area x) The damaged IPS tube of 400KV main bus-A has been fixed.	1) 400KV Bus 1 at Jodhpur(RS) 2) 400KV Bus 2 at Jodhpur(RS) 3) 400 KV A&B-Jodhpur (RS) Ckt 4) 400 KV Rajwesi(RW)-Jodhpur (RS) Ckt 5) 400/220 kv 315 MVA ICT 1 at Jodhpur(RS) 6) 400/220 kv 315 MVA ICT 2 at Jodhpur(RS) 7) 400 KV Jodhpur-Kankani (RS) Ckt-1 8) 400 KV Kankani(PG)-Jodhpur(RS) (PG) Ckt
29	GI-2	Delhi	24-May-2023 17:43	24-May-2023 17:59		0	380	0.000	0.706	45210	53847	i) During antecedent condition, 400/220 KV 500 MVA ICT-4 at Mandola(PG) was already under emergency shutdown for attending hot spot on 207 Bay's CT R and Y Phase terminals. ii) The load of 220KV Gopalpur and Sabji Mandi S/s was fed from 220 KV Mandola(PG)-Gopalpur(DTL) (DTL) Ckt-1 & 2 and the load of 220KV Narrela S/s was fed from 220 KV Mandola(PG)-Narela(DV) (DTL) Ckt-1 & 2. iii) As reported, the details of event is as follows: a. Y Phase CT at 220KV side of ICT-4 was earthed from both sides for replacement of defective jumper. b. On connection of Tan delta kit earthing, sparking was observed in earthing lead. Discharge current from kit resulted in circulating current and eventually as spill current in Bus-1 & check zone. c. Further, low IR value of cable cores from busbar panel at Mandola(PG) to Gopalpur (ckt-1) isolator selection relays led to coupling of 220KV Bus 1 & 2 at Mandola(PG). d. This led to tripping of both 220KV Bus 1 & 2 at Mandola(PG). e. Due to tripping of 220KV Bus 1 & 2 at Mandola(PG), all the elements connected to Bus-1 & 2 also tripped and both the buses became dead. iv) As per DR of 400/220 KV 500 MVA ICT-4 at Mandola(PG), current of approx. 135A in Y-phase CT at LV side is observed. As reported, this spill current led to operation of bus bar differential protection. v) As per PMU at Mandola(PG), no fault is observed in the system. vi) As per SCADA, change in demand of approx. 380MW is observed in Delhi control area. vii) The load of 220KV Gopalpur and Sabji Mandi S/s was normalized through 220KV Wazirabad-Gopalpur ckt-1&2 at 17:46hrs and the load of 220KV Narrela S/s was normalized through 220 KV DSIOC Bawana- Narela ckt-1&2 at 17:59hrs.	1) 400/220 kv 500 MVA ICT 2 at Mandola(PG) 2) 220 KV Mandola(PG)-Narela(DV) (DTL) Ckt-1 3) 220 KV Mandola(PG)-Narela(DV) (DTL) Ckt-2 4) 220 KV Mandola(PG)-Gopalpur(DTL) (DTL) Ckt-1 5) 220 KV Mandola(PG)-Gopalpur(DTL) (DTL) Ckt-2 6) 220KV Bus 1 at Mandola(PG) 7) 220KV Bus 2 at Mandola(PG) 8) 25 MVAR Bus Reactor No 1 at 220 KV Mandola(PG)
30	GI-2	Haryana	25-May-2023 09:25	25-May-2023 11:22		0	0	0.000	0.000	51139	50996	i) During antecedent condition, 800 KV HVDC Kurukshetra(PG) Pole-1, 2, 3 & 4 were carrying 243MW, 240MW, 232MW & 236MW respectively from Champa to Kurukshetra. ii) As reported at 09:25hrs, Pole-4 was blocked from Kurukshetra end due to issue in measurement panel DCCT. Due to this, Pole-2 blocked on CAT-B protection from Pole-4. iii) At the same time, Pole-1 and Pole-3 also blocked due to DMR-2 transient fault. iv) As per PMU at Kurukshetra(PG), no fault is observed in the system, but fluctuation in voltage is observed. v) As per SCADA, no load loss is observed in Haryana control area.	1) 800 KV HVDC Kurukshetra(PG) Pole-01 2) 800 KV HVDC Kurukshetra(PG) Pole-02 3) 800 KV HVDC Kurukshetra(PG) Pole-03 4) 800 KV HVDC Kurukshetra(PG) Pole-04
31	GI-1	Punjab	27-May-2023 12:26	27-May-2023 15:04		0	355	0.000	0.830	43398	42786	i) As reported at 12:26 hrs, 220 KV Nallagarh(PG)-Mohali(PS) (PS) Ckt-1 and 2 tripped due to infringing of peacock which led to bus fault at 220KV Mohali S/s. Fault distance was 55km from Nallagarh(PG) end. ii) As per DR of 220 KV Nallagarh(PG) (end)-Mohali(PS) (PS) Ckt-1 and 2, both the ckt's tripped on B-N phase to earth fault sensed in zone-2. Fault current was 2.6kA from Nallagarh(PG) end. Delayed fault clearance of 540ms is observed. iii) As per PMU at Nallagarh(PG), B-N phase to earth fault with delayed fault clearance time of 560msec is observed. iv) As per SCADA, change in load of approx. 355MW is observed in Punjab control area.	1) 220 KV Nallagarh(PG)-Mohali(PS) (PS) Ckt-1 2) 220 KV Nallagarh(PG)-Mohali(PS) (PS) Ckt-2
32	GI-2	Haryana	28-May-2023 12:10	28-May-2023 16:02		0	0	0.000	0.000	43900	47516	i) During antecedent condition, 800 KV HVDC Kurukshetra(PG) Pole-1, 2, 3 & 4 were carrying 369MW, 367MW, 354MW & 364MW respectively from Champa to Kurukshetra. ii) As reported at 12:10hrs, 800 KV HVDC Kurukshetra(PG)-Champa(PG) (PG) Ckt-1 & 3 tripped as block command was received from Champa end due to DC Filter overload protection operation at Champa end. iii) As per PMU at Kurukshetra(PG), no fault is observed in the system, but fluctuation in voltage is observed.	1) 800 KV HVDC Kurukshetra(PG)-Champa(PG) (PG) Ckt-1 2) 800 KV HVDC Kurukshetra(PG)-Champa(PG) (PG) Ckt-3

20.Details of Grid Events during the Month of May 2023
Northern Region



Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (H:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(G1 for 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
33	GD-1	Rajasthan	28-May-2023 13:02 to 13:40	28-May-2023 18:59		8000	0	19.885	0.000	40231	47381	a) At 13:02:58.080 hrs, 220KV Bhadla TPREL Line tripped due to R-N fault. It was reported that the fault occurred due to damage of wave trap at 220KV TPREL end. CB did not open at Bhadla end and therefore LBB operated at Bhadla end as per DR. Fault cleared with the delay of ~280msec. b) Due to LBB operation, element connected at 220KV Bus-4 at Bhadla(PG) i.e., 220KV Bhadla ESSEL line & 400/220 KV 500 MVA ICT 6 at Bhadla(PG) also tripped at the same instant. c) At 13:03:01.120 hrs, 220KV Bhadla CSP Jodhpur tripped due to R-N fault followed by Y-N fault during dead time of R-ph-A/R. Fault occurred due to snapping of OPGW. d) During voltage dip of faults in lines, reduction in RE generation connected at Fatehgarh 1 & 2 was observed (as per SCADA) on LVRT operation. (Generation at Bhadla(PG) & Bhadla2(PG) was already near to zero before the tripping event). The total generation loss as per SCADA data was ~910 MW which recovered within ~2min. e) Further at 13:20 hrs, 765KV Bhadla2-Fatehgarh2 ckt-2 tripped on permanent R-N fault in line followed by tripping of 765/400KV 1500MVA ICT 1 at Bhadla2(PG) on differential protection operation on R-N fault, flashover in 400KV side jumper and gantry was observed. f) During voltage dip of this fault also, reduction in RE generation connected at Fatehgarh 1 & 2 was observed (as per SCADA) on LVRT operation. (Generation at Bhadla(PG) & Bhadla2(PG) was already almost zero before the tripping event). The total generation loss as per SCADA data was ~1800 MW out of which ~1150MW recovered within ~2min. g) Further at 13:35 hrs, 765KV Bhadla2-Bikaner ckt-1 tripped on permanent Y-N fault in line followed by tripping of 220KV Bhadla2-ASEPL ckt on R-N fault. h) Further at 13:36hrs, 765KV Bhadla2-Ajmer ckt-2 tripped on R-B-N double phase to ground fault followed by tripping of 400KV Bhadla2-Kolayat ckt on R-N fault at 13:37hrs. i) During voltage dip of this fault also, reduction in RE generation connected at Fatehgarh 1 & 2 was observed (as per SCADA) on LVRT operation. (Generation at Bhadla(PG) & Bhadla2(PG) was already almost zero before the tripping event). The total generation loss as per SCADA data was ~800 MW which recovered within ~1.5min. j) Further at 13:40hrs, 765KV Bhadla2-Fatehgarh2 ckt-1 & 765KV Bhadla2-Ajmer ckt-1 tripped on R-N fault in respective lines during reclaim time. k) During voltage dip of this fault also, reduction in RE generation connected at Fatehgarh 1 & 2 was observed (as per SCADA) on LVRT operation. (Generation at Bhadla(PG) & Bhadla2(PG) was already almost zero before the tripping event). The total generation loss as per SCADA data was 1200 out of which ~700MW recovered within ~2min. l) With the tripping of these two lines, out of six 765KV lines at 765KV Bhadla2(PG), only one 765KV line i.e., 765KV Bhadla2-Bikaner ckt-2 remained intact.	1) 220 KV Bhadla(PG)-TPREL Solar(TP) (Tata Power) Ckt-1 2) 220 KV Bhadla(PG)-ESUCRL SL_BHD_PG (ESUCRL) (ESUCRL) Ckt-1 3) 400/220 KV 500 MVA ICT 6 at Bhadla(PG) 4) 220 KV Bhadla(PG) - Bus 4 5) 220 KV Bhadla(PG)-CS_Jodhpur SL_BHD_PG (Cleansolar_Jodhpur) (Cleansolar_Jodhpur) Ckt-1 6) 765 KV Bhadla_2 (PG)-Fatehgarh_1(PG) (PFTL) Ckt-2 7) 765/400 KV 1500 MVA ICT 1 at Bhadla_2 (PG) 8) 220 KV Nokhra SL_BHD2 (NTPC-Bhadla_2 (PG) (NTPC_NOKHRA) Ckt-1 9) 765 KV Bikaner-Bhadla_2 (PG) Ckt-1 10) 220 KV Nokhra SL_BHD2 (NTPC-Bhadla_2 (PG)-Avaada Sunrays) (Avaada_Sunrays) Ckt-1 11) 765 KV Ajmer-Bhadla_2 (PG) Ckt-2 12) 400 KV Kolayat Solar NTPC_1 (NTPC_KOLAYAT SL)-Bhadla_2 (PG) (NTPC_KOLAYAT SL) Ckt-1 13) 765 KV Bhadla_2 (PG)-Fatehgarh_1(PG) (PFTL) Ckt-1 14) 765 KV Bhadla_2 -Ajmer (PG) Ckt-1
34	GD-1	Punjab	31-May-2023 04:48	31-May-2023 07:08		0	90	0.000	0.200	39599	44912	i) 220 KV Dasuya(PS) 5/s has double bus scheme. ii) As reported, brief of the event is as follows: a) At 04:48hrs on 31st May/23, 220 KV Dasuya-Alawalpur (PS) Ckt tripped on R-N phase to earth fault from Alawalpur end only; fault sensed in zone-1 from Alawalpur end. This fault was not sensed from Dasuya end. Hence distance protection did not operate and line did not trip from Dasuya end on this fault. b) On this fault, other lines from 200KV Dasuya(PS) tripped on back-up protection (Z-2/Z-3/directional E/F) operation from remote end only. c) Back up over current earth fault protection of 220 KV Dasuya-Alawalpur (PS) Ckt also didn't operate. iii) As per DR of 220 KV Dasuya(PS)-Jalandhar(PG) (end) (PG) Ckt-1 & 2, directional E/F protection operated at Jalandhar(PG) end. Fault current in R-phase were 700A and 950A respectively for Ckt-1 & 2 from Jalandhar(PG) end. iv) As per PMU at 400KV Jalandhar(PG), R-N phase to earth fault with delayed clearance of fault in 3520 ms is observed. v) As per SCADA change in demand of approx. 90MW is observed in Punjab control area.	1) 220 KV Dasuya(PS)-Jalandhar(BB) (BBMB) Ckt 2) 220 KV Dasuya(PS)-Jalandhar(PG) (PG) Ckt-1 3) 220 KV Dasuya(PS)-Jalandhar(PG) (PG) Ckt-2 4) 220 KV Fongli(BB)-Dasuya(PS) (BBMB) Ckt-1 5) 220 KV Fongli(BB)-Dasuya(PS) (BBMB) Ckt-2 6) 220 KV Dasuya-Alawalpur (PS) Ckt 7) 220 KV Samal(PS)-Dasuya(PS) (PG) Ckt-1 8) 220 KV Samal(PS)-Dasuya(PS) (PG) Ckt-2 9) 220KV Dasuya-Railway ckt

20.Details of Grid Events during the Month of May 2023

Western Region



Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-1	WR	03-May-23 16:25	04-May-23 11:48	19:23	70	-	0.001	-	57758	55041	At 16:25 Hrs/03-05-2023, 220 kV Bhuj- Dayapar-2 line tripped on Y-B phase fault due to B phase LA failure at Dayapar end. There was a generation loss of 70 MW at 220 kV Dayapar (Inox) Wind Power Plant due to loss of evacuation path.	Tripping of 1. 220 kV Bhuj- Dayapar 2
2	GD-1	WR	03-May-23 19:40	-	-	88	-	0.001	-	63132	56224	At 19:40 Hrs/03-05-2023, 220 kV Bhachau- Bhuvad 1&2 tripped on Y-E & Y-B phase fault respectively due to tower collapse. There was a generation loss of 88 MW at 220 kV Bhuvad (Renew Power) Wind Power Plant.	Tripping of 1. 220 kV Bhachau- Bhuvad 1&2
3	GI-1	WR	04-May-23 15:09	04-May-23 16:07	00:58	104	-	0.002	-	58765	56351	At 15:09 Hrs/04-05-2023, 220 kV Ratadiya-Bhuj-1 tripped on Y-E fault due to damage of insulator anchor at tower No.15. 220 kV Bus coupler was under planned outage at Ratadia & resulted in generation loss of 104 MW at 220 kV Ratadia(ADANI) Wind Power plant.	Tripping of 1. 220 kV Bhuj- Ratadiya 1
4	GI-2	WR	05-May-23 14:40	05-May-23 15:22	00:42	-	-	-	-	61687	58316	At 14:40 Hrs/05-05-2023, Y phase CT of Tie bay of 400 kV Bina(PG) 2 line blasted at 400 kV Bina(MP) substation. Due to the blast, B-phase Main bay CT of 400/220 kV Bina(MP) ICT 3 , B-phase grading capacitor of 400 kV Bina(PG) Tie CB & B-phase isolator of 400 kV Bina(MP) damaged. 400 kV Bina(MP)- Bina(PG) 1,2,3&4, 400/220 kV Bina(MP) ICT 1,2&3 and 400 kV Bina(MP) Main Bus 1 tripped due to the event. At the same time 765 kV Bina(PG)- Seoni S/C tripped on Over Voltage protection operation at Bina(PG) end. As reported by MP SLDC, no load loss occurred due to the event.	Tripping of 1. 400 kV Bina(MP)- Bina(PG) 1,2,3&4 2. 400/220 kV Bina(MP) ICTs 1,2&3 3. 400 kV Bina(MP) Main Bus 1 4. 765 kV Bina(PG)- Seoni S/C
5	GI-2	WR	11-May-23 10:24	11-May-23 11:49	01:25	-	-	-	-	69033	63398	At 10:24 Hrs/11-05-2023, 400 kV Chorania- Charal line tripped on B-E fault due to agricultural waste burning between location 52-53. At the same time, 400 kV Chorania Bus 1 and all the connected elements tripped on Bus bar protection operation. As reported by GETCO, R Phase current observed in DR of 400 kV Charal line during B-E fault. Bus bar protection operated due to CT secondary fault of 400kV Charal line and same has been rectified. There was no load loss due to the event.	Tripping of 1. 400 kV Chorania Bus-1 2. 400 kV Chorania- Hadala 3. 400 kV Chorania- Vadavi 2 4. 400 kV Chorania- Charal 5. 400 kV Chorania- Pachham 6. 400 kV Chorania- Kasor
6	GD-1	WR	12-May-23 13:44	12-May-23 18:59	05:15	245	-	0.003	-	73415	63604	At 13:44 Hrs/12-05-2023, 220 kV Bhuj- Naranpar tripped on B-E fault. Due to loss of evacuation path, 245 MW generation loss occurred at 220 kV Naranpar(GIWEL) Wind Power Plant.	Tripping of 1. 220 kV Bhuj- Naranpar
7	GI-1	WR	12-May-23 20:28	12-May-23 23:10	02:42	-	-	-	-	76241	61690	At 20:28 Hrs/12-05-2023, 220 kV Sujalpur(PG) Bus 2 and all the connected elements tripped on R-E fault on Bus bar protection operation (monkey climbed over the 220 kV Bus 2). 400/220 kV Shujalpur(PG) ICTs 1&2 tripped at LV side only and remained in charged condition from 400 kV side. As reported by MP SLDC, there was no load loss due to the event.	Tripping of 1. 220 kV Sujalpur(PG)- Rajgarh(MP) 2 2. 220 kV Sujalpur(PG)- Sujalpur(MP) 2 3. 400/220 kV Sujalpur(PG) ICTs 1&2
8	GD-1	WR	17-May-23 11:15	17-May-23 12:16	01:01	800	-	0.011	-	73072	64852	At 11:15 Hrs/17-05-2023, while shifting 220kV side bay (221) of 400/220kV Bhuj ICT6, from 220 kV Bhuj Bus 2 to 220 kV Bhuj Bus 1, 220kV Bhuj Bus 1 & 2 (Section-B) tripped on busbar differential protection operation due to Rph – Yph fault in isolator 89B of 221 Bay. At the same time, 220 kV Bhuj- Naranpar, 220 kV Bhuj- Gadhsisa & 220 kV Vadva lines tripped at respective RE stations end due to Over reach of Distance protection relays. At the same time, 220 kV Bhuj- Baranda A/R successfully from Baranda end due to relay over reach. Generation loss of 800 MW occurred at 220 kV Dayapar(INOX), 220 kV Gadhsisa Renew Power), 220 kV Vadva(GIWEL), 220 kV Naranpar(GIWEL) Wind Power Plants due to loss of evacuation path.	Tripping of 1. 220 kV Bhuj- Dayapar 2 2. 220 kV Bhuj- Naranpar 3. 220 kV Bhuj- Gadhsisa 4. 220 kV Bhuj- Vadva 5. 400/220 kV Bhuj ICTs 1,2&6 6. 220 kV Bhuj Bus 1&2 Section B

20.Details of Grid Events during the Month of May 2023



Western Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
9	GD-1	WR	18-May-23 13:13	18-May-23 13:50	00:37	504	-	0.007	-	73550	65452	At 13:13 Hrs/18-05-2023, 400 kV ACBIL-MCCPL and 400 kV ACBIL-Bilaspur tripped on Y-B Phase fault. ACBIL Unit-1 & Unit-2 tripped due to loss of evacuation path. At the same time, MCCPL Unit-1 also tripped due to boiler trip. About 504 MW generation loss occurred due to the event.	Tripping of 1.400 kV ACBIL- MCCPL 2.400 kV ACBIL- Bilaspur 3.ACBIL Units 1&2 4.MCCPL Unit 1
10	GD-1	WR	20-May-23 00:57	20-May-23 01:31	00:34	-	300	-	0.005	77324	64684	At 00:57 Hrs/20-05-2023, 220kV Satna(MP) Buses 1&2 tripped on Busbar protection operation due to CT blast of 220kV Katni line at 220kV Satna(MP). All the connected 220kV lines and 220/132kV Transformers tripped. There was a load loss of around 300 MW due to the event.	Tripping of 1. 220 kV Satna(MP)- Satna(PG) 1,2&3 2.220 kV Satna(MP)- Chhatarpur 3.220 kV Satna(MP)- Kotar 4.220 kV Satna(MP)- Rewa 5.220 kV Satna(MP)- SGTP
11	GD-1	WR	21-May-23 13:11	22-May-23 12:44	23:33	166	-	0.002	-	69061	62012	At 13:11 Hrs/21-05-2023, 220 kV Bhuj- Dayapar 2 tripped on B-E fault. Generation loss of 166 MW occurred at 220 kV Dayapar(INOX) Wind Power plant due to evacuation path loss.	Tripping of 1.220 kV Bhuj- Dayapar 2
12	GD-1	WR	26-May-23 14:19	26-May-23 15:19	01:00	280	-	0.004	-	71016	63708	At 14:19 Hrs/26-05-2023, due to heavy wind 33KV feeder-12 B-phase conductor got damaged and fell down on Feeder-1 resulting in tripping of 220/33 kV Pritamnagar-ICT-1,2&3. Generation loss of 280 MW occurred at 220 kV Pritamnagar (Adani) Wind Power plant.	Tripping of 1.220/33 kV Pritamnagar-ICT-1 2.220/33 kV Pritamnagar-ICT-2 3.220/33 kV Pritamnagar-ICT-3
13	GD-1	WR	27-May-23 16:50	27-May-23 18:02	01:12	-	12	-	0.000	73162	63457	At 16:50 Hrs/27.05.2023, 220 kV Annupur-Kotmikala-1 & 2 line tripped on Y phase to earth fault leading to the black out of Kotmikala substation, prior to the event 220kV Kotmikala-Churri-1&2 were kept out on power regulation. Load loss of 12 MW observed at 220kV Kotmikala due to the event.	Tripping of 1.220 kV Annupur-Kotmikala-1 2.220 kV Annupur-Kotmikala-2
14	GD-1	WR	29-May-23 14:30	29-May-23 17:06	02:36	250	-	0.003	-	73965	64057	At 14:30 Hrs/29-05-2023, 220 kV Bachau-Nararpur (Ostro)-1&2 tripped on single line to ground fault. Generation loss of 250 MW occurred at 220 kV Ostro (Renew Power) Wind Power plant due to loss of evacuation path.	Tripping of 1.220 kV Bachau-Nararpur (Ostro)-1 2.220 kV Bachau-Nararpur (Ostro)-2

20.Details of Grid Events during the Month of May 2023
Southern Region



Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid		Brief details of the event (pre fault and post fault system conditions)	Name of Elements (Tripped/Manually opened)
	(GI for 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-1	Karnataka	01-May-23 02:45	01-May-23 03:58	1 hr 13mins	100	50	0.27%	0.15%	36881	32518	Complete Outage of 220kV Nagjheri PH, 220kV Kodalalli PH, 220kV Kadra PH of KPCL and 220kV/110kV Karwar SS of KPTCL: During antecedent conditions, 220kV Nagjheri PH was operating with single bus configuration at 220kV level. 220kV Kaiga Kadra and 220kV Kaiga Kodalalli were under outage. 220kV Kodalalli PH, 220kV Kadra PH and 220kV/110kV Karwar SS were being radially fed from 220kV Nagjheri PH. As per the reports submitted, the triggering incident was 220kV Bus PT failure at 220kV Nagjheri PH. Immediately, BBP operated and all the elements connected to the bus tripped. This led to complete outage of 220kV Nagjheri PH, 220kV Kodalalli PH, 220kV Kadra PH and 220kV/110kV Karwar SS.	1. 220kV Nagjheri Ambewadi line-1&2 2. 220kV Nagjheri Hubli Line-1,2&3 3. 220kV Nagjheri Bidnal 4. 220kV Nagjheri Kodalalli Line-1&2
2	GD-1	Karnataka	03-May-23 08:10	03-May-23 08:33	23mins	320	410	0.84%	0.97%	38249	42103	Complete Outage of 220kV/110kV Shahbad SS, 220kV/110kV Humnabad SS, 220kV/110kV Halburga SS, 220kV/110kV Kapnoor SS, 220kV/110kV Shahpur and 220kV/110kV Sedam SS of KPTCL and 220kV Bus outage at 400kV/220kV RTPS Generating Station of KPCL: During antecedent conditions, 220kV Sedam Tandur line was under open condition. 220kV/110kV Shahbad SS, 220kV/110kV Kapnoor SS, 220kV/110kV Humnabad SS, 220kV/110kV Halburga SS, 220kV/110kV Shahpur and 220kV/110kV Sedam SS were being radially fed from 220kV Bus at 400kV/220kV RTPS generating station and 220kV Lingasugur Shahpur line. 400kV/220kV RTPS generating station is operating with single bus configuration at 220kV level. As per the information received, the triggering incident was B-phase PT failure in 400kV/220kV ICT-1 causing 220kV BBP to operate and all the elements connected to the 220kV bus tripped. Subsequently, it is suspected that 220kV Lingasugur Shahpur line tripped on over loading. This resulted in loss of power supply to 220kV/110kV Shahbad SS, 220kV/110kV Humnabad SS, 220kV/110kV Halburga SS, 220kV/110kV Kapnoor SS, 220kV/110kV Shahpur and 220kV/110kV Sedam SS.	1. 220kV Lingasugur Shahpur 2. 400kV/220kV RTPS ICT-1 3. 400kV Raichur Raichur_PG-2 4. 220kV Raichur Sedam 5. 220kV Raichur Malat 6. 220kV Raichur Lingasugur 7. 220kV Raichur Shahpur
3	GD-1	Tamil Nadu	07-May-23 00:33	07-May-23 02:09	1hr 36mins	15	0	0.04%	0.00%	39154	43781	Complete Outage of 230kV JSW_Vilathikulam_Wind:As per the reports submitted, the triggering incident was R-N fault in 230kV TTGS JSW_Vilathikulam_Wind line and the line tripped. Tripping of the only connected line resulted in complete outage of 230kV JSW_Vilathikulam_Wind.	1.230kV TTGS JSW_Vilathikulam_Wind
4	GD-1	Karnataka	08-May-23 05:10	08-May-23 06:11	1hr 1min	0	0	0.00%	0.00%	39154	43781	Complete Outage of 220kV Rychalu SS-2 of KSPDCL: As per the reports submitted, the triggering incident was B-N fault in 400kV Pavagada Devanahalli Line-2. At the same time, 220kV Pavagada Ryachalu SS-2 line tripped only at Rychalu end on high set EF protection. Tripping of the only connected line resulted in complete outage of 220kV Rychalu SS-2	1. 220kV Pavagada Ryachalu SS-2 line
5	GD-1	Karnataka	10-May-23 17:29	10-May-23 18:26	57mins	150	40	0.37%	0.09%	40556	44611	Complete Outage of 220kV Kadra PH of KPCL and 220kV/110kV Karwar SS of KPTCL: During antecedent conditions, 220kV Kaiga Kadra and 220kV Kaiga Kodalalli were under outage. 220kV Kadra PH and 220kV/110kV Karwar SS were being radially fed through 220kV Kadra Kodalalli line. As per the reports submitted, the triggering incident was RYB fault in 220kV Kadra Kodalalli line. This led to complete outage of 20kV Kadra PH and 220kV/110kV Karwar SS	1. 220kV Kadra Kodalalli
6	GD-1	Karnataka	11-May-23 18:34	11-May-23 19:06	32mins	329	0	0.79%	0.00%	41445	45175	Complete Outage of 220kV Varahi PH of KPCL: During antecedent conditions, 220kV Varahi Simoga Line-1&2 were under outage. At 18:29hrs and 18:32hrs, due to heavy rain, 220kV Varahi Kemar Line-2 and 220kV Varahi Kemar Line-1 tripped on R-N fault. Subsequently, 220kV Varahi Heggurje and 220kV Varahi Shimoga Line-3 tripped on over current protection. At 18:34hrs, due to loss of evacuation path all the units tripped on over frequency at 220kV Varahi PH causing complete outage of the power house.	1. 220kV Varahi Unit-3&4 2. 220kV Varahi Shimoga Line-3 3. 220kV Varahi Heggurje 4. 220kV Varahi Kemar Line-1&2
7	GD-1	Karnataka	17-May-23 13:36	17-May-23 13:45	9mins	0	45	0.00%	0.08%	50821	57136	Complete Outage of 220kV Kadra PH of KPCL and 220kV/110kV Karwar SS of KPTCL: During antecedent conditions, 220kV Kaiga Kadra and 220kV Kaiga Kodalalli were under outage. 220kV Kadra PH and 220kV/110kV Karwar SS were being radially fed through 220kV Kadra Kodalalli line. As per the reports submitted, the triggering incident was relay maloperation of 220kV Kadra Kodalalli line at Kodalalli end. This led to a complete outage of 20kV Kadra PH and 220kV/110kV Karwar SS.	1. 220kV Kadra Kodalalli

20.Details of Grid Events during the Month of May 2023													
Southern Region													
Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid		Brief details of the event (pre fault and post fault system conditions)	Name of Elements (Tripped/Manually opened)
	(GI for 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
8	GD-1	Karnataka	19-May-22 13:09	19-May-22 14:09	1hr	0	750	0.00%	1.30%	52844	57840	Tripping of 220kV Bus-2 of 400kV/220kV Hoody SS and Complete Outage of 220kV/66kV Exora SS, 220kV/66kV EDC SS, 220kV/66kV Nimans Station, 220kV/66kV ITI SS, 220kV/66kV Vikas Tech Park SS and 220kV/66kV Sarjapur SS of KPTCL: As per the reports submitted, the triggering incident was tripping of 400kV/220kV Hoody ICT-2 due to operational issue in circuit breaker. Subsequently, 400kV/220kV Hoody ICT-3 tripped on overloading. Tripping of both these ICTs resulted in loss of power supply of 220kV Bus-2 of 400kV/220kV Hoody SS which further led to Complete Outage of 220kV/66kV Exora SS, 220kV/66kV EDC SS, 220kV/66kV Nimhans Station, 220kV/66kV ITI SS, 220kV/66kV Vikas Tech Park SS and 220kV/66kV Sarjapur SS.	1. 400kV/220kV Hoody ICT-2&3
9	GD-1	Karnataka	20-May-23 15:48	21-May-23 02:33	10hrs 45mins	0	130	0.00%	0.23%	50316	56687	Cpmplete Outage of 220kV/66kV Exora SS, 220kV/66kV Sarjapur SS and 220kV/66kV Vikas Tech park SS of KPTCL: As per the reports submitted, the triggering incident was B-N fault in 220kV Somanahally Malur line. Since the line is radially feeding 220kV/66kV Exora SS, 220kV/66kV Sarjapur SS and 220kV/66kV Vikas Tech park SS , tripping of this line resulted in complete outage of 220kV/66kV Exora SS, 220kV/66kV Sarjapur SS and 220kV/66kV Vikas Tech park SS.	1. 220kV Somanahally Malur
10	GD-1	Andhra Pradesh	21-May-23 15:47	21-May-23 16:30	43mins	22	80	0.05%	0.17%	45393	48442	Complete Outage of 400kV/220kV Gani SS, 220kV Gani PS-1, 220kV Gani PS-2, 220kV Gani PS-3 and 220kV Gani PS-4, 220kV/132kV Nandyal SS and Tripping of 220kV Bus-2 of 220kV Somayajulapalli SWS of APTRANSCO and : During antecedent conditions, 220kV Bus-2 of 220kV/132kV Somyajulapally SWS is being radially fed from 400kV/220kV Gani SS. 220kV Gani PS-1, 2,3&4 are radially connected to 400kV/220kV Gani SS. As per the reports submitted, the triggering incident was B-N fault in 400kV Ghani Narnoor Line-1&2 and the lines tripped. This resulted in Complete Outage of 400kV/220kV Gani SS leading to loss of power supply to 220kV Bus-2 of 220kV Somayajulapalli SWS and 220kV/132kV Nandyal SS. This also resuled in complete outage of 220kV Gani PS-1,2,3 &4.	1. 400kV Ghani Narnoor line-1&2
11	GD-1	Karnataka	21-May-23 01:03	21-May-23 02:12	1hr 09mins	0	0	0.00%	0.00%	43866	46981	Complete Outage of 220kV Rychalu SS-2 of KSPDCL: As per the reports submitted, the triggering incident was B-N fault in 400kV Pavagada Devanahalli Line-2. At the same time, 220kV Pavagada Ryachalu SS-2 line tripped only at Ryachalu end on high set EF protection. Tripping of the only connected line resuled in complete outage of 220kV Rychalu SS-2.	1. 220kV Pavagada Ryachalu SS-2 line
12	GD-1	Kerala	22-May-23 16:04	22-May-23 16:13	9mins	200	0	0.43%	0.00%	46847	53215	Complete Outage of 220kV/110kV Shornur SS, 220kV/110kV Elankur SS, and Tripping of 220kV Bus-2 of 220kV/110kV Areakode SS of KSEB: During antecedent conditions, 220kV/110kV Areakode SS was operating with split bus conditions with 220kV Areakode Shornur line and 220kV Areakode Elankur line on 220kV Bus-2. As per the reports submitted, the triggering incident was Y-N fault in 220kV Madakathara Elankur line and 220kV Areakode Shornur line which are on the same tower. At Shornur, the Y-pole of the breaker failed to open causing LBB to operate and the elements connected to the 220kV Bus-2 of Shornur tripped. Tripping of 220kV Madakathara Elankur and 220kV Areakode Shornur led to the loss of supply to 220kV/110kV Elankur SS, 220kV/110kV Shornur SS and tripping of 220kV Bus-2 of 220kV/110kV Areakode SS.	1. 220kV Madakathara Elankur 2. 220kV Areakode Shoranur 3. 220kV/110kV 100MVA Shoranur Transformer-2
13	GD-1	Karnataka	23-May-23 15:39	23-May-23 16:05	26mins	350	0	0.72%	0.00%	48600	53997	Complete Outage of 220kV/110kV Mahalingapura SS, 220kV/110kV Kuduchi SS, 220kV/110kV Athani SS and 220kV/110kV Soudatti SS of KPTCL: During antecedent conditions, 220kV/110kV Soudatti radially connected to 220kV/110kV Mahalingapura SS due to outage of 220kV Soudatti Bidnal line and 220kV Mahalingapura Vajramatti Line-1&2 were under LC. As per the reports submitted, the triggering incident was Y-B fault in 220kV Mahalingapura Narendra Line-2. Subsequently, 220kV Mahalingapura Narendra Line-1 tripped on over loading and 220kV Kudachi Chikkodi Line-1 & 2 were hand tripped. This led to complete outage of 220kV/110kV Mahalingapura SS, 220kV/110kV Kuduchi SS, 220kV/110kV Athani SS and 220kV/110kV Soudatti SS.	1. 220kV Narendra Mahalingapura Line-1&2 2. 220kV Kudachi Chikkodi Line-1&2
14	GD-1	Kerala	23-May-23 19:03	23-May-23 19:08	5mins	100	0	0.26%	0.00%	38604	48068	Complete Outage of 220kV/110kV Mylatty SS, 220kV/110kV Ambalathara SS and 220kV/110kV/33kV Taliparamba SS of KSEB: 220kV/110kV Mylatty SS, 220kV/110kV Ambalathara SS and 220kV/110kV/33kV Taliparamba SS are radially connected to 220kV/110kV Kanihirode SS through 220kV Ambalathara Kanihirode and 220kV Taliparamba Kanihirode lines. As per the reports submitted, the triggering incident was Y-N fault in 220kV Ambalathara Kanihirode and 220kV Taliparamba Kanihirode lines. Tripping of both these lines resulted in complete Outage of 220kV/110kV Mylatty SS, 220kV/110kV Ambalathara SS and 220kV/110kV/33kV Taliparamba SS.	1. 220kV Ambalathara Kanihirode 2. 220kV Taliparamba Kanihirode
15	GD-1	Andhra Pradesh	30-May-23 09:20	30-May-23 11:12	1hr 52mins	0	0	0.00%	0.00%	44208	50203	Complete Outage of 220kV Tallapally SWS of APTRANSCO: As per the reports submitted, the triggering incident was R-N fault in 220kV Tallapally Srisaillam RB Line-2. At the Tallapally end, distance protection failed to clear the fault. Fault was cleared by the tripping of 400kV/220kV Nsagar ICT-1, 2, & 3 on backup over current protection operation and connected lines tripped on Zone-2 protection at the remote ends. This resulted in the complete outage of 220kV Tallapally SWS.	1. 220kV Tallapally Srisaillam RB Line-1&2 2. 220kV Tallapally Piduguralla Line-1&2 3. 220kV Tallapally Nsagar_TS Line-1,2&3 4. 400kV/220kV Nsagar ICT-1,2&3 5. 220kV Tallapally Chakurthy 6. 220V Tallapally VTPS
16	GD-1	Karnataka	30-May-23 18:43	30-May-23 20:51	2hr 08mins	0	0	0.00%	0.00%	38705	44887	Complete Outage of 220kV/66kV Tirumani SS-1 of KSPDCL: As per the reports submitted, the triggering incident was B-N fault in 220kV Pavagada Tirumani SS-1 line. Tripping of the only connected line resulted in a complete outage of 220kV/66kV Tirumani SS-1 .	1. 220kV Pavagada Tirumani SS-1 line.

20.Details of Grid Events during the Month of May 2023
Southern Region



Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid		Brief details of the event (pre fault and post fault system conditions)	Name of Elements (Tripped/Manually opened)
	(GI 1or 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
17	GI-1	Andhra Pradesh	03-May-23 20:45	03-May-23 22:05	1hr 20mins	0	0	0.00%	0.00%	39154	43781	Tripping of 220kV Bus of 220kV/132kV/33kV Gudivada SS: 220kV/132kV/33kV Gudivada SS is operating with single bus configuration at 220kV. The triggering incident was R-N fault in 220kV Gudivada Bheemavaram line. At Gudivada end, the circuit breaker failed to open causing LBB to operate and all the lines connected to the 220kV Bus tripped. 132kV was intact during the event.	1. 220kV Gudivada Bheemavaram 2. 220kV Gudivada Nunna Line-1&2 3. 220kV Gudivada Akiveedu 4. 220kV/132kV 160MVA Gudivada PTR-1&3 5. 220kV/132kV 100MVA Gudivada PTR-2
18	GI-1	Tamil Nadu	10-May-23 11:12	10-May-23 11:39	27 mins	0	0	0.00%	0.00%	47398	46696	Tripping of 230kV Bus-2 of 230kV Checkanurani SWS of TANTRANSCO: As per the reports submitted, the triggering incident was Y-N fault in 230kV Checkanurani Indubharath line(Idle charged from Checkanurani end). At Checkanurani end, CB failed to open and LBB operated causing all the elements connected to the Bus-2 to trip.	1. 230kV Checkanurani Indubharath 2. 230kV Checkanurani Sembatty 3. 230kV Checkanurani Savasapuram 4. 230kV Checkanurani TTPS 5. 230kV Checkanurani Kayathar 6. 230kV Checkanurani Amuthapuram 7. 400kV/230kV Madhurai ICT-3
19	GI-1	Andhra Pradesh	15-May-23 15:14	15-May-23 22:05	6 hrs 51 mins	500	0	0.97%	0.00%	51674	54532	Tripping of 220kV Bus-2 of 400kV/220kV VTPS of APGENCO: As per the reports submitted, the triggering incident was failure of Rph CT of U#3 GT at 220kV VTPS end. Overall differential protection of U#3 GT operated, but due to persistence of fault current, LBB operated resulting in the tripping of all the elements connected to 220kV Bus-2 at 400kV/220kV VTPS .	1. VTPS Unit-2, 3&6 2. 220kV VTPS Rentachinthal 3. 220kV VTPS Kondapalli Line-2 4. 220kV VTPS Narsarao Pet 5. 220kV VTPS Tadikonda Line-2 6. 220kV VTPS Chilikalla Line-2 7. 220kV VTPS Piduguralla Line-2 8. 220kV VTPS Nuzivedu line
20	GI-1	Andhra Pradesh	16-May-23 22:02	17-May-23 00:49	2 hrs 47 mins	245	0	0.59%	0.00%	41193	51332	Tripping of 220kV Bus-1 of 220kV Nagarjunsagar PH of TSGENCO: As per the reports submitted, 220kV Bus-1 of 220kV Nagarjunsagar PH got de-energised due to Bus-1 BBP operation.	1. 220kV Nagarjun Sagar Srisalam RB-1 2. Nagarjun Sagar Unit-1,3&5 3. 220kV Nagarjun Sagar Tallapally Line-1 4. 220kV/132kV 100MVA PTR-1
21	GI-1	Andhra Pradesh	17-May-23 17:57	17-May-23 18:25	28mins	900	0	2.25%	0.00%	40013	50683	Tripping of 220kV Bus-1 of 400kV/220kV VTPS of APGENCO: As per the reports submitted, the triggering incident was maloperation of LBB protection of U#1 GT at 220kV VTPS end. This resulted in the tripping of all the elements connected to 220kV Bus-1 at 400kV/220kV VTPS. Subsequently, running units#3 and 6 got tripped due to the loss of auxiliary supply.	1. VTPS Unit-1, 3, 4, 5 and 6 2. 220kV VTPS Podili 3. 220kV VTPS Tallapalli 4. 220kV VTPS Tadikonda-1 5. 220kV VTPS Kondala-1 6. 220kV VTPS Gunadala-1 7. 220kV VTPS Piduguralla-1
22	GI-1	Telangana	26-May-23 19:44	27-May-23 01:25	Shr 41mins	0	0	0.00%	0.00%	39585	47991	Tripping of 220kV Bus-1 of 220kV/132kV Malayalpalay SS of TSTRANSCO: As per the reports submitted, the triggering incident was R-phase jumper failure in 220kV Malayalpalay Mandamary line and caused a fault in 220kV Bus-1. Immediately, 220kV Bus-1 BBP operated and all the elements connected to the bus tripped including 400kV/220kV Ramagundam ICT-2&4.	1. 400kV/220kV Ramagundam ICT-2&4 2. 220kV Mamidipally Mandamary line 3. 220kV Mamidipally Jagityal Line-1& 3 4. 220kV Mamidipally Manthani 5. 220kV Mamidipally Dursheed 6. 220kV Mamidipally Medaram 7. 230kV/110kV 160MVA Mamidipally PTR-1
23	GI-1	Telangana	30-May-23 10:35	30-May-23 11:31	56 mins	0	0	0.00%	0.00%	46986	52024	Tripping of 220kV Bus-2 of 220kV Upper Jurala PH of TSGENCO: During antecedent conditions, there was no generation at 220kV Upper Jurala PH. As per the reports submitted, the triggering incident was R-N fault in 220kV Jurala Raichur_KA Line-2. At the same time, the Bus Coupler tripped on over current protection. Tripping of only connected line and bus coupler resulted in de-energization of 220kV Bus-2 at 220kV Upper Jurala PH.	1. 220kV Jurala Raichur_KA Line-2 2. 220kV Bus coupler at 220kV Jurala PH

20.Details of Grid Events during the Month of May 2023



Eastern Region

Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1 or 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-1	Jorethang	14.05.2023 16:36	14.05.2023 16:39	00:03	43	0	0.15%	0.00%	27759	24125	At 16:36 Hrs on 14.05.2023, 220 kV Jorethang-New Melli D/c tripped from Jorethang end only. Consequently, one running unit at Jorethang tripped and power supply interrupted at Jorethang. Around 43 MW generation loss occurred.	U#1 at Jorethang 220 kV Jorethang-New Melli D/c
2	GD-1	Therubali	15.05.2023 11:13	15.05.2023 11:51	00:38	20	25	0.08%	0.10%	24632	24277	At 11:13 Hrs, OPGW wire of 220 V Therubali-Lakshmipur-2 snapped between location no. 1209 & 1210 and fault was not cleared from Therubali end. This led to tripping of all associated feeders at Therubali and total power failure at 220kV Therubali, 220kV Kasipur & 220kV Jaypatna sub-stations in south Odisha. There was load loss of around 25MW in Therubali area and generation loss of 20 MW at Balimela HEP following the fault.	220 kV Therubali-Lakshmipur D/c 220 kV Therubali-Bhanjanagar D/c 220 kV Therubali-Narendrapur-2 220 kV Therubali-Gunupur 220 kV Therubali-Indravati-1,2,3 220 kV Therubali-Kashipur 60 MW U#5 at Balimela
3	GD-1	Chatra	15.05.2023 14:22	15.05.2023 16:04	01:42	0	28	0.00%	0.12%	28932	24211	At 14:22 Hrs on 15.05.2023, 220 kV Daltonganj-Chatra-1 tripped due to Y_N fault leading to total power failure at Chatra, Latehar as 220 kV Daltonganj-Latehar-1 was under shutdown and Latehar, Chatra were radially fed through 220 kV Daltonganj-Chatra-1 only. Around 28 MW load loss reported at Latehar and Chatra by SLDC Jharkhand.	220 kV Daltonganj-Chatra-1
4	GI-2	JITPL	18.05.2023 14:07	18.05.2023 20:37	06:30	1096	0	3.96%	0.00%	27653	24688	At 14:07 Hrs on 18.05.2023, U#2 at JITPL tripped due to operation of unit differential protection. After 1.5 seconds, U#1 at JITPL also tripped due to tripping of its Station transformer leading to tripping of the unit on loss of auxiliary supply. Around 1096 MW generation loss occurred at JITPL S/s.	2*600 MW Units at JITPL
5	GD-1	Lakshmikantpur	23.05.2023 02:36	23.05.2023 03:30	00:54	0	289	0.00%	1.19%	29222	24324	At 02:36 Hrs on 23rd May 2023, 220 kV Subhashgram (WB)-Lakshmikantpur-2 tripped due to Y-Earth fault. At the same time, 220 kV Main Bus-2 at Subhashgram (WB) and 220 kV Subhashgram-Lakshmikantpur-1 also tripped leading to total power failure at Lakshmikantpur which is radially fed through 220 kV Subhashgram (WB). Around 289 MW load loss reported during the event at Lakshmikantpur, Sirakol, Kakdwip and Falta.	220 kV Subhashgram-Lakshmikantpur D/c 220 kV Subhashgram-Subhashgram (PG)-2 220 kV Subhashgram-Kasba-2 220 kV Main Bus#2 at Subhashgram

20.Details of Grid Events during the Month of May 2023												
North-Eastern Region												
Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM:SS)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the		Antecedent Generation/Load in the Regional Grid		Brief details of the event (pre fault and post fault system conditions)
	(G1 to G2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)	
1	GD 1	Daporizo, Along, Pasighat, Roing, Tezu and Namsai areas of Arunachal Pradesh Power System	05-May-23 20:18	05-May-23 21:39	01:21:00	0	31	0.00%	1.17%	3109	2647	Daporizo, Along, Pasighat, Roing, Tezu and Namsai areas of Arunachal Pradesh Power System were connected with the rest of NER Grid through 132 kV Daporijo - Ziro Line. At 20:18 Hrs on 05.05.2023, 132 kV Daporijo - Ziro Line tripped. Due to tripping of this element, Daporizo, Along, Pasighat, Roing, Tezu and Namsai areas of Arunachal Pradesh Power System were separated from the rest of NER Grid and subsequently collapsed due to no source available in these areas. 132 kV Daporijo - Ziro Line was declared faulty at 21:39 Hrs on 05.05.2023. Power supply was extended to Daporizo, Along, Pasighat, Roing, Tezu and Namsai areas of Arunachal Pradesh Power System by charging 132 kV Daporijo - Ziro Line at 11:25 Hrs on 06.05.2023
2	GD 1	Along, Pasighat, Roing, Tezu and Namsai areas of Arunachal Pradesh Power System	12-May-23 02:28	12-May-23 03:40	01:12:00	0	11	0.00%	0.52%	2187	2120	Along, Pasighat, Roing, Tezu and Namsai areas of Arunachal Pradesh Power System were connected with the rest of NER Grid through 132 kV Along - Daporijo Line . At 02:28 Hrs on 12.05.2023,132 kV Along - Daporijo Line e tripped. Due to tripping of this element, Along, Pasighat, Roing, Tezu and Namsai areas of Arunachal Pradesh Power System were separated from the rest of NER Grid and subsequently collapsed due to no source available in these areas. 132 kV Along - Daporijo Line was declared faulty at 03:40 Hrs on 12.05.2023. Power supply was extended to Along, Pasighat, Roing, Tezu and Namsai areas of Arunachal Pradesh Power System by charging 132 kV Along - Daporijo Line at 07:32 Hrs on 12.05.2023.
3	GD 1	Lumshnong and Amrit areas of Meghalaya Power System	14-May-23 12:46	14-May-23 12:54	00:08:00	0	33	0.00%	1.75%	1840	1883	Lumshnong and Amrit areas of Meghalaya Power System were connected with rest of NER grid through 132 kV Khleirhat-Lumshnong Line. 132 kV Lumshnong-Panchgram Line was under planned shutdown since 07:25 Hrs on 14.05.2023. At 12:46 Hrs on 14.05.2023, 132 kV Khleirhat-Lumshnong Line tripped. Due to tripping of this element, Lumshnong and Amrit areas of Meghalaya Power System were separated from rest of NER Grid and subsequently collapsed due to no source available in these areas. Power supply was extended to Lumshnong and Amrit areas of Meghalaya Power System by charging 132 kV Khleirhat-Lumshnong Line at 12:54 Hrs on 14.05.2023
4	GD 1	Lumshnong and Amrit areas of Meghalaya Power System	16-May-23 15:57	16-May-23 16:16	00:19:00	0	36	0.00%	1.51%	1823	2379	Lumshnong and Amrit areas of Meghalaya Power System were connected with rest of NER grid through 132 kV Khleirhat-Lumshnong Line. 132 kV Lumshnong-Panchgram Line was under planned shutdown since 03:31 Hrs on 16.05.2023. At 15:57 Hrs on 16.05.2023, 132 kV Khleirhat-Lumshnong Line tripped. Due to tripping of this element, Lumshnong and Amrit areas of Meghalaya Power System were separated from rest of NER Grid and subsequently collapsed due to no source available in these areas. Power supply was extended to Lumshnong and Amrit areas of Meghalaya Power System by charging 132 kV Khleirhat-Lumshnong Line at 16:16 Hrs on 16.05.2023.
5	GD 1	Dhaligaon, Barpeta, Bornagar, Joghghopa and Gosaigaon areas of Assam Power System	16-May-23 19:49	16-May-23 20:08	00:19:00	0	45	0.00%	1.83%	2855	2460	Dhaligaon, Barpeta, Bornagar, Joghghopa and Gosaigaon areas of Assam Power System were connected with rest of NER grid through 132 kV BTPS - Dhaligaon D/C Lines. 132 kV Nalbari-Barpeta Line was under shutdown to avoid overloading of 132 kV BTPS-Dhaligaon D/C Lines, 132 kV Bornagar - Rangia Line was under shutdown to avoid overloading of Rangia ICTs and 132 kV Gosaigaon - Gauripur Line was under shutdown to avoid overloading of 132 kV BTPS - Kokrajhar D/C Lines At 19:49 Hrs on 16.05.2023, 132 kV BTPS - Dhaligaon D/C Lines tripped. Due to tripping of these elements, Dhaligaon, Barpeta, Bornagar, Joghghopa and Gosaigaon areas of Assam Power System were separated from rest of NER Grid and subsequently collapsed due to no source available in these areas Power supply was extended to Dhaligaon, Barpeta, Bornagar, Joghghopa and Gosaigaon areas of Assam Power System by charging 132 kV BTPS-Dhaligaon 1 Line at 20:08 Hrs on 16.05.2023.
6	GD 1	Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System	24-May-23 08:19	24-May-23 08:49	00:30	3	25	0%	1%	2024	2035	Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System were connected with rest of NER grid through 132 kV Balipara - Tenga Line. At 08:19 Hrs on 24.05.2023, 132 kV Balipara - Tenga Line tripped. Due to tripping of this element, Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System were separated from rest of NER Grid and subsequently collapsed due to load generation mismatch in these areas. Power supply was extended to Tenga, Khupi areas and Dikshi HEP of Arunachal Pradesh Power System by charging 132 kV Balipara - Tenga Line at 08:49 Hrs on 24.05.2023.

20.Details of Grid Events during the Month of May 2023													
North-Eastern Region													
Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM:SS)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the		Antecedent Generation/Load in the Regional Grid		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(G1 1or 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
7	GD 1	Kohima,Wokha, Chiephobozou, Meluri and Kiphire areas of Nagaland Power System	24-May-23 11:30	24-May-23 11:47	00:17	0	30	0%	1%	1878	2052	Kohima,Wokha, Chiephobozou, Meluri and Kiphire areas of Nagaland Power System were connected with rest of NER grid through 132 kV Dimapur-Kohima Line. 132 kV Sanis - Wokha tripped at 10:15 Hrs on 24.05.2023 & 132 kV Imphal (Turebam) - Karong was under emergency shutdown. At 11:30 Hrs on 24.05.2023, 132 kV Dimapur-Kohima Line tripped. Due to tripping of this element, Kohima,Wokha, Chiephobozou, Meluri and Kiphire areas of Nagaland Power System were separated from rest of NER Grid and subsequently collapsed due to no source available in these areas. Power supply was extended to Kohima,Wokha, Chiephobozou, Meluri and Kiphire areas of Nagaland Power System by charging 132 kV Dimapur-Kohima Line at 11:47 Hrs on 24.05.2023.	132 kV Dimapur-Kohima Line
8	GD 1	Kohima, Chiephobozou, Meluri and Kiphire areas of Nagaland Power System and Karong area of Manipur Power System	25-May-23 17:43	25-May-23 18:12	00:29:00	6	47	0.28%	1.76%	2163	2663	Kohima, Chiephobozou, Meluri and Kiphire areas of Nagaland Power System and Karong area of Manipur Power System with rest of NER grid through 132 kV Dimapur - Kohima & 132 kV Wokha-Chiephobozou Lines. 132 kV Karong-Gampazol line was under emergency shutdown due to hotspot found at in jumper since 05.05.2023. At 17:43 Hrs on 25.05.2023, 132 kV Dimapur - Kohima & 132 kV Wokha-Chiephobozou Lines tripped. Due to tripping of these elements, Kohima, Chiephobozou, Meluri and Kiphire areas of Nagaland Power System and Karong area of Manipur Power System were separated from rest of NER Grid and subsequently collapsed due load generation mismatch in these areas. Power supply was extended to Kohima, Chiephobozou, Meluri and Kiphire areas of Nagaland Power System and Karong area of Manipur Power System by charging 132 kV Dimapur-Kohima line at 18:12 Hrs on 25.05.2023.	132 kV Dimapur - Kohima & 132 kV Wokha-Chiephobozou Lines
	GD 1	Udaipur area of Tripura Power System	27-May-23 08:38	27-May-23 09:18	00:40:00	29.3	37	1.28%	1.90%	2286	1943	Udaipur area of Tripura Power System was connected with rest of NER grid through 132 kV Palatana - Udaipur and 132 kV Monarchak-Udaipur Lines. At 08:38 Hrs on 27.05.2023, 132 kV Palatana - Udaipur and 132 kV Monarchak-Udaipur Lines tripped. Due to tripping of these elements, Udaipur area of Tripura Power System was separated from rest of NER Grid and subsequently collapsed due to load generation mismatch in this area. Power supply was extended to Udaipur area of Tripura Power System by charging 132 kV Palatana - Udaipur Line at 09:18 Hrs on 27.05.2023.	132 kV Palatana - Udaipur and 132 kV Monarchak-Udaipur Lines
10	GD 1	Dharmanagar area of Tripura Power System and Dullavchera area of Assam Power System	29-May-23 14:03	29-May-23 16:12	02:09:00	0	30	0.00%	1.23%	2150	2433	Dharmanagar area of Tripura Power System and Dullavchera area of Assam Power System were connected with rest of NER grid through 132 kV Dharmanagar - Dullavchera and 132 kV Dharmanagar - PK Bari Lines. 132 kV Hallakandi-Dullavchera Line was declared faulty since 13:01 Hrs on 29.05.2023. At 14:03 Hrs on 29.05.2023,132 kV Dharmanagar - Dullavchera and 132 kV Dharmanagar - PK Bari Lines tripped. Due to tripping of these elements, Dharmanagar area of Tripura Power System and Dullavchera area of Assam Power System were separated from the rest of NER Grid and subsequently collapsed due to no source available in these areas. Power supply was extended to Dharmanagar area of Tripura Power System and Dullavchera area of Assam Power System by charging 132 kV Hallakandi-Dullavchera Line at 16:12 Hrs on 29.05.2023.	132 kV Dharmanagar - Dullavchera and 132 kV Dharmanagar - PK Bari Lines
11	GD 1	Pasighat, Roing, Tezu and Namsai areas of Arunachal Pradesh Power System	29-May-23 15:01	29-May-23 16:35	01:34:00	0	12	0.00%	0.48%	2209	2481	Pasighat, Roing, Tezu and Namsai areas of Arunachal Pradesh Power System were connected with rest of NER grid through 132 kV Along - Pasighat Line. At 15:01 Hrs on 29.05.2023,132 kV Along - Pasighat Line tripped. Due to tripping of this element, Pasighat, Roing, Tezu and Namsai areas of Arunachal Pradesh Power System were separated from the rest of NER Grid and subsequently collapsed due to no source available in these areas. Power supply was extended to Pasighat, Roing, Tezu and Namsai areas of Arunachal Pradesh Power System by charging 132 kV Along - Pasighat Line at 16:35 Hrs on 29.05.2023.	132 kV Along - Pasighat Line
12	GD 1	Kohima, Chiephobozou, Wokha, Sanis, Meluri and Kiphire areas of Nagaland Power System and Karong area of Manipur Power System	30-May-23 17:00	30-May-23 17:33	00:33	0	41	0%	2%	2102	2705	Kohima,Chiephobozou, Wokha, Sanis, Meluri and Kiphire areas of Nagaland Power System and Karong area of Manipur Power System were connected with rest of NER grid through 132 kV Doyang-Sanis and 132 kV Imphal- Karong Lines. 132 kV Dimapur-Kohima line was under emergency shutdown for infringement clearance. At 17:00 Hrs on 30.05.2023, 132 kV Doyang-Sanis and 132 kV Imphal- Karong Lines tripped. Due to tripping of these elements, Kohima,Chiephobozou, Wokha, Sanis, Meluri and Kiphire areas of Nagaland Power System and Karong area of Manipur Power System were separated from rest of NER Grid and subsequently collapsed due to no source available in these areas. Power supply was extended to Kohima,Chiephobozou, Wokha, Sanis, Meluri and Kiphire areas of Nagaland Power System and Karong area of Manipur Power System by charging 132 kV Doyang-Sanis Line at 17:33 Hrs on 30.05.2023	132 kV Doyang-Sanis and 132 kV Imphal- Karong Lines
13	GD 1	Karong area of Manipur Power System	31-May-23 10:33	31-May-23 10:48	00:15	0	12	0%	0%	1915	2812	Karong area of Manipur Power System was connected with the rest of NER Grid through 132 kV Karong - Kohima & 132 kV Imphal -Karong Lines. At 10:33 Hrs on 31.05.2023,132 kV Karong - Kohima & 132 kV Imphal -Karong Lines tripped. Due to tripping of these elements, Karong area of Manipur Power System was separated from rest of NER Grid and subsequently collapsed due to no source available in this area. Power supply was extended to Karong area of Manipur Power System by charging 132 kV Kohima - Karong Line at 10:48 Hrs on 31.05.2023	132 kV Karong - Kohima & 132 kV Imphal -Karong Lines
14	GI-I	Tripura	15-May-23 12:20	15-May-23 14:30	02:10	37	0	2%	0%	2157	2241	AGTCCPP Unit 2 tripped at 12:20 Hrs on 15.05.2023 due to Exhaust Thermocouple Failure. Revision done from Block No. 59 on 15.05.2023.	AGTCCPP Unit 2

20.Details of Grid Events during the Month of May 2023
North-Eastern Region



Sl No.	Category of Grid Event (G1 1or 2/ GD-1 to GD-5)	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM:SS)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the		Antecedent Generation/Load in the Regional Grid		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	Generation Loss(MW)					Load Loss (MW)	% Generation Loss(MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)			
15	GI-I	Tripura	15-May-23 16:40	15-May-23 18:30	01:50	12	0	1%	0%	1987	2395	AGTCCPP Unit 5 tripped at 16:40 Hrs on 15.05.2023 due to tripped on Rotor E/F Stg-I. Revision done from Block No. 75 on 15.05.2023.	AGTCCPP Unit 5
16	GI-I	Tripura	19-May-23 11:21	20-May-23 13:00	01:39	25	0	1%	0%	2158	2157	AGTCCPP Unit 1 & Unit 5 tripped at 11:21 Hrs on 19.05.2023. Unit 1 tripped due to Problem in generating transformer & Unit 5 tripped due to non availability of GTG-1. Revision done from Block No. 53 on 19.05.2023 .	AGTCCPP Unit 1 & Unit 5
17	GI-I	Tripura	20-May-23 11:12	20-May-23 13:30	02:18	15	0	1%	0%	2363	2158	AGTCCPP Unit 3 tripped at 11:12 Hrs on 20.05.2023 due to Low Gas Pressure. Revision done from Block No. 55 on 20.05.2023.	AGTCCPP Unit 3
18	GI-I	Tripura	24-May-23 18:34	24-May-23 20:30	01:56	25	0	1%	0%	2692	2781	AGTCCPP Unit 4 tripped at 18:34 Hrs on 24.05.2023 due to High Lube Oil Temperature . Revision done from Block No. 83 on 24.05.2023 .	AGTCCPP Unit 4
19	GI-I	Assam	25-May-23 14:47	25-May-23 17:00	02:13	25	0	1%	0%	1894	2522	Kopili St II Unit 1 tripped at 14:47 Hrs on 25.05.2023 due to Cooling Water System Problem . Revision done from Block No. 69 on 25.05.2023	Kopili St II Unit 1
20	GI-I	Assam	25-May-23 18:58	25-May-23 21:00	02:02	25	0	1%	0%	1944	2491	Kopili St II Unit 1 tripped at 17:00 Hrs on 25.05.2023 due to Excitation problem. Revision done from Block No. 85 on 25.05.2023	Kopili St II Unit 1

21. NEW ELEMENTS COMMISSIONED* IN MAY 2023

COMMISSIONING OF NEW GENERATING UNITS

REGION	S.NO.	ENTITY	UNIT NAME / LOCATION	ADD. CAPACITY (MW)	UNIT NO.	INS. CAPACITY (MW)	DATE®
NR	1	BBMB	Bhakra Left Bank Power House-I(Hydro)/ Himachal Pradesh	126	I	630	21-05-2023
	2	TP SAURYA LIMITED (TPSL)	TP Saurya Limited (Solar)/Rajasthan	110	-	110	27-05-2023
	3	SBSR POWER CLEANTECH ELEVEN PVT LTD (SBSRPC-11)	SBSR Power Cleantech Eleven Pvt Ltd(Solar)/Rajasthan	25	-	300	31-05-2023
WR	4	CONTINUUM POWER TRADING PVT. LTD	Continuum Power Trading Pvt. Ltd (Wind)/Gujarat	2	I	92	09-05-2023
	5	ADANI WIND ENERGY KUTCHH FIVE LTD.	Adani Wind Energy Kutchh Five Ltd. (Wind)/Gujarat	13	I	131.5	25-05-2023
	6	SITAC KABINI RENEWABLE PRIVATE LTD.	Sitac Kabini Renewable Private Ltd. (Wind)/Gujarat	29.7	I	286.2	29-05-2023
	7	SITAC KABINI RENEWABLE PRIVATE LTD.	Sitac Kabini Renewable Private Ltd. (Wind)/Gujarat	16.2	I	302.4	29-05-2023
	8	APRAAVA ENERGY PRIVATE LIMITED (AEPL)	Apraava Energy Private Limited (AEPL) (Wind)/Gujarat	29.4	I	81.9	08-05-2023
	9	APRAAVA ENERGY PRIVATE LIMITED (AEPL)	Apraava Energy Private Limited (AEPL) (Wind)/Gujarat	25.2	I	107.1	26-05-2023
	10	TORRENT SOLARGEN LIMITED	Torrent Solargen Limited (Wind)/Gujarat	27	I	27	26-05-2023
	11	ADANI WIND ENERGY KUTCHH FOUR LTD.	Adani Wind Energy Kutchh Four Ltd. (Wind)/Gujarat	23.1	I	100.8	18-05-2023
	12	INOX WIND INFRASTRUCTURE SERVICES LTD.	INOX Wind Infrastructure Services Ltd. (Wind)/Gujarat	20	I	50	15-05-2023
	13	SRUJAN ENERGY SYSTEM PRIVATE LTD.	Srijan Energy System Private Ltd./ Gujarat	24.3	I	116.1	26-05-2023
	14	NTPC	NTPC Gandhar (Solar)/ Gujarat	10	I	20	31-05-2023
SR	15	CONTINUUM POWER TRADING PVT. LTD	Continuum Power Trading Pvt. Ltd (Wind)/Gujarat	36	I	128	31-05-2023
	16	JSW RENEW TWO	JSW Renew Two(Wind)/Tamilnadu	37.8	-	116.1	10-05-2023
	17	JSW RENEW TWO	JSW Renew Two(Wind)/Tamilnadu	24.3	-	116.1	27-05-2023

®RE (Solar & Wind generation added capacity FTC is in phases. Date mentioned is the date by which complete (Added) capacity

COMMISSIONING OF NEW ICTs

REGION	S.NO.	ENTITY	SUB-STATION	VOLTAGE (kV)	ICT NO.	CAPACITY (MVA)	DATE
NR	1	PGCIL	Bhadla_II	400/220/33	II	500	17-05-2023
	2	PGCIL	Bhadla_II	400/33	II	550	19-05-2023
	3	RRVPL	Bhadla	400/220/33	III	500	22-05-2023
	4	PGCIL	Moga	400/220/33	II	500	23-05-2023
	5	PGCIL	Ludhiana	400/220/33	I	500	24-05-2023
	6	UPPTCL	Sultanpur	400/220/33	IV	315	27-05-2023
	7	PGCIL	Bhadla_II	400/220/33	III	500	30-05-2023
SR	8	APTRANSCO	Hindupur	400/220	III	315	22-05-2023
	9	KSEB	Kottayam	400/220	II	315	13-05-2023
ER	10	PGCIL	Ranchi	400/220	III	500	30-05-2023
NER	11	AEGCL	Amingaon	220/132	I	160	10-05-2023
	12	AEGCL	Amigaon	220/132	II	160	10-05-2023

COMMISSIONING OF NEW TRANSMISSION LINES

REGION	S.NO.	ENTITY	LINE NAME	CKT NO.	VOLTAGE (kV)	DATE
WR	1	GETCO	400kV Kansar-Soja	II	400	30-05-2023

LILO OF TRANSMISSION LINES

REGION	S.NO.	ENTITY	LINE NAME (LILOed LINE)	LILO AT	VOLTAGE (kV)	DATE
NR	1	PGCIL	400kV Panki-Fatehpur-I (400kV Kanpur-Fatehpur-I)	Panki	400	16-05-2023
	2	PGCIL	400kV Panki-Fatehpur-II (400kV Kanpur-Fatehpur-II)	Panki	400	23-05-2023
SR	3	KSEB	400kV Kottayam-Kochi-I (400 kV Kochi-Tirunelveli-I)	Kottayam	400	13-05-2023
	4	KSEB	400kV Tirunelveli-Kottayam-I (400 kV Kochi-Tirunelveli-I)	Kottayam	400	13-05-2023

COMMISSIONING OF BUS/LINE REACTORS

REGION	S.NO.	ENTITY	SUB-STATION / LINE (@SUB-STATION)	VOLTAGE (kV)	CAPACITY (MVAR)	DATE
NR	1	UPRVUNL	Bus Reactor-@Obra C TPS	765	189	21-04-2023
	1	PBTSL	400kV Khetri-Bikaner_II Ckt-I @Khatri	400	80	30-05-2023
	2	PBTSL	400KV Khetri-Bikaner_II Ckt-II @Khatri	400	80	31-05-2023
	3	PBTSL	400KV Khetri-Bikaner_II Ckt-III @Khatri	400	80	31-05-2023
	4	PBTSL	400KV Khetri-Bikaner_II Ckt-IV @Khatri	400	80	31-05-2023
WR	5	MSETCL	Bus Reactor @Nanded	400	125	12-05-2023
ER	6	WBSETCL	Bus Reactor @Gokarna	400	125	12-05-2023
SR	7	KSEB	Bus Reactor-I @Kottayam	400	125	13-05-2023

COMMISSIONING OF HVDC/FACTS DEVICE/SYSTEM

REGION	S.NO.	NAME	SUB-STATION / CONSTITUENT	RATINGS	VOLTAGE (kV)	DATE

*Includes first time charging (FTC) as well

22.Voltage Profile

विद्युत विभव रूपरेखा माह - मई 2023

VOLTAGE PROFILE - MAY 2023

Date of reporting: 05-Jun-23

क्र.स. Sl. No.	क्षेत्र REGION	उपकेंद्र SUBSTATION	VOLTAGE < V(lower)* (V=380,728 kV)	V(lower) < VOLTAGE < V(upper)*	VOLTAGE > V(upper)* (V=420,800 kV)	Voltage Deviation Index (%age of time voltage is outside range)	Number of hours voltage was outside IEGC band during month	उच्चतम (कि.वो.) Maximum(kV)	निम्नतम(कि.वो.) Minimum(kV)	औसत (कि.वो.) Average(kV)
1	पूर्वी क्षेत्र ER	अंगुल ANGUL	0%	100%	0%	0%	0	800	749	775
2		दालिपली DARLIPALI	0%	100%	0%	0%	0	792	763	778
3		गया GAYA	0%	100%	0%	0%	0	784	746	765
4		जेरत JEERAT	0%	100%	0%	0%	0	796	728	762
5		झारसुगडा JHARSUGUDA	0%	99%	1%	1%	6	805	770	787
6		मिदनापुर MEDINIPUR	0%	100%	0%	0%	0	796	740	769
7		रांची RANCHI	0%	100%	0%	0%	0	798	759	781
8		सासाराम SASARAM	0%	100%	0%	0%	0	797	742	769
1	उत्तरी क्षेत्र NR	आगरा AGRA	0%	100%	0%	0%	1	809	746	778
2		आगरा (फतेहाबाद) AGRA (FATEHABAD)	0%	100%	0%	0%	0	798	739	769
3		अजमेर AJMER	0%	100%	0%	0%	2	804	754	781
4		अलीगढ़ ALIGARH	0%	100%	0%	0%	1	804	742	773
5		अनपरा सी ANPARA-C	0%	100%	0%	0%	0	780	754	765
6		अनपरा डी ANPARA-D	0%	100%	0%	0%	0	778	751	764
7		अंता ANTA	0%	99%	1%	1%	11	808	764	787
8		बलिया BALLIA	0%	100%	0%	0%	0	792	739	766
9		बारा BARA	0%	100%	0%	0%	0	795	732	774
10		भादला-2 BHADLA-2	0%	100%	0%	0%	0	796	710	771
11		भादला-2 BHADLA-2	0%	100%	0%	0%	0	799	711	772
12		भिवानी BHIWANI	0%	99%	1%	1%	5	809	748	780
13		बीकानेर BIKANER	0%	100%	0%	0%	0	800	736	772
14		बरैली BAREILLY	0%	99%	1%	1%	11	807	744	777
15		चित्तौड़गढ़ CHITTORGARH	0%	100%	0%	0%	4	804	760	783
16		फतेहगढ़-2 FATEHGARH-2	0%	100%	0%	0%	1	808	699	770
17		फतेहपुर FATEHPUR	0%	100%	0%	0%	0	795	740	772
18		ग्रेंटर नोएडा GREATER NOIDA	0%	99%	1%	1%	5	814	747	777
19		हापड़ HAPUR	0%	99%	1%	1%	6	814	731	770
20		जवाहरपुर JAWAHARPUR	0%	94%	6%	6%	45	812	754	785
21		झाटिकरा JHATIKARA	0%	100%	0%	0%	1	809	744	774
22		कानपुर जीआईएस KANPUR GIS	0%	100%	0%	0%	1	802	743	770
23		खैतरी KHETRI	0%	100%	0%	0%	1	805	743	774
24		कोटेश्वर KOTESHWAR	0%	100%	0%	0%	4	809	747	774
25		लालितपुर LALITPUR	0%	100%	0%	0%	0	774	742	757
26		लखनऊ LUCKNOW	0%	100%	0%	0%	0	797	741	770
27		मैनपुरी MAINPURI	0%	99%	1%	1%	9	813	751	780
28		मेरठ MEERUT	0%	99%	1%	1%	6	813	747	778
29		मोहा MOHA	0%	100%	0%	0%	0	799	738	769
30		ओबरा सी OBRA C	0%	99%	1%	1%	7	818	742	763
31		उरई ORAI	0%	99%	1%	1%	4	806	748	782
32		फागी PHAGI	0%	100%	0%	0%	3	808	754	781
33		उन्नाव UNNAO	0%	100%	0%	0%	0	794	737	762
34		वाराणसी VARANASI	0%	100%	0%	0%	0	794	752	773
1	पश्चिमी क्षेत्र WR	अकोला AKOLA	0%	100%	0%	0%	0	794	750	770
2		औरंगाबाद AURANGABAD	0%	100%	0%	0%	0	799	745	778
3		भोपाल (बीडीटीसीएल) BHOPAL (BDTCL)	0%	100%	0%	0%	0	796	751	772
4		भुज BHUJ	0%	100%	0%	0%	0	799	747	776
5		भुज-2 BHUJ-II	0%	100%	0%	0%	0	795	742	770
6		बिलासपुर BILASPUR	0%	100%	0%	0%	0	788	757	773
7		बिना BINA	0%	100%	0%	0%	1	800	746	779
8		बनारस BANASKANTHA	0%	99%	1%	1%	5	807	758	782
9		चाण CHAMPA	0%	91%	9%	9%	66	810	770	783
10		धुले (बीडीटीसीएल) DHULE (BDTCL)	0%	100%	0%	0%	0	794	745	775
11		धर्मपुराध DHARAMJAIGARH	0%	100%	0%	0%	0	794	756	773
12		रायपुर पूलिंग RAIPUR POOLING	0%	100%	0%	0%	0	799	767	782
13		एकतुनी EKTUNI	0%	100%	0%	0%	0	793	744	771
14		गदरवाड़ा GADARWARA	0%	100%	0%	0%	0	801	761	784
15		ग्वालियर GWALIOR	0%	100%	0%	0%	1	803	741	781
16		इंदौर INDORE	0%	100%	0%	0%	0	794	747	771
17		जबलपुर JABALPUR	0%	100%	0%	0%	3	803	756	785
18		खंडवा KHANDWA	0%	100%	0%	0%	0	793	749	773
19		कोरडी KORADI	0%	100%	0%	0%	0	789	751	766
20		लकाडिया LAKADIYA	0%	99%	1%	1%	10	805	758	784
21		रायगढ़ पूलिंग RAIGARH POOLING	0%	100%	0%	0%	2	803	773	788
22		पड़घे PADGHE	0%	99%	1%	1%	7	810	742	779
23		परली PARLI	0%	100%	0%	0%	0	801	746	781
24		पुणे PUNE	0%	99%	1%	1%	7	805	736	777
25		राजनन्दागांव RAJNANDGAON	0%	99%	1%	1%	7	806	771	788
26		सासन SASAN	0%	100%	0%	0%	0	793	759	777
27		सतना SATNA	0%	100%	0%	0%	1	802	756	783
28		सिवनी SEONI	0%	100%	0%	0%	0	797	754	777
29		सोपट SIPAT	0%	100%	0%	0%	0	787	758	774
30		सोलापुर SOLAPUR	0%	99%	1%	1%	8	805	750	785
31		तिरुठा TIRORA	0%	100%	0%	0%	0	802	752	763
32		तामनार TAMNAR	0%	100%	0%	0%	0	801	771	787
33		वडोदरा VADODARA	0%	100%	0%	0%	0	801	751	782
34		विंध्याचल पूलिंग VINDHYACHAL PS	0%	100%	0%	0%	0	798	761	780
35		वर्धा WARDHA	0%	100%	0%	0%	0	802	755	782
36		वरार वावरा WARORA	0%	100%	0%	0%	0	800	757	781
1	दक्षिणी क्षेत्र SR	कडपा CUDDAPAH	0%	87%	13%	13%	96	815	755	788
2		चिक्लुरीपेट CHILAKALURIPETA	0%	94%	6%	6%	46	816	747	782
3		कुरुन कुरुन KURNOOL	0%	100%	0%	0%	0	796	747	776
4		महेश्वरम MAHESWARAM	0%	99%	1%	1%	6	804	744	776
5		निजामाबाद NIZAMABAD	0%	94%	6%	6%	42	813	757	788
6		नेल्लूर पूलिंग NELLORE PS	0%	100%	0%	0%	0	792	750	774
7		रायचूर RAICHUR	0%	100%	0%	0%	0	799	750	779
8		श्रीकाकुलम SRIKAKULAM	0%	98%	2%	2%	16	807	746	782
9		तिरुवलम THIRUVALEM	0%	98%	2%	2%	11	814	737	772
10		वेमगिरी VEMAGIRI	0%	93%	7%	7%	54	813	744	782
1	पूर्वोत्तर क्षेत्र NER	बिस्वनाथ चौराई BISWANATH CHARIALI (400 kV)	0%	100%	0%	0%	0	411	391	401
2		बोंगाईगांव BONGAIGAON (400 kV)	0%	100%	0%	0%	0	414	397	407
3		बोंगाईगांव टीपीएस BONGAIGAON TPS (400 kV)	0%	100%	0%	0%	0	417	401	410
4		इम्फाल IMPHAL (400 kV)	0%	100%	0%	0%	0	419	391	405
5		बर्निहाट BYRNHAT (400 kV)	0%	100%	0%	0%	0	419	402	411
6		कामेंग KAMENG (400 kV)	0%	100%	0%	0%	0	412	394	403
7		अज़ारा AZARA (400 kV)	0%	100%	0%	0%	0	402	391	397
8		मिसा MISA (400 kV)	0%	100%	0%	0%	0	413	393	403
9		न्यू मारियानी NEW MARIANI (400 kV)	0%	100%	0%	0%	0	416	396	405
10		न्यू कोहिमा NEW KOHIMA (400 kV)	0%	100%	0%	0%	0	419	395	407
11		पालाताना PALATANA (400 kV)	0%	100%	0%	0%	0	413	401	408
12		पुबेकचनबारी PK BARI (400 kV)	0%	100%	0%	0%	0	411	393	403
13		रंगानादी RANGANADI (400 kV)	0%	100%	0%	0%	0	419	400	409
14		सिलचर SILCHAR (400 kV)	0%	100%	0%	0%	0	417	398	408
15		सूर्ययामोनिनगर SURJYAMANINAGAR (400 kV)	0%	100%	0%	0%	0	409	393	402
16		थोबाल THOUBAL (400 kV)	0%	100%	0%	0%	0	405	381	391

All listed stations are 765 kV stations unless otherwise mentioned

*Percentage is calculated w.r.t. Time of one month.

23.List of Outages of Elements monitored by NLDC for the month of May-2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Category	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
Inter Regional Elements										
1	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-I	HVDC	WR, NR	Adani Trans Ind Ltd	MO	01-May-2023 00:00	REVERSE THE DIRECTION FROM WR-NR TO NR-WR (CONTROL THE LOADING OF BHINMAL-ZERDA	08-May-2023 21:17	189:17:00	0
2	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-II	HVDC	WR, NR	Adani Trans Ind Ltd	MO	01-May-2023 00:00	REVERSE THE DIRECTION FROM WR-NR TO NR-WR (CONTROL THE LOADING OF BHINMAL-ZERDA	08-May-2023 21:24	189:24:00	0
3	+/- 800kV HVDC Champa - Kurukshetra Pole-III	HVDC	WR, NR	POWERGRID	MO	01-May-2023 00:00	Voltage Regulation	08-May-2023 14:02	182:02:00	0
4	+/- 800kV HVDC Champa - Kurukshetra Pole-IV	HVDC	WR, NR	POWERGRID	MO	01-May-2023 00:00	Voltage Regulation	08-May-2023 14:33	182:33:00	0
5	400KV-BINAGURI-BONGAIGAON-1	Line	ER, NER	ER-II	SO	01-May-2023 00:00	Reconductoring works by replacement of old Moose Conductor by New HTLS Conductor	23-May-2023 17:26	545:26:00	0
6	765 kV-JHARSUGUDA-RAIPUR PS (DURG)-I	Line	ER, WR	POWERGRID	MO	01-May-2023 00:00	Voltage Regulation	01-Jun-2023 00:00	744:00:00	0
7	800kV HVDC AGRA-BNC Pole-I	HVDC	NR, NER	POWERGRID	MO	01-May-2023 00:00	Voltage Regulation	01-Jun-2023 00:00	744:00:00	0
8	800kV HVDC AGRA-BNC Pole-II	HVDC	NR, NER	POWERGRID	MO	01-May-2023 00:00	Voltage Regulation	14-May-2023 18:38	330:38:00	0
9	132kV Rihand - Nagar Untari Ckt-I	Line	NR, ER	SLDC	SO	01-May-2023 11:30	Replacemnet of old isolator with new one	09-May-2023 00:30	181:00:00	0
10	400kV Binaguri - Bongaigaon Ckt-II	Line	ER, NER	POWERGRID	SE	01-May-2023 15:50	De-capped Pilot insulator string at T0179 due to lightening	01-May-2023 19:49	03:59:00	0
11	132kV Sahupuri - Karmanasa Ckt-I	Line	ER, NR	UPPCL/BSPHCL	TL	01-May-2023 17:27	sahupuri:- B-N, 4km, 5.37kA	01-May-2023 20:28	03:01:00	1
12	220kV Malanpur - Auraiya Ckt-I	Line	WR, NR	MPPTCL/UPPCL	TL	01-May-2023 19:45	Malanpur indication- YG phase, Zone-I, Location- 86.36 km Fault current malanpur end Y-phase 1928 Amp. , G-1944 Amp. Auraiya indication- Y phase, Zone-I, Location- 51.50 km Fault current Auraiya end Y-phase 2.729 KA.	02-May-2023 11:01	15:16:00	1
13	400kV Alipurduar - Bongaigaon Ckt-I	Line	ER, NER	POWERGRID	SE	02-May-2023 10:05	critical conductor stand cut at location 22A/1	02-May-2023 20:29	10:24:00	0
14	400kV Zerda - Kankroli Ckt-I	Line	WR, NR	GETCO/POWERGRID	TS	02-May-2023 12:51	Kankroli: B-N, 3.8kA, 97.68KM	02-May-2023 14:10	01:19:00	1
15	70 KV VINDHYACHAL(PG) POLE-2	HVDC	NR, WR	POWERGRID	SO	02-May-2023 13:15	FOR INTERNAL INSPECTION OF BLOCK#2 NORTH SIDE T12 CONVERTER TRANSFORMER HVDC Block 1 will remain in Service during sais shutdown period.	15-May-2023 07:04	305:49:00	0
16	400kV Alipurduar - Bongaigaon Ckt-II	Line	ER, NER	POWERGRID	So	03-May-2023 07:56	A critical conductor strand cut at location 30/0	03-May-2023 17:04	09:08:00	0
17	132kV Rihand - Garwah Ckt-I	Line	ER, NR	UPPCL/SEB	TL	04-May-2023 11:34	Zone-1, distance- 101.5 KM, fault current- Ia-0.48KA, Ib-0.02KA, Ic-0.02KA.	04-May-2023 20:43	09:09:00	1
18	220KV-MALANPUR-AURIYA-1	Line	WR, NR	MP	SO	08-May-2023 11:48	FOR LINE MAINTENANCE WORK	08-May-2023 19:50	08:02:00	0
19	132kV Rihand - Nagar Untari Ckt-I	Line	NR, ER	SLDC	SO	08-May-2023 12:42	Replacement of Isolator of 132KV Pipri-Garhwa Feeder	14-May-2023 00:38	131:56:00	0
20	220KV-BUDHIPADAR-RAIGARH-1	Line	ER, WR	GRIDCO	SO	09-May-2023 10:52	Trimming of tree branches at loc no. 35 to 40, 77 to 80, 105 to 109 & tightening of jumpers of the line & also tightening of jumper & clamp of bay equipment's	09-May-2023 18:35	07:43:00	0
21	+/- 800kV HVDC Champa - Kurukshetra Pole-II	HVDC	WR, NR	POWERGRID	TP	10-May-2023 22:24	Tripped due to software malfunction at Kurukshtra end.	10-May-2023 23:27	01:03:00	1
22	+/- 800kV HVDC Champa - Kurukshetra Pole-IV	HVDC	WR, NR	POWERGRID	TP	10-May-2023 22:24	software malfunction	11-May-2023 00:25	02:01:00	1
23	220KV-BUDHIPADAR-KORBA-1	Line	ER,WR	GRIDCO	SO	11-May-2023 08:08	Trimming of tree branches at loc no. 35 to 40, 77 to 80, 105 to 109 & tightening of jumpers of the line & also tightening of jumper & clamp of bay equipment's	11-May-2023 23:05	14:57:00	0
24	400KV-JHARSUGUDA-RAIGARH-4	Line	ER, WR	PG (ODISHA PROJECT)	SO	11-May-2023 11:16	Direct connectivity & removal of Vedanta LIL0 point at Loc-298 & 298A/299 of PGCIL Sundargarh-Raigarh 400KV Line -4	17-May-2023 11:34	144:18:00	0
25	220KV-MEHGAON-AURIYA-1	Line	WR, NR	MP	SO	11-May-2023 11:31	FOR LINE MAINTENANCE WORK	11-May-2023 18:06	06:35:00	0
26	400kV Biharshariff - Balia Ckt-I	Line	ER, NR	POWERGRID	SE	12-May-2023 09:49	for attending Hot Spot in Y Ph Line Isolator (89L)	12-May-2023 18:38	08:49:00	0
27	+/- 800kV HVDC Champa - Kurukshetra Pole-I	HVDC	WR, NR	POWERGRID WR1	SO	13-May-2023 06:40	SCADA Database Upgradation of New ICT-3 at Kurukshetra end	14-May-2023 23:23	40:43:00	0
28	+/- 800kV HVDC Champa - Kurukshetra Pole-II	HVDC	WR, NR	POWERGRID WR1	SO	13-May-2023 06:41	SCADA Database Upgradation of New ICT-3 at Kurukshetra end	14-May-2023 22:43	40:02:00	1
29	+/- 800kV HVDC Champa - Kurukshetra Pole-III	HVDC	WR, NR	POWERGRID WR1	SO	13-May-2023 06:44	SCADA Database Upgradation of New ICT-3 at Kurukshetra end	14-May-2023 23:31	40:47:00	0
30	+/- 800kV HVDC Champa - Kurukshetra Pole-IV	HVDC	WR, NR	POWERGRID WR1	SO	13-May-2023 06:45	SCADA Database Upgradation of New ICT-3 at Kurukshetra end	14-May-2023 23:02	40:17:00	1
31	765kV Sasaram - Fatehpur Ckt-I	Line	ER, NR	POWERGRID	TS	14-May-2023 11:33	Line tripped at Fatehpur only due to DT received from Sasaram end.	14-May-2023 12:20	00:47:00	1
32	220kV Ponda - Ambewadi Ckt-I	Line	WR, SR	GOA/KPTCL	TL	15-May-2023 02:45	Zone 1, C-N, Fault distance 58 kms, Ic=547.5 Amps	15-May-2023 19:26	16:41:00	1
33	220kV Xeldom - Ambewadi Ckt-I	Line	WR, SR	GOA/KPTCL	TL	15-May-2023 02:45	Zone 1, Y-Phase, Dist: 48 kms, Fault Current : 0.55 ka.	15-May-2023 03:39	00:54:00	1
34	+/- 800kV HVDC Champa - Kurukshetra Pole-I	HVDC	WR, NR	POWERGRID WR1	SO	15-May-2023 05:30	Onload testing of HVDC software	16-May-2023 07:55	26:25:00	0
35	+/- 800kV HVDC Champa - Kurukshetra Pole-II	HVDC	WR, NR	POWERGRID WR1	SO	15-May-2023 05:30	Onload testing of HVDC software	16-May-2023 07:55	26:25:00	1
36	+/- 800kV HVDC Champa - Kurukshetra Pole-III	HVDC	WR, NR	POWERGRID WR1	SO	15-May-2023 05:30	Onload testing of HVDC software	16-May-2023 07:55	26:25:00	0

NLDC Outage report of Month May 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
37	+/- 800kV HVDC Champa - Kurukshetra Pole-IV	HVDC	WR, NR	POWERGRID WR1	SO	15-May-2023 05:30	Onload testing of HVDC software	16-May-2023 07:55	26:25:00	1
38	400kV Sasaram - Allahabad Ckt-I	Line	ER, NR	POWERGRID	MO	15-May-2023 10:32	Voltage Regulation	15-May-2023 20:49	10:17:00	0
39	220kV Xeldom - Ambewadi Ckt-I	Line	WR, SR	GOA/KPTCL	TL	17-May-2023 03:56	Zone: 1, Ph B-N, Dist: 25.8kms, Fault Current: 0.751kA.	17-May-2023 04:43	00:47:00	2
40	220kV Xeldom - Ambewadi Ckt-I	Line	WR, SR	GOA/KPTCL	TL	17-May-2023 04:43	The 220kv Ambewadi xeldem line which was tripped at 4.43 hrs of today on B-N fault	17-May-2023 18:45	14:02:00	3
41	+/- 800kV HVDC Champa - Kurukshetra Pole-I	HVDC	WR, NR	POWERGRID	TS	18-May-2023 00:59	Tripped on External Block	18-May-2023 12:26	11:27:00	1
42	+/- 800kV HVDC Champa - Kurukshetra Pole-II	HVDC	WR, NR	POWERGRID	TL	18-May-2023 00:59	Tripped on DC line Fault.	18-May-2023 05:39	04:40:00	2
43	+/- 800kV HVDC Champa - Kurukshetra Pole-III	HVDC	WR, NR	POWERGRID	TL	18-May-2023 00:59	Tripped on DC line Fault.	18-May-2023 07:21	06:22:00	1
44	+/- 800kV HVDC Champa - Kurukshetra Pole-IV	HVDC	WR, NR	POWERGRID	TL	18-May-2023 00:59	Tripped on DC line Fault.	18-May-2023 06:19	05:20:00	2
45	220kV Ponda - Ambewadi Ckt-I	Line	WR, SR	GOA/KPTCL	SO	18-May-2023 02:13	to open the CB of 220kV Ambewadi Ponda Line at Ponda S/s and idle charged from ambewadi end	01-Jun-2023 00:00	333:47:00	1
46	+/- 800kV HVDC Champa - Kurukshetra Pole-II	HVDC	WR, NR	POWERGRID	TS	18-May-2023 06:19	due to T- zone Protection operated at champa	18-May-2023 10:47	04:28:00	3
47	+/- 800kV HVDC Champa - Kurukshetra Pole-IV	HVDC	WR, NR	POWERGRID	TS	18-May-2023 06:19	due to T- zone Protection operated at champa	18-May-2023 09:19	03:00:00	3
48	220kV Alipurduar - Salakati Ckt-I	Line	ER, NR	POWERGRID	SE	19-May-2023 09:44	Replacement of severely damaged TLA at Loc-291 due to heavy lightening	19-May-2023 17:52	08:08:00	0
49	220kV-PONDA-AMBEWADI-1	Line	WR, SR	Goa	SO	21-May-2023 07:52	Annual Premonsoon Maintenance Shutdown	21-May-2023 18:36	10:44:00	0
50	220kV-XELDEM-AMBEWADI-1	Line	WR, SR	Goa	SO	21-May-2023 07:52	Annual Premonsoon Maintenance Shutdown	21-May-2023 18:35	10:43:00	0
51	765kV Angul - Srikaulam Ckt-II	Line	ER, SR	POWERGRID	TL	21-May-2023 14:46	Y to B fault, Iy=5.2KA, Ib=4.4KA, angul end distance=481.1km	21-May-2023 16:06	01:20:00	1
52	132kV Rihand - Garwah Ckt-I	Line	ER, NR	UPPCL/ISEB	TL	21-May-2023 22:18	CT blast occurred at 132 KV Roberzganj	22-May-2023 02:35	04:17:00	2
53	132kV Rihand - Nagar Untari Ckt-I	Line	ER, NR	UPPCL/ISEB	TL	21-May-2023 22:20	CT blast occurred at 132 KV Roberzganj	22-May-2023 02:42	04:22:00	1
54	220kV-PONDA-AMBEWADI-1	Line	WR, SR	Goa	SO	22-May-2023 07:10	FOR REPLACEMENT OF SUSPENSION INSULATOR	31-May-2023 19:38	228:28:00	0
55	765kV-FATEHPUR-PUSAULI-1	Line	ER, NR	ER-I	SO	22-May-2023 09:20	REPLACEMENT OF INSULATORS AT MAJOR CROSSING LOCATIONS	22-May-2023 20:24	11:04:00	0
56	220kV Xeldom - Ambewadi Ckt-I	Line	WR, SR	GOA/KPTCL	TL	22-May-2023 22:06	Zone -1, Fault Distance :38.47 KM Fault dis :38.47 KM Fault current-Ia 3.56 KA , Ib-213.3A , Ic-644.9A	23-May-2023 15:16	17:10:00	4
57	765kV Sasaram - Fatehpur Ckt-I	Line	ER, NR	POWERGRID	SO	23-May-2023 09:37	REPLACEMENT OF INSULATORS AT MAJOR CROSSING LOCATIONS	23-May-2023 21:02	11:25:00	1
58	400kV Binaguri - Bongaigaon Ckt-II	Line	ER, NR	POWERGRID	SO	24-May-2023 09:03	Re- Conductoring work under NERSS - XII package	08-Jun-2023 16:30	367:27:00	0
59	765kV-FATEHPUR-PUSAULI-1	Line	ER, NR	ER-I	SO	24-May-2023 09:44	REPLACEMENT OF INSULATORS AT MAJOR CROSSING LOCATIONS	24-May-2023 20:18	10:34:00	0
60	132kV Anpara - Morwa Ckt-I	Line	WR, NR	UPPCL/MPPT CL	TL	24-May-2023 10:53	O/C R phase, 86H/5 trip relay optd	24-May-2023 13:58	03:05:00	1
61	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-II	HVDC	WR, NR	Adani Trans Ind Ltd	TL	24-May-2023 12:18	DC line fault location Tower no. 349	24-May-2023 16:02	03:44:00	1
62	400kV Bhadravati - Ramagundam Ckt-I	Line	WR, SR	POWERGRID	TL	24-May-2023 15:03	tripped on Y-N fault	24-May-2023 16:58	01:55:00	1
63	765kV Sasaram - Fatehpur Ckt-I	Line	ER, NR	POWERGRID	TS	24-May-2023 21:08	plcc problem	25-May-2023 00:41	03:33:00	2
64	132kV Sahupuri - Karmanasa Ckt-I	Line	ER, NR	UPPCL/BSPHCL	TL	25-May-2023 05:47	G-nd PU Zone 1 trip Dist 4.5 km IL1 5.86 KL1 IL2 0.07K IL3 0.07K G-nd PU Zone 1 trip Dist 4.5 km IL1 5.86 KL1 IL2 0.07K IL3 0.07K	25-May-2023 10:46	04:59:00	2
65	+/- 800kV HVDC Raigarh - Pugalur Pole-III	HVDC	SR, WR	pgsr2	SO	25-May-2023 07:51	AMP Works of Pole-3 at Raigarh & Pugalur Substations	26-May-2023 18:53	35:02:00	0
66	765kV-FATEHPUR-PUSAULI-1	Line	ER, NR	ER-I	SO	25-May-2023 09:10	REPLACEMENT OF INSULATORS AT MAJOR CROSSING LOCATIONS	25-May-2023 22:06	12:56:00	0
67	+/- 800kV HVDC Champa - Kurukshetra Pole-I	HVDC	WR, NR	POWERGRID	TL	25-May-2023 09:25	issue in measurement panel DCCT, Pole-2 blocked by CAT B from Pole-4 . Pole-1 and Pole-3 blocked due to DMR-2 transient fault. issue in measurement panel DCCT, Pole-2 blocked by CAT B from Pole-4 . Pole-1 and Pole-3 blocked due to DMR-2 transient fault.	25-May-2023 10:34	01:09:00	2
68	+/- 800kV HVDC Champa - Kurukshetra Pole-II	HVDC	WR, NR	POWERGRID	TL	25-May-2023 09:25	issue in measurement panel DCCT, Pole-2 blocked by CAT B from Pole-4 . Pole-1 and Pole-3 blocked due to DMR-2 transient fault. issue in measurement panel DCCT, Pole-2 blocked by CAT B from Pole-4 . Pole-1 and Pole-3 blocked due to DMR-2 transient fault.	25-May-2023 11:22	01:57:00	4
69	+/- 800kV HVDC Champa - Kurukshetra Pole-III	HVDC	WR, NR	POWERGRID	TL	25-May-2023 09:25	issue in measurement panel DCCT, Pole-2 blocked by CAT B from Pole-4 . Pole-1 and Pole-3 blocked due to DMR-2 transient fault.	25-May-2023 11:08	01:43:00	2
70	+/- 800kV HVDC Champa - Kurukshetra Pole-IV	HVDC	WR, NR	POWERGRID	TS	25-May-2023 09:25	issue in measurement panel DCCT, Pole-2 blocked by CAT B from Pole-4 . Pole-1 and Pole-3 blocked due to DMR-2 transient fault.	25-May-2023 15:29	06:04:00	4
71	765kV Gwalior - Phagi Ckt-I	Line	WR, NR	POWERGRID/R RVPNL	TS	25-May-2023 22:29	Tie breaker & Main C.B. Tripped at Phagi End.	26-May-2023 10:04	11:35:00	1
72	220kV Xeldom - Ambewadi Ckt-I	Line	WR, SR	GOA/KPTCL	TL	25-May-2023 22:37	Tripped from Xeldem end.Fault Current: Ia: 468.9A, Ib:393.7A, Ic:372.9A.	25-May-2023 23:27	00:50:00	5
73	400kV RAPP - Shujalpur Ckt-II	Line	WR, NR	NPCIL/POWER GRID	TS	26-May-2023 01:20	"TEE-2 Protection OPTD".	26-May-2023 21:37	20:17:00	1

NLDC Outage report of Month May 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
74	400kV Zerda - Kankroli Ckt-I	Line	WR, NR	GETCO/POWER GRID	TS	26-May-2023 03:25	Fault details at Zerda end: 44.1KM/6.7KA.	26-May-2023 04:40	01:15:00	2
75	220kV Xeldom - Ambewadi Ckt-I	Line	WR, SR	GOA/KPTCL	TL	26-May-2023 07:10	Fault Current: Ia: 440A, Ib:3417A, Ic:295A, Trip 86 actuated.	26-May-2023 08:42	01:32:00	6
76	132kV Rihand - Nagar Untari Ckt-I	Line	ER, NR	UPPCL/JSEB	TL	26-May-2023 10:41	Phase to earth fault R-N Zone 1, Fault current 2.07kA, Distance 46.85km from Rihand end	26-May-2023 16:50	06:09:00	2
77	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-I	HVDC	WR, NR	Adani Trans Ind Ltd	TS	26-May-2023 10:45	due to fault in VCS pump-2	26-May-2023 12:48	02:03:00	1
78	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-I	HVDC	WR, NR	Adani Trans Ind Ltd	TS	26-May-2023 16:19	220V DC power cable was found faulty	26-May-2023 18:14	01:55:00	2
79	132kV Sahupuri - Karmanasa Ckt-I	Line	ER, NR	UPPCL/BSPHCL	TL	26-May-2023 16:43	R phase, Zone 1, 3.16KA, Distance 17.4 km from Sahupuri end	26-May-2023 19:08	02:25:00	3
80	220kV Bhanpura - Ranpur Ckt-I	Line	WR, NR	MPPTCL/RRVPN L	TL	26-May-2023 20:09	Relay Indication at Ranpur End: M2 Relay Details: E/F in Y Phase Fault current: IL1: 0.30KA IL2: 0.61KA IL3: 0.35KA Zone 1 General trip M1 Relay Details: Fault Current: IL1: 298.311A IL2: 615.995A IL3: 387.907A ILN: 1234.423A 86A & 86B operated Dist:43.5km	27-May-2023 16:34	20:25:00	1
81	220KV-XELDEM-AMBEWADI-1	Line	WR, SR	Goa	SO	27-May-2023 07:28	FOR REPLACEMENT OF SUSPENSION INSULATOR	27-May-2023 17:59	10:31:00	0
82	+/- 800kV HVDC Champa - Kurukshetra Pole-II	HVDC	WR, NR	POWERGRID	SE	27-May-2023 08:28	to rectify broken jumper	27-May-2023 16:29	08:01:00	4
83	+/- 800kV HVDC Champa - Kurukshetra Pole-IV	HVDC	WR, NR	POWERGRID	SO	27-May-2023 08:30	to rectify broken jumper	27-May-2023 16:26	07:56:00	4
84	+/- 800kV HVDC Champa - Kurukshetra Pole-I	HVDC	WR, NR	POWERGRID	SE	27-May-2023 15:59	For DMR connection	27-May-2023 16:21	00:22:00	2
85	+/- 800kV HVDC Champa - Kurukshetra Pole-III	HVDC	WR, NR	POWERGRID	SE	27-May-2023 16:00	For DMR Connection	27-May-2023 16:23	00:23:00	2
86	+/- 800kV HVDC Champa - Kurukshetra Pole-IV	HVDC	WR, NR	POWERGRID	SO	28-May-2023 07:41	sparking in filter bank	28-May-2023 08:29	00:48:00	4
87	500 KV HVDC MAHINDERGARH(APL)-ADANI MUNDRA(A)	HVDC	NR, WR	ADANI	SO	28-May-2023 07:43	Outage being availed to carry out earthwire replacement with OPGW in creek area	28-May-2023 17:02	09:19:00	0
88	+/- 800kV HVDC Champa - Kurukshetra Pole-I	HVDC	WR, NR	POWERGRID	TS	28-May-2023 12:10	DC filter over load	28-May-2023 13:14	01:04:00	3
89	+/- 800kV HVDC Champa - Kurukshetra Pole-III	HVDC	WR, NR	POWERGRID	TS	28-May-2023 12:10	due to DC Filter Overload Alarm	28-May-2023 13:25	01:15:00	3
90	+/- 500kV HVDC Talcher - Kolar Pole-II	HVDC	ER, SR	POWERGRID	TS	28-May-2023 17:47	due to operation of PRV OF OLTC of Pole-2 y-phase converter transformer	29-May-2023 16:03	22:16:00	1
91	765KV-SOLAPUR-RAICHUR-1	Line	WR, SR	POWERGRID WR1	SO	29-May-2023 08:25	Line terminal equipments AMP in Substation & Rectification of Shutdown defects in Transmission line (FY 2022-23)	30-May-2023 21:46	37:21:00	0
92	765KV-SOLAPUR-RAICHUR-1 L/R@ SOLAPUR - 765KV	Line Reactor	WR, SR	POWERGRID WR1	SO	29-May-2023 08:43	OCC 119// Note : Dia to be kept open// Differed on 2nd// SRPC consent given for 29th	30-May-2023 21:46	37:03:00	0
93	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-I	HVDC	WR, NR	Adani Trans Ind Ltd	MO	29-May-2023 10:20	To control loading of 400kV Bhinmal-Zerda	29-May-2023 16:03	05:43:00	2
94	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-II	HVDC	WR, NR	Adani Trans Ind Ltd	MO	29-May-2023 10:26	To control loading of 400kV Bhinmal-Zerda	29-May-2023 16:11	05:45:00	1
95	220kV Korba(East) - Budhipadar Ckt-I	Line	WR, ER	CSPTCL/GRIDCO	MO	29-May-2023 12:01	To control loading on Korba West ICT	29-May-2023 14:32	02:31:00	0
96	220kV Mudshingi - Chikkodi Ckt-I	Line	WR, SR	MSETCL/KPTCL	SO	29-May-2023 14:41	ESD to attend hot spot observed in thermoscanning at loc no. 305, Y ph. (Temp. 87.5 deg.)	30-May-2023 20:01	29:20:00	0
97	765kV Gwalior - Agra Ckt-II	Line	WR, NR	POWERGRID	TL	29-May-2023 15:26	Y-N fault Iy= 4.6 KA, D= 129 Km from gwalior	29-May-2023 16:20	00:54:00	1
98	220KV-XELDEM-AMBEWADI-1	Line	WR, SR	Goa	SO	30-May-2023 07:28	FOR REPLACEMENT OF SUSPENSION INSULATOR	30-May-2023 17:21	09:53:00	0
99	500 KV HVDC MAHINDERGARH(APL)-ADANI MUNDRA(A)	HVDC	NR, WR	ADANI	SO	31-May-2023 07:42	To carry out earthwire replacement with OPGW in creek area	31-May-2023 13:00	05:18:00	0
100	400kV Alipurduar - Bongaigaon Ckt-II	Line	ER, NR	POWERGRID	SE	31-May-2023 10:38	To attend top phase one deadend which is slipped slightly at Tower No 241 and attached on the load of the helical gripper.	31-May-2023 19:48	09:10:00	0
101	+/- 500kV HVDC APL Mundra - Mohindargarh Pole-II	HVDC	WR, NR	Adani Trans Ind Ltd	TL	31-May-2023 17:03	Pole-2 tripped on DC Line Fault	31-May-2023 20:56	03:53:00	2

Transnational Elements

1	400kV Alipurduar - Jigmeling (bypass at Punatsangchhu)	Line	ER, BHUTAN	POWERGRID/BHUTAN	MO	01-May-2023 00:00	Voltage Regulation	01-Jun-2023 00:00	744:00:00	0
2	400KV Binaguri -Tala Ckt-II	Line	ER, BHUTAN	POWERGRID/THEP	MO	01-May-2023 00:00	Voltage Regulation	01-May-2023 21:42	21:42:00	0
3	400KV Binaguri -Tala Ckt-IV	Line	ER, BHUTAN	POWERGRID/THEP	SO	04-May-2023 11:14	for GDM(Gas Density Monitoring)	06-May-2023 11:14	48:00:00	0
4	400kV Binaguri - Malbase Ckt-I	Line	ER, BHUTAN	POWERGRID/THEP	SE	06-May-2023 09:43	For Attending SF6 gas leakage	06-May-2023 18:42	08:59:00	0
5	400KV Binaguri -Tala Ckt-II	Line	ER, BHUTAN	POWERGRID/THEP	TS	07-May-2023 22:13	DT RECEIVED at Binaguri	08-May-2023 11:34	13:21:00	1
6	220kV Birpara - Chukha Ckt-I	Line	ER, BHUTAN	POWERGRID/BHUTAN	SO	08-May-2023 10:16	changing of complete set of flashover disc insulators	08-May-2023 20:14	09:58:00	0
7	220kV Birpara - Malbase Ckt-I	Line	ER, BHUTAN	POWERGRID/BHUTAN	SE	08-May-2023 13:36	For attending damaged conductor found during patrolling at loc 43 at Bot ph of 220KV BRP-MLB SC Line	08-May-2023 19:44	06:08:00	0

NLDC Outage report of Month May 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
8	400kV Binaguri -Tala Ckt-IV	Line	ER, BHUTAN	POWERGRID/T HEP	MO	08-May-2023 18:37	Voltage Regulation	20-May-2023 15:56	285:19:00	0
9	400KV-ALIPURDUAR (PG)-JIGMELLING-1	Line	ER, BHUTAN	ER-II	SO	09-May-2023 08:14	Replacement of defective insulators due to lightening	09-May-2023 19:21	11:07:00	0
10	220kV Birpara - Chukha Ckt-I	Line	ER, BHUTAN	POWERGRID/B HUTAN	TL	09-May-2023 08:24	Chukha End: B-N fault, Zone-1,9.45kA (B-ph jumper) Birpara End: B-N fault.	13-May-2023 16:17	103:53:00	1
11	400kV Alipurduar - Jigmeling Ckt-I	Line	ER, BHUTAN	POWERGRID/B HUTAN	MO	09-May-2023 19:21	Voltage Regulation	18-May-2023 13:06	209:45:00	0
12	220kV Birpara - Chukha Ckt-II	Line	ER, BHUTAN	POWERGRID/B HUTAN	TS	11-May-2023 08:54	bus bar protection operated at chukha	11-May-2023 09:55	01:01:00	1
13	132kV Raxul - Parwanipur CKT-I	Line	ER, NEPAL	BSHPCL/NEPAL	TL	14-May-2023 19:25	IA 470.7 amp IB 478.8 amp 1C 482.8 amp IN 36 amp	14-May-2023 23:07	03:42:00	1
14	400kV Binaguri -Tala Ckt-I	Line	ER, BHUTAN	POWERGRID/T HEP	SO	15-May-2023 10:26	for installation of transmission line surge arrester	17-May-2023 11:31	49:05:00	0
15	132kV Surajmaninagar - South Komilla Ckt-I	Line	NER, BANGLADESH	TSECL/PGCB	SE	15-May-2023 22:26	to refill SF6 Gas	15-May-2023 23:31	01:05:00	0
16	400kV Binaguri -Tala Ckt-I	Line	ER, BHUTAN	POWERGRID/T HEP	MO	17-May-2023 16:57	Voltage Regulation	18-May-2023 09:10	16:13:00	0
17	400kV Binaguri -Tala Ckt-I	Line	ER, BHUTAN	POWERGRID/T HEP	SE	18-May-2023 09:15	For sag rectification of earth wire in Span 289-290 which is found in loosen condition due to heavy storm on dtd.16.05.2023 which created clearance issue	18-May-2023 19:30	10:15:00	0
18	400KV Alipurduar - Jigmeling Ckt-II	Line	ER, BHUTAN	POWERGRID/B HUTAN	MO	18-May-2023 15:20	Voltage Regulation	19-May-2023 08:40	17:20:00	0
19	400kV Binaguri -Tala Ckt-I	Line	ER, BHUTAN	POWERGRID/T HEP	MO	18-May-2023 19:30	Voltage Regulation	23-May-2023 11:08	111:38:00	0
20	400kV Binaguri -Tala Ckt-I	Line	ER, BHUTAN	POWERGRID/T HEP	MO	18-May-2023 19:30	Voltage Regulation	23-May-2023 11:08	111:38:00	0
21	400KV-ALIPURDUAR (PG)-JIGMELLING-2	Line	ER, BHUTAN	ER-II	SO	19-May-2023 08:40	Replacement of defective insulators due to lightening	19-May-2023 19:47	11:07:00	0
22	400KV Alipurduar - Jigmeling Ckt-II	Line	ER, BHUTAN	POWERGRID/B HUTAN	MO	19-May-2023 20:03	Voltage Regulation	20-May-2023 08:50	12:47:00	0
23	220kV Birpara - Chukha Ckt-I	Line	ER, BHUTAN	POWERGRID/B HUTAN	TL	19-May-2023 22:55	RY Phase fault 51 kms towards birpara from chukha Fault Current R Phase: 2.285 kA , Y Phase : 2.372kA	19-May-2023 23:34	00:39:00	2
24	400KV-ALIPURDUAR (PG)-JIGMELLING-2	Line	ER, BHUTAN	ER-II	SO	20-May-2023 09:15	Replacement of defective insulators due to lightening	20-May-2023 17:57	08:42:00	0
25	400kV Alipurduar - Jigmeling Ckt-II	Line	ER, BHUTAN	POWERGRID/B HUTAN	MO	20-May-2023 17:57	Voltage Regulation	21-May-2023 08:03	14:06:00	0
26	400KV-ALIPURDUAR (PG)-JIGMELLING-2	Line	ER, BHUTAN	ER-II	SO	21-May-2023 08:05	Replacement of defective insulators due to lightening	21-May-2023 20:11	12:06:00	0
27	400KV Alipurduar - Jigmeling Ckt-II	Line	ER, BHUTAN	POWERGRID/B HUTAN	MO	21-May-2023 20:11	Voltage Regulation	22-May-2023 08:54	12:43:00	0
28	400KV-ALIPURDUAR (PG)-JIGMELLING-2	Line	ER, BHUTAN	ER-II	SO	22-May-2023 08:54	Replacement of defective insulators due to lightening	22-May-2023 19:06	10:12:00	0
29	400kV Alipurduar - Jigmeling Ckt-II	Line	ER, BHUTAN	POWERGRID/B HUTAN	MO	22-May-2023 19:06	Voltage Regulation	23-May-2023 09:03	13:57:00	0
30	400kV Binaguri - Malbase Ckt-I	Line	ER, BHUTAN	POWERGRID/T HEP	SO	23-May-2023 10:02	for installation of Transmission line Surge Arrester at location TKS #40.	24-May-2023 21:46	35:44:00	0
31	400KV-ALIPURDUAR (PG)-JIGMELLING-2	Line	ER, BHUTAN	ER-II	SO	23-May-2023 10:02	Replacement of defective insulators due to lightening	23-May-2023 18:57	08:55:00	0
32	400KV Alipurduar - Jigmeling Ckt-II	Line	ER, BHUTAN	POWERGRID/B HUTAN	MO	23-May-2023 18:57	Voltage Regulation	26-May-2023 08:11	61:14:00	0
33	400KV-ALIPURDUAR (PG)-JIGMELLING-1	Line	ER, BHUTAN	ER-II	SO	26-May-2023 08:39	Replacement of defective insulator due to lightening	26-May-2023 17:19	08:40:00	0
34	400kV Alipurduar - Jigmeling Ckt-I	Line	ER, BHUTAN	POWERGRID/B HUTAN	MO	26-May-2023 17:47	Voltage Regulation	27-May-2023 08:05	14:18:00	0
35	400KV-ALIPURDUAR (PG)-JIGMELLING-1	Line	ER, BHUTAN	ER-II	SO	27-May-2023 08:31	Replacement of defective insulator due to lightening	27-May-2023 18:15	09:44:00	0
36	400KV Alipurduar - Jigmeling Ckt-I	Line	ER, BHUTAN	POWERGRID/B HUTAN	MO	27-May-2023 18:15	Voltage Regulation	28-May-2023 08:04	13:49:00	0
37	400KV-ALIPURDUAR (PG)-JIGMELLING-1	Line	ER, BHUTAN	ER-II	SO	28-May-2023 08:10	Replacement of defective insulator due to lightening	28-May-2023 20:01	11:51:00	0

NLDC Outage report of Month May 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
38	400KV Alipurduar - Jigmeling Ckt-I	Line	ER, BHUTAN	POWERGRID/B HUTAN	MO	28-May-2023 20:01	Voltage Regulation	29-May-2023 09:56	13:55:00	0
39	220kV Birpara - Chukha Ckt-II	Line	ER, BHUTAN	POWERGRID/B HUTAN	SO	29-May-2023 09:20	double tension fitting at tower and install TLSA	29-May-2023 17:07	07:47:00	1
40	400KV-ALIPURDUAR (PG)-JIGMELLING-1	Line	ER, BHUTAN	ER-II	SO	29-May-2023 09:56	Replacement of defective insulator due to lightening	29-May-2023 21:04	11:08:00	0
41	400kV Binaguri -Tala Ckt-IV	Line	ER, BHUTAN	POWERGRID/T HEP	SE	29-May-2023 10:45	For rectification of jumper by replacement at Loc.303 due to flashing occurred in between jumper & tower body due jumper swung in heavy thunderstorm.	29-May-2023 20:20	09:35:00	0
42	220kV Birpara - Chukha Ckt-II	Line	ER, BHUTAN	POWERGRID/B HUTAN	MO	29-May-2023 17:07	Voltage Regulation	30-May-2023 08:59	15:52:00	1
43	400KV Alipurduar - Jigmeling Ckt-II	Line	ER, BHUTAN	POWERGRID/B HUTAN	MO	29-May-2023 22:46	Voltage Regulation	05-Jun-2023 10:30	155:44:00	0
44	220kV Birpara - Chukha Ckt-II	Line	ER, BHUTAN	POWERGRID/B HUTAN	SO	30-May-2023 08:59	double tension fitting at tower and install TLSA	30-May-2023 19:25	10:26:00	1
45	400KV-BINAGURI-TALA-1	Line	ER, BHUTAN	ER-II	SO	30-May-2023 10:47	Measurement of line impedance on parallel circuits	30-May-2023 18:06	07:19:00	0
46	400kV Binaguri -Tala Ckt-II	Line	ER, BHUTAN	POWERGRID/T HEP	SO	30-May-2023 10:48	for GDM (Gas Density Monitoring)	01-Jun-2023 00:00	37:12:00	1
47	220kV Birpara - Chukha Ckt-II	Line	ER, BHUTAN	POWERGRID/B HUTAN	SO	31-May-2023 08:32	double tension fitting at tower and install TLSA	31-May-2023 15:54	07:22:00	1
Northern Region Elements										
1	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	01-May-2023 00:00	Voltage Regulation	01-May-2023 09:01	09:01:00	0
2	765kV Ajmer - Phagi Ckt-II	Line	NR	POWERGRID	MO	01-May-2023 00:00	Voltage Regulation	01-May-2023 06:54	06:54:00	0
3	765KV ANPARA-D - OBRA C	Line	NR		TS	01-May-2023 00:00	Current Transformer of 765 KV Anpara-D to Obra-C Line has blasted at 10.53 Hrs in Y PHASE.then y-n overcurrent , zone 1 tripped in distance protection	09-May-2023 13:21	205:21:00	1
4	765KV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	01-May-2023 00:00	Voltage Regulation	01-May-2023 08:22	08:22:00	0
5	765kV FATEHPUR - AGRA Ckt-II	Line	NR	POWERGRID	MO	01-May-2023 00:00	Voltage Regulation	02-May-2023 20:03	44:03:00	0
6	765kV MEERUT - BHIWANI Ckt-I	Line	NR	POWERGRID	MO	01-May-2023 00:00	Voltage Regulation	01-May-2023 09:39	09:39:00	0
7	765kV ORAI - ALIGARH Ckt-I	Line	NR	POWERGRID	MO	01-May-2023 00:00	Voltage Regulation	08-May-2023 09:31	177:31:00	0
8	765kV PHAGI - BHIWANI Ckt-I	Line	NR	RRVNL/PG	MO	01-May-2023 00:00	Voltage Regulation	03-May-2023 10:01	58:01:00	0
9	765kV Fatehgarh II - Bhadla I Ckt-I	Line	NR	PFTL	SO	12-May-2023 22:56	For flex logic modification in D60 relay.	13-May-2023 00:29	01:33:00	0
10	765kV KANPUR - ALIGARH Ckt-I	Line	NR	POWERGRID	SE	14-May-2023 22:36	To attend damaged insulator string at loc No-455	15-May-2023 03:10	04:34:00	0
11	765kV MOGA - MEERUT Ckt-I	Line	NR	POWERGRID	MO	23-May-2023 23:41	Voltage Regulation	24-May-2023 09:37	09:56:00	0
12	765/400kV 1500MVA ICT-III at Phagi	ICT	NR	Rajasthan/RRV PNL	TS	25-May-2023 22:37	M/T DUE TO LV ISOLATOR HEAVY SPARK,Emergency shutdown to attend LV Isolator 412-89ATR of ICT-3.	26-May-2023 20:15	21:38:00	1
13	765kV KANPUR - ALIGARH Ckt-I	Line	NR	POWERGRID	MO	01-May-2023 13:14	Voltage Regulation	02-May-2023 09:52	20:38:00	0
14	765kV Ajmer - Phagi Ckt-I	Line	NR	POWERGRID	TV	01-May-2023 13:23	Tripped on over voltage	01-May-2023 16:06	02:43:00	1
15	765kV Fatehgarh II - Bhadla I Ckt-I	Line	NR	PFTL	TV	01-May-2023 13:23	Tripped due to Over Voltage	01-May-2023 13:53	00:30:00	1
16	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	TV	01-May-2023 13:24	Tripped on over voltage	01-May-2023 13:41	00:17:00	1
17	765kV Ajmer - Phagi Ckt-I	Line	NR	POWERGRID	MO	01-May-2023 16:09	Voltage Regulation	02-May-2023 07:40	15:31:00	1
18	765KV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	01-May-2023 17:03	Voltage Regulation	02-May-2023 08:17	15:14:00	0
19	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	01-May-2023 17:16	Voltage Regulation	02-May-2023 09:11	15:55:00	0

NLDC Outage report of Month May 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
20	765kV MEERUT - BHIWANI Ckt-I	Line	NR	POWERGRID	MO	02-May-2023 04:01	taken out on over voltage	03-May-2023 09:50	29:49:00	0
21	765kV VARANASI - KANPUR Ckt-II	Line	NR	POWERGRID	TS	02-May-2023 16:41	DT received at kanpur end	02-May-2023 17:52	01:11:00	1
22	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	TP	02-May-2023 16:45	Maloperation	02-May-2023 17:45	01:00:00	2
23	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	02-May-2023 17:04	Voltage regulation	03-May-2023 00:00	06:56:00	0
24	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	02-May-2023 17:57	Voltage Regulation	03-May-2023 08:31	14:34:00	2
25	765kV AJMER - CHITTORGARH Ckt-I	Line	NR	POWERGRID	MO	02-May-2023 21:22	Voltage Regulation	03-May-2023 09:16	11:54:00	0
26	765kV KANPUR - ALIGARH Ckt-I	Line	NR	POWERGRID	MO	02-May-2023 21:23	Voltage Regulation	03-May-2023 06:53	09:30:00	0
27	765kV FATEHPUR - AGRA Ckt-I	Line	NR	POWERGRID	MO	03-May-2023 13:17	Voltage Regulation	04-May-2023 08:01	18:44:00	0
28	765kV MEERUT - BHIWANI Ckt-I	Line	NR	POWERGRID	MO	03-May-2023 13:58	Voltage Regulation	04-May-2023 10:20	20:22:00	0
29	765kV PHAGI - BHIWANI Ckt-II	Line	NR	RRVPNL/PG	MO	03-May-2023 15:56	Voltage Regulation	04-May-2023 09:36	17:40:00	0
30	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	03-May-2023 16:40	Voltage Regulation	04-May-2023 08:26	15:46:00	0
31	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	03-May-2023 17:15	Voltage Regulation	04-May-2023 06:59	13:44:00	0
32	765kV AJMER - CHITTORGARH Ckt-II	Line	NR	POWERGRID	MO	03-May-2023 21:17	Voltage Regulation	04-May-2023 09:11	11:54:00	0
33	765kV KANPUR - ALIGARH Ckt-I	Line	NR	POWERGRID	MO	03-May-2023 21:29	Voltage Regulation	04-May-2023 20:25	22:56:00	0
34	189MVAR 765kV Bus Reactor at Obra-C	Bus Reactor	NR	Uttar Pradesh/UPPTCL	TS	04-May-2023 00:49	Unnao line tripped and at same time 765KV Bus Reactor also tripped because on that day & time 765KV Switchyard charged through only 765KV obra-C-Unnao line.	18-May-2023 17:26	352:37:00	1
35	765kV OBRA-C TO UNNAO	Line	NR		TL	04-May-2023 00:49	B-N fault, Zone-1, Dist. 57.68km, Fault current of 5.8065kA from Unnao end	04-May-2023 14:11	13:22:00	1
36	765/400kV 1500MVA ICT-IV at Jhatikara	ICT	NR	POWERGRID	TS	04-May-2023 01:10	765/400 kV 1500 MVA ICT 4 at Jhatikara tripped on R-Ph differential protection.	04-May-2023 07:42	06:32:00	1
37	765/400kV 1500MVA ICT-II at Bareilly	ICT	NR	POWERGRID	SO	04-May-2023 10:11	AMP WORK	04-May-2023 18:43	08:32:00	0
38	765kV PHAGI - BHIWANI Ckt-I	Line	NR	RRVPNL/PG	MO	04-May-2023 16:12	taken out on over voltage	05-May-2023 10:00	17:48:00	0
39	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	04-May-2023 17:00	taken out on over voltage	05-May-2023 08:32	15:32:00	0
40	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	TV	04-May-2023 17:46	taken out on over voltage	05-May-2023 08:58	15:12:00	3
41	ICT-III at Bhadla-II	ICT	NR		TS	05-May-2023 12:26	Bus bar protection of 400kV Bus-1 at Bhadla-II operated	05-May-2023 15:19	02:53:00	1
42	765kV PHAGI - BHIWANI Ckt-II	Line	NR	RRVPNL/PG	MO	05-May-2023 16:30	Voltage Regulation	06-May-2023 09:18	16:48:00	0
43	765kV LALITPUR - FATEHABAD Ckt-I	Line	NR	LPGL/UPPTCL	TL	05-May-2023 17:30	Y-N fault, Fault current 10.288kA, Dist. 15.60km from Agra Fatehabad(UP).	05-May-2023 18:32	01:02:00	1
44	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	05-May-2023 17:32	Voltage Regulation	06-May-2023 07:50	14:18:00	0
45	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	05-May-2023 17:39	Voltage Regulation	06-May-2023 08:41	15:02:00	0
46	765kV PHAGI - BHIWANI Ckt-I	Line	NR	RRVPNL/PG	MO	06-May-2023 17:19	Voltage Regulation	07-May-2023 09:36	16:17:00	0
47	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	06-May-2023 17:20	Voltage Regulation	07-May-2023 08:53	15:33:00	3
48	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	06-May-2023 17:40	Voltage Regulation	07-May-2023 08:26	14:46:00	0

NLDC Outage report of Month May 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
49	765kV Bikaner - Khetri Ckt-I	Line	NR	BKTL	TS	07-May-2023 15:09	no abnormalities found at Khetri end Tripped form Khetri end due to power swing informed by site	07-May-2023 18:08	02:59:00	1
50	765kV PHAGI - BHIWANI Ckt-II	Line	NR	RRVPNL/PG	MO	07-May-2023 16:58	Voltage Regulation	07-May-2023 20:30	03:32:00	0
51	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	07-May-2023 17:03	Voltage Regulation	08-May-2023 08:13	15:10:00	0
52	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	07-May-2023 17:23	Voltage Regulation	08-May-2023 08:47	15:24:00	0
53	765kV PHAGI - BHIWANI Ckt-I	Line	NR	RRVPNL/PG	TL	07-May-2023 18:23	Y-N, Bhiwani- 90.773KM/ 6.444 kA	14-May-2023 21:42	171:19:00	1
54	765 KV MOGA-MEERUT (PG) CKT-1	Line	NR	POWERGRID	SO	08-May-2023 07:15	for replacement of CLR Polymer Insulators at Tower No. 249,258,386 & 398.	08-May-2023 18:08	10:53:00	0
55	765KV Bara-Mainpuri ckt 2	Line	NR	Uttar Pradesh/UPPT CL	TL	08-May-2023 14:10	E/F in B-ph. ZONE-1 , Distance protection opted. , Fault Current-2465.725A, Fault Distance- 201.4KM.	08-May-2023 19:22	05:12:00	1
56	765/400 KV 1000 MVA ICT 3 AT BHIWANI(PG)	ICT	NR	POWERGRID	SE	08-May-2023 16:53	To take B phase in service and R phase out of service	09-May-2023 02:54	10:01:00	0
57	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	08-May-2023 17:12	Voltage Regulation	09-May-2023 08:24	15:12:00	0
58	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	08-May-2023 18:02	Voltage Regulation	09-May-2023 09:02	15:00:00	3
59	765KV Bara-Mainpuri ckt 2	Line	NR	Uttar Pradesh/UPPT CL	TL	08-May-2023 19:22	E/F in B-ph. ZONE-1 , Distance protection opted. , Fault Current-2465.725A, Fault Distance- 201.4KM.	10-May-2023 04:28	33:06:00	2
60	765kV Fatehgarh II - Bhadla I Ckt-I	Line	NR	PFTL	TV	09-May-2023 12:51	tripped on overvoltage caued by reduction in solar generation. Details awaited.	09-May-2023 13:13	00:22:00	2
61	765kV Fatehgarh II - Bhadla II Ckt-I	Line	NR	PFTL	TV	09-May-2023 12:51	tripped on overvoltage caued by reduction in solar generation. Details awaited.	09-May-2023 13:09	00:18:00	1
62	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	TV	09-May-2023 12:57	Tripped on overvoltage caued by reduction in solar generation.	09-May-2023 13:27	00:30:00	4
63	765/400 KV 1500 MVA ICT 3 AT PHAGI(RS)	ICT	NR	SLDC	SO	09-May-2023 16:59	1. Testing and maintenance of Transforers. 2. Tightening of clamps and connectors	10-May-2023 01:35	08:36:00	0
64	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	09-May-2023 17:07	Voltage Regulation	10-May-2023 08:21	15:14:00	0
65	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	09-May-2023 17:41	Voltage Regulation	10-May-2023 09:05	15:24:00	0
66	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	10-May-2023 17:20	Voltage Regulation	11-May-2023 07:51	14:31:00	0
67	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	10-May-2023 17:53	Voltage Regulation	11-May-2023 08:49	14:56:00	4
68	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	11-May-2023 17:11	Voltage Regulation	12-May-2023 08:05	14:54:00	0
69	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	11-May-2023 17:36	Voltage Regulation	12-May-2023 08:53	15:17:00	0
70	765/400kV 1000MVA ICT-I at Anpara C	ICT	NR	LANCO	TS	11-May-2023 19:34	765/400KV, 1000MVA ICT at 765/400KV Switchyard has been false tripped on Y-Phase LV-WTI Temp High	11-May-2023 21:51	02:17:00	1
71	+/- 500kV HVDC RIHAND - DADRI Pole-II	HVDC	NR	POWERGRID	SE	12-May-2023 02:51	Overheating in Marshalling Box of Turret CT's	12-May-2023 08:00	05:09:00	0
72	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	12-May-2023 17:21	Manually opened due to High Voltage	13-May-2023 07:30	14:09:00	0
73	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	12-May-2023 17:40	Manually opened due to High Voltage	13-May-2023 08:42	15:02:00	4
74	765kV Bikaner - Bhadla II Ckt-I	Line	NR	POWERGRID	SO	12-May-2023 18:32	for Implementation of appropriate flexi-logic to increase the drop out level in GE D60 relay (Main-2):	12-May-2023 19:35	01:03:00	0
75	765kV Bikaner - Bhadla II Ckt-II	Line	NR	POWERGRID	SO	12-May-2023 20:06	for Implementation of appropriate flexi-logic to increase the drop out level in GE D60 relay (Main-2):	12-May-2023 21:08	01:02:00	0
76	765/400 KV 1500 MVA ICT 1 AT BHADLA(PG)	ICT	NR	POWERGRID	SO	12-May-2023 20:48	for AMP work.	13-May-2023 03:25	06:37:00	0

NLDC Outage report of Month May 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
77	765/400 KV 1500 MVA ICT 1 AT BAREILLY_2(PG)	ICT	NR	POWERGRID	SO	13-May-2023 10:02	for AMP work.	13-May-2023 18:41	08:39:00	0
78	765KV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	13-May-2023 17:02	Manually opened due to High Voltage	14-May-2023 08:47	15:45:00	0
79	765KV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	13-May-2023 17:32	Manually opened due to High Voltage	14-May-2023 09:31	15:59:00	0
80	765/400 KV 1500 MVA ICT 2 AT BHADLA(PG)	ICT	NR	POWERGRID	SO	13-May-2023 18:44	for AMP work.	14-May-2023 01:19	06:35:00	0
81	765KV Fatehgarh 2 - Bhadla Ckt-2	Line	NR	POWERGRID NR	SO	13-May-2023 19:11	for D60 relay logic modifications	13-May-2023 20:22	01:11:00	0
82	765KV Fatehgarh II - Bhadla II Ckt-II	Line	NR	PFTL	SO	13-May-2023 20:29	for D60 relay logic modifications	13-May-2023 21:03	00:34:00	0
83	765KV Fatehgarh II - Bhadla II Ckt-I	Line	NR	PFTL	SO	13-May-2023 21:13	for D60 relay flex logic modifications	13-May-2023 22:28	01:15:00	1
84	765KV Fatehgarh II - Bhadla I Ckt-I	Line	NR	PFTL	TL	13-May-2023 21:44	Bhadla site details: R-B fault, 3.7kA, 132km.	14-May-2023 05:21	07:37:00	3
85	765KV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	14-May-2023 15:52	Voltage Regulation	15-May-2023 08:15	16:23:00	4
86	765KV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	14-May-2023 15:57	Voltage Regulation	15-May-2023 07:50	15:53:00	0
87	765KV AJMER - CHITTORGARH Ckt-I	Line	NR	POWERGRID	MO	14-May-2023 16:14	Voltage Regulation	15-May-2023 08:58	16:44:00	0
88	765/400KV 1500MVA ICT-III at Phagi	ICT	NR	Rajasthan/RRV PNL	SE	14-May-2023 18:36	heavy spark on 703-89BT isolator, the CB (703-52B and 703-52T)of ICT-3 tripped manually	14-May-2023 23:03	04:27:00	1
89	765KV ANTA - PHAGI Ckt-II	Line	NR	Rajasthan/RRV PNL	TL	15-May-2023 00:26	At phagi end M1:- Zone-I , Y- phase location= 31.49 KM , M2 :-Z-1, Y-phase Ib= 11.37 Ka , In-11.36KA Location= 31.85 KM At anta End M2:- Y-phase trip , Zone-2, Distance- 173 KM, Ia-1.318KA, Ib-3.96KA, Ic-247.7A	15-May-2023 02:12	01:46:00	1
90	765KV KANPUR - ALIGARH Ckt-I	Line	NR	POWERGRID	MO	15-May-2023 03:10	Voltage Regulation	15-May-2023 09:05	05:55:00	0
91	765/400KV 1000MVA ICT-I at Unnao	ICT	NR	UPPCL	SE	15-May-2023 09:52	For attending hot-spot on 400KV LV side B-phase transformer Isolator.	15-May-2023 13:05	03:13:00	0
92	765KV BHADLA - BIKANER Ckt-I	Line	NR	POWERGRID	TL	15-May-2023 11:51	tripped on phase to phase fault (Y-B) ,6KA, Fault distance 105 km(zone-1) from Bikaner end.	17-May-2023 08:18	44:27:00	1
93	765/400KV 1000MVA ICT-III at Unnao	ICT	NR	UPPCL	SE	15-May-2023 16:11	LV side (400KV side) at B-phase line isolator found hot point during Thermo-vision scan.	15-May-2023 17:42	01:31:00	0
94	765KV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	15-May-2023 16:59	taken out on voltage regulation	16-May-2023 07:56	14:57:00	0
95	765KV AJMER - CHITTORGARH Ckt-II	Line	NR	POWERGRID	MO	15-May-2023 17:09	taken out on voltage regulation	16-May-2023 08:15	15:06:00	0
96	765KV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	15-May-2023 17:28	taken out on voltage regulation	16-May-2023 08:15	14:47:00	0
97	765KV PHAGI - BHIWANI Ckt-I	Line	NR	RRVPNL/PG	MO	15-May-2023 18:46	taken out on over voltage	16-May-2023 08:32	13:46:00	1
98	765KV ALIGARH - JHATIKARA Ckt-I	Line	NR	POWERGRID	TL	15-May-2023 21:42	From Aligarh, 2.94ka,,158 km ,Y-N fault	16-May-2023 03:42	06:00:00	1
99	765KV ALIGARH - JHATIKARA Ckt-I	Line	NR	POWERGRID	MO	16-May-2023 03:42	Voltage Regulation	16-May-2023 10:54	07:12:00	1
100	765KV VARANASI - KANPUR Ckt-I	Line	NR	POWERGRID	TL	16-May-2023 13:22	R-B fault, FD- 167 km from Kanpur, FC- Ir- 4.1 kA, IB- 4.2KA at 1322 hrs	16-May-2023 14:12	00:50:00	1
101	765KV ORAI - ALIGARH Ckt-I	Line	NR	POWERGRID	TL	16-May-2023 16:23	765 KV Orai-Aligarh-1 tripped on R-N fault at 16:23 Hrs . Aligarh end details- F/D-229.60 kMS, f/c-2.01 KA.	16-May-2023 16:44	00:21:00	1
102	765KV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	16-May-2023 17:34	Voltage Regulation	17-May-2023 08:44	15:10:00	0
103	765KV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	16-May-2023 17:46	Voltage Regulation	17-May-2023 08:55	15:09:00	4
104	765/400 KV 1500 MVA ICT 4 AT FATEHGARH_II(PG)	ICT	NR	POWERGRID	SO	16-May-2023 17:48	For carrying out Tertiary bay erection works and 33 kV IPS tube connection works	17-May-2023 01:35	07:47:00	0

NLDC Outage report of Month May 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
105	765/400kV 1500MVA ICT-III at Phagi	ICT	NR	Rajasthan/RRVP NL	SO	16-May-2023 18:28	To attend connector of R phase of LV side main isolator and spare ICT isolator connector tube which is dis-loctaed from spare isolator side	16-May-2023 22:34	04:06:00	1
106	765/400 KV 1500 MVA ICT 2 AT LUCKNOW_2(PG)	ICT	NR	POWERGRID	SO	17-May-2023 08:40	for AMP works	17-May-2023 20:46	12:06:00	0
107	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	17-May-2023 16:50	Voltage Regulation	18-May-2023 06:13	13:23:00	0
108	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	17-May-2023 17:09	Voltage Regulation	18-May-2023 08:37	15:28:00	0
109	765kV PHAGI - BHIWANI Ckt-II	Line	NR	RRVNL/PG	MO	17-May-2023 18:43	Voltage Regulation	18-May-2023 10:56	16:13:00	0
110	765kV FATEHPUR - AGRA Ckt-II	Line	NR	POWERGRID	MO	17-May-2023 18:47	Voltage Regulation	18-May-2023 10:46	15:59:00	0
111	765kV BHADLA - BIKANER Ckt-II	Line	NR	POWERGRID	SE	17-May-2023 21:45	to attend hot-spot in Y-phase Line isolator contacts at Bikaner end.	18-May-2023 02:26	04:41:00	0
112	765kV MOGA - BHIWANI Ckt-I	Line	NR	POWERGRID	TV	17-May-2023 23:47	tripped on over voltage	18-May-2023 07:46	07:59:00	1
113	765kV MOGA - MEERUT Ckt-I	Line	NR	POWERGRID	MO	18-May-2023 03:50	Voltage Regulation	18-May-2023 10:00	06:10:00	0
114	765kV ORAI - ALIGARH Ckt-II	Line	NR	POWERGRID	MO	18-May-2023 03:57	Voltage Regulation	18-May-2023 12:51	08:54:00	0
115	765/400 KV 1500 MVA ICT 1 AT LUCKNOW_2(PG)	ICT	NR	POWERGRID	SO	18-May-2023 10:49	for AMP works.	19-May-2023 19:58	33:09:00	0
116	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	18-May-2023 16:41	Voltage Regulation	19-May-2023 07:25	14:44:00	0
117	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	18-May-2023 17:18	Voltage Regulation	19-May-2023 08:19	15:01:00	4
118	765kV AJMER - CHITTORGARH Ckt-I	Line	NR	POWERGRID	MO	18-May-2023 18:46	Voltage Regulation	19-May-2023 08:59	14:13:00	0
119	765/400kV 1000MVA ICT-I at Unnao	ICT	NR	UPPCL	SE	18-May-2023 21:51	For attending hot-spot on R-phase Line Isolator (400kV side).	18-May-2023 23:15	01:24:00	0
120	765/400 KV 1000 MVA ICT 1 AT ANPARA_C(LAN)	ICT	NR	SLDC	SE	19-May-2023 10:45	to replace the old TMU card.	19-May-2023 15:25	04:40:00	0
121	189 MVAR BUS REACTOR NO 1 AT 765KV UNNAO(UP)	Bus Reactor	NR	STU	SO	19-May-2023 12:11	Annual Routine Protection and Relay Testing of 189MVAR Bus Reactor	19-May-2023 18:43	06:32:00	0
122	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	19-May-2023 17:02	Voltage Regulation	20-May-2023 08:23	15:21:00	0
123	765kV AJMER - CHITTORGARH Ckt-II	Line	NR	POWERGRID	MO	19-May-2023 18:07	Voltage Regulation	20-May-2023 09:07	15:00:00	0
124	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	19-May-2023 18:08	Voltage Regulation	20-May-2023 07:16	13:08:00	0
125	189 MVAR BUS REACTOR NO 1 AT 765KV UNNAO(UP)	Bus Reactor	NR	STU	SO	20-May-2023 09:50	Annual Routine Protection and Relay Testing of 189MVAR Bus.(d-3)	20-May-2023 16:37	06:47:00	0
126	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	20-May-2023 17:40	Manually opened due to High Voltage	21-May-2023 08:24	14:44:00	0
127	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	20-May-2023 17:48	Manually opened due to High Voltage	21-May-2023 08:45	14:57:00	4
128	765kV PHAGI - BHIWANI Ckt-I	Line	NR	RRVNL/PG	MO	20-May-2023 18:16	Manually opened due to High Voltage	21-May-2023 08:53	14:37:00	1
129	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	21-May-2023 17:37	Manually opened due to High Voltage	22-May-2023 08:48	15:11:00	0
130	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	21-May-2023 17:44	Manually opened due to High Voltage	22-May-2023 07:01	13:17:00	0
131	765kV AJMER - CHITTORGARH Ckt-I	Line	NR	POWERGRID	MO	22-May-2023 16:31	Voltage Regulation	23-May-2023 08:54	16:23:00	0
132	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	22-May-2023 16:43	Voltage Regulation	23-May-2023 08:23	15:40:00	0

NLDC Outage report of Month May 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
133	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	22-May-2023 16:44	Voltage Regulation	23-May-2023 08:41	15:57:00	4
134	765/400kV 1500MVA ICT-II at Fatehgarh II	ICT	NR	POWERGRID	SE	22-May-2023 21:43	To attend R-Phase Pole of 70752 CB which got stuck during charging of 240 MVAR Bus Reactor 2 at Fatehgarh 2.	22-May-2023 22:13	00:30:00	0
135	765/400 KV 1500 MVA ICT 1 AT GR.NOIDA_2(UPC)	ICT	NR	STU	SO	23-May-2023 10:05	For Normalization of ICT - Y phase will be charge by change over from Spare ICT	23-May-2023 14:13	04:08:00	0
136	765kV AGRA - ALIGARH Ckt-I	Line	NR	POWERGRID	TL	23-May-2023 16:15	Y-N Fault. Aligarh end details- F/D-97.5 Kms , F/C-4 KA	23-May-2023 16:54	00:39:00	1
137	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	23-May-2023 17:05	Voltage Regulation	24-May-2023 09:29	16:24:00	0
138	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	23-May-2023 17:12	Voltage Regulation	24-May-2023 08:58	15:46:00	0
139	765kV PHAGI - BHIWANI Ckt-II	Line	NR	RRVPNL/PG	MO	23-May-2023 17:23	Voltage Regulation	24-May-2023 09:56	16:33:00	0
140	765kV KANPUR - ALIGARH Ckt-I	Line	NR	POWERGRID	TL	23-May-2023 18:27	Kanpur end details- 254.010 Kms, F/C-3.956 KA	23-May-2023 19:17	00:50:00	1
141	765/400kV 1000MVA ICT-I at Unnao	ICT	NR	UPPCL	SE	23-May-2023 20:41	To attend hot spot at R-Phase line isolator	23-May-2023 23:06	02:25:00	0
142	765kV KOTESHWAR - MEERUT Ckt-II	Line	NR	POWERGRID	TL	23-May-2023 21:28	765kV Meerut-Koteshwar-2 tripped at 21:28hrs/23.05.2023 on R-N fault due to Heavy wind storm reported at the site..FLR:-Meerut-107 KM/6.28 kA.	23-May-2023 22:51	01:23:00	1
143	765kV KOTESHWAR - MEERUT Ckt-II	Line	NR	POWERGRID	TS	24-May-2023 02:19	R-N fault, Fault current 6.41kA, Dist. 0.3km from Koteshwar & Dist. 178km, Fault current 3.75kA from Meerut.	24-May-2023 07:13	04:54:00	2
144	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	24-May-2023 16:27	Voltage Regulation	25-May-2023 08:28	16:01:00	0
145	765kV PHAGI - BHIWANI Ckt-I	Line	NR	RRVPNL/PG	MO	24-May-2023 16:47	Voltage Regulation	25-May-2023 09:44	16:57:00	1
146	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	24-May-2023 16:55	Voltage Regulation	25-May-2023 08:58	16:03:00	4
147	765kV FATEHPUR - AGRA Ckt-I	Line	NR	POWERGRID	MO	24-May-2023 22:08	taken out on over voltage	25-May-2023 11:12	13:04:00	0
148	765kV AJMER - CHITTORGARH Ckt-II	Line	NR	POWERGRID	MO	25-May-2023 01:30	taken out on over voltage	25-May-2023 09:14	07:44:00	0
149	765kV Bikaner - Bhadla II Ckt-II	Line	NR	POWERGRID	MO	25-May-2023 01:36	taken out on over voltage	25-May-2023 07:52	06:16:00	0
150	765kV ORAI - ALIGARH Ckt-I	Line	NR	POWERGRID	MO	25-May-2023 04:30	Voltage Regulation	25-May-2023 11:59	07:29:00	1
151	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	25-May-2023 17:03	Voltage Regulation	26-May-2023 07:55	14:52:00	0
152	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	25-May-2023 17:14	Voltage Regulation	26-May-2023 08:34	15:20:00	0
153	765kV PHAGI - BHIWANI Ckt-II	Line	NR	RRVPNL/PG	MO	25-May-2023 17:18	Voltage Regulation	26-May-2023 06:53	13:35:00	0
154	765kV KOTESHWAR - MEERUT Ckt-II	Line	NR	POWERGRID	TS	25-May-2023 17:44	DT Received	26-May-2023 19:17	25:33:00	3
155	765kV MEERUT - BHIWANI Ckt-I	Line	NR	POWERGRID	TL	25-May-2023 18:18	Line tripped on R-N fault at 18:18Hrs 25.05.2023. Meerut: 10kA, 42kM	25-May-2023 19:27	01:09:00	1
156	765kV BHADLA - BIKANER Ckt-I	Line	NR	POWERGRID	TL	25-May-2023 18:44	Bhadla: 76kM 4kA/79kM, 4.8kA Bikaner: 64.8kM, 7kA/66kM, 6.9kA	25-May-2023 19:58	01:14:00	2
157	765kV Bikaner - Bhadla II Ckt-I	Line	NR	POWERGRID	TL	25-May-2023 19:30	Bikaner: 109.4kM, 7.19kA Bhadla-II: 65.8kM, 8kA	25-May-2023 21:39	02:09:00	1
158	765kV PHAGI - BHIWANI Ckt-I	Line	NR	RRVPNL/PG	TL	25-May-2023 20:09	on B-N fault. Bhiwani: 58.9kM, 8.2kA	25-May-2023 22:06	01:57:00	2
159	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	TL	25-May-2023 20:43	tripped on R-N fault FLR: Ajmer: 326.100kM (100%) 3.01kA	25-May-2023 22:24	01:41:00	5
160	765kV Fatehgarh II - Bhadla II Ckt-II	Line	NR	PFTL	TL	25-May-2023 20:43	Tripped on Zone-2 due to Heavy thunderstorms near Bhadla region. FLR: Fatehgarh_2: R-N Fault, 260Km	25-May-2023 21:52	01:09:00	1
161	765/400kV 1500MVA ICT-I at Bhadla II	ICT	NR	POWERGRID	TS	25-May-2023 20:49	on differential protection operation.	26-May-2023 00:41	03:52:00	1
162	765kV FATEHPUR - AGRA Ckt-II	Line	NR	POWERGRID	MO	25-May-2023 21:01	Voltage Regulation	26-May-2023 19:10	22:09:00	0

NLDC Outage report of Month May 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
163	765kV ORAI - ALIGARH Ckt-II	Line	NR	POWERGRID	MO	25-May-2023 21:09	taken out to over voltage	29-May-2023 09:33	84:24:00	0
164	765kV Fatehgarh 2 - Bhadla Ckt-2	Line	NR	POWERGRID NR	TL	25-May-2023 21:16	Tripped on B-N Fault. FLR: Bhadla-21.56Km/8.0Ka, Fatehgarh_2- 155Km	25-May-2023 22:32	01:16:00	1
165	765kV Fatehgarh II - Bhadla I Ckt-I	Line	NR	PFTL	TL	25-May-2023 21:16	Tripped on Y-N Fault. FLR: Bhadla-30.5Km/8.0Ka, Fatehgarh_2: 121Km/1.87Ka.	25-May-2023 21:56	00:40:00	4
166	765kV Ajmer - Phagi Ckt-II	Line	NR	POWERGRID	TL	25-May-2023 22:12	Tripped on B-N fault; Ajmer end- 3.9Ka, 77.97 km, Phagi: 48.05 km	26-May-2023 09:07	10:55:00	1
167	765kV Ajmer - Phagi Ckt-I	Line	NR	POWERGRID	TL	25-May-2023 22:25	Ajmer end: B-N fault, 77.97km, 5.372Ka, Phagi-(AIS): 57.4 km from Phagi end	26-May-2023 07:45	09:20:00	2
168	240MVAR 765kV Bus Reactor-I at Phagi	Bus Reactor	NR	Rajasthan/RRV PNL	TS	25-May-2023 22:29	tripped along bus-1	26-May-2023 11:08	12:39:00	1
169	240MVAR 765kV Bus Reactor-II at Phagi	Bus Reactor	NR	Rajasthan/RRV PNL	TS	25-May-2023 22:29	tripped along bus-1	26-May-2023 06:54	08:25:00	1
170	765 KV VARANASI-KANPUR_GIS (PG) CKT-1	Line	NR	POWERGRID	SC	26-May-2023 09:12	Transmission Line Diversion work due to construction of Ganga Expressway by UPEIDA	26-May-2023 11:15	02:03:00	0
171	765 KV VARANASI-KANPUR_GIS (PG) CKT-2	Line	NR	POWERGRID	SC	26-May-2023 09:12	Transmission Line Diversion work due to construction of Ganga Expressway by UPEIDA	26-May-2023 11:17	02:05:00	0
172	765kV KANPUR - ALIGARH Ckt-I	Line	NR	POWERGRID	SE	26-May-2023 11:50	Hot Spot in Kanpur Aligarh Loc. 463 R phase	26-May-2023 18:31	06:41:00	1
173	765kV AJMER - PHAGI Ckt-I	Line	NR	POWERGRID/RR VPNL	SO	26-May-2023 17:00	2023 to restore damaged one Tension polymer insulator in middle phase at location	27-May-2023 10:49	17:49:00	2
174	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	26-May-2023 17:34	voltage regulation	27-May-2023 09:09	15:35:00	0
175	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	26-May-2023 18:06	Voltage Regulation	27-May-2023 10:05	15:59:00	5
176	765kV Bikaner - Khetri Ckt-I	Line	NR	BKTL	TL	27-May-2023 04:49	Phase to earth fault Y-N, tripped due to Zone-1 protection operated. Cross arm damaged (T.No. 405)	28-May-2023 02:29	21:40:00	2
177	765kV PHAGI - BHIWANI Ckt-II	Line	NR	RRVPNL/PG	TL	27-May-2023 05:27	PHAGI:- Y-N, 3.7ka, 187KM BHIWANI:- Y-N, 7.12KA, 85km	27-May-2023 09:42	04:15:00	1
178	765kV FATEHPUR - AGRA Ckt-II	Line	NR	POWERGRID	TV	27-May-2023 06:21	Tripped, tripping on over voltage reported	27-May-2023 07:43	01:22:00	1
179	765kV MOGA - MEERUT Ckt-I	Line	NR	POWERGRID	MO	27-May-2023 06:22	Voltage Regulation	27-May-2023 10:58	04:36:00	0
180	765kV AGRA - JHATIKARA Ckt-I	Line	NR	POWERGRID	MO	27-May-2023 06:31	Voltage Regulation	27-May-2023 15:44	09:13:00	0
181	765kV AGRA FATEHABAD - GREATER NOIDA Ckt-I	Line	NR	Uttar Pradesh/UPPT CL	MO	27-May-2023 06:49	Voltage Regulation	29-May-2023 09:45	50:56:00	0
182	765 KV VARANASI-KANPUR_GIS (PG) CKT-1	Line	NR	POWERGRID	SC	27-May-2023 07:03	Transmission Line Diversion work due to construction of Ganga Expressway by UPEIDA	06-Jun-2023 07:16	240:13:00	0
183	765 KV VARANASI-KANPUR_GIS (PG) CKT-2	Line	NR	POWERGRID	SC	27-May-2023 07:05	Transmission Line Diversion work due to construction of Ganga Expressway by UPEIDA	06-Jun-2023 19:30	252:25:00	0
184	765kV FATEHPUR - AGRA Ckt-II	Line	NR	POWERGRID	MO	27-May-2023 07:43	Voltage Regulation	27-May-2023 17:54	10:11:00	1
185	765kV LALITPUR - FATEHABAD Ckt-I	Line	NR	LPGL/UPPTCL	TL	27-May-2023 11:04	flag fatehbad end Ia-2206.736(A) , A(ABC) Phase,Z1,199.6km, SOTF	27-May-2023 18:56	07:52:00	2
186	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	27-May-2023 18:06	Manually opened due to High Voltage	28-May-2023 09:12	15:06:00	0
187	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	27-May-2023 18:09	Manually opened due to High Voltage	28-May-2023 07:01	12:52:00	0
188	765kV Bikaner - Khetri Ckt-II	Line	NR	BKTL	SO	27-May-2023 19:15	for restoration work at tower no 405 (Transposition Tower)	28-May-2023 03:06	07:51:00	0
189	765kV MOGA - BHIWANI Ckt-I	Line	NR	POWERGRID	MO	28-May-2023 02:58	Voltage Regulation	28-May-2023 09:56	06:58:00	1
190	765kV AJMER - CHITTORGARH Ckt-I	Line	NR	POWERGRID	MO	28-May-2023 03:33	Voltage Regulation	28-May-2023 10:39	07:06:00	0
191	765kV FATEHPUR - AGRA Ckt-I	Line	NR	POWERGRID	MO	28-May-2023 08:10	Voltage Regulation	29-May-2023 09:40	25:30:00	0
192	765/400kV 1500MVA ICT-I at Bhadla II	ICT	NR	POWERGRID	TS	28-May-2023 13:29	Tripped due to heavy wind storms	28-May-2023 21:11	07:42:00	2

NLDC Outage report of Month May 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
193	765kV Bikaner - Bhadla II Ckt-I	Line	NR	POWERGRID	TL	28-May-2023 13:35	Tripped, heavy wind storm reported	28-May-2023 18:48	05:13:00	2
194	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	TL	28-May-2023 13:40	Tripped, heavy wind storm reported	28-May-2023 19:55	06:15:00	6
195	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	TL	28-May-2023 13:40	Tripped, heavy wind storm reported	28-May-2023 15:50	02:10:00	1
196	765kV Fatehgarh II - Bhadla II Ckt-I	Line	NR	PFTL	TL	28-May-2023 13:40	Tripped, heavy wind storm reported	28-May-2023 14:33	00:53:00	2
197	765kV Fatehgarh II - Bhadla II Ckt-II	Line	NR	PFTL	TL	28-May-2023 13:40	Tripped due to heavy wind storm.765kV Fatehgarh-2 Bhadla-2 Ckt2 flashover marks are observed in R-Y phase conductor near gantry, which is may be due to swing of conductors towards Gantry tower during heavy storms at Bhadla-2	28-May-2023 18:59	05:19:00	2
198	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	28-May-2023 17:10	Voltage Regulation	29-May-2023 08:33	15:23:00	0
199	765kV AJMER - CHITTORGARH Ckt-II	Line	NR	POWERGRID	MO	28-May-2023 19:22	Voltage Regulation	29-May-2023 09:38	14:16:00	0
200	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	28-May-2023 20:18	Voltage Regulation	29-May-2023 09:09	12:51:00	1
201	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	29-May-2023 16:54	Manually opened due to High Voltage	30-May-2023 09:09	16:15:00	0
202	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	29-May-2023 17:08	Manually opened due to High Voltage	30-May-2023 11:37	18:29:00	6
203	765/400kV 1500MVA ICT-I at Meerut	ICT	NR	POWERGRID	SE	30-May-2023 01:32	due to abnormal sound being noticed from B-ph Bushing.	31-May-2023 05:34	28:02:00	0
204	765kV Fatehgarh II - Bhadla I Ckt-I	Line	NR	PFTL	TL	30-May-2023 02:02	Fatehgarh:- Y-N, 6.87KA, 32.9KM	30-May-2023 04:15	02:13:00	5
205	765kV BIKANER - MOGA Ckt-I	Line	NR	POWERGRID	MO	30-May-2023 15:43	Voltage Regulation	31-May-2023 08:24	16:41:00	0
206	765kV Ajmer - Bhadla II ckt-II	Line	NR	POWERGRID	MO	30-May-2023 17:31	Voltage Regulation	31-May-2023 08:53	15:22:00	1
207	765kV LALITPUR - FATEHABAD Ckt-II	Line	NR	LPGL/UPPTCL	TL	30-May-2023 18:42	B-N Fault , Ic-9.647KA Z1 & FD= 18.30km from Fatehbad end	31-May-2023 04:05	09:23:00	1
208	765kV Fatehgarh II - Bhadla II Ckt-I	Line	NR	PFTL	SE	30-May-2023 18:56	Emergency Shutdown is required fault rectification.	30-May-2023 19:39	00:43:00	2
209	765kV FATEHPUR - AGRA Ckt-II	Line	NR	POWERGRID	MO	31-May-2023 00:43	Voltage Regulation	31-May-2023 09:51	09:08:00	1
210	765kV ORAI - ALIGARH Ckt-I	Line	NR	POWERGRID	MO	31-May-2023 02:28	Voltage Regulation	03-Jun-2023 10:07	79:39:00	1
211	765 KV MOGA-MEERUT (PG) CKT-1	Line	NR	POWERGRID	SO	31-May-2023 08:36	For Rectification of shut down nature defect	31-May-2023 18:00	09:24:00	0
212	765kV BIKANER - MOGA Ckt-II	Line	NR	POWERGRID	MO	31-May-2023 17:16	Voltage Regulation	01-Jun-2023 00:00	06:44:00	0
213	765kV Ajmer - Bhadla II ckt-I	Line	NR	POWERGRID	MO	31-May-2023 17:34	Voltage Regulation	01-Jun-2023 00:00	06:26:00	6
214	765kV Fatehgarh II - Bhadla II Ckt-II	Line	NR	PFTL	SO	31-May-2023 18:10	for tracing the location of fault inside substation gantry structure	31-May-2023 22:24	04:14:00	2

Western Region Elements

1	765kV AURANGABAD - PUNE Ckt-I	Line	WR	POWERGRID	MO	01-May-2023 00:00	To control loading of pune Chakkan & Pune Pune loading	12-May-2023 14:44	278:44:00	0
2	765kV Bhuj - Lakadia -I	Line	WR	POWERGRID	MO	01-May-2023 00:00	Line was tripped due to over voltage at 20:00 on 18.04.2023, Now it is converted to over voltage	12-May-2023 13:00	277:00:00	0
3	765kV BINA - JABALPUR PS Ckt-I	Line	WR	POWERGRID	MO	01-May-2023 00:00	Voltage Regulation	17-May-2023 09:59	393:59:00	0
4	765kV DHARAMJIYAGARH - JABALPUR PS Ckt-II	Line	WR	POWERGRID	MO	01-May-2023 00:00	Voltage Regulation	04-May-2023 11:08	83:08:00	0
5	765kV Lakadia - Banaskantha Ckt-II	Line	WR	Adani Trans Ind Ltd	MO	01-May-2023 00:00	Voltage Regulation	17-May-2023 10:03	394:03:00	0
6	765kV RAIPUR-PS(DURG) - CHAMPA PS Ckt-II	Line	WR	POWERGRID	MO	01-May-2023 00:00	Voltage Regulation	26-May-2023 08:53	608:53:00	0

NLDC Outage report of Month May 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
7	765kV RAIPUR-PS(DURG) - WARDHA Ckt-I	Line	WR	POWERGRID	MO	01-May-2023 00:00	Voltage Regulation	02-May-2023 22:20	46:20:00	0
8	765kV WARDHA - AURANGABAD Ckt-II	Line	WR	POWERGRID	MO	01-May-2023 00:00	Voltage Regulation	09-May-2023 12:45	204:45:00	0
9	765kV WARORA - PARLI NEW Ckt-II	Line	WR	PWTL-PG/PPTL-PG	TS	01-May-2023 16:08	operation of Bucholz trip of R-ph reactor During investigation no abnormality was found except for the suspected ABB make RXSF aux relay provided for Bucholz trip, same has been replaced with spare relay.	01-May-2023 23:07	06:59:00	1
10	765kV RAIPUR-PS(DURG) - WARDHA Ckt-II	Line	WR	POWERGRID	TL	01-May-2023 20:35	tripped on R-G fault at 20:35 Hrs on 01/05/2023 due to dead end failure at Location No.210. Fault details from Durg end: 85.6km and 12.02kA.	02-May-2023 13:57	17:22:00	1
11	400KV-APL-MUNDRA-APL-MUNDRA HVDC TERMINAL-1	Line	WR	APL	SO	02-May-2023 06:49	Annual Maintenance and Electrical Testing work	02-May-2023 18:48	11:59:00	0
12	765kV RAIPUR-PS(DURG) - WARDHA Ckt-I	Line	WR	POWERGRID	MO	02-May-2023 22:21	Voltage Regulation	05-May-2023 10:31	60:10:00	0
13	765kV SEONI - WARDHA Ckt-II	Line	WR	POWERGRID	SO	04-May-2023 09:08	For spare changeover work@Seoni SS	04-May-2023 23:36	14:28:00	0
14	765kV DHARAMJAYGARH - JABALPUR PS Ckt-I	Line	WR	POWERGRID	SO	04-May-2023 11:45	For attending S/D nature defect in line	04-May-2023 22:56	11:11:00	0
15	765kV SEONI - BINA Ckt-I	Line	WR	POWERGRID	TV	05-May-2023 14:40	Over voltage stage # 2 protection operation	05-May-2023 18:10	03:30:00	1
16	765kV RAIPUR-PS(DURG) - WARDHA Ckt-I	Line	WR	POWERGRID	MO	05-May-2023 20:39	Line tripped on SOTF , Converted to Voltage regulation due to high voltage	06-May-2023 09:09	12:30:00	0
17	765kV DHARAMJAYGARH - JABALPUR PS Ckt-II	Line	WR	POWERGRID	MO	06-May-2023 01:44	to contain high voltage at CHAMPA region. CHAMPA - 802 KV , DHRM- 782 kv	27-May-2023 18:10	520:26:00	0
18	765KV/400KV TAMNAR-ICT-4	ICT	WR	POWERGRID WR1	SO	06-May-2023 08:45	Spare Change Over. Spare to be taken out of service. Last Spare Changeover date 04.04.2023	06-May-2023 15:07	06:22:00	0
19	765kV RAIPUR-PS(DURG) - WARDHA Ckt-III	Line	WR	POWERGRID	MO	07-May-2023 09:49	taken out on over voltage	05-Jun-2023 20:08	706:19:00	0
20	765KV-AKOLA (2)-KORADI-III-2	Line	WR	MEGPTCL	SO	07-May-2023 10:48	To attend the sag correction in tower no. 534, to stop the deforming of tower members in the first section.	07-May-2023 19:02	08:14:00	0
21	240MVAR LR(F) of 765kV Bilaspur - Rajnandgaon Ckt-II at	Line Reactor	WR	POWERGRID/R RWTL - ADANI	TS	09-May-2023 12:33	Hand tripped due to Sparking and Chattering sound observed in 713 LR Isolator	09-May-2023 16:12	03:39:00	1
22	765KV-WARDHA-AURANGABAD-4	Line	WR	POWERGRID WR1	SO	09-May-2023 13:12	for Spare L/R Changeover work(for taking spare unit out of service) at AURANGABAD S/S. Last spare changer over on 16.03.2023	10-May-2023 02:31	13:19:00	0
23	765kV WARDHA - AURANGABAD Ckt-IV	Line	WR	POWERGRID	MO	10-May-2023 02:31	line previously out in planned shutdown now converted into voltage regulation	15-May-2023 11:54	129:23:00	0
24	765kV WARDHA - AURANGABAD Ckt-IV	Line	WR	POWERGRID	MO	10-May-2023 02:31	line previously out in planned shutdown now converted into voltage regulation	01-Jun-2023 00:00	525:29:00	0
25	765KV/400KV AURANGABAD-ICT-1	ICT	WR	POWERGRID WR1	SO	10-May-2023 10:11	For taking Spare Unit out of service	10-May-2023 23:19	13:08:00	0
26	765kV SATNA - GWALIOR Ckt-I	Line	WR	POWERGRID	TL	10-May-2023 13:19	R-e/F , 2.2KA, 306KM from Satna and 11.8KA, 37KM from Gwalior	10-May-2023 14:08	00:49:00	1
27	400KV-APL-MUNDRA-APL-MUNDRA HVDC TERMINAL-3	Line	WR	APL	SO	11-May-2023 06:48	Annual Maintenance and Electrical Testing work	11-May-2023 17:33	10:45:00	0
28	765KV/400KV PARLI NEW-ICT-2	ICT	WR	POWERGRID WR1	SO	12-May-2023 09:16	AMP Works of ICT & its associated equipments.	12-May-2023 21:20	12:04:00	0
29	765KV-BILASPUR-RAJNANDGAON-RRWTL-1	Line	WR	STL	SO	12-May-2023 10:24	Annual Maintenance for Defect Rectification Work	12-May-2023 17:20	06:56:00	0
30	765kV BINA - GWALIOR Ckt-III	Line	WR	POWERGRID	TL	12-May-2023 12:06	due to R-Phase to earth fault Fault Distance : 115 KM Fault Current :4.50 KM	12-May-2023 13:03	00:57:00	1
31	765kV SATNA - GWALIOR Ckt-I	Line	WR	POWERGRID	TS	12-May-2023 12:06	Line Tripped due to tripping of 765 kV Bina Gwalior 3.(Main bay was under palnnd shutdown at Gwalior SS).Line was in same dia.	12-May-2023 13:04	00:58:00	2
32	765kV BINA - GWALIOR Ckt-III	Line	WR	POWERGRID	TL	12-May-2023 14:02	tripped on Rph-Ground Fault	12-May-2023 20:11	06:09:00	2
33	765kV SATNA - GWALIOR Ckt-I	Line	WR	POWERGRID	TS	12-May-2023 14:03	line not charged due to main bay pole discrepancy issue . Line Tripped due to tripping of 765 kV Bina Gwalior 3. Line was in same dia.	12-May-2023 16:40	02:37:00	3
34	765KV-PUNE-GIS-SOLAPUR-1	Line	WR	POWERGRID WR1	SO	12-May-2023 14:51	Spare Change over . Spare to taken out of service . Last Spare changeover 24.01.2023	12-May-2023 21:36	06:45:00	0

NLDC Outage report of Month May 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
35	765KV-PUNE-GIS-SOLAPUR-1 L/R@ PUNE-GIS - 765KV	Line Reactor	WR	POWERGRID WR1	SO	12-May-2023 14:51	Spare Change over . Spare to taken out of service . Last Spare changeover 24.01.2023	12-May-2023 21:36	06:45:00	0
36	765KV AURANGABAD - PUNE Ckt-I	Line	WR	POWERGRID	MO	12-May-2023 22:10	To control the loading of Pune-Pune Ckt	19-May-2023 16:58	162:48:00	0
37	765KV/400KV SEONI-ICT-1	ICT	WR	POWERGRID WR1	SO	16-May-2023 09:44	For AMP Works@Seoni SS	16-May-2023 18:55	09:11:00	0
38	765KV-BINA-JABALPUR-1	Line	WR	POWERGRID	SO	17-May-2023 10:03	Attending S/D nature defect in line & For Line Treminal equipment AMP work. A/R OFF of ckt # 2 is required and Dia to be kept open at both ends. For installation of new NGR at Bina end.	17-May-2023 21:44	11:41:00	0
39	765kv BINA - JABALPUR PS Ckt-I	Line	WR	POWERGRID	MO	17-May-2023 21:44	Voltage Regulation	01-Jun-2023 00:00	338:16:00	0
40	765KV-SOLAPUR-PARLI NEW-2	Line	WR	POWERGRID WR1	SO	18-May-2023 09:12	AMP Works of Line terminal equipments at Solapur end	18-May-2023 20:18	11:06:00	0
41	765kv SOLAPUR - PARLI NEW Ckt-II	Line	WR	POWERGRID/P PTL	MO	18-May-2023 20:20	Voltage Regulation	19-May-2023 09:42	13:22:00	0
42	765KV/400KV BHUJ-ICT-4	ICT	WR	POWERGRID	SO	19-May-2023 10:33	Spare changeover, last changeover was on 03.01.2023. DIA TO BE KEPT OPEN AT BOTH SIDES	20-May-2023 03:00	16:27:00	0
43	765KV-BHOPAL-BDTCL-JABALPUR-1	Line	WR	POWERGRID	SO	19-May-2023 10:43	For Line Terminal equipment AMP work. Dia to be kept open at both ends.	19-May-2023 19:38	08:55:00	0
44	765KV-JABALPUR-BHOPAL-1 L/R@ JABALPUR - 765KV	Line Reactor	WR	POWERGRID	SO	19-May-2023 10:43	For Reactor & switchable CB AMP work	19-May-2023 19:38	08:55:00	0
45	765KV/400KV EKTUNI-ICT-3	ICT	WR	MSLDC	SO	19-May-2023 11:03	Diagnostic Testing & Routine Maintenance(SPARE ICT UNIT)	19-May-2023 18:55	07:52:00	0
46	765KV PUNE - SOLAPUR Ckt-I	Line	WR	POWERGRID	SE	19-May-2023 17:11	line for removing of foreign material Plastic Polythene from tower nearby jumper at tower no.T0406, B-phase.	19-May-2023 19:37	02:26:00	0
47	765KV AURANGABAD - PUNE Ckt-I	Line	WR	POWERGRID	MO	20-May-2023 08:55	Power Regulation	24-May-2023 16:47	103:52:00	0
48	240MVAR LR(S) of 765kv Aurangabad - Solapur Ckt-I at	Line Reactor	WR	POWERGRID	SE	20-May-2023 12:08	Due to oil leakage	20-May-2023 19:35	07:27:00	0
49	765kv AURANGABAD - SOLAPUR Ckt-I	Line	WR	POWERGRID	SE	20-May-2023 12:08	To attend the oil leakage outage is required on LR	20-May-2023 20:26	08:18:00	0
50	765/400kv 1500MVA ICT-I at TAMNAR PS	ICT	WR	POWERGRID	SE	20-May-2023 23:05	To attend hotspot	21-May-2023 12:59	13:54:00	0
51	765/400kv 1500MVA ICT-II at TAMNAR PS	ICT	WR	POWERGRID	SE	21-May-2023 02:07	To attend hotspot	21-May-2023 04:22	02:15:00	0
52	765KV-SATNA-VINDHYACHAL(PS)-2	Line	WR	POWERGRID	SO	21-May-2023 09:44	Conductor repair work at location between 73 - 74. A/R off of Ckt 1 and Dia to be Kept open at both ends. Simultaneous outage of 765KV Satna-Vindhyachal # 2 and 765KV Sasan-Satna # 2 is required.	21-May-2023 21:35	11:51:00	0
53	765KV-SASAN-SATNA-2	Line	WR	POWERGRID	SO	21-May-2023 09:46	At Loc 83-84, this line undercross 765KV-SATNA-VINDHYACHAL(PS)-2 line at loc 73-74. Simultaneous outage of 765KV Satna-Vindhyachal # 2 and 765KV Sasan-Satna # 2 is required.	21-May-2023 20:26	10:40:00	0
54	240MVAR LR(S) of 765kv Akola(2) - Ektuni (Aurangabad)	Line Reactor	WR	Maharashtra/ MEGPTCL	TS	22-May-2023 16:57	due to Buchholz Relay Operated in Y-Ph at Akola II SS.	22-May-2023 19:34	02:37:00	1
55	765KV/400KV PUNE-GIS-ICT-1	ICT	WR	POWERGRID WR1	SO	23-May-2023 06:41	SPARE CHANGEOVER WORKS	23-May-2023 17:07	10:26:00	0
56	330MVAR LR(S) of 765kv Wardha - Aurangabad Ckt-II at	Line Reactor	WR	POWERGRID	SE	23-May-2023 08:11	Due to oil leakage	23-May-2023 15:10	06:59:00	0
57	765kv WARDHA - AURANGABAD Ckt-II	Line	WR	POWERGRID	SE	23-May-2023 13:33	to take the Reactor in service, outage of 765KV Aurangabad-Wardha#2 is required for 1 hr	23-May-2023 15:10	01:37:00	0
58	240MVAR LR(S) of 765kv Jharsuguda - Durg Ckt-I at Durg	Line Reactor	WR	POWERGRID	SO	23-May-2023 22:37	For charging of line	23-May-2023 23:47	01:10:00	0
59	765KV/400KV RAIGARH-PS-ICT-3	ICT	WR	POWERGRID WR1	SO	24-May-2023 08:34	Spare Switching. Spare to be taken out of service. Last Spare changeover 25.03.2023	24-May-2023 14:55	06:21:00	0
60	765kv BINA - GWALIOR Ckt-III	Line	WR	POWERGRID	TL	24-May-2023 15:53	Tripped on R-ph/E fault Gwalior:- 23.2km/15.01kA Bina:- 231.7km/2.77kA	01-Jun-2023 00:00	176:07:00	3
61	765kv PUNE - SOLAPUR Ckt-I	Line	WR	POWERGRID	SO	24-May-2023 16:54	jumper sub conductor at Loc No: 253 is found hanging	24-May-2023 22:27	05:33:00	0
62	765KV WARORA - PARLI NEW Ckt-II	Line	WR	PWTL-PG/PPTL-PG	TL	24-May-2023 20:47	R-Y-B Fault, 40.2km from warora end, Ir=15kA, Iy=16.2kA,Ib=15kA R-Y-B Fault, 314.8 km from Parli end, fault current = 3.55kA	25-May-2023 02:52	06:05:00	2
63	765KV AURANGABAD - PUNE Ckt-I	Line	WR	POWERGRID	MO	24-May-2023 23:06	to control the loading of pune aurangabad line	01-Jun-2023 00:00	168:54:00	0
64	BHUJ - 765KV B/R 1	Bus Reactor	WR	POWERGRID	SO	25-May-2023 11:36	Spare changeover, last changeover was on 05.12.2022. DIA TO BE KEPT OPEN.	25-May-2023 14:54	03:18:00	0

NLDC Outage report of Month May 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
65	765KV-SATNA-VINDHYACHAL(PS)-1	Line	WR	POWERGRID	SO	25-May-2023 11:50	Line AMP works and Terminal equipment amp works.	25-May-2023 19:30	07:40:00	0
66	765KV BHUJ - BANASKANTHA Ckt-II	Line	WR	POWERGRID	SE	25-May-2023 11:56	for improving the clearance of OPGW to Top phase conductor at Loc 341-342.	25-May-2023 16:57	05:01:00	0
67	765KV/400KV WARORA-PG-ICT-1	ICT	WR	POWERGRID WR1	SO	26-May-2023 09:06	FOR SPARE CHANGEOVER WORK. Spare to be taken in service. Last Spare changeover 17.11.2022	26-May-2023 18:27	09:21:00	0
68	765KV-BILASPUR-SEONI-2	Line	WR	POWERGRID WR1	SO	26-May-2023 09:28	Spare LR change over works	26-May-2023 16:11	06:43:00	0
69	765KV-BILASPUR-SEONI-2 L/R@ BILASPUR - 765KV	Line Reactor	WR	POWERGRID WR1	SO	26-May-2023 09:28	Spare LR change over works. Spare was taken out of service on date 14.12.22. In this SD Spare will be taken in service	26-May-2023 16:11	06:43:00	0
70	765KV Lakadia - Banaskantha Ckt-I	Line	WR	Adani Trans Ind Ltd	TS	26-May-2023 23:57	Due to carrier receive Main Bay (710) CB Tripped.	27-May-2023 02:02	02:05:00	1
71	765KV/400KV TAMNAR-ICT-3	ICT	WR	POWERGRID WR1	SE	27-May-2023 08:53	To Attend Oil Leakage on Neutral CT	27-May-2023 15:50	06:57:00	0
72	765kv VINDHYACHAL PS - JABALPUR PS Ckt-II	Line	WR	POWERGRID	TL	27-May-2023 14:35	B-N FAULT	27-May-2023 16:21	01:46:00	1
73	765kv DHARAMJAYGARH - JABALPUR PS Ckt-III	Line	WR	POWERGRID	TL	27-May-2023 15:46	Fault Distance: 84.95 KM Fault Current: ly-12.26 kA lb-11.47 kA	27-May-2023 19:50	04:04:00	1
74	765kv DHARAMJAYGARH - JABALPUR PS Ckt-I	Line	WR	POWERGRID	MO	28-May-2023 16:32	taken out on over voltage	01-Jun-2023 00:00	79:28:00	0
75	765KV Lakadia - Banaskantha Ckt-II	Line	WR	Adani Trans Ind Ltd	MO	28-May-2023 21:25	Voltage Regulation	06-Jun-2023 16:23	210:58:00	0
76	765KV DHULE - VADODARA PS Ckt-I	Line	WR	BDTCL/POWER GRID	TL	28-May-2023 21:35	R-Y-phase Fault Distance: 269 KM Fault Current Rph : 3.647 kA - Yph : 3.358 kA Zone: 02	29-May-2023 00:40	03:05:00	1
77	765KV/400KV CHAMPA-ICT-4	ICT	WR	POWERGRID WR1	SO	30-May-2023 09:33	For Spare Change Over.	30-May-2023 17:27	07:54:00	0
78	765kv KHANDWA PS - DHULE Ckt-II	Line	WR	KTL-STERLITE/BDTC	TL	30-May-2023 15:09	Y-Phase to Earth fault	30-May-2023 16:58	01:49:00	1
79	765KV BINA - GWALIOR Ckt-II	Line	WR	POWERGRID	TS	30-May-2023 18:29	due to ingress of moisture in Common MB.	30-May-2023 20:46	02:17:00	1
80	CHAMPA - 765KV B/R 1	Bus Reactor	WR	POWERGRID WR1	SO	31-May-2023 10:10	For Spare Change Over.	31-May-2023 13:55	03:45:00	0

Eastern Region Elements

1	765 kv ANGUL - JHARSUGUDA Ckt-III	Line	ER	POWERGRID	MO	01-May-2023 00:00	Voltage Regulation	13-May-2023 12:48	300:48:00	0
2	765KV-MEDINIPUR-NEW JEERAT-1	Line	ER	ER-II	SE	02-May-2023 05:05	Damaged CLR insulator Replacement work due to lightning	02-May-2023 19:42	14:37:00	0
3	262MVAR 765KV B/R-1 AT DARLIPALI (DSTPS)	Bus Reactor	ER	DARLIPALI (NTPC)	SO	02-May-2023 08:26	ANNUAL TESTING OF BREAKER, CT, ISOLATOR, LA OF REACTOR BAY	07-May-2023 19:46	131:20:00	0
4	765KV-MEDINIPUR-NEW JEERAT-1	Line	ER	ER-II	SE	03-May-2023 05:13	Damaged CLR insulator Replacement work due to lightning	03-May-2023 15:43	10:30:00	0
5	765KV-MEDINIPUR-NEW JEERAT-1	Line	ER	ER-II	SE	04-May-2023 05:08	DAMAGED INSULATOR REPLACEMENT DUE TO LIGHTNING	04-May-2023 21:11	16:03:00	0
6	765KV-MEDINIPUR-NEW JEERAT-2	Line	ER	ER-II	SO	06-May-2023 05:10	Replacement of defective CLR insulator caused due to lightening	06-May-2023 19:46	14:36:00	0
7	765KV-MEDINIPUR-NEW JEERAT-2	Line	ER	ER-II	SO	07-May-2023 05:18	Replacement of defective CLR insulator caused due to lightening	07-May-2023 18:44	13:26:00	0
8	765KV-MEDINIPUR-NEW JEERAT-2	Line	ER	ER-II	SO	08-May-2023 05:48	Replacement of defective CLR insulator caused due to lightening	08-May-2023 15:24	09:36:00	0
9	330MVAR 765KV B/R-2 AT ANGUL	Bus Reactor	ER	PG (ODISHA PROJECT)	SO	08-May-2023 09:09	AMP/Spare Rotation	08-May-2023 16:54	07:45:00	0
10	132KV Surajpura-Ramnagar circuit	Line	ER		TL	09-May-2023 15:00	on E/F, O/C relay.the relay details are Ia - 1350A Ib - 694 A Ic - 246 A In - 0 Ig - 312, 443, 2004	10-May-2023 15:53	24:53:00	1
11	132KV Surajpura-Ramnagar circuit	Line	ER		TL	14-May-2023 17:30	on E/F and O/C relay. Relay details are Ia - 458 A, Ib - 1083 A, Ic - 502 A In - 0	14-May-2023 19:26	01:56:00	2
12	765KV-NEW RANCHI-MEDINIPUR-1	Line	ER	ER-II	SO	15-May-2023 08:09	Replacement of CLR insulator damaged due to lightening	15-May-2023 19:01	10:52:00	0

NLDC Outage report of Month May 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
13	765KV-NEW RANCHI-MEDINIPUR-2	Line	ER	ER-II	SO	16-May-2023 08:35	Replacement of CLR Insulator damaged due to lightening	16-May-2023 19:23	10:48:00	0
14	765/400kV 1500MVA ICT-IV AT ANGUL	ICT	ER	POWERGRID	SE	16-May-2023 13:08	To attend B-phase oil leakage	16-May-2023 18:28	05:20:00	0
15	765kV Medinipur - New Jeerut Ckt-II	Line	ER	PMJTL	SE	17-May-2023 09:27	to attend broken insulator	17-May-2023 16:13	06:46:00	0
16	765kV Medinipur - New Jeerut Ckt-II	Line	ER	PMJTL	TL	18-May-2023 16:49	MEDINIPUR: B-N, 20.8KM,7.47KA, N. JEERAT:B-N, 105.4KM, 3.76KA	18-May-2023 17:31	00:42:00	1
17	765kV NEW RANCHI - MEDINIPUR Ckt-I	Line	ER	POWERGRID/P MJTL	SO	24-May-2023 06:09	replacement of Broken Insulator	24-May-2023 15:25	09:16:00	0
18	765kV NEW RANCHI - MEDINIPUR Ckt-I	Line	ER	POWERGRID/P MJTL	TL	25-May-2023 17:01	Medinipur: Y-E, Zone - 1, 75.8 km, F/C 4.530 kA Ranchi: Y-E, ZONE-1, 201 KM, f/c 3.2 KA	25-May-2023 18:41	01:40:00	1
19	765/400kV 1500MVA ICT-I at New Jeerat	ICT	ER	PMJTL	TS	26-May-2023 18:03	Differential protection operation at R Ph	27-May-2023 02:09	08:06:00	1
20	765 kV ANGUL - JHARSUGUDA Ckt-IV	Line	ER	POWERGRID	MO	28-May-2023 09:02	Voltage Regulation	01-Jun-2023 00:00	86:58:00	0

Southern Region Elements

1	765KV CHILAKALURIPETA - CUDDAPAH Ckt-II	Line	SR	POWERGRID	MO	01-May-2023 00:00	Voltage Regulation	05-May-2023 08:08	104:08:00	0
2	765kV KURNOOL - CUDDAPAH Ckt-II	Line	SR	POWERGRID	MO	01-May-2023 00:00	Line tripped at 18:03 hrs and kept line open on over volatge	02-May-2023 15:59	39:59:00	0
3	765kV NIZAMABAD - MAHESHWARAM Ckt-II	Line	SR	POWERGRID	MO	01-May-2023 00:00	Voltage Regulation	14-May-2023 17:07	329:07:00	0
4	765kV VEMAGIRI - CHILAKALURIPETA Ckt-I	Line	SR	POWERGRID	MO	02-May-2023 20:45	Voltage Regulation	03-May-2023 07:23	10:38:00	0
5	765kV VEMAGIRI - CHILAKALURIPETA Ckt-I	Line	SR	POWERGRID	MO	02-May-2023 01:37	Voltage Regulation	02-May-2023 06:42	05:05:00	0
6	765KV-CHILAKALURIPETA-VEMAGIRI_PG-1	Line	SR	pgsr1_sd	SO	02-May-2023 06:43	Commissioning of NGR Bypass breaker	02-May-2023 20:45	14:02:00	0
7	765KV-CHILAKALURIPETA-VEMAGIRI_PG-1 L/R@ CHILAK	Line Reactor	SR	pgsr1_sd	SO	02-May-2023 06:43	Commissioning of NGR Bypass breaker	01-Jun-2023 00:00	713:17:00	0
8	765kV VEMAGIRI - CHILAKALURIPETA Ckt-II	Line	SR	POWERGRID	SO	03-May-2023 07:53	Commissioning of NGR Bypass breaker	03-May-2023 20:08	12:15:00	0
9	765KV-CHILAKALURIPETA-CUDDAPAH-2	Line	SR	pgsr1_sd	SO	05-May-2023 08:09	Commissioning of NGR Bypass breaker	05-May-2023 22:04	13:55:00	0
10	765KV-CHILAKALURIPETA-CUDDAPAH-2 L/R@ CHILAKAL	Line Reactor	SR	pgsr1_sd	SO	05-May-2023 08:12	Commissioning of NGR Bypass breaker	06-May-2023 11:04	26:52:00	0
11	765KV CHILAKALURIPETA - CUDDAPAH Ckt-II	Line	SR	POWERGRID	MO	05-May-2023 22:05	Returned from Planned Shutdown converted to Voltage regulation	06-May-2023 11:04	12:59:00	0
12	765kV KURNOOL - CUDDAPAH Ckt-I	Line	SR	POWERGRID	SO	06-May-2023 01:19	808 kv voltage at cuddapah	08-May-2023 10:22	57:03:00	0
13	765KV-CHILAKALURIPETA-CUDDAPAH-1	Line	SR	pgsr1_sd	SO	06-May-2023 10:17	Commissioning of NGR Bypass breaker	06-May-2023 21:54	11:37:00	0
14	765KV-CHILAKALURIPETA-CUDDAPAH-1 L/R@ CHILAKAL	Line Reactor	SR	pgsr1_sd	SO	06-May-2023 10:17	Commissioning of NGR Bypass breaker	01-Jun-2023 00:00	613:43:00	0
15	765kV VEMAGIRI - CHILAKALURIPETA Ckt-I	Line	SR	POWERGRID	MO	07-May-2023 10:45	taken out on over voltage	19-May-2023 07:07	284:22:00	0
16	765kV CUDDAPAH - THIRUVALAM Ckt-II	Line	SR	POWERGRID	MO	08-May-2023 02:29	Voltage Regulation	15-May-2023 10:04	175:35:00	0
17	765kV NIZAMABAD - MAHESHWARAM Ckt-I	Line	SR	POWERGRID	MO	14-May-2023 17:23	Voltage Regulation	18-May-2023 23:32	102:09:00	0
18	765kV SRIKAKULAM - VEMAGIRI Ckt-I	Line	SR	POWERGRID	TL	16-May-2023 15:58	SKLM End: M1: FD: 154.9kM, FC: 3.69kA, M2: FD: 171kM, FC: 3.4kA VMG End: M2: FD: 151.25kM, FC: 3.621kA	16-May-2023 17:47	01:49:00	1
19	765/400kV 1500MVA ICT-II at VEMAGIRI	ICT	SR	POWERGRID	SO	20-May-2023 06:09	AMP Works	20-May-2023 23:02	16:53:00	0
20	765kV NIZAMABAD - MAHESHWARAM Ckt-II	Line	SR	POWERGRID	MO	20-May-2023 18:24	Voltage Regulation	29-May-2023 15:30	213:06:00	0

NLDC Outage report of Month May 2023

S. No.	Name of Transmission Element	Type of the element	Region Involved	Owner/ Agency	Catagory	Tripping Date and Time	Brief Reason/Relay Indication	Restoration Date and Time	Outage Duration	Number of Cumulative tripping in the month
21	765kV CHILAKALURIPETA - CUDDAPAH Ckt-I	Line	SR	POWERGRID	MO	21-May-2023 18:00	Voltage Regulation	01-Jun-2023 00:00	246:00:00	0
22	765/400kV 1500MVA ICT-II at VEMAGIRI	ICT	SR	POWERGRID	TS	28-May-2023 16:07	differential trip	29-May-2023 04:51	12:44:00	1
23	765kV VEMAGIRI - CHILAKALURIPETA Ckt-II	Line	SR	POWERGRID	TL	28-May-2023 16:07	tripped on Yph-G fault	28-May-2023 22:14	06:07:00	1
24	765kV NIZAMABAD - MAHESHWARAM Ckt-I	Line	SR	POWERGRID	MO	30-May-2023 18:36	Voltage Regulation	12-Jun-2023 07:52	301:16:00	0

North Eastern Region Elements

Nil

	TL= Tripping due to Line Fault
	TS= Tripping due to S/S Fault
	MO= Opened due to system constraints
	TV= Tripped on Overvoltage
	SC= Planned Shutdown for construction activities
	SO= Planned Shutdown for O&M activities
	SE= Emergency Shutdown
	TP= Protection Maloperation
	ME= Miscellaneous outage

24. ALL TIME HIGHEST

31-05-2023

	Maximum Demand Met during the day (MW)	Demand Met during Evening Peak hrs(MW)	Energy Met (MU)	Hydro Gen. (MU)	Wind Gen. (MU)	Solar Gen. (MU)
NR	77091 28-06-2022	71909 09-09-2022	1737 28-06-2022	420 22-08-2022	78 09-06-2022	147 10-05-2023
WR	71321 27-12-2022	63593 18-04-2023 (20:00)	1539 18-04-2023	167 18-12-2014	272 22-05-2022	70.69 12-05-2023
SR	64314 15-03-2023	52366 18-04-2023 (20:00)	1329 19-04-2023	208 31-08-2018	297 12-07-2022	142.7 21-03-2023
ER	29302 19-04-2023 (23:20)	28579 18-04-2023 (20:00)	631 18-04-2023	157 14-09-2022	-	7 23-03-2023
NER	3603 17-08-2022	3510 12-08-2022	69 11-08-2022	41 01-08-2022	-	2 22-06-2022
All India	221347 23-05-2023	207956 18-04-2023 (20:00)	4836 18-04-2023	877 30-08-2022	555 22-05-2022	351 10-05-2023
Regions	States	Max. Demand Met during the day (MW)		Energy Consumption (MU)		
			As on date		As on date	
NR	Punjab	14267	22-08-2022	334.5	29-06-2022	
	Haryana	12540	28-06-2022	266.2	07-07-2021	
	Rajasthan	17097	23-01-2023	330.9	23-05-2023	
	Delhi	7770	29-06-2022	153.5	28-06-2022	
	UP	26002	10-09-2022	547.4	19-08-2022	
	Uttarakhand	2594	14-06-2022	54.3	15-06-2022	
	HP	2071	06-01-2023	39.6	05-06-2022	
	J&K(UT) and Ladakh(UT)	3044	02-02-2023	65.4	20-01-2023	
	Chandigarh	426	08-07-2021	8.4	08-07-2021	
Railways NR ISTS	-	-	-	-		
WR	Chhattisgarh	5642	18-04-2023 (16:00)	129.8	19-04-2023	
	Gujarat	21627	18-04-2023 (14:00)	461.7	18-04-2023	
	MP	17238	13-01-2023	329.3	10-01-2023	
	Maharashtra	28846	14-04-2022	627.8	28-04-2022	
	Goa	759	18-04-2023 (19:00)	17.0	26-05-2023	
	DD & DNH	1278	23-02-2023	29.6	19-04-2023	
	AMNSIL	977	18-08-2021	21.0	31-05-2022	
Balco	-	-	-	-		
SR	Andhra Pradesh*	12653	18-05-2023	251.0	18-05-2023	
	Telangana*	15497	30-03-2023	303.4	03-03-2023	
	Karnataka	16110	20-04-2023 (11:00)	309.5	20-04-2023	
	Kerala	5024	18-04-2023 (22:00)	103.3	19-04-2023	
	Tamil Nadu	19387	20-04-2023 (12:00)	415.4	20-04-2023	
	Pondy	512	17-05-2023	11.6	18-05-2023	
ER	Bihar	6990	06-08-2022	143.4	18-08-2022	
	DVC	3751	18-04-2023 (20:44)	81.2	22-04-2022	
	Jharkhand	1857	19-04-2023 (21:20)	38.3	14-05-2023	
	Odisha	7192	19-04-2023 (15:35)	145.5	25-09-2022	
	West Bengal	11868	18-04-2023 (14:43)	245.7	18-04-2023	
	Sikkim	137	03-02-2022	2.5	28-01-2020	
	Railways ER ISTS	-	-	-	-	
NER	Arunachal Pradesh	172	31-05-2023	2.9	31-05-2023	
	Assam	2376	12-08-2022	47.6	12-08-2022	
	Manipur	258	31-01-2022	3.7	10-02-2022	
	Meghalaya	415	09-02-2022	7.8	31-01-2022	
	Mizoram	157	16-01-2023	2.3	18-01-2023	
	Nagaland	169	27-08-2019	3.1	15-07-2022	
	Tripura	347	18-04-2023 (19:50)	6.8	22-06-2022	
*SR	Andhra Pradesh (Undivided)	13162	23-03-2014	284.8	22-03-2014	

25. System Reliability Indices Report for the month of May 2023

Percentage (%) of times ATC was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	17	4.25	0.57
2	ER-NR	1	0.25	0.03
3	Import of NR	1	0.25	0.03
4	NEW-SR	1	0.25	0.03
5	NER Import	0	0.00	0.00

Percentage(%) of times (N-1) Criteria was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	3	0.75	0.10
2	ER-NR	1	0.25	0.03
3	Import of NR	1	0.25	0.03
4	NEW-SR	1	0.25	0.03
4	NER Import	1	0.25	0.03

Remarks: Flows crossing Total Transfer Capability (TTC) on interregional corridors has been worked out as a proxy for (N-1) violation.



POWER SYSTEM OPERATION CORPORATION LIMITED

पावर सिस्टम ऑपरेशन कारपोरेशन लिमिटेड

NATIONAL LOAD DESPATCH CENTRE – राष्ट्रीय भार प्रेषण केन्द्र

First floor, B-9, Qutab Institutional Area,
Katwaria Sarai, New Delhi-110016.
