



ग्रिड-इंडिया
GRID-INDIA

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड
(भारत सरकार का उद्यम)
GRID CONTROLLER OF INDIA LIMITED
(A Government of India Enterprise)



[formerly Power System Operation Corporation Limited (POSOCO)]
राष्ट्रीय भार प्रेषण केन्द्र / **National Load Despatch Centre**

कार्यालय : बी-9, प्रथम एवं द्वितीय तल, कुतुब इंस्टीट्यूशनल एरिया, कटवारिया सराय, नई दिल्ली - 110016
Office : 1st and 2nd Floor, B-9, Qutab Institutional Area, Katwaria Sarai, New Delhi -110016
CIN : U40105DL2009GOI188682, Website : www.grid-india.in, E-mail : gridindiacc@grid-india.in, Tel.: 011- 42785855

संदर्भ संख्या : - GRID-INDIA/NLDC/MR/

दिनांक : 24.04.2024

सेवा में,

वितरण सूची के अनुसार

विषय:- निष्पादन रिपोर्ट – मार्च 2024

महोदय,

आई०ई०जी०सी०-2010 के प्रावधान के अनुसार, मार्च 2024 माह की अखिल भारतीय प्रणाली की निष्पादन रिपोर्ट संलग्न है।

धन्यवाद

भवदीय

(सुरजीत बनर्जी)

मुख्य महाप्रबन्धक (प्रणाली प्रचालन)

(रा०भा०प्रे०के०)

संलग्नक : मासिक प्रणाली रिपोर्ट

वितरण सूची Distribution List

- 1 सचिव, के.वि.नि.आ. तीसरा एवं चौथा तल, चंद्रलोक भवन, 36, जनपथ, नई दिल्ली-110001
Secretary, CERC, 3rd & 4th Floor, Chanderlok Building, 36, Janpath, New Delhi-110001
- 2 मुख्य अभियंता (जी एम), के.वि.प्रा., सेवा भवन, आर. के. पुरम, नई दिल्ली-110066
Chief Engineer (GM), CEA, Sewa Bhavan, R.K.Puram, New Delhi-110066
- 3 सदस्य सचिव, उ. क्षेत्र. वि. स., 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली - 110016
Member Secretary, NRPC, 18/A, SJSS Marg, Katwaria Sarai, New Delhi-110016
- 4 सदस्य सचिव, प. क्षेत्र. वि. स., एफ-3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई - 400093
Member Secretary, WRPC, F-3, MIDC Area, Andheri (East), Mumbai-400093
- 5 सदस्य सचिव, द. क्षेत्र. वि. स., 29, रेस कोर्स क्रॉस रोड, बंगलूरु - 560009
Member Secretary, SRPC, 29, Race Course Cross Road, Bangalore-560009
- 6 सदस्य सचिव, पू. क्षेत्र. वि. स., 14, गोल्फ क्लब रोड, कोलकाता - 700033
Member Secretary, ERPC, 14, Golf Club Road, Kolkata-700033
- 7 सदस्य सचिव, उ. पू. क्षेत्र. वि. स., मेघालय राज्य आवासीय वित्त सहकारी समिति लिमिटेड भवन, नॉग्रिम हिल्स, शिलोंग - 793003
Member Secretary, NERPC, Meghalaya State Housing Finance Cooperative Society Ltd. Building, Nongrim Hills, Shillong -793003
- 8 मुख्य अभियंता, राष्ट्रीय विद्युत समिति, एनआरपीसी भवन, तृतीय तल, 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली - 110016
Chief Engineer, National Power Committee, NRPC Building, 3rd floor, 18/A, SJSS Marg, Katwaria Sarai, New Delhi-110016
- 9 कार्यपालक निदेशक, पू. क्षेत्र. भा. प्रे. के., 14, गोल्फ क्लब रोड, कोलकाता - 700033
Executive Director, ERLDC, 14, Golf Club Road, Kolkata-700033
- 10 कार्यपालक निदेशक, प. क्षेत्र. भा. प्रे. के., एफ-3, एम आई डी सी क्षेत्र, अंधेरी (पूर्व), मुंबई - 400093
Executive Director, WRLDC, F-3, MIDC Area, Andheri (East), Mumbai-400093
- 11 कार्यपालक निदेशक, उ. क्षेत्र. भा. प्रे. के., 18/ए, शहीद जीत सिंह सनसनवाल मार्ग, नई दिल्ली - 110016
Executive Director, NRPC, 18/A, SJSS Marg, Katwaria Sarai, New Delhi-110016
- 12 कार्यपालक निदेशक, द. क्षेत्र. भा. प्रे. के., 29, रेस कोर्स क्रॉस रोड, बंगलूरु - 560009
Executive Director, SRLDC, 29, Race Course Cross Road, Bangalore-560009
- 13 मुख्य महाप्रबंधक, पू. क्षेत्र. भा. प्रे. के., डोंगतिह, लोअर नॉग्रह, लापलंग, शिलोंग- 793006
Chief General Manager, NERLDC, Dongtiah, Lower Nongrah, Laplang, Shillong-793006



ग्रिड-इंडिया
GRID-INDIA

GRID CONTROLLER OF INDIA LIMITED


Formerly Power System Operation Corporation Limited

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड

NATIONAL LOAD DESPATCH CENTRE –राष्ट्रीय भार प्रेषण केन्द्र

मासिक ऑपरेशन रिपोर्ट

Monthly
Operation Report



मार्च 2024

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड
राष्ट्रीय भार प्रेषण केंद्र, नई दिल्ली

GRID CONTROLLER OF INDIA LIMITED

Formerly Power System Operation Corporation Limited

NATIONAL LOAD DESPATCH CENTRE, NEW DELHI



ग्रिड-इंडिया
GRID-INDIA

माह मार्च 2024 के लिए प्रचालन निष्पादन रिपोर्ट

OPERATIONAL PERFORMANCE REPORT FOR THE

MONTH OF MARCH -2024


पृष्ठसूची CONTENTS

1	माह मार्च 2024 की सारांश रिपोर्ट Summary of report for the month of MARCH 2024	1-5
2	क्षेत्रवार स्थापित विद्युत क्षमता Region wise Installed Capacity	6
3	राष्ट्रीय स्तर पर सांध्यकालीन शिखर मांगपूर्ति Peak demand met at National level	7-8
4	राष्ट्रीय स्तर पर विद्युत ऊर्जा खपत Energy consumption at National level	9-10
5	फ्रिक्वेंसी रूपरेखा Frequency profile	11-12
6	राष्ट्रीय स्तर पर जल विद्युत ऊर्जा उत्पादन Hydro generation at National level	13-14
7	राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन Wind generation at National level	15
8	राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन Solar generation at National level	16
9	राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग पूर्ति Daily maximum demand met at National level	17
10	15 मार्च के माँग एवं उत्पादन प्लॉट (अधिकतम मांग पूर्ति) व माँग का डाटा (15 मिनट अंतराल) Demand and generation plots for 15-MARCH (Max Demand Met) and Demand data (15-minute interval)	18-22
11	ऊर्जा आपूर्ति की वास्तविक स्थिति Actual power supply position	23
12	ऊर्जा आवश्यकता एवं आपूर्ति की पिछले वर्ष माह मार्च 2023 से तुलना Energy requirement and met comparison with MARCH 2023	24
13	शिखर मांग आवश्यकता एवं आपूर्ति की पिछले वर्ष माह मार्च 2023 से तुलना Peak demand requirement and met comparison with MARCH 2023	25


14	क्षेत्रीय स्तर पर शिड्यूल एवं ड्रावल Schedule & drawal at regional level	26
15	अंतर क्षेत्रीय विनिमय Inter-regional exchanges	27-36
16	अंतर राष्ट्रीय विद्युत विनिमय Inter-national exchanges	37-39
17	एसटीओए (द्विपक्षीय एवं सामूहिक) एवं यू आइ का ब्यौरा Bilateral and collective short-term open access & UI details	40
18	पावर मार्केट की सूचना Power market information	41-47
19	अक्षय ऊर्जा प्रमाण पत्र प्रक्रिया Renewable energy certificate mechanism	48-50
20	मुख्य घटनाएँ एवं डिस्टर्बेंस Important events/disturbances	51-58
21	नए कमीशंड पारेषण तत्व New elements commissioned	59
22	विभव रूपरेखा Voltage profile	60
23	अब तक उच्चतम (मांग व ऊर्जा) आँकड़े : माह मार्च 2024 तक All Time Highest (Demand & Energy) figures: Till MARCH 2024	61
24	मार्च 2024 के लिए सिस्टम रिलाइबिलिटी सूचकांक System Reliability Indices for MARCH 2024	62

1. SUMMARY OF REPORT FOR THE MONTH OF MARCH-2024


EVENING PEAK HOUR (at 1900hrs) DEMAND MET AT NATIONAL LEVEL (MW)

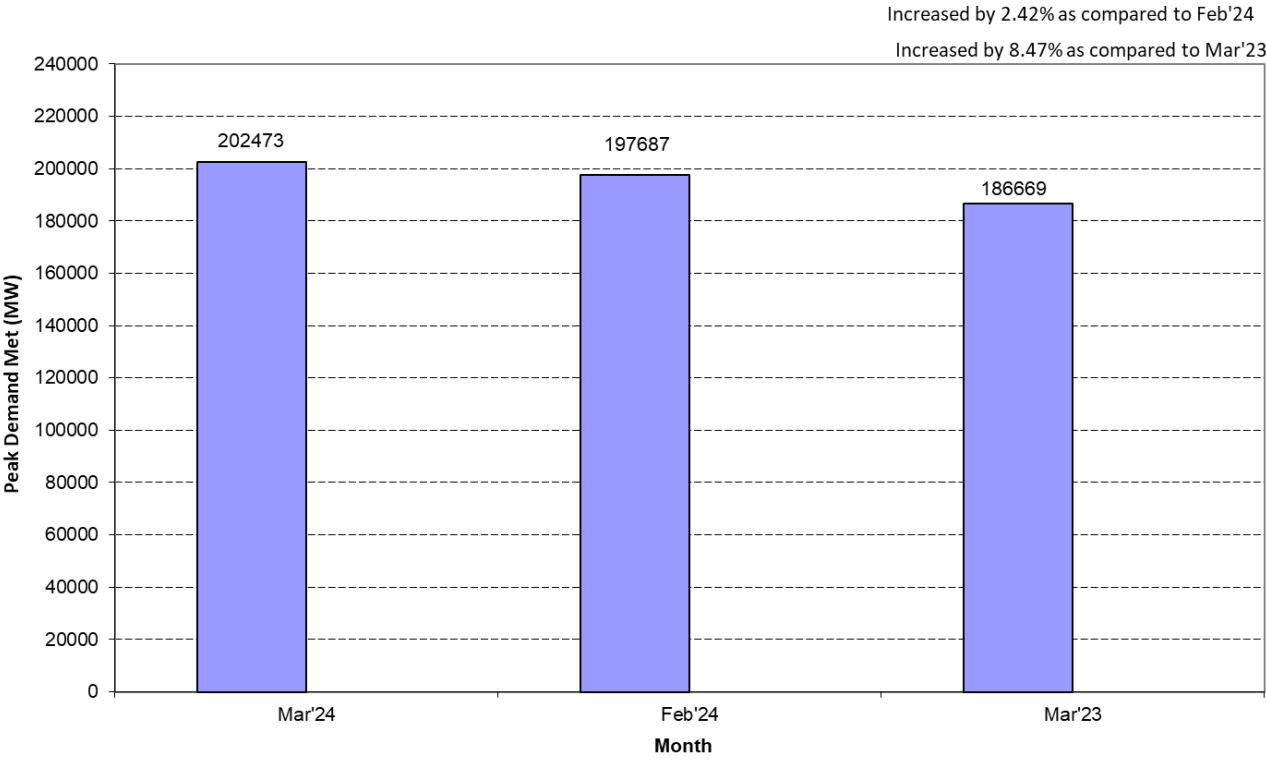


Frequency within IEGC Band

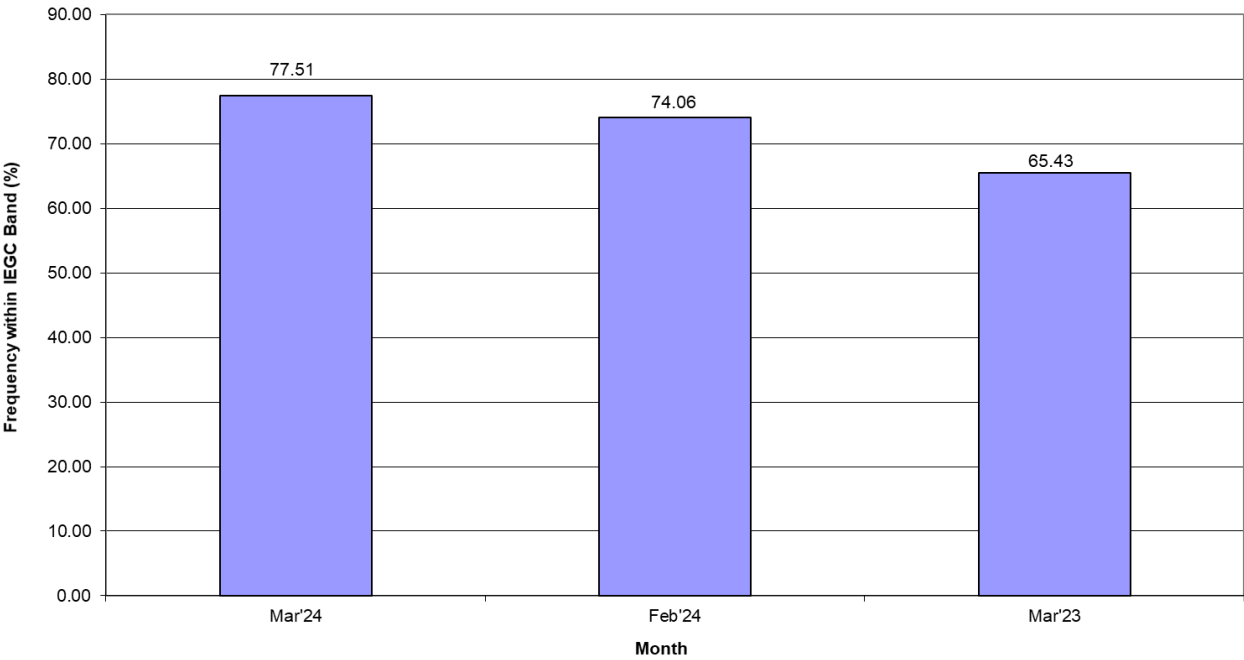


ENERGY MET AT NATIONAL LEVEL (MU)

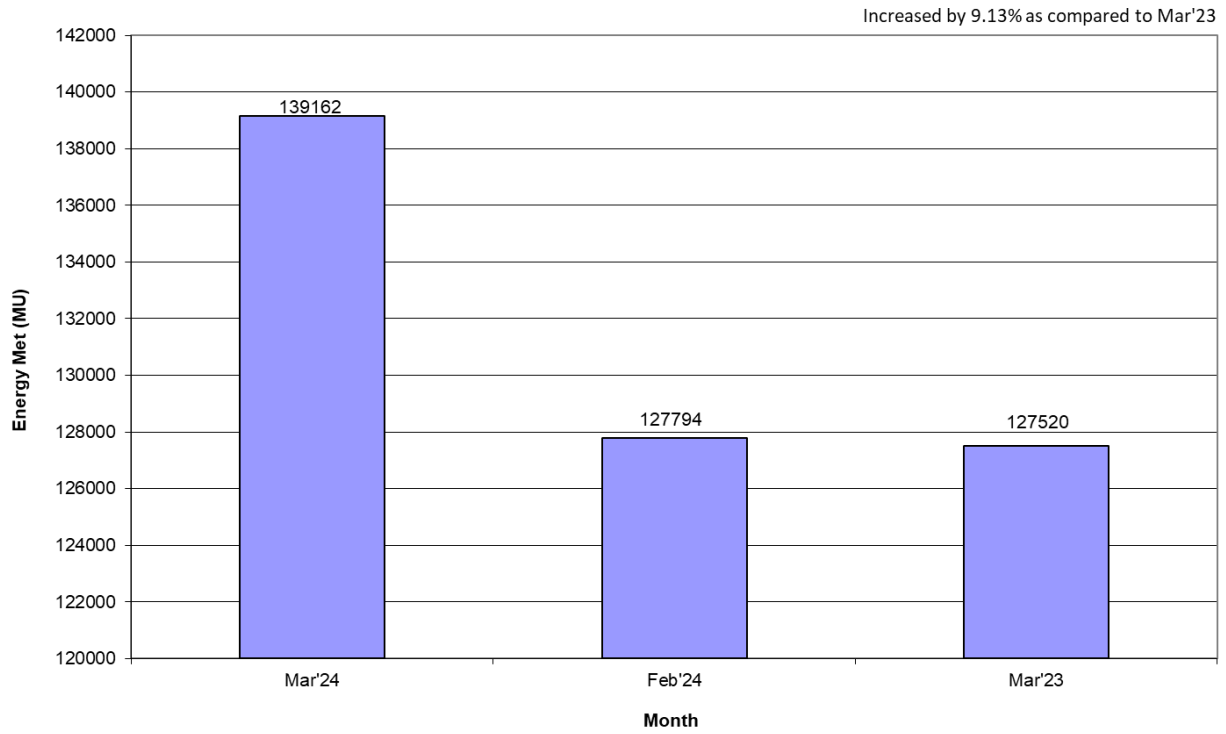


AVERAGE ENERGY MET AT NATIONAL LEVEL (MU/Day)

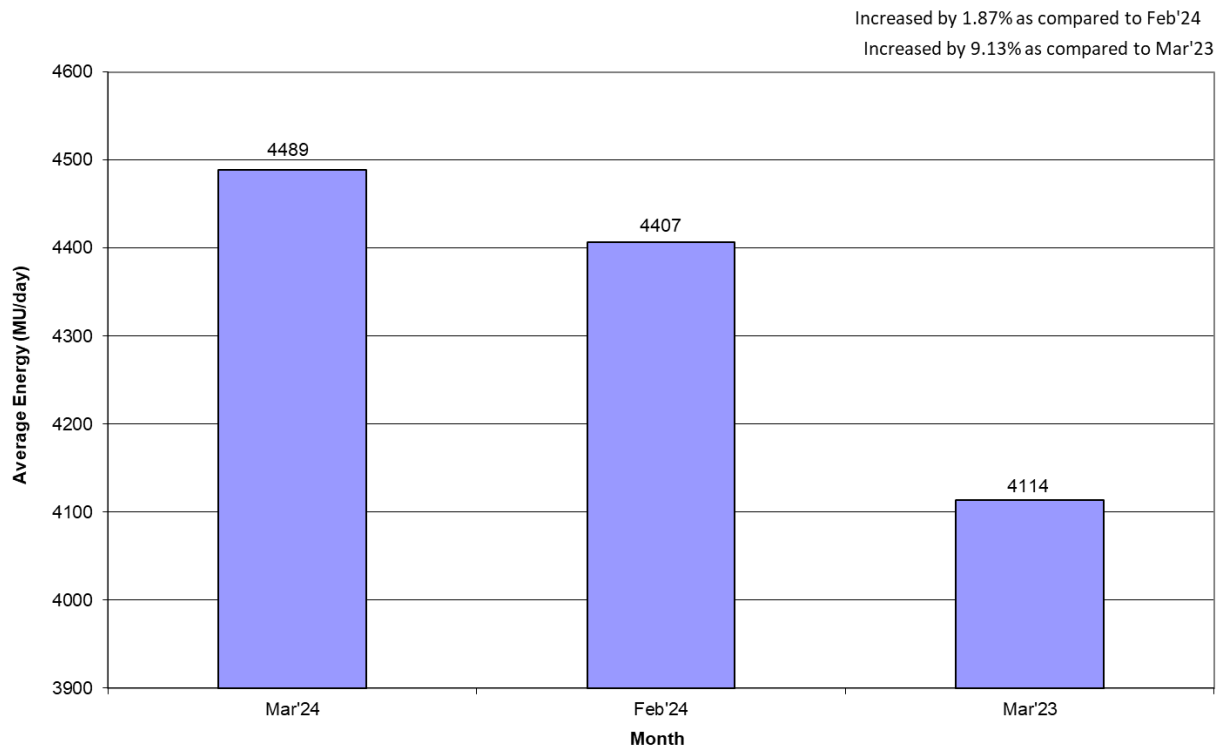


HYDRO GENERATION AT NATIONAL LEVEL (MU)

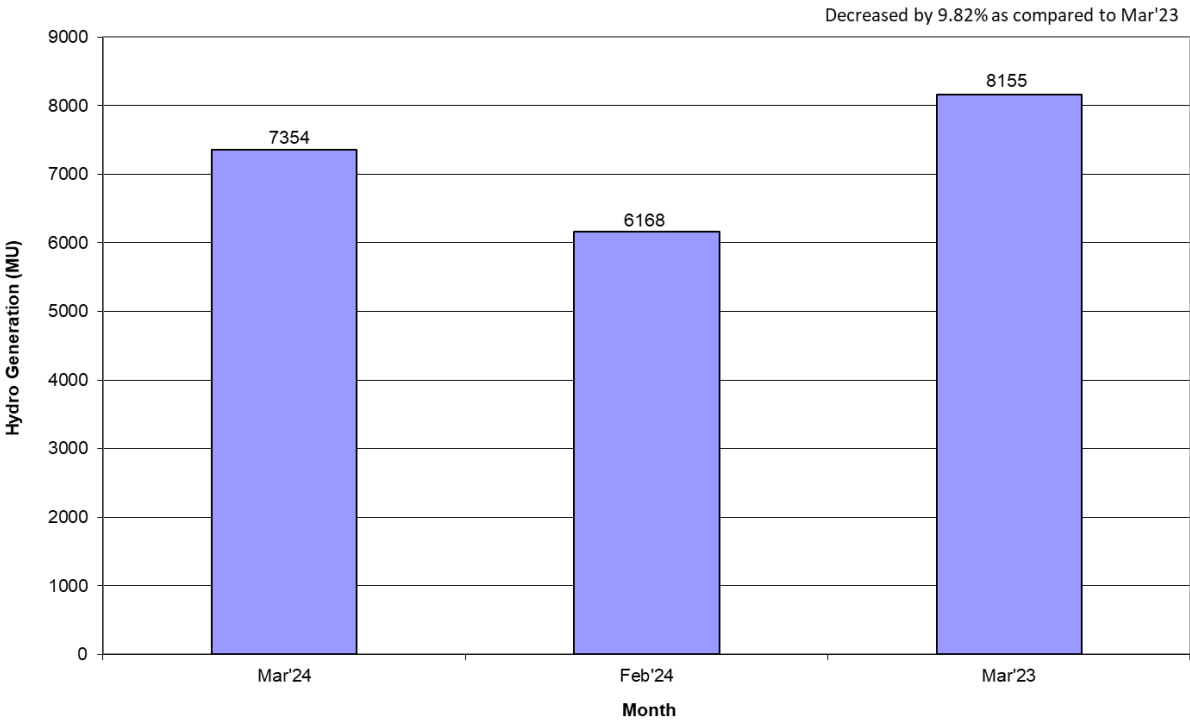


AVERAGE HYDRO GENERATION AT NATIONAL LEVEL (MU/Day)

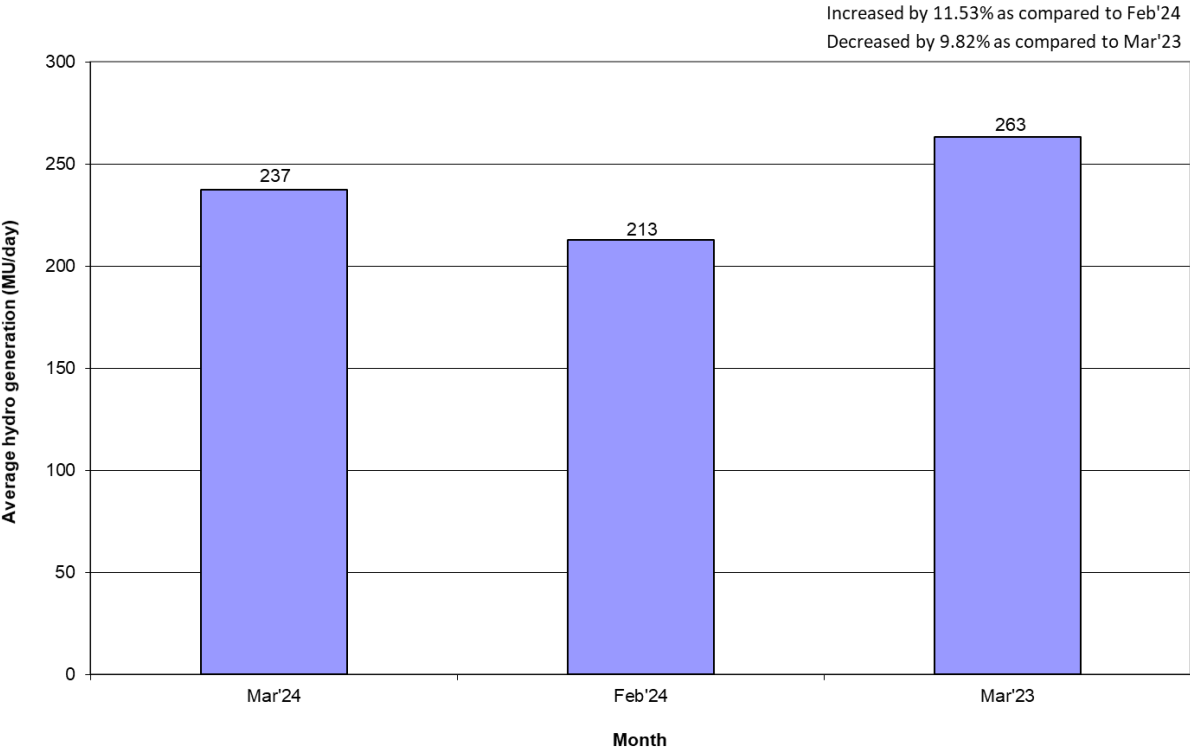


WIND GENERATION AT NATIONAL LEVEL (MU)

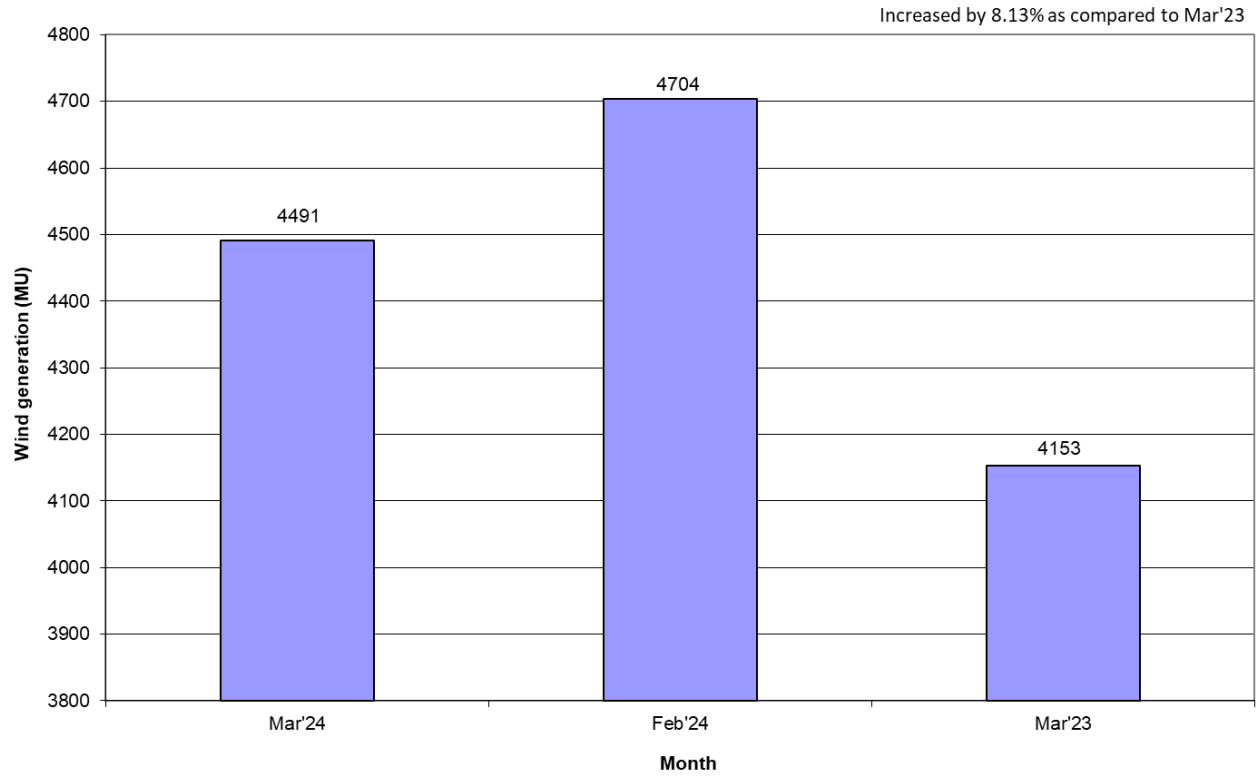


AVERAGE WIND GENERATION AT NATIONAL LEVEL (MU/Day)

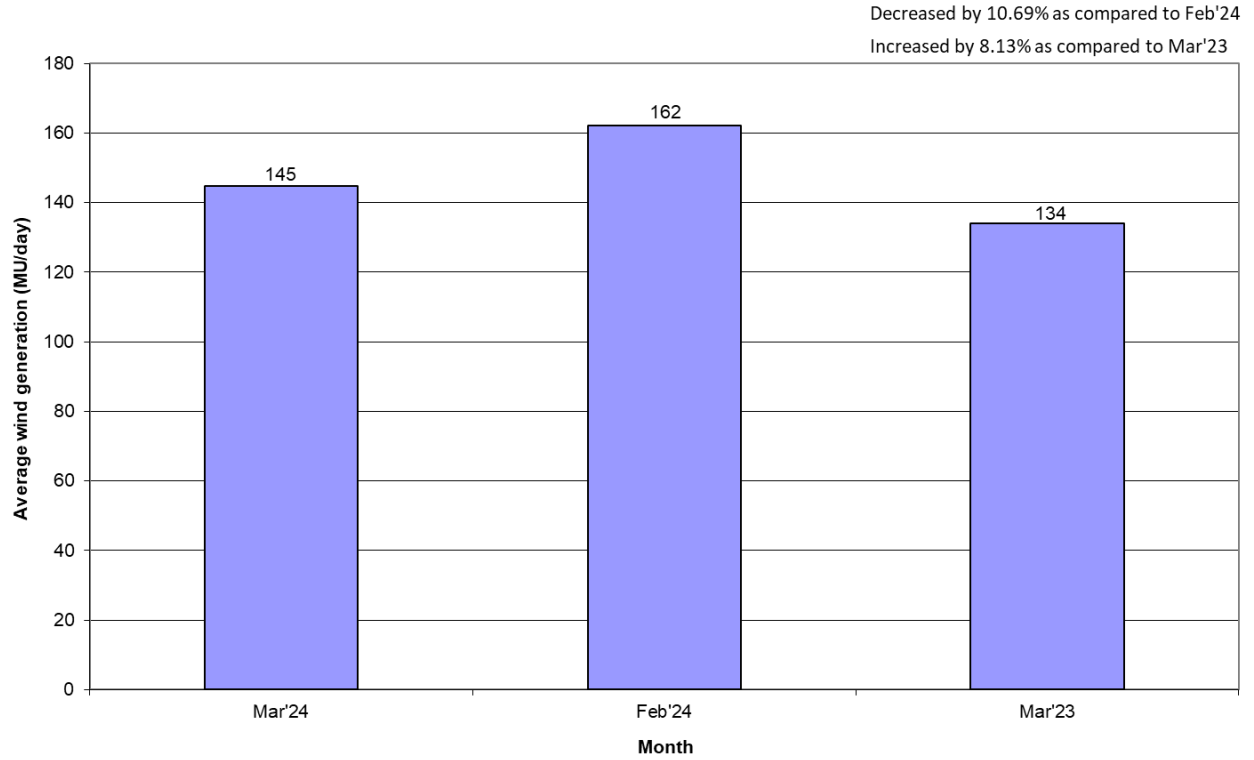

SOLAR GENERATION AT NATIONAL LEVEL (MU)

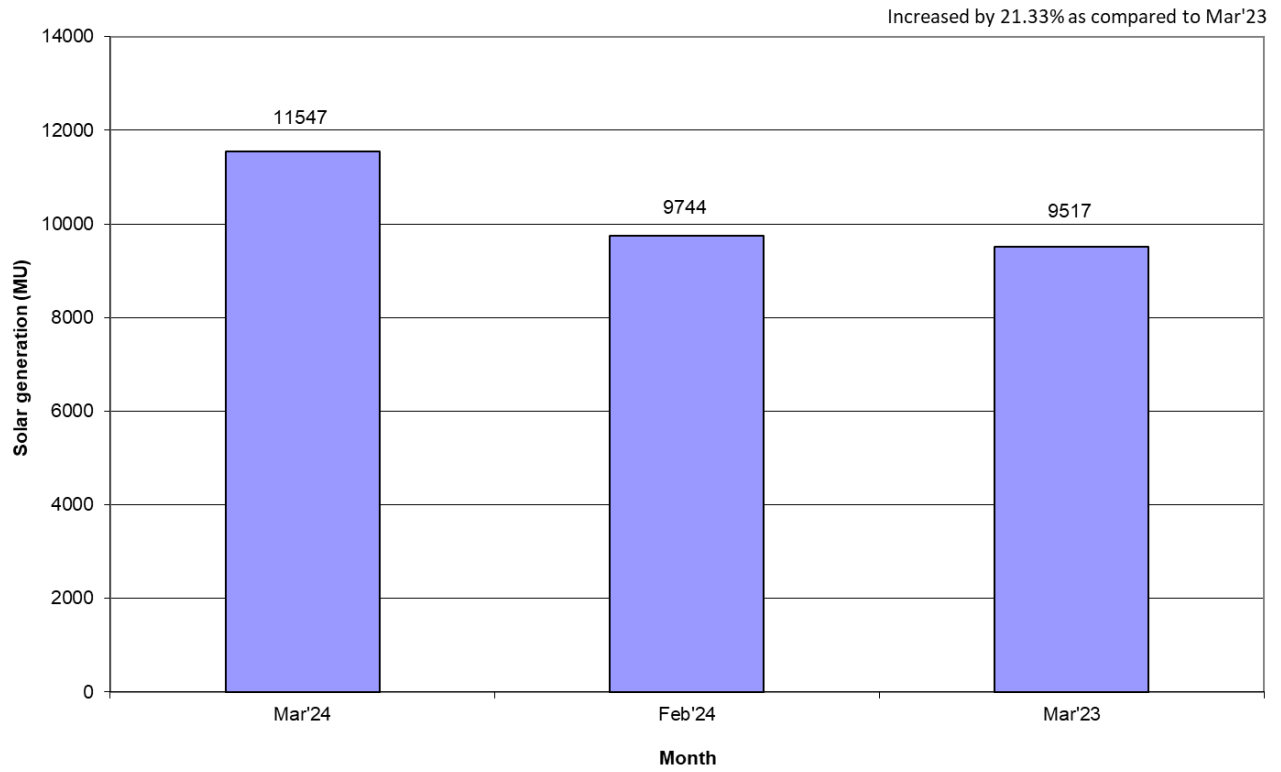

AVERAGE SOLAR GENERATION AT NATIONAL LEVEL (MU/Day)

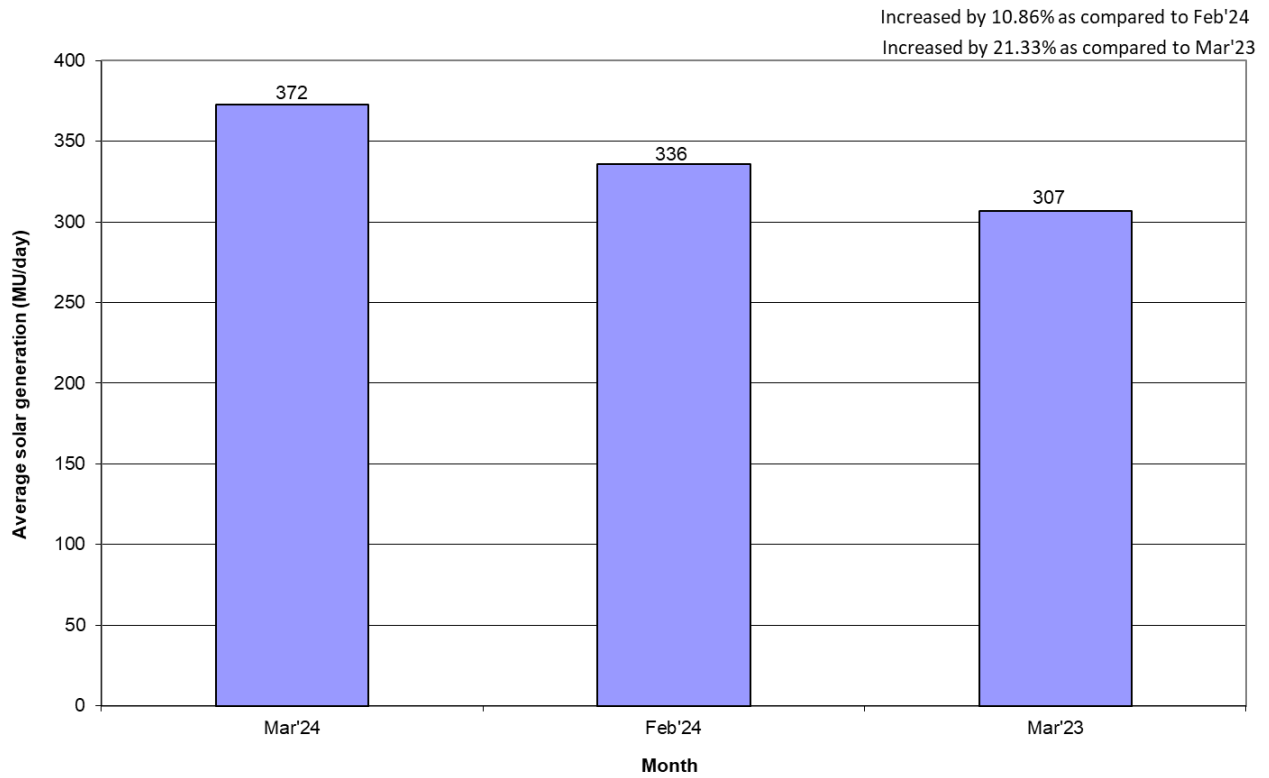

2. ALL INDIA REGIONWISE INSTALLED CAPACITY

As on 31.03.2024
(All figures are in MW)

S No	Region	THERMAL					NUCLEAR	HYDRO	RES @ MNRE	GRAND TOTAL
		COAL	LIGNITE	GAS	DIESEL	TOTAL				
1	NR	56951	1580	5995	0	64526	1620	20830	38493	125469
2	WR	74663	1400	10806	0	86869	3240	7563	48709	146380
3	SR	49894	3640	6492	434	60460	3320	11827	53819	129426
4	ER	28512	0	80	0	28592	0	4764	2009	35366
5	NER	949	0	1665	36	2650	0	1944	575	5169
6	ISLANDS	0	0	0	120	120	0	0	40	160
	ALL INDIA	210969	6620	25038	589	243217	8180	46928	143645	441970

Remarks: Data from CEA website

3. राष्ट्रीय स्तर पर संध्याकालीन शिखर विद्युत मांग पूर्ति
EVENING PEAK HOUR DEMAND MET AT NATIONAL LEVEL


माह: मार्च 2024 MONTH:- MAR 2024

सभी आंकड़े मेगावाट मे All figures in MW

दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
1-Mar-24	49382	61613	51161	21874	2643	186673
2-Mar-24	45482	60003	50712	22779	2772	181748
3-Mar-24	46073	57440	46830	21273	2484	174100
4-Mar-24	50603	60241	51835	21891	2544	187114
5-Mar-24	51708	60889	51404	22125	2682	188808
6-Mar-24	51002	61303	52528	22417	2711	189961
7-Mar-24	51288	62833	52787	22520	2667	192095
8-Mar-24	50373	59664	51427	22571	2641	186676
9-Mar-24	51477	62313	50926	22438	2691	189845
10-Mar-24	48557	60622	47008	22886	2539	181612
11-Mar-24	52689	64341	52377	23392	2716	195515
12-Mar-24	52930	64854	53086	23206	2619	196695
13-Mar-24	51453	64219	53663	23816	2675	195826
14-Mar-24	53920	65232	53089	24072	2651	198964
15-Mar-24	52787	64470	53389	24283	2738	197667
16-Mar-24	54297	63696	52389	22809	2771	195962
17-Mar-24	51368	60339	47907	22750	2737	185101
18-Mar-24	53697	63172	52831	22750	2813	195263
19-Mar-24	53274	62349	52440	22971	2828	193862
20-Mar-24	53680	62298	52231	18734	2518	189461
21-Mar-24	52833	64173	52656	21621	2523	193806
22-Mar-24	53791	64979	52897	22934	2660	197261
23-Mar-24	52546	64393	52394	23566	2621	195520
24-Mar-24	46280	58255	47423	22506	2446	176910
25-Mar-24	42042	52025	49168	19689	2431	165355
26-Mar-24	49568	62887	51861	22191	2511	189018
27-Mar-24	52972	65150	52949	24150	2676	197897
28-Mar-24	55172	66749	44532	25265	2721	194439
29-Mar-24	54944	65061	52942	25559	2805	201311
30-Mar-24	56198	64044	52603	26731	2897	202473
31-Mar-24	52834	62334	48671	25002	1926	190767
उच्चतम MAXIMUM	56198	66749	53663	26731	2897	202473
निम्नतम MINIMUM	42042	52025	44532	18734	1926	165355
औसत AVERAGE	51459	62321	51230	22928	2634	190571
अब तक का उच्चतम All Time Max.	76274	66749	53663	28579	3510	215592
दिनांक Date	04.09.23	28.03.24	13.03.24	18.04.23	12.08.22	28.08.23

नोट : सभी आंकड़े 1900 बजे की मांगपूर्ति पर आधारित है ।
 Note: The above figures correspond to value at 1900 Hrs

EVENING PEAK HOUR DEMAND(at 1900hrs)MET DURING THE MONTH OF MARCH 2024

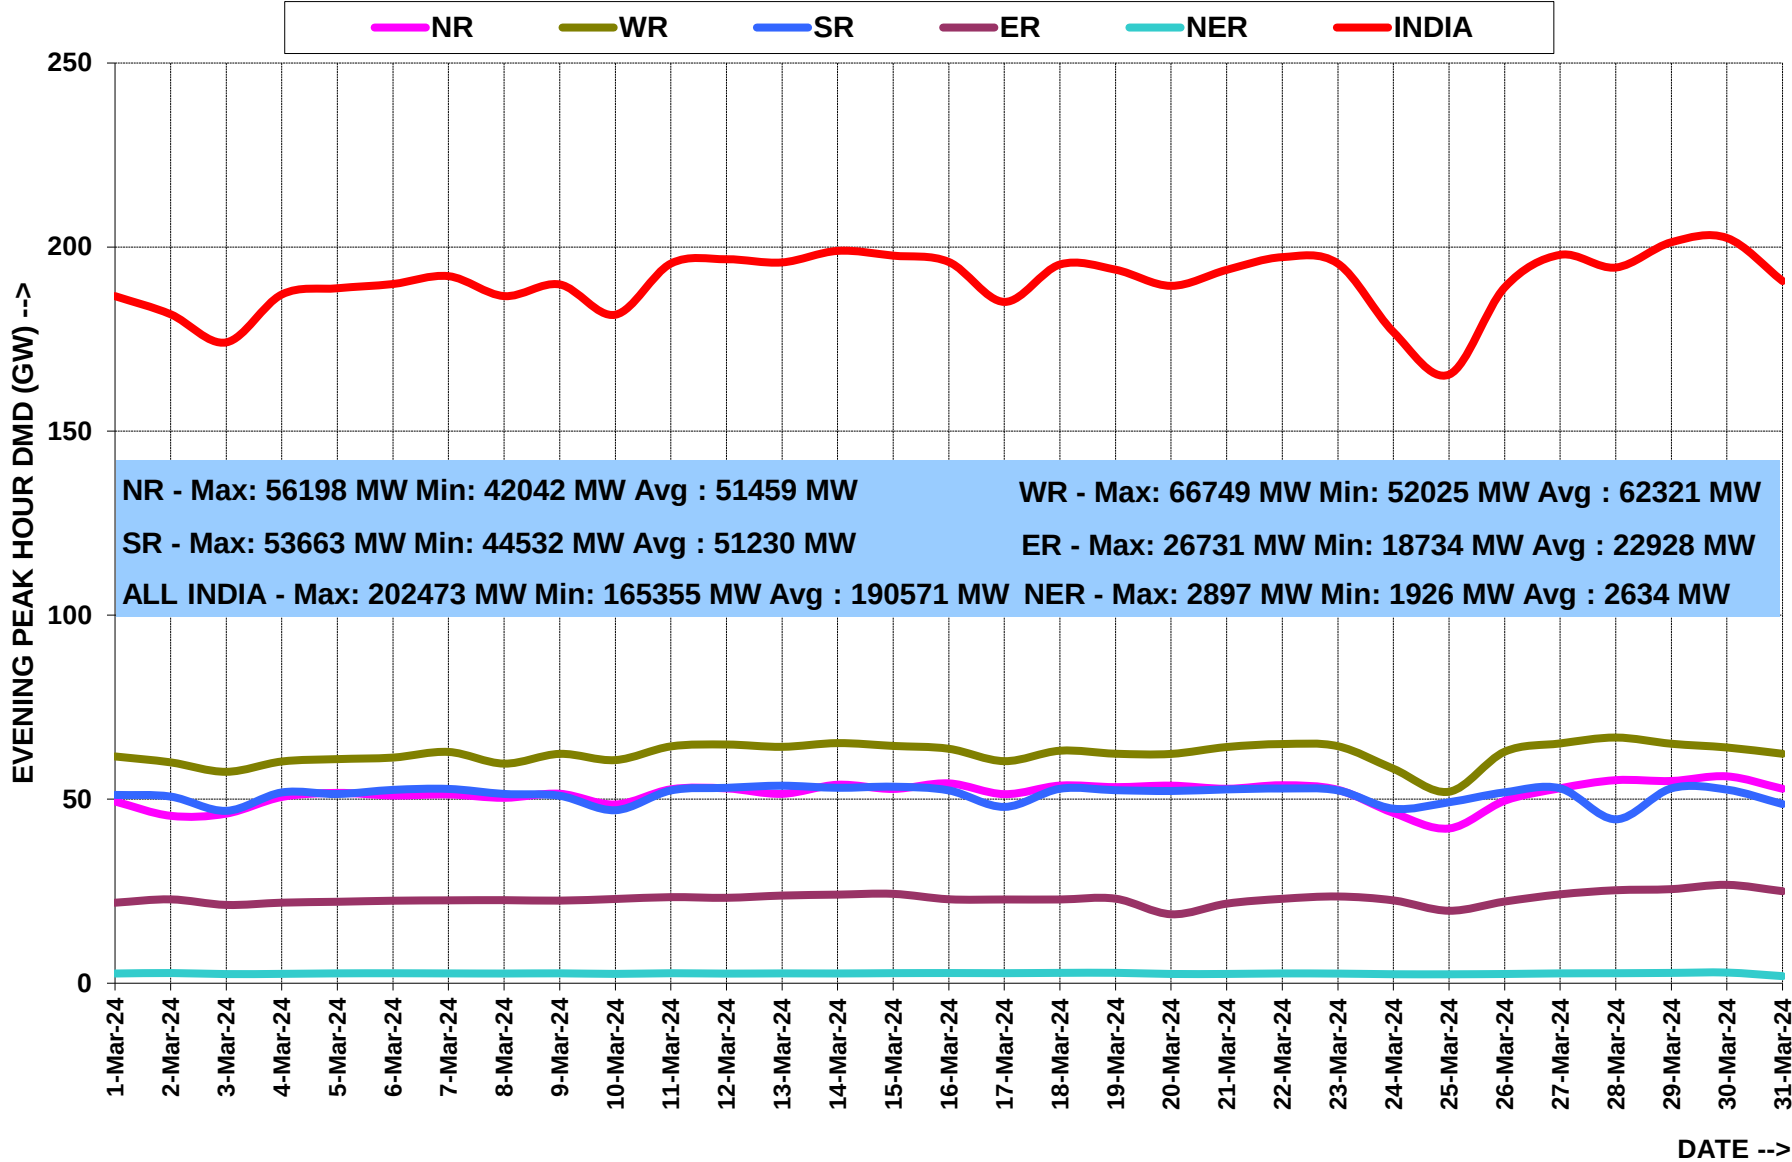


4. राष्ट्रीय स्तर पर विद्युत ऊर्जा आपूर्ति ENERGY MET AT NATIONAL LEVEL

माह: मार्च 2024 MONTH:- MAR 2024

सभी आंकड़े मिलियन यूनिट में All figures in MU

दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Mar-24	1122	1477	1339	463	49	4450
02-Mar-24	958	1423	1331	475	50	4237
03-Mar-24	948	1343	1269	451	47	4057
04-Mar-24	1043	1390	1325	452	49	4260
05-Mar-24	1089	1416	1359	466	48	4378
06-Mar-24	1094	1424	1363	477	48	4406
07-Mar-24	1096	1447	1374	490	48	4456
08-Mar-24	1099	1434	1374	490	50	4447
09-Mar-24	1098	1449	1358	491	49	4445
10-Mar-24	1061	1442	1297	490	46	4336
11-Mar-24	1102	1504	1363	498	48	4516
12-Mar-24	1145	1529	1388	504	50	4615
13-Mar-24	1135	1524	1401	524	50	4634
14-Mar-24	1149	1534	1403	527	51	4663
15-Mar-24	1183	1528	1404	529	50	4694
16-Mar-24	1181	1515	1380	521	51	4648
17-Mar-24	1161	1462	1286	488	49	4445
18-Mar-24	1189	1491	1349	512	52	4593
19-Mar-24	1201	1482	1357	504	52	4596
20-Mar-24	1196	1467	1344	420	48	4475
21-Mar-24	1155	1505	1343	432	49	4485
22-Mar-24	1169	1524	1366	469	48	4575
23-Mar-24	1170	1525	1358	484	48	4586
24-Mar-24	1078	1465	1291	481	45	4359
25-Mar-24	958	1303	1302	451	46	4059
26-Mar-24	1040	1439	1342	454	41	4317
27-Mar-24	1137	1544	1369	510	49	4610
28-Mar-24	1185	1585	1385	543	50	4747
29-Mar-24	1216	1580	1390	564	52	4803
30-Mar-24	1170	1552	1378	582	53	4735
31-Mar-24	1144	1495	1310	542	43	4534
कुल TOTAL	34670	45799	41901	15285	1508	139162
उच्चतम MAXIMUM	1216	1585	1404	582	53	4803
निम्नतम MINIMUM	948	1303	1269	420	41	4057
औसत AVERAGE	1118	1477	1352	493	49	4489
संचयी 2023-24 Cumulative 2023-24	474861	515698	422734	186730	19744	1619766
अब तक का उच्चतम All Time Max.	1796	1618	1404	639	72	5224
दिनांक Date	04.09.23	02.09.23	15.03.24	08.06.23	15.09.23	02.09.23

ENERGY MET DURING THE MONTH OF MARCH' 2024

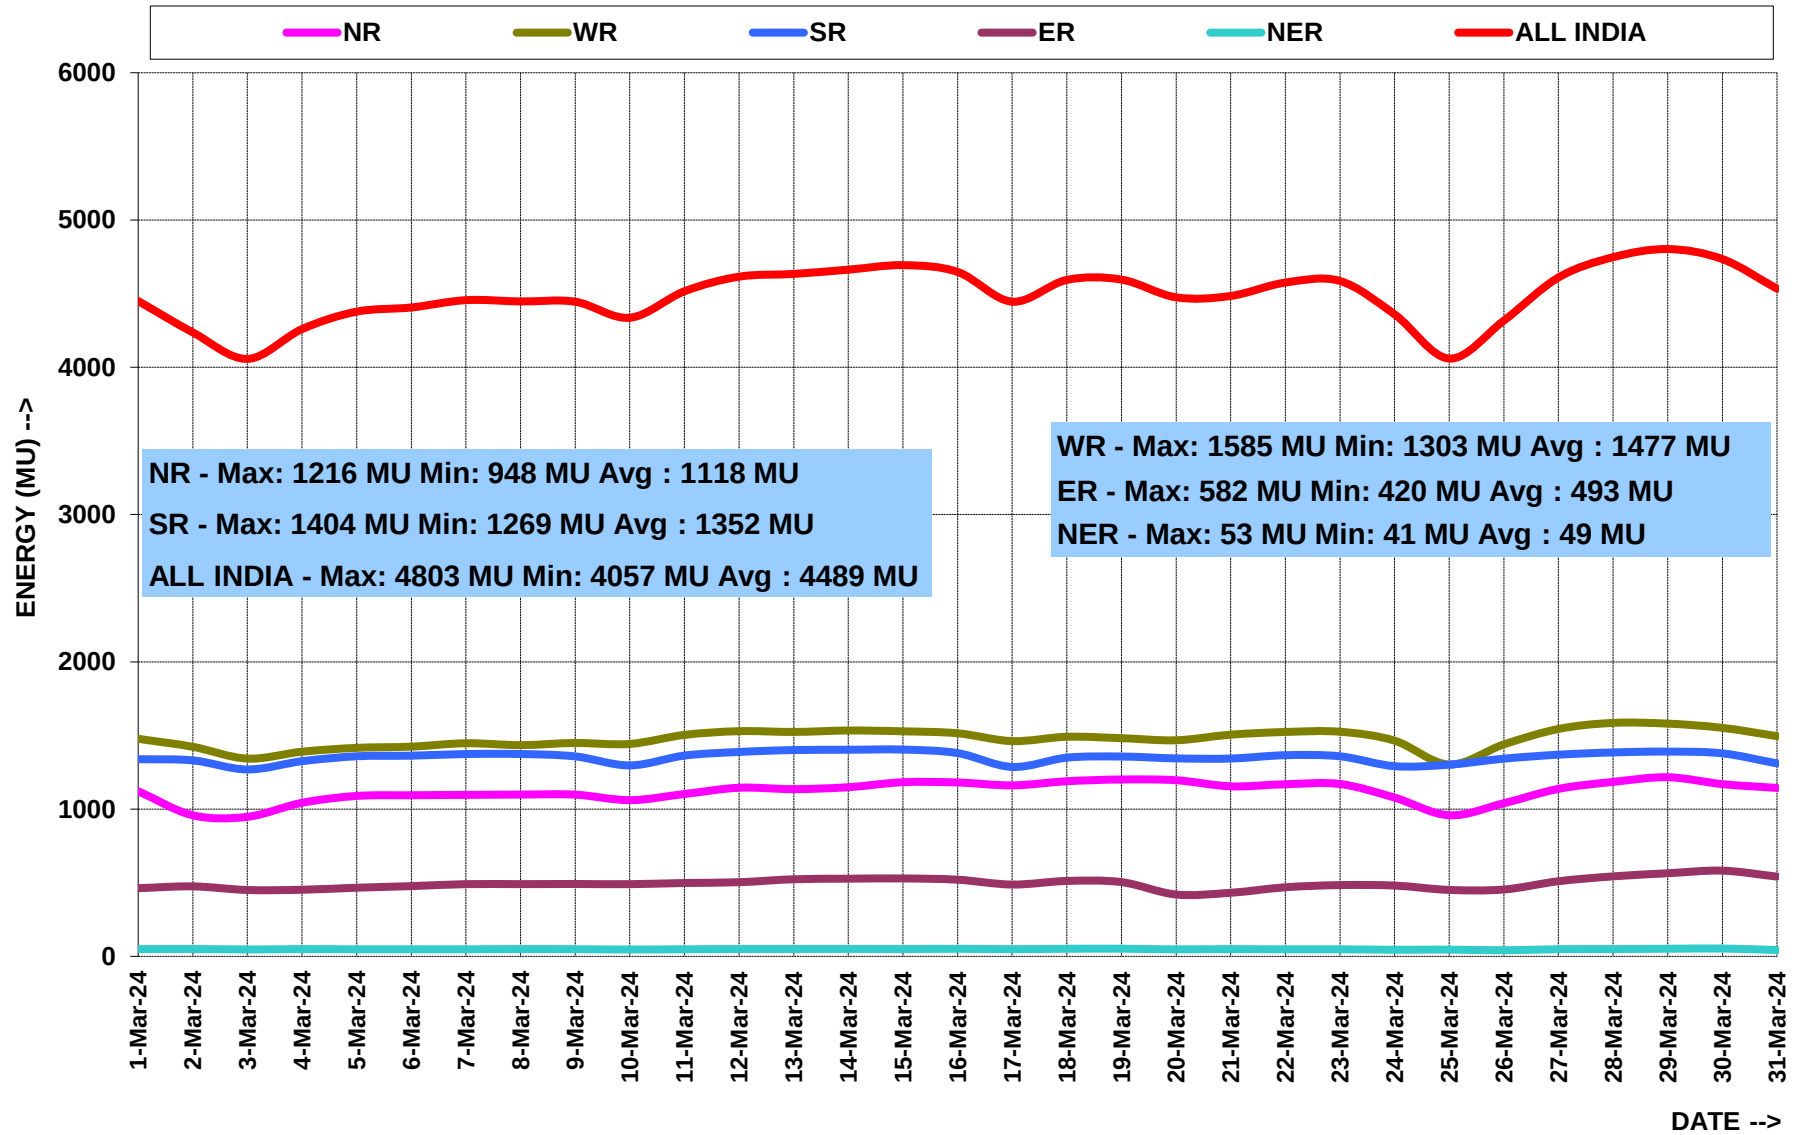

5. वर्ष 2023-24 के लिए आवृत्ति रूपरेखा FREQUENCY PROFILE FOR YEAR 2023-24

राष्ट्रीय ग्रीड NATIONAL GRID								
फ्रीक्वेंसी रूपरेखा (Hz)			<49.9	49.9-50.05	>50.05	उच्चतम फ्रीक्वेंसी	निम्नतम फ्रीक्वेंसी	औसत फ्रीक्वेंसी
% समय	Apr-23	All India Grid	10.54	67.90	21.56	50.33	49.49	49.99
	May-23	All India Grid	9.83	68.48	21.69	50.43	49.48	49.99
	Jun-23	All India Grid	6.47	67.82	25.71	50.41	49.51	50.01
	Jul-23	All India Grid	4.60	74.96	20.44	50.23	49.76	50.01
	Aug-23	All India Grid	7.08	77.28	15.63	50.20	49.74	50.00
	Sep-23	All India Grid	5.26	77.90	16.84	50.21	49.77	50.00
	Oct-23	All India Grid	8.87	74.42	16.71	50.21	49.71	49.99
	Nov-23	All India Grid	6.83	74.36	18.81	50.26	49.73	50.00
	Dec-23	All India Grid	7.83	75.21	16.96	50.26	49.71	49.99
	Jan-24	All India Grid	6.80	75.83	17.37	50.25	49.73	50.00
	Feb-24	All India Grid	6.24	74.06	19.70	50.26	49.74	50.00
	Mar-24	All India Grid	6.02	77.51	16.46	50.26	49.76	50.00
	2023-24 (upto Mar)	All India Grid	7.20	73.83	18.97	50.43	49.48	50.00

5.1 मार्च 2024 के लिए आवृत्ति रूपरेखा FREQUENCY PROFILE FOR MARCH 2024

फ्रिक्वेंसी रूपरेखा (Hz)		<49.9	49.9-50.05	>50.05	उच्चतम फ्रिक्वेंसी	निम्नतम फ्रिक्वेंसी	औसत फ्रिक्वेंसी	एफ़.वी.आई.
% समय	01-Mar-24	6.56	75.97	17.47	50.28	49.75	50.00	0.04
	02-Mar-24	5.00	71.75	23.25	50.30	49.73	50.01	0.05
	03-Mar-24	0.98	68.11	30.90	50.34	49.87	50.04	0.07
	04-Mar-24	3.26	73.69	23.04	50.30	49.82	50.01	0.05
	05-Mar-24	7.67	73.18	19.14	50.29	49.72	50.00	0.05
	06-Mar-24	8.76	76.93	14.31	50.23	49.73	49.99	0.05
	07-Mar-24	4.72	81.84	13.44	50.25	49.81	50.00	0.03
	08-Mar-24	5.69	75.88	18.43	50.25	49.70	50.00	0.04
	09-Mar-24	7.44	74.87	17.69	50.23	49.62	50.00	0.05
	10-Mar-24	5.96	78.81	15.23	50.23	49.76	50.00	0.04
	11-Mar-24	8.47	78.34	13.18	50.27	49.73	49.99	0.04
	12-Mar-24	9.46	75.95	14.59	50.21	49.75	49.98	0.05
	13-Mar-24	6.66	80.03	13.31	50.23	49.80	49.99	0.04
	14-Mar-24	3.63	82.85	13.52	50.26	49.80	49.99	0.03
	15-Mar-24	5.64	77.22	17.14	50.22	49.80	50.00	0.04
	16-Mar-24	6.79	73.61	19.59	50.27	49.80	50.00	0.04
	17-Mar-24	3.47	76.06	20.46	50.43	49.80	50.01	0.04
	18-Mar-24	4.79	77.43	17.78	50.19	49.78	50.00	0.03
	19-Mar-24	2.09	80.22	17.69	50.21	49.84	50.01	0.03
	20-Mar-24	3.73	78.38	17.89	50.31	49.78	50.01	0.04
	21-Mar-24	5.82	79.78	14.40	50.26	49.79	50.00	0.04
	22-Mar-24	5.82	81.71	12.47	50.21	49.77	49.99	0.03
	23-Mar-24	6.69	81.09	12.22	50.21	49.76	49.99	0.03
	24-Mar-24	5.10	80.78	14.12	50.28	49.80	49.99	0.03
	25-Mar-24	6.61	81.45	11.94	50.28	49.74	49.99	0.04
	26-Mar-24	9.73	76.34	13.92	50.23	49.67	49.99	0.05
	27-Mar-24	11.45	73.08	15.47	50.26	49.74	49.99	0.05
	28-Mar-24	11.06	76.57	12.36	50.26	49.59	49.98	0.06
	29-Mar-24	6.70	77.94	15.36	50.24	49.77	50.00	0.04
	30-Mar-24	1.77	84.20	14.03	50.22	49.83	50.01	0.02
	31-Mar-24	5.16	78.83	16.01	50.23	49.79	50.00	0.04


6.राष्ट्रीय स्तर पर जल विद्युत उत्पादन
HYDRO GENERATION AT NATIONAL LEVEL

माह: मार्च 2024 MONTH:- MAR 2024

सभी आंकड़े मिलियन यूनिट में All figures in MU

दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Mar-24	109	28	44	19	7	208
02-Mar-24	129	25	40	14	8	215
03-Mar-24	160	21	36	15	9	239
04-Mar-24	144	24	49	14	10	241
05-Mar-24	129	25	49	14	11	228
06-Mar-24	126	26	48	18	9	228
07-Mar-24	122	33	56	18	9	238
08-Mar-24	114	33	53	18	10	228
09-Mar-24	119	34	55	20	8	236
10-Mar-24	119	33	47	16	11	227
11-Mar-24	124	41	56	18	10	249
12-Mar-24	122	37	62	20	9	250
13-Mar-24	126	35	58	19	9	247
14-Mar-24	127	35	56	20	11	249
15-Mar-24	125	30	47	20	9	231
16-Mar-24	121	28	44	17	9	218
17-Mar-24	119	25	33	19	8	204
18-Mar-24	125	29	43	17	8	221
19-Mar-24	129	31	42	16	8	225
20-Mar-24	122	27	35	14	8	205
21-Mar-24	124	28	38	18	10	218
22-Mar-24	137	28	49	19	19	251
23-Mar-24	139	28	49	19	18	253
24-Mar-24	140	23	37	17	15	231
25-Mar-24	130	24	38	15	11	218
26-Mar-24	137	31	44	21	16	250
27-Mar-24	131	31	58	21	15	256
28-Mar-24	144	43	64	22	12	285
29-Mar-24	153	36	54	19	10	272
30-Mar-24	157	27	47	22	12	265
31-Mar-24	166	25	46	21	11	269
कुल TOTAL	4065	925	1476	560	328	7354
उच्चतम MAXIMUM	166	43	64	22	19	285
निम्नतम MINIMUM	109	21	33	14	7	204
औसत AVERAGE	131	30	48	18	11	237
संचयी 2023-24 Cumulative 2023-24	76459	16860	21494	22597	6718	144128
अब तक का उच्चतम All Time Max.	443	167	208	157	41	877
दिनांक Date	01.08.23	18.12.14	31.08.18	14.09.22	29.08.23	30.08.22

HYDRO ENERGY DURING THE MONTH OF MARCH' 2024

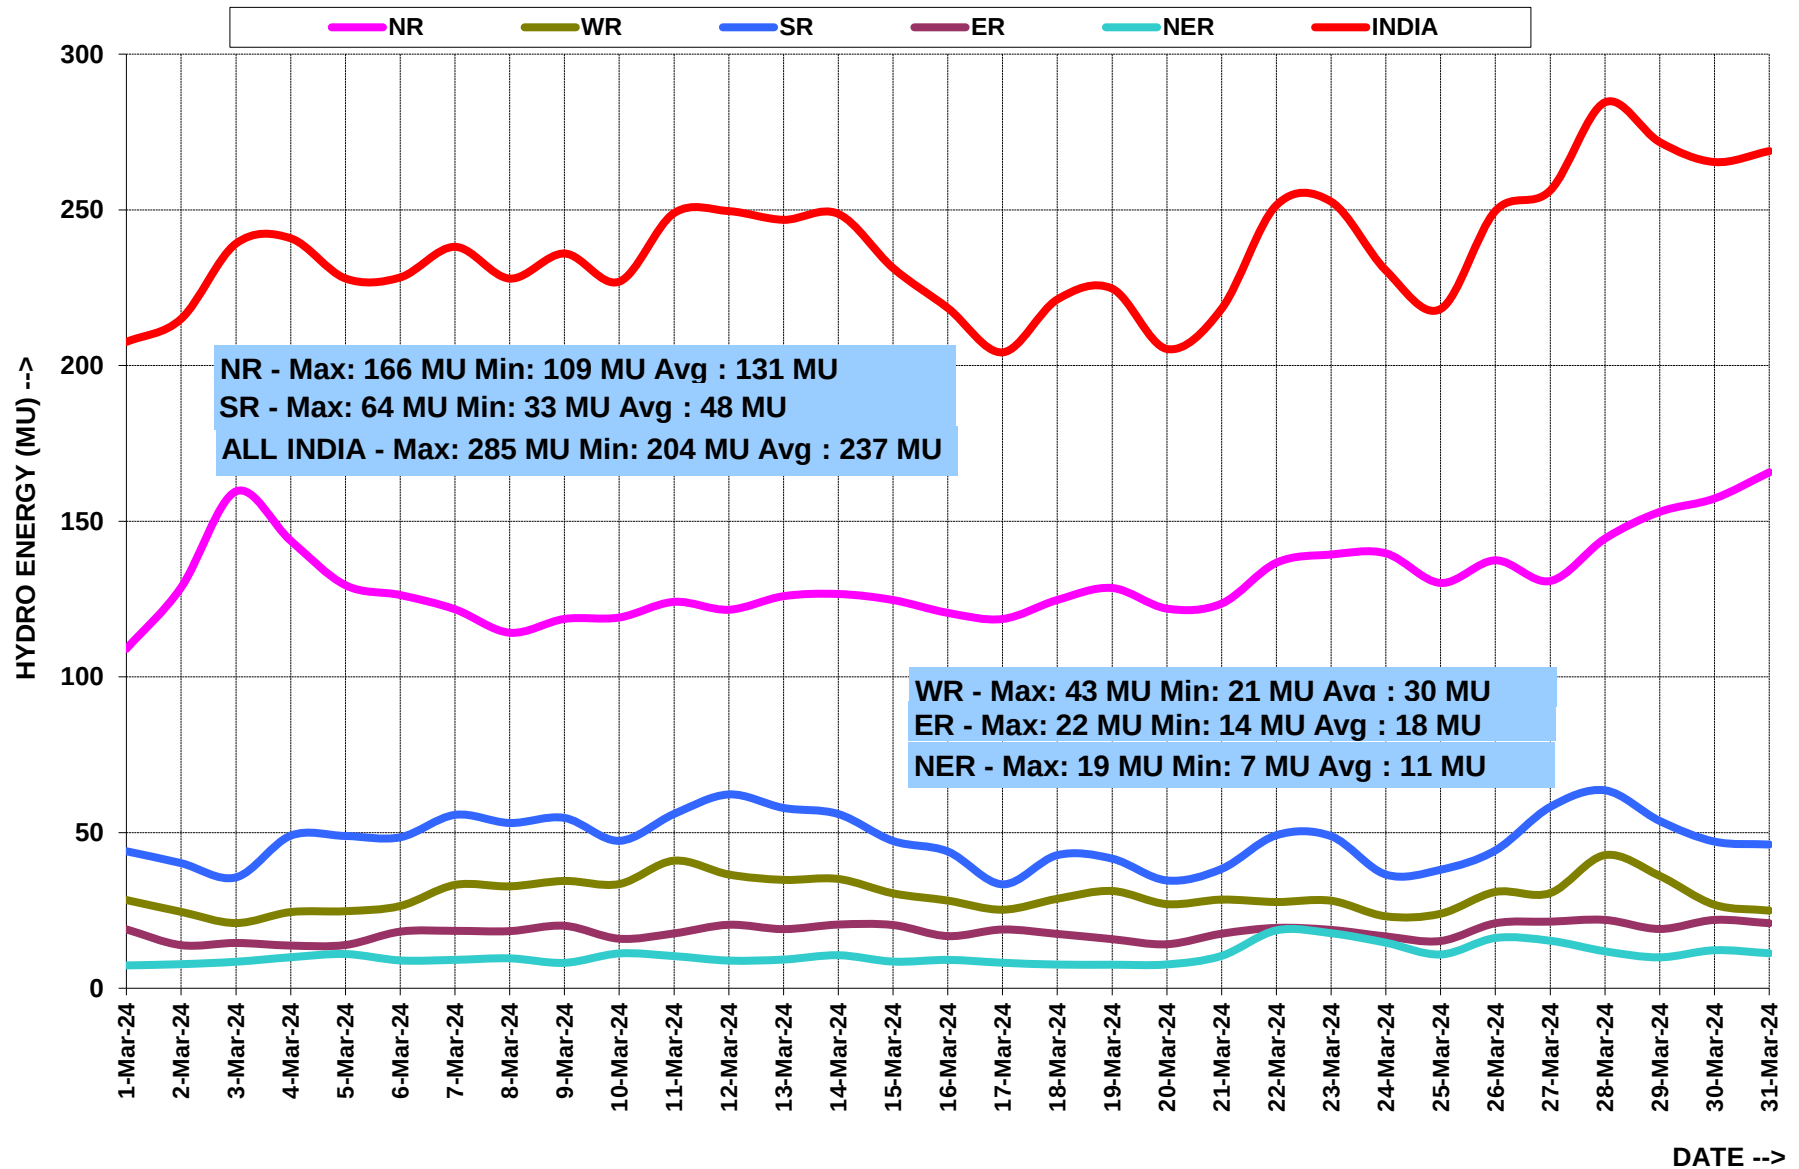

7. राष्ट्रीय स्तर पर पवन ऊर्जा उत्पादन
WIND GENERATION AT NATIONAL LEVEL

माह: मार्च 2024 MONTH:- MAR 2024

सभी आंकड़े मिलियन यूनिट में All figures in MU

दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Mar-24	33	92	77	-----	-----	201
02-Mar-24	51	151	54	-----	-----	256
03-Mar-24	12	110	30	-----	-----	153
04-Mar-24	16	66	29	-----	-----	111
05-Mar-24	33	106	31	-----	-----	171
06-Mar-24	13	81	32	-----	-----	127
07-Mar-24	15	68	29	-----	-----	113
08-Mar-24	19	75	27	-----	-----	121
09-Mar-24	24	96	31	-----	-----	151
10-Mar-24	16	74	43	-----	-----	134
11-Mar-24	10	68	43	-----	-----	121
12-Mar-24	12	84	35	-----	-----	131
13-Mar-24	21	98	38	-----	-----	157
14-Mar-24	10	69	34	-----	-----	113
15-Mar-24	24	75	38	-----	-----	138
16-Mar-24	20	86	35	-----	-----	140
17-Mar-24	29	89	41	-----	-----	159
18-Mar-24	11	80	38	-----	-----	129
19-Mar-24	18	70	39	-----	-----	128
20-Mar-24	24	75	45	-----	-----	144
21-Mar-24	16	81	73	-----	-----	171
22-Mar-24	16	91	39	-----	-----	146
23-Mar-24	14	94	37	-----	-----	144
24-Mar-24	16	92	44	-----	-----	153
25-Mar-24	6	63	47	-----	-----	116
26-Mar-24	9	70	45	-----	-----	124
27-Mar-24	27	80	45	-----	-----	151
28-Mar-24	21	85	35	-----	-----	142
29-Mar-24	25	92	36	-----	-----	152
30-Mar-24	39	95	38	-----	-----	172
31-Mar-24	19	74	31	-----	-----	124
कुल TOTAL	623	2630	1238	-----	-----	4491
उच्चतम MAXIMUM	51	151	77	-----	-----	256
निम्नतम MINIMUM	6	63	27	-----	-----	111
औसत AVERAGE	20	85	40	-----	-----	145
संचयी 2023-24 Cumulative 2023-24	8363	37011	34824	-----	-----	80198
अब तक का उच्चतम All Time Max.	86	273	298	-----	-----	611
दिनांक Date	07.08.23	07.08.23	21.07.23	-----	-----	02.08.23

*Source: As reported by SLDCs. Limited visibility of embedded wind generator data.

8. राष्ट्रीय स्तर पर सौर ऊर्जा उत्पादन
SOLAR GENERATION AT NATIONAL LEVEL

माह: मार्च 2024 MONTH:- MAR 2024

सभी आंकड़े मिलियन यूनिट में All figures in MU

दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL
01-Mar-24	93	74	134	6.1	1.1	307
02-Mar-24	120	59	142	3.0	1.2	326
03-Mar-24	161	83	137	2.5	1.0	385
04-Mar-24	164	86	136	3.1	0.5	389
05-Mar-24	149	89	141	3.4	1.2	383
06-Mar-24	139	86	131	2.9	1.3	359
07-Mar-24	161	87	135	3.0	1.3	387
08-Mar-24	166	88	137	5.1	1.2	398
09-Mar-24	163	88	130	5.7	1.2	388
10-Mar-24	135	84	124	6.0	1.2	350
11-Mar-24	159	85	125	6.5	1.2	377
12-Mar-24	161	85	131	3.5	1.0	381
13-Mar-24	147	87	132	3.3	1.2	370
14-Mar-24	162	87	133	2.9	1.0	385
15-Mar-24	162	84	129	3.0	1.2	379
16-Mar-24	167	80	127	2.9	1.2	377
17-Mar-24	154	80	133	2.2	1.1	370
18-Mar-24	165	80	132	2.0	1.0	380
19-Mar-24	161	83	129	3.2	0.9	377
20-Mar-24	163	84	137	1.9	0.4	387
21-Mar-24	151	79	123	2.8	0.3	356
22-Mar-24	160	87	130	3.9	1.0	382
23-Mar-24	148	86	134	3.0	0.9	373
24-Mar-24	140	83	132	3.4	0.9	360
25-Mar-24	143	85	133	3.2	1.2	366
26-Mar-24	143	83	135	3.3	0.7	366
27-Mar-24	148	84	137	3.3	0.7	373
28-Mar-24	149	82	133	2.8	1.1	369
29-Mar-24	153	77	135	2.9	1.2	369
30-Mar-24	162	83	140	2.5	0.9	388
31-Mar-24	158	80	149	2.5	0.4	390
कुल TOTAL	4709	2567	4136	106	30	11547
उच्चतम MAXIMUM	167	89	149	7	1	398
निम्नतम MINIMUM	93	59	123	2	0	307
औसत AVERAGE	152	83	133	3	1	372
संचयी 2023-24 Cumulative 2023-24	44679	21261	41308	1218	352.5	108716
अब तक का उच्चतम All Time Max.	167	89	149	6.7	2.4	398
दिनांक Date	16.03.24	05.03.24	31.03.24	23.03.23	22.06.22	08.03.24

*Source: RLDCs for solar connected to ISTS; SLDCs for embedded solar. Limited visibility of embedded solar data.

9. राष्ट्रीय स्तर पर दैनिक अधिकतम विद्युत मांग पूर्ति
DAILY MAXIMUM DEMAND MET AT NATIONAL LEVEL

माह: मार्च 2024 MONTH:- MAR 2024

सभी आंकड़े मेगावाट में All figures in MW


दिनांक Date	उत्तरी क्षे. NR	पश्चिमी क्षे. WR	दक्षिणी क्षे. SR	पूर्वी क्षे. ER	पूर्वोत्तर क्षे. NER	कुल TOTAL	विभिन्नता फैक्टर Diversity Factor*
01-Mar-24	60366	70750	66439	22539	2743	219075	1.017
02-Mar-24	50376	67447	65164	22928	2797	203128	1.027
03-Mar-24	49395	61979	62119	21622	2566	193298	1.023
04-Mar-24	54491	65877	65958	22462	2760	206560	1.024
05-Mar-24	56675	67235	66832	22755	2709	211528	1.022
06-Mar-24	56946	67412	66821	23031	2770	213020	1.019
07-Mar-24	57479	68110	67290	23215	2713	214946	1.018
08-Mar-24	59333	68648	68084	22395	2715	219016	1.010
09-Mar-24	57574	67706	65151	23311	2774	212226	1.020
10-Mar-24	55048	67230	61556	22889	2608	206220	1.015
11-Mar-24	57825	70440	67079	23837	2793	217995	1.018
12-Mar-24	57998	70488	67328	24149	2744	218897	1.017
13-Mar-24	58132	70363	68735	24219	2790	220555	1.017
14-Mar-24	57318	70030	68096	24542	2684	217550	1.024
15-Mar-24	59608	69916	68009	24816	2850	221701	1.016
16-Mar-24	58487	69789	66152	23404	2851	217346	1.015
17-Mar-24	56863	66416	60604	23304	2784	205066	1.024
18-Mar-24	60011	69627	65884	24145	2962	218272	1.020
19-Mar-24	59975	68444	65287	23616	2954	215800	1.021
20-Mar-24	59778	67168	64531	19946	2607	212150	1.009
21-Mar-24	55454	69204	64211	21936	2621	208363	1.024
22-Mar-24	57096	70021	65985	23110	2673	214313	1.021
23-Mar-24	56363	69336	64669	23981	2708	211750	1.025
24-Mar-24	52989	66455	60638	22787	2536	199723	1.028
25-Mar-24	44156	58225	62820	20592	2511	182600	1.031
26-Mar-24	50626	67302	65485	22824	2534	202753	1.030
27-Mar-24	54048	70339	65227	24936	2723	211199	1.029
28-Mar-24	55896	71401	66241	25556	2801	215341	1.030
29-Mar-24	56179	71739	66641	26192	2902	219734	1.018
30-Mar-24	56657	69629	65669	27094	2925	213485	1.040
31-Mar-24	53463	65639	60559	25924	2042	201533	1.030
उच्चतम MAXIMUM	60366	71739	68735	27094	2962	221701	1.040
निम्नतम MINIMUM	44156	58225	60559	19946	2042	182600	1.009
औसत AVERAGE	56020	68205	65331	23486	2715	211134	1.022
अब तक का उच्चतम All Time Max.	81220	74799	68735	29641	3712	239978	
दिनांक Date	04.09.23	29.01.24	13.03.24	28.07.23	04.09.23	01.09.23	

* Diversity factor = (Sum of regional max demands) / All India max demand


नोट : यह आंकड़े एनएलडीसी स्काडा प्रणाली में दर्ज दैनिक अधिकतम मांगपूर्ति दर्शाते हैं ।

Note: The above figures denote daily maximum demand met recorded in NLDC SCADA.


10. DEMAND AND GENERATION PLOTS FOR 15 MARCH (MAXIMUM DEMAND MET)

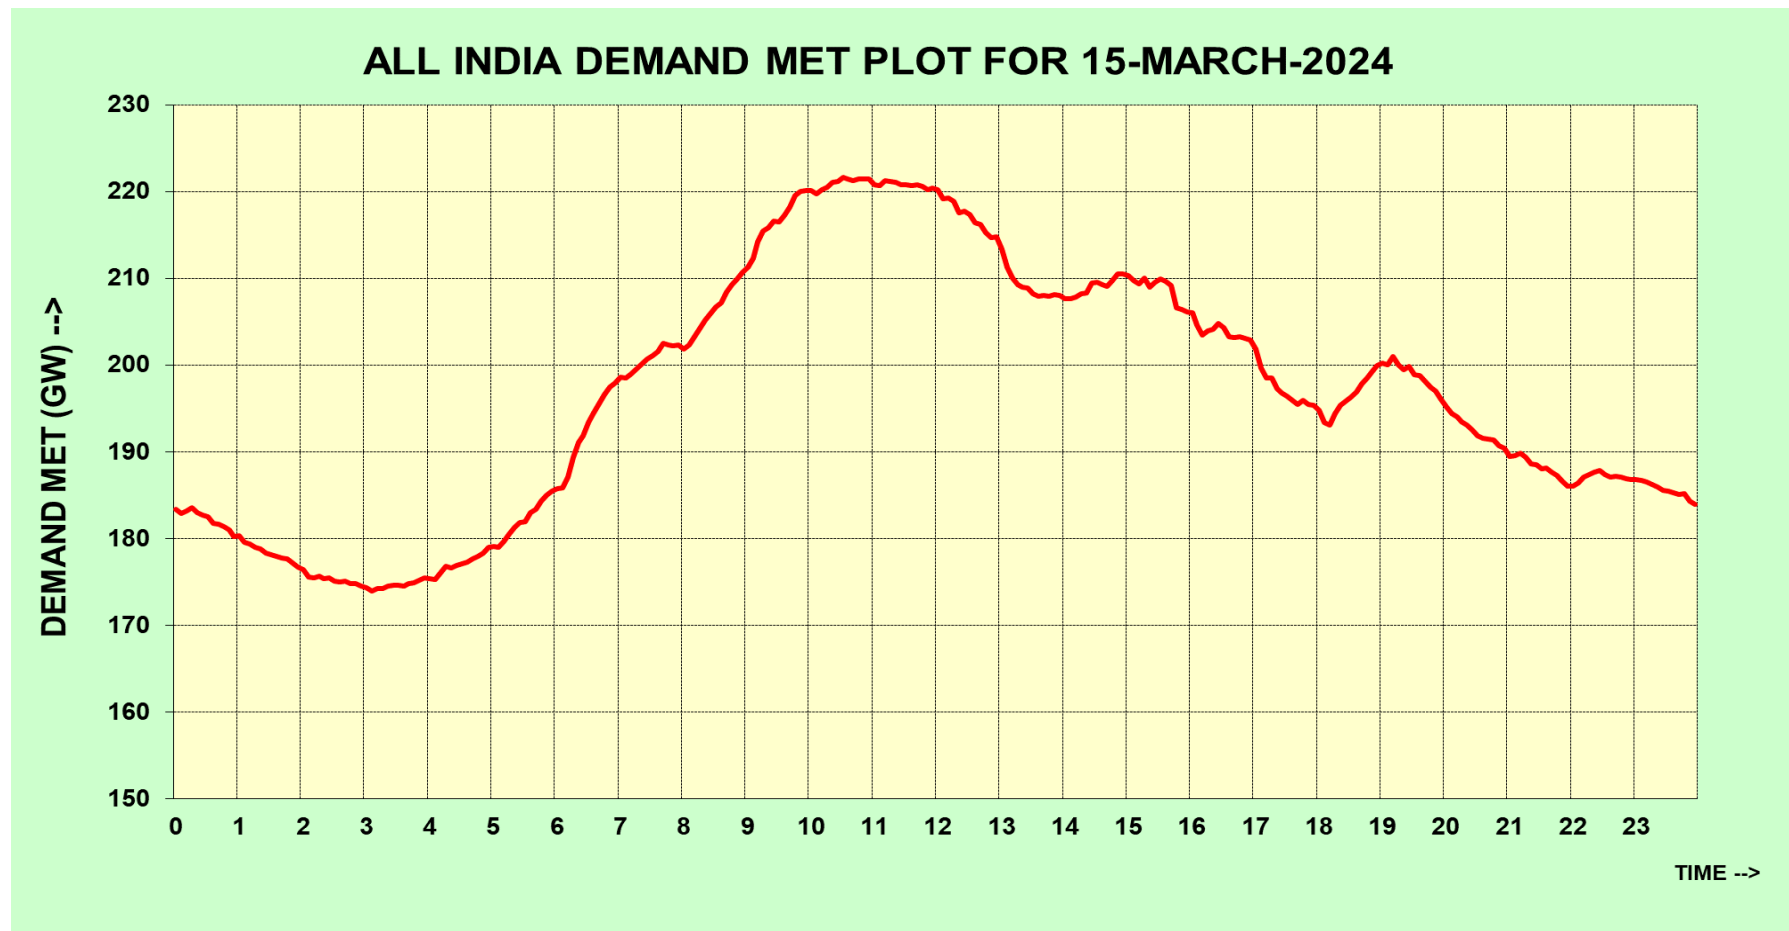


REGIONAL DEMAND MET PLOT FOR 15-MARCH-2024

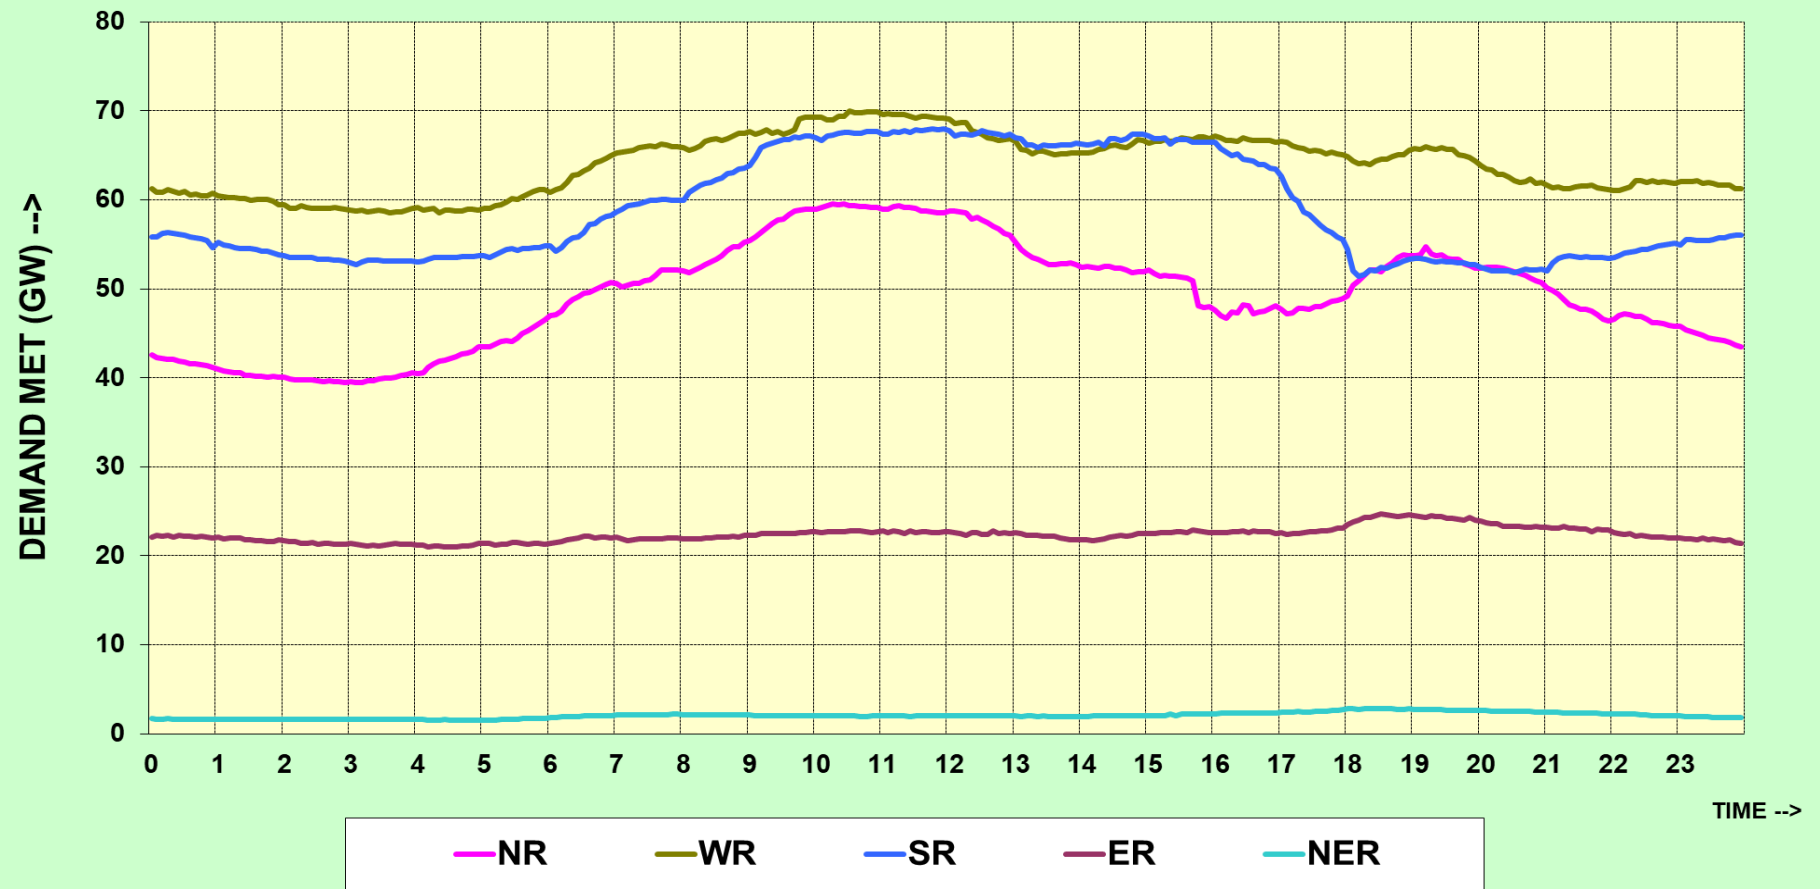

ALL INDIA GENERATION PLOT FOR 15-MARCH-2024

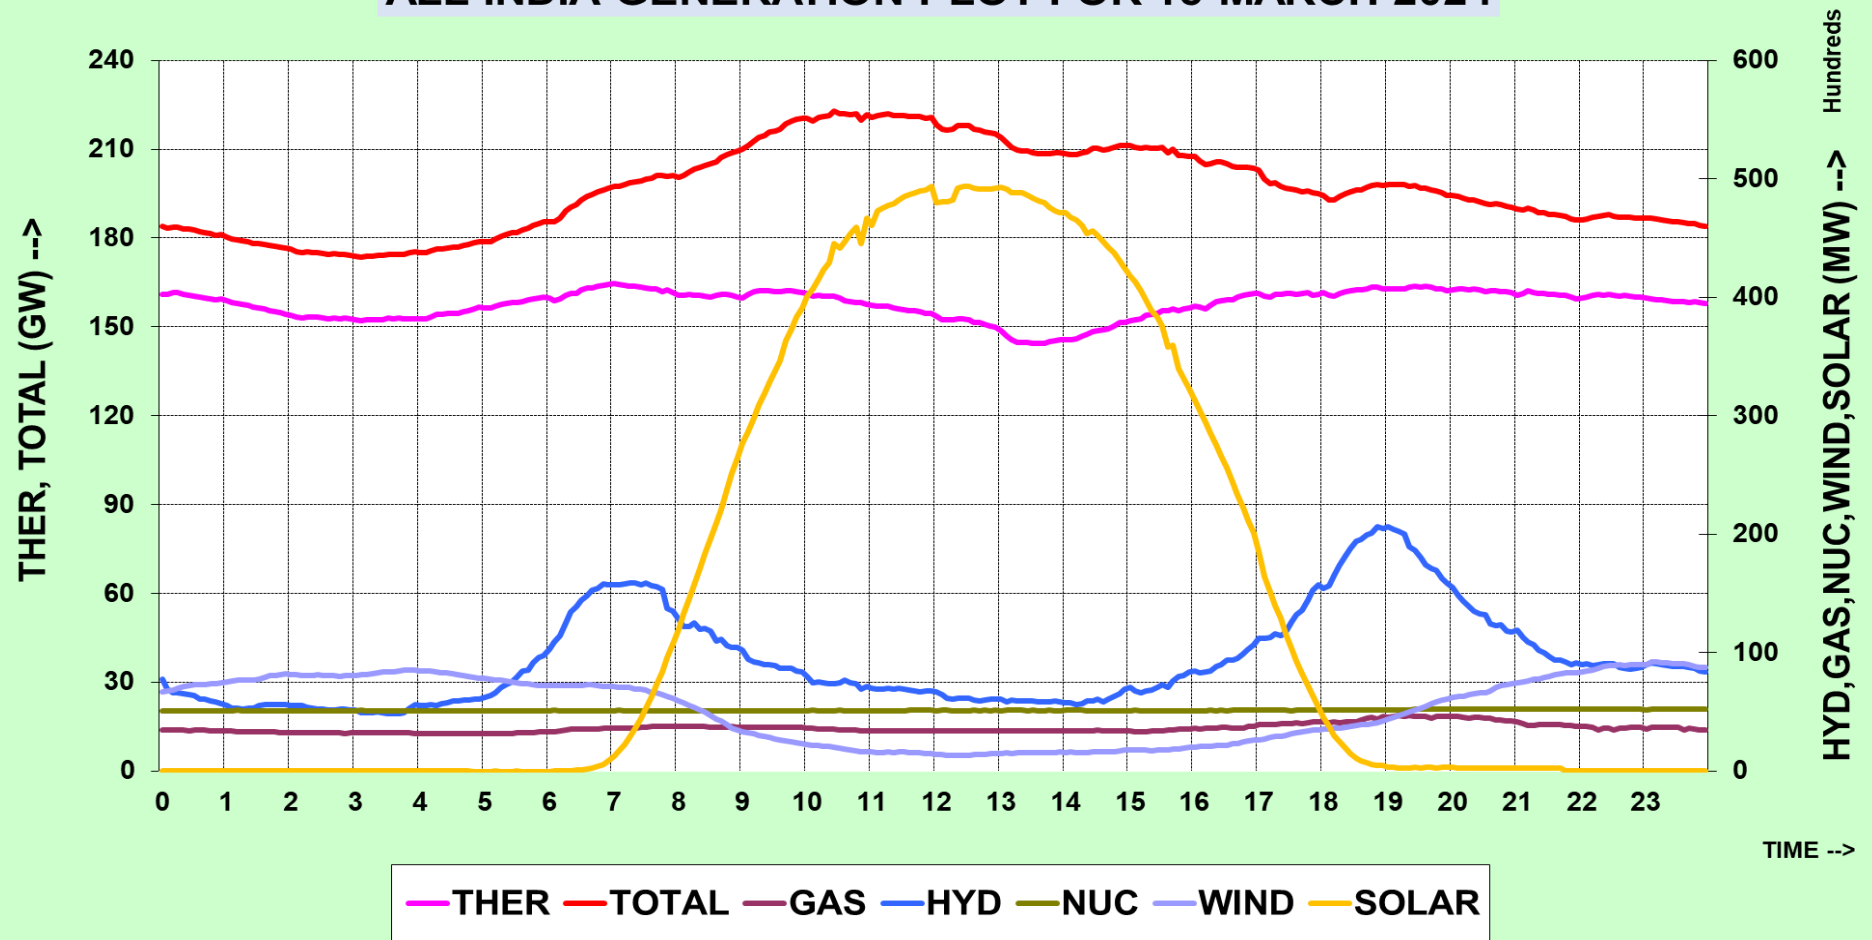

All India Fuel-wise Generation Patterns for 15-MARCH-2024

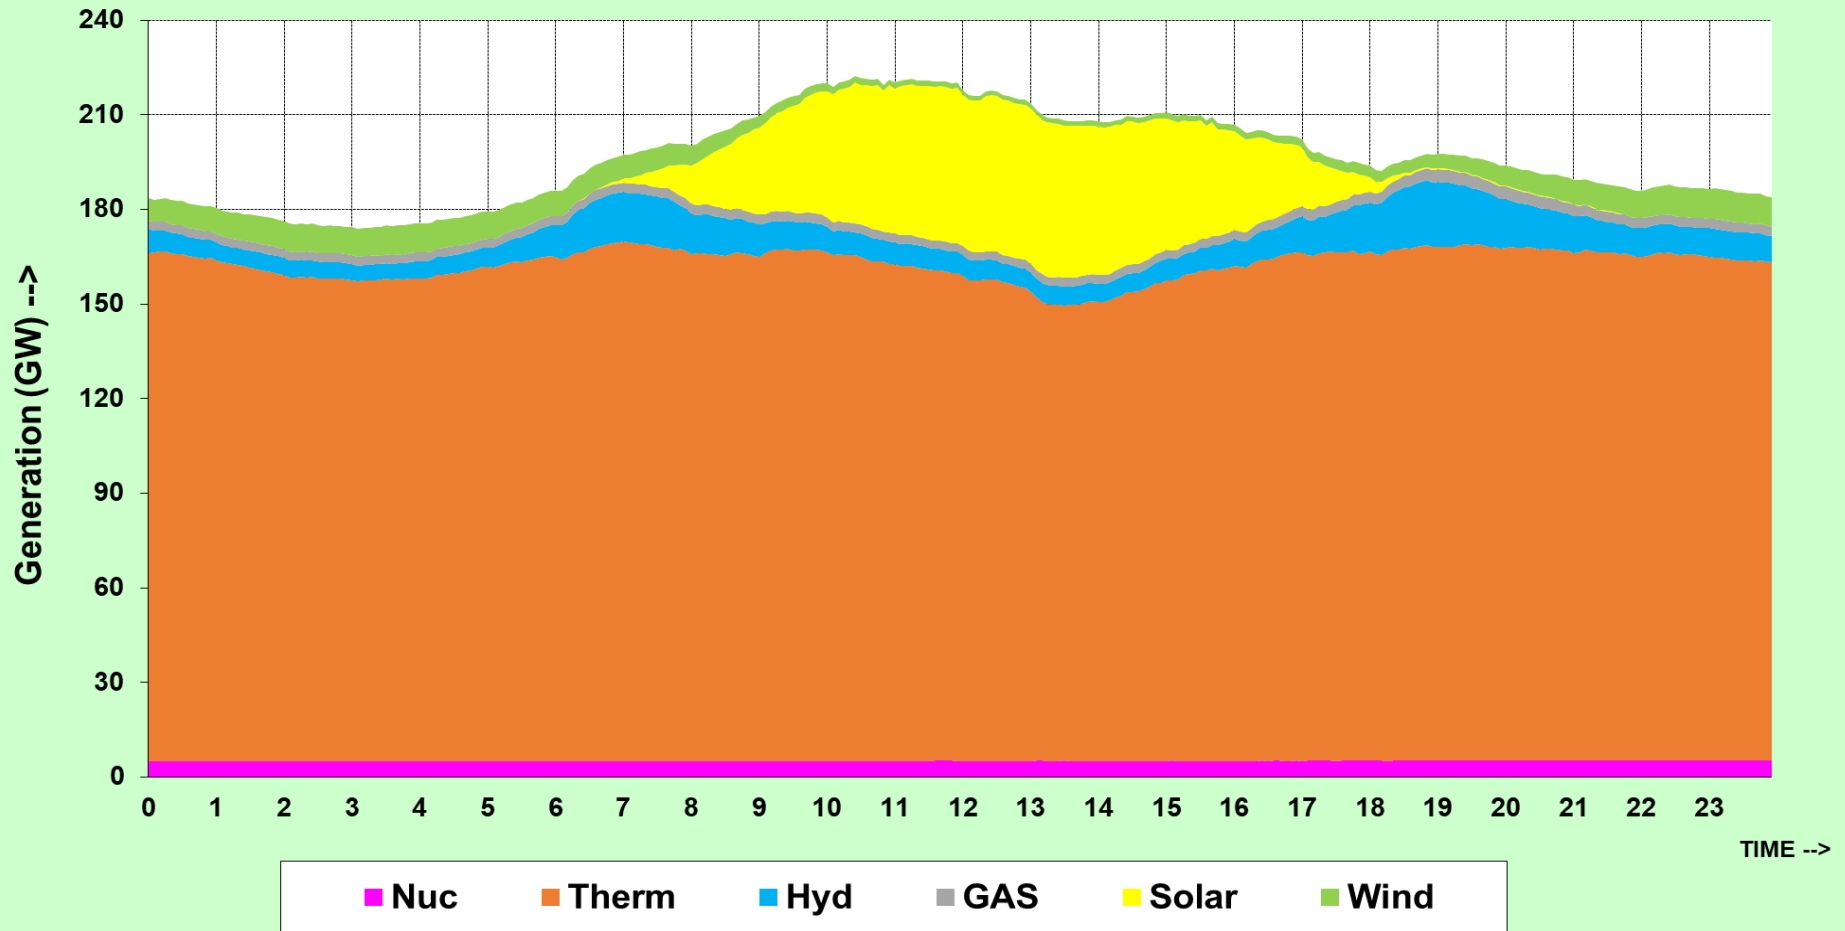

15 मार्च 2024 (अधिकतम माँग) की आल इंडिया माँग आपूर्ति
ALL INDIA DEMAND MET FOR 15 MARCH 2024 (MAXIMUM DEMAND*)

Time (hrs)	All India Demand (MW)		Time (hrs)	All India Demand (MW)
00:05	182952		12:05	219165
00:20	183062		12:20	217602
00:35	181761		12:35	216453
00:50	181029		12:50	214684
01:05	179621		13:05	211289
01:20	178798		13:20	208982
01:35	177984		13:35	207995
01:50	177238		13:50	208154
02:05	175552		14:05	207708
02:20	175389		14:20	208297
02:35	174993		14:35	209269
02:50	174813		14:50	210567
03:05	173928		15:05	209720
03:20	174533		15:20	209045
03:35	174577		15:35	209658
03:50	175240		15:50	206424
04:05	175276		16:05	204651
04:20	176624		16:20	204152
04:35	177293		16:35	203302
04:50	178388		16:50	203080
05:05	179005		17:05	199696
05:20	181261		17:20	197287
05:35	183001		17:35	195919
05:50	185019		17:50	195487
06:05	185886		18:05	193418
06:20	191080		18:20	195360
06:35	194559		18:35	196868
06:50	197473		18:50	199230
07:05	198516		19:05	200007
07:20	200142		19:20	199528
07:35	201544		19:35	198787
07:50	202271		19:50	197043
08:05	202294		20:05	194396
08:20	205237		20:20	193103
08:35	207166		20:35	191594
08:50	209974		20:50	190679
09:05	212319		21:05	189581
09:20	215869		21:20	188660
09:35	217293		21:35	188156
09:50	220038		21:50	186622
10:05	219756		22:05	186466
10:20	221106		22:20	187699
10:35	221464		22:35	187152
10:50	221460		22:50	186944
11:05	220687		23:05	186754
11:20	221080		23:20	185946
11:35	220670		23:35	185264
11:50	220233		23:50	184334
Maximum Demand of 221701 MW met@10:43 hrs (from 1 min. interval SCADA DATA)				

* 15 minute interval SCADA DATA of instantaneous demand

11. ACTUAL POWER SUPPLY POSITION - MARCH 2024

REGION	STATE	Requirement/Availability in MU/DAY			Requirement/Availability in MU				Peak Demand/Peak Met in MW			
		Requirement	Energy met	Surplus(+)/Deficit(-)	Requirement	Energy met	Surplus(+)/Deficit(-)	% Shortage	Requirement	Peak Demand Met	Surplus(+)/Deficit(-)	% Shortage
NR	Chandigarh	4	4	0.0	109	109	0	0.0	237	237	0	0.0
	Delhi	71	71	0.0	2204	2204	0	0.0	4482	4482	0	0.0
	Haryana	138	138	0.0	4289	4289	0	0.0	7747	7747	0	0.0
	Himachal Pradesh	31	31	-0.1	953	949	-3	-0.3	1982	1982	0	0.0
	J&K(UT) and Ladakh(UT)	55	55	-0.2	1714	1707	-6	-0.4	2896	2896	0	0.0
	Punjab	152	152	0.0	4698	4698	0	0.0	10214	10214	0	0.0
	Rajasthan	288	288	0.0	8937	8937	0	0.0	17030	17030	0	0.0
	Uttar Pradesh	337	337	0.0	10440	10439	-1	0.0	21243	21243	0	0.0
	Uttarakhand	39	39	0.0	1220	1219	-1	-0.1	2260	2260	0	0.0
	Railway	4	4	0.0	117	117	0	0.0	213	213	0	0.0
	NFL	0	0	0.0	2	2	0	0.0	5	5	0	0.0
	TOTAL	1119	1118	-0.4	34683	34672	-12	0.0	60002	60002	0	0.0
WR	Gujarat	418	418	0.0	12947	12947	0	0.0	21843	21843	0	0.0
	Madhya Pradesh	252	252	0.0	7813	7813	0	0.0	13594	13594	0	0.0
	Chhattisgarh	127	127	0.0	3948	3948	0	0.0	6148	6148	0	0.0
	Maharashtra	606	606	0.0	18796	18795	0	0.0	28795	28735	-60	-0.2
	Goa	14	14	0.0	448	448	0	0.0	767	767	0	0.0
	DNHDDPDCL	28	28	0.0	866	866	0	0.0	1283	1283	0	0.0
	AMNSIL	19	19	0.0	595	595	0	0.0	928	928	0	0.0
	BALCO	12	12	0.0	387	387	0	0.0	527	527	0	0.0
	TOTAL	1477	1477	0.0	45799	45799	0	0.0	70528	70528	0	0.0
SR	Andhra Pradesh	215	215	-0.7	6679	6658	-22	-0.3	12216	12216	0	0.0
	Telangana	258	257	-0.8	7993	7968	-25	-0.3	13828.825	13810	-19	-0.1
	Karnataka	285	285	-0.8	8848	8823	-25	-0.3	17220	17220	0	0.0
	Kerala	84	83	-0.3	2595	2587	-8	-0.3	5302	5301	-1	0.0
	Tamil Nadu	337	336	-1.1	10452	10419	-33	-0.3	17044.81	17035	-10	-0.1
	Puducherry	9	9	0.0	270	269	-1	-0.3	453	453	0	0.0
	TOTAL	1188	1185	-3.7	36837	36723	-114	-0.3	68094	68094	0	0.0
ER	Bihar	93	93	-0.1	2883	2879	-4	-0.1	5758	5758	0	0.0
	Jharkhand	37	36	-0.8	1146	1120	-25	-2.2	1870	1870	0	0.0
	DVC	71	71	0.0	2190	2190	0	0.0	3403	3403	0	0.0
	Odisha	122	122	0.0	3794	3794	0	0.0	6133	6133	0	0.0
	West Bengal	170	170	0.0	5256	5256	0	0.0	10188	10188	0	0.0
	Sikkim	2	2	0.0	54	54	0	0.0	118	118	0	0.0
	Railways_ER ISTS	0	0	0.0	4	4	0	0.0	17	17	0	0.0
	TOTAL	494	493	-0.9	15327	15297	-29	-0.2	27079	27079	0	0.0
NER	Arunachal Pradesh	3	3	0.0	89	89	0	0.0	177	177	0	0.0
	Assam	28	28	0.0	882	882	0	0.0	1814	1782	-32	-1.8
	Manipur	3	3	0.0	91	91	0	0.0	226	226	0	0.0
	Meghalaya	6	6	0.0	181	181	0	0.0	398	398	0	0.0
	Mizoram	2	2	0.0	60	60	0	0.0	136	136	0	0.0
	Nagaland	2	2	0.0	69	69	0	0.0	158	157	-1	-0.6
	Tripura	4	4	0.0	124	124	0	0.0	288	288	0	0.0
	TOTAL	48	48	0.0	1496	1496	0	0.0	2985	2985	0	0.0
ALL INDIA		4327	4322	-5.0	134143	133988	-155	-0.1				

NOTE: BASED ON THE DATA FURNISHED BY ENTITIES ON DAILY BASIS

12. ENERGY COMPARISON OF MARCH 2024 vs MARCH 2023

REGION	STATE	Energy Requirement (MU)					Energy Met (MU)				
		Mar-23	Mar-24	Difference	% Change	Average MU/day for Mar-24	Mar-23	Mar-24	Difference	% Change	Average MU/day for Mar-24
NR	Chandigarh	102	109	7	7	4	102	109	7	7	4
	Delhi	2126	2204	78	4	71	2126	2204	78	4	71
	Haryana	3951	4289	338	9	138	3949	4289	340	9	138
	Himachal Pradesh	996	953	-43	-4	31	994	949	-44	-4	31
	J&K(UT) and Ladakh(UT)	1726	1714	-12	-1	55	1718	1707	-11	-1	55
	Punjab	4283	4698	416	10	152	4266	4698	432	10	152
	Rajasthan	7532	8937	1405	19	288	7515	8937	1422	19	288
	Uttar Pradesh	9686	10440	755	8	337	9680	10439	759	8	337
	Uttarakhand	1176	1220	44	4	39	1163	1219	57	5	39
	Railway/NFL	119	119	0	0	4	119	119	0	0	4
	TOTAL	31697	34683	2987	9	1119	31631	34672	3041	10	1118
WR	Gujarat	12140	12947	807	7	418	12140	12947	807	7	418
	Madhya Pradesh	7282	7813	531	7	252	7255	7813	558	8	252
	Chhattisgarh	3461	3948	487	14	127	3458	3948	490	14	127
	Maharashtra	17129	18796	1667	10	606	17128	18795	1667	10	606
	Goa	416	448	32	8	14	415	448	33	8	14
	DNHDDPDCL	872	866	-6	-1	28	872	866	-6	-1	28
	AMNSIL	555	595	40	7	19	555	595	40	7	19
	BALCO	383	387	4	1	12	383	387	4	1	12
	TOTAL	42237	45799	3562	8	1477	42206	45799	3593	9	1477
SR	Andhra Pradesh	6725	6679	-46	-1	215	6725	6658	-67	-1	215
	Telangana	8573	7993	-580	-7	258	8581	7968	-613	-7	257
	Karnataka	8696	8848	152	2	285	8705	8823	118	1	285
	Kerala	2710	2595	-115	-4	84	2713	2587	-126	-5	83
	Tamil Nadu	10854	10452	-403	-4	337	10866	10419	-447	-4	336
	Puducherry	283	270	-13	-5	9	284	269	-14	-5	9
	TOTAL	37842	36837	-1005	-3	1188	37873	36723	-1150	-3	1185
ER	Bihar	2882	2883	1	0	93	2869	2879	10	0	93
	Jharkhand	971	1146	175	18	37	903	1120	217	24	36
	DVC	2283	2190	-93	-4	71	2283	2190	-93	-4	71
	Odisha	3392	3794	402	12	122	3392	3794	402	12	122
	West Bengal	4986	5256	270	5	170	4982	5256	275	6	170
	Sikkim	49	54	4	9	2	49	54	4	9	2
	Railways_ER ISTS		4	-	-	0		4	-	-	0
	TOTAL	14564	15327	763	5	494	14478	15297	820	6	493
NER	Arunachal Pradesh	86	89	3	4	3	86	89	3	4	3
	Assam	844	882	38	4	28	844	882	38	5	28
	Manipur	84	91	7	9	3	84	91	8	9	3
	Meghalaya	194	181	-13	-7	6	191	181	-9	-5	6
	Mizoram	54	60	6	12	2	54	60	6	12	2
	Nagaland	70	69	-2	-2	2	70	69	-2	-2	2
	Tripura	123	124	1	1	4	123	124	1	1	4
	TOTAL	1456	1496	40	3	48	1451	1496	45	3	48
ALL INDIA		127795	134143	6348	5	4327	127639	133988	6349	5	4322

13. DEMAND COMPARISON OF MARCH 2024 vs MARCH 2023

REGION	STATE	Peak Requirement (MW)				Peak Met (MW)			
		Mar-23	Mar-24	Difference	% Change	Mar-23	Mar-24	Difference	% Change
NR	Chandigarh	204	237	33	16.2	204	237	33	16.2
	Delhi	3979	4482	503	12.6	3979	4482	503	12.6
	Haryana	7732	7747	15	0.2	7732	7747	15	0.2
	Himachal Pradesh	1922	1982	60	3.1	1922	1982	60	3.1
	J&K(UT) and Ladakh(UT)	2859	2896	37	1.3	2859	2896	37	1.3
	Punjab	8840	10214	1374	15.5	8840	10214	1374	15.5
	Rajasthan	15637	17030	1393	8.9	15637	17030	1393	8.9
	Uttar Pradesh	19572	21243	1671	8.5	19572	21243	1671	8.5
	Uttarakhand	2185	2260	75	3.4	2185	2260	75	3.4
	Railway/NFL	178	218	40	22.3	178	218	40	22.3
WR	Gujarat	19464	21843	2379	12	19464	21843	2379	12.2
	Madhya Pradesh	14298	13594	-704	-5	14298	13594	-704	-4.9
	Chhattisgarh	5399	6148	749	14	5399	6148	749	13.9
	Maharashtra	28576	28795	219	1	28566	28735	169	0.6
	Goa	718	767	49	7	718	767	49	6.8
	DNHDDPDCL	1272	1283	11	0.9	1272	1283	11	0.9
	AMNSIL	901	928	27	3.0	901	928	27	3.0
	BALCO	521	527	5	1.0	521	527	5	1.0
SR	Andhra Pradesh	12181	12216	35	0.3	12181	12216	35	0.3
	Telangana	15515	13829	-1686	-10.9	15497	13810	-1687	-10.9
	Karnataka	15828	17220	1392	8.8	15828	17220	1392	8.8
	Kerala	4517	5302	785	17.4	4517	5301	784	17.4
	Tamil Nadu	18053	17045	-1008	-5.6	18048	17035	-1013	-5.6
	Puducherry	441	453	12	2.7	441	453	12	2.7
ER	Bihar	5378	5758	380	7.1	5378	5758	380	7.1
	Jharkhand	1537	1870	333	21.6	1537	1870	333	21.6
	DVC	3610	3403	-207	-5.7	3610	3403	-207	-5.7
	Odisha	5759	6133	374	6.5	5759	6133	374	6.5
	West Bengal	8784	10188	1404	16.0	8776	10188	1412	16.1
	Sikkim	115	118	3	2.6	115	118	3	2.6
	Railways_ER ISTS*		17	17	-		17	17	-
NER	Arunachal Pradesh	172	177	5	2.9	172	177	5	2.9
	Assam	1670	1814	144	8.6	1670	1782	112	6.7
	Manipur	212	226	14	6.4	212	226	14	6.4
	Meghalaya	374	398	24	6.4	374	398	24	6.4
	Mizoram	129	136	7	5.6	129	136	7	5.6
	Nagaland	156	158	2	1.0	156	157	1	0.4
	Tripura	264	288	24	9.1	264	288	24	9.1

14. SCHEDULE AND DRAWAL OF CONSTITUENTS - MARCH 2024

REGION	STATE	SCHEDULE (MU)	ACTUAL DRAWAL (MU)	Over drawal(+)/ Under Drawal(-) (MU)	% OD/UD	SCHEDULE (MU/DAY)	ACTUAL DRAWAL (MU/DAY)	Over drawal(+)/ Under Drawal(-) (MU/DAY)
NR	Chandigarh	111.90	111.54	-0.36	-0.32	3.61	3.60	-0.01
	Delhi	1941.49	1950.36	8.87	0.46	62.63	62.91	0.29
	Haryana	3127.54	3120.29	-7.25	-0.23	100.89	100.65	-0.23
	Himachal Pradesh	706.62	692.84	-13.78	-1.95	22.79	22.35	-0.44
	J&K(UT) and Ladakh(UT)	1475.05	1453.98	-21.07	-1.43	47.58	46.90	-0.68
	Punjab	1840.79	1801.12	-39.67	-2.15	59.38	58.10	-1.28
	Rajasthan	2313.05	2272.56	-40.49	-1.75	74.61	73.31	-1.31
	Uttar Pradesh	2803.84	2782.61	-21.23	-0.76	90.45	89.76	-0.68
	Uttarakhand	784.35	788.15	3.80	0.48	25.30	25.42	0.12
	Railway	114.19	117.29	3.10	2.71	3.68	3.78	0.10
	NFL	2.27	2.18	-0.09	-3.88	0.07	0.07	0.00
	Total	15221.09	15092.92	-128.17	-0.84	491.00	486.87	-4.13
WR	Gujarat	5535.71	5477.12	-58.59	-1.06	178.57	176.68	-1.89
	Madhya Pradesh	4353.16	4202.13	-151.03	-3.47	140.42	135.55	-4.87
	Chhattisgarh	2046.95	2037.73	-9.22	-0.45	66.03	65.73	-0.30
	Maharashtra	6320.96	6219.91	-101.05	-1.60	203.90	200.64	-3.26
	Goa	447.98	449.45	1.48	0.33	14.45	14.50	0.05
	DNHDDPDCL	867.29	865.99	-1.30	-0.15	27.98	27.94	-0.04
	AMNSIL	274.84	279.09	4.25	1.55	8.87	9.00	0.14
	BALCO*	388.49	386.65	-1.84	-0.47	12.53	12.47	-0.06
	Total	20235.38	19918.08	-317.30	-1.57	652.75	642.52	-10.24
SR	Andhra Pradesh	2666.09	2629.71	-36.38	-1.36	86.00	84.83	-1.17
	Telangana	5234.73	5228.99	-5.74	-0.11	168.86	168.68	-0.19
	Karnataka	4957.22	4911.01	-46.21	-0.93	159.91	158.42	-1.49
	Kerala	2461.99	2502.34	40.35	1.64	79.42	80.72	1.30
	Tamil Nadu	7350.94	7330.12	-20.82	-0.28	237.13	236.46	-0.67
	Puducherry	291.79	282.35	-9.44	-3.24	9.41	9.11	-0.30
	Goa (SR)	71.40	69.44	-1.96	-2.75	2.30	2.24	-0.06
	Total	23034.16	22953.96	-80.20	-0.35	743.04	740.45	-2.59
ER	Bihar	2587.34	2593.85	6.51	0.25	83.46	83.67	0.21
	Jharkhand	743.83	744.49	0.66	0.09	23.99	24.02	0.02
	DVC	-1246.01	-1237.97	8.05	-0.65	-40.19	-39.93	0.26
	Odisha	1553.84	1527.60	-26.24	-1.69	50.12	49.28	-0.85
	West Bengal	935.72	893.32	-42.39	-4.53	30.18	28.82	-1.37
	Sikkim	52.81	53.88	1.07	2.02	1.70	1.74	0.03
	Railways_ER ISTS*	4.13	4.08	-0.05	-1.20	0.13	0.13	0.00
	Total	4631.65	4579.24	-52.40	-1.13	149.41	147.72	-1.69
NER	Arunachal Pradesh	91.77	85.85	-5.92	-6.45	2.96	2.77	-0.19
	Assam	703.66	713.10	9.44	1.34	22.70	23.00	0.30
	Manipur	96.74	91.34	-5.40	-5.58	3.12	2.95	-0.17
	Meghalaya	163.77	154.21	-9.56	-5.84	5.28	4.97	-0.31
	Mizoram	50.90	45.27	-5.63	-11.06	1.64	1.46	-0.18
	Nagaland	70.78	66.06	-4.72	-6.67	2.28	2.13	-0.15
	Tripura	127.43	123.48	-3.95	-3.10	4.11	3.98	-0.13
	Total	1305.05	1279.31	-25.74	-1.97	42.10	41.27	-0.83
All India Total		64427.32	63823.51	-603.81	-0.94	2078.30	2058.82	-19.48

15. INTER REGIONAL EXCHANGES 2023-24 (All figures in MU)													
	Apr'23	May'23	June'23	July'23	Aug'23	Sep'23	Oct'23	Nov'23	Dec'23	Jan'24	Feb'24	Mar'24	Fin. Year 2023-24
Name of Line													
Import of NR from WR (WR-NR)													
WR - NR 765 kV Gwalior - Agra 2x5/C	635.95	996.71	863.68	972.77	772.12	902.82	479.75	675.87	1109.33	1292.73	685.48	313.31	9700.52
WR-NR 765 kV Gwalior - Phagi 2x5/C	553.05	453.93	342.56	671.61	397.70	687.31	582.69	906.94	1039.97	857.36	683.53	311.37	7488.02
WR-NR 765 kV Jabalpur-Orai D/C	430.29	804.53	778.33	964.77	658.94	991.15	602.03	622.44	986.15	1084.38	544.06	208.69	8675.76
WR-NR 765 kV Satna-Orai	505.37	598.85	574.83	615.77	543.29	593.66	548.69	623.24	692.79	691.06	560.49	552.46	7100.50
WR-NR 765 kV Gwalior-Orai	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
WR - NR HVDC Champa - Kurukshetra	804.26	1126.68	2069.11	2235.18	1955.13	2230.56	739.22	674.04	450.87	1556.24	1385.18	1281.19	16507.66
WR - NR HVDC Vindhyachal	0.49	3.23	3.13	94.78	21.55	7.26	50.51	28.33	18.10	26.05	0.00	0.00	253.43
WR - NR 400 kV Zerda Kankroli	0.00	0.00	1.48	15.36	13.10	8.58	0.00	1.30	3.11	9.71	1.89	0.00	54.53
WR - NR 400 kV Zerda Bhinnmal	0.00	0.00	0.00	12.54	13.56	23.81	0.34	3.28	11.42	20.30	0.35	0.01	85.61
WR - NR 400 kV RAPP C - Shujalpur D/C	2.28	31.04	16.05	164.49	80.51	147.53	18.12	25.82	78.97	145.10	15.75	0.00	725.66
WR - NR 220 kV Bhanpura - Ranpur	9.67	65.53	68.13	70.02	74.29	61.03	65.71	43.01	33.94	38.18	5.64	30.13	565.28
WR - NR 220 kV Bhanpura - Modak	0.00	0.00	0.00	0.00	0.00	38.00	62.92	72.56	72.98	34.77	11.48	57.84	350.55
WR - NR 220 kV Auraiya - Malanpur/Mehgaon	0.00	0.15	0.00	0.00	0.00	0.00	0.00	0.00	0.71	0.00	0.00	0.00	0.86
WR - NR 400 kV Vindhyachal-Rihand D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.47	0.00	0.00	0.47
WR - NR HVDC Mundra - Mohindergarh	132.55	340.75	234.27	124.89	667.23	827.57	920.93	511.53	563.55	931.29	547.02	624.02	6425.60
WR-NR 765 kV Banaskata-Chittorgarh D/C	0.00	3.26	16.02	169.31	260.02	66.60	0.00	4.54	27.97	46.56	22.32	0.00	616.60
WR-NR 765 kV Varanasi-Vindhyachal	1030.05	1663.34	1854.30	1854.38	1551.38	1697.01	1174.50	1049.13	1321.93	1485.20	629.64	780.64	16091.50
Total WR - NR	4103.96	6088.00	6821.89	7965.87	7008.82	8282.89	5245.41	5242.03	6411.79	8219.40	5092.83	4159.66	74642.55
Export of NR to WR (NR-WR)													
NR - WR 765 kV Gwalior - Agra 2x5/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	1.20	1.20
NR - WR 765 kV Gwalior - Phagi 2x5/C	0.00	5.41	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	5.41
NR - WR 765 kV Jabalpur-Orai D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	6.06	6.06
NR - WR 765 kV Satna-Orai	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
NR - WR 765 kV Gwalior-Orai	440.87	385.11	301.32	367.88	368.83	385.80	399.85	459.18	533.25	500.66	435.25	344.55	4922.55
NR - WR HVDC Champa- Kurukshetra	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
NR - WR HVDC Vindhyachal	289.83	273.88	267.04	184.43	225.73	180.86	26.34	219.10	161.65	131.32	230.46	274.31	2464.95
NR - WR 400 kV Zerda Kankroli	185.75	94.43	108.34	24.78	31.17	41.36	96.48	75.31	44.39	13.91	39.18	265.56	1020.66
NR - WR 400 kV Zerda Bhinnmal	282.42	181.64	200.56	73.76	74.62	64.65	158.50	60.27	38.76	19.27	89.32	44.64	1288.41
NR - WR 400 kV RAPP C - Shujalpur D/C	85.74	45.64	45.64	0.00	3.36	0.00	46.93	23.25	0.00	0.00	88.00	189.57	528.13
NR - WR 220 kV Bhanpura - Ranpur	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	27.59	8.15	35.74
NR - WR 220 kV Bhanpura - Modak	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	11.30	2.66	2.33	16.29
NR - WR 220 kV Auraiya - Malanpur/Mehgaon	56.56	28.58	50.82	47.16	97.78	68.03	111.08	74.65	30.32	32.76	65.50	73.62	736.86
NR-WR 400 kV Rihand-Vindhyachal D/C	644.30	672.49	642.32	664.33	653.25	658.85	669.33	655.41	657.92	560.83	319.58	650.01	7448.62
NR - WR HVDC Mundra - Mohindergarh	243.86	54.36	36.25	94.16	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	428.63
NR - WR 765 kV Banaskata-Chittorgarh D/C	976.83	428.19	421.52	94.53	51.63	180.84	597.81	524.56	292.98	164.35	222.27	638.07	4593.58
NR-WR 765 kV Varanasi-Vindhyachal	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Total NR - WR	3206.16	2169.73	2073.81	1551.03	1506.37	1580.39	2106.32	2091.73	1759.27	1434.40	1519.81	2498.07	23497.09

	Apr'23	May'23	June'23	July'23	Aug'23	Sep'23	Oct'23	Nov'23	Dec'23	Jan'24	Feb'24	Mar'24	Fin. Year 2023-24
Name of Line													
Import of NR from ER (ER-NR)													
ER - NR 765 kV Sasaram - Fatehpur	166.02	114.36	82.57	74.16	131.29	131.20	192.41	301.01	254.85	260.73	320.01	234.94	2263.55
ER - NR 765 kV Gaya - Varanasi 2*5/C	224.56	107.46	28.46	47.20	75.64	115.88	182.55	439.13	474.87	419.93	546.17	296.63	2958.48
ER - NR 765 kV Gaya - Ballia	246.38	335.46	321.28	300.74	224.31	332.43	250.12	325.32	373.66	432.02	272.37	201.39	3615.48
ER - NR HVDC Alipurduar - Agra	0.00	0.00	375.05	784.99	444.13	750.81	497.43	168.00	0.00	1.34	0.00	0.00	3021.75
ER-NR 400 kV Patna - Ballia D/C	219.16	246.32	242.35	242.23	300.66	262.01	203.70	186.43	90.17	338.23	443.37	338.56	3113.19
ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	127.03	223.63	277.35	376.44	415.21	330.20	255.04	312.10	270.56	284.40	179.74	88.67	3140.37
ER - NR 400 kV Biharshariff - Ballia D/C	22.11	72.32	102.97	92.77	101.30	90.47	56.79	138.97	145.18	163.30	59.71	13.10	1058.99
ER - NR 400 kV Motihari - Gorakhpur D/C	156.88	188.70	180.09	228.59	251.16	190.46	142.10	216.07	233.85	268.64	240.45	166.77	2463.76
ER - NR 400 kV Biharshariff - Varanasi D/C	67.56	47.21	34.66	24.65	44.14	47.88	63.00	164.47	171.28	183.46	181.32	74.87	1104.50
ER - NR 400 kV Sasaram -Varanasi	74.99	38.68	46.09	55.64	28.71	57.56	16.47	4.09	2.63	7.91	5.60	27.79	366.16
ER - NR 400 kV Sasaram -Allahabad	51.91	33.39	21.29	28.77	17.25	52.61	27.20	32.87	36.28	31.03	25.33	9.90	367.83
ER - NR 220 kV Sahupuri-Karamnasa	78.64	82.22	82.32	43.45	51.19	29.26	36.16	53.46	34.10	44.57	40.86	28.12	604.35
ER - NR 132 kV Sahupuri - Karamnasa	1.92	0.00	0.96	1.12	0.96	2.02	3.28	5.11	1.62	1.44	3.84	3.83	26.10
ER - NR 132 kV 132 kV Rihand - Nagar Untari	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	1.21	1.21
ER - NR 132 kV Rihand - Garhwa	0.46	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.18	0.00	0.00	0.05	0.69
ER-NR 400 kV Naubatpur - Ballia D/C	211.13	243.59	239.56	236.53	300.12	264.57	198.04	328.08	343.58	353.99	156.20	103.40	2978.79
Total ER-NR	1648.75	1733.34	2035.00	2537.28	2386.07	2657.36	2124.29	2675.11	2432.81	2790.99	2474.97	1589.23	27085.20
Import of NR from NER (NER-NR)													
NER-NR HVDC Biswanath Chariaili - Agra	0.00	0.00	153.62	339.28	465.76	447.38	470.05	190.40	0.00	0.00	0.00	4.48	2070.97
Total NER - NR	0.00	0.00	153.62	339.28	465.76	447.38	470.05	190.40	0.00	0.00	0.00	4.48	2070.97
Export of NR to ER (NR-ER)													
NR - ER 765 kV Sasaram - Fatehpur	0.00	2.65	7.74	3.45	0.00	4.62	0.00	0.00	0.00	0.00	0.00	0.00	18.46
NR - ER 765 kV Gaya - Varanasi 2*5/C	0.30	38.74	102.98	45.94	11.70	32.51	8.41	1.45	0.00	0.00	0.00	0.00	242.03
NR - ER 765 kV Gaya - Ballia	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
NR - ER HVDC Alipurduar - Agra	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
NR - ER 400 kV Patna - Ballia 2xD/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
NR - ER 400 kV Muzaffarpur - Gorakhpur D/C	3.47	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	1.47	4.94
NR - ER 400 kV Biharshariff - Ballia D/C	17.15	4.18	13.06	0.00	0.00	3.12	4.14	0.75	0.00	0.00	0.61	33.88	76.89
ER - NR 400 kV Motihari - Gorakhpur D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
NR - ER 400 kV Biharshariff - Varanasi D/C	2.90	7.31	20.53	10.39	0.22	12.39	4.69	0.00	0.00	0.00	0.00	1.96	60.39
NR - ER 400 kV Sasaram -Varanasi	0.00	0.00	0.00	0.00	1.67	0.00	0.85	5.47	4.05	3.29	2.61	0.28	18.22
NR - ER 400 kV Sasaram -Allahabad	2.25	0.00	0.00	0.82	2.28	0.00	0.23	0.00	0.00	0.24	0.72	1.41	7.95
NR - ER 220 kV Sahupuri-Karamnasa	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.48	0.48
NR - ER 132 kV Sahupuri - Karamnasa	0.01	0.96	0.48	0.96	0.00	0.58	0.48	0.00	1.44	0.96	1.44	0.48	7.79
NR - ER 132 kV 132 kV Rihand - Nagar Untari	1.74	2.20	1.08	3.37	2.39	3.46	1.80	2.75	0.00	1.23	0.20	0.00	20.22
ER - NR 132 kV Rihand - Garhwa	10.23	8.48	19.67	18.35	14.38	11.19	11.51	8.39	4.64	12.89	13.67	5.30	138.70
NR-ER 400 kV Ballia - Naubatpur D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Total NR - ER	38.05	64.52	165.54	83.28	32.64	67.87	32.11	18.81	10.13	18.61	19.25	45.26	596.07
Export of NR to NER (NER-NR)													
NR-NR HVDC Biswanath Chariaili - Agra	261.93	291.71	104.47	0.00	0.00	0.00	0.00	257.02	0.00	486.81	502.32	486.53	2390.79
Total NR - NER	261.93	291.71	104.47	0.00	0.00	0.00	0.00	257.02	0.00	486.81	502.32	486.53	2390.79

	Apr'23	May'23	June'23	July'23	Aug'23	Sep'23	Oct'23	Nov'23	Dec'23	Jan'24	Feb'24	Mar'24	Fin. Year 2023-24
Name of Line													
Export of WR to ER (WR-ER)													
WR - ER 765 kV Ranchi - Dharamjaygarh 2x5/C	139.81	504.96	673.15	734.00	331.39	537.29	228.34	42.77	55.89	144.01	12.73	10.41	3414.75
WR - ER 765 kV Dharamjaygarh - Jharsuguda 2xD/C	652.31	469.82	490.99	593.61	768.89	177.22	238.94	52.91	224.71	96.99	168.60	435.14	4370.13
WR - ER 765 kV Durg - Jharsuguda D/C	0.00	0.64	1.75	26.78	7.42	1.32	0.00	0.00	0.00	0.00	0.00	0.00	37.91
WR - ER 400 kV Sipat - Ranchi D/C	15.97	93.84	118.29	133.75	52.57	87.51	30.29	8.20	13.05	16.97	0.75	0.37	571.57
WR - ER 400 kV Raigarh - Jharsuguda 2xD/C	0.44	6.23	8.79	6.26	28.69	11.41	0.82	0.78	0.99	0.01	0.00	0.59	65.02
WR - ER 220 kV Korba - Budhipadar D/C	36.08	80.04	73.19	22.96	28.75	29.18	26.25	36.70	47.92	14.51	10.54	37.13	443.25
WR - ER 220 kV Raigarh - Budhipadar	0.15	0.57	1.17	0.00	0.35	0.34	0.00	0.08	2.74	0.06	0.00	0.47	5.93
Total WR - ER	844.75	1156.11	1367.33	1517.34	1218.07	844.29	524.64	141.44	345.30	272.55	192.63	484.12	8908.56
Import of WR from ER (ER - WR)													
ER - WR 765 kV Ranchi - Dharamjaygarh 2x5/C	144.10	11.95	15.57	10.81	83.69	14.84	62.72	294.10	166.96	114.80	421.37	519.88	1860.80
ER - WR 765 kV Dharamjaygarh - Jharsuguda 2XD/C	25.46	58.29	33.08	15.65	2.33	214.83	131.20	338.83	241.82	386.37	174.98	18.33	1641.17
ER - WR 765 kV Durg - Jharsuguda D/C	394.08	204.42	148.02	71.84	73.64	163.98	298.15	464.99	456.27	465.79	397.81	501.18	3640.17
ER - WR 400 kV Sipat - Ranchi D/C	55.56	5.71	9.07	7.22	29.65	8.91	40.59	105.31	60.55	61.48	151.92	167.95	703.91
ER - WR 400 kV Raigarh - Jharsuguda 2xD/C	248.78	148.94	125.69	125.00	127.87	110.94	267.35	221.93	208.02	310.82	371.43	254.70	2521.47
ER - WR 220 kV Korba - Budhipadar D/C	1.45	0.00	0.14	6.23	1.99	1.46	3.18	3.22	2.35	33.09	17.42	0.87	71.40
ER - WR 220 kV Raigarh - Budhipadar	55.98	38.46	41.41	66.29	74.76	49.37	81.54	41.32	24.30	48.09	73.44	59.99	654.94
Total ER - WR	925.41	467.76	372.98	303.04	393.92	564.32	884.73	1469.71	1160.27	1420.43	1608.37	1522.90	11093.85
Export of ER to NER (ER - NER)													
ER - NER 400 kV Binaguri - Bongaigaon D/C	6.99	16.15	105.81	142.19	71.19	215.10	134.98	60.68	0.64	4.12	6.09	6.82	770.75
ER - NER 400 kV Alipurduar - Bongaigaon D/C	4.62	34.31	135.94	83.03	84.82	161.59	95.15	85.48	0.00	1.71	2.63	10.78	700.05
ER - NER 220 kV Birpara - Salakati D/C	0.54	3.12	31.19	37.25	25.19	47.94	25.71	15.50	0.00	0.38	0.45	1.56	188.82
Total ER - NER	12.16	53.58	272.93	262.48	181.20	424.63	255.83	161.66	0.64	6.20	9.16	19.16	1659.62
Import of ER from NER (NER - ER)													
NER - ER 400 kV Binaguri - Bongaigaon D/C	52.83	40.19	37.75	2.10	10.62	0.07	5.53	48.07	75.32	53.10	17.90	65.72	409.21
NER - ER 400 kV Alipurduar - Bongaigaon D/C	182.37	135.22	72.81	20.59	29.76	3.08	23.52	172.08	294.27	231.86	141.39	253.99	1560.94
NER - ER 220 kV Birpara - Salakati D/C	34.59	31.32	10.78	0.62	2.83	0.14	2.65	38.72	64.62	39.51	27.84	27.58	281.19
Total NER - ER	269.78	206.73	121.33	23.31	43.22	3.29	31.70	258.87	434.22	324.47	187.14	347.29	2251.34
Export of ER to SR (ER - SR)													
ER - SR HVDC Gazuwaka	375.93	395.23	208.61	178.44	321.36	201.99	378.26	352.24	239.96	240.59	353.34	461.44	3707.38
ER - SR HVDC Talchar - Kolar	1233.20	1204.28	984.75	977.61	1284.58	1076.42	1294.48	1214.02	1257.33	611.06	993.37	1223.47	13354.56
ER - SR 765 kV Angul- Srikakulam D/C	1683.42	1561.33	1412.42	1184.37	1380.27	1160.32	1534.32	1466.97	1513.04	1468.02	1655.15	1863.17	17882.82
Total ER - SR	3292.55	3160.85	2605.77	2340.42	2986.21	2438.74	3207.06	3033.23	3010.33	2319.67	3001.86	3548.08	34944.77
Import of ER from SR (SR - ER)													
SR - ER HVDC Gazuwaka	0.00	0.00	55.34	114.11	32.48	0.00	0.00	6.03	0.00	0.00	0.00	0.00	207.97
SR - ER HVDC Talchar - Kolar	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.01
SR - ER 765 kV Angul- Srikakulam D/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Total SR - ER	0.00	0.00	55.34	114.11	32.48	0.00	0.00	6.03	0.00	0.00	0.00	0.00	207.97

	Apr'23	May'23	June'23	July'23	Aug'23	Sep'23	Oct'23	Nov'23	Dec'23	Jan'24	Feb'24	Mar'24	Fin. Year 2023-24
Name of Line													
Export of WR to SR (WR-SR)													
WR - SR HVDC Bhadrawati	544.41	411.52	171.68	139.64	464.81	222.80	593.89	435.49	593.74	438.40	511.83	653.79	5182.01
WR - SR 765 kV Sholapur - Raichur 2x5/C	417.69	222.76	146.07	83.93	451.70	125.10	226.89	116.70	185.60	358.47	476.22	816.76	3627.89
WR - SR 765 kV Wardha - Nizamabad D/C	1323.51	873.44	1018.25	852.05	1313.80	864.24	1099.04	930.66	873.02	1038.49	181.65	957.39	11325.54
WR - SR 400KV Kolhapur-Kudgi D/C	0.00	0.00	0.00	0.00	0.06	0.00	0.00	0.00	0.00	0.03	0.00	0.01	0.10
WR-SR HVDC Raigarh-Pugalur	3004.35	1791.86	1182.91	885.62	2135.69	1450.16	2583.88	1858.37	1697.06	1365.48	2307.50	3450.25	23713.12
WR-SR 220kV Xeldem - Ambewadi S/C	77.16	70.18	68.17	61.74	68.61	67.55	69.49	67.29	61.47	59.32	64.33	70.91	806.21
WR-SR 220kV Ponda - Ambewadi S/C	0.29	1.54	0.28	0.16	5.23	0.04	0.08	0.97	0.04	1.38	1.26	1.38	12.64
WR-SR 765 kV Warora - Warangal D/C	-	-	-	-	-	-	-	-	-	1060.47	1296.17	1769.98	4126.62
Total WR - SR	5367.41	3371.30	2587.37	2023.14	4439.89	2729.89	4573.27	3409.48	3410.93	4322.03	4838.96	7720.47	48794.12
Import of WR from SR (SR - WR)													
SR - WR HVDC Bhadrawati	4.11	25.09	178.09	308.60	10.36	114.86	0.00	0.00	0.00	0.00	0.00	0.00	641.13
SR - WR 765 kV Raichur - Sholapur 2x5/C	29.13	205.27	344.82	478.51	54.56	420.76	215.80	334.15	175.90	151.44	64.99	0.60	2475.92
SR - WR 765 kV Wardha - Nizamabad D/C	0.00	3.90	0.32	18.33	0.00	19.87	0.03	0.89	0.00	0.53	0.05	0.00	43.93
SR - WR 400KV Kolhapur-Kudgi D/C	623.59	719.30	784.98	796.02	623.43	850.54	765.68	701.36	642.95	615.99	577.88	446.18	8147.91
SR-WR HVDC Pugalur-Raigarh	0.00	3.73	14.87	16.65	0.00	0.09	0.00	0.00	0.00	0.00	0.00	0.00	35.33
WR-SR 220kV Ambewadi - Xeldem S/C	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
WR-SR 220kV Ambewadi-Ponda S/C	0.00	0.00	0.01	0.00	0.01	0.01	0.02	0.01	0.02	0.02	0.00	0.00	0.10
SR-WR 765 kV Warangal - Warora D/C	-	-	-	-	-	-	-	-	-	0.26	0.00	0.00	0.26
Total SR - WR	656.84	957.30	1323.09	1618.10	688.36	1406.13	981.53	1036.41	818.88	768.24	642.92	446.78	11344.58
TOTAL ALL INDIA	20628	19721	20060	20679	21383	21447	20437	19992	19795	22384	20090	22872	249487
*In case of multiple ckt / DC pole year corresponds to the commissioning of final element													

Date	15.1 Import-Export of NR with WR during March 2024																	
	Import of NR from WR (WR-NR)																	
	WR - NR 765 kV Gwalior - Agra 2x5/C	WR-NR 765 kV Gwalior-Phagi 2x5/C	WR-NR 765 kV Jabalpur- Orai D/C	WR-NR 765 kV Satna- Orai	WR-NR 765 kV Gwalior-Orai	WR - NR HVDC Champa- Kurukshetra	WR - NR HVDC Vindhyachal	WR - NR 400 kV Zerda- Kankroli	WR - NR 400 kV Zerda- Bhinmal	WR-NR 400 kV RAPP C - Shujalpur D/C	WR - NR 220 kV Bhanpura - Ranpur	WR - NR 220 kV Bhanpura - Modak	WR - NR 220 kV Auraiya - Malanpur / Mehgaon	WR-NR 400 kV Rihand Vindhyachal D/C	WR - NR HVDC Mundra - M'garh	WR -NR 765 kV Banaskata - Chittorgarh D/C	WR-NR 765 kV Varanasi- Vindhyachal	Total WR - NR
1-Mar-24	21.32	21.52	17.46	20.72	0.00	35.56	0.00	0.00	0.00	0.00	0.00	0.02	0.00	0.00	36.28	0.00	23.12	176.00
2-Mar-24	6.80	0.07	1.67	15.70	0.00	22.18	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	29.71	0.00	14.54	90.67
3-Mar-24	1.61	1.46	5.58	15.13	0.00	30.57	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	15.79	0.00	12.78	82.92
4-Mar-24	5.98	11.68	1.30	18.49	0.00	35.10	0.00	0.00	0.00	0.00	0.00	0.86	0.00	0.00	10.24	0.00	20.84	104.49
5-Mar-24	9.99	8.90	2.35	18.52	0.00	46.80	0.00	0.00	0.00	0.00	1.45	2.30	0.00	0.00	12.64	0.00	23.30	126.25
6-Mar-24	13.06	19.00	7.39	18.86	0.00	46.52	0.00	0.00	0.00	0.00	1.46	2.38	0.00	0.00	14.04	0.00	24.26	146.97
7-Mar-24	9.43	13.61	3.99	19.17	0.00	46.59	0.00	0.00	0.00	0.00	1.42	2.50	0.00	0.00	12.23	0.00	23.80	132.74
8-Mar-24	7.95	12.12	1.88	17.52	0.00	46.56	0.00	0.00		0.00	1.41	2.17	0.00	0.00	9.35	0.00	17.98	116.94
9-Mar-24	7.08	8.32	1.12	16.77	0.00	46.40	0.00	0.00		0.00	1.44	2.05	0.00	0.00	7.36	0.00	21.69	112.23
10-Mar-24	11.11	14.99	7.86	18.91	0.00	25.38	0.00	0.00		0.00	1.38	1.90	0.00	0.00	7.52	0.00	26.11	115.16
11-Mar-24	11.83	14.65	6.53	18.49	0.00	24.01	0.00	0.00		0.00	1.35	2.15	0.00	0.00	16.76	0.00	21.62	117.39
12-Mar-24	11.68	13.79	9.43	18.89	0.00	26.80	0.00	0.00		0.00	1.32	2.10	0.00	0.00	24.23	0.00	28.00	136.24
13-Mar-24	12.02	10.50	7.20	18.20	0.00	34.54	0.00	0.00	0.00	0.00	1.27	2.32	0.00	0.00	24.63	0.00	32.70	143.38
14-Mar-24	16.02	12.49	12.39	18.15	0.00	31.57	0.00	0.00		0.00	1.27	2.30	0.00	0.00	15.76	0.00	33.92	143.87
15-Mar-24	15.21	4.46	9.95	17.92	0.00	47.40	0.00	0.00		0.00	1.05	2.11	0.00	0.00	23.58	0.00	36.12	157.80
16-Mar-24	15.84	7.62	11.22	18.81	0.00	46.68	0.00	0.00	0.00	0.00	1.00	2.33	0.00	0.00	32.47	0.00	34.05	170.02
17-Mar-24	18.22	9.72	14.31	19.18	0.00	46.56	0.00	0.00	0.01	0.00	0.98	2.30	0.00	0.00	30.88	0.00	35.02	177.18
18-Mar-24	17.32	11.42	12.02	18.94	0.00	40.52	0.00	0.00		0.00	1.00	2.30	0.00	0.00	24.74	0.00	28.80	157.06
19-Mar-24	19.60	10.48	15.51	19.65	0.00	35.13	0.00	0.00		0.00	0.97	2.38	0.00	0.00	28.71	0.00	31.57	164.00
20-Mar-24	14.50	13.94	12.65	19.55	0.00	35.50	0.00	0.00		0.00	0.93	2.22	0.00	0.00	36.29	0.00	28.08	163.66
21-Mar-24	12.61	13.03	13.40	18.32	0.00	34.82	0.00	0.00		0.00	0.82	2.21	0.00	0.00	21.92	0.00	21.65	138.78
22-Mar-24	0.32	6.15	0.00	15.62	0.00	58.47	0.00	0.00		0.00	0.70	2.44	0.00	0.00	32.18	0.00	13.07	128.95
23-Mar-24	4.95	12.13	4.68	18.25	0.00	59.89	0.00	0.00		0.00	0.84	1.63	0.00	0.00	48.34	0.00	16.86	167.57
24-Mar-24	2.54	11.44	2.56	17.52	0.00	61.05	0.00	0.00		0.00	0.52	0.34	0.00	0.00	22.61	0.00	21.45	140.03
25-Mar-24	0.00	5.16	0.00	14.76	0.00	58.10	0.00	0.00		0.00	0.63	1.45	0.00	0.00	7.30	0.00	20.56	107.96
26-Mar-24	2.94	6.84	0.00	16.94	0.00	59.60	0.00	0.00		0.00	0.61	1.63	0.00	0.00	7.86	0.00	14.87	111.29
27-Mar-24	9.06	12.17	4.64	18.34	0.00	44.95	0.00	0.00		0.00	0.30	2.17	0.00	0.00	11.35	0.00	21.56	124.54
28-Mar-24	11.80	9.28	8.35	17.72	0.00	34.84	0.00	0.00		0.00	1.08	2.15	0.00	0.00	14.59	0.00	34.06	133.87
29-Mar-24	12.99	4.39	7.49	16.16	0.00	35.17	0.00	0.00		0.00	1.10	2.23	0.00	0.00	14.69	0.00	36.68	130.90
30-Mar-24	6.08	3.15	3.23	15.91	0.00	38.99	0.00	0.00		0.00	2.03	2.45	0.00	0.00	15.59	0.00	32.37	119.80
31-Mar-24	3.45	6.89	2.53	15.35	0.00	44.94	0.00	0.00		0.00	1.80	2.45	0.00	0.00	14.38	0.00	29.21	121.00
Total	313.31	311.37	208.69	552.46	0.00	1281.19	0.00	0.00	0.01	0.00	30.13	57.84	0.00	0.00	624.02	0.00	780.64	4159.66
Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day																		

Date	15.1 Import-Export of NR with WR during March 2024																	
	Export of NR to WR (NR- WR)																	
	NR - WR 765 kV Gwalior - Agra 2x5/C	NR-WR 765 kV Gwalior-Phagi 2x5/C	NR-WR 765 kV Jabalpur- Orai D/C	NR-WR 765 kV Satna- Orai	NR-WR 765 kV Gwalior-Orai	NR - WR HVDC Champa- Kurukshetra	NR - WR HVDC Vindhyachal	NR - WR 400 kV Zerda- Kankroli	NR - WR 400 kV Zerda- Bhinmal	NR-WR 400 kV RAPP C - Shujalpur D/C	WR - NR 220 kV Bhanpura - Ranpur	WR - NR 220 kV Bhanpura - Modak	NR - WR 220 kV Auraiya - Malanpur / Mehgaon	NR-WR 400 kV Rihand- Vindhyachal D/C	NR - WR HVDC Mundra - M'garh	NR - WR 765 kV Banaskata - Chittorgarh D/C	NR-WR 765 kV Varanasi- Vindhyachal	Total NR - WR
1-Mar-24	0.00	0.00	0.00	0.00	13.42	0.00	12.18	3.56	5.52	0.81	1.65	0.00	1.83	10.96	0.00	12.20	0.00	62.13
2-Mar-24	0.00	0.00	0.00	0.00	6.12	0.00	12.18	4.67	10.18	9.49	3.12	1.20	2.04	10.21	0.00	7.30	0.00	66.51
3-Mar-24	0.00	0.00	0.00	0.00	7.70	0.00	12.15	6.71	3.95	8.14	3.18	1.13	2.33	15.46	0.00	14.51	0.00	75.26
4-Mar-24	0.00	0.00	0.00	0.00	9.60	0.00	12.02	4.05	6.89	6.07	0.20	0.00	2.03	20.45	0.00	20.31	0.00	81.62
5-Mar-24	0.00	0.00	0.00	0.00	9.95	0.00	12.10	3.32	6.71	6.75	0.00	0.00	2.14	19.91	0.00	10.02	0.00	70.90
6-Mar-24	0.00	0.00	0.00	0.00	12.56	0.00	12.14	3.37	5.35	3.75	0.00	0.00	2.28	22.45	0.00	13.06	0.00	74.96
7-Mar-24	0.00	0.00	0.00	0.00	12.85	0.00	9.05	5.02	6.04	6.20	0.00	0.00	2.53	22.39	0.00	16.03	0.00	80.11
8-Mar-24	0.00	0.00	0.00	0.00	12.61	0.00	7.30	6.15		6.55	0.00	0.00	2.82	21.75	0.00	19.28	0.00	76.46
9-Mar-24	0.00	0.00	0.00	0.00	11.19	0.00	10.25	8.15		7.40	0.00	0.00	2.85	22.30	0.00	14.99	0.00	77.13
10-Mar-24	0.00	0.00	0.00	0.00	12.44	0.00	12.14	3.78		5.25	0.00	0.00	2.76	22.39	0.00	14.26	0.00	73.02
11-Mar-24	0.00	0.00	0.00	0.00	11.92	0.00	12.16	7.82		6.77	0.00	0.00	2.86	22.30	0.00	17.30	0.00	81.13
12-Mar-24	0.00	0.00	0.00	0.00	11.85	0.00	12.12	7.80		5.28	0.00	0.00	2.66	22.40	0.00	14.90	0.00	77.01
13-Mar-24	0.00	0.00	0.00	0.00	12.10	0.00	12.11	8.16	0.00	5.56	0.00	0.00	2.60	22.49	0.00	14.80	0.00	77.82
14-Mar-24	0.00	0.00	0.00	0.00	12.72	0.00	12.17	7.42		5.33	0.00	0.00	0.92	21.58	0.00	16.93	0.00	77.07
15-Mar-24	0.00	0.00	0.00	0.00	10.16	0.00	12.17	8.52		7.06	0.00	0.00	1.96	22.25	0.00	14.50	0.00	76.62
16-Mar-24	0.00	0.00	0.00	0.00	10.58	0.00	12.16	9.46	0.00	4.91	0.00	0.00	2.16	22.19	0.00	24.11	0.00	85.57
17-Mar-24	0.00	0.00	0.00	0.00	10.08	0.00	10.90	9.79	0.00	4.23	0.00	0.00	2.13	22.15	0.00	23.03	0.00	82.31
18-Mar-24	0.00	0.00	0.00	0.00	11.42	0.00	2.48	8.32		4.30	0.00	0.00	2.37	22.36	0.00	22.42	0.00	73.67
19-Mar-24	0.00	0.00	0.00	0.00	10.87	0.00	2.43	8.01		4.60	0.00	0.00	2.16	22.22	0.00	20.46	0.00	70.75
20-Mar-24	0.00	0.00	0.00	0.00	11.50	0.00	2.71	10.70		5.13	0.00	0.00	2.25	21.76	0.00	26.17	0.00	80.22
21-Mar-24	0.00	0.00	0.00	0.00	11.98	0.00	7.29	11.70		5.63	0.00	0.00	2.48	22.10	0.00	27.03	0.00	88.21
22-Mar-24	0.00	0.00	-0.31	0.00	10.42	0.00	7.40	13.80		9.12	0.00	0.00	3.18	22.46	0.00	32.65	0.00	98.72
23-Mar-24	0.00	0.00	0.00	0.00	12.57	0.00	7.28	14.32		6.70	0.00	0.00	3.01	22.45	0.00	36.94	0.00	103.27
24-Mar-24	0.00	0.00	0.00	0.00	12.20	0.00	6.91	13.91		7.57	0.00	0.00	3.12	21.70	0.00	34.05	0.00	99.46
25-Mar-24	1.20	0.00	4.36	0.00	10.76	0.00	6.13	12.00		9.21	0.00	0.00	2.88	18.95	0.00	31.19	0.00	96.68
26-Mar-24	0.00	0.00	2.01	0.00	11.56	0.00	6.06	8.80		8.67	0.00	0.00	2.33	21.38	0.00	29.36	0.00	90.17
27-Mar-24	0.00	0.00	0.00	0.00	12.35	0.00	6.08	11.44		6.35	0.00	0.00	2.18	22.29	0.00	25.60	0.00	86.29
28-Mar-24	0.00	0.00	0.00	0.00	10.75	0.00	6.08	14.85		6.02	0.00	0.00	2.36	22.43	0.00	23.96	0.00	86.45
29-Mar-24	0.00	0.00	0.00	0.00	10.11	0.00	6.10	11.63		7.05	0.00	0.00	1.85	22.23	0.00	18.58	0.00	77.55
30-Mar-24	0.00	0.00	0.00	0.00	9.91	0.00	6.00	9.38		5.22	0.00	0.00	2.13	22.11	0.00	18.58	0.00	73.33
31-Mar-24	0.00	0.00	0.00	0.00	10.30	0.00	6.06	8.95		4.45	0.00	0.00	2.42	21.94	0.00	23.55	0.00	77.67
Total	1.20	0.00	6.06	0.00	344.55	0.00	274.31	265.56	44.64	189.57	8.15	2.33	73.62	650.01	0.00	638.07	0.00	2498.07

Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day

Date	15.2 Import-Export of NR with ER & NER during March 2024																		
	Import of NR from ER (ER-NR)																	Import of NR from NER (NER-NR)	
	ER - NR 765 kV Sasaram - Fatehpur	ER - NR 765 kV Gaya - Varanasi 2*5/C	ER - NR 765 kV Gaya Balia	ER - NR HVDC Alipurduar - Agra	ER-NR 400 kV Patna - Balia D/C	ER - NR 400 kV Muzaffarpur - Gorakhpur D/C	ER - NR 400 kV Biharshariff - Balia D/C	ER - NR 400 kV Motihari - Gorakhpur D/C	ER - NR 400 kV Biharshariff - Varanasi D/C	ER-NR 400 kV Sasaram - Varanasi	ER-NR 400 kV Sasaram - Allahabad	ER - NR 220 kV Sahupuri-Karamnasa	ER - NR 132 kV Sahupuri - Karamnasa	ER - NR 132 kV Rihand - Nagar Untari	NR - ER 132 kV Rihand - Garhwa	ER-NR 400 kV Naubatpur - Balia D/C	Total ER - NR	NER-NR HVDC Biswanath Chariali - Agra	Total NER-NR
1-Mar-24	11.72	17.52	8.86		20.16	6.54	2.64	9.54	7.48	0.00	1.35	1.92			0.00	6.48	94.21	0.00	0.00
2-Mar-24	5.53	4.90	3.48		11.65	0.38	0.00	4.90	1.46	0.83	0.32	0.94			0.00	3.10	37.49	0.00	0.00
3-Mar-24	5.89	2.39	2.10		6.40	0.00	0.00	3.90	0.61	1.10	0.12	0.14			0.00	2.01	24.66	0.00	0.00
4-Mar-24	9.22	9.55	5.00		11.42	3.47	0.00	7.17	4.23	0.68	0.50	1.30			0.00	3.52	56.06	0.00	0.00
5-Mar-24	9.20	10.50	4.52		9.01	5.03	0.02	8.50	4.25	0.57	0.57	1.44			0.00	3.48	57.09	0.00	0.00
6-Mar-24	9.86	11.38	5.01		12.53	4.49	0.07	7.22	4.57	0.65	0.50	1.26			0.00	3.83	61.37	0.00	0.00
7-Mar-24	7.15	6.57	3.95		10.95	1.56	0.00	5.38	2.66	1.12	0.07	0.00	0.00	1.21	0.00	3.02	43.64	0.00	0.00
8-Mar-24	6.35	5.97	4.11		8.98	0.92	0.00	4.63	2.25	1.45	0.00	0.48	0.48		0.00	2.44	38.06	0.00	0.00
9-Mar-24	5.50	5.80	4.30		8.41	0.48	0.00	4.43	1.51	1.80	0.00	0.48	0.48			2.48	35.67	0.00	0.00
10-Mar-24	6.19	6.58	5.39		9.12	0.39	0.00	5.15	2.45	0.82	0.30	0.08				2.80	39.27	4.48	4.48
11-Mar-24	7.90	9.76	5.95		13.23	3.50	0.00	5.20	3.54	0.69	0.47	0.20				4.40	54.84	0.00	0.00
12-Mar-24	7.50	8.74	5.58		13.72	2.19	0.00	3.86	2.93	0.70	0.44	0.20				2.58	48.44	0.00	0.00
13-Mar-24	5.56	5.67	5.65		9.32	0.28	0.00	4.32	2.45	1.02	0.14	0.62			0.00	2.59	37.62	0.00	0.00
14-Mar-24	5.49	6.26	6.31		9.32	1.16	0.00	4.93	2.91	0.77	0.30	0.88				2.59	40.92	0.00	0.00
15-Mar-24	6.59	5.22	6.58		9.95	0.96	0.00	3.86	2.56	0.89	0.49	1.05				2.82	40.97	0.00	0.00
16-Mar-24	5.98	4.09	5.45		8.96	0.38	0.00	4.08	2.45	0.74	0.00	0.95	0.95			2.66	36.69	0.00	0.00
17-Mar-24	6.54	9.60	8.70		10.52	0.30	0.00	4.34	1.24	0.75	0.40	1.08	0.48			3.11	47.06	0.00	0.00
18-Mar-24	7.78	12.27	8.38		13.40	0.60	0.00	4.92	1.24	0.87	0.24	1.07	0.48			4.16	55.41	0.00	0.00
19-Mar-24	8.01	11.17	8.23		9.50	0.00	0.00	5.81	0.85	0.82	0.28	1.01				3.76	49.44	0.00	0.00
20-Mar-24	11.05	13.88	7.32		14.89	5.30	0.16	8.48	3.78	0.49	0.65	1.09	0.48			4.76	72.33	0.00	0.00
21-Mar-24	11.59	17.26	8.18		14.72	7.48	2.01	8.71	4.51	0.25	0.81	1.42	0.48		0.00	5.21	82.63	0.00	0.00
22-Mar-24	10.89	15.75	6.64		12.08	6.33	1.45	7.35	3.78	0.93	0.91	1.15				4.72	71.98	0.00	0.00
23-Mar-24	9.69	15.96	7.42		13.26	6.98	1.64	7.54	3.47	0.82	0.29	1.35				4.16	72.58	0.00	0.00
24-Mar-24	8.11	12.59	7.45		11.95	5.56	0.50	6.30	1.22	0.97	0.12	1.05				3.49	59.31	0.00	0.00
25-Mar-24	4.95	8.49	6.47		8.95	2.64	0.00	4.03	0.30	1.18	0.00	0.81	0.00			2.57	40.39	0.00	0.00
26-Mar-24	8.29	14.66	8.26		10.60	7.40	1.72	6.26	3.02	0.76	0.36	1.32				3.82	66.47	0.00	0.00
27-Mar-24	8.83	16.46	8.95		12.75	6.03	1.12	5.50	2.82	0.88	0.27	1.15				3.92	68.68	0.00	0.00
28-Mar-24	6.56	8.92	8.63		8.37	3.01	0.62	0.67	0.03	1.21	0.00	0.72			0.00	2.27	41.01	0.00	0.00
29-Mar-24	7.01	4.22	7.68		7.62	1.86	0.00	3.51	0.00	1.31	0.00	0.74	0.00			1.92	35.87	0.00	0.00
30-Mar-24	4.20	5.94	7.89		9.18	0.42	0.00	3.75	0.00	1.41	0.00	1.04			0.05	2.49	36.37	0.00	0.00
31-Mar-24	5.81	8.56	8.95		7.64	3.03	1.15	2.53	0.30	1.31	0.00	1.18	0.00			2.24	42.70	0.00	0.00
Total	234.94	296.63	201.39	0.00	338.56	88.67	13.10	166.77	74.87	27.79	9.90	28.12	3.83	1.21	0.05	103.40	1589.23	4.48	4.48

Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day

Date	15.2 Import-Export of NR with ER & NER during March 2024																		
	Export of NR to ER (NR- ER)																	Export of NR to NER (NR-NER)	
	NR - ER 765 kV Sasaram - Fatehpur	NR - ER 765 kV Gaya - Varanasi 2*5/C	NR - ER 765 kV Gaya Ballia	NR - ER HVDC Alipurduar - Agra	NR-ER 400 kV Patna - Ballia D/C	NR - ER 400 kV Muzaffarpur - Gorakhpur D/C	NR - ER 400 kV Biharshariff - Ballia D/C	NR - ER 400 kV Motihari - Gorakhpur D/C	NR - ER 400 kV Biharshariff - Varanasi D/C	NR-ER 400 kV Sasaram - Varanasi	NR-ER 400 kV Sasaram - Allahabad	NR - ER 220 kV Sahupuri- Karamnasa	NR - ER 132 kV Sahupuri - Karamnasa	NR - ER 132 kV Rihand - Nagar Untari	NR - ER 132 kV Rihand - Garhwa	NR-ER 400 kV Ballia- Naubatpur D/C	Total NR -ER	NR-NER HVDC Biswanath Chariali - Agra	Total NR-NER
1-Mar-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.28	0.00	0.00			0.50	0.00	0.78	16.98	16.98
2-Mar-24	0.00	0.00	0.00		0.00	0.00	1.82	0.00	0.00	0.00	0.00	0.00			0.48	0.00	2.30	18.36	18.36
3-Mar-24	0.00	0.00	0.00		0.00	1.29	2.98	0.00	0.00	0.00	0.00	0.00			0.28	0.00	4.55	17.76	17.76
4-Mar-24	0.00	0.00	0.00		0.00	0.00	0.14	0.00	0.00	0.00	0.00	0.00			0.35	0.00	0.49	16.72	16.72
5-Mar-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.42	0.00	0.42	17.59	17.59
6-Mar-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.42	0.00	0.42	18.85	18.85
7-Mar-24	0.00	0.00	0.00		0.00	0.00	0.71	0.00	0.00	0.00	0.00	0.48	0.48	0.00	0.44	0.00	2.11	18.11	18.11
8-Mar-24	0.00	0.00	0.00		0.00	0.00	1.41	0.00	0.00	0.00	0.41	0.00	0.00		0.19	0.00	2.01	18.02	18.02
9-Mar-24	0.00	0.00	0.00		0.00	0.00	1.62	0.00	0.00	0.00	0.17	0.00	0.00			0.00	1.79	11.85	11.85
10-Mar-24	0.00	0.00	0.00		0.00	0.00	1.88	0.00	0.00	0.00	0.00	0.00				0.00	1.88	0.00	0.00
11-Mar-24	0.00	0.00	0.00		0.00	0.00	1.62	0.00	0.00	0.00	0.00	0.00				0.00	1.62	11.12	11.12
12-Mar-24	0.00	0.00	0.00		0.00	0.00	1.53	0.00	0.00	0.00	0.00	0.00				0.00	1.53	15.54	15.54
13-Mar-24	0.00	0.00	0.00		0.00	0.00	1.85	0.00	0.00	0.00	0.00	0.00			0.72	0.00	2.57	16.75	16.75
14-Mar-24	0.00	0.00	0.00		0.00	0.00	1.85	0.00	0.00	0.00	0.00	0.00				0.00	1.85	17.20	17.20
15-Mar-24	0.00	0.00	0.00		0.00	0.00	1.85	0.00	0.00	0.00	0.00	0.00				0.00	1.85	16.82	16.82
16-Mar-24	0.00	0.00	0.00		0.00	0.00	2.05	0.00	0.00	0.00	0.02	0.00	0.00			0.00	2.07	15.28	15.28
17-Mar-24	0.00	0.00	0.00		0.00	0.00	2.08	0.00	0.00	0.00	0.00	0.00	0.00			0.00	2.08	15.72	15.72
18-Mar-24	0.00	0.00	0.00		0.00	0.00	2.40	0.00	0.00	0.00	0.00	0.00	0.00			0.00	2.40	15.80	15.80
19-Mar-24	0.00	0.00	0.00		0.00	0.18	2.50	0.00	0.00	0.00	0.00	0.00				0.00	2.68	16.54	16.54
20-Mar-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.00	0.00	16.44	16.44
21-Mar-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			0.75	0.75	16.67	16.67
22-Mar-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00				0.00	0.00	16.40	16.40
23-Mar-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00				0.00	0.00	16.40	16.40
24-Mar-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00				0.00	0.00	16.80	16.80
25-Mar-24	0.00	0.00	0.00		0.00	0.00	1.15	0.00	0.00	0.00	0.04	0.00	0.00			0.00	1.19	15.64	15.64
26-Mar-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00				0.00	0.00	16.20	16.20
27-Mar-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00				0.00	0.00	15.55	15.55
28-Mar-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.12	0.00			0.75	0.00	0.87	12.96	12.96
29-Mar-24	0.00	0.00	0.00		0.00	0.00	1.36	0.00	0.81	0.00	0.27	0.00	0.00			0.00	2.44	16.41	16.41
30-Mar-24	0.00	0.00	0.00		0.00	0.00	3.08	0.00	1.15	0.00	0.25	0.00			0.00	0.00	4.48	16.72	16.72
31-Mar-24	0.00	0.00	0.00		0.00	0.00	0.00	0.00	0.00	0.00	0.13	0.00	0.00			0.00	0.13	15.33	15.33
Total	0.00	0.00	0.00	0.00	0.00	1.47	33.88	0.00	1.96	0.28	1.41	0.48	0.48	0.00	5.30	0.00	45.26	486.53	486.53
Disclaimer:- Blank entry if the line under outage/shutdown on corresponding day																			

Date	15.3 Import and Export of ER with WR & NER during March 2024																							
	Export of WR to ER (WR-ER)								Import of WR from ER (ER - WR)								Export of ER to NER (ER-NER)				Import of ER from NER (NER-ER)			
	WR - ER 765 kV Dharamjygarh - Ranchi 2x5/C	WR - ER 765 kV Dharamjygarh - Jharsuguda Q/C	WR - ER 765 kV Durg - Jharsuguda D/C	WR - ER 400 kV Sipat - Ranchi D/C	WR - ER 400 kV Raigarh - Jharsuguda- 2xb/C	WR - ER 220 kV Korba - Budhipadar D/C	WR - ER 220 kV Raigarh - Budhipadar	Total WR - ER	ER - WR 765 kV Dharamjygarh - Ranchi 2x5/C	ER-WR 765 kV Dharamjygarh - Jharsuguda D/C	ER-WR 765 kV Durg - Jharsuguda D/C	ER - WR 400 kV Sipat - Ranchi D/C	ER - WR 400 kV Raigarh - Jharsuguda- 2xD/C	ER - WR 220 kV Korba - Budhipadara D/C	ER - WR 220 kV Raigarh - Budhipadar	Total ER - WR	ER - NER 400 kV Binaguri - Bongaigaon D/C	ER - NER 400 kV Alipurduar - Bongaigaon D/C	ER - NER 220 kV Birpara - Salakati D/C	Total ER - NER	NER - ER 400 kV Binaguri - Bongaigaon D/C	NER - ER 400 kV Alipurduar - Bongaigaon 2xD/C	NER - ER 220 kV Birpara - Salakati D/C	Total NER - ER
1-Mar-24	0.0	13.6	0.0	0.0	0.0	0.7	0.0	14.24	18.4	0.9	14.0	5.8	8.4	0.2	2.9	50.65	0.02	0.00	0.02	0.03	1.82	7.50	0.94	10.26
2-Mar-24	0.0	18.1	0.0	0.0	0.0	0.9	0.0	19.08	18.2	0.1	12.6	5.2	7.8	0.0	3.0	46.81	0.06	0.00	0.02	0.09	1.21	5.63	0.62	7.46
3-Mar-24	0.0	16.6	0.0	0.0	0.0	1.6	0.0	18.15	19.6	0.2	12.1	5.6	8.9	0.0	2.4	48.85	0.04	0.00	0.02	0.06	1.70	7.00	0.87	9.58
4-Mar-24	0.0	12.4	0.0	0.0	0.0	1.0	0.0	13.42	22.9	0.9	13.7	6.6	9.1	0.0	2.9	56.08	0.06	0.00	0.00	0.06	1.92	7.79	0.64	10.35
5-Mar-24	0.0	10.7	0.0	0.0	0.0	1.0	0.0	11.73	22.5	0.2	14.5	6.2	8.6	0.0	3.2	55.19	0.00	0.00	0.00	0.00	2.28	9.35	0.72	12.34
6-Mar-24	0.0	13.0	0.0	0.0	0.0	1.0	0.0	14.01	21.3	0.2	14.2	6.7	9.6	0.1	3.1	55.29	0.00	0.00	0.00	0.00	1.73	7.57	0.61	9.90
7-Mar-24	0.0	21.9	0.0	0.0	0.0	1.8	0.0	23.68	19.2	0.0	12.6	6.0	6.1	0.0	2.7	46.55	0.00	0.00	0.00	0.00	1.90	8.57	0.77	11.24
8-Mar-24	0.0	17.0	0.0	0.0	0.0	1.8	0.0	18.75	20.7	0.0	11.8	6.2	6.2	0.0	2.7	47.62	0.00	0.00	0.00	0.00	2.03	8.65	0.81	11.49
9-Mar-24	0.0	14.7	0.0	0.0	0.0	1.6	0.0	16.31	19.8	0.1	11.8	5.9	7.5	0.0	1.8	47.06	1.15	2.33	0.30	3.77	0.63	3.95	0.34	4.92
10-Mar-24	0.1	20.1	0.0	0.0	0.0	2.0	0.0	22.15	17.1	0.0	11.4	5.3	6.8	0.0	2.0	42.62	3.76	8.03	0.70	12.48	0.68	3.00	0.24	3.92
11-Mar-24	0.0	23.9	0.0	0.0	0.0	0.8	0.0	24.69	19.0	0.0	15.9	7.1	8.8	0.0	2.6	53.48	0.22	0.00	0.11	0.33	0.49	4.03	0.13	4.65
12-Mar-24	0.3	21.2	0.0	0.0	0.0	1.0	0.0	22.51	14.0	0.0	15.8	5.7	9.5	0.1	1.6	46.79	0.23	0.01	0.10	0.34	0.74	4.51	0.09	5.35
13-Mar-24	0.2	17.8	0.0	0.0	0.0	0.8	0.0	18.78	10.6	0.4	12.4	4.5	7.0	0.2	2.4	37.41	0.21	0.04	0.09	0.34	0.68	4.34	0.08	5.10
14-Mar-24	1.8	9.0	0.0	0.0	0.0	0.6	0.0	11.48	7.7	1.0	14.2	4.1	9.8	0.1	2.5	39.30	0.08	0.00	0.05	0.13	1.67	7.86	0.33	9.86
15-Mar-24	1.3	10.5	0.0	0.0	0.0	1.8	0.0	13.65	6.2	0.7	14.1	3.5	9.7	0.0	1.4	35.55	0.00	0.00	0.04	0.04	1.49	7.46	0.25	9.20
16-Mar-24	0.4	5.1	0.0	0.0	0.0	1.5	0.0	6.98	6.1	1.8	13.6	3.6	9.7	0.0	1.2	36.17	0.00	0.00	0.00	0.00	1.77	8.38	0.35	10.50
17-Mar-24	0.4	4.7	0.0	0.0	0.0	1.6	0.0	6.63	8.7	0.6	12.3	3.8	8.7	0.0	1.4	35.62	0.12	0.01	0.05	0.18	0.92	5.49	0.21	6.62
18-Mar-24	0.1	6.2	0.0	0.0	0.1	2.5	0.1	8.88	10.4	3.0	7.8	4.4	8.7	0.0	1.2	35.61	0.04	0.00	0.01	0.05	0.96	5.75	0.39	7.10
19-Mar-24	0.0	7.5	0.0	0.0	0.2	1.9	0.2	9.95	9.7	1.1	12.5	3.6	4.0	0.0	0.3	31.14	0.37	0.21	0.01	0.59	0.67	3.94	0.37	4.98
20-Mar-24	0.0	2.4	0.0	0.0	0.3	1.5	0.0	4.18	20.7	2.7	20.9	5.8	4.9	0.0	1.1	56.02	0.01	0.00	0.00	0.01	1.65	7.40	1.26	10.31
21-Mar-24	0.0	2.7	0.0	0.0	0.0	1.0	0.0	3.68	22.9	2.3	26.4	6.5	9.3	0.0	1.6	68.94	0.00	0.00	0.00	0.00	2.23	8.36	1.23	11.82
22-Mar-24	0.0	11.3	0.0	0.0	0.0	0.9	0.0	12.17	30.4	0.4	24.7	8.1	8.7	0.0	1.5	73.87	0.00	0.00	0.00	0.00	4.74	15.43	2.37	22.54
23-Mar-24	0.0	15.3	0.0	0.0	0.0	0.3	0.0	15.62	25.8	0.0	22.7	7.5	9.5	0.0	1.4	66.87	0.00	0.00	0.00	0.00	4.49	15.38	1.73	21.60
24-Mar-24	0.0	8.5	0.0	0.0	0.0	0.7	0.0	9.19	22.5	0.3	23.5	6.1	8.6	0.0	1.8	62.86	0.00	0.00	0.00	0.00	4.23	14.87	1.13	20.23
25-Mar-24	0.0	9.1	0.0	0.0	0.0	1.2	0.0	10.28	22.9	0.8	23.3	6.0	6.2	0.0	2.0	61.12	0.00	0.00	0.00	0.00	2.53	9.44	1.54	13.52
26-Mar-24	0.0	8.5	0.0	0.0	0.0	1.0	0.0	9.50	29.9	0.7	25.8	7.9	8.2	0.0	2.3	74.81	0.00	0.00	0.00	0.00	4.95	15.73	2.54	23.23
27-Mar-24	0.0	15.6	0.0	0.0	0.0	0.7	0.0	16.23	20.7	0.0	21.3	6.5	9.8	0.0	1.8	60.02	0.00	0.00	0.00	0.00	3.72	13.44	1.95	19.11
28-Mar-24	2.3	24.5	0.0	0.3	0.0	0.7	0.0	27.66	7.4	0.0	14.7	2.6	8.1	0.0	1.7	34.50	0.02	0.00	0.00	0.02	1.88	8.27	1.16	11.31
29-Mar-24	1.6	22.3	0.0	0.1	0.0	0.8	0.0	24.81	5.2	0.0	15.7	2.6	8.7	0.0	1.9	34.05	0.10	0.08	0.04	0.22	1.98	7.96	1.13	11.06
30-Mar-24	1.7	28.1	0.0	0.0	0.0	1.3	0.0	31.22	7.5	0.0	15.8	3.3	8.3	0.0	1.0	35.88	0.32	0.06	0.02	0.40	2.60	6.96	0.91	10.46
31-Mar-24	0.2	22.9	0.0	0.0	0.0	1.2	0.1	24.49	11.9	0.0	19.1	5.1	9.4	0.0	0.7	46.19	0.00	0.00	0.00	0.00	5.43	9.96	1.88	17.28
Total	10.41	435.14	0.00	0.37	0.59	37.13	0.47	484.12	519.88	18.33	501.18	167.95	254.70	0.87	59.99	1522.90	6.82	10.78	1.56	19.16	65.72	253.99	27.58	347.29

Date	15.4 Import and Export of SR with ER & WR during March 2024																									
	Export of ER to SR (ER - SR)				Import of ER from SR (SR - ER)				Export of WR to SR (WR-SR)										Import of WR from SR (SR - WR)							
	ER - SR HVDC Gazuwaka	ER - SR HVDC Talchar - Kolar	ER-SR 765 kV Angul- Srikakulam D/C	Total ER - SR	SR - ER HVDC Gazuwaka	SR - ER HVDC Talchar -	SR-ER 765 kV Angul- Srikakulam D/C	Total SR - ER	WR - SR HVDC Bhadrawati	WR - SR 765 kV Sholapur - Raichur 2x5/C	WR-SR 765 kV Wardha - Nizamabad D/C	WR-SR 400KV Kolhapur-Kudgi D/C	WR-SR HVDC Raigarh- Puglur	WR-SR 220kV Keldem - Ambewadi S/C	WR-SR 220kV Ponda - Ambewadi S/C	WR-SR 765 kV Warora - Warangal D/C	Total WR - SR	SR - WR HVDC Bhadrawati	SR - WR 765 kV Raichur - Sholapur 2x5/C	SR-WR 765 kV Wardha - Nizamabad D/C	SR-WR 400KV Kolhapur- Kudgi D/C	SR-WR HVDC Raigarh- Puglur	WR-SR 220kV Keldem - Ambewadi S/C	WR-SR 220kV Ponda - Ambewadi S/C	SR-WR 765 kV Warangal - Warora D/C	Total SR - WR
1-Mar-24	14.71	41.05	60.73	116.49	0.00	0.00	0.00	0.00	13.31	19.98	0.00	0.00	104.53	2.40	0.00	55.41	195.63	0.00	0.40	0.00	19.33	0.00	0.00	0.00	0.00	19.73
2-Mar-24	14.71	46.00	61.76	122.47	0.00	0.00	0.00	0.00	16.22	26.16	0.00	0.00	128.09	1.67	0.00	59.93	232.07	0.00	0.04	0.00	16.01	0.00	0.00	0.00	0.00	16.05
3-Mar-24	14.71	45.97	60.23	120.91	0.00	0.00	0.00	0.00	22.32	32.90	0.00	0.00	116.70	2.21	0.79	61.67	236.59	0.00	0.00	0.00	8.78	0.00	0.00	0.00	0.00	8.78
4-Mar-24	13.40	46.70	61.31	121.41	0.00	0.00	0.00	0.00	20.97	28.88	0.00	0.00	117.30	2.10	0.00	59.66	228.91	0.00	0.00	0.00	11.96	0.00	0.00	0.00	0.00	11.96
5-Mar-24	10.75	42.31	63.95	117.01	0.00	0.00	0.00	0.00	24.01	30.91	0.00	0.00	120.18	2.24	0.00	61.00	238.34	0.00	0.00	0.00	11.12	0.00	0.00	0.00	0.00	11.12
6-Mar-24	13.08	41.24	62.50	116.82	0.00	0.00	0.00	0.00	24.18	30.28	0.00	0.01	110.19	2.31	0.00	59.25	226.22	0.00	0.00	0.00	12.78	0.00	0.00	0.00	0.00	12.78
7-Mar-24	14.57	38.33	62.55	115.45	0.00	0.00	0.00	0.00	24.18	33.44	0.00	0.00	108.82	2.24	0.00	60.68	229.36	0.00	0.00	0.00	13.16	0.00	0.00	0.00	0.00	13.16
8-Mar-24	14.57	41.16	59.62	115.35	0.00	0.00	0.00	0.00	22.11	27.49	0.00	0.00	124.23	2.30	0.00	56.73	232.86	0.00	0.00	0.00	14.33	0.00	0.00	0.00	0.00	14.33
9-Mar-24	14.58	37.41	58.32	110.31	0.00	0.00	0.00	0.00	24.14	24.81	0.00	0.00	117.84	2.33	0.00	55.22	224.34	0.00	0.00	0.00	15.12	0.00	0.00	0.00	0.00	15.12
10-Mar-24	14.57	36.09	57.97	108.63	0.00	0.00	0.00	0.00	24.09	22.45	0.00	0.00	101.34	2.29	0.59	53.92	204.68	0.00	0.08	0.00	12.57	0.00	0.00	0.00	0.00	12.65
11-Mar-24	14.57	40.03	58.81	113.41	0.00	0.00	0.00	0.00	20.57	29.62	0.00	0.00	101.12	2.35	0.00	57.70	211.36	0.00	0.00	0.00	10.73	0.00	0.00	0.00	0.00	10.73
12-Mar-24	14.46	44.59	57.89	116.94	0.00	0.00	0.00	0.00	19.83	30.69	0.00	0.00	92.45	2.40	0.00	57.79	203.16	0.00	0.00	0.00	13.30	0.00	0.00	0.00	0.00	13.30
13-Mar-24	14.55	36.69	56.92	108.16	0.00	0.00	0.00	0.00	21.41	31.26	9.29	0.00	105.29	2.33	0.00	57.34	226.92	0.00	0.00	0.00	14.68	0.00	0.00	0.00	0.00	14.68
14-Mar-24	14.84	34.30	59.73	108.87	0.00	0.00	0.00	0.00	24.12	29.30	52.28	0.00	108.35	2.27	0.00	54.92	271.24	0.00	0.00	0.00	15.27	0.00	0.00	0.00	0.00	15.27
15-Mar-24	15.00	38.85	61.53	115.38	0.00	0.00	0.00	0.00	21.16	32.30	59.14	0.00	108.24	2.36	0.00	58.03	281.23	0.00	0.00	0.00	13.78	0.00	0.00	0.00	0.00	13.78
16-Mar-24	14.60	35.91	58.81	109.32	0.00	0.00	0.00	0.00	17.75	29.58	56.91	0.00	109.72	2.35	0.00	55.56	271.87	0.00	0.00	0.00	13.87	0.00	0.00	0.00	0.00	13.87
17-Mar-24	13.91	43.79	58.16	115.86	0.00	0.00	0.00	0.00	24.13	19.31	44.94	0.00	100.97	1.54	0.00	48.95	239.84	0.00	0.02	0.00	14.14	0.00	0.00	0.00	0.00	14.16
18-Mar-24	14.38	43.46	60.60	118.44	0.00	0.00	0.00	0.00	24.11	17.98	44.13	0.00	116.27	2.35	0.00	54.15	258.99	0.00	0.00	0.00	15.15	0.00	0.00	0.00	0.00	15.15
19-Mar-24	14.83	46.22	62.08	123.13	0.00	0.00	0.00	0.00	16.25	25.65	50.09	0.00	113.60	2.20	0.00	56.73	264.52	0.00	0.00	0.00	13.65	0.00	0.00	0.00	0.00	13.65
20-Mar-24	14.84	46.06	62.16	123.06	0.00	0.00	0.00	0.00	18.72	20.35	47.52	0.00	122.43	2.31	0.00	54.42	265.75	0.00	0.00	0.00	16.65	0.00	0.00	0.00	0.00	16.65
21-Mar-24	17.29	36.14	61.92	115.35	0.00	0.00	0.00	0.00	24.04	18.60	46.70	0.00	121.85	2.38	0.00	53.59	267.16	0.00	0.00	0.00	18.55	0.00	0.00	0.00	0.00	18.55
22-Mar-24	17.44	36.13	62.59	116.16	0.00	0.00	0.00	0.00	24.11	23.63	51.44	0.00	128.73	2.48	0.00	58.17	288.56	0.00	0.01	0.00	15.56	0.00	0.00	0.00	0.00	15.57
23-Mar-24	17.59	36.12	63.36	117.07	0.00	0.00	0.00	0.00	20.42	22.35	51.37	0.00	108.93	2.43	0.00	58.98	264.48	0.00	0.05	0.00	13.05	0.00	0.00	0.00	0.00	13.10
24-Mar-24	17.58	36.11	59.71	113.40	0.00	0.00	0.00	0.00	20.81	19.73	49.08	0.00	123.11	2.38	0.00	55.77	270.88	0.00	0.00	0.00	16.08	0.00	0.00	0.00	0.00	16.08
25-Mar-24	17.64	36.12	60.42	114.18	0.00	0.00	0.00	0.00	24.10	31.02	58.98	0.00	124.59	1.73	0.00	57.97	298.39	0.00	0.00	0.00	10.30	0.00	0.00	0.00	0.00	10.30
26-Mar-24	17.53	36.11	63.33	116.97	0.00	0.00	0.00	0.00	20.02	27.74	59.25	0.00	124.28	2.05	0.00	61.21	294.55	0.00	0.00	0.00	13.86	0.00	0.00	0.00	0.00	13.86
27-Mar-24	14.11	36.11	58.48	108.70	0.00	0.00	0.00	0.00	19.88	21.78	52.69	0.00	108.55	2.64	0.00	55.34	260.88	0.00	0.00	0.00	19.16	0.00	0.00	0.00	0.00	19.16
28-Mar-24	14.14	36.12	57.94	108.20	0.00	0.00	0.00	0.00	14.18	27.63	56.34	0.00	98.15	2.59	0.00	56.98	255.87	0.00	0.00	0.00	19.03	0.00	0.00	0.00	0.00	19.03
29-Mar-24	14.14	36.11	54.61	104.86	0.00	0.00	0.00	0.00	21.42	26.17	52.69	0.00	97.43	2.60	0.00	54.98	255.29	0.00	0.00	0.00	17.05	0.00	0.00	0.00	0.00	17.05
30-Mar-24	14.14	36.12	57.58	107.84	0.00	0.00	0.00	0.00	19.47	27.09	57.03	0.00	96.17	2.55	0.00	58.89	261.20	0.00	0.00	0.00	14.04	0.00	0.00	0.00	0.00	14.04
31-Mar-24	14.21	36.12	57.60	107.93	0.00	0.00	0.00	0.00	21.76	27.68	57.52	0.00	90.80	2.53	0.00	59.04	259.33	0.00	0.00	0.00	13.12	0.00	0.00	0.00	0.00	13.12
TOTAL	461.44	1223.47	1863.17	3548.08	0.00	0.00	0.00	0.00	653.79	816.76	957.39	0.01	3450.25	70.91	1.38	1769.98	7720.47	0.00	0.60	0.00	446.18	0.00	0.00	0.00	0.00	446.78

16. भूटान , नेपाल, बांग्लादेश एवं म्यान्मार के साथ अंतरराष्ट्रीय विद्युत विनिमय

अप्रैल 2023 से मार्च 2024 April 2023 to March 2024

अंतरराष्ट्रीय विद्युत विनिमय [भारत 'से निर्यात' 'को आयात']
Transnational Exchange ('Export from'/'Import to' India)

माह MONTH	भूटान BHUTAN		नेपाल NEPAL		बांग्लादेश BANGLADESH		म्यान्मार MYANMAR	
	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)	Energy Exported (In MU)	Energy Imported (In MU)
अप्रैल 2023 APR'23	23.06	43.80	357.99	0.00	687.30	0.00	0.73	0.00
मई 2023 MAY'23	0.48	125.72	271.80	0.34	775.10	0.00	0.09	0.00
जून 2023 JUN'23	0.00	650.47	80.00	88.86	743.92	0.00	0.77	0.00
जुलाई 2023 JUL'23	0.00	1331.68	0.00	223.72	780.77	0.00	1.02	0.00
अगस्त 2023 AUG'23	0.00	1277.91	0.00	281.61	767.79	0.00	0.94	0.00
सितंबर 2023 SEP'23	0.00	937.81	0.00	323.59	754.88	0.00	0.77	0.00
अक्टूबर 2023 OCT'23	0.00	588.64	0.00	460.97	755.92	0.00	0.84	0.00
नवंबर 2023 NOV'23	51.41	36.77	0.00	271.72	628.24	0.00	0.72	0.00
दिसम्बर 2023 DEC'23	212.51	0.00	88.76	5.09	593.51	0.00	0.70	0.00
जनवरी 2024 JAN'24	287.94	0.00	271.79	0.00	601.77	0.00	0.65	0.00
फरवरी 2024 FEB'24	312.87	0.00	368.61	0.00	593.99	0.00	0.60	0.00
मार्च 2024 MAR'24	241.74	0.00	371.03	0.00	730.33	0.00	0.63	0.00
कुल Total	1130.02	4992.80	1809.97	1655.89	8413.52	0.00	8.47	0.00

* Based on daily operational data

Date	16.1 Import from neighbouring countries during March 2024 (All figures in MU)													
	Import from Bhutan								Import from Bangladesh		Import from Nepal			Import from Myanmar
	400 kV Tala-Binaguri I,II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurwar D/C*	400 kV Jigmeling-Alipurwar D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-Mar-24	0.00	0.00	0.00	0.00	0.00	0.00	0.31	0.00	0.00	0.00	0.00	0.00	0.00	0.00
2-Mar-24	0.00	0.00	0.00	0.00	0.00	0.00	0.38	0.00	0.00	0.00	0.00	0.00	0.00	0.00
3-Mar-24	0.00	0.00	0.00	0.00	0.00	0.00	0.19	0.00	0.00	0.00	0.00	0.00	0.00	0.00
4-Mar-24	0.00	0.00	0.00	0.00	0.00	0.00	0.23	0.00	0.00	0.00	0.00	0.00	0.00	0.00
5-Mar-24	0.00	0.00	0.00	0.00	0.00	0.00	0.27	0.00	0.00	0.00	0.00	0.00	0.00	0.00
6-Mar-24	0.00	0.00	0.00	0.00	0.00	0.00	0.20	0.02	0.00	0.00	0.00	0.00	0.00	0.00
7-Mar-24	0.00	0.00	0.00	0.00	0.00	0.00	0.05	0.00	0.00	0.00	0.00	0.00	0.00	0.00
8-Mar-24	0.00	0.00	0.00	0.00	0.00	0.00	0.08	0.00	0.00	0.00	0.00	0.00	0.00	0.00
9-Mar-24	0.00	0.00	0.00	0.00	0.00	0.00	0.28	0.00	0.00	0.00	0.00	0.00	0.00	0.00
10-Mar-24	0.00	0.00	0.00	0.00	0.00	0.00	0.27	0.00	0.00	0.00	0.00	0.00	0.00	0.00
11-Mar-24	0.00	0.00	0.00	0.00	0.00	0.00	0.36	0.00	0.00	0.00	0.00	0.00	0.00	0.00
12-Mar-24	0.00	0.00	0.00	0.00	0.00	0.00	0.43	0.00	0.00	0.00	0.00	0.00	0.00	0.00
13-Mar-24	0.00	0.00	0.00	0.00	0.00	0.00	0.31	0.00	0.00	0.00	0.00	0.00	0.00	0.00
14-Mar-24	0.00	0.00	0.00	0.00	0.00	0.00	0.29	0.00	0.00	0.00	0.00	0.00	0.00	0.00
15-Mar-24	0.00	0.00	0.00	0.00	0.00	0.00	0.30	0.00	0.00	0.00	0.00	0.00	0.00	0.00
16-Mar-24	0.00	0.00	0.00	0.00	0.00	0.00	0.22	0.00	0.00	0.00	0.00	0.00	0.00	0.00
17-Mar-24	0.07	0.00	0.00	0.00	0.00	0.00	0.22	0.00	0.00	0.00	0.00	0.00	0.00	0.00
18-Mar-24	1.78	0.00	0.00	0.00	0.00	0.00	0.49	0.00	0.00	0.00	0.00	0.00	0.00	0.00
19-Mar-24	0.00	0.00	0.00	0.00	0.00	0.00	0.49	0.00	0.00	0.00	0.00	0.00	0.00	0.00
20-Mar-24	0.00	0.00	0.00	0.00	0.00	0.00	0.49	0.00	0.00	0.00	0.00	0.00	0.00	0.00
21-Mar-24	0.00	0.00	0.00	0.00	0.00	0.14	0.49	0.00	0.00	0.00	0.00	0.00	0.00	0.00
22-Mar-24	1.15	0.01	0.00	0.00	0.00	1.05	0.49	0.00	0.00	0.00	0.00	0.00	0.00	0.00
23-Mar-24	0.30	0.00	0.00	0.00	0.00	0.53	0.49	0.00	0.00	0.00	0.00	0.00	0.00	0.00
24-Mar-24	0.00	0.00	0.00	0.00	0.00	0.15	0.49	0.00	0.00	0.00	0.00	0.00	0.00	0.00
25-Mar-24	0.00	0.00	0.00	0.00	0.00	0.00	0.25	0.00	0.00	0.00	0.00	0.00	0.00	0.00
26-Mar-24	1.23	0.17	0.00	0.00	0.00	1.36	0.25	0.00	0.00	0.00	0.00	0.00	0.00	0.00
27-Mar-24	0.72	0.00	0.00	0.00	0.00	0.00	0.25	0.00	0.00	0.00	0.00	0.00	0.00	0.00
28-Mar-24	0.00	0.00	0.00	0.00	0.00	0.00	0.25	0.00	0.00	0.00	0.00	0.00	0.00	0.00
29-Mar-24	0.00	0.00	0.00	0.00	0.00	0.00	0.25	0.00	0.00	0.00	0.00	0.00	0.00	0.00
30-Mar-24	0.00	0.00	0.00	0.00	0.00	0.00	0.25	0.00	0.00	0.00	0.00	0.00	0.00	0.00
31-Mar-24	0.00	0.00	0.00	0.00	0.00	0.00	0.27	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Total	5.25	0.17	0.00	0.00	0.00	3.23	9.59	0.02	0.00	0.00	0.00	0.00	0.00	0.00
Based on SEM/Energy meter data for links where available (*Mangdechu generation receipt at APD through a bypassed arrangement at 400kV Punatsanchu station)														

Date	16.2 Export to neighbouring countries during March 2024													
	(All figures in MU)													
	Export to Bhutan								Export to Bangladesh		Export to Nepal			Export to Myanmar
	400 kV Tala-Binaguri I,II & IV	400 kV Binaguri-Malbase	220 kV Birpara-Chuka D/C	220 kV Birpara-Malbase	400 kV Punatsanchu-Alipurwar D/C*	400 kV Jigmeling-Alipurwar D/C	132 kV Rangia-Motanga	132 kV Salakati-Gelephu	400 kV Behrampur-Bheramara 1,2,3&4	132 kV Surjyamaninagar-Comilla D/C	132 kV Tanakpur-Mahendranagar	400 kV Muzaffarpur-Dhalkebar	From BIHAR Source	11 kV Moreh-Tamu
1-Mar-24	0.39	1.32	2.54	1.02	1.75	0.00	0.00	0.34	19.77	1.12	1.49	9.35	2.69	0.02
2-Mar-24	0.57	1.47	2.32	0.83	1.85	0.00	0.00	0.29	19.42	2.48	1.42	8.15	2.42	0.02
3-Mar-24	0.49	1.34	2.38	0.80	1.66	0.00	0.00	0.34	20.15	2.67	0.99	8.83	1.54	0.02
4-Mar-24	0.09	1.45	2.25	0.79	0.98	1.04	0.00	0.33	20.21	2.78	1.41	8.76	1.93	0.02
5-Mar-24	0.54	1.43	2.51	0.84	0.00	2.64	0.00	0.42	18.27	2.86	1.51	8.93	1.91	0.02
6-Mar-24	0.64	1.56	2.97	0.81	0.00	1.94	0.00	0.34	19.70	2.84	1.50	8.42	2.71	0.02
7-Mar-24	1.10	2.06	3.40	1.18	0.00	2.93	0.00	0.42	19.48	2.73	1.43	9.28	2.37	0.02
8-Mar-24	2.22	0.65	3.49	1.33	0.00	2.07	0.00	0.40	19.47	2.57	1.31	8.84	2.35	0.02
9-Mar-24	1.62	1.01	3.75	0.97	0.00	2.40	0.00	0.25	19.30	2.54	1.28	8.25	2.43	0.02
10-Mar-24	1.95	2.28	3.53	0.20	0.00	3.09	0.00	0.09	21.83	2.66	1.28	9.81	2.64	0.02
11-Mar-24	1.10	2.16	3.53	1.08	0.00	2.70	0.00	0.19	21.84	2.76	1.35	8.84	2.60	0.02
12-Mar-24	1.19	2.27	3.47	1.14	0.00	2.39	0.00	0.16	21.77	2.87	1.37	8.97	2.82	0.02
13-Mar-24	0.75	1.82	3.96	0.66	0.00	2.62	0.00	0.18	21.83	3.16	1.30	10.25	2.08	0.02
14-Mar-24	1.15	2.18	4.13	0.82	0.00	2.89	0.00	0.29	21.85	2.77	1.34	9.04	1.90	0.02
15-Mar-24	1.13	2.18	3.35	1.08	0.00	2.66	0.00	0.25	17.43	2.44	1.35	9.56	2.70	0.02
16-Mar-24	0.97	2.07	3.43	1.14	0.00	2.70	0.00	0.30	21.46	2.75	1.28	8.93	2.08	0.00
17-Mar-24	0.00	3.04	3.60	1.56	0.00	2.80	0.00	0.25	21.61	3.01	1.30	10.23	2.47	0.02
18-Mar-24	0.00	4.28	4.56	1.27	0.00	2.13	0.00	0.24	21.77	3.11	1.33	10.21	2.39	0.02
19-Mar-24	1.46	2.53	4.57	0.80	0.00	2.15	0.00	0.22	21.59	3.01	1.39	10.64	2.41	0.02
20-Mar-24	1.18	2.28	4.34	1.55	0.00	2.13	0.00	0.39	21.73	2.84	1.30	10.29	2.55	0.02
21-Mar-24	0.01	1.07	2.96	1.22	0.00	0.00	0.00	0.25	21.76	2.74	1.28	7.68	2.66	0.02
22-Mar-24	0.00	0.00	2.66	1.19	0.00	0.00	0.00	0.36	20.09	2.61	1.29	8.67	2.78	0.00
23-Mar-24	0.00	0.82	2.94	1.39	0.00	0.00	0.00	0.27	21.92	2.92	1.18	6.94	1.88	0.02
24-Mar-24	0.00	1.08	3.10	1.45	0.00	0.00	0.00	0.18	21.95	2.79	1.10	6.15	0.70	0.02
25-Mar-24	0.32	1.37	3.21	1.52	0.00	0.07	0.00	0.28	20.56	3.17	0.79	3.99	0.56	0.02
26-Mar-24	0.00	0.00	2.79	1.58	0.00	0.00	0.00	0.37	20.62	2.91	0.97	3.89	0.56	0.02
27-Mar-24	0.00	0.43	3.20	1.41	0.00	1.17	0.00	0.48	21.50	2.83	1.12	6.79	1.28	0.02
28-Mar-24	0.45	1.53	3.26	1.43	0.00	2.32	0.00	0.41	21.62	2.87	1.04	7.25	2.35	0.02
29-Mar-24	0.05	1.18	2.95	1.26	0.00	1.02	0.00	0.29	21.66	2.75	1.05	7.23	2.53	0.02
30-Mar-24	0.00	1.19	2.86	1.20	0.00	0.97	0.00	0.26	21.74	3.06	1.00	7.04	0.73	0.02
31-Mar-24	0.01	1.10	2.88	1.42	0.00	0.49	0.00	0.37	20.64	3.17	0.91	3.58	2.81	0.02
Total	19.40	49.17	100.90	34.93	6.24	47.31	0.00	9.21	644.53	85.79	38.66	254.81	65.84	0.63

Based on SEM/Energy meter data for links where available (*Mangdechu generation receipt at APD through a bypassed arrangement at 400kV Punatsanchu station)

17. एसटीओए (द्विपक्षीय एवं सामूहिक) एवं डी एस एम बिलिंग का ब्योरा – मार्च 2024

STOA (BILATERAL AND COLLECTIVE) & DSM BILLING DETAILS - MARCH 2024

द्विपक्षीय एसटीओए BILATERAL SHORT TERM OPEN ACCESS

मार्च 2024	MARCH 2024		Apr'23- Mar'24	
नोडल क्षे.भा.प्रे.के. का नाम Name of Nodal RLDC	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Energy Approved(MU)	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Energy Approved (MU)
ऊ. क्षे. NR	56	185	8638	34376
प.क्षे. WR	326	461	9446	18657
द.क्षे. SR	364	3147	8645	24556
पू.क्षे. ER	250	209	5838	6984
पूर्वोत्तर क्षे. NER	70	30	1433	612
कुल TOTAL	1066	4032	34000	85185

एसटीओए SHORT TERM OPEN ACCESS

	सामूहिक एसटीओए Collective STOA		द्विपक्षीय एसटीओए Bilateral STOA	
माह MONTH	क्रेताओं / विक्रेताओं की सं. NO. of Buyers/Sellers	अनुमोदित ऊर्जा (मि.यु.) Approved Energy (MU)	अनुमोदित लेन – देनों की संख्या No. of Approved Transactions	अनुमोदित ऊर्जा (मि.यु.) Approved Energy (MU)
अप्रैल 2023 Apr'23	5580	6941	3322	9714
मई 2023 May'23	5798	6626	3469	8418
जून 2023 Jun'23	5783	6966	3925	10583
जुलाई 2023 Jul'23	6428	6719	3872	10780
अगस्त 2023 Aug'23	5954	6805	4841	12338
सितंबर 2023 Sep'23	6440	6506	4481	12402
अक्टूबर 2023 Oct'23	6571	7388	4658	5866
नवंबर 2023 Nov'23	7848	7741	773	2892
दिसम्बर 2023 Dec'23	8441	7397	1033	3649
जनवरी 2024 Jan'24	9045	8184	1219	2158
फरवरी 2024 Feb'24	8419	7349	1341	2355
मार्च 2024 Mar'24	9939	7856	1066	4032
कुल TOTAL	86246	86478	34000	85185

मासिक डी एस एम बिलिंग का ब्योरा* 2023-24
MONTHLY DSM BILLING DETAILS* 2023-24

अनंतिम आँकड़े
Provisional data
subject to change
करोड़ रु. में (RS. IN CRORES)

क्षेत्र REGION →	उत्तरी क्षेत्र NORTH	पश्चिमी क्षेत्र WEST	दक्षिणी क्षेत्र SOUTH	पूर्वी क्षेत्र EAST	पूर्वोत्तर क्षेत्र NORTH EAST
सप्ताह WEEK ↓					
04.03.24 to 10.03.24	68.13	117.41	154.38	---	0.00
11.03.24 to 17.03.24	125.84	163.65	205.30	---	0.00
18.03.24 to 24.03.24	67.77	159.67	214.48	---	0.00
25.03.24 to 31.03.24	98.59	162.04	184.63	---	0.00

* Amount shown is Payable to DSM pool ^Provisional Data

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL) पावर एक्स्चेंज के माध्यम से विनिमय – माह:- मार्च 2024 EXCHANGES THROUGH POWER EXCHANGES - MARCH 2024				
क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
1	AD HYDRO POWER LIMITED	उत्तरी क्षेत्र NR	14.57	0.00
2	ADANI SOLAR ENERGY JAISALMER TWO PRIVATE LIMITED(Project-2)		25.28	0.00
3	ADANI SOLAR ENERGY JODHPUR TWO LIMITED		11.75	0.00
4	ADANI SOLAR ENERGY RJ TWO PRIVATE LIMITED		15.97	0.00
5	ADANI SOLAR ENERGY RJ TWO PRIVATE LIMITED (Infirrm)		27.53	0.00
6	ADANI SOLAR ENERGY RJ TWO PRIVATE LIMITED(Phalodi)		0.27	0.00
7	Adept Renewable Technologies Private Limited		27.59	0.00
8	Amp Energy Green Six Private Limited		25.38	0.00
9	Amplus Ages Private Limited		25.01	0.00
10	Budhil HEP (Greenko Budhil Hydro Power Pvt. Ltd.)		0.86	0.00
11	Chandigarh (UT)		38.68	0.23
12	Delhi		171.00	99.54
13	Grian Energy Private Limited		21.23	0.00
14	Haryana		147.02	67.90
15	Himachal Pradesh		130.76	37.38
16	IGSTPS JHAJJAR		4.74	0.00
17	Jammu Kashmir		49.37	252.76
18	KARCHAM WANGTOO HYDRO ELECTRIC PLANT.		19.72	0.00
19	NEPAL ELECTRICITY AUTHORITY TANAKPUR		0.00	31.87
20	NTPC Dadri Stage I		2.25	0.00
21	NTPC Dadri Stage II		4.68	0.00
22	NTPC Rihand stage I		9.32	0.00
23	NTPC Rihand stage II		6.48	0.00
24	NTPC Rihand stage III		3.94	0.00
25	NTPC Singrauli		8.08	0.00
26	NTPC Tanda Stage II		11.55	0.00
27	NTPC Unchahar Stage I		4.03	0.00
28	NTPC Unchahar Stage II		4.25	0.00
29	NTPC Unchahar Stage III		4.15	0.00
30	NTPC Unchahar Stage IV		7.47	0.00
31	North Central Railway Prayagraj		0.00	40.89
32	Onewolt Energy Private Limited		24.71	0.00
33	Punjab		11.71	824.16
34	RENEW SURYA AAYAN PRIVATE LIMITED		57.46	0.00
35	RENEW SURYA PRATAP PRIVATE LIMITED		38.51	0.00
36	RENEW SURYA PRATAP PRIVATE LIMITED _Infirrm		0.34	0.00
37	RENEW SURYA ROSHNI PRIVATE LIMITED-Fatehgarh-III PS		57.82	0.00
38	RENEW SURYA VIHAAN PRIVATE LIMITED		20.40	0.00
39	Rajasthan		260.37	412.29
40	ReNew Surya Ravi Private Limited		54.78	1.68
41	SHREE CEMENT LIMITED TPS		6.77	0.00
42	Salnj HEP		7.29	0.04
43	Singoli Bhatwari HEP		12.15	0.00
44	Sorang HEP (Himachal Sorang Power Pvt. Ltd.)		4.96	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- मार्च 2024
EXCHANGES THROUGH POWER EXCHANGES - MARCH 2024

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
45	TPSL 200MW TPTCL Banderwala		16.04	0.00
46	Transition Energy Services Private Limited		18.76	0.00
47	Uttar Pradesh		900.13	465.82
48	Uttarakhand		24.21	296.60

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL) पावर एक्स्चेंज के माध्यम से विनिमय – माह:- मार्च 2024 EXCHANGES THROUGH POWER EXCHANGES - MARCH 2024				
क्र. स. स. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
49	ACB (INDIA) LIMITED	पश्चिमी क्षेत्र WR	42.99	0.20
50	ADANI GREEN ENERGY TWENTY SIX A LIMITED_Infirm		0.03	0.00
51	ADANI RENEWABLE ENERGY FIFTY FIVE LIMITED_Infirm		0.18	0.00
52	ADANI RENEWABLE ENERGY HOLDING FOUR LIMITED		104.95	0.00
53	ADANI WIND ENERGY KUTCHH FOUR Ltd. Nakhatrana		64.07	0.00
54	ADANI WIND ENERGY KUTCHH FOUR Ltd. Nakhatrana (infirm)		16.05	0.00
55	Adani Green Energy Twenty Five A Limited_Infirm		0.07	0.00
56	Adani Green Energy Twenty Five B Limited_Infirm		14.64	0.00
57	Adani Green Energy Twenty Six B Limited_Infirm		1.15	0.00
58	Adani Power Limited - Raigarh TPP		175.55	0.00
59	Adani Power Limited-Raipur TPP		337.44	11.65
60	ArcelorMittal Nippon Steel India Limited		0.00	114.39
61	BHARAT ALUMINIUM COMPANY LTD		12.92	0.00
62	BHARAT ALUMINIUM COMPANY LTD (Bulk Consumer)		0.00	8.12
63	CONTINUUM POWER TRADING (TN) PRIVATE LIMITED		14.78	0.00
64	Chhattisgarh		349.56	38.70
65	D B Power Limited		189.38	0.00
66	DGEN MEGA POWER PROJECT		11.67	0.00
67	DHARIWAL STU OTH		8.36	0.00
68	Daman and Diu - Dadra and Nagar Haveli		2.86	61.32
69	Dhariwal ISTS		18.02	0.00
70	GMR Warora Energy Limited		6.50	0.00
71	Goa WR		14.74	11.83
72	Gujarat		63.71	1104.61
73	INOX GREEN ENERGY SERVICES LIMITED		0.55	0.00
74	Jaypee Nigrie Super Thermal Power Plant		33.60	0.00
75	Jhabua Power Limited		7.96	0.00
76	Jindal Power Limited, Stage-1		112.30	5.51
77	Jindal Power Limited, Stage-2		278.13	12.71
78	Jindal Steel & Power Ltd , DCP		104.94	2.28
79	KSK MAHANADI POWER COMPANY LIMITED		8.00	0.00
80	MAHAN ENERGEN LIMITED.		247.16	29.99
81	MB POWER (MADHYA PRADESH) LIMITED		9.94	18.76
82	Madhya Pradesh		649.49	60.82
83	Maharashtra		208.90	315.09
84	Maruti Clean Coal and Power Limited		9.82	0.00
85	NPCIL KAKRAPAR ATOMIC POWER STATION UNIT 4 INFIRM		65.45	0.00
86	NREL-Dayapar Wind		5.74	0.00
87	NTPC Gadawara		2.88	0.00
88	NTPC Jhanor Gandhar GPS		0.00	0.58
89	NTPC Kawas GPS		0.00	0.56
90	NTPC Korba Stage I &II		2.46	0.00
91	NTPC Korba Stage III		0.34	0.00
92	NTPC Lara Stage I		0.08	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.)
POWER MARKET INFORMATION (Source IEX & PXIL)
पावर एक्स्चेंज के माध्यम से विनिमय – माह:- मार्च 2024
EXCHANGES THROUGH POWER EXCHANGES - MARCH 2024

क्र. स. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
93	NTPC Mouda Stage I		2.02	0.00
94	NTPC Mouda Stage II		2.43	0.00
95	NTPC SAIL POWER COMPANY LIMITED		0.16	0.00
96	NTPC Sipat Stage I		1.28	0.00
97	NTPC Sipat Stage II		2.63	0.00
98	NTPC Solapur		6.83	0.00
99	NTPC Vindhyachal Stage I		2.98	0.00
100	NTPC Vindhyachal Stage II		3.55	0.00
101	NTPC Vindhyachal Stage III		2.17	0.00
102	NTPC Vindhyachal Stage IV		2.32	0.00
103	NTPC Vindhyachal Stage V		0.83	0.00
104	NTPC khargone		7.41	0.00
105	Nani Virani Wind Energy Private Limited		1.41	0.00
106	R.K.M POWERGEN PRIVATE LIMITED		52.25	0.00
107	Ratnagiri Gas & Power Private Limited		0.00	1.36
108	SKS Power Generation Chhattisgarh Limited		4.87	48.71
109	Sasan Power Limited		16.64	0.00
110	TRN ENERGY PRIVATE LIMITED		30.35	0.59
111	The Tata Power Co Ltd (MTPS)		9.42	0.00
112	WIND FIVE RENERGY LIMITED		8.85	0.00

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL) पावर एक्स्चेंज के माध्यम से विनिमय – माह:- मार्च 2024 EXCHANGES THROUGH POWER EXCHANGES - MARCH 2024				
क्र. स. स. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
113	Andhra Pradesh	दक्षिणी क्षेत्र SR	161.26	229.71
114	Goa SR		0.14	10.28
115	IL&FS TAMIL NADU POWER COMPANY LIMITED		5.06	0.00
116	JINDAL POWER LIMITED SIMHAPURI		13.27	0.12
117	JSW RENEW ENERGY LIMITED		3.98	0.00
118	JSW RENEW ENERGY LIMITED INFIRM		0.79	0.00
119	JSW RENEW ENERGY TWO LIMITED		0.09	0.00
120	Karnataka		14.49	103.22
121	Kerala		8.40	280.24
122	NLC INDIA LIMITED NEYVELI NEW THERMAL POWER STATION		4.22	0.00
123	NLC INDIA LIMITED THERMAL POWER STATION I EXPANSION		1.76	0.00
124	NLC INDIA LIMITED THERMAL POWER STATION II EXPANSION		0.61	0.00
125	NLC INDIA LIMITED THERMAL POWER STATION II STAGE I		0.69	0.00
126	NLC INDIA LIMITED THERMAL POWER STATION II STAGE II		1.17	0.00
127	NLC Tamilnadu Power Limited		0.94	0.01
128	NTECL VALLUR		1.37	0.00
129	NTPC KUDGI		5.12	0.00
130	NTPC Ramagundam Stage I &II		2.84	0.00
131	NTPC Ramagundam Stage III		0.59	0.00
132	NTPC Simhadri Stage I		0.78	0.00
133	NTPC Simhadri Stage II		2.19	0.00
134	NTPC Talcher Super Thermal Power Station Stage II		5.54	0.00
135	NTPC Telangana		1.32	0.00
136	OSTRO KANNADA POWER PRIVATE LIMITED		14.16	0.00
137	Pondicherry UT		55.21	0.00
138	RENEW SURYA OJAS PRIVATE LIMITED-Wind		11.78	0.00
139	RENEW SURYA OJAS PRIVATE LIMITED_INFIRM		22.23	0.00
140	RENEW SURYA ROSHNI PRIVATE LIMITED Koppal PS		6.39	0.00
141	RENEW SURYA ROSHNI PRIVATE LIMITED Koppal PS_Infirm		0.74	0.00
142	Ramagundam Floating solar		9.79	0.00
143	SEIL ENERGY INDIA LIMITED		32.48	0.00
144	SEIL Energy India Limited Project II		24.12	0.00
145	Simhadri FSP 15 MW		2.58	0.00
146	Simhadri Floating solar (10 MW)		1.57	0.00
147	Tamil Nadu		43.74	476.73
148	Telangana		178.65	1015.82

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL) पावर एक्स्चेंज के माध्यम से विनिमय - माह:- मार्च 2024 EXCHANGES THROUGH POWER EXCHANGES - MARCH 2024				
क्र. स. स. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
149	ADHUNIK POWER & NATURAL RESOURCES LIMITED	पूर्वी क्षेत्र ER	11.07	0.00
150	Bihar		571.80	2.09
151	Chuzachen HEP		0.11	0.00
152	Damodar Valley Corporation		17.64	44.13
153	Druk Green Power Corporation Limited (DGPC-LBhutan)		0.00	307.33
154	GMR KAMALANGA ENERGY LTD-CTU		0.48	0.00
155	IND BARATH ENERGY UTKAL LIMITED		27.68	0.00
156	Jharkhand		90.57	12.58
157	Jindal India Thermal Power Limited		119.15	0.00
158	KANTI BULEE UTPADAN NIGAM LIMITED		1.97	0.00
159	Kabeli B-1 Hydro Power Project NEPAL ELECTRICITY AUTHORITY		0.39	0.00
160	LIKHU-IV NEA		0.21	0.00
161	Lower Modi Hydro Power Project NEPAL ELECTRICITY AUTHORITY		0.25	0.00
162	NABINAGAR POWER GENERATING COMPANY LIMITED		68.81	0.00
163	NEA Nepal Dordi Khola Hydropower Project		0.47	0.00
164	NEA Nepal Solu Khola (Dudhkoshi) Hydropower Project		3.79	0.00
165	NEA Nepal Upper Dordi A Hydropower Project		0.56	0.00
166	NEPAL ELECTRICITY AUTHORITY MUZAFFARPUR		0.00	265.86
167	NTPC BARH Stage I		4.81	0.00
168	NTPC BARH Stage II		37.04	0.00
169	NTPC Darlipali		1.25	0.00
170	NTPC Farakka stage I		10.03	0.00
171	NTPC Farakka stage III		4.58	0.00
172	NTPC Kahalgaon stage I		10.18	0.00
173	NTPC Kahalgaon stage II		17.32	0.00
174	NTPC North Karanpura STPS		0.83	0.00
175	NTPC North Karanpura STPS infirm (UNIT # 2)		31.16	0.00
176	NTPC Talcher Stage I		4.72	0.00
177	NTPP BRBCL		0.66	0.00
178	Odisha		201.05	372.11
179	Sikkim		8.18	3.94
180	Solu Hydropower Project NEPAL ELECTRICITY AUTHORITY		0.23	0.00
181	Tashiding HEP, Shiga Energy Private Limited		0.00	0.00
182	West Bengal		162.22	228.81

18. पावर मार्केट की सूचना (स्रोत : आई.ई.एक्स. एवं पी.एक्स.आई.एल.) POWER MARKET INFORMATION (Source IEX & PXIL) पावर एक्स्चेंज के माध्यम से विनिमय – माह:- मार्च 2024 EXCHANGES THROUGH POWER EXCHANGES - MARCH 2024				
क्र. सं. S. No.	क्षेत्रीय इकाई Regional Entity	क्षेत्र Region	पावर एक्स्चेंज के माध्यम से (मि.यु. मे) Through Power Exchange in MU	
			(DAM+HP DAM+RTM)	
183	AGARTALA GAS BASED POWER STATION	पूर्वोत्तर क्षेत्र NER	0.01	0.00
184	ASSAM GAS BASED POWER STATION		1.46	0.00
185	Arunachal Pradesh		5.93	20.03
186	Assam		50.52	38.26
187	Bongaigaon Thermal Power Station NTPC		4.89	0.00
188	Doyang HPS, NEEPCO		0.05	0.00
189	KAMENG HYDRO POWER STATION		12.08	0.00
190	Kopili Power Station NEEPCO		0.42	0.00
191	Manipur		17.03	9.22
192	Meghalaya		0.72	49.65
193	Mizoram		1.24	0.00
194	Nagaland		4.91	4.20
195	Palatana Plant		0.72	0.00
196	Pare Hydro Power Station		0.05	0.00
197	Ranganadi Hydro Power Station		0.04	0.00
198	Tripura		11.50	2.65
Total			7856	7856

19. INFORMATION ABOUT RENEWABLE ENERGY
CERTIFICATE MECHANISM
MONTH : MARCH 2024

RE Source & Unit wise break up (01.03.2024-31.03.2024)

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	1	1	2	2
2	Urban or Municipal Waste	12	1	0	0
3	Solar Thermal	0	0	0	0
4	Solar PV	13	15	0	0
5	Small Hydro	0	0	100	1
6	Others	0	0	0	0
7	Geothermal	0	0	0	0
8	Biomass	0	0	0	0
9	Bio-fuel cogeneration	0	0	0	0
	Total	26	17	102	3

RECs Issued (01.03.2024-31.03.2024)

Sr.No.	Non Solar	Solar	Total
1	4537567	101720	4639287

Redemption of REC (01.03.2024-31.03.2024)

Sr.No.	Non Solar	Solar	Total
1	1715397	87155	1802552

19. INFORMATION ABOUT RENEWABLE ENERGY
CERTIFICATE MECHANISM
MONTH : MARCH 2024

RE Source & Unit wise break up (Apr'23-Mar'24)

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	420	26	524	30
2	Urban or Municipal Waste	12	1	0	0
3	Solar Thermal	0	0	0	0
4	Solar PV	362	81	283	14
5	Small Hydro	201	9	201	9
6	Others	0	0	0	0
7	Geothermal	0	0	0	0
8	Biomass	5	1	5	1
9	Bio-fuel cogeneration	8	2	23	5
	Total	1008	120	1036	59

RECs Issued (Apr'23-Mar'24)

Sr.No.	Non Solar	Solar	Total
1	27224898	1129640	28354538

Redemption of REC (Apr'23-Mar'24)

Sr.No.	Non Solar	Solar	Total
1	10976144	820869	11797013

19. INFORMATION ABOUT RENEWABLE ENERGY
CERTIFICATE MECHANISM
MONTH : MARCH 2024

RE Source & Unit wise break up Since Inception to Mar'24

Sr.No	Source Wise	Accreditation		Registration	
		Capacity (MW)	Unit	Capacity (MW)	Unit
1	Wind	3132	530	2977	531
2	Urban or Municipal Waste	12	1	0	0
3	Solar Thermal	0	0	0	0
4	Solar PV	1631	573	1468	479
5	Small Hydro	845	42	857	44
6	Others	4	2	3	1
7	Geothermal	0	0	0	0
8	Biomass	402	37	378	35
9	Bio-fuel cogeneration	823	91	383	55
	Total	6849	1276	6066	1145

RECs Issued since Inception to Mar'24

Sr.No.	Non Solar	Solar	Total
1	115105038	13540378	128645416

Redemption of REC since Inception to Mar'24

Sr.No.	Non Solar	Solar	Total
1	78504329	12449257	90953586

REC Closing balance as on 31.03.2024

Sr.No.	Non Solar	Solar	Total
1	36600709	1091121	37691830

20.Details of Grid Events during the Month of March 2024 in Northern Region



Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH-MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t. Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI for GI-2/GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GI-2	Haryana	02-Mar-2024 19:24	02-Mar-2024 23:34	04:10	0	0	0.000	0.000	37364	46283	i) During antecedent condition, 800kV HVDC Champa-Kurukshetra was carrying total 600MW (approx. 150MW by each Pole). ii) As reported at 19:24hrs, 800 KV HVDC Kurukshetra (PG) Pole-01 and Pole-03 tripped due to DC differential protection operated at Kurukshetra(PG) end (further details yet to be received from PowerGrid). iii) Due to tripping of two poles (Pole-01 and Pole-03), power shifted to other two Poles(Pole-02 and Pole-04) and power order remained same 600MW. iv) As per PMU, fluctuation in voltage was observed. v) As per SCADA, no change in demand is observed in Haryana control area.	1) 800 KV HVDC Kurukshetra(PG) Pole-2 2) 800 KV HVDC Kurukshetra(PG) Pole-4
2	GD-1	Jammu and Kashmir	03-Mar-2024 00:19	03-Mar-2024 01:21	01:02	0	23	0.000	0.072	30649	31909	i) 220/66kV Drass(PG) have double main bus arrangement at 220kV side. 220kV Drass is connected with 220/132kV Kargil which is further connected with Khalsi and Leh. Chutak HEP is connected at 66kV level at 220/66kV Kargil and Nimmo Bazgo HEP is connected at 66kV level at 220/66kV Leh. ii) During antecedent condition (at 00:17hrs) approx. 23MW power was coming from Alustung to Drass and approx. 22MW power was going out from Drass to Kargil. iii) As reported, at 00:19 hrs, 220 KV Alustung-Drass (PG) Ckt tripped on R-N phase to earth fault. iv) Due to this tripping supply to 220 KV Drass (PG) Kargil Ckt was lost and blackout occurred at 220/66kV Drass(PG), Kargil, Khalsi and Leh. v) 220 KV Drass (PG) Kargil Ckt was charged at 01:33 hrs and supply was restored. vi) As per PMU at Amargah, R-N phase to earth fault is observed with fault clearing time of 120ms. vii) As per SCADA, load loss of approx. 23MW at 00:19hrs is observed in J&K control area.	1) 220 KV Alustung-Drass (PG) Ckt
3	GD-1	Jammu and Kashmir	03-Mar-2024 03:09	03-Mar-2024 04:26	01:17	0	14	0.000	0.051	29266	27567	i) During antecedent condition (at 03:07hrs) approx. 04MW power was coming from Alustung to Drass and approx. 03MW power was going out from Drass to Kargil. Chutak HEP was generating ~10MW. ii) At 03:10hrs, 220 KV Alustung-Drass (PG) Ckt tripped on R-N phase to earth fault. This again resulted into blackout at 220/66kV Drass(PG), Kargil, Khalsi and Leh. iii) Due to this tripping supply to 220 KV Drass (PG) Kargil Ckt was lost and blackout occurred at 220/66kV Drass(PG) S/s. iv) 220 KV Drass (PG) Kargil Ckt was charged at 04:26 hrs and supply to Drass was restored. v) As per PMU at Amargah, R-N phase to earth fault is observed with fault clearing time of 120ms. vi) As per SCADA, load loss of approx.14MW at 03:09hrs is observed in J&K control area.	1) 220 KV Alustung-Drass (PG) Ckt
4	GI-2	Rajasthan	03-Mar-2024 14:01	05-Mar-2024 17:54	03:53	2510	0	5.612	0.000	44723	42911	i) On 03rd March, 2024, at 14:02 hrs, 400 KV Kankani-Jaisalmer (RS) Ckt-2 tripped on R-N phase to phase fault. ii) As per PMU at Bhadla2(PG), R-Y phase to phase observed, which cleared within 100msec. iii) At the same time, drop in RE generation of approximately 2510 MW is observed as per SCADA data. Approx. 2200MW drop observed in STS RE generation, ~60MW drop in Rajasthan wind generation and ~310MW drop in Rajasthan solar generation.	1) 400 KV Kankani-Jaisalmer (RS) Ckt-2
5	GD-1	Uttar Pradesh	07-Mar-2024 12:12	07-Mar-2024 13:57	01:45	0	0	0.000	0.000	52783	52018	i) During antecedent condition, 400 KV Singrauli(NT)-Vindhyachal(PG) (PG) ckt-2 was already under planned outage. ii) As reported, at 12:12 hrs, 400 KV Singrauli(NT)-Vindhyachal(PG) (PG) ckt-1 tripped due to maloperation of auto-recloser lock-out relay (B6R2). As per DR, A/R lockout of main-1 CB is observed. iii) Due to tripping of 400 KV Singrauli(NT)-Vindhyachal(PG) (PG) ckt-1, there was no outgoing path available at Vindhyachal B-8(PG) and all other elements tripped at Vindhyachal B-8(PG) and complete blackout occurred at Vindhyachal B-8(PG). iv) As per PMU at Singrauli(NT), no fault is observed in the system. v) As per SCADA, no change in demand in UP control area and no generation loss at Singrauli(NT) is observed.	1) 400 KV Singrauli(NT)-Vindhyachal(PG) (PG) ckt-1 2) 70 KV Vindhyachal(PG) Pole-1 3) 70 KV Vindhyachal(PG) Pole-2 4) 400 KV Vindhyachal North(PG) - Bus 1 5) 400 KV Vindhyachal North(PG) - Bus 2 6) 93 MVAR Bus Reactor No 2 at 400KV Vindhyachal(PG) 7) 125 MVAR Bus Reactor No 3 at 400KV Vindhyachal(PG) 8) 125 MVAR Bus Reactor No 4 at 400KV Vindhyachal(PG)
6	GI-1	Jammu and Kashmir	10-Mar-2024 22:35	10-Mar-2024 23:15	00:40	115	0	0.337	0.000	34098	39965	i) During antecedent condition, only 115 MW Salal HPS - UNIT 5 was under running condition and it was generating approx. 115MW as per SCADA. ii) 220 KV Kishampur(PG)-Salal(NH) (PG) Ckt-1 & 3, 220 KV Salal(NH)-Jammu(PDG) (PG) Ckt-2 and 115 MW Salal HPS - UNIT 5 were connected to 220KV Bus 1 at Salal(NH) and rest of the elements were connected to 220KV Bus 2 at Salal(NH). iii) As reported, at 22:35hrs, 220 KV Kishampur(PG)-Salal(NH) (PG) Ckt-1 & 3, 220 KV Salal(NH)-Jammu(PDG) (PG) Ckt-2 and 115 MW Salal HPS - UNIT 5 tripped due to LBB operation. Hence 220KV Bus 1 at Salal(NH) became dead. iv) As per PMU at Kishampur(PG), R-N phase to earth fault is observed with delayed fault clearing time of 360ms. v) As per SCADA, no load loss is observed in J&K control area. vi) As per SCADA, generation loss of approx. 115MW is observed at Salal(NH) HEP.	1) 220 KV Kishampur(PG)-Salal(NH) (PG) Ckt-1 2) 220 KV Kishampur(PG)-Salal(NH) (PG) Ckt-3 3) 220 KV Salal(NH)-Jammu(PDG) (PG) Ckt-2 4) 220KV Bus 1 at Salal(NH) 5) 115 MW Salal HPS - UNIT 5
7	GD-1	Rajasthan	11-Mar-2024 05:08	11-Mar-2024 06:51	01:43	0	265	0.000	0.697	33592	38005	i) As reported, at 05:08 hrs, interrupter of CB Pole (R-Ph.) blasted at the time of opening of CB of 125MVAR Bus Reactor at Hindaun(RS) on voltage regulation. ii) During the same time, 400 KV Hindaun(RS)-Chhabra(RV/UN) (RS) Ckt, 400 KV Hiraepura-Hindaun (RS) Ckt, 400 KV Alwar(ATL)-Hindaun(RS) (ATL) Ckt, 400/220 KV 315 MVA ICT 1 and 2 at Hindaun(Rail) also tripped (exact reason of tripping yet to be shared). Hence complete blackout occurred at 400/220KV Hindaun(Rail) S/s. iii) As per DR of 400 KV Hindaun(RS)-Chhabra(RV/UN) (end) (RS) Ckt, zone-2 distance protection operated at Chhabra end. R-N phase to earth fault was observed with fault current of 1.67kA and delayed fault clearance time of ~355ms. (DR nomenclature & time sync issue in DR need to be corrected). iv) As per SCADA SOE, 220kV Hindaun220-Sikar(RS) Ckt, 220kV Hindaun220-Hindaun(RS) Ckt and 220kV Hindaun-Chokawada(RS) Ckt-1 also tripped during the same time (exact reason of tripping yet to be shared). v) As per PMU at Basu(PG), R-N phase to earth fault is observed with delayed fault clearing time of 360ms. vi) As per SCADA, load loss of approx. 265MW is observed in Rajasthan control area.	1) 400/220 KV 315 MVA ICT -1 at Hindaun(Rail) 2) 400/220 KV 315 MVA ICT -2 at Hindaun(Rail) 3) 400 KV Hindaun(RS)-Chhabra(RV/UN) (RS) Ckt 4) 400 KV Hiraepura-Hindaun (RS) Ckt 5) 400 KV Alwar(ATL)-Hindaun(RS) (ATL) Ckt
8	GI-2	Uttar Pradesh	11-Mar-2024 01:56	11-Mar-2024 02:51	00:55	0	0	0.000	0.000	31852	34021	i) During antecedent condition, 400/220 KV 315 MVA ICT 1 & 6 and 765/400KV 1000 MVA ICT 1, 2 & 3 at Unnao(UP) were carrying 138MW, 140MW, 549MW, 551MW and 570MW respectively. 400/220 KV 315 MVA ICT 2 at Unnao(UP) was not in service. ii) As reported, at 01:56 hrs, R-N phase to earth fault occurred at 400 KV Bareilly-Unnao (UP) Ckt-2 with fault location of 85 km from Unnao(UP) end. But line CB at Unnao(UP) end of 400 KV Bareilly-Unnao (UP) Ckt-2 failed to clear the fault, hence LBB operated. iii) Due to LBB operation, 400 KV Agra-Unnao (UP) Ckt, 400 KV Unnao(UP)-Jehta, Hardoi Road (UP) (PG) Ckt-2, 400/220 KV 315 MVA ICT 1 at Unnao(UP), 765/400 KV 1000 MVA ICT 2 & 3 at Unnao(UP) also tripped and 400KV Bus 1 at Unnao(UP) became dead. iv) As per DR of 400 KV Bareilly-Unnao (UP) Ckt-2, zone-1 distance protection operated at Unnao end and fault was sensed in zone-1 (carrier-aided trip) at Bareilly end. Fault was cleared within 245ms at Unnao end and 170ms at Bareilly end. R-N phase to earth fault was observed with fault current of 6.329kA from Unnao end and 2.122kA from Bareilly end. v) As per DR of 400 KV Unnao(UP)-Jehta, Hardoi Road (UP) (PG) Ckt-2, DT received at Jehta, Hardoi Road end. vi) As per SCADA SOE, CB of FSC at Unnao(UP) end connected to 400KV Bareilly-Unnao (UP) Ckt-2 closed during the same time. (It is suspected that fault may have initiated due to this. Exact reason of fault need to be shared). vii) As per PMU at Agra(PG), R-N phase to earth fault is observed with delayed fault clearing time of 280ms. viii) As per SCADA, no load loss is observed in UP control area.	1) 400 KV Bareilly-Unnao (UP) Ckt-2 2) 400 KV Agra-Unnao (UP) Ckt 3) 400 KV Unnao(UP)-Jehta, Hardoi Road (UP) (PG) Ckt-2 4) 400/220 KV 315 MVA ICT 1 at Unnao(UP) 5) 765/400 KV 1000 MVA ICT 2 at Unnao(UP) 6) 765/400 KV 1000 MVA ICT 3 at Unnao(UP) 7) 400KV Bus 1 at Unnao(UP)

20.Details of Grid Events during the Month of March 2024 in Northern Region



Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH-MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t. Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI for GI-2/GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
9	GD-1	Jammu & Kashmir	13-Mar-2024 18:49	13-Mar-2024 21:18	02:29	260	0	0.575	0.000	45219	52806	i) During antecedent condition, 130MW Unit-2 & 3 at Dulhasi HEP were running (generating approx. 130 MW each) and total generated power of 260MW was evacuating through 400 KV Dulhasi(NH) Kishenpur(PG) Ckt-1 only. 130MW Unit-1 at Dulhasi HEP and 400 KV Dulhasi(NH) Kishenpur(PG) Ckt-2 were not in service. ii) As reported, at 18:49hrs, 400 KV Dulhasi(NH) Kishenpur(PG) Ckt-1 tripped on R-Y-B-N 3-phase to earth fault. As per DR, fault was sensed in zone-1 at Dulhasi(NH) end and fault currents were Ir=1.63kA, Iy=1.18kA and Ib=1.88kA from Dulhasi(NH) end. iii) Due to tripping of 400 KV Dulhasi(NH) Kishenpur(PG) Ckt-1, 130MW Unit-2 & 3 at Dulhasi HEP also tripped due to loss of evacuation path on over-speed protection operation. iv) As per PMU at Kishenpur (PG), R-Y-B-N 3-phase to earth fault is observed with fault clearing time of 80ms. v) As per SCADA, generation loss of approx. 260MW is observed at Dulhasi HEP.	1) 400 KV Dulhasi(NH) Kishenpur(PG) Ckt-1 2) 130MW Unit-2 at Dulhasi HEP 3) 130MW Unit-3 at Dulhasi HEP
10	GI-2	Rajasthan	14-Mar-2024 12:55	14-Mar-2024 13:34	00:39	0	335	0.000	0.623	53031	53777	i) During antecedent condition, MVA power flows of 400/220 KV 315 MVA ICT-1 & 2 and 220/132KV 100MVA ICT-1, 2 & 3 at Merta(RS) were 275MVA, 261MVA, 60MVA, 55MVA and 54MVA respectively as per SCADA. 220KV Merta(RS) Makrana(RS) Ckt was not in service. ii) As reported, at 12:55hrs, 6-phase jumper of 220KV Merta(RS) Bhopalgah(RS) Ckt snapped and this broken jumper fell on conductor of ICT-1. As per DR, 400/220 KV 315 MVA ICT-1 at Merta(RS) tripped on C/T C/T protection operation with Ir=5.2kA. iii) Due to tripping of ICT-1, 400/220 KV 315 MVA ICT-2 at Merta(RS) got over-loaded. As per DR, 400/220 KV 315 MVA ICT-2 at Merta(RS) tripped on phase directional C/T protection operation with Ir=5.33kA. iv) During the same time, LBB of 220KV Merta(RS) Bhopalgah(RS) Ckt operated (exact reason for line CB at Merta(RS) end unable to clear the fault yet to be shared). v) Due to LBB operation, all the elements connected to 220KV Bus-1 & 2 at Merta(RS) tripped and both the buses became dead. vi) As per PMU at Merta(RS), R-N phase to earth fault is observed with delayed fault clearance time of 880 ms. vii) As per SCADA, change in demand of approx. 335MW is observed in Rajasthan control area.	1) 400/220 KV 315 MVA ICT-1 at Merta(RS) 2) 400/220 KV 315 MVA ICT-2 at Merta(RS) 3) 220KV Merta(RS) Bhopalgah(RS) Ckt 4) 220KV Merta(RS) Kuchera(RS) Ckt 5) 220KV Merta(RS) Jethana(RS) Ckt 6) 220/132KV 100MVA ICT-1 at Merta(RS) 7) 220/132KV 100MVA ICT-2 at Merta(RS) 8) 220/132KV 100MVA ICT-3 at Merta(RS)
11	GD-1	Uttar Pradesh	15-Mar-2024 02:49	15-Mar-2024 05:19	02:30	56	0	0.154	0.000	36385	39522	i) Power of 4*110MW Vishnuprayag HEP evacuates through 400 KV Alaknanda GVK (UPC)- Vishnuprayag(UP) (UP) Ckt and 400 KV Muzaffarnagar(UP)-Vishnuprayag(UP) (UP) Ckt. During antecedent condition, 110 MW Vishnuprayag HPS - UNIT 1 & 3 were under running condition and were generating approx. 10MW and 46MW respectively. ii) As reported, at 02:49 hrs, 400 KV Alaknanda GVK (UPC)- Vishnuprayag(UP) (UP) Ckt and 400 KV Muzaffarnagar(UP)-Vishnuprayag(UP) (UP) Ckt tripped due to bus bar protection operation at Vishnuprayag end (exact reason of fault yet to be shared). iii) As further reported, fault distance was 120.76m from Alaknanda end. DT received at Alaknanda GVK (UPC) and Muzaffarnagar(UP) end and fault current was 1.77kA from Alaknanda(UP) end. Fault clearing time was ~58ms. iv) With the tripping of both the evacuating lines, 110 MW Vishnuprayag HPS - UNIT 1 and 3 tripped due to unavailability of power evacuating path. v) As per PMU at Muzaffarnagar(UP), B-N phase to earth fault with fault clearance time of 120 ms is observed. vi) As per SCADA, no change in demand in UP control area is observed. Generation loss of approx. 56MW is also observed at Vishnuprayag HEP. vii) After bus bar protection operation, an inspection was carried out and a foul smell was observed from B-phase CB at Vishnuprayag(UP) end of 400 KV Muzaffarnagar(UP)-Vishnuprayag(UP) (UP) Ckt, hence the line was taken under shutdown.	1) 400 KV Muzaffarnagar(UP)-Vishnuprayag(UP) (UP) Ckt 2) 400 KV Alaknanda GVK(UPC)-Vishnuprayag(UP) (UP) Ckt 3) 110 MW Vishnuprayag HPS - UNIT 1 4) 110 MW Vishnuprayag HPS - UNIT 3
12	GD-1	Rajasthan	18-Mar-2024 13:32	18-Mar-2024 15:53	02:21	850	0	1.608	0.000	52873	53887	i) Total power of 220/132KV AREPRL(IP) (i.e., 250MW+Azure:200MW and Renew:50MW) evacuates through 220 KV Bhadla(PG) Bhadla Solar(Adani) (Adani) Ckt-1 and 2. During antecedent condition, 220 KV Bhadla(PG) Bhadla Solar(Adani) (Adani) Ckt-1 and 2 were carrying approx. 118MW each. ii) As reported, at 13:32 hrs, 220 KV Bhadla(PG) Bhadla Solar(Adani) (Adani) Ckt-1 tripped on R-N phase to earth fault, occurred as conductor of 11kV line passing through the bottom of 220KV line snapped and fell on 220KV line. iii) After this, loading of 220 KV Bhadla(PG) Bhadla Solar(Adani) (Adani) Ckt-2 reached approx. 236MW. iv) Again at 13:38 hrs, 220 KV Bhadla(PG) Bhadla Solar(Adani) (Adani) Ckt-2 tripped on R-N phase to earth fault. Complete blackout occurred at 220/132KV AREPRL(IP). v) As per PMU at Bhadla(PG), B-N phase to earth fault is observed with fault clearing time of 120ms. vi) As per SCADA, change in NR total solar generation of approx. 850MW @13:32hrs and approx. 550MW @13:38hrs are observed.	1) 220 KV Bhadla(PG) Bhadla Solar(Adani) (Adani) Ckt-1 2) 220 KV Bhadla(PG) Bhadla Solar(Adani) (Adani) Ckt-2
13	GI-1	Jammu & Kashmir	18-Mar-2024 04:15	18-Mar-2024 06:15	02:00	0	225	0.000	0.560	33379	40178	i) 220/132KV Zankote S/s have two bus at 220KV side i.e., main bus & reserve bus. ii) During antecedent condition, 220KV Amargah(INDIGRID)-Zankote(K) D/C (carrying 162MW each) was feeding Zankote load. iii) As reported, at 04:15 hrs, 220 KV Amargah(INDIGRID) Zankote(K) (POD K) Ckt-1 tripped on R-N phase to earth fault from Zankote end only. But as per DR at Amargah end, current in R- and Y- phase increased upto ~0.8kA and ~1.4kA respectively. (Exact reason, nature and location of fault yet to be shared) iv) As further reported, at the same time, 220 KV Amargah(INDIGRID) Zankote(K) (POD K) Ckt-1 also tripped on R-N phase to earth fault from Zankote end only. But as per DR at Amargah end, current in B- phase increased upto ~1.0kA. (Exact reason, nature and location of fault yet to be shared) v) As per PMU at Amargah(PG), rise in B-ph voltage is observed. vi) As per SCADA, change in demand of approx. 225MW is observed in J&K control area.	1) 220 KV Amargah (INDIGRID)-Zankote(K) (POD K) Ckt-1 2) 220 KV Amargah (INDIGRID)-Zankote(K) (POD K) Ckt-2
14	GD-1	Himachal Pradesh	19-Mar-2024 19:18	19-Mar-2024 21:26	02:08	0	380	0.000	0.693	45527	54798	i) 220/66KV Uperanangal(IP) S/s have double main bus scheme at 220KV level. ii) During antecedent condition, 220 KV Nallagarh(PG)- Uperanangal (HP) (HPSEB) Ckt-1 & 2 were carrying 260MW each. 220 KV Baddi- Uperanangal (HP) Ckt was not in service (as per SCADA). iii) As reported, at 19:18 hrs, 220 KV Nallagarh(PG)- Uperanangal (HP) (HPSEB) Ckt-1 & 2 tripped on R-N phase to earth fault. (Exact reason, nature and location of fault yet to be shared) iv) As further reported, 220 KV Uperanangal(HP) Wardthinan (HPSEB) Ckt, 220/66KV 80/100MVA ICT-1 & 2 at Uperanangal(HP) also tripped during the same time (Exact reason, nature and location of fault yet to be shared). Complete blackout occurred at 220/66KV Uperanangal(HP) S/s. v) As per PMU at Nallagarh(PG), R-N phase to earth fault is observed with fault clearing time of 120ms. vi) As per SCADA, change in demand of approx. 380MW is observed in HP control area.	1) 220 KV Nallagarh(PG)- Uperanangal (HP) (HPSEB) Ckt-1 2) 220 KV Nallagarh(PG)- Uperanangal(HP) (HPSEB) Ckt-2 3) 220 KV Uperanangal(HP) Wardthinan (HPSEB) Ckt 4) 220/66KV 80/100MVA ICT-1 at Uperanangal(HP) 5) 220/66KV 80/100MVA ICT-2 at Uperanangal(HP)
15	GI-2	Haryana	21-Mar-2024 18:19	21-Mar-2024 19:33	01:14	0	0	0.000	0.000	44363	50373	i) During antecedent condition, 800KV HVDC Champa-Kurukshetra was carrying total 1440MW (Pole 01- 490MW, Pole 02- 490MW, Pole 03- 230MW, Pole 04- 230MW). ii) As reported at 18:19hrs, 800 KV HVDC Kurukshetra (PG) Pole-02 and Pole-04 tripped due to DC supply failure from Champa end (further details yet to be received from PowerGrid). iii) Due to tripping of two poles (Pole-02 and Pole-04), power order reduced from 1440MW to 1370MW and shifted to the other two Poles. iv) As per PMU, fluctuation in voltage was observed. v) As per SCADA, no change in demand is observed in Haryana control area.	1) 800 KV HVDC Kurukshetra(PG) Pole-02 2) 800 KV HVDC Kurukshetra(PG) Pole-04
16	GD-1	Haryana	23-Mar-2024 00:58	23-Mar-2024 02:45	01:47	0	170	0.000	0.404	35356	42057	i) 220/132/33KV Hissar(BB) S/s has double main bus scheme at 220KV level. ii) As reported, at 00:58hrs, burning of B-ph CT of 220/132KV 100MVA ICT-2 at Hissar(BB) occurred. iii) During the same time, all the lines and 220/132KV CTS connected at 220KV Hissar(BB) also tripped (Exact reason, nature and location of fault yet to be shared). iv) Due to tripping of all the elements connected to both the buses, both 220KV Bus-1 & 2 at Hissar(BB) and eventually the complete 220/132/33KV Hissar(BB) S/s became dead. v) As per PMU at Hissar(PG), two consecutive B-N phase to earth faults with fault clearing time of 80ms and 360ms (delayed) are observed. vi) As per SCADA, change in demand of approx. 170MW is observed in Haryana control area.	1) 220 KV Hissar(BB)-Hissar (AHV) (HVNL) Ckt-1 2) 220 KV Hissar(BB)-Hissar (AHV) (HVNL) Ckt-2 3) 220 KV Bhiwani-Hissar (BB) Ckt-1 4) 220 KV Bhiwani-Hissar (BB) Ckt-2 5) 220 KV Hissar-Songur (BB) Ckt-1 6) 220 KV Hissar-Songur (BB) Ckt-2 7) 220 KV Hissar(BB) Jindal Steel(HR) (HVNL) Ckt 8) 220 KV Hissar(BB) Chirawa(RS) (BB) Ckt 9) 220 KV Barnala-Songur(BB) Ckt 10) 220/132KV 100MVA ICT-1 at Hissar(BB) 11) 220/132KV 100MVA ICT-2 at Hissar(BB) 12) 220/132KV 100MVA ICT-3 at Hissar(BB)
17	GI-2	Haryana	27-Mar-2024 15:04	27-Mar-2024 16:16	01:12	0	0	0.000	0.000	50774	50034	i) During antecedent condition, 800KV HVDC Champa-Kurukshetra was carrying total 1460MW (approx. 365MW by each Pole). ii) As reported at 15:04hrs, 800 KV HVDC Kurukshetra (PG) Pole-02 and Pole-04 were blocked due to unavailability of Lane-1 and 2 caused by software issue at Champa end (further details yet to be received from PowerGrid). iii) Due to tripping of two poles (Pole-02 and Pole-04), power order slightly reduced from 1460MW to 1400MW and shifted to the other two Poles. iv) As per PMU, fluctuation in voltage was observed. v) As per SCADA, no change in demand is observed in Haryana control area.	1) 800 KV HVDC Kurukshetra(PG) Pole-02 2) 800 KV HVDC Kurukshetra(PG) Pole-04

20.Details of Grid Events during the Month of March 2024 in Northern Region



Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH-MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t. Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI Ior GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
18	GD-1	Rajasthan	29-Mar-2024 17:22	29-Mar-2024 18:54	01:32	0	120	0.000	0.239	47653	50240	i)Bt10/132kV Bhiwadi(RS) has double main bus scheme at 220kV side. ii)As reported, at 17:10hrs, 400 KV Khetri (PKTSL) Bhiwadi(PG) (PRTSL) Ckt-2 tripped on Y-N phase to earth fault during heavy wing storm with fault distance of 123.3km from Khetri and fault current of 2.34kA from Khetri and 39.7kA from Bhiwadi. iii)As per PMU at Bhiwadi(PG), at 17:10 hrs, Y-N phase to earth fault with unsuccessful A/R followed by R-N fault is observed with fault clearing time of 80ms and 80ms respectively. iv)As per SCADA SOE, 132 KV Bhiwadi(RS) Bhiwadi132(RS) (RS) Ckt-2 tripped at 17:17hrs (exact reason, nature and location of fault yet to be shared). As per PMU, Y-N phase to earth fault with fault clearing time of 80ms is observed during the same time. v)Further, at 17:22hrs, bus bar protection operated at 220kV Bhiwadi(RS) due to failure of B-phase CVT of 220kV Main Bus -II. Due to this, both 220 KV Bhiwadi(PG)-Bhiwadi(RS) (RS) Ckt-1 & 2 tripped from Bhiwadi(RS) end only. vi)Bt01/132kV 160MVA ICT-1 & 2 and 100MVA ICT-3 at Bhiwadi(RS) also tripped and supply to 132kV feeders connected to Bhiwadi(RS) lost. Complete blackout occurred at 220/132kV Bhiwadi(RS) 5/s. vii)As per PMU at Bhiwadi(PG), at 17:22hrs, B-N phase to earth fault is observed with fault clearing time of 120ms. viii)Again, at 17:26 hrs, 220 KV Bhiwadi(PG)-Kushkhara(RS) (RS) Ckt tripped on R-N phase to earth fault with fault distance of 0.865km from Bhiwadi(PG) end. ix)As per DR at Bhiwadi(PG) end of 220 KV Bhiwadi(PG)-Kushkhara(RS) (RS) Ckt, fault current was 24.41kA from Bhiwadi(PG), fault was sensed in zone-1, line was successfully auto-reclosed from Bhiwadi(PG) end and tripped only from Kushkhara end. x)As per PMU at Bhiwadi(PG), at 17:26 hrs, R-N fault followed by R-N fault with unsuccessful A/R is observed with fault clearing time of 120ms and 80ms respectively. xi)As per SCADA, change in demand of approx. 120MW in Rajasthan control area is observed.	1) 400 KV Khetri (PKTSL) Bhiwadi(PG) (PRTSL) Ckt-2 2) 220 KV Bhiwadi(PG) Bhiwadi(RS) (RS) Ckt-1 3) 220 KV Bhiwadi(PG) Bhiwadi(RS) (RS) Ckt-2 4) 220/132kV 160MVA ICT-1 at Bhiwadi(RS) 5) 220/132kV 160MVA ICT-2 at Bhiwadi(RS) 6) 220/132kV 100MVA ICT-3 at Bhiwadi(RS) 7) 220 KV Bhiwadi(PG) Kushkhara(RS) (RS) Ckt
19	GI-2	Haryana	29-Mar-2024 20:26	29-Mar-2024 21:02	00:36	0	0	0.000	0.000	43682	53455	i)During antecedent condition, 800kV HVDC Champa-Kurukshetra was carrying total 1450MW (Pole 01- 725MW, Pole 02- 365MW, Pole 03- 0MW, Pole 04- 360MW). ii)As reported at 20:26hrs, 800 KV HVDC Kurukshetra(PG) Pole-02 and Pole-04 tripped due to unavailability of Lane-1 and 2 caused by software issue at Champa end. Further details yet to be received from PowerGrid. iii)Due to tripping of two poles (Pole-02 and Pole-04), power order reduced from 1450MW to 1370MW and shifted to the Pole-01. iv)As per PMU, fluctuation in voltage was observed. v)As per SCADA, no change in demand is observed in Haryana control area.	1) 800 KV HVDC Kurukshetra(PG) Pole-02 2) 800 KV HVDC Kurukshetra(PG) Pole-04
20	GD-1	Rajasthan	29-Mar-2024 20:22	29-Mar-2024 21:58	01:36	2020	308	5.726	0.965	43506	53019	i)As reported, at 20:22hrs, R-ph CT (220 KV side) of 220 KV/132 KV ICT-1 at Kota Sakatpura blast. As per PMU, R-N fault converted into 3-ph fault with delayed clearance of 760msec is observed. ii)Bus bar protection is not available at Kota Sakatpura 5/s and 2-4 time delay setting is kept as 160msec. 2-2 time delay setting of 220kV KTPS-Sakatpura ckt-1,2,3 & 4 are kept as 160msec. iii)On this fault, 220kV feeders to RAPS-A-1, Ranpur & Mandalgarh from Kota Sakatpura tripped on 2-4 distance protection at Kota Sakatpura end. 220kV KTPS-Sakatpura ckt-1 & 3 also tripped on 2-2 distance protection operation at KTPS end. 220/132kV ICT-1 at Kota Sakatpura also tripped on differential protection operation. iv)Due to tripping of aforementioned 220kV lines, loading of remaining 220kV lines at KTPS & Kota Sakatpura increased significantly. Within approx. 400-700msec of fault, 220kV KTPS-Heerapura ckt and 220kV KTPS-Besawar ckt tripped on 2-1 distance protection operation after power swing detection, 220kV KTPS-Bundi ckt & 220kV Bundi-Gulabpura ckt and 220kV Kota Sakatpura-Anta ckt tripped on distance protection operation suspected due to load encroachment. v)Further, 220kV RAPS-C-Anta ckt and 220kV RAPS-B-Kota Sakatpura ckt also tripped on 2-1 distance protection operation after power swing detection. vi)Further, at approx. 20:22:10hrs, SUT-4 at RAPS-B tripped on over frequency protection operation (setting: 51.5Hz with 200msec delay). Auto transfer initiated and load transferred to UT-4 however it failed after 1 sec, as per Auto transfer scheme, resulting in one - one PCP tripping and reactor trip on PHT pressure high. vii)At the same time, SUT-5 & SUT-6 at RAPS-C tripped on over frequency (51.5 Hz with 200 msec time delay). Auto transfer scheme initiated in both Unit-5 & 6 however it failed due to frequency mismatch. Subsequently reactors of RAPS-S&B tripped on PHT pressure high. Highest frequency recorded was ~53.16Hz. viii)After aforementioned trippings, only RAPS-A unit-2 was available which was feeding 220kV Debari, 220kV Chittorgarh via 220kV RAPS-A-RAPS-B tie line and load at 220/132kV Kota Sakatpura via 220kV RAPS-A-Kota Sakatpura ckt-2. ix)Further at 20:28hrs, frequency decreased to 47.8Hz and 220kV RAPS-A-Kota Sakatpura ckt-2 tripped on under frequency as per islanding scheme. x)With this tripping, system with RAPS-A unit-2 and load at Debari & Chittorgarh got islanded. RAPS-A generation was reduced to 160MW. Island operated till approx. 22:47hrs, frequency of island was maintained in the range of 51-52Hz and voltage was in the range of 230-240kV. Further, at ~22:47hrs, RAPS-A unit-2 turbine generator tripped on over fluxing (~112.5%), voltage recorded just before the tripping was ~282kV. xi)As per SCADA, total generation loss of approx. 2000MW is observed and at the same time load loss of approx. 300MW is observed in Rajasthan control area.	1)810 MW Kota TPS Unit-1, & 2 2)810 MW Kota TPS Unit-3, 4 & 5 3)815 MW Kota TPS Unit-6 & 7 4)820kV KTPS-Kota Sakatpura ckt-1 & 3 5)820kV KTPS-Besawar ckt 6)820kV KTPS-Bundi ckt 7)820kV KTPS-Heerapura ckt 8)820kV Kota Sakatpura-RAPS-A ckt-1 & 2 9)820kV Kota Sakatpura-Mandalgarh ckt 10)820kV Kota Sakatpura-RAPS-B ckt 11)820kV Kota Sakatpura-Anta ckt 12)820kV Kota Sakatpura-Ranpur ckt 13)820kV RAPS-C-Anta ckt 14)800MW RAPS-A Unit-2 15)820 MW RAPS-B Unit-4 16)820 MW RAPS-C Unit-5 & 6

20.Details of Grid Events during the Month of March 2024 in Western Region													
Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t. Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI for GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-1	WR	00:07 / 04-03-2024	06:32 / 04-03-2024	06:25	162	-	0.27%	-	59749	52197	At 00:07 Hrs/ 04.03.2024, 220kV Bhuj Gadhisia line tripped on R-E fault. On patrolling, it was found a foreign material (conductor) fell on the line conductor at tower No.3/2. At the same time, 220kV Bhuj-Baranda s/c tripped on R-E fault from Baranda end only.Wind generation loss of 122 MW at Gadhisia & 40 MW at Baranda reported.	1. 220kV Bhuj Gadhisia line 2. 220kV Bhuj Baranda
2	GD-1	WR	23:04 / 04-03-2024	14:55 / 05-03-2024	15:51	-	-	-	-	65030	55459	As informed by Pachora substation Pachora (GRInfra) had taken outage in 400 KV Bhopal-Pachora-1 for Isolator alignment issue. For 400 KV Bhopal-Pachora-1 of line after completion of work, Pachora Bus Reactor was being opened, at 23:04 hrs / 04-03-2024, during opening of bus reactor their was issue in isolator of 411 bay at Pachora. IPS tube fell over at 411 (The bay of 400 KV Bhopal-Pachora-2) at Pachora and 410 Bay at Pachora (Main bay of 400 KV Bhopal-Pachora-2) and DT was sent to Bhopal end. At Bhopal Circuit breaker of 413 Bay Blasted due to falling of IPS tube and busbar protection operated at 400 KV Bhopal-BDTCL and 400 KV station became dead. No load loss / generation loss occurred due to the event.	Tripping of following Elements: 1. 400KV Bhopal- Pachora Ckt-2 2. 400KV Bhopal-Bhopal (MP) Ckt-1&2 3. 765/400KV ICT - 1 & 2 at Bhopal BDTCL 4. 400KV Bus- 1 & 2 at Bhopal BDTCL
3	GD-1	WR	15:35 / 05-03-2024	16:24 / 05-03-2024	00:49	174	-	0.25%	-	70296	63144	At 15:35 Hrs/ 05.03.2024, 220 KV Rewa Barsatadesh - 2 tripped at Barsatadesh end only due to master trip relay operated at Barsatadesh leading to black out of 220 KV Barsatadesh substation. Since Ckt-1 was taken out few seconds back for availing planned S/D for power quality meter installation. Both the lines were in charged condition from Rewa end. Due to above incident solar generation loss of 174 MW reported at Barsatadesh (Arisun).	1. 220kV Barsatadesh Rewa - 2 2. 220KV/33KV Barsatadesh ICT - 1 3. 220KV/33KV Barsatadesh ICT - 2 4. 220KV/33KV Barsatadesh ICT - 3
4	Near Miss	WR	10:31 / 11-03-2024	10:53 / 11-03-2024	00:22	-	752	-	1.07%	76933	70410	At 10:31 hrs / 11-03-2024, 400 KV Pune-LoniKhand 1 tripped on R-E fault due to sugarcane burning by farmer between location 60-61. Same time 400 KV Pune-Chakan tripped due to maloperation of Main-2 relay at Chakan. 210 element operated and B phase tripped and remaining poles tripped after 1.5 seconds on pole discrepancy operation. On inspection it was found that Main-2 at Chakan end of 400 KV Pune-Chakan line maloperated. Load loss of 752 MW occurred due to the event (436 MW load relief due to LTS operation in 220 KV Chinchwad-Unse, 220/132 KV ICTs at Alepheta, 220 KV Pune-Unse-D/C and 400 KV Pune-Chakan (During charging, around 179 MW load relief at Shirur, Theur, Markai and Sanawadi due to under voltage stage-1&2 scheme at LoniKhand and 137 MW load shedding implemented for charging of 400 KV Pune-Chakan).	Tripping of following Elements: 1. 400 KV Pune-LoniKhand 1 2. 400 KV Pune-Chakan
5	GI-2	WR	23:06 / 13-03-2024	01:13 / 14-03-2024	02:07	-	-	-	-	72885	61986	At 23:06 hrs / 13-03-2024, Y phase Bus-2 side current transformer of bus coupler at 400 KV Kansari caught fire resulting in Bus bar protection operation of 400 KV Kansari-Bus-1 and 400 KV Kansari-Bus-2 and tripping of all connected elements. With these tripping 400 KV side at Kansari became dead and 220 KV side was intact. No load loss occurred during the event.	Tripping of following Elements: 1. 400 KV Banskanthe Kansari 2. 400 KV Chankarika-Kansari-1&2 3. 400 KV Soja-Kansari-1,3&4 4. 400 KV Kansari-Kankrob-1&2 5. 400 KV Kansari-Veluda 6. 400/220 KV Kansari-ICT-1,2,3&4 (315 MVA) 7. 400 KV Kansari-Bus-1&2
6	GD-1	WR	00:48 / 18-03-2024	04:27 / 18-03-2024	03:39	922	-	1.36%	-	67727	56241	At 21:33 hrs /17-03-2024, 765 KV Durg-Bus Reactor-1 tripped on differential protection operation due to Y phase CT failure of Bus Reactor resulting in tripping of 765 KV Durg-Bus-2, 765 KV Durg-Wardha-3 tripped due to DT receipt at Wardha end, Over voltage stage-1 operated at Wardha end and DT sent to Durg end. 765 KV Durg-Wardha-4 tripped due to DT receipt at Wardha end. 765 KV Durg-Kotra-1 tripped due to Line reactor REF protection operation at Durg end. At 00:48 hrs /18-03-2024, flashover occurred in Line Isolator of 765 KV Durg-Itharaguda 2 (Line was under outage due to voltage regulation). The fault was not cleared by STUB protection because fault current was less than pickup value and all lines connected to 765 KV Durg tripped from remote ends. 765 KV Durg-Itharaguda-1 tripped due to Directional Earth Fault Protection operation at Itharaguda end. 765 KV Durg-Rajanaadgaon-1&2 tripped on TEF protection at Rajanaadgaon end and DT receipt at Durg. 765 KV Durg-Champa-2 tripped due to DEF Protection operation at Champa end. 765 KV Durg-Kotra-2 tripped from Kotra end on Zone 3 Protection. Due to no voltage source at Durg end 765/400 KV Durg-ICT-1&2 and 765 KV Durg-Bus-1 became dead. Generation loss of around 922 MW occurred at Rajpur Energen Limited due to loss of evacuation path.	Tripping of following Elements: 1. 765 KV Durg-B/R 2. 765 KV Durg-Bus-2 3. 765 KV Durg-Wardha-3&4 4. 765 KV Durg- Kotra 1 B. Incident-2 1. 765 KV Durg-Itharaguda-1 2. 765 KV Durg-Rajanaadgaon-1&2 3. 765 KV Durg-Champa-2 4. 765 KV Durg-Kotra-2
7	GD-1	WR	08:53 / 19-03-2024	11:01 / 19-03-2024	02:08	10	-	0.01%	-	74812	64831	At 08:53 Hrs/ 19.03.2024, 220/33kv ICT 1 Srijan Wind RE Tripped due to LBB operation via feeder 4 resulting in loss of evacuation path and generation loss of 10 MW reported.	220/33kv ICT 1 at Srijan Wind RE
8	GD-1	WR	11:58 / 20-03-2024	12:57 / 20-03-2024	00:59	0.8	-	0.00%	-	73937	66129	At 11:58 Hrs/ 20.03.2024, 220 KV Bhuj Kotda madh line tripped at Kotda madh end only due to false DT signal received at Kotda madh end. Generation loss of 0.8 MW reported.	220 KV Bhj Kotda madh line
9	GD-1	WR	05:51 / 22-03-2024	06:42 / 22-03-2024	00:51	118	-	0.15%	-	77179	69196	At 05:51 Hrs/ 22.03.2024, 220KV-Indore-58E5 (Pritamnagar) Ckt tripped on R-G fault from Pritamnagar end only. Generation loss of 118 MW reported due to loss of evacuation path.	220 KV 58E5 PRITAMNAGAR INDORE
10	GD-1	WR	01:28 / 25-03-2024	02:31 / 25-03-2024	01:03	130	-	0.20%	-	64274	57350	At 01:28 Hrs / 25-03-2024, 220 KV-Indore-Pritamnagar(AWEMP19N) tripped on R-E fault from Pritamnagar end due to Voltage Transformer fuse failure at Indore end, auto recloser successful at Indore end. During patrolling OPGW suspension clamp at Tower 26/s was found open. Generation loss of 130 MW at Pritamnagar(AWEMP19N) reported due to loss of evacuation path.	Tripping of following Elements: 1. 220 KV Indore-Pritamnagar(AWEMP19N)
11	GD-1	WR	15:21 / 29-03-2024	15:55 / 29-03-2024	00:34	160	-	0.20%	-	79574	70554	At 15:21 Hrs / 29-03-2024, 400 KV JP Bina-Bina (PG) tripped on Y-E fault and at same time 400 KV JP Bina-Bina (MP) tripped on B-E fault from Bina(MP) end only, auto recloser successful at JP Bina end. Both the lines are in same tower. Heavy rain and thunderstorm were reported at the time of tripping. Generation loss of 160 MW occurred at JP Bina due to loss of evacuation path.	Tripping of following Elements: 1. 400 KV JP Bina-Bina (PG) 2. 400 KV JP Bina-Bina (MP) 3. JP Bina unit-2 (250 MW)
12	GD-1	WR	22:28 / 30-03-2024	23:50 / 30-03-2024	01:22	804	-	1.05%	-	76228	62984	At 22:28 Hrs / 30-03-2024, 400 KV Mahan Energen-Bilaspur-1&2 on R-E fault and R-Y phase to phase fault. No abnormality found during patrolling. Heavy rain and thunderstorm were reported at the time of tripping. Generation loss of 804 MW occurred at Mahan Energen Limited due to loss of evacuation path.	Tripping of following Elements: 1. 400 KV Mahan Energen-Bilaspur-1&2 2. Mahan Energen-Unit-1&2 (600 MW)
13	GD-1	WR	01:36 / 31-03-2024	02:13 / 31-03-2024	00:37	35	-	0.05%	-	73889	61724	At 01:36 Hrs / 31-03-2024, 220KV Kotda madh-Bhuj tripped at Kotda madh end only on DT receipt. From PMU plots, it was observed that no fault was there in the system and the tripping was undesirable, DT received at Kotda Madh end without any protection operation at Bhuj end. Generation loss of 35 MW occurred at 220 KV Kotda madh (Alfarar) WPP due to the loss of evacuation path.	Tripping of following Elements: 1. 220KV Kotda madh-Bhuj

20.Details of Grid Events during the Month of March 2024 in Southern Region



Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	Generation Loss(MW)					Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)			
1	GD-1	Karnataka	16-03-2024 13:28	16-03-2024 14:15	0:47	0	380	0.00%	0.60%	53982	62981	Complete outage of 220kV/66kV Davanagere SS, 220kV/66kV Hosadurga SS, 220kV/66kV Benikere SS and Tripping of 220kV Bus-1 of 220kV/66kV Honnali SS of KPTCL: During the antecedent conditions 220kV/66kV Davanagere SS, 220kV/66kV Hosadurga SS, 220kV/66kV Benikere SS and 220kV Bus-1 of 220kV/66kV Honnali SS were being radially fed through 400kV/220kV Guttur SS through 220kV Guttur-Davanagere-1,2 and 3 lines. The triggering incident is the suspected fault in 66kV network downstream to Davanagere leading to the tripping of 220kV Guttur-Davanagere-2 & 3 due to the logic issue wherein I-2 was given trip without any time delay at Guttur end. Owing to which load being shifted on Guttur-Davanagere-1. Subsequently after around 2 sec from line-2,3 tripping, 220kV Guttur-Davanagere-1 tripped on I-2 at Davanagere end. Tripping of 220kV Guttur-Davanagere-1,2&3 lead to the complete outage of 220kV/66kV Davanagere SS, 220kV/66kV Hosadurga SS, 220kV/66kV Benikere SS and Tripping of 220kV Bus-1 of 220kV/66kV Honnali SS of KPTCL.	1. 220kV Guttur-Davanagere-1,2&3
2	GD-1	Karnataka	16-03-2024 15:39	16-03-2024 16:14	0:35	0	380	0.00%	0.60%	54025	63381	Complete outage of 220kV/66kV Davanagere SS, 220kV/66kV Hosadurga SS, 220kV/66kV Benikere SS and Tripping of 220kV Bus-1 of 220kV/66kV Honnali SS of KPTCL: During the antecedent conditions 220kV/66kV Davanagere SS, 220kV/66kV Hosadurga SS, 220kV/66kV Benikere SS and 220kV Bus-1 of 220kV/66kV Honnali SS were being radially fed through 400kV/220kV Guttur SS through 220kV Guttur-Davanagere-1,2 and 3 lines of which line-2 was under forced outage. The triggering incident is the tripping of 220kV Guttur-Davanagere-1,2,3 leading to the complete outage of 220kV/66kV Davanagere SS, 220kV/66kV Hosadurga SS, 220kV/66kV Benikere SS and Tripping of 220kV Bus-1 of 220kV/66kV Honnali SS of KPTCL.	1. 220kV Guttur-Davanagere-1,2&3
3	GD-1	Karnataka	19-03-2024 10:37	19-03-2024 11:15	00:38	0	186	0.00%	0.29%	53384	65093	Complete Outage of 220kV/110kV Bagalkot SS and Outage of 220kV Bus-1 of 220kV/110kV Vijaynagar SS of KPTCL: As per the reports submitted, the triggering incident was Y-phase CVT flashover in 220kV Bagalkot Vijaynagar Line-2 at Bagalkot end. Subsequently due to which R-ph CT flash over was observed in 220kV Bagalkot Vijaynagar Line-1 at Bagalkot end but due to DC issue the fault was not cleared at Vijaynagar and SC, 220kV Kudligi-Vijaynagar-1 and 220kV Mahalingapur-Vijaynagar-1 tripped at remote ends to clear the fault. Subsequently, Y-B bus fault is observed at Bagalkot end and due to non-availability of bus bar protection all the remote ends at Bagalkot end on Z2 leading to complete outage of 220kV/110kV Bagalkot SS and Outage of 220kV Bus-1 of 220kV/110kV Vijaynagar SS of KPTCL.	1. 220kV Vijaynagar Bagalkot line-1&2 2. 220kV Vijaynagar Kudligi line-1 3. 220kV Karakudi Kaverur Line-1,2,3&4 4. 220kV Gadag Bagalkot Line-1&2
4	GD-1	Tamil Nadu	19-03-2024 11:27	19-03-2024 11:52	00:25	0	53	0.00%	0.08%	53293	64897	Complete Outage of 230kV/110kV Karakudi_TN of TANTRANSO: As per the reports submitted, the triggering incident was an R-phase jumper failure between the Line switch to the breaker of 230kV Karakudi_PG Karakudi_TN line-1 at Karakudi_TN SS. Immediately, 230kV BBP operated and all the lines connected to be bus tripped except 230kV Karakudi NT Kudli Line-1. 230kV Karakudi NT Kudli Line-1 tripped on suspected delayed operation of 86 Relay. Subsequently, at 11:28hrs, 110kV Karakudi Vaidhathur Line tripped on line to ground fault. Tripping of the only source led to the outage of the 110kV system of 230kV/110kV Karakudi_TN SS which in turn led to complete outage of 230kV/110kV Karakudi SS.	1. 230kV Karakudi_TN Karakudi_PG Line-1&2 2. 230kV Karakudi NT Kudli line 3. 230kV Karakudi Kaverur Line-1,2,3&4 4. 230kV/110kV Karakudi Auto Transformer -1
5	GD-1	Karnataka	20-03-2024 10:30	20-03-2024 10:41	00:11	0	200	0.00%	0.31%	52871	64448	Complete outage of 220kV/66kV Davanagere SS, 220kV/66kV Hosadurga SS, 220kV/66kV Benikere SS and Tripping of 220kV Bus-1 of 220kV/66kV Honnali SS of KPTCL: During the antecedent conditions 220kV/66kV Davanagere SS, 220kV/66kV Hosadurga SS, 220kV/66kV Benikere SS and 220kV Bus-1 of 220kV/66kV Honnali SS were being radially fed through 400kV/220kV Guttur SS through 220kV Guttur-Davanagere-1,2 and 3 lines of which line-1 was under forced outage. The triggering incident is the tripping of 220kV Guttur-Davanagere-2&3 leading to the complete outage of 220kV/66kV Davanagere SS, 220kV/66kV Hosadurga SS, 220kV/66kV Benikere SS and Tripping of 220kV Bus-1 of 220kV/66kV Honnali SS of KPTCL.	1. 220kV Guttur-Davanagere-1,2&3
6	GD-1	Karnataka	23-03-2024 11:42	23-03-2024 12:01	00:19	0	400	0.00%	0.62%	54238	64551	Complete outage of 220kV/66kV Davanagere SS, 220kV/66kV Hosadurga SS, 220kV/66kV Benikere SS and Tripping of 220kV Bus-1 of 220kV/66kV Honnali SS of KPTCL: During the antecedent conditions 220kV/66kV Davanagere SS, 220kV/66kV Hosadurga SS, 220kV/66kV Benikere SS and 220kV Bus-1 of 220kV/66kV Honnali SS were being radially fed through 400kV/220kV Guttur SS through 220kV Guttur-Davanagere-1,2 and 3 lines of which line-1 was under forced outage. The triggering incident is the tripping of 220kV Guttur-Davanagere-2&3 leading to the complete outage of 220kV/66kV Davanagere SS, 220kV/66kV Hosadurga SS, 220kV/66kV Benikere SS and Tripping of 220kV Bus-1 of 220kV/66kV Honnali SS of KPTCL.	1. 220kV Guttur-Davanagere-1,2&3
7	GD-1	Karnataka	29-03-2024 22:47	30-03-2024 01:43	02:56	0	140	0.00%	0.25%	45815	55625	Complete Outage of 220kV/110kV/11kV Raichur_KA SS of KPTCL: 220kV Upper Jurala PH of TSENCO: During antecedent conditions, 220kV Upper Jurala PH was being radially fed from 220kV/110kV/11kV Raichur_KA SS. As per the reports submitted, the triggering incident was fire in 110kV/11kV Transformer-6 of 220kV/110kV/11kV Raichur_KA SS. Other transformers tripped on high set earth fault protection and 220kV Raichur_KA RTPS lines tripped from remote ends. This resulted in complete outage of 220kV/110kV Raichur_KA SS which in turn resulted in complete outage of 220kV Upper Jurala PH.	1. 220kV Raichur_KA RTPS Line-1&2 2. 110kV/11kV Raichur_KA Transformer-4,5&6
8	GD-1	Karnataka	31-03-2024 16:12	31-03-2024 19:48	03:36	0	0	0.00%	0.00%	45515	59140	Complete Outage of 220kV Pulichinhala Generating station of TSENCO: As per the reports submitted, the triggering incident is B-N fault in 220kV Pulichinhala Seethapuram line. During Auto Reclosure dead time due to a problem in single phase tripping circuit of 220 KV Seethapuram line, LBB operated causing all the 220kV lines connected to 220kV Bus of 220kV Pulichinhala Generating station.	1. 220kV Chilikallu Pulichinhala 2. 220kV Pulichinhala Seethapuram
9	GD-1	Karnataka	31-03-2024 11:36	31-03-2024 18:59	07:23	0	0	0.00%	0.00%	45815	55625	Complete outage of 220kV Bettedaverekere US of KPTCL: 220kV Bettedaverekere US is tapped from 220kV Shimoga Anthraasnahalli Line. The triggering incident was B-N fault in 220kV Shimoga Anthraasnahalli Line. Tripping of the line resulted in complete outage of 220kV Bettedaverekere US.	1. 220kV Shimoga Anthraasnahalli Line
10	GI-2	Tamil Nadu	07-03-2024 13:59	10-03-2024 11:03	21:02	0	0	0.00%	0.00%	50578	64916	Tripping of 765kV Bus section-3 at 765kV/400kV NCPS GIS of TANTRANSO: As per the reports submitted, the triggering incident was misoperation of BBP in 765kV Bus section-13 at 765kV/400kV NCPS. Immediately, all the elements connected to the bus tripped.	1. 765kV NCPS NCTPSTG3-2
11	GI-2	Karnataka	12-03-2024 07:19	12-03-2024 11:09	03:50	0	0	0.00%	0.00%	45003	58825	Tripping of 400kV Bus-1 of 400kV/220kV Guttur SS of KPTCL: As per the reports submitted, the triggering incident was R-N fault in 400kV Guttur Bus-1. Immediately, BBP operated and all the elements connected to the bus tripped.	1. 400kV Kaiga Guttur Line-1&2 2. 400kV Guttur Narendra Line-1&2 3. 400kV Guttur RTPS Line 4. 400kV Guttur Hingur Line 5. 400kV/220kV Guttur ICT-1

20.Details of Grid Events during the Month of March 2024 in Eastern Region



Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI 1or GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD-1	Begusarai	05.03.2024 11:56	05.03.2024 12:25	00:29	0	100	0.00%	0.51%	25304	19707	At 11:56 Hrs on 05.03.2024, Y, B, N fault occurred in 220 kV Begusarai-KOC-1, which was kept idle charged from Begusarai end. Distance protection operated at Begusarai but the breaker didn't open. Since LBB and bus bar protection is not available at Begusarai, other feeders tripped in Zone-3 from remote ends and total power failure occurred at Begusarai S/s. Around 100 MW load loss reported at Begusarai.	220 kV Begusarai-Barauni D/c 220 kV Begusarai-Saharsa D/c
2	GD-1	Budhipadar	09.03.2024 14:07	09.03.2024 14:52	00:45	620	100	2.38%	0.50%	26093	19888	At 13:45 Hrs on 9th March 2024, 220 kV Budhipadar-Lapanga-2 tripped due to B-Earth fault. Loading of Budhipadar-Lapanga-1 reached around 350 MW, which was hand-tripped at 14:00 Hrs. Entire Budhipadar complex generation with IBTPS and Vedanta, SMC, Bhushan Steel, AAI, Concast CPPs started evacuating through remaining interconnection with grid through 220 kV Budhipadar-Raigarh and 220 kV Budhipadar-Korba D/C, which tripped one by one due to high loading and at 14:07 Hrs, this complex was isolated from the grid and formed an island which didn't survive due to large load generation imbalance. Net generation loss of around 620 MW occurred and load loss of around 100 MW occurred.	220 kV Budhipadar-Lapanga-2 220 kV Budhipadar-Lapanga-1 132 kV Budhipadar-Lapanga-1 220 kV Budhipadar-Raigarh-1 220 kV Budhipadar-Korba-1 220 kV Budhipadar-Korba-2 220 kV Budhipadar-IBTPS-1&2 220 kV Budhipadar-IBTPS-3&4 220 kV Budhipadar-Vedanta-1&2 UR1 & UR2 at IBTPS
3	GD-1	Garhwa	30.03.2024 22:27	30.03.2024 23:35	01:08	0	80	0.00%	0.31%	31097	26025	At 22:27 Hrs on 30.03.2024, 220 kV Daltonganj - Garhwa (New) D/C tripped due to single Phase to ground fault leading to total power failure at 220 kV Garhwa S/s with a load loss of around 80 MW. As per SLDC Jharkhand, the lines tripped due to inclement weather conditions in the area.	220 kV Daltonganj-Garhwa D/c
4	GI-2	Barh	31.03.2024 04:41	31.03.2024 07:00	02:19	1251	0	4.28%	0.00%	29220	27969	At 04:41 Hrs on 31.03.2024, 400 kV Bus-3 & Bus-4 at Barh tripped. As reported, B_ph CT of main bay of Barh-Patna-2 burst at Barh end and at that time 400 kV Bus-3 & Bus-4 and all associated elements tripped including U&S (660 MW each). Total generation loss of around 1251 MW occurred.	400 kV Barh-Mothari-1 400 kV Barh-Mothari-2 400 kV Barh-Patna-1 400 kV Barh-Patna-2 400 kV Barh-Kahalgaoon-1 400 kV Barh-Kahalgaoon-2 400 kV Bus-3&4 at Barh Barh Unit-4 (660 MW) Barh Unit-5 (660 MW)
5	GD-1	Garhwa(New)	31.03.2024 07:29	31.03.2024 07:36	00:07	0	30	0.00%	0.15%	27709	19938	At 07:29 Hrs on 31.03.2024, 220 kV Daltonganj-Garhwa(New)-1 tripped due to B, N fault which led to total power failure at 220 kV Garhwa(New) S/s as 220 kV Daltonganj-Garhwa (New)-2 was already under breakdown. Charging attempt of ckt-1 also failed at 08:06 Hrs. Presently both lines are under breakdown condition. Only Traction load was managed through 132 kV Garhwa- Japla T/L by 07:36 Hrs. Other loads have not been restored yet.	220 kV Daltonganj-Garhwa-1
6	GD-1	Bantala (KLC)	31.03.2024 21:49	31.03.2024 22:00	00:11	0	78	0.00%	0.30%	32052	25701	At 21:49 Hrs on 31.03.2024, Y-Ph CT of 220 kV New Town AA3- Bantala burst at Bantala end leading to tripping of the said line. At the same time 220 kV Subhasgram- Bantala also tripped from Subhasgram end with Y-Ph fault leading to total power failure at 220 kV Bantala S/s with a load loss of 78 MW.	220 kV Subhasgram-Bantala 220 kV New Town AA 3-Bantala

20.Details of Grid Events during the Month of March 2024 in North-East Region													
Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(G-I for GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
1	GD1	Sonabil, Ghoramari, Depota, Rowta, Dhekiajuli and Tangla areas of Assam Power system	04-03-2024 13:07	04-03-2024 13:33	00:26:00	0	38	0.00%	2.00%	1562	1904	Sonabil, Rowta, Depota, Ghoramari, Dhekiajuli and Tangla areas of Assam Power System were connected with rest of NER Grid through 220kV Balipara-Sonabil II line. 220 kV Sonabil-Balipara-1 line, 132 kV Rangia- Tangla Line, 132 kV Rangia- Sipahar Line was under outage prior to the event. At 13:07 Hrs of 04.03.2024, 220 kV Balipara-Sonabil II tripped. Due to tripping of this element, SPS at Sonabil operated due to which 200/132 kV ICT-1 & II at Sonabil tripped and Sonabil, Rowta, Depota, Ghoramari, Dhekiajuli and Tangla areas and Rowta Solar Generation of Assam Power System were isolated from NER Grid and collapsed due to load generation mismatch in these areas. Power supply was extended to Sonabil, Rowta, Depota, Ghoramari, Dhekiajuli and Tangla areas of Assam Power System by charging 220/132kV 100MVA ICT-1 at Sonabil at 13:33 Hrs of 04.03.2024.	220 kV Balipara-Sonabil II, 220/132 kV 100 MVA ICT-1 & II at Sonabil
2	GD1	Churachandpur and Thanlon areas of Manipur Power system	05-03-2024 13:25	05-03-2024 13:34	00:09:00	0	8	0.00%	0.46%	1810	1730	Churachandpur and Thanlon areas of Manipur Power system were connected to the rest of the grid through 132 kV Ningthoukhong-Churachandpur D/C lines. 132 kV Ningthoukhong-Churachandpur line is under outage since 13.01.2024. At 13:25 Hrs of 05.03.2024, 132 kV Lokat-Ningthoukhong and 132 kV Ningthoukhong-Churachandpur lines tripped. Due to tripping of these elements, Churachandpur and Thanlon areas of Manipur power system got isolated from rest of the grid due to no source available in these areas. Power supply was extended to Churachandpur, Thanlon and Elangangkopki areas by charging 132 kV Ningthoukhong-Churachandpur II line at 13:34 Hrs of 05.03.2024.	132 kV Lokat-Ningthoukhong and 132 kV Ningthoukhong-Churachandpur II lines
3	GD1	Pasighat area of Arunachal Pradesh Power system	07-03-2024 15:46	07-03-2024 17:26	01:40:00	0	5	0.00%	0.25%	1796	1973	Pasighat area of Arunachal Pradesh Power system was connected with the rest of the grid through 132 kV Along-Pasighat & 132 kV Roing-Pasighat lines. At 15:46 Hrs of 07.03.2024, 132 kV Along - Pasighat and 132kV Pasighat - Roing lines tripped. Due to tripping of these lines, Pasighat area of Arunachal Pradesh Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Pasighat area of Arunachal Pradesh Power System by charging 132kV Pasighat - Roing line at 17:26 Hrs of 07.03.2024.	132 kV Roing-Pasighat & 132 kV Along-Pasighat lines
4	GD1	NRPP & LRPP generation of Assam Power system	08-03-2024 14:56	08-03-2024 17:43	02:47:00	157	0	9.21%	0.00%	1705	1832	NRPP Generating Station of Assam Power System was connected with rest of NER Grid through 220kV Tinsukia-NRPP and 220 kV NTPS-NRPP lines. At 14:56 Hrs of 08.03.2024, 220kV Tinsukia-NRPP and 220 kV NTPS-NRPP lines tripped. Due to tripping of these lines, NRPP Generating Station was isolated from NER grid and collapsed due to load generation mismatch in this area. At the same time, LRPP generating units also tripped due to voltage collapse. Power supply was extended to 220kV NRPP Generating Station of Assam Power System by charging 220kV Tinsukia-NRPP line at 17:43 Hrs of 08.03.2024.	220 kV Amguri-NTPS, 220 kV NTPS-NRPP, 220 kV NTPS-Tinsukia lines, NRPP Unit-I & II and LRPP Unit-1,2,3,4,5,6,7
5	GD1	Dharmanagar area of Tripura Power system	10-03-2024 10:24	10-03-2024 11:54	01:30:00	0	13	0.00%	0.71%	1855	1843	Dharmanagar area of Tripura Power System is connected with the rest of the grid by 132 kV Dharmanagar-Dullachhera & 132 kV Dharmanagar-PK Bari lines. 132 kV Dharmanagar-PK Bari line tripped at 10:18 Hrs of 10.03.2024. At 10:24 Hrs of 10.03.2024, 132 kV Dharmanagar-Dullachhera line also tripped. Due to tripping of this element, Dharmanagar area of Tripura Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Dharmanagar area of Tripura Power System by charging 132 kV Dharmanagar-PK Bari line at 11:54 Hrs of 10.03.2024.	132 kV Dharmanagar-Dullachhera lines
6	GD1	Wokha area of Nagaland Power system	12-03-2024 10:30	12-03-2024 11:05	00:35:00	0	5	0.00%	0.25%	1758	2020	Wokha area of Nagaland Power System was connected with rest of NER Grid through 132 kV Wokha-Sanis and 132 kV Wokha-Chiephebozou lines. At 10:30 Hrs of 12.03.2024, 132 kV Wokha-Sanis and 132 kV Wokha-Chiephebozou lines. Due to tripping of this element, Wokha area of Nagaland Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Wokha area of Nagaland Power System by charging 132 kV Wokha-Sanis line at 11:05 Hrs of 12.03.2024. 132 kV Wokha-Chiephebozou line was charged at 11:45 Hrs of 12.03.2024.	132 kV Wokha-Chiephebozou & 132 kV Wokha-Sanis lines
7	GD1	Sarusajai, Kahelipara, AIIMS, Kamakhya and Dispur areas of Assam Power system	16-03-2024 05:57	16-03-2024 06:33	00:36:00	0	115	0.00%	6.21%	1680	1853	Sarusajai, Kahelipara, AIIMS, Kamakhya and Dispur areas of Assam Power System were connected with rest of the NER grid through 220kV Sarusajai - Mirza II, 220kV Sarusajai - Jawaharnagar, 220kV Sarusajai - Sonapur and 132kV Dispur - Chandrapur lines. At 05:57 Hrs, 220kV Sarusajai - Mirza II, 220kV Sarusajai-Jawaharnagar, 220kV Sarusajai-Sonapur and 132kV Dispur -Chandrapur lines tripped leading to blackout of 220kV Sarusajai S/S, 132kV Kahelipara S/S, 132kV AIIMS S/S, 132kV Kamakhya S/S and 132kV Dispur S/S. 220kV Sarusajai Bus-1, 220kV Sarusajai - Mirza I was under PSD for Bay reconducting work of 220kV Sarusajai - Mirza I at Sarusajai end from 05:55 Hrs of 16.03.2024.132kV Kamakhya - Sishugram and 132kV AIIMS-Amingaon lines were in opened condition to avoid overloading of 220kV Rangia ICT. As Reported by SDC Assam telephonically, 220kV Bus II at Sarusajai energized at 06:12 Hrs by charging 220kV Sarusajai - Mirza II, then Power extended to Kahelipara S/S at 06:31. Power was restored to Dispur by charging 132kV Dispur - Chandrapur at 06:30 Hrs. Power restored to Kamakhya S/S at 06:17 Hrs by charging 132kV Sarusajai -Kamakhya line. Power fully restored to Sarusajai Area at 06:33 Hrs. Power Extended to AIIMs at 06:53 Hrs.	220kV Sarusajai - Mirza II, 220kV Sarusajai-Jawaharnagar, 220kV Sarusajai-Sonapur and 132kV Dispur -Chandrapur lines
8	GD1	Dharmanagar area of Tripura Power system and Dullavchhera area of Assam Power system	16-03-2024 15:54	16-03-2024 16:31	00:37:00	0	18 MW in Dharmanagar & 13 MW in Dullavchhera	0.00%	1.33%	2000	2326	Dharmanagar area of Tripura Power System and Dullavchhera area of Assam Power System were connected with rest of NER Grid through 132 kV Dharmanagar - PK Bari line and 132 kV Dullavchhera-Halakandi line. At 15:54 Hrs of 16.03.2024, 132 kV Dharmanagar - PK Bari line, 132 kV Dharmanagar-Dullavchhera & 132 kV Dullavchhera-Halakandi lines tripped. Due to tripping of these lines, Dharmanagar area of Tripura Power System and Dullavchhera area of Assam power system were isolated from NER grid and collapsed due to no source available in these areas. Power was extended to Dharmanagar area of Tripura Power System by charging 132 kV Dharmanagar- PK Bari line at 16:14 Hrs of 16.03.2024. Power was finally restored to Dullavchhera area of Assam Power System by charging 132 kV Dullavchhera-Halakandi at 16:31 Hrs of 16.03.2024.	132 kV Dharmanagar- PK Bari line, 132 kV Dharmanagar-Dullavchhera & 132 kV Dullavchhera-Halakandi lines
9	GD1	Rangia, Kamalpur, Amingaon, Sishugram, Nalbari, Kamkhya and Natkuchi areas of Assam Power System	20-03-2024 05:33	20-03-2024 06:29	00:56:00	0	86	0.00%	5.11%	1700	1684	Rangia, Kamalpur, Amingaon, Sishugram, Nalbari, Kamkhya and Natkuchi areas of Assam Power System were connected with rest of the NER grid through 220kV Rangia - BTPS D/C lines. At 05:33 Hrs, 220kV Rangia - BTPS D/C lines tripped leading to SPS operation at Rangia S/S which led to blackout of 220 kV Rangia, Kamalpur, Amingaon, Sishugram, Nalbari, Kamakhya and Natkuchi areas of Assam Power System. Power supply was extended to 220 kV Rangia S/S and subsequently to Kamalpur, Amingaon, Sishugram, Nalbari, Kamakhya and Natkuchi areas of Assam Power System by charging 220kV Rangia - BTPS 2 line at 06:29 Hrs of 20.03.2024. 220kV Rangia - BTPS 1 line was charged at 06:36 Hrs.	220 kV BTPS-Rangia D/C
10	GD1	North Lakhimpur, Dhemaji, Silpathar and Majuli areas of Assam Power System	22-03-2024 12:31	22-03-2024 13:19	00:48:00	0	44	0.00%	2.15%	2292	2049	North Lakhimpur, Dhemaji, Silpathar and Majuli areas of Assam Power System were connected with rest of NER Grid through 132 kV North Lakhimpur- Pare line, 132 kV North Lakhimpur- Nirjuli line, and 132 kV North Lakhimpur- Gohpur 1 line. 132 kV Gohpur - North Lakhimpur 2 line was under PSD 09:26 Hrs. At 12:31 Hrs of 22-03-2024, 132 kV North Lakhimpur- Pare line, 132 kV North Lakhimpur Nirjuli line, and 132 kV North Lakhimpur- Gohpur 1 line tripped due to LBL operation. Due to tripping of these elements, North Lakhimpur, Dhemaji, Silpathar and Majuli areas of Assam Power System were isolated from NER Grid and collapsed due to no source available in these areas. Power was extended to North Lakhimpur by charging 132 kV North Lakhimpur- Nirjuli line at 13:19 Hrs.	132 kV North Lakhimpur- Pare, 132 kV North Lakhimpur Nirjuli, and 132 kV North Lakhimpur- Gohpur 1 lines

20.Details of Grid Events during the Month of March 2024 in Northern Region



Sl No.	Category of Grid Event	Affected Area	Time and Date of occurrence of Grid Event	Time and Date of Restoration	Duration (HH:MM)	Loss of generation / loss of load during the Grid Event		% Loss of generation / loss of load w.r.t Antecedent Generation/Load in the Regional Grid during the Grid Event		Antecedent Generation/Load in the Regional Grid*		Brief details of the event (pre fault and post fault system conditions)	Elements Tripped
	(GI for GI 2/ GD-1 to GD-5)					Generation Loss(MW)	Load Loss (MW)	% Generation Loss (MW)	% Load Loss (MW)	Antecedent Generation (MW)	Antecedent Load (MW)		
11	GD1	Depota, Rowta, Dhekiajuli, Sipajhar and Tangla areas of Assam Power system	22-03-2024 05:03	22-03-2024 05:25	00:22:00	0	19	0.00%	1.45%	2124	1307	Depota, Rowta, Dhekiajuli, Sipajhar and Tangla areas of Assam power system were connected to the rest of the grid through 132 kV Sonabil-Depota line & 132 kV Sonabil-Ghoramari-Depota link. At 05:03 Hrs of 22.03.2024, 132 kV Sonabil-Depota, 132 kV Depota-Rowta, 132 kV Depota-Dhekiajuli & 132 kV Rowta-Dhekiajuli lines tripped. Due to tripping of these elements, Depota, Rowta, Dhekiajuli, Sipajhar and Tangla areas of Assam power system were isolated from NER grid and collapsed due to no source available in these areas. 132 kV Sipajhar and Tangla GSS were shifted to 132 kV Rangia side to restore power at 05:11 hrs and 05:15 hrs respectively. Power was extended to Depota and connected substations by charging 132 kV Sonabil-Depota line at 05:25 Hrs of 22.03.2024.	132 kV Sonabil-Depota, 132 kV Depota-Ghoramari, 132 kV Depota-Rowta, 132 kV Depota-Dhekiajuli & 132 kV Rowta-Dhekiajuli lines
12	GD1	Jirania area of Tripura Power system	23-03-2024 22:25	23-03-2024 22:47	00:22:00	0	14	0.00%	0.70%	2020	2014	Jirania area of Tripura Power System is connected with rest of NER Grid via 132kV Budhjungnagar – Jirania and 132kV Baramura – Jirania lines. At 22:25 Hrs of 23.03.2024, 132kV Budhjungnagar – Jirania line tripped and 132kV Baramura-Jirania line was out since 20:30 Hrs of 23-03-2024. Due to tripping of these lines, Jirania area of Tripura Power System was isolated from NER Grid and collapsed due to no source available in this area. Power supply was extended to Jirania area of Tripura Power System by charging 132 kV Budhjungnagar – Jirania line at 22:47 Hrs of 23.03.2024.	132kV Budhjungnagar-Jirania and 132kV Baramura-Jirania lines
13	GD1	Renggang area of Manipur Power system	23-03-2024 22:44	23-03-2024 23:53	01:09:00	0	2	0.00%	0.12%	2001	1642	Renggang area of Manipur Power System was connected with rest of NER Grid through 132 kV Renggang - Loktak and 132 kV Jiribam(MA) - Renggang lines. 132 kV Jiribam(MA) - Renggang line was under outage since 18:18 Hrs of 17-11-2023. At 22:44 Hrs of 23-03-2024, 132kV Loktak – Renggang and 132kV Loktak – Ningthoukhong lines tripped. Due to tripping of these lines, Renggang area of Manipur Power System got isolated from NER grid and collapsed due to no source available in these areas. Power was extended to Renggang by charging 132 kV Loktak – Renggang at 23:53 Hrs of 23-03-2024.	132 kV Loktak-Renggang & 132 kV Loktak-Ningthoukhong lines
14	GD1	Nangalibira, Rongkhong, Ampati and Phulbari areas of Meghalaya Power system	26-03-2024 01:56	26-03-2024 02:28	00:32:00	0	14	0.00%	1.13%	2010	1235	Nangalibira, Rongkhong, Ampati and Phulbari areas of Meghalaya Power System are connected with the rest of NER Grid through 132 kV Agia- Nangalibira line, 132 kV Mendipathar- Nangalibira and 132 kV Nangalibira-Nongstoin lines. Prior to the event, 132 kV Nangalibira-Nongstoin line tripped at 01:23 Hrs. At 01:56 Hrs of 26-03-2024, 132 kV Agia- Nangalibira line and 132 kV Mendipathar - Nangalibira line tripped. Due to tripping of these elements, Nangalibira, Rongkhong and Ampati areas of Meghalaya Power System were isolated from NER Grid and collapsed due to no source available in these areas. Power was extended to Nangalibira, Rongkhong, Ampati and Phulbari areas of Meghalaya Power System by charging 132 kV Agia- Nangalibira line at 02:28 Hrs.	132 kV Agia-Nangalibira & 132 kV Mendipathar-Nangalibira lines
15	GD1	Lumshnong area of Meghalaya Power system	26-03-2024 00:32	26-03-2024 01:18	00:46:00	0	27	0.00%	2.04%	2049	1325	Lumshnong area of Meghalaya Power System is connected with rest of NER Grid through 132 kV Lumshnong – Khliehriat and 132 kV Lumshnong-Panchgram lines. 132 kV Lumshnong - Panchgram line was under outage since 23:35 of 25.03.2024. At 00:32 Hrs of 26-03-2024, 132 kV Lumshnong – Khliehriat line tripped. Due to tripping of this element, Lumshnong area of Meghalaya Power System was isolated from NER Grid and collapsed due to no source available in this area. Power was extended to Lumshnong area of Meghalaya Power System by charging 132 kV Lumshnong – Khliehriat line at 01:18 Hrs.	132 kV Lumshnong-Khliehriat line
16	GD1	Hatsinigimari area of Assam Power system	31-03-2024 19:31	31-03-2024 21:55	02:24:00	0	2	0.00%	0.20%	221	989	Hatsinigimari area of Assam Power System was connected with rest of NER Grid through 132 kV Agia - Hatsinigimari line, 132 kV Ampati- Hatsinigimari D/C lines are under construction. At 19:31 Hrs of 31-03-2024, 132 kV Agia - Hatsinigimari line tripped. Due to tripping of this element, Hatsinigimari area of Assam Power System due to no source available mismatch in this area. Power supply was extended to Hatsinigimari area of Assam Power System by charging 132 kV Agia - Hatsinigimari line at 21:55 Hrs of 31.03.2024	132 kV Agia-Hatsinigimari Line
17	GD1	Tezu and Namsai areas of Arunachal Pradesh Power system	31-03-2024 23:59	Not yet restored		0	0.3	0.00%	0.02%	2143	1236	Tezu and Namsai areas of Arunachal Pradesh Power System was connected with rest of NER Grid via 132 kV Roing – Tezu line. At 23:59 Hrs of 31.03.2024, 132 kV Roing – Tezu line tripped due to tower collapse in loc. no. 72 leading to blackout of Tezu and Namsai areas of Arunachal Pradesh Power System. Power is yet to be extended to Tezu and Namsai areas of Arunachal Pradesh.	132 kV Roing-Tezu line
18	GD1	Monarchak, Rabindranagar and Udaipur areas of Tripura Power system	31-03-2024 07:36	31-03-2024 08:54	01:18:00	110	2	5.64%	0.10%	1950	1963	Monarchak, Rabindranagar, and Udaipur areas of Tripura Power System are connected with rest of NER Grid through 132 kV Monarchak-Udaipur and 132 kV Palatana-Udaipur lines. 132 kV Palatana-Udaipur line is under outage since 07:32 hrs of 31-03-2024. At 07:36 Hrs of 31-03-2024, 132 kV Monarchak-Udaipur line tripped. Due to tripping of this element, Monarchak Generating station, Rabindranagar, and Udaipur areas of Tripura Power System were isolated from NER Grid and collapsed due to load generation mismatch in these areas. Rokhia Unit-7 & 8 also tripped. Power was extended to Monarchak Generating station, Rabindranagar, and Udaipur areas of Tripura Power System by charging 132 kV Palatana-Udaipur line at 08:54 Hrs of 31-03-2024.	132 kV Monarchak-Udaipur line, Monarchak GT & ST, Rokhia Unit-7 & 8
19	GD1	Rokhia generating station of Tripura Power system	31-03-2024 09:29	31-03-2024 10:09	00:40:00	0	0	0.00%	0.00%	1760	1927	Rokhia Generating Station of Tripura Power System is connected with rest of NER Grid through 132 kV Rokhia-Agartala D/C and 132 kV Monarchak-Rokhia lines. 132 kV Rokhia-Agartala 2 line was under outage since 07:30 Hrs & 132 kV Monarchak-Rokhia line was under outage since 07:36 Hrs of 31.03.2024. At 09:29 Hrs of 31-03-2024, 132 kV Rokhia-Agartala 1 line tripped leading to blackout of Rokhia Generating Station of Tripura Power System. Power was extended to Rokhia Generating Station of Tripura Power System by charging 132 kV Rokhia-Agartala 1 line at 10:09 Hrs of 31-03-2024.	132 kV Rokhia-Agartala 1 line
20	GD1	Serchhip area of Mizoram Power system	31-03-2024 09:18	31-03-2024 10:14	00:56:00	0	8	0.00%	0.44%	1917	1806	Serchhip area of Mizoram Power System was connected with rest of NER Grid through 132 kV Zuangtui - Serchhip line. 132 kV Lunglei-Serchhip line is kept open due to system requirement. At 09:18 Hrs of 31-03-2024, 132 kV Zuangtui - Serchhip line tripped. Due to tripping of this element led to blackout of Serchhip area of Mizoram Power System due to no source available in this area. Power was extended to Serchhip area of Mizoram Power System by charging 132 kV Zuangtui - Serchhip line at 10:14 Hrs.	132 kV Zuangtui-Serchhip line

21. NEW ELEMENTS COMMISSIONED* IN MARCH 2024						
COMMISSIONING OF NEW GENERATING UNITS						
REGION	S.NO.	ENTITY	UNIT NAME / LOCATION	ADD. CAPACITY (MW)	UNIT NO.	INS. CAPACITY (MW)
NR	1	BANDERWALA TPSL	Bandewala TPSL(Solar)Rajasthan	200	-	300
	2	PHALODI SOLAR PLANT ASERIZPL	Phalodi Solar Plant ASERIZPL(Solar)Rajasthan	92.5	-	150
	3	RISING SUN ENERGY (K) PRIVATE LIMITED (RSEKPL)	Rising Sun Energy (K) Private Limited(Solar)Rajasthan	26	-	190
	4	PHALODI SOLAR PLANT ASERIZPL	Phalodi Solar Plant ASERIZPL(Solar)Rajasthan	57.5	-	150
	5	TRANSITION GREEN ENERGY PRIVATE LIMITED	Transition Green Energy Private Limited(Solar)Rajasthan	55.55	-	100
	6	TRANSITION SUSTAINABLE ENERGY SERVICES PRIVATE LIMITED	Transition Sustainable Energy Services Private Limited(Solar)Rajasthan	20	-	50
	7	RENEW SURYA ROSHNI PRIVATE LIMITED	Renew Surya Roshni Private Limited(Solar + BESS)Rajasthan	95	-	400
	8	RENEW SURYA PRATAP PRIVATE LIMITED	Renew Surya Pratap Private Limited(Solar)Rajasthan	22	-	200
	9	ADANI SOLAR ENERGY RJ TWO PRIVATE LIMITED	Adani Solar Energy RJ Two Private Limited(Solar)Rajasthan	15	-	180
	10	ANTA SOLAR POWER PLANT NTPC LTD	Anta Solar Power Plant NTPC Ltd(Solar)Rajasthan	57	-	90
WR	11	MASAYA SOLAR	Maaya (Solar)Madhya Pradesh	50	I	300
	12	APRAVA ENERGY PRIVATE LIMITED (AEPL)	Apravo Energy Private Limited (Wind)Gujarat	46.2	I	210
	13	ALFANAR NETRA VAYU	Alfanar Netra Vayu(Wind)Gujarat	41.8	I	161.8
SR	14	RSRPL	RSRPL(Wind)Karnataka	17.33	LOT-VII	291.06
	15	JSW Renew Energy Two Limited	JSW Renew Energy Two Limited (Wind)Tamilnadu	18.9	LOT-XII	264.6
	16	JSW	JSW(Wind)Tamilnadu	18.9	LOT-III	56.7
	17	RSOPL	RSOPL(Wind)Karnataka	20.79	LOT-III	246.01
	18	RSOPL	RSOPL(Wind)Karnataka	24.26	LOT-IV	270.26
	19	RSOPL	RSOPL(Wind)Karnataka	24.26	LOT-V	294.51
*RE (Solar & Wind generation added capacity FTEC is in phases. Date mentioned is the date by which complete (Added) capacity						
COMMISSIONING OF NEW ICTS						
REGION	S.NO.	ENTITY	SUB-STATION	VOLTAGE (kV)	ICT NO.	CAPACITY (MVA)
NR	1	PBTSL	Bikaner_2	400/220/5	II	500
	2	PGYTL	Mohanlalgaonj	400/220/33	II	500
	3	PGYTL	Mohanlalgaonj	400/220/33	I	500
	4	UPPTCL	Sarnath	400/220/33	I	315
	5	POWERGRID	Bhadla_2	400/220/33	VIII	500
WR	6	AGEL (Adani Green Energy Limited)	Khavda PSS 3	400/33	I	330
	7	AGEL (Adani Green Energy Limited)	Khavda PSS 3	400/33	II	330
	8	AREH4L	Khavda PSS2	400/33	I	330
	9	AREH4L	Khavda PSS2	400/33	II	330
	10	PNTSL (Powergrid Neemuch Transmission System Ltd)	Neemuch	400/220	I	500
	11	PNTSL (Powergrid Neemuch Transmission System Ltd)	Neemuch	400/220	II	500
	12	GETCO	Kasor	400/220	IV	500
	13	Kallam TL (Indigrd)	Kallam PS	400/220/33	I	500
	14	Kallam TL (Indigrd)	Kallam PS	400/220/33	II	500
	15	POWERGRID (SR-2)	Pravada	400/220/33	VI	500
SR	16	POWERGRID (SR-2)	Kolar	400/220/33	III	500
	17	POWERGRID (SR-2)	Hosur	400/220/33	IV	500
	18	KPTCL	Kalaburagi	400/220/33	II	500
	19	TS TRANSCO	Manidipally	400/220/33	I	315
	20	KPTCL	Gowripura JSW	400/33	I	315
	21	KPTCL	Gowripura JSW	400/33	II	315
ER	22	WBSETCL	New chanditala	400/220	IV	315
	23	WBSETCL	Jerat	400/220	IV	315
NER	24	AEGCL	Behaiting	220/132	I	100
	25	AEGCL	LTPS	132/33	II	16
	26	AEGCL	Rangia	132/33	I	50
	27	AEGCL	Hailakandi	132/33	I	50
COMMISSIONING OF NEW TRANSMISSION LINES						
REGION	S.NO.	ENTITY	LINE NAME	CKT NO.	VOLTAGE (kV)	DATE
NR	1	PNTSL (Powergrid Neemuch Transmission System Ltd)	400kV Neemuch-Chittorgarh	I	400	29-03-2024
	2	PNTSL (Powergrid Neemuch Transmission System Ltd)	400kV Neemuch-Chittorgarh	II	400	30-03-2024
	3	UPPTCL	400kV Panki-Parki TPS	II	400	13-03-2024
WR	4	AREH4L	400kV Khavda PSS2 (AREH4L)-Khavda PSI	I	400	02-03-2024
	5	GETCO	400kV Jeparu-Hadala	I	400	17-03-2024
	6	AGEL (Adani Green Energy Limited)	400kV Khavda PSS3 (AGEL) - Khavda PSI	I	400	23-03-2024
	7	GETCO	400kV Vadasi-Chara	I	400	29-03-2024
	8	PNTSL (Powergrid Neemuch Transmission System Ltd)	400kV Neemuch-Mandhar	I	400	30-03-2024
	9	PNTSL (Powergrid Neemuch Transmission System Ltd)	400kV Neemuch-Mandhar	II	400	30-03-2024
	10	GETCO	400kV Amreli-Vadinar	I	400	30-03-2024
SR	11	GETCO	400kV Amreli-Vadinar	II	400	30-03-2024
	12	KPTCL	400kV Gowripura Wind - Rajapura solar	I	400	30-03-2024
LILO OF TRANSMISSION LINES						
REGION	S.NO.	ENTITY	LINE NAME (LILOed LINE)	LILO AT	VOLTAGE (kV)	DATE
NR	1	PGCL	Zerda-Kankrol-II (Bhimtal-Zerda & 400kV Bhimtal-Kankrol)	Bhimtal	400	08-03-2024
	2	UPPTCL	Lucknow-Mohanlalgaonj-I (Lucknow-Sultanpur)	Mohanlalgaonj	400	11-03-2024
	3	UPPTCL	Sultanpur-Mohanlalgaonj-I (Lucknow-Sultanpur)	Mohanlalgaonj	400	11-03-2024
	4	PGYTL	Mohanlalgaonj-Umao-I (Sangai Nagar, Lucknow- Umao)	Mohanlalgaonj	400	20-03-2024
	5	PGYTL	Lucknow-Mohanlalgaonj-I (Sangai Nagar, Lucknow- Umao)	Mohanlalgaonj	400	20-03-2024
COMMISSIONING OF BUS/LINE REACTORS						
REGION	S.NO.	ENTITY	SUB-STATION / LINE (S/SUB-STATION)	VOLTAGE (kV)	CAPACITY (MVAR)	DATE
NR	1	PGYTL	Bus Reactor-I@Mohanlalgaonj	400	125	11-03-2024
	2	POWERGRID	Bus Reactor-II@Meerut	400	50	13-03-2024
	3	POWERGRID	Bus Reactor-III@Ballabgarh	400	125	31-03-2024
	4	UPPTCL	Barilly-Umao-II@Barilly	400	63	03-03-2024
	5	SELUPPTCL	Maipuri-Umao@Maipuri	765	150	20-03-2024
	6	SELUPPTCL	Maipuri-Bana-II@Maipuri	765	330	20-03-2024
	7	POWERGRID	Barilly-Lucknow-II@Barilly	400	80	28-03-2024
WR	8	PNTSL (Powergrid Neemuch Transmission System Ltd)	Bus Reactor-I@Neemuch	400	125	29-03-2024
	9	TSTRANSCO	Bus Reactor-I@Ketherreddyapally	400	125	13-03-2024
	10	TSTRANSCO	Bus Reactor-II@Maheshwaram	400	125	04-03-2024
	11	POWERGRID(SR-2)	Bus Reactor-I@Hussan	400	80	13-03-2024
	12	POWERGRID(SR-2)	Palakkad-Trichur-II@Trichur	400	50	26-03-2024
	13	POWERGRID(SR-2)	Nagpettanam-Trichy-II@Trichy	400	80	26-03-2024
SR	14	TSTRANSCO	Bus Reactor-I@Choumppal	400	125	21-03-2024
	15	TSTRANSCO	Bus Reactor-I@Narasapur	400	125	27-03-2024
ER	16	POWERGRID	Bus Reactor-V@Biharsharif	400	125	23-03-2024
COMMISSIONING OF HVDC/FACTS DEVICE/SYSTEM						
REGION	S.NO.	ELEMENT NAME	SUB-STATION / CONSTITUENT	RATINGS	VOLTAGE (kV)	DATE
*Includes first time charging (FTEC) as well						

22.Voltage Profile

विद्युत विभव रूपरेखा माह - मार्च 2024

VOLTAGE PROFILE - MARCH 2024

Date of reporting: 05-Apr-24

क्र.स. Sl. No.	क्षेत्र REGION	उपकेंद्र SUBSTATION	VOLTAGE < V(lower)* (V=380,728 kV)	V(lower) < VOLTAGE < V(upper)*	VOLTAGE > V(upper)* (V=420,800 kV)	Voltage Deviation Index (%age of time voltage is outside range)	Number of hours voltage was outside IECG band during month	उच्चतम (कि.वो.) Maximum(kV)	निम्नतम(कि.वो.) Minimum(kV)	औसत (कि.वो.) Average(kV)
1	पूर्वी क्षेत्र ER	अंगुल ANGUL	0%	100%	0%	0%	0	792	749	771
2		दार्लिपली DARIIPALI	0%	100%	0%	0%	0	786	764	774
3		गया GAYA	0%	100%	0%	0%	0	788	754	771
4		जेरत JEERAT	0%	100%	0%	0%	0	789	733	762
5		झारसुगुडा JHARSUGUDA	0%	100%	0%	0%	0	798	770	783
6		मिदनापुर MEDINIPUR	0%	100%	0%	0%	0	793	744	768
7		रांची RANCHI	0%	100%	0%	0%	0	791	763	778
8		सासाराम SASARAM	0%	100%	0%	0%	0	778	741	765
1	उत्तरी क्षेत्र NR	आगरा AGRA	0%	100%	0%	0%	0	801	757	781
2		आगरा (फतेहाबाद) AGRA (FATEHABAD)	0%	100%	0%	0%	0	793	744	774
3		अजमेर AJMER	0%	100%	0%	0%	2	805	740	781
4		अलीगढ़ ALIGARH	0%	100%	0%	0%	0	802	751	779
5		अनपरा सी ANPARA-C	0%	100%	0%	0%	0	784	759	770
6		अनपरा डी ANPARA-D	0%	100%	0%	0%	0	782	758	768
7		अंता ANTA	0%	100%	0%	0%	0	798	717	778
8		बालिया BALLIA	0%	100%	0%	0%	0	783	745	767
9		बारा BARA	0%	100%	0%	0%	0	789	759	773
10		भाड़ला BHADLA	0%	100%	0%	0%	0	791	731	772
11		भाड़ला-2 BHADLA-2	0%	100%	0%	0%	0	797	728	774
12		भिवानी BHIWANI	0%	100%	0%	0%	3	804	746	782
13		बीकानेर BIKANER	0%	100%	0%	0%	0	798	720	773
14		बरेली BAREILLY	0%	100%	0%	0%	2	804	749	782
15		चित्तौड़गढ़ CHITTORGARH	0%	100%	0%	0%	2	805	751	783
16		फतेहगढ़-2 FATEHGARH-2	0%	100%	0%	0%	0	804	738	774
17		फतेहपुर FATEHPUR	0%	100%	0%	0%	0	794	750	772
18		ग्रेटर नोएडा GREATER NOIDA	0%	99%	1%	1%	7	808	753	784
19		हापड़ HAPUR	0%	100%	0%	0%	2	805	745	779
20		जाह्नपुर JAWAHARPUR	0%	100%	0%	0%	1	804	743	776
21		झाटिकरा JHATIKARA	0%	100%	0%	0%	0	800	738	778
22		कानपुर जीआरएस KANPUR GIS	0%	100%	0%	0%	0	798	750	776
23		खैतवा KHETWA	0%	100%	0%	0%	0	803	745	777
24		कोटेश्वर KOTESHWAR	0%	100%	0%	0%	0	801	745	777
25		लालितपुर LALITPUR	0%	100%	0%	0%	0	776	742	761
26		लखनऊ LUCKNOW	0%	100%	0%	0%	0	794	748	775
27		मैनपुरी MAINPURI	0%	100%	0%	0%	0	805	739	774
28		मेरठ MEERUT	0%	100%	0%	0%	2	806	747	781
29		मेरठ(UP) MEERUT (UP)	0%	100%	0%	0%	0	802	745	778
30		मोगा MOGA	0%	100%	0%	0%	2	805	741	772
31		ओबरा सी OBRA C	0%	100%	0%	0%	0	779	751	764
32		उरई ORAI	0%	99%	1%	1%	8	810	766	789
33		फागी PHAGI	0%	100%	0%	0%	1	802	740	780
34		रामपुर RAMPUR	0%	100%	0%	0%	1	804	738	777
35		उन्नाव UNNAO	0%	100%	0%	0%	0	789	743	770
36		वाराणसी VARANASI	0%	100%	0%	0%	0	793	758	777
1	पश्चिमी क्षेत्र WR	अकोला AKOLA	0%	100%	0%	0%	0	793	750	773
2		औरंगाबाद AURANGABAD	0%	100%	0%	0%	0	800	752	777
3		भोपाल (बीडीटीसीएल) BHOPAL (BDTCL)	0%	100%	0%	0%	0	792	747	770
4		भुज BHUJ	0%	100%	0%	0%	0	796	747	774
5		भुज-2 BHUJ-II	0%	100%	0%	0%	0	789	748	770
6		बिलासपुर BILASPUR	0%	100%	0%	0%	0	785	757	770
7		बीना BINA	0%	100%	0%	0%	0	800	764	781
8		बनसकंठा BANASKANTHA	0%	100%	0%	0%	1	802	756	783
9		चांपा CHAMPA	0%	100%	0%	0%	3	807	763	786
10		धुले (बीडीटीसीएल) DHULE (BDTCL)	0%	100%	0%	0%	0	798	751	774
11		धर्मजयगढ़ DHARAMJAGARH	0%	100%	0%	0%	0	788	760	773
12		रायपुर पूलिंग RAIPUR POOLING	0%	100%	0%	0%	0	795	764	779
13		एकतुनी EKTUNI	0%	100%	0%	0%	0	792	748	772
14		गदरवाड़ा GADARWARA	0%	100%	0%	0%	0	796	767	780
15		ग्वालियर GWALIOR	0%	100%	0%	0%	1	805	763	784
16		इंदौर INDORE	0%	100%	0%	0%	0	795	750	772
17		जबलपुर JABALPUR	0%	100%	0%	0%	1	804	771	786
18		खड़ग KHANDWA	0%	100%	0%	0%	0	794	751	773
19		कोरडी KORADI	0%	100%	0%	0%	0	783	751	770
20		लाकाडिया LAKADIVA	0%	100%	0%	0%	1	803	753	779
21		रायगढ़ पूलिंग RAIGARH POOLING	0%	100%	0%	0%	0	795	769	781
22		पडुछे PADGHE	0%	100%	0%	0%	0	801	739	774
23		परली PARLI	0%	100%	0%	0%	4	804	757	781
24		पुणे PUNE	0%	100%	0%	0%	2	808	745	776
25		राजनन्दगांव RAJNANDGAON	0%	100%	0%	0%	3	804	762	785
26		सासन SASAN	0%	100%	0%	0%	0	791	766	777
27		सतना SATNA	0%	100%	0%	0%	1	803	767	784
28		सिवनी SEONI	0%	100%	0%	0%	0	793	755	775
29		सीपत SIPAT	0%	100%	0%	0%	0	784	759	771
30		सोलापुर SOLAPUR	0%	100%	0%	0%	2	806	759	782
31		तिरोड़ा TIRODA	0%	100%	0%	0%	0	778	754	767
32		तमनार TAMNAR	0%	100%	0%	0%	0	791	767	779
33		वडोदरा VADODARA	0%	100%	0%	0%	2	803	745	776
34		विंध्याचल पूलिंग VINHYACHAL PS	0%	100%	0%	0%	0	795	770	780
35		वधा WARDHA	0%	100%	0%	0%	0	802	758	780
36		वरारार WARORA	0%	100%	0%	0%	0	799	756	776
1	दक्षिणी क्षेत्र SR	अरियलूर ARIYALUR	0%	100%	0%	0%	0	801	735	773
2		कडपा CUDDAPAH	0%	98%	2%	2%	18	811	751	783
3		चिल्कुरीपेट CHILAKALURIPETA	0%	99%	1%	1%	11	812	750	781
4		कन्नूल KURNOOL	0%	100%	0%	0%	1	803	747	774
5		महेश्वरम MAHESWARAM	0%	97%	3%	3%	23	813	753	781
6		निजामाबाद NIZAMABAD	0%	93%	7%	7%	53	818	750	782
7		नेल्लूर पूलिंग NELLORE PS	0%	100%	0%	0%	0	800	749	772
8		नॉर्थ चेन्नै पूलिंग NORTH CHENNAI PS	0%	97%	3%	3%	25	817	730	772
9		रायचूर RAICHUR	0%	100%	0%	0%	0	801	753	775
10		श्रीकाकुलम SRIKAKULAM	0%	100%	0%	0%	2	807	750	777
11		थिरुवल्लम THIRUVALEM	0%	100%	0%	0%	0	798	739	771
12		वेंमगिरि VEMAGIRI	0%	99%	1%	1%	11	812	755	781
13		वारंगल WARANGAL	0%	99%	1%	1%	8	810	751	779
1	पूर्वोत्तर क्षेत्र NER	बिस्वनाथ चारिआल बिसवानाथ चारिआल (400 kV)	0%	100%	0%	0%	0	416	367	404
2		बोंगाईगांव BONGAIGAON (400 kV)	0%	100%	0%	0%	0	415	399	407
3		बोंगाईगांव टोपाएस बोंगाईगांव TPS (400 kV)	0%	100%	0%	0%	0	416	400	409
4		इम्फाल IMPHAL (400 kV)	0%	100%	0%	0%	0	418	394	406
5		बर्निहाट BYRNHAT (400 kV)	0%	100%	0%	0%	0	420	400	411
6		कामेंग KAMENG (400 kV)	0%	100%	0%	0%	0	414	391	402
7		अज़ारा AZARA (400 kV)	0%	100%	0%	0%	0	411	402	406
8		मिसा MISA (400 kV)	0%	100%	0%	0%	0	413	391	403
9		नू नू मारिआनी NEW MARIANI (400 kV)	0%	100%	0%	0%	0	416	394	406
10		नू कोहिमा NEW KOHIMA (400 kV)	0%	100%	0%	0%	0	420	391	407
11		पालाताना PALATANA (400 kV)	0%	100%	0%	0%	0	415	401	407
12		पुबकेचनबारी PK BARI (400 kV)	0%	100%	0%	0%	0	413	392	402
13		रंगानादी RANGANADI (400 kV)	0%	100%	0%	0%	3	423	388	409
14		सिलचर SILCHAR (400 kV)	0%	100%	0%	0%	0	418	397	408
15		सूर्यजयानगर SURJYAMANINAGAR (400 kV)	0%	100%	0%	0%	0	410	388	401
16		थोबाल THOUBAL (400 kV)	0%	100%	0%	0%	0	415	389	403

All listed stations are 765 kV stations unless otherwise mentioned

*Percentage is calculated w.r.t. Time of one month.

23.ALL TIME HIGHEST

31-03-2024

	Maximum Demand Met during the day (MW)	Demand Met during Evening Peak hrs(MW)	Energy Met (MU)	Hydro Gen. (MU)	Wind Gen. (MU)	Solar Gen. (MU)
NR	81220 04-09-2023	76274 04-09-2023	1796 04-09-2023	443 01-08-2023	86 07-08-2023	167 16-03-2024
WR	74799 29-01-2024	66749 28-03-2024	1618 02-09-2023	167 18-12-2014	273 07-08-2023	88.75 05-03-2024
SR	68735 13-03-2024	53663 13-03-2024	1404 15-03-2024	208 31-08-2018	298 21-07-2023	148.7 31-03-2024
ER	29641 28-07-2023	28579 18-04-2023	639 08-06-2023	157 14-09-2022	-	7 23-03-2023
NER	3712 04-09-2023	3510 12-08-2022	72 15-09-2023	41 29-08-2023	-	2 22-06-2022
All India	239978 01-09-2023	215592 28-08-2023	5224 02-09-2023	877 30-08-2022	611 02-08-2023	398 08-03-2024
Regions	States	Max. Demand Met during the day (MW)		Energy Consumption (MU)		
			As on date		As on date	
NR	Punjab	15237	23-06-2023	343.5	24-06-2023	
	Haryana	12692	18-08-2023	273.1	18-08-2023	
	Rajasthan	17949	20-01-2024	371.6	04-09-2023	
	Delhi	7770	29-06-2022	153.5	28-06-2022	
	UP	28553	25-07-2023	580.0	03-09-2023	
	Uttarakhand	2594	14-06-2022	55.8	17-06-2023	
	HP	2235	20-01-2024	40.7	22-08-2023	
	J&K(UT) and Ladakh(UT)	3636	29-06-2023	66.8	26-01-2024	
	Chandigarh	426	08-07-2021	8.4	08-07-2021	
	Railways NR ISTS	-	-	-	-	
WR	Chhattisgarh	6148	29-03-2024	142.1	30-03-2024	
	Gujarat	24544	01-09-2023	511.6	02-09-2023	
	MP	17819	29-12-2023	335.9	10-11-2023	
	Maharashtra	28969	07-02-2024	643.8	28-03-2024	
	Goa	776	07-06-2023	17.1	08-06-2023	
	DD & DNH	1327	17-08-2023	30.9	10-08-2023	
	AMNSIL	1083	10-01-2024	21.0	31-05-2022	
	Balco	-	-	-	-	
SR	Andhra Pradesh*	13255	07-03-2024	263.8	16-06-2023	
	Telangana*	15623	08-03-2024	311.0	13-03-2024	
	Karnataka	17220	12-03-2024	331.4	22-03-2024	
	Kerala	5301	26-03-2024	104.7	27-03-2024	
	Tamil Nadu	19409	22-03-2024	417.2	29-03-2024	
	Pondy	512	17-05-2023	11.6	18-05-2023	
ER	Bihar	7578	27-07-2023	161.3	28-07-2023	
	DVC	3751	18-04-2023	81.2	22-04-2022	
	Jharkhand	1923	16-06-2023	43.3	17-06-2023	
	Odisha	7192	19-04-2023	145.5	25-09-2022	
	West Bengal	11868	18-04-2023	245.7	18-04-2023	
	Sikkim	137	03-02-2022	2.5	28-01-2020	
	Railways ER ISTS	-	-	-	-	
NER	Arunachal Pradesh	189	17-03-2024	3.4	25-03-2024	
	Assam	2498	16-09-2023	50.0	15-09-2023	
	Manipur	258	31-01-2022	3.7	10-02-2022	
	Meghalaya	415	09-02-2022	7.8	31-01-2022	
	Mizoram	162	27-01-2024	2.6	02-03-2024	
	Nagaland	179	28-09-2023	3.29	05-09-2023	
	Tripura	370	07-06-2023	7.0	06-06-2023	
*SR	Andhra Pradesh (Undivided)	13162	23-03-2014	284.8	22-03-2014	

24.System Reliability Indices Report for the month of March 2024

Percentage (%) of times ATC was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	0	0.00	0.00
2	ER-NR	0	0.00	0.00
3	Import of NR	0	0.00	0.00
4	NEW-SR	0	0.00	0.00
5	NER Import	0	0.00	0.00

Percentage(%) of times (N-1) Criteria was violated

S.No.	Corridor	Number of Blocks Violated	Number of Hours Violated	%Violation
1	WR-NR	0	0.00	0.00
2	ER-NR	0	0.00	0.00
3	Import of NR	0	0.00	0.00
4	NEW-SR	0	0.00	0.00
4	NER Import	0	0.00	0.00

Remarks: Flows crossing Total Transfer Capability (TTC) on interregional corridors has been worked out as a proxy for (N-1) violation.



POWER SYSTEM OPERATION CORPORATION LIMITED

पावर सिस्टम ऑपरेशन कारपोरेशन लिमिटेड

NATIONAL LOAD DESPATCH CENTRE – राष्ट्रीय भार प्रेषण केन्द्र

First floor, B-9, Qutab Institutional Area,
Katwaria Sarai, New Delhi-110016.
